

**P-1008 Single Marine Center Work
School of Infantry – 52 Area
SOLICITATION: N62473-11-R-0404**




**Contractor:
Accurate Engineering**





**CPM Scheduling Consultant:
HSE Contractors Inc.**

JUNE 2011 Progress Report

Project Breakdown :

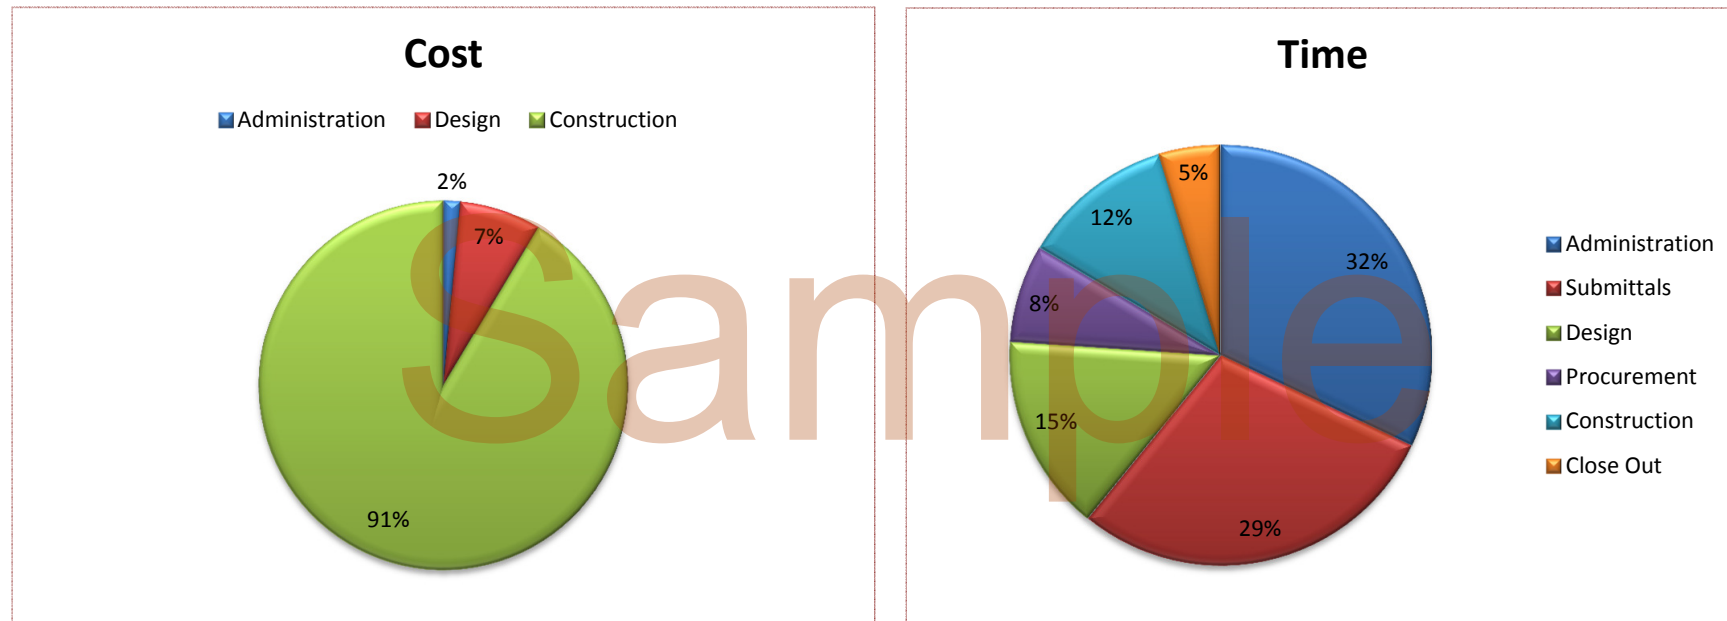


Project Percent Complete :

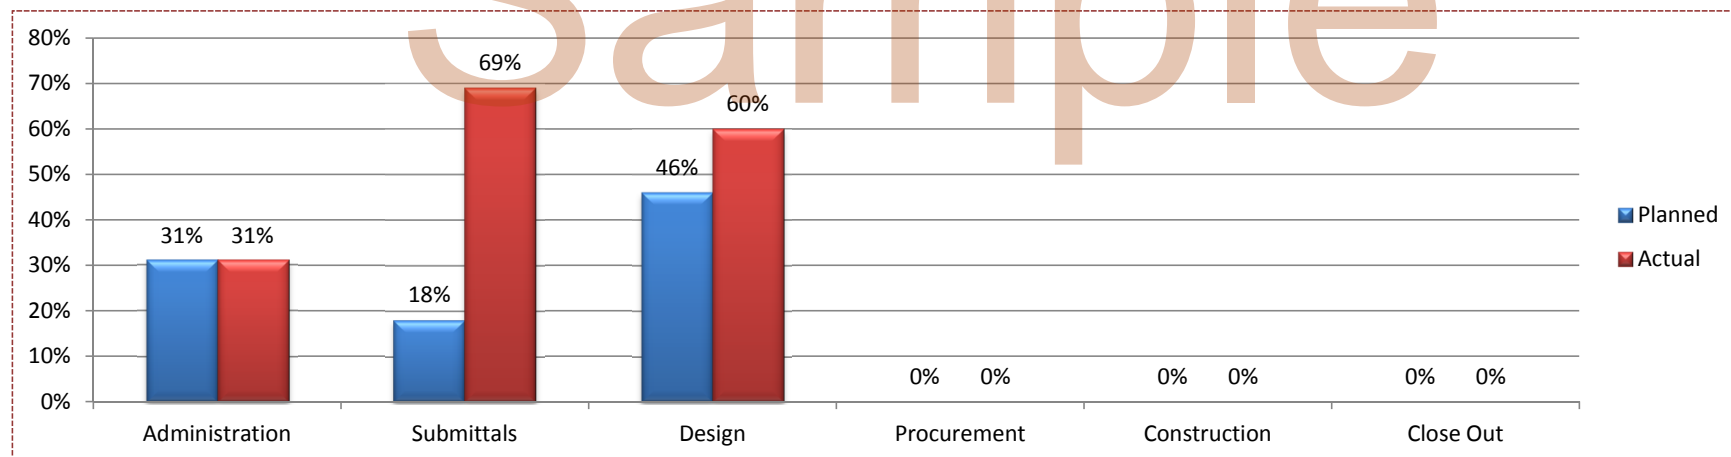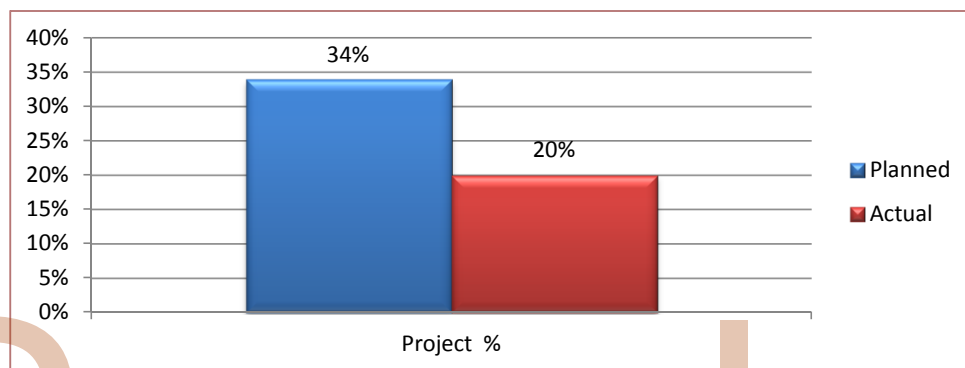



Schedule Performance :


Progress Chart

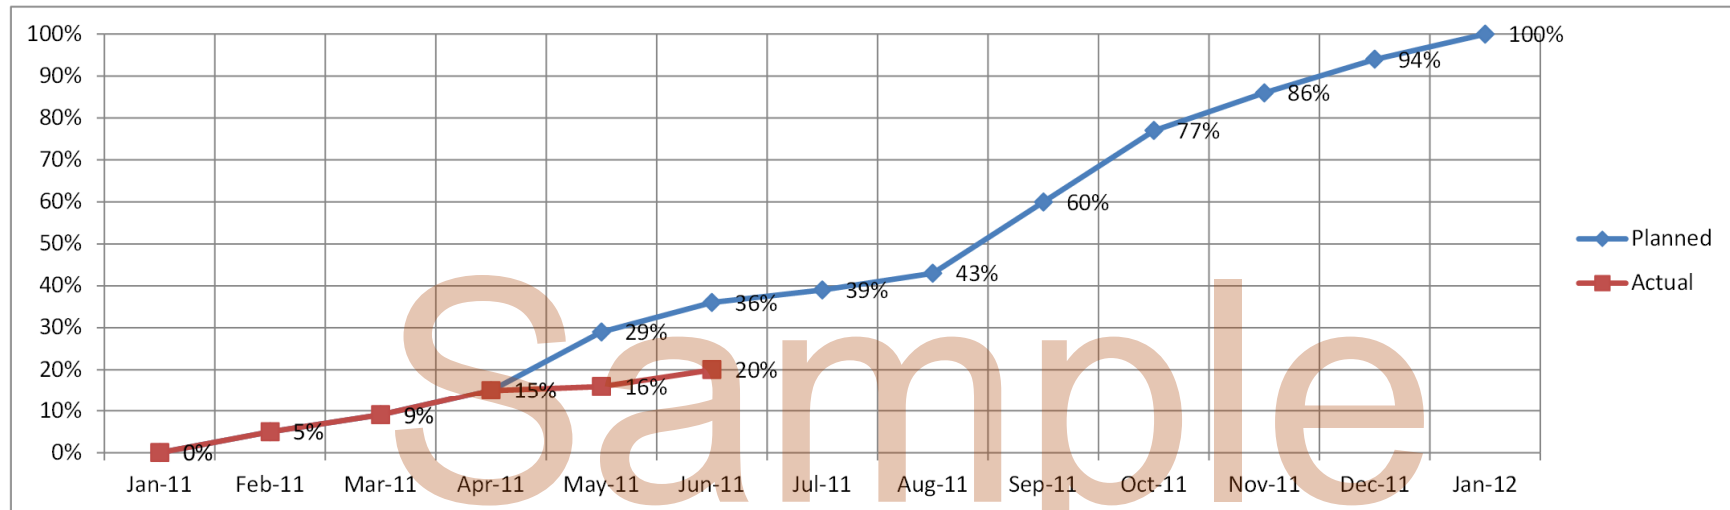


HSE Contractors Comment: The Contractor is behind schedule and progress rate should be increased to recover the delays.

Cost Performance :

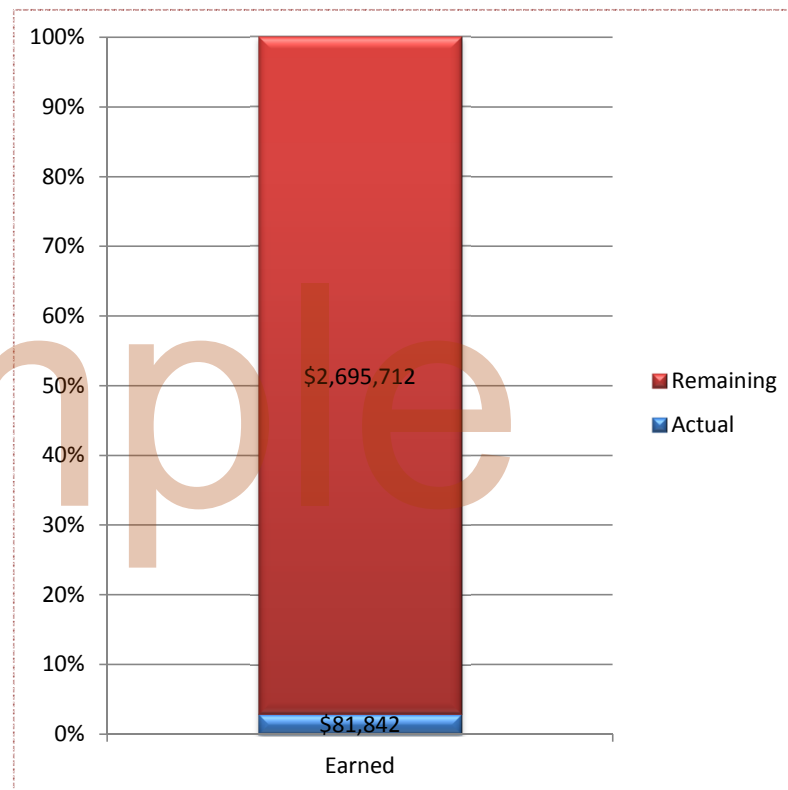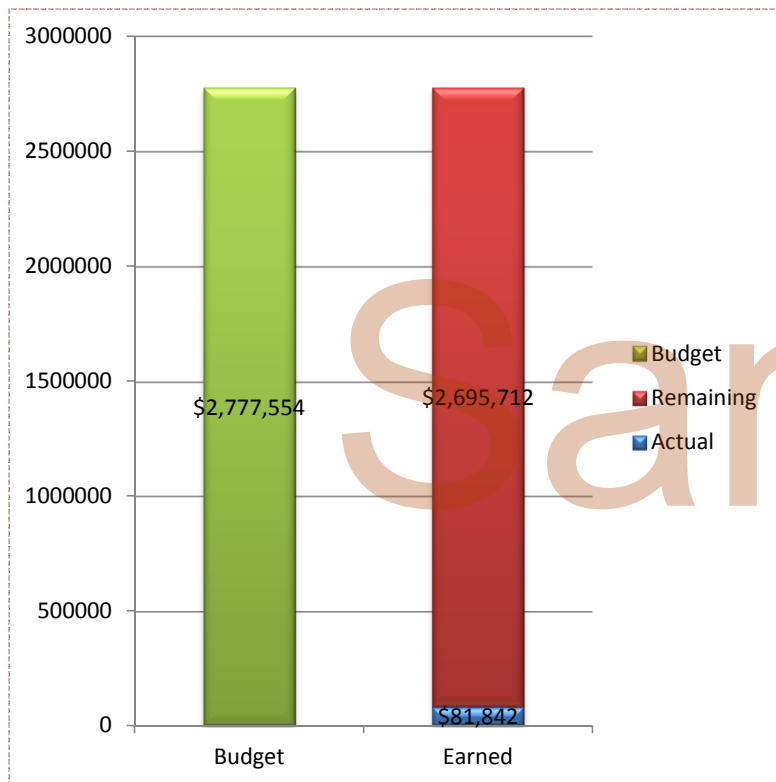

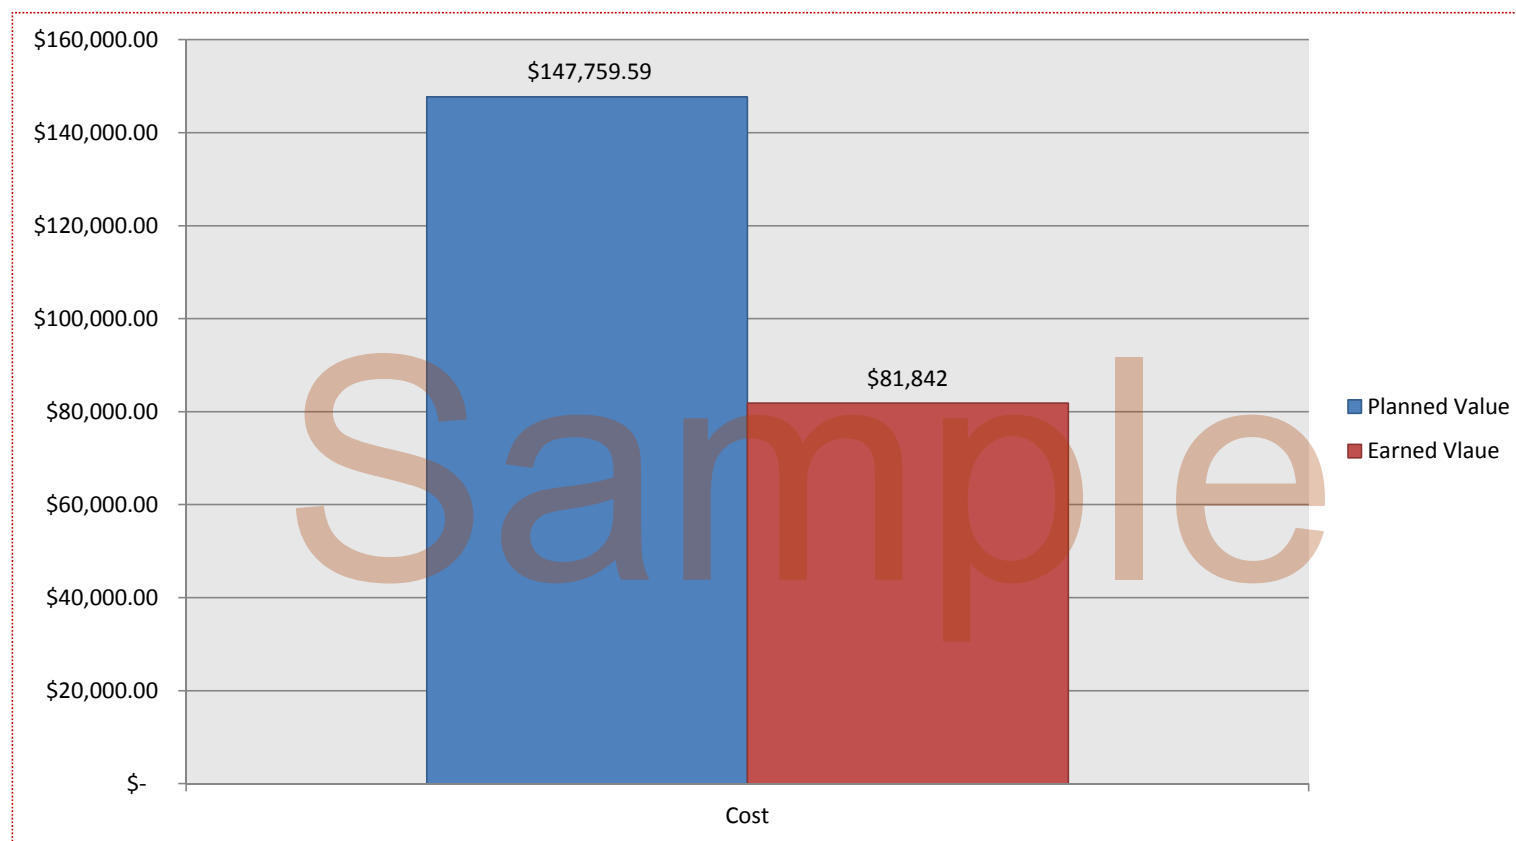

Progress Summary :

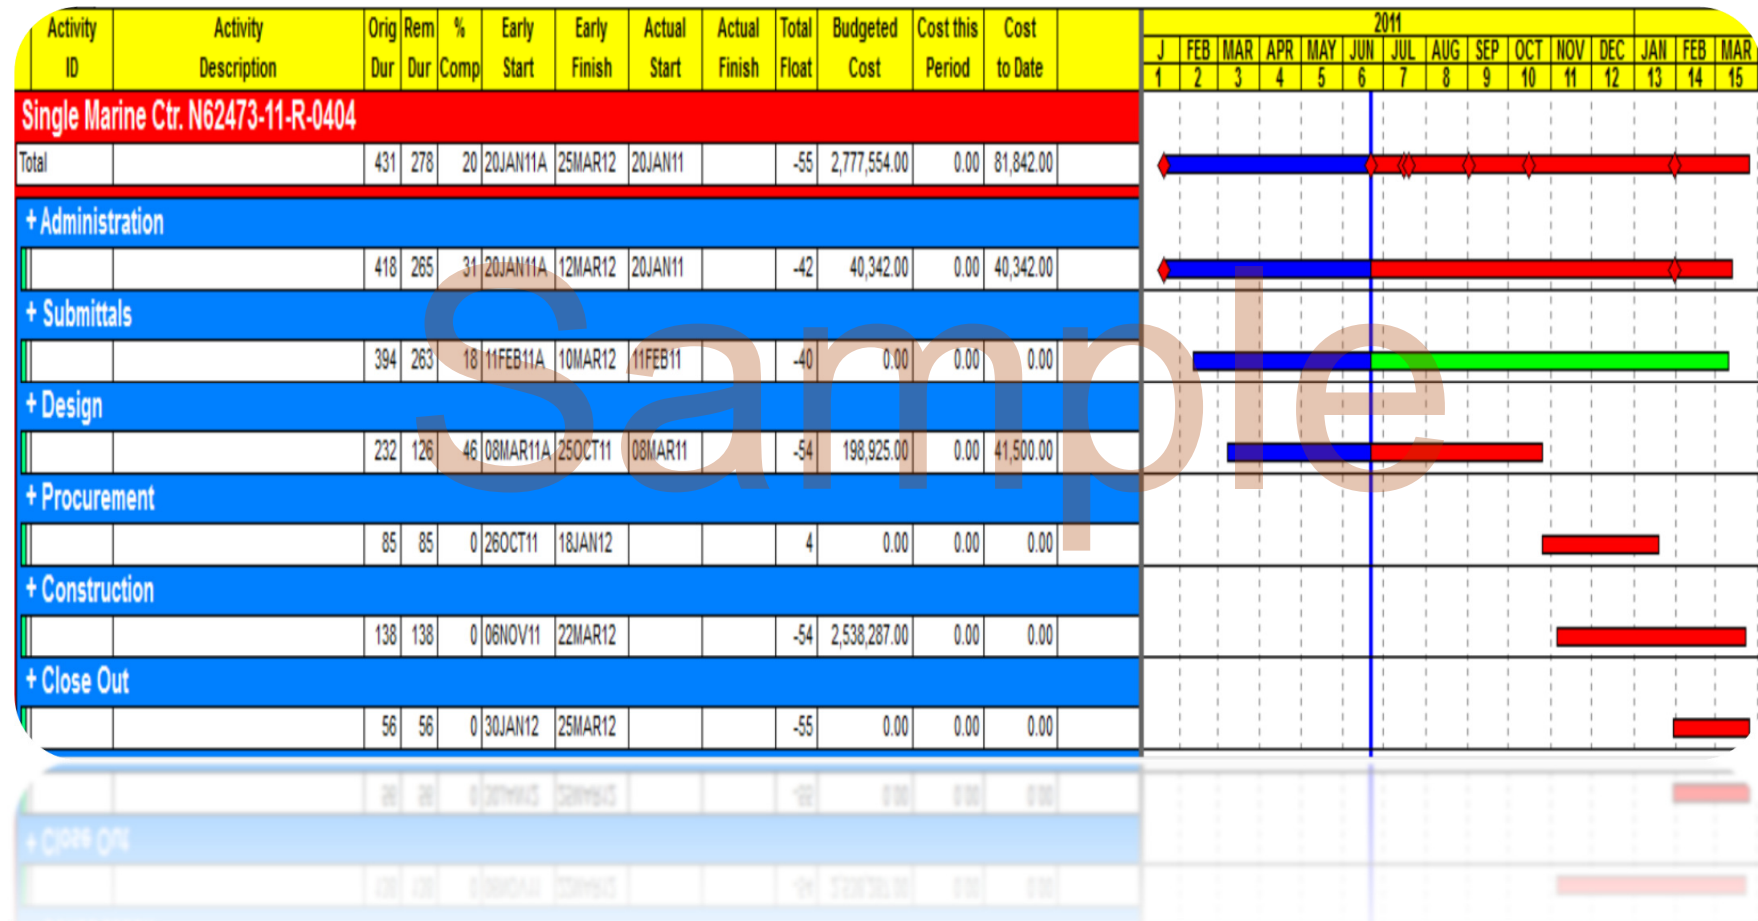

Progress Activities (From 31/5/2011 till 17/6/2011) :

Phase	Activity Description	Status	Actual % of Complete	Planned % of Complete
Submittals	Request & Receive Excavation work permit	Completed	100%	100%
	Total % of Phase		18%	69%
Design	Over The Shoulder Review	Completed	100%	100%
	Total % of Phase		46%	60%

One Month Look Ahead Activities (From 17/6/2011 till 31/7/2011) :

Phase	Activity Description	Status	Actual % of Complete	Planned % of Complete
Submittals	Approval of Submittal Register	Not-Started	0%	100%
	Approval of SOV	Not-Started	0%	100%
	Base Comm-Site Util Relocate - Outage Request	Not-Started	0%	100%
	QC Plan Submittal	Not-Started	0%	100%
	Product submittal/shop drawing samples	Not-Started	0%	100%
	Environmental Protection Plan Meeting	Not-Started	0%	100%
	Waste Management Plan Submittal	Not-Started	0%	100%
	Submit Health & Safety Plan	Not-Started	0%	100%
	Dirt & Dust control plan Submittal	Not-Started	0%	100%
	SWPP Plan Submittal	Not-Started	0%	100%
	Product Submittal/shop drawing samples Approval	Not-Started	0%	100%
	Environmental Protection Plan	Not-Started	0%	100%
	Fire Protection/Mass Notification Sys. Submittal	Not-Started	0%	100%

Phase	Activity Description	Status	Actual % of Complete	Planned % of Complete
Submittals	Approval of QC Plan	Not-Started	0%	100%
	Fire Protection/Mass Notification Sys. Approval	Not-Started	0%	80%
	Approval for Health & Safety Plan	Not-Started	0%	100%
	Finishes Submittal	Not-Started	0%	100%
	Commissioning Plan Submittal	Not-Started	0%	100%
	Approval of Commissioning Plan Submittal	Not-Started	0%	100%
	Approval of Waste Management Plan Submittal	Not-Started	0%	100%
	Approval of Dirt & Dust control plan Submittal	Not-Started	0%	100%
	Approval of SWPP Plan Submittal	Not-Started	0%	100%
	Approval for Environmental Protection Plan	Not-Started	0%	100%
	Finishes Approval	Not-Started	0%	0%
	Submission of NAS Construction Baseline Schedule	Not-Started	0%	93%
Design	Design Development 2nd Submittal	In-Progress	20%	100%
	Design Development Govt Acceptance	Not-Started	0%	100%
	Prefinal 100% Design Submittal	Not-Started	0%	93%

Delayed Activities :

Phase	Activity Description	Status	Actual % of Complete	Planned % of Complete
Delayed Activities did not affect project duration				
Submittals	Request & Receive Excavation work permit	Completed	100%	100%
	Approval of Submittal Register	Not-Started	0%	100%
	Approval of SOV	Not-Started	0%	100%
	Base Comm-Site Util Relocate - Outage Request	Not-Started	0%	100%
	QC Plan Submittal	Not-Started	0%	100%
	Product submittal/shop drawing samples	Not-Started	0%	100%
	Approval of QC Plan	Not-Started	0%	100%
	Fire Protection/Mass Notification Sys. Approval	Not-Started	0%	80%
	Approval for Health & Safety Plan	Not-Started	0%	100%
	Finishes Submittal	Not-Started	0%	100%
	Commissioning Plan Submittal	Not-Started	0%	100%
	Approval of Commissioning Plan Submittal	Not-Started	0%	100%
	Approval of Waste Management Plan Submittal	Not-Started	0%	100%
	Approval of Dirt & Dust control plan Submittal	Not-Started	0%	100%
	Approval of SWPP Plan Submittal	Not-Started	0%	100%
	Approval for Environmental Protection Plan	Not-Started	0%	100%
	Submission of NAS Construction Baseline Schedule	Not-Started	0%	93%
	Environmental Protection Plan Meeting	Not-Started	0%	100%
	Waste Management Plan Submittal	Not-Started	0%	100%
	Submit Health & Safety Plan	Not-Started	0%	100%
	Dirt & Dust control plan Submittal	Not-Started	0%	100%
	SWPP Plan Submittal	Not-Started	0%	100%
	Product Submittal/shop drawing samples Approval	Not-Started	0%	100%
	Environmental Protection Plan	Not-Started	0%	100%
	Fire Protection/Mass Notification Sys. Submittal	Not-Started	0%	100%
	Approval of Submittal Register	Not-Started	0%	100%
	Approval of SOV	Not-Started	0%	100%
Delayed Activities that affected project duration				
Design	Design Development Submittal	In-Progress	20%	100%

Conclusion : The Contractor is behind schedule by 55 Calendar days, he is responsible to recover 37 Calendar days since the owner is responsible of 18 Calendar days from these delays.
These days must be recovered from the critical activities which are the design and construction activities.

Sample
