


Act ID	Description	Orig Dur	Percent Complete	Early Start	Early Finish	Target Start	Target Finish	Finish Variance	2015												2016							
									FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP
A/E DESIGN																												
DESIGN DOCUMENTS & PERMITS																												
1000	FINALIZE CONTRACT TERMS WITH A/E FIRM	15	100	23FEB15 A	18MAR15 A	23FEB15	18MAR15	0	[Gantt bar: 23FEB15 to 18MAR15]																			
1010	BASIC DESIGN DOCUMENT DEVELOPMENT	50	100	16MAR15 A	01JUN15 A	16MAR15	01JUN15	0	[Gantt bar: 16MAR15 to 01JUN15]																			
1020	ALVOGEN REVIEW AND APPROVAL OF BASIC DESIGN DOCS	20	100	02JUN15 A	21AUG15 A	02JUN15	21AUG15	0	[Gantt bar: 02JUN15 to 21AUG15]																			
1030	ISSUE FOR BID DOCUMENTS DEVELOPMENT	50	100	15JUN15 A	14AUG15 A	15JUN15	14AUG15	0	[Gantt bar: 15JUN15 to 14AUG15]																			
1040	EARLY RELEASE FOR DEMOLITION PACKAGE	20	100	27MAR15 A	01JUN15 A	27MAR15	01JUN15	0	[Gantt bar: 27MAR15 to 01JUN15]																			
1050	CHILLERS/BOILERS/AHU'S DESIGN PACKAGE	30	100	27MAR15 A	07AUG15 A	27MAR15	07AUG15	0	[Gantt bar: 27MAR15 to 07AUG15]																			
1060	ALVOGEN COMPLETE REVIEW OF EXISTING LAYOUT	15	100	23FEB15 A	30APR15 A	23FEB15	30APR15	0	[Gantt bar: 23FEB15 to 30APR15]																			
1070	DEVELOPMENT OF INSTRUMENTATION & CONTROLS	30	100	16MAR15 A	02OCT15 A	16MAR15	09SEP15	-17	[Gantt bar: 16MAR15 to 09SEP15]																			
1080	Completion of Electrical & USP System DD's	10	100	01JUN15 A	26AUG15 A	01JUN15	26AUG15	0	[Gantt bar: 01JUN15 to 26AUG15]																			
CM - PRECONSTRUCTION SERVICES																												
1100	GMP ESTIMATE SUBMITTED (+/-10%)	30	100	02JUN15 A	13JUL15 A	02JUN15	13JUL15	0	[Gantt bar: 02JUN15 to 13JUL15]																			
1110	ALVOGEN REVIEW & APPROVE THE GMP	25	100	10JUL15 A	24JUL15 A	10JUL15	24JUL15	0	[Gantt bar: 10JUL15 to 24JUL15]																			
1120	SUBMIT CHANGES FROM BASIC DESIGN TO IFB'S	25	100	17AUG15 A	23SEP15 A	17AUG15	23SEP15	0	[Gantt bar: 17AUG15 to 23SEP15]																			
1130	FILE AND OBTAIN DEMO PERMITS FOR PROCESS SUITE	20	100	02JUN15 A	14AUG15 A	02JUN15	14AUG15	0	[Gantt bar: 02JUN15 to 14AUG15]																			
1131	Permit Package & Obtain Permit for CUP fitout	40	100	01JUN15 A	08OCT15 A	01JUN15	16SEP15	-16	[Gantt bar: 01JUN15 to 16SEP15]																			
1132	Develop Permit package for Process Suite Fitout	50	100	02JUN15 A	11SEP15 A	02JUN15	14AUG15	-19	[Gantt bar: 02JUN15 to 14AUG15]																			
1133	File for and Obtain Process Suite fitout permit	30	100	03SEP15 A	14OCT15 A	03SEP15	14OCT15	0	[Gantt bar: 03SEP15 to 14OCT15]																			
1140	COMPLETE REMAINING AIR PERMITS	30	100	23FEB15 A	12MAR15 A	23FEB15	12MAR15	0	[Gantt bar: 23FEB15 to 12MAR15]																			
ALVOGEN - PROCURE LONG LEAD PROCESS EQUIPMENT																												
OWNER PURCHASED PROCESS EQUIPMENT - Summary																												
1200	AWD/SUB/APP FLUID BED DRYER	50	100	23FEB15 A	15MAY15 A	23FEB15	15MAY15	0	[Gantt bar: 23FEB15 to 15MAY15]																			
1201	SUBMIT/APPROVE FLUID BED AHU & OTHER EQUIPMENT	20	100	03JUN15 A	14AUG15 A	03JUN15	14AUG15	0	[Gantt bar: 03JUN15 to 14AUG15]																			
1202	SUBMIT/APPROVE TORIT DUST COLLECTOR SYSTEM	20	100	10JUL15 A	14AUG15 A	10JUL15	14AUG15	0	[Gantt bar: 10JUL15 to 14AUG15]																			
1203	SUBMIT / APPROVE INSTRUMENTATION & CONTROLS	40	100	11JUN15 A	14JAN16 A	11JUN15	11SEP15	-85	[Gantt bar: 11JUN15 to 11SEP15]																			
1210	FABRICATE & DELIVER FLUID BED DRYER (9 MONTHS)	157	100	18MAY15 A	05JAN16 A	18MAY15	08JAN16	3	[Gantt bar: 18MAY15 to 08JAN16]																			
1211	FABRICATE & DELIVER THE FLUID BED AHU	134	100	17AUG15 A	18DEC15 A	17AUG15	22FEB16	44	[Gantt bar: 17AUG15 to 22FEB16]																			
1212	FABRICATE & DELIVER PRO EXHAUST BLOWER	114	100	17AUG15 A	12JAN16 A	17AUG15	25JAN16	9	[Gantt bar: 17AUG15 to 25JAN16]																			
1213	FABRICATE & DELIVER PRO DUST COLLECTOR	121	100	28AUG15 A	06JAN16 A	28AUG15	16FEB16	29	[Gantt bar: 28AUG15 to 16FEB16]																			
1214	FAB & DELIV DUST COLL EXPLOSION PROTECTION SYS	44	100	21OCT15 A	21JAN16 A	21OCT15	21DEC15	-21	[Gantt bar: 21OCT15 to 21DEC15]																			
1215	FAB & DELIV PRO AFTER FILTER UNIT	107	100	17AUG15 A	14JAN16 A	17AUG15	14JAN16	0	[Gantt bar: 17AUG15 to 14JAN16]																			
1216	FAB & DELIVER STEAM GENERATOR UNIT	70	100	08OCT15 A	14JAN16 A	08OCT15	15JAN16	1	[Gantt bar: 08OCT15 to 15JAN16]																			


Start date 23FEB15
Finish date 23NOV16
Data date 31JAN16
Run date 11FEB16
Page number 1A
 © Primavera Systems, Inc.

ALVOGEN BID SCHEDULE
FLUID BED & UTILITIES BUILDING
HENDERSON CONSTRUCTORS, INC.

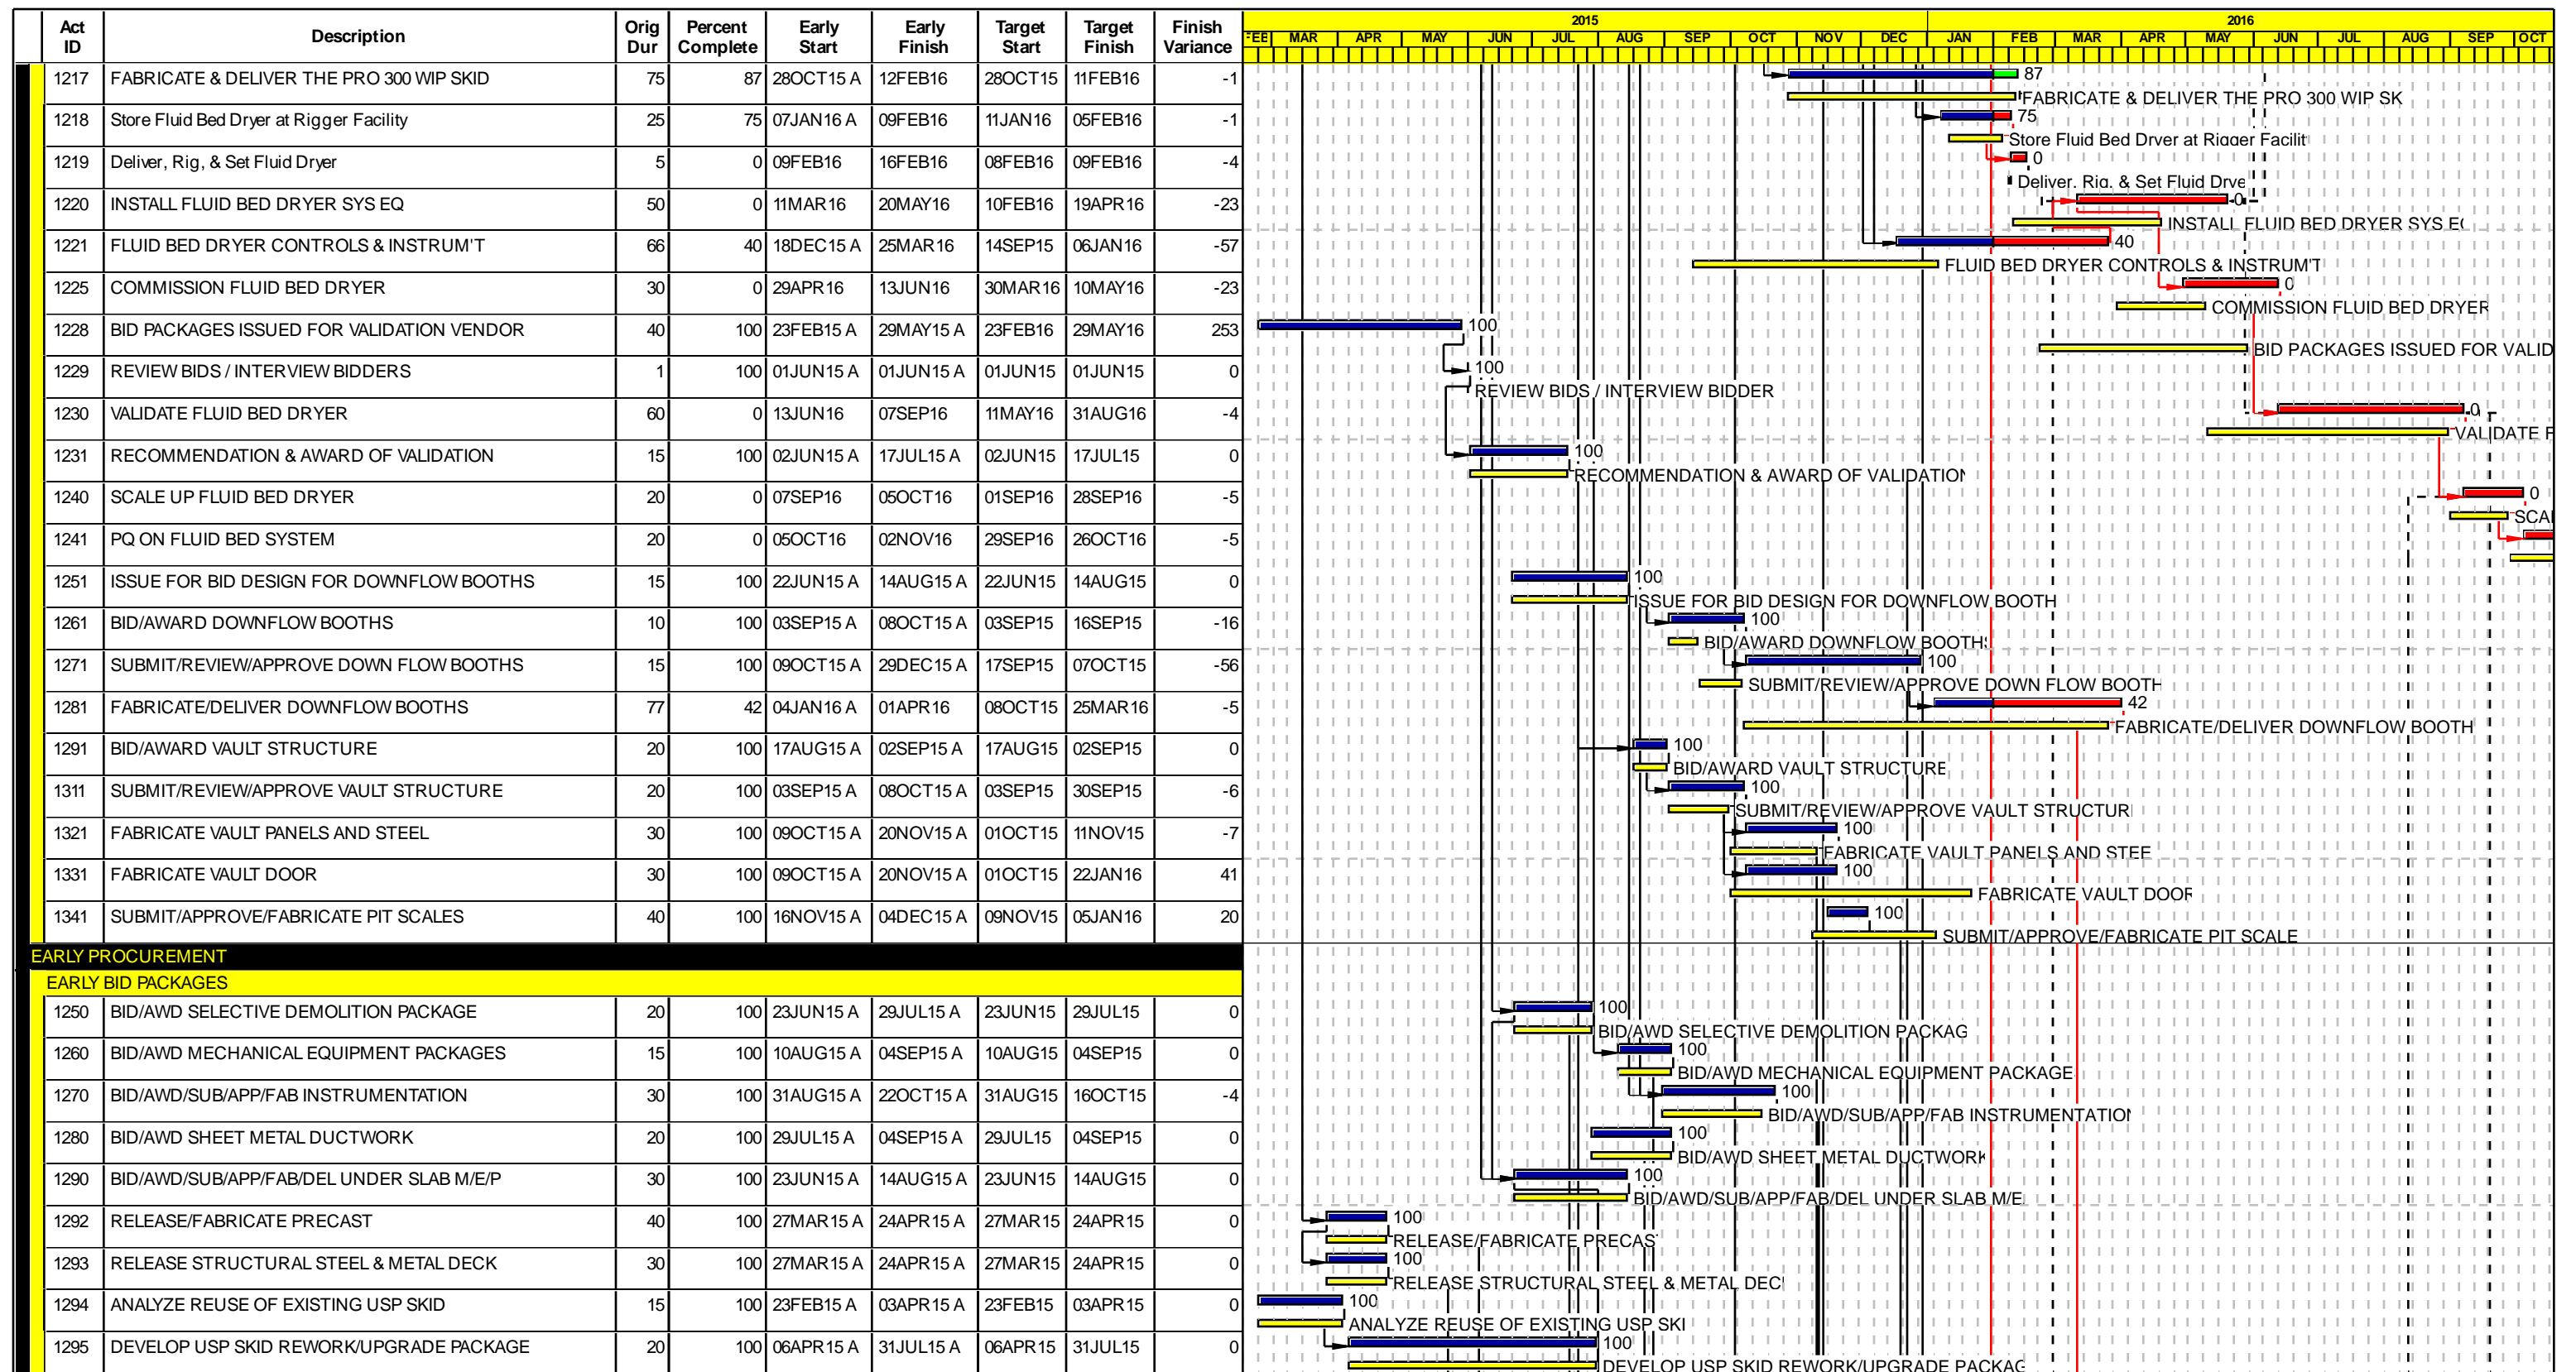


Start date	23FEB15
Finish date	23NOV16
Data date	31JAN16
Run date	11FEB16
Page number	2A
© Primavera Systems, Inc.	

ALVOGEN BID SCHEDULE
FLUID BED & UTILITIES BUILDING
HENDERSON CONSTRUCTORS, INC.

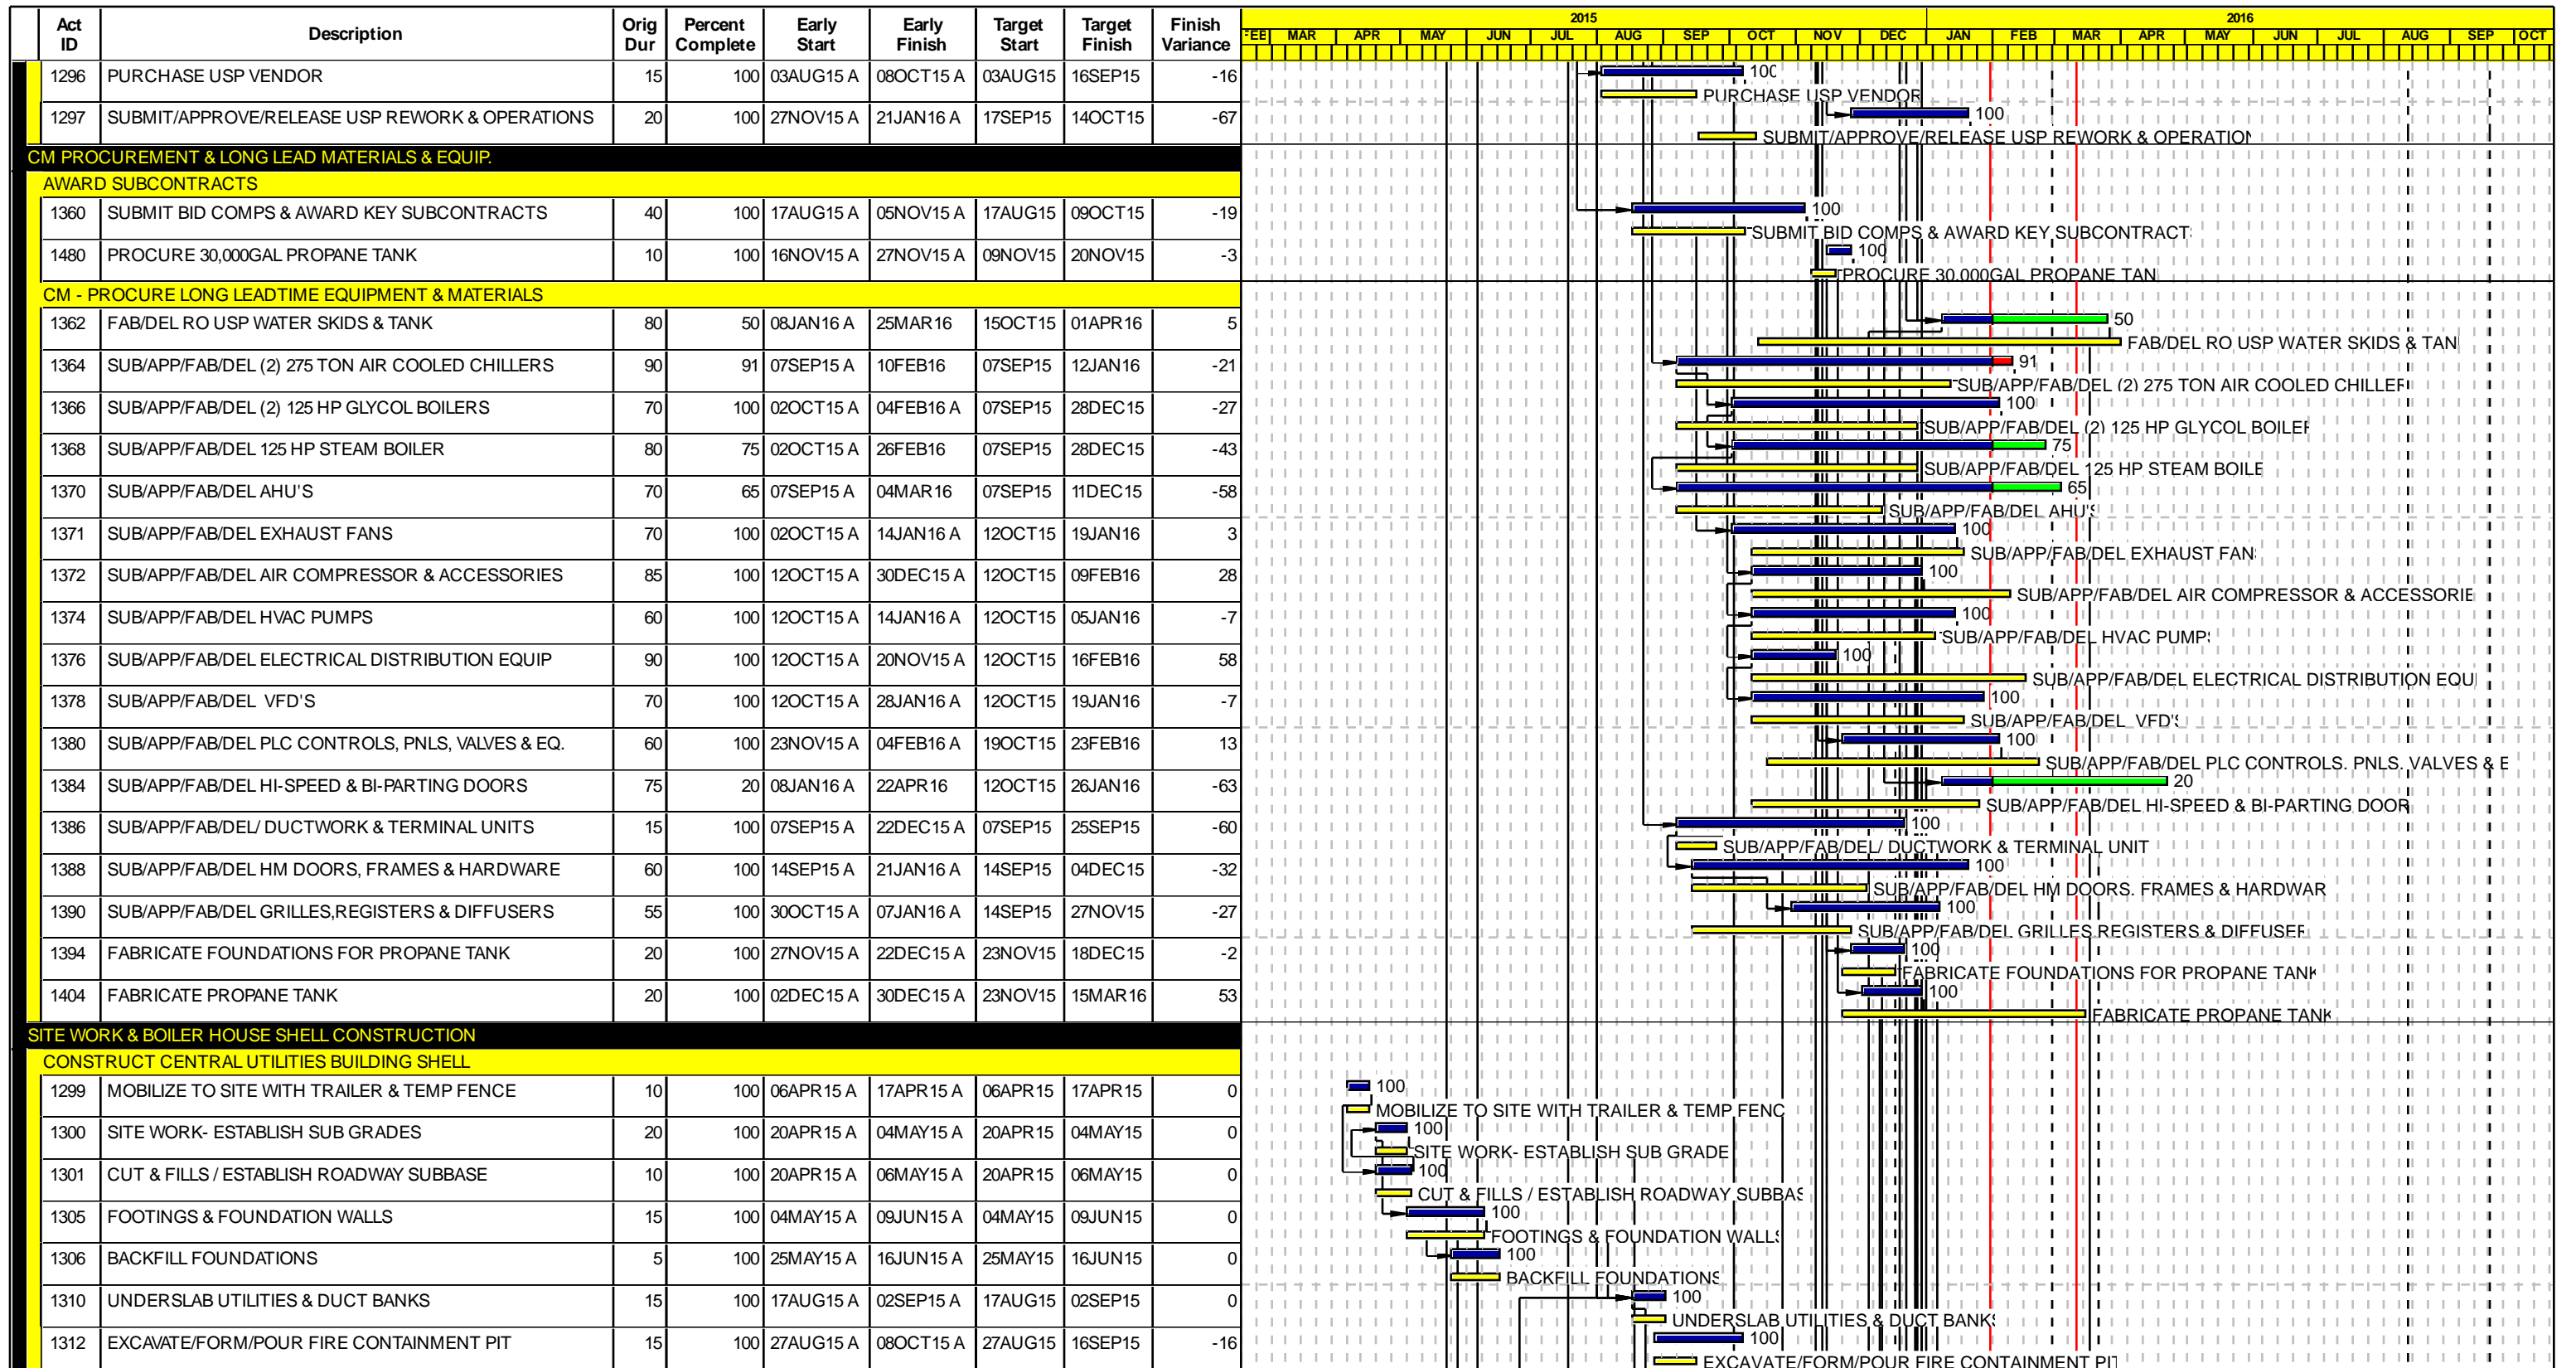


Start date 23FEB15
Finish date 23NOV16
Data date 31JAN16
Run date 11FEB16
Page number 3A
 © Primavera Systems, Inc.

ALVOGEN BID SCHEDULE
FLUID BED & UTILITIES BUILDING
HENDERSON CONSTRUCTORS, INC.

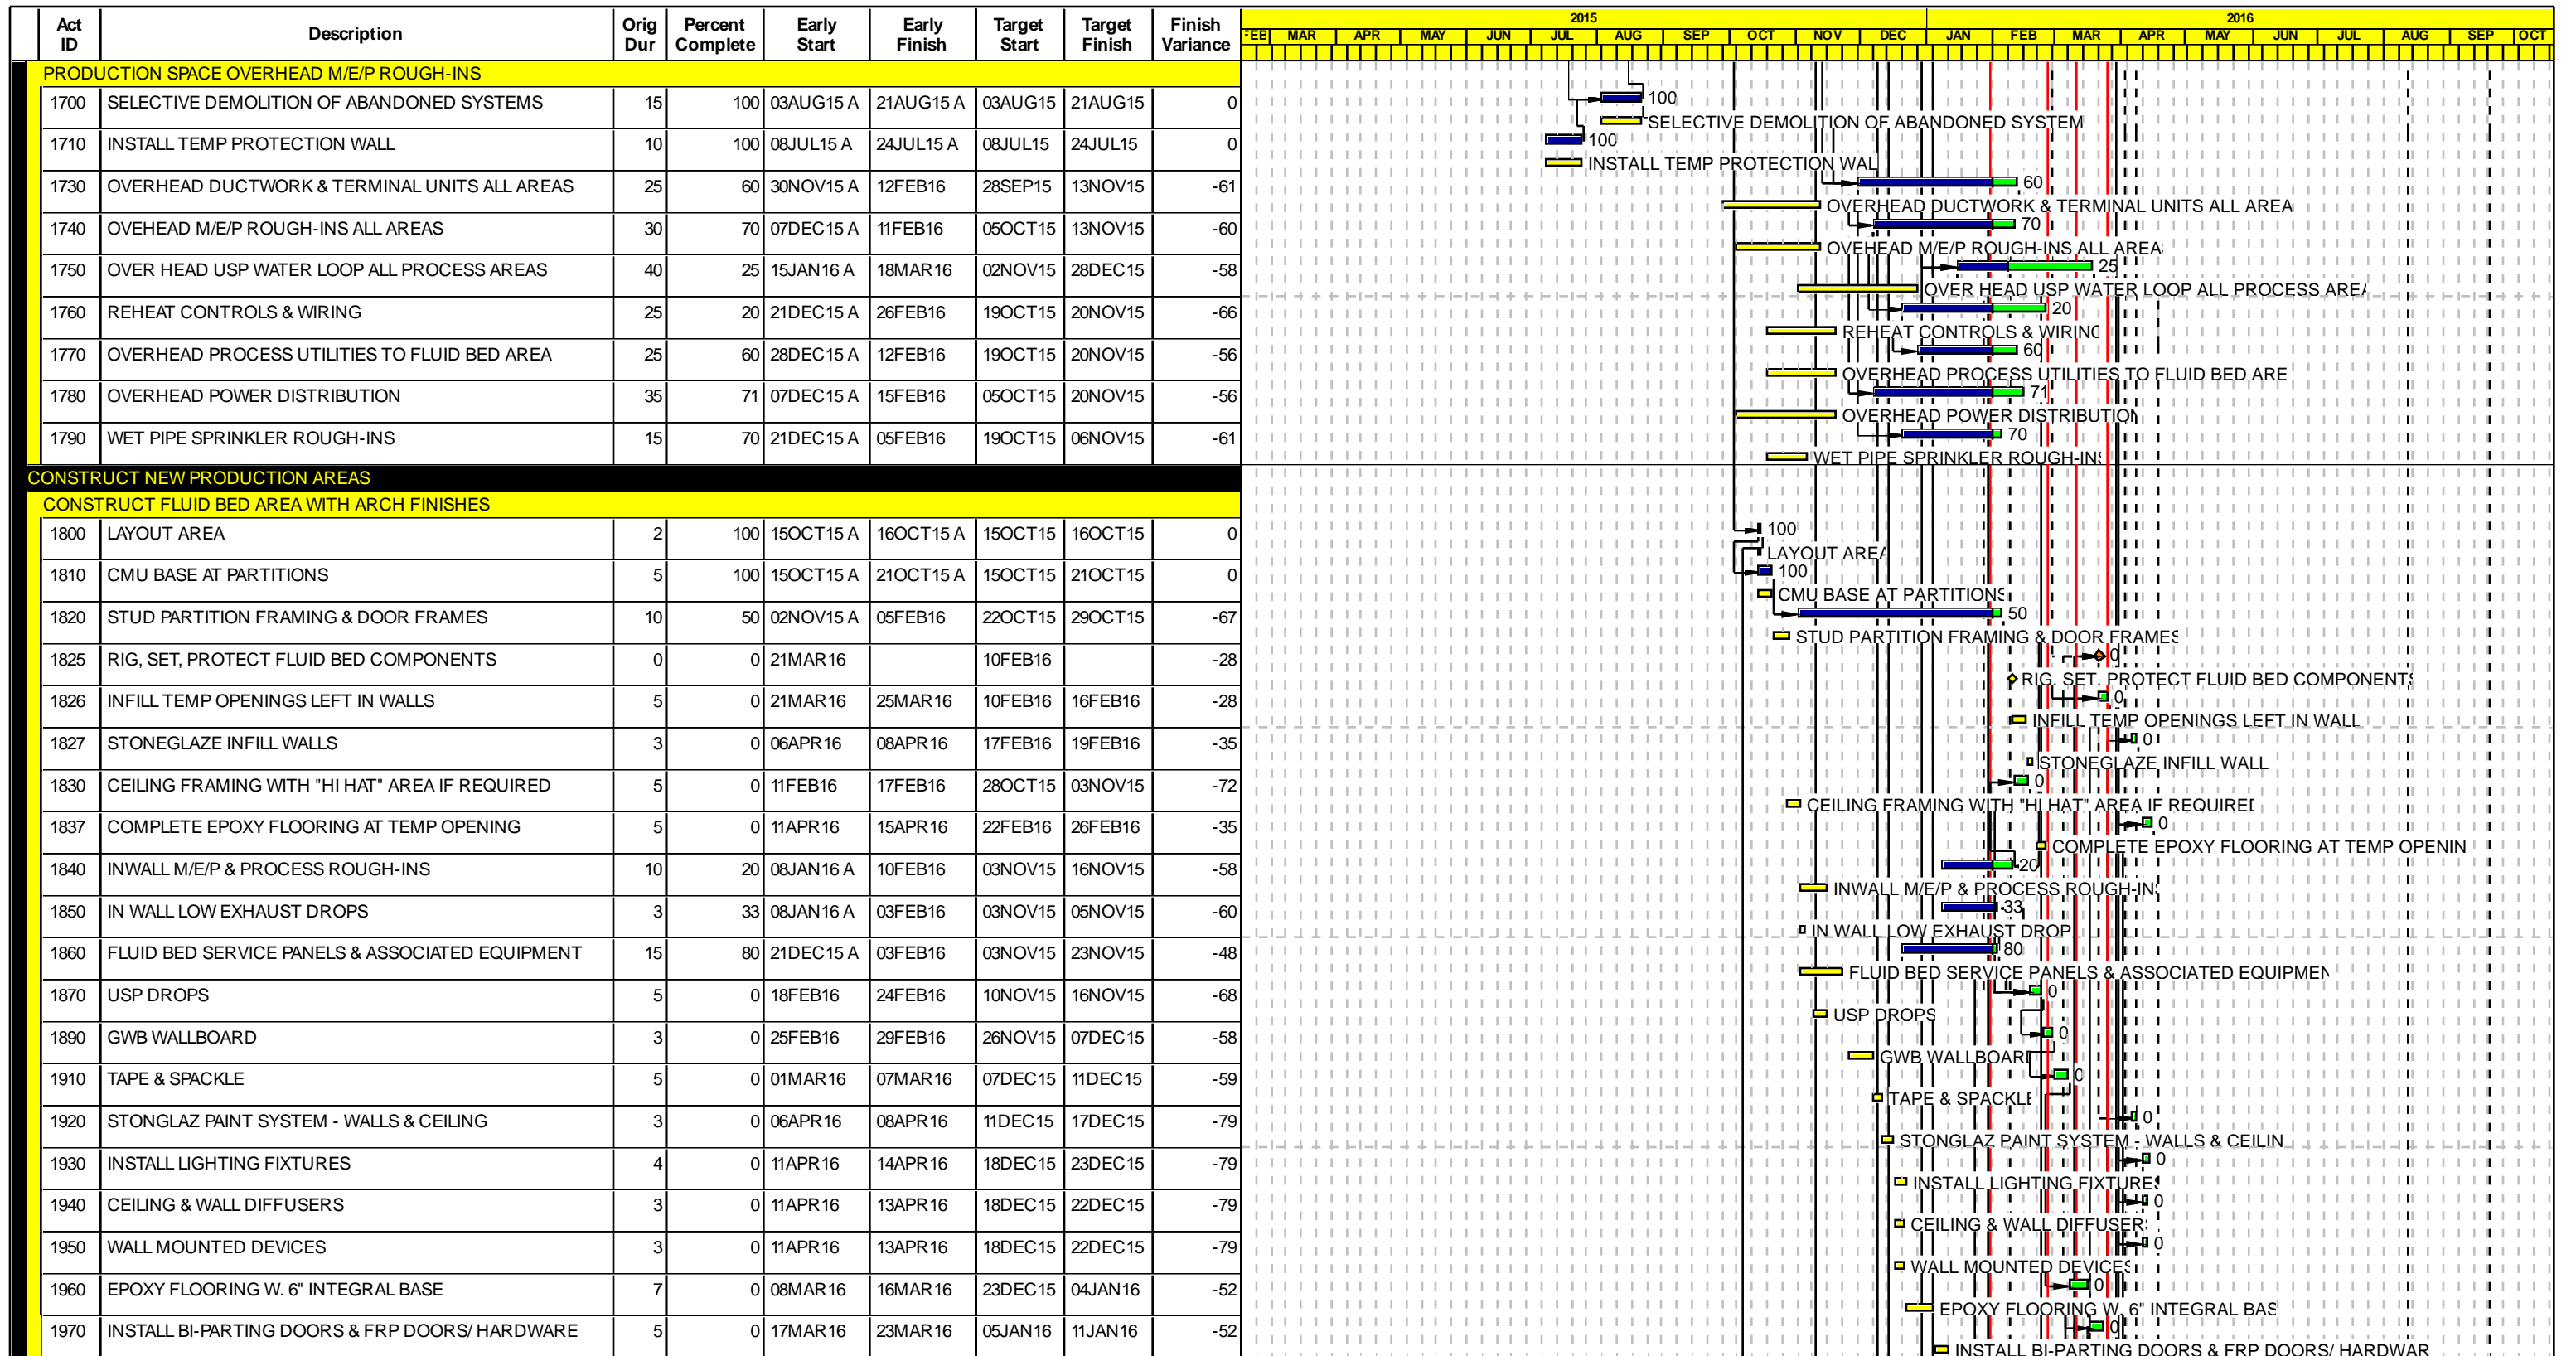


Start date 23FEB15
Finish date 23NOV16
Data date 31JAN16
Run date 11FEB16
Page number 6A
 © Primavera Systems, Inc.

ALVOGEN BID SCHEDULE
FLUID BED & UTILITIES BUILDING
HENDERSON CONSTRUCTORS, INC.

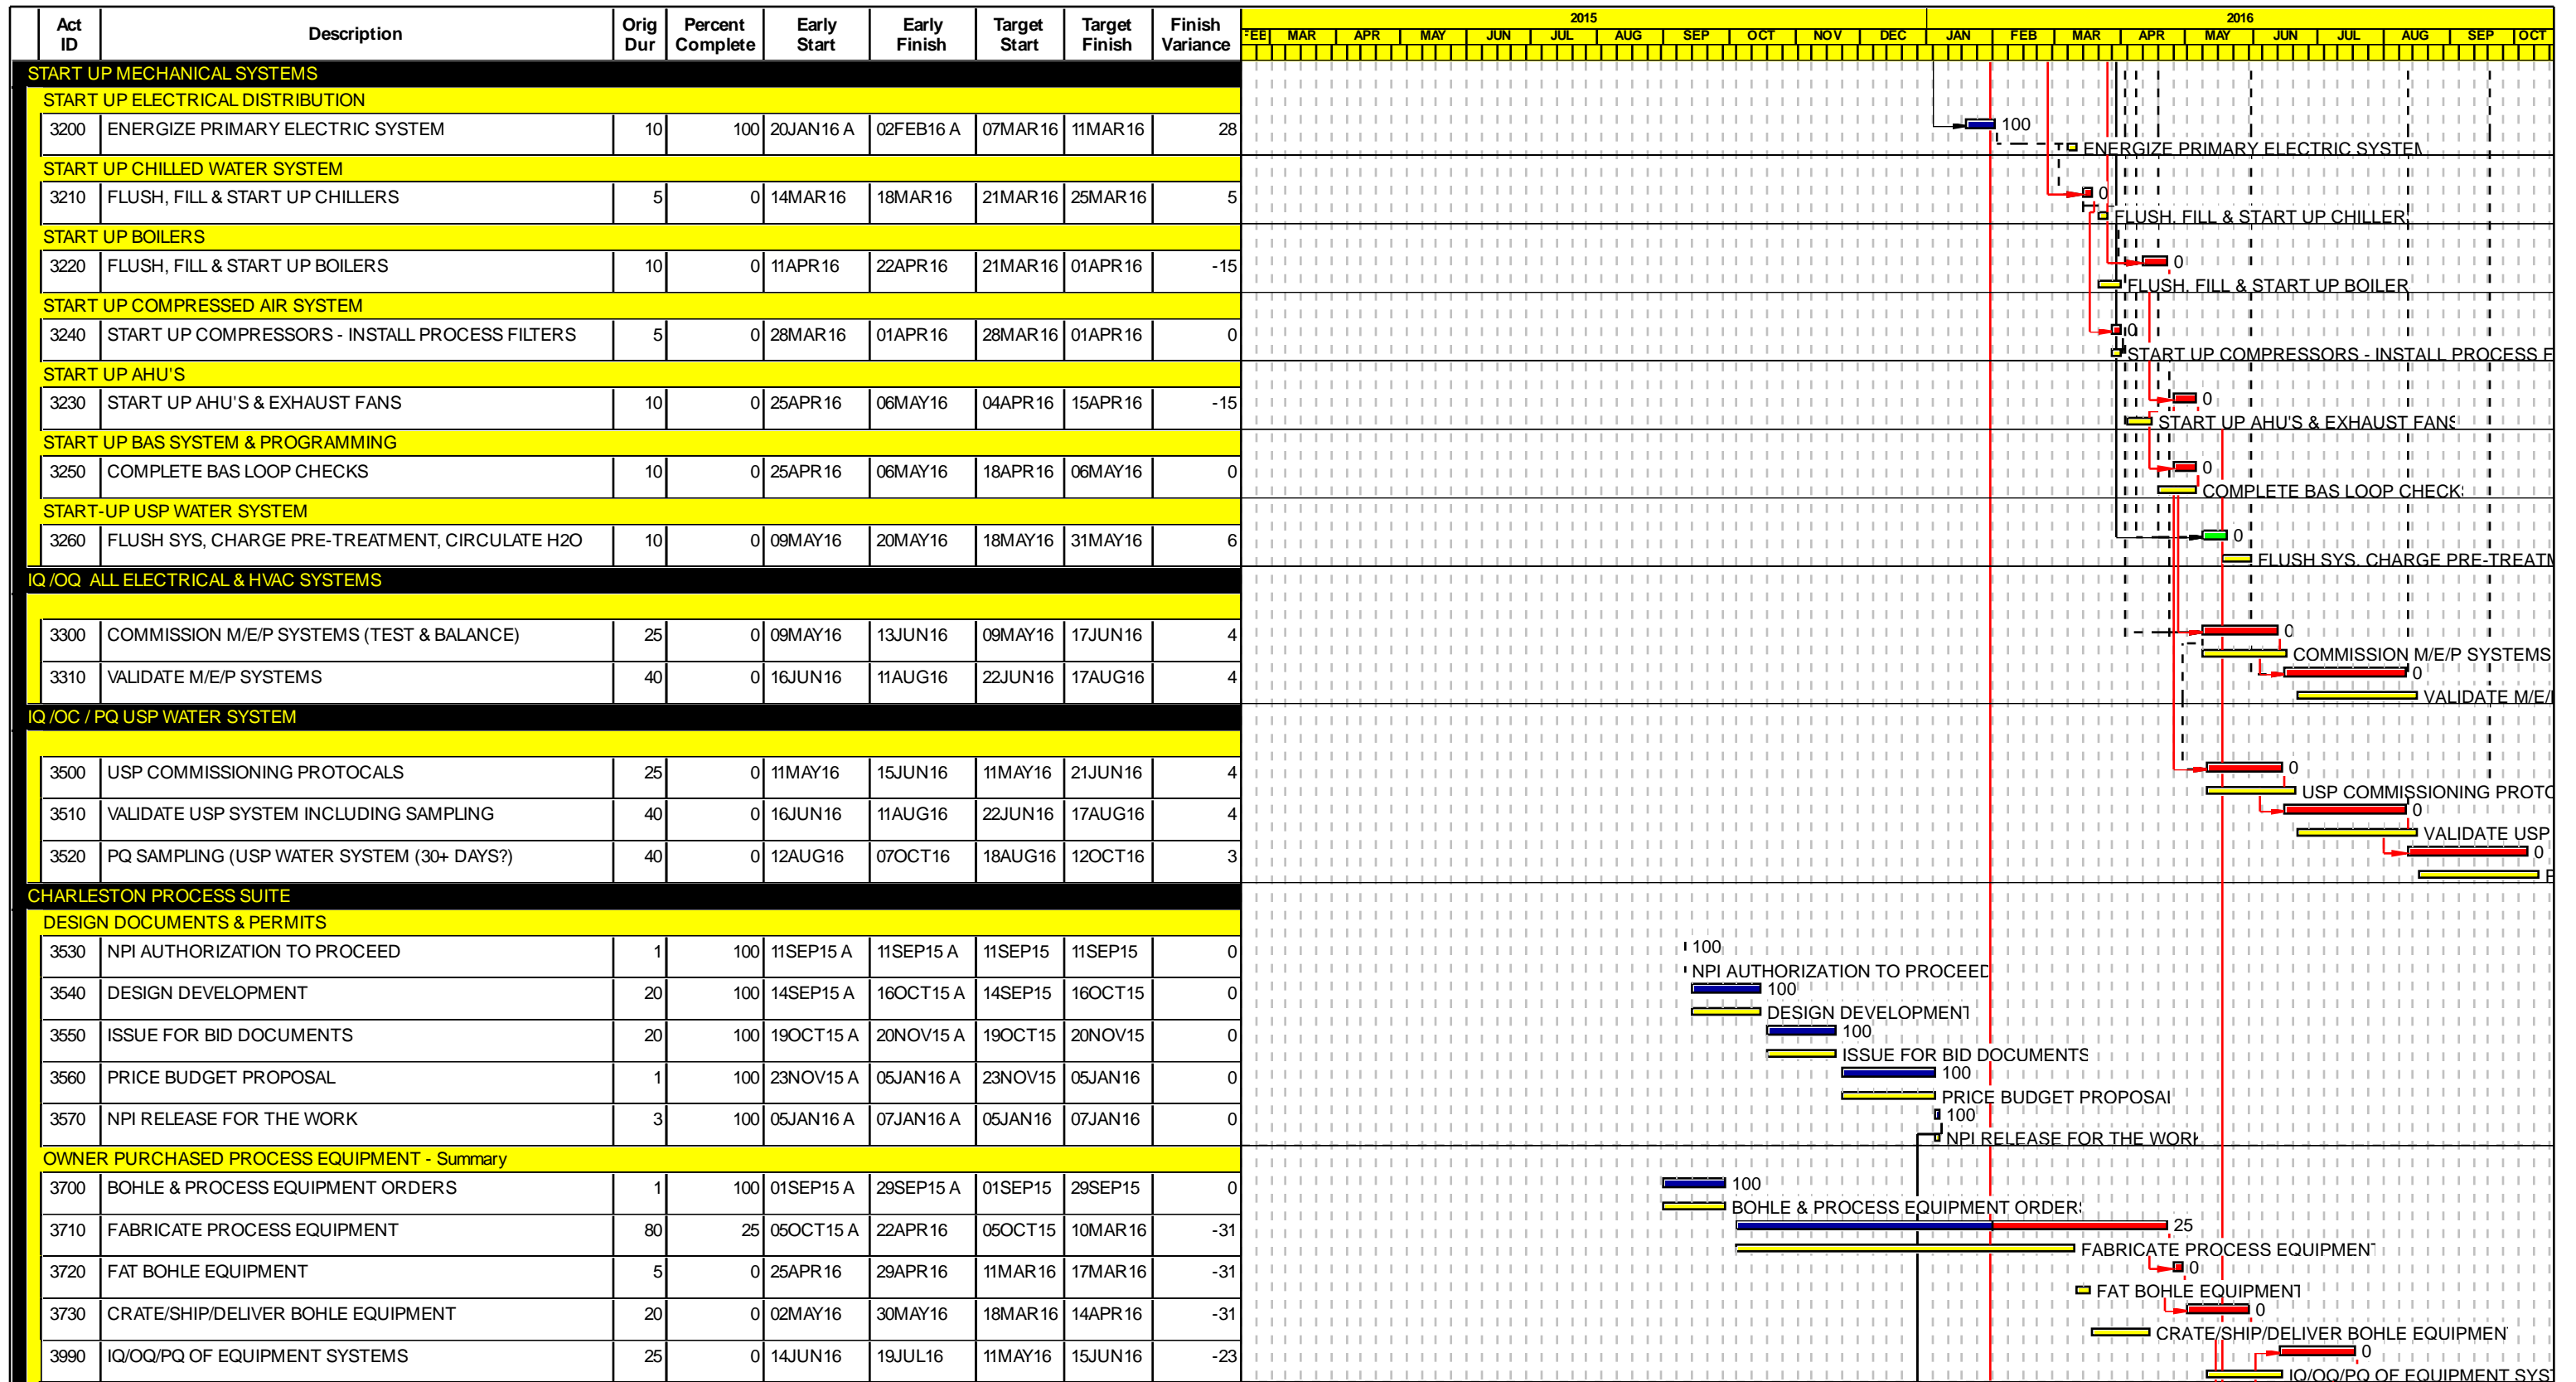

Start date 23FEB15
Finish date 23NOV16
Data date 31JAN16
Run date 11FEB16
Page number 9A
 © Primavera Systems, Inc.

ALVOGEN BID SCHEDULE
FLUID BED & UTILITIES BUILDING
HENDERSON CONSTRUCTORS, INC.

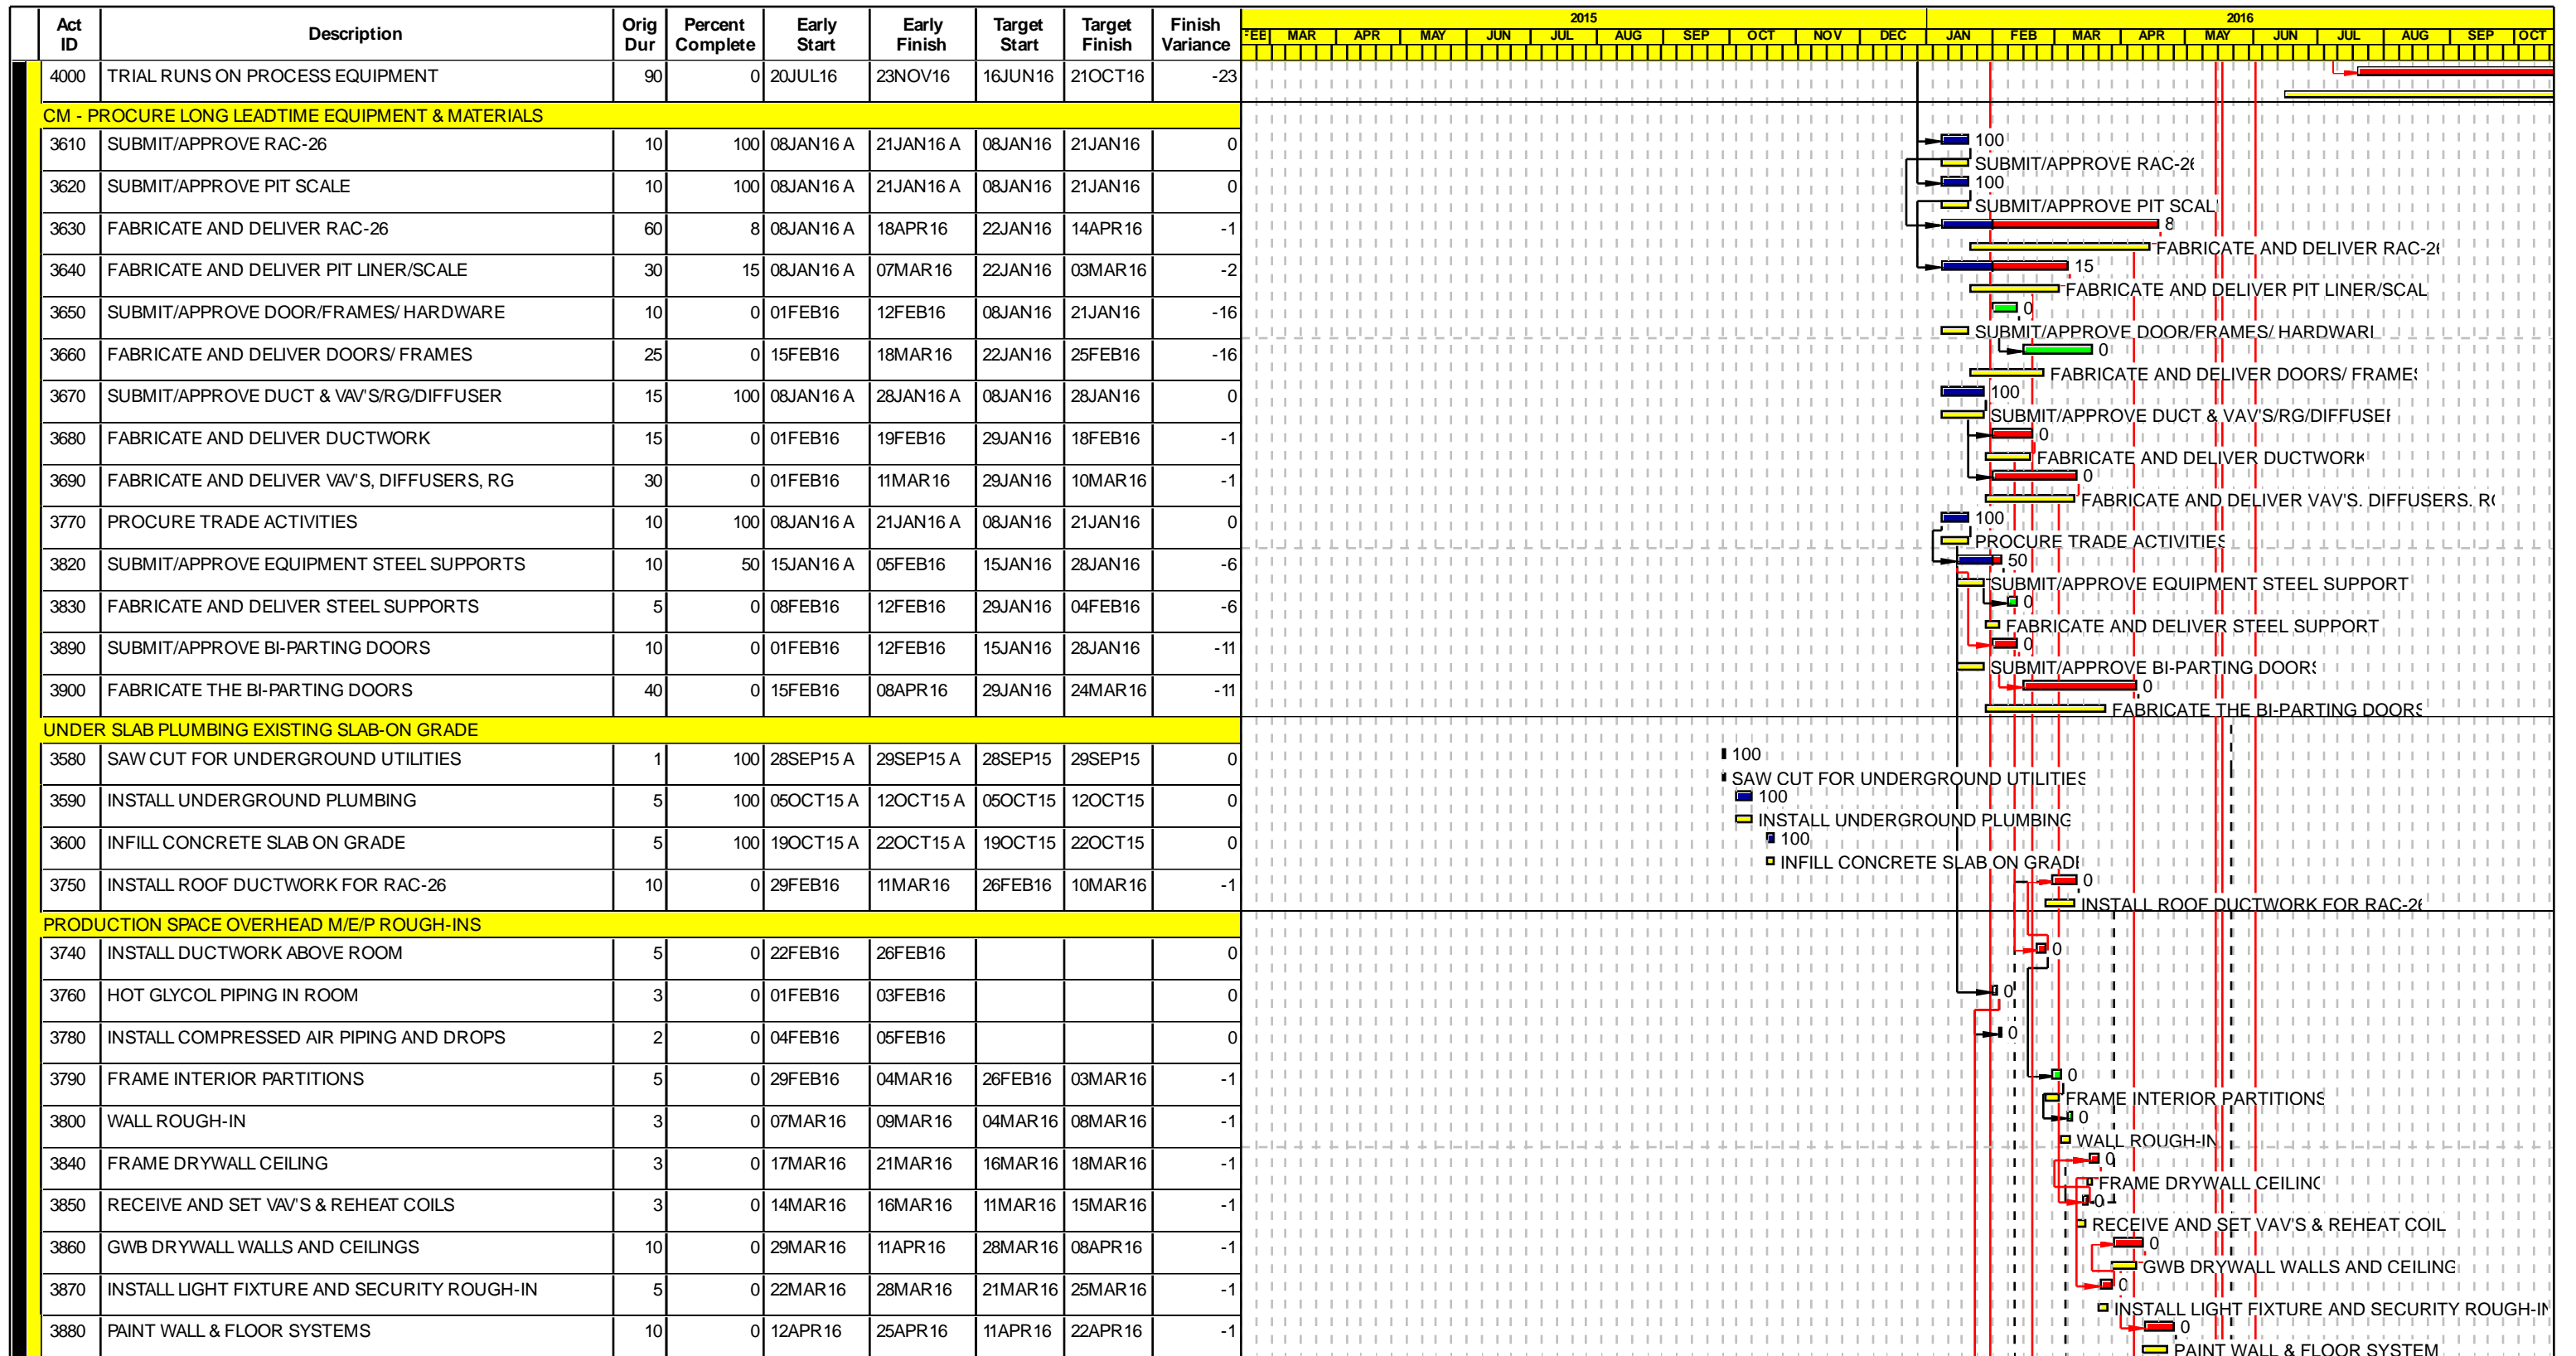

Start date 23FEB15
Finish date 23NOV16
Data date 31JAN16
Run date 11FEB16
Page number 10A
 © Primavera Systems, Inc.

ALVOGEN BID SCHEDULE
FLUID BED & UTILITIES BUILDING
HENDERSON CONSTRUCTORS, INC.

Act ID	Description	Orig Dur	Percent Complete	Early Start	Early Finish	Target Start	Target Finish	Finish Variance	2015												2016									
									FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	
3910	RECEIVE AND SET BI-PARTING DOORS	5	0	07JUN16	13JUN16	02MAY16	06MAY16	-25																						0
3920	RECEIVE AND SET PROCESS EQUIPMENT	5	0	31MAY16	06JUN16	25APR16	29APR16	-25																						0
3930	RECEIVE AND SET SCALE	2	0	07MAR16	09MAR16	04MAR16	07MAR16	-2																						0
START UP AHU'S																														
3940	RECEIVE AND SET RAC-26	2	0	18APR16	20APR16	15APR16	18APR16	-1																						0
3950	INSTALL CHILLED WATER & HOT GLYCOL ON ROOF	5	0	04FEB16	10FEB16	27JAN16	02FEB16	-6																						0
3960	MEP CONNECTIONS TO RAC-26	5	0	20APR16	27APR16	19APR16	25APR16	-1																						0
3970	START-UP RAC-26	1	0	06MAY16	06MAY16	26APR16	26APR16	-8																						0
3980	START-UP AND COMMISSION MEP SYSTEMS	10	0	31MAY16	13JUN16	27APR16	10MAY16	-23																						0

Start date 23FEB15
Finish date 23NOV16
Data date 31JAN16
Run date 11FEB16
Page number 11A
 © Primavera Systems, Inc.

ALVOGEN BID SCHEDULE
FLUID BED & UTILITIES BUILDING
HENDERSON CONSTRUCTORS, INC.
