


Infinity Condo Detailed Schedule Layout

y ID	Activity Name	Original Duration	Start	Finish	Predecessors	2023 J F M A M J J A	S
finity Conde	0	570	Jun-05-23	Sep-02-25			
Key Dates / N		570	Jun-05-23	Sep-02-25			÷
		495	Jun-05-23	May-14-25			:
Construction							1
Piling & Founda	ation	149	Jun-05-23	Jan-05-24			
Tower Crane		315	Jul-25-23	Oct-17-24			
Concrete Work		344	Aug-28-23	Jan-06-25			
Tower Decks		246	Sep-05-23	Aug-21-24			
Level 2		63	Sep-05-23	Dec-04-23			ļ
Typical floors		201	Oct-17-23	Jul-31-24			
Level 3		43	Oct-17-23	Dec-18-23			
Pour 1 North		33	Oct-17-23	Dec-04-23			
3200	Frame Shoring	6	Oct-17-23	Oct-24-23	3173		
3201	Reinforce	3	Oct-24-23	Oct-26-23	3200		
3202	MEP	2	Oct-25-23	Oct-26-23	3201, 3201		
3203	Inspect	1	Oct-26-23	Oct-26-23	3201, 3202, 3201		
3204	Pour Deck	1	Nov-20-23	Nov-20-23	3203, 3185		
3206	Vertical	3	Nov-20-23	Nov-22-23	3204, B3010		
3207	Stress	1 4	Nov-21-23	Nov-21-23	3204		
3208 3208A	Strip Re-shore	3	Nov-22-23 Nov-22-23	Nov-29-23 Nov-28-23	3207, 3206 3208, 3178		-
3208A 3208B	FRP Perimeter Drop Beams	7	Nov-22-23	Dec-04-23	3208, 3178 3208A		· ;
Pour 2 South		19	Nov-20-23	Dec-18-23	3200A		-
3210	Frame Shoring	6	Nov-20-23	Nov-29-23	3200, 3180, 3182		
3210	Reinforce	3	Dec-04-23	Dec-06-23	3210		
3212	MEP	2	Dec-05-23	Dec-06-23	3211, 3211		
3213	Inspect	1	Dec-06-23	Dec-06-23	3211, 3212, 3211	J	
3214	Pour Deck	1	Dec-07-23	Dec-07-23	3213		
3216	Vertical	3	Dec-08-23	Dec-12-23	3214		
3217	Stress	1	Dec-08-23	Dec-08-23	3214		
3218	Strip	4	Dec-11-23	Dec-14-23	3217, 3208, 3216		1
3218A	Re-shore	3	Dec-11-23	Dec-13-23	3218, 3187		1
3218B	FRP Perimeter Drop Beams	6	Dec-11-23	Dec-18-23	3218A, 3208B		1
Level 4		22	Dec-04-23	Jan-04-24			
Pour 1 North		14	Dec-04-23	Dec-21-23			
3221	Frame Shoring	3	Dec-04-23	Dec-06-23	3206		
3222	Reinforce	2	Dec-06-23	Dec-07-23	3221		
3223	MEP	2	Dec-07-23	Dec-08-23	3222, 3222		
3224	Inspect	1	Dec-08-23	Dec-08-23	3222, 3223, 3222		
3225	Pour Deck	1	Dec-11-23	Dec-11-23	3224, 3206		-
3228 3227	Stress Vertical	4	Dec-12-23 Dec-12-23	Dec-12-23 Dec-15-23	3225 3225		· •
3229	Strip	2	Dec-13-23	Dec-13-23	3225 3228, 3218, 3227		:
3229 3229A	Re-shore	3	Dec-15-23	Dec-14-23	3229		-
3229B	FRP Perimeter Drop Beams	3	Dec-19-23	Dec-21-23	3229A, 3218B		1
Pour 2 South		11	Dec-19-23	Jan-04-24	,		1
3231	Frame Shoring	3	Dec-19-23	Dec-21-23	3216		
3232	Reinforce	2	Dec-20-23	Dec-21-23	3231		
3233	MEP	2	Dec-21-23	Dec-22-23	3232, 3232		
3234	Inspect	1	Dec-22-23	Dec-22-23	3232, 3233, 3232		
3235	Pour Deck	1	Dec-26-23	Dec-26-23	3234, 3216		1
3238	Stress	1	Dec-27-23	Dec-27-23	3235		
3237	Vertical	4	Dec-27-23	Jan-02-24	3235		-
Remaining Work Summary Critical Remaining Work Milestone Page 1 of 2						Data Date: Jun-05 Project Start: Jun- Project Finish: Se	-0



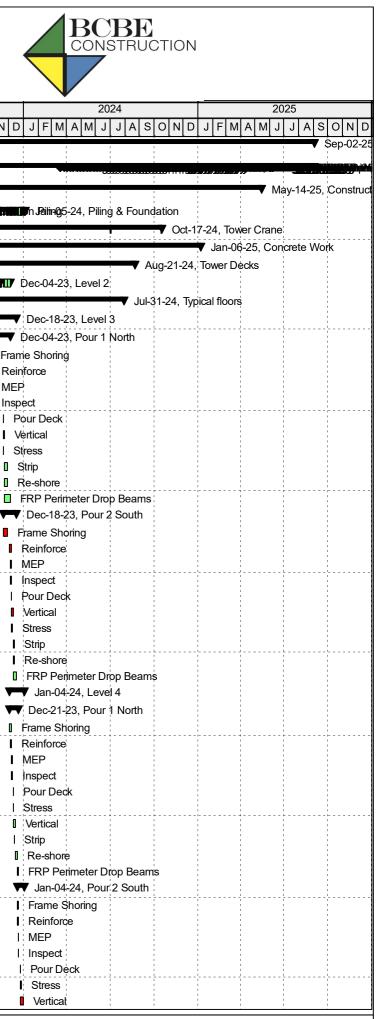

Infinity Condo **Detailed Schedule Layout**

	Activity Name								
ivity ID		Original	Start	Finish	Predecessors	2023	2024 2025	2025	
		Duration				JFMAMJJASON	D J F M A M J J A S O N D J F M A M J J A	SON	
3239	Strip	2	Dec-28-23	Dec-29-23	3238, 3229, 3237		l Strip		
3239A	Re-shore	3	Jan-02-24	Jan-04-24	3239, 3218A		Re-shore	5 5	
3239B	FRP Perimeter Drop Beams	3	Jan-02-24	Jan-04-24	3239A, 3229B		FRP Perimeter Drop Beams		
Level 5		18	Dec-21-23	Jan-17-24			VII Jan-17-24, Level 5	1	
Level 6		15	Jan-08-24	Jan-26-24			M Jan-26-24, Level 6		
Level 7		13	Jan-17-24	Feb-02-24			₩ Feb-02-24, Level 7		
Level 8		12	Jan-29-24	Feb-13-24			I Feb-13-24, Level 8		
Level 9		11	Feb-08-24	Feb-22-24			🁿 Feb-22-24, Level 9		
Level 10		11	Feb-19-24	Mar-04-24					
Level 11		11	Feb-28-24	Mar-13-24			▼ Mar-13-24, Level 11	1	
Level 12		11	Mar-08-24	Mar-22-24			₩ Mar-22-24, Level 12	5 5	
Level 14		9	Mar-19-24	Mar-29-24			▼ Mar-29-24, Level 14	1 1 1	
Level 15		11	Mar-28-24	Apr-11-24			Apr-11-24, Level 15		
Level 16		11	Apr-08-24	Apr-22-24			Apr-22-24, Level 16		
Level 17		11	Apr-17-24	May-01-24			🐨 May-01-24, Level 17		
Level 18		10	Apr-26-24	May-09-24			🐨 May-09-24, Level 18		
Level 19		10	May-06-24	May-17-24			▼ May-17-24, Level 19		
Level 20		11	May-14-24	May-29-24			▼ May-29-24, Level 20		
Level 21		11	May-23-24	Jun-07-24			₩ Jun-07-24, Level 21		
Level 22		11	Jun-04-24	Jun-18-24			✓ Jun-18-24, Level 22	5 5 5	
Level 23 Main	Roof	19	Jun-13-24	Jul-10-24			Jul-10-24, Level 23 Main Roof		
Level 24 High		17	Jul-03-24	Jul-26-24			Jul-26-24, Level 24 High Roof	5 5 5	
Level 25 Eleva		10	Jul-18-24	Jul-31-24					
Level 2 Podium		98	Jan-03-24	May-17-24			May-17-24, Level 2 Podium		
Hardscape		139	Feb-07-24	Aug-21-24			Unintrationality Aug-21-24, Hardscape		
Placing Boom		226	Aug-28-23	Jul-17-24			Jul-17-24, Placing Boom		
Buckhoists		184	Dec-27-23	Sep-13-24			V Sep-13-24, Buckhoists		
Porte Cochere		49	Mar-20-24	May-28-24			May-28-24, Porte Cochere		
Garage Leave-ou	it A ros 1	22	Dec-04-24	Jan-06-25			Jan-06-25, Garage Lea	ave_out A	
Grade Slab		100	Feb-13-24	Jul-02-24			Willing Jul-02-24, Grade Slab		
Interior Build Ou	a	270	Jan-24-24	Feb-13-25			Million Sur-02-24, Grade Stab Million Feb-13-25, Interior		
		275		Mar-20-25					
Building System	is a second s	319	Feb-21-24 Feb-14-24	Mar-20-25 May-14-25			Miar-20-25, Bui	1	
Exterior				-			May-14-2	.o, ⊏xienc	
Roofing		165	Feb-14-24	Oct-04-24					
Common Areas		85	Apr-02-24	Jul-31-24			Julian Julian Julia Juli		
	ding, Mechanical Building, Pool	217	Apr-12-24	Feb-19-25			1000000000000000000000000000000000000		
Final Site Work		231	Apr-03-24	Feb-28-25			EXAMPLE 1 Feb-28-25, Final		
Close Out		128	Mar-03-25	Aug-31-25				FAUNGAB10	

٠

