


Infinity Condo Detailed Schedule Layout





Data Date: Jun-05-23
Project Start: Jun-05-23
Project Finish: Sep-02-25

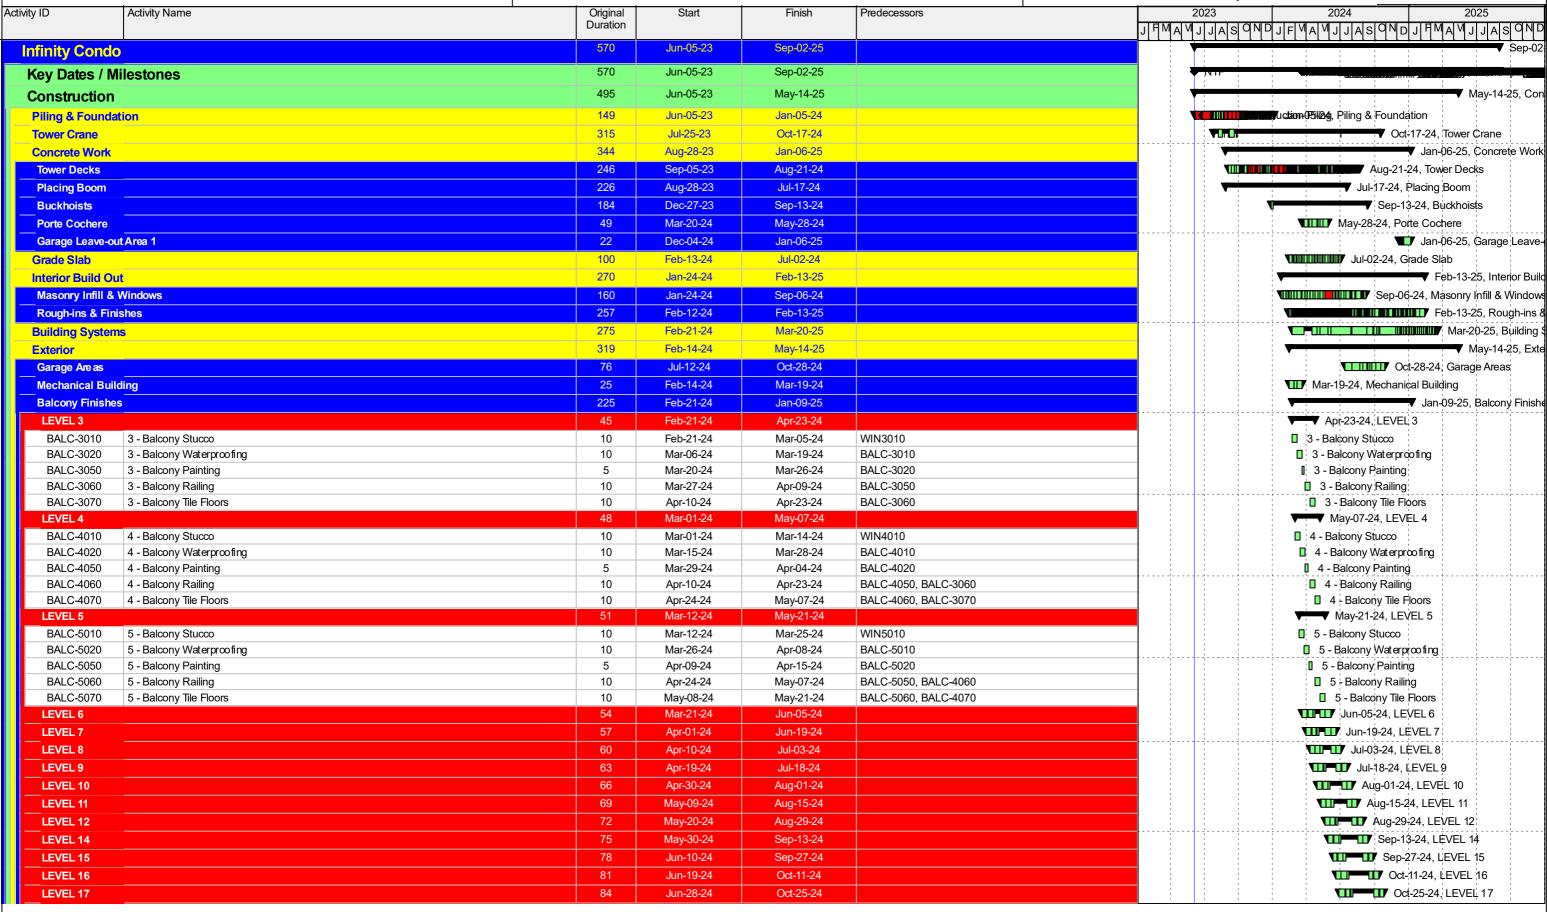

Infinity Condo Detailed Schedule Layout



y ID	Activity Name	Original	Start	Finish	Predecessors	2023 2024 2025
		Duration				J FMAMJJAS OND J FMAMJJAS OND J FMAMJJAS ON
LEVEL 18		87	Jul-10-24	Nov-08-24		Nov-08-24, LEVEL 18
LEVEL 19		90	Jul-19-24	Nov-26-24		Nov-26-24, LEVEL 19
LEVEL 20		93	Jul-30-24	Dec-10-24		Dec-10-24, LEVEL 20
LEVEL 21		96	Aug-08-24	Dec-24-24		Dec-24-24, LEVEL 21
LEVEL 22		99	Aug-19-24	Jan-09-25		Jan-09-25, LEVEL 22
Cafe/Game Ro	om Building	45	Jun-11-24	Aug-13-24		Aug-13-24, Cafe/Game Room Build
Building Exteri		182	Aug-27-24	May-14-25		▼ May-14-25, B
East Elevation		66	Sep-03-24	Dec-05-24		Dec-05-24, East Elevation
1st Drop		18	Sep-03-24	Sep-26-24		▼▼ Sep-26-24, 1st Drop
A2250	Concrete Remediation	3	Sep-03-24	Sep-05-24	MAS24000	I Concrete Remediation
A2260	Install Stucco	10	Sep-06-24	Sep-19-24	A2250	□ Install Stucco
A2270	Cure Stucco	2	Sep-20-24	Sep-23-24	A2260	I Cure Stucco
A2280	Paint Exterior	3	Sep-24-24	Sep-26-24	A2270	I Paint Exterior
2nd Drop		12	Sep-03-24	Sep-18-24		▼ Sep-18-24, 2nd Drop
A2410	Concrete Remediation	2	Sep-03-24	Sep-04-24	A2250	l Concrete Remediation
A2420	Install Stucco	5	Sep-05-24	Sep-11-24	A2410	☐ Install Stucco
A2430	Cure Stucco	2	Sep-12-24	Sep-13-24	A2420	I Cure Stucco
A2440	Paint Exterior	3	Sep-16-24	Sep-18-24	A2430	I Paint Exterior
3rd Drop		18	Sep-03-24	Sep-26-24		▼▼ Sep-26-24, 3rd Drop
A2450	Concrete Remediation	3	Sep-03-24	Sep-05-24	A2410	I Concrete Remediation
A2460	Install Stucco	10	Sep-06-24	Sep-19-24	A2450	☐ Install Stucco
A2470	Cure Stucco	2	Sep-20-24	Sep-23-24	A2460	I Cure Stucco
A2480	Paint Exterior	3	Sep-24-24	Sep-26-24	A2470	l Paint Exterior
4th Drop		18	Sep-27-24	Oct-22-24		▼▼ Oct-22-24, 4th Drop
A2490	Concrete Remediation	3	Sep-27-24	Oct-01-24	A2280	
A2500	Install Stucco	10	Oct-02-24	Oct-15-24	A2490	☐ Install Stucco
A2510	Cure Stucco	3	Oct-16-24	Oct-17-24	A2500	I Cure Stucco I Paint Exterior
A2520 5th Drop	Paint Exterior	18	Oct-18-24 Sep-27-24	Oct-22-24 Oct-22-24	A2510	TIP Oct-22-24, 5th Drop
				Oct-22-24		VIII Oct-22-24, 6th Drop
6th Drop		18	Sep-27-24			
7th Drop		12	Oct-23-24	Nov-07-24		₩ Nov-07-24, 7th Drop
8th Drop		12	Oct-23-24	Nov-07-24		₩ Nov-07-24, 8th Drop
9th Drop		18	Oct-23-24	Nov-15-24		■ Nov-15-24, 9th Drop
10th Drop		18	Nov-08-24	Dec-05-24		Dec-05-24, 10th Drop
11th Drop		18	Nov-08-24	Dec-05-24		Dec-05-24, 11th Drop
12th Drop		12	Nov-18-24	Dec-05-24		™ Dec-05-24, 12th Drop
West Elevation	n	47	Dec-06-24	Feb-12-25		Feb-12-25, West Ele
North Elevation	on	28	Feb-12-25	Mar-21-25		□ Mar-21-25, North
South Elevation	on	30	Mar-24-25	May-02-25		▼ May-02-25, S
Roof		182	Aug-27-24	May-14-25		□□□ May-14-25, F
Roofing		165	Feb-14-24	Oct-04-24		Oct-04-24, Roofing
Common Areas	S Company of the Comp	85	Apr-02-24	Jul-31-24		Jul-31-24, Common Areas
Cafe/Game Building, Mechanical Building, Pool		217	Apr-12-24	Feb-19-25		▼■■■■■ Feb-19-25, Cafe/Ga
Final Site Worl		231	Apr-03-24	Feb-28-25		Feb-28-25, Final Sit
Close Out		128	Mar-03-25	Aug-31-25		ALINA PAINS

Data Date: Jun-05-23
Project Start: Jun-05-23
Project Finish: Sep-02-25
