

Multi-Agency Regional Resiliency Center (M.A.R.R.C.)

June Update Analysis Report

CALIFORNIA
CONSTRUCTION
AUTHORITY



CPM Scheduling Consultant: HSE CONTRACTORS INC.

Data Date: July 01, 2025

NTP for construction	October -07-2024
Substantial Completion	April-21-2026
Contract Completion Date	April-21-2026

Contents

1. Purpose of the Report	3
2. Key Dates as of this update:	3
3. Elapsed Duration:	4
4. Activity Status	4
5. Three weeks ahead and one week behind	5
6. Longest Path Analysis	8
Most Critical Activities Needing Immediate Attention:	8
7. Critical Activities in the longest path for the next month	9
Critical Path Activities – Next Month (July 2025)	9
8. Critical Activities in the longest path for the next month	10
Layout	10
9. 4-Week lookahead	11


1. Purpose of the Report

the purpose of this report is to provide a detailed analysis of the current status of the project, focusing on the four weeks look ahead, the schedule comparison, highlighting potential causes of delays and challenges affecting the project schedule. It aims to identify the key factors that might drive a project delay. This report will offer actionable recommendations to avoid potential delays these. By evaluating the progress of remaining activities, the report seeks to support effective decision-making and enhance project management strategies to achieve timely project completion.


2. Key Dates as of this update:

Activity ID	Milestone Description	May-Update Finish	June-Update Finish	Current Variance	Trend
CM-MS24	K Final Completion	Mar-03-26	Mar-13-26	-10	
CM-MS4	E2 Final Completion	Apr-21-26	Apr-21-26	0	
CM-MS5	Auditorium Final Completion	Apr-21-26	Apr-21-26	0	
CM-MS14	Final Completion	Apr-21-26	Apr-21-26	0	

3. Elapsed Duration:

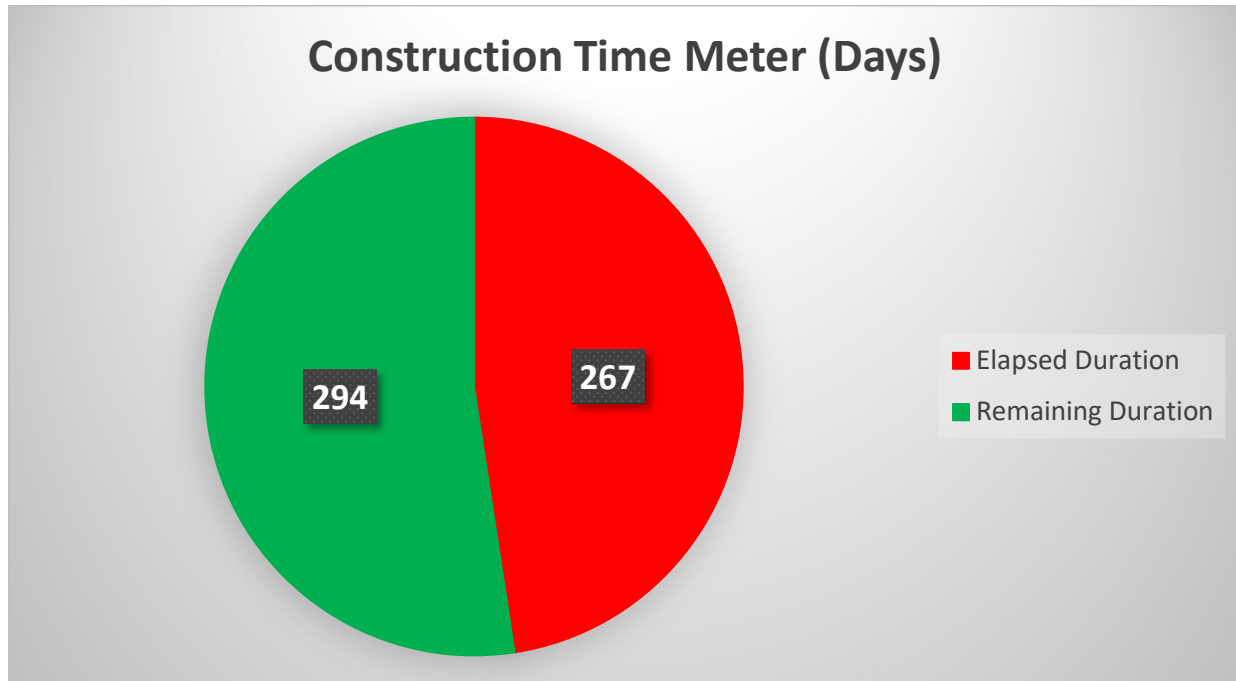

4. Activity Status

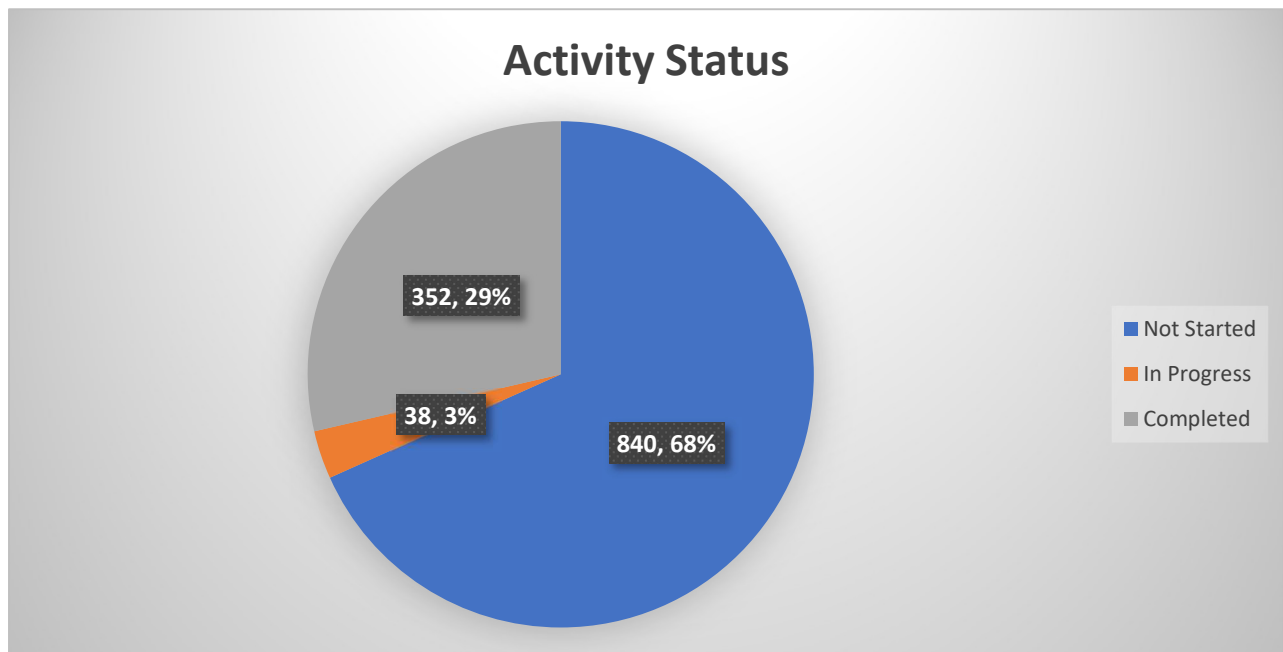

5. Three weeks ahead and one week behind

Delayed Construction Activities (the activities in **red** are added delay events that may push the schedule final completion in the next updates as it they not have actual dates)

Activity ID	Activity Name	Orig Dur	May Start	May Finish	June Start	June Finish	V-Start	V-Finish
Construction Administration and Purchasing		40	Oct-07-24	Jun-13-25	Oct-07-24 A	Jul-15-25	0	-21
C-ADMIN13	Owner Utility Approvals and Coordination	40	Oct-07-24	Jun-13-25	Oct-07-24 A	Jul-15-25	0	-21
Deferred Approvals		96	Mar-14-25	Jul-29-25	Mar-14-25 A	Aug-28-25	0	-22
Construction		228	Dec-20-24	Nov-17-25	Dec-20-24 A	Dec-12-25	0	-17
Fragnets		27	Jun-02-25	Jul-09-25	Jul-01-25	Aug-07-25	-21	-21
ASI-04 - Dry System		27	Jun-02-25	Jul-09-25	Jul-01-25	Aug-07-25	-21	-21
FRAG-ASI04-1110	CCA submission of OSFM (estimated)	1	Jun-02-25	Jun-02-25	Jul-01-25	Jul-01-25	-21	-21
FRAG-ASI04-1120	OSFM Review of Shop Drawings	26	Jun-03-25	Jul-09-25	Jul-02-25	Aug-07-25	-21	-21
LA County Water Works Permit Process		139	Dec-20-24	Jun-30-25	Dec-20-24 A	Jul-30-25	0	-21
FRAG-LACWW-1000	LA County Water Works Permit Review Process by CCA	40	Dec-20-24	Jun-02-25	Dec-20-24 A	Jul-01-25	0	-21
FRAG-LACWW-1010	Water Line material procurement	20	Jun-03-25	Jun-30-25	Jul-02-25	Jul-30-25	-21	-21
Package A-E2 Event Center		121	Jun-09-25	Nov-11-25	Jun-09-25 A	Dec-12-25	0	-21
Site Utilities		100	Jun-16-25	Nov-11-25	Jul-16-25	Dec-12-25	-21	-21
Communication		100	Jun-16-25	Nov-11-25	Jul-16-25	Dec-12-25	-21	-21
C-A-SU-COM2	LV Vendor Pulls and Completion	100	Jun-16-25	Nov-11-25	Jul-16-25	Dec-12-25	-21	-21
Dry Utility Reroute		100	Jun-16-25	Nov-11-25	Jul-16-25	Dec-12-25	-21	-21
C-A-SU-SCE2	New Transformer and Switch Installation	100	Jun-16-25	Nov-11-25	Jul-16-25	Dec-12-25	-21	-21
Package B- Auditorium		110	Jun-16-25	Nov-11-25	Jun-27-25 A	Dec-12-25	-9	-21
Site Utilities		100	Jun-16-25	Nov-11-25	Jul-16-25	Dec-12-25	-21	-21
Communication		100	Jun-16-25	Nov-11-25	Jul-16-25	Dec-12-25	-21	-21
C-B-SITEUTIL-11	LV Vendor Pulls and Completion	100	Jun-16-25	Nov-11-25	Jul-16-25	Dec-12-25	-21	-21
Dry Utility Reroute		100	Jun-16-25	Nov-11-25	Jul-16-25	Dec-12-25	-21	-21
C-B-SITEUTIL-13	New Transformer and Switch Installation	100	Jun-16-25	Nov-11-25	Jul-16-25	Dec-12-25	-21	-21
Metal Building Exterior		4	Jun-02-25	Jun-05-25	Jul-01-25	Jul-07-25	-21	-21
Roofing		4	Jun-02-25	Jun-05-25	Jul-01-25	Jul-07-25	-21	-21
C-C-PEMB-EXT-12	MEP Equipment	4	Jun-02-25	Jun-05-25	Jul-01-25	Jul-07-25	-21	-21
Electrical Room C116		6	Jun-09-25	Jun-20-25	Jun-25-25 A	Jul-09-25	-12	-12
C-C-INTBO-B-ELEC2	Prime and Paint	5	Jun-09-25	Jun-13-25	Jun-25-25 A	Jul-01-25	-12	-12
C-C-INTBO-B-ELEC3	Plywood Backing	5	Jun-16-25	Jun-20-25	Jul-02-25	Jul-09-25	-12	-12
Fire Riser Room C115		6	Jun-09-25	Jun-20-25	Jun-25-25 A	Jul-09-25	-12	-12
C-C-INTBO-B-FIRE2	Prime and Paint	5	Jun-09-25	Jun-13-25	Jun-25-25 A	Jul-01-25	-12	-12
C-C-INTBO-B-FIRE3	Fire Riser Room Fit Out with Equipment	5	Jun-16-25	Jun-20-25	Jul-02-25	Jul-09-25	-12	-12

Delayed Submittals & Approvals/Procurement Activities

Activity ID	Activity Name	Orig Dur	May Start	May Finish	June Start	June Finish	V-Start	V-Finish
Construction Administration and Purchasing								
		40	Oct-07-24	Jun-13-25	Oct-07-24 A	Jul-15-25	0	-21
C-ADMIN13	Owner Utility Approvals and Coordination	40	Oct-07-24	Jun-13-25	Oct-07-24 A	Jul-15-25	0	-21
Deferred Approvals								
		96	Mar-14-25	Jul-29-25	Mar-14-25 A	Aug-28-25	0	-22
Fire Alarm/Voice Evac		96	Mar-14-25	Jul-29-25	Mar-14-25 A	Aug-28-25	0	-22
DA-FA3	Fire Alarm Systems- CCA/CSFM Approval (A/B/C)	20	Mar-14-25	Jun-02-25	Mar-14-25 A	Jul-02-25	0	-30
DA-FA4	Fire Alarm Systems- Procurement (A/B/C)	40	Jun-03-25	Jul-29-25	Jul-03-25	Aug-28-25	-22	-22
EV Chargers								
		20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
DA-EV1	EV Chargers- Preparation	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
Division 4-Masonry								
		40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21
040513, 040516, 042200 Masonry Mortar PD, SD's, Samples, Mock-Up		40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21
SUB-CMU3	Masonry Submittals - Procurement	40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21
Division 6-Woods and Plastics								
		81	May-02-25	Aug-28-25	May-02-25 A	Oct-01-25	0	-18
061000 Rough Carpentry -Certs, PD		20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
SUB-RCAR1	Rough Carpentry Submittals- Preparation	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
066413 Fiberglass Reinforced Plastic Wall Panels (FRP) - PD, SD's, Samples		40	Jun-05-25	Jul-31-25	Jul-01-25	Aug-26-25	-18	-18
SUB-FRP3	FRP Submittals - Fabrication	40	Jun-05-25	Jul-31-25	Jul-01-25	Aug-26-25	-18	-18
066416 Fiber Reinforced Laminate Wall Panels (FRL) - PD, SD's, Samples		60	Jun-05-25	Aug-28-25	Jul-01-25	Oct-01-25	-18	-18
SUB-FRL3	FRL Submittals - Fabrication	60	Jun-05-25	Aug-28-25	Jul-01-25	Oct-01-25	-18	-18
Division 7-Thermal and Moisture Protection								
		62	Mar-11-25	Jun-27-25	Mar-11-25 A	Jul-29-25	0	-21
071326, 072726, 074263 CASM, SASM, Wall Cladding Rainscreen - PD, SD's, Mock-up		27	May-28-25	Jun-06-25	May-28-25 A	Jul-09-25	0	-22
SUB-INSUL3	CASM/SASM/Rain Screen Protection Submittals- Procure	0	May-28-25	Jun-02-25	May-28-25 A	Jul-01-25	0	-22
SUB-INSUL4	CASM/SASM/Rain Screen Protection Submittals Deliver	5	Jun-02-25	Jun-06-25	Jul-02-25	Jul-09-25	-22	-22
072800- Concrete Slab Vapor Emission and Alkalinity Control - PD		20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
SUB-CONVB1	Vapor and Emissions Control Submittals- Preparation	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
075400, 077233 TPO Membrane Roofing and Roof Hatches- PD, SD's, Samples		5	Jun-02-25	Jun-06-25	Jul-01-25	Jul-08-25	-21	-21
SUB-ROOF4	TPO Roofing Submittals - Delivery to the Site	5	Jun-02-25	Jun-06-25	Jul-01-25	Jul-08-25	-21	-21
076200 Sheet Metal Flashing and Trim - PD, SD's, Samples and Mock-up		48	Mar-11-25	Jun-09-25	Mar-11-25 A	Jul-09-25	0	-21
SUB-SMFL3	Sheet Metal Flashing Submittals - Procurement	30	Mar-11-25	Jun-02-25	Mar-11-25 A	Jul-01-25	0	-21
SUB-SMFL4	Sheet Metal Flashing Submittals - Delivery to the Site	5	Jun-03-25	Jun-09-25	Jul-02-25	Jul-09-25	-21	-21
079200 Sealants and Caulking -PD and Samples		20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
SUB-SEAL3	Sealants Submittals - Procurement	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
Division 8- Openings								
		81	May-13-25	Aug-26-25	May-13-25 A	Oct-02-25	0	-21
083100 Access Doors & Panels -PD, Schedule, Samples		42	May-30-25	Aug-04-25	May-30-25 A	Aug-27-25	0	-17
SUB-ACCDR2	Access Door Submittals- AOR Approval	10	May-30-25	Jun-08-25	May-30-25 A	Jul-01-25	0	-23
SUB-ACCDR3	Access Door Submittals-Procurement	40	Jun-09-25	Aug-04-25	Jul-02-25	Aug-27-25	-17	-17
083313, 083333 Coiling Counter Doors and OH Coiling Doors- PD, Schedule, SD's, Sam		40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21
SUB-COCHCD3	Coiling Counter and OH Doors Submittals - Procurement	40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21
Window Wall Storefront Systems								
		81	May-16-25	Aug-26-25	May-16-25 A	Oct-02-25	0	-21
DA-SF2	Window Wall/Storefront- AOR Approval (A/B/C)	10	May-16-25	Jun-02-25	May-16-25 A	Jul-01-25	0	-29
DA-SF4	Window Wall/Storefront- Procurement (A/B/C)	60	Jun-03-25	Aug-26-25	Jul-02-25	Oct-02-25	-21	-21
093000 Tile and Stone- PD, SD's, Mock-up		60	Jun-02-25	Aug-25-25	Jul-01-25	Oct-01-25	-21	-21
SUB-TILE3	Tile and Stone Submittals- Procurement	60	Jun-02-25	Aug-25-25	Jul-01-25	Oct-01-25	-21	-21
095100 Acoustical Ceiling Suspension System & Tile - PD, SD's, Samples		30	Jun-09-25	Jul-21-25	Jul-01-25	Aug-12-25	-16	-16
SUB-ACT3	ACT Submittals- Procurement	30	Jun-09-25	Jul-21-25	Jul-01-25	Aug-12-25	-16	-16
096513, 096519, 096769, 096813 RD & Acce, Tile FLR, Carpet Tile and Poly FLR - PD, Sa		40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21
SUB-CPTSV3	Carpet and Sheet Vinyl Submittals- Procurement	40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21
096900 Access Flooring - PD, Samples, SD's, Mock-up		20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
SUB-ACCF11	Access Flooring Submittals- Preparation	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
097216 Vinyl Wallcovering- PD, SD's, Samples		20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
SUB-VWC1	Vinyl Wall Coverings Submittals- Preparation	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
099723 Concrete Sealer -PD, Samples, SD's, Mock-up		34	Jun-02-25	Aug-04-25	Jun-23-25 A	Aug-08-25	-15	-4
SUB-CS1	Concrete Sealer Submittals- Preparation	20	Jun-02-25	Jun-27-25	Jun-23-25 A	Jul-01-25	-15	-2
SUB-CS2	Concrete Sealer Submittals - AOR Approval	10	Jun-28-25	Jul-07-25	Jul-02-25	Jul-11-25	-4	-4
SUB-CS3	Concrete Sealer Submittals - Procurement	20	Jul-08-25	Aug-04-25	Jul-14-25	Aug-08-25	-4	-4
101400, 101419 Signage and Dimensional Letter Signage- PD, Samples, SD's		52	May-29-25	Aug-04-25	May-29-25 A	Sep-11-25	0	-27
SUB-SIGN2	Signage Submittals AOR Approval	10	May-29-25	Jun-07-25	May-29-25 A	Jul-01-25	0	-24
SUB-SIGN3	Signage Submittals- Procurement	40	Jun-09-25	Aug-04-25	Jul-17-25	Sep-11-25	-27	-27
102226 Operable Partitions- PD, Samples, SD's, Mock-up		113	Apr-30-25	Oct-08-25	Apr-30-25 A	Nov-13-25	0	-26
SUB-OPPART2	Operable Partitions Submittals AOR Approval	10	Apr-30-25	Jun-09-25	Apr-30-25 A	Jul-01-25	0	-22
SUB-OPPART3	Operable Partitions Submittals- Procurement	80	Jun-10-25	Oct-08-25	Jul-17-25	Nov-13-25	-26	-26
104100, 104400 Emergency Access/Info and FEC's - PD, SD's, List of Materials		40	Jun-11-25	Aug-06-25	Jul-01-25	Aug-26-25	-14	-14
SUB-EACFEC3	Emergency Access and FEC Cabinets- Procurement (* est	40	Jun-11-25	Aug-06-25	Jul-01-25	Aug-26-25	-14	-14


Activity ID	Activity Name	Orig Dur	May Start	May Finish	June Start	June Finish	V-Start	V-Finish
Division 22-Plumbing		97	Feb-27-25	Jul-03-25	Feb-27-25 A	Jul-09-25	0	-3
224000 Plumbing Fixtures - PD		40	May-01-25	Jul-03-25	May-01-25 A	Jul-09-25	0	-3
SUB-PLFIX3	Plumbing Fixtures- Procurement	40	May-01-25	Jun-26-25	May-01-25 A	Jul-01-25	0	-3
SUB-PLFIX4	Plumbing Fixtures- Delivery to the Site	5	Jun-27-25	Jul-03-25	Jul-02-25	Jul-09-25	-3	-3
225000 Plumbing Equipment - PD		84	Feb-27-25	Jun-10-25	Feb-27-25 A	Jul-09-25	0	-20
SUB-PLEQUIP3	Plumbing Equipment- Procurement	40	Feb-27-25	Jun-03-25	Feb-27-25 A	Jul-01-25	0	-20
SUB-PLEQUIP4	Plumbing Equipment- Delivery to the Site	5	Jun-04-25	Jun-10-25	Jul-02-25	Jul-09-25	-20	-20
230923 Direct Digital Control System for HVAC - SD's		84	Feb-10-25	Jun-09-25	Feb-10-25 A	Jul-09-25	0	-21
SUB-MECHDDC3	Mechanical DDC Submittals - Procurement	40	Feb-10-25	Jun-02-25	Feb-10-25 A	Jul-01-25	0	-21
SUB-MECHDDC4	Mechanical DDC Submittals - Delivery to the Site	5	Jun-03-25	Jun-09-25	Jul-02-25	Jul-09-25	-21	-21
237313 VRF Heating and Cooling Air Rotation Units - SD's, PD		50	Jun-02-25	Aug-11-25	Jul-01-25	Sep-10-25	-21	-21
SUB-MECHVRV3	Mechanical VRF Submittals - Procurement	50	Jun-02-25	Aug-11-25	Jul-01-25	Sep-10-25	-21	-21
260519,260523,260526,260533,260536,260800 LV,Cnt,Grd,PC,Cab,RV's,Boxes,Cbl Tg,C		64	Feb-21-25	Jun-09-25	Feb-21-25 A	Jul-09-25	0	-21
SUB-ELG3	Electrical GeneralSubmittals - Procurement	30	Feb-21-25	Jun-02-25	Feb-21-25 A	Jul-01-25	0	-21
SUB-ELG4	Electrical GeneralSubmittals - Delivery to the Site	5	Jun-03-25	Jun-09-25	Jul-02-25	Jul-09-25	-21	-21
260573.16, 260573.19 Coordination Studies and Arc Flash Hazard Analysis - PD and St		20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
SUB-COARC1	Coordination and Arc Flash Studies - Preparation	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
262816, 263353 Wiring Devices, UPS's - PD,		40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21
SUB-ELWDUPS3	Electrical Wiring Devices and UPS Submittals - Procurer	40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21
Division 27-Communications		20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
270553, 271323, 271513 Id for Com Systems, Fiber Optic and Copper Cabling -PD and SI		20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
SUB-COMC1	Com System Cabling Submittals- Preparation	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
271100, 271116 Com EquipRoom Fittings, Racks,Frames and Enclosures-PD and SD's		20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
SUB-COME1	Com System Equipment Submittals- Preparation	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
Division 32-Exterior Improvements		40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21
320000, 320923, 321613 Offsite Improve, Cement and Concrete, Curb and Gutter- Sampl		20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
SUB-OFFS1	Offsite Improvement Submittals - Preparation	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
321123,321216,321300 Aggregate Base Courses, Asphalt and Rigid Paving		20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
SUB-ASRGDPV3	Asphalt and Rigid Paving Submittals- Procurement	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
321723, 321726 Pavement Markings and Tactile Warning Surfaces- PD, SD's		40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21
SUB-PAVE3	Pavement Marking and Tactile Surfaces Submittals - Pr	40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21
323113,323119 Chain Link and Decorative Metal Fencing and Gates PD, Samples, Engine		20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
SUB-FENC1	Chain Link Fencing and Metal Gates Submittals- Prepa	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21
320100,321543,328000,329300,323300 Land Plant,Mat,Irr, Maint, DG and SiteFurn-PD,Sr		30	Jun-02-25	Jul-14-25	Jul-01-25	Aug-12-25	-21	-21
SUB-LAND3	Landscaping Submittals- Procurement	30	Jun-02-25	Jul-14-25	Jul-01-25	Aug-12-25	-21	-21
Division 33-Utilities		145	Nov-14-24	Jun-09-25	Nov-14-24 A	Jul-09-25	0	-21
331000, 331100 Water Utilities and Distribution- PD, SD's, Samples, Reports		145	Nov-14-24	Jun-09-25	Nov-14-24 A	Jul-09-25	0	-21
SUB-SUW3	Site Utilities Water- Procurement	20	Nov-14-24	Jun-02-25	Nov-14-24 A	Jul-01-25	0	-21
SUB-SUIW4	Site Utilities Water - Delivery to the Site	5	Jun-03-25	Jun-09-25	Jul-02-25	Jul-09-25	-21	-21

The following Activities have been modified to start early this month previously they would start in October and they're critical if they're delayed, they will delay the substantial completion of the project the activity highlighted in green has an actual start date

Activity ID	Activity Name	Total Float	Orig Dur	May-UPD Start	May-UPD Finish	Current Start	Current Finish	V-Start	V-Finish
Package B- Auditorium		0	197	Jun-23-25	Apr-21-26	Jun-27-25 A	Apr-21-26	-4	0
SOG		0	18	Jun-28-25	Oct-17-25	Jun-27-25 A	Jul-25-25	1	54
Foundations/ SOG		0	10	Jun-28-25	Oct-17-25	Jun-27-25 A	Jul-25-25	1	54
C-B-FOUND/SOG-10	FND: Cure Grade Beams	2	5	Jun-28-25	Jul-02-25	Jun-27-25 A	Jul-01-25	1	1
C-B-FOUND/SOG-13	SOG: Formwork (including Column Blockouts)	2	5	Sep-17-25	Sep-30-25	Jul-01-25	Jul-08-25	54	54
C-B-FOUND/SOG-12	SOG: Vapor Barrier	2	3	Sep-12-25	Sep-16-25	Jul-07-25	Jul-09-25	48	48
C-B-FOUND/SOG-14	SOG: Reinforcement	2	7	Oct-01-25	Oct-09-25	Jul-10-25	Jul-18-25	53	53
C-B-FOUND/SOG-15	SOG: Pour (2 Pours) (including exterior MEP Pads for Equipment)	2	2	Oct-10-25	Oct-13-25	Jul-21-25	Jul-22-25	53	53
C-B-FOUND/SOG-17	SOG: Cure	2	5	Oct-13-25	Oct-17-25	Jul-21-25	Jul-25-25	84	84
C-B-FOUND/SOG-18	SOG: Clean	2	1	Oct-10-25	Oct-10-25	Jul-21-25	Jul-21-25	53	53

6. Longest Path Analysis

Activity ID	Activity Name	Total Float	Orig Dur	BL Start	BL-Finish	Start	Finish	V-Start	V-Finish
Metal Building Superstructure									
Structural Steel									
C-B-PEMB-2	Mobilize and Set Up Crane	0	1	Jun-23-25	Jun-23-25	Jul-28-25	Jul-28-25	-24	-24
C-B-PEMB-3	Erect Structural Steel	0	25	Jun-24-25	Jul-29-25	Jul-28-25	Aug-29-25	-23	-23
C-B-PEMB-4	Plumb & Line	0	10	Jul-30-25	Aug-12-25	Sep-02-25	Sep-15-25	-23	-23
C-B-PEMB-10	Safety Cable and Stancions	0	3	Jul-30-25	Aug-01-25	Sep-02-25	Sep-04-25	-23	-23
C-B-PEMB-5	Bolt Up	0	10	Aug-06-25	Aug-19-25	Sep-09-25	Sep-29-25	-23	-23
Slab on Metal Deck Sequence									
Interstitial Space									
Decking									
C-B-PEMB-6	Spread Metal Decking - Interstitial Space	0	2	Aug-20-25	Aug-21-25	Sep-30-25	Oct-01-25	-23	-23
C-B-PEMB-7	Weld Deck - Interstitial Space	0	5	Aug-22-25	Aug-28-25	Oct-02-25	Oct-08-25	-23	-23
Roof									
Roof Accessories									
C-B-PEMB-8	Spread Roof Accessories	0	2	Aug-29-25	Sep-02-25	Oct-09-25	Oct-10-25	-23	-23
C-B-PEMB-9	Install Roof Accessories	0	5	Sep-03-25	Sep-09-25	Oct-13-25	Oct-17-25	-23	-23

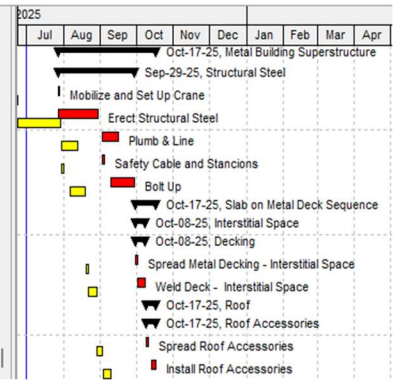

Most Critical Activities Needing Immediate Attention:

1. Structural Steel Sequence (23 days delayed)

- Mobilize and Set Up Crane (now starting Jul-28-25 vs original Jun-23-25)
- Erect Structural Steel (23 days delayed)
- Plumb & Line (23 days delayed)

2. Metal Deck Installation (23 days delayed)

- Spread Metal Decking - Interstitial Space (now starting Sep-29-25 vs original Aug-20-25)
- Weld Deck - Interstitial Space (23 days delayed)

3. Roof Installation (23 days delayed)

- Spread Roof Accessories (now starting Oct-03-25 vs original Aug-22-25)
- Install Roof Accessories (now starting Oct-13-25 vs original Sep-03-25)

7. Critical Activities in the longest path for the next month

Critical Path Activities – Next Month (July 2025)

1. Structural Steel (Event Center & Auditorium) – DELAYED

- **Erect Structural Steel - Event Space**
 - Previous month: Jun-09-25 to Jul-21-25
 - Current: **On track** (Jun-09-25 to Jul-21-25)
- **Plumb & Line - Event Space**
 - Previous month: Jun-30-25 to Jul-21-25
 - Current: **On track** (Jun-30-25 to Jul-21-25)
- **Erect Structural Steel - Auditorium**
 - Previous month: Jun-24-25 to Jul-29-25
 - Current: **Delayed by 23 days** (Jul-28-25 to Aug-29-25)

2. Slab-on-Grade (SOG) – EARLY START (Potential Risk)

- **SOG: Reinforcement & Pour**
 - Previous month: Oct-01-25 to Oct-13-25
 - Current: **Started 53 days early** (Jul-10-25 to Jul-22-25)
 - *Risk: Early work may clash with delayed steel erection.*

3. High-Risk Delays

Activity	Previous month Dates	Current Dates	Delay
Mobilize Crane (Auditorium)	Jun-23-25	Jul-28-25	24 days
Erect Steel (Auditorium)	Jun-24-25 to Jul-29-25	Jul-28-25 to Aug-29-25	23 days

8. Critical Activities in the longest path for the next month Layout

Critical Activities in the longest path for the next month

Activity ID		Activity Name		Total Float	Orig Dur	BL Start	BL-Finish	Start	Finish	V-Start	V-Finish	2025						2026						
												Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	
Multi-Agency Regional Resiliency Center (M.A.R.R.C.) - June 2025				0	365	Oct-07-24	Apr-21-26	Oct-07-24 A	Apr-21-26	0	0													
Project Duration				0	365	Oct-07-24	Apr-21-26	Oct-07-24 A	Apr-21-26	0	0													
PD-MS1		Construction Duration (Complete by April 7, 2026) Work Days		0	365	Oct-07-24	Apr-21-26	Oct-07-24 A	Apr-21-26	0	0													
Construction				0	54	Jun-09-25	Oct-17-25	Jun-09-25 A	Aug-29-25	0	29													
Package A-E2 Event Center				0	37	Jun-09-25	Aug-06-25	Jun-09-25 A	Aug-06-25	0	0													
Metal Building Superstructure				0	37	Jun-09-25	Aug-06-25	Jun-09-25 A	Aug-06-25	0	0													
Structural Steel				0	37	Jun-09-25	Aug-06-25	Jun-09-25 A	Aug-06-25	0	0													
C-A-S-PEMB2		Erect Structural Steel - Event Space		0	30	Jun-09-25	Jul-21-25	Jun-09-25 A	Jul-21-25	0	0													
C-A-S-PEMB3		Plumb & Line - Event Space		0	15	Jun-30-25	Jul-21-25	Jun-30-25 A	Jul-21-25	0	0													
C-A-S-PEMB6		Production Welding- Event Space		0	10	Jul-10-25	Jul-23-25	Jul-10-25	Jul-23-25	0	0													
C-A-S-PEMB5		Bolt Up - Event Space		0	10	Jul-10-25	Jul-23-25	Jul-10-25	Jul-23-25	0	0													
C-A-S-PEMPB11		Erect Structural Steel - South Bar		0	20	Jul-10-25	Aug-06-25	Jul-10-25	Aug-06-25	0	0													
Package B- Auditorium				0	40	Jun-23-25	Oct-17-25	Jul-07-25	Aug-29-25	-9	29													
SOG				0	15	Sep-12-25	Oct-17-25	Jul-07-25	Jul-25-25	48	54													
Foundations/ SOG				0	15	Sep-12-25	Oct-17-25	Jul-07-25	Jul-25-25	48	54													
C-B-FOUND/SOG-12		SOG: Vapor Barrier		2	3	Sep-12-25	Sep-16-25	Jul-07-25	Jul-09-25	48	48													
C-B-FOUND/SOG-14		SOG: Reinforcement		2	7	Oct-01-25	Oct-09-25	Jul-10-25	Jul-18-25	53	53													
C-B-FOUND/SOG-15		SOG: Pour (2 Pours) (including exterior MEP Pads for Equipment)		2	2	Oct-10-25	Oct-13-25	Jul-21-25	Jul-22-25	53	53													
C-B-FOUND/SOG-17		SOG: Cure		2	5	Oct-13-25	Oct-17-25	Jul-21-25	Jul-25-25	84	84													
C-B-FOUND/SOG-18		SOG: Clean		2	1	Oct-10-25	Oct-10-25	Jul-21-25	Jul-21-25	53	53													
Metal Building Superstructure				0	25	Jun-23-25	Jul-29-25	Jul-28-25	Aug-29-25	-24	-23													
Structural Steel				0	25	Jun-23-25	Jul-29-25	Jul-28-25	Aug-29-25	-24	-23													
C-B-PEMB-2		Mobilize and Set Up Crahe		0	1	Jun-23-25	Jun-23-25	Jul-28-25	Jul-28-25	-24	-24													
C-B-PEMB-3		Erect Structural Steel		0	25	Jun-24-25	Jul-29-25	Jul-28-25	Aug-29-25	-23	-23													

9. 4-Week lookahead

4-Week Lookahead



Activity ID	Activity Name	Total Float	Orig Dur	BL Start	BL-Finish	Start	Finish	V-Start	V-Finish	2025							2026				
										Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
Multi-Agency Regional Resiliency Center (M.A.R.R.C.) - June 2025		0	382	Oct-07-24	Apr-21-26	Oct-07-24 A	Apr-21-26	0	0	▼ Apr-21-26, Multi-Agency Regional Resiliency Center (M.A.R.R.C.) - June 2025											
BERNARDS KEY MILESTONES		187	0	Jul-23-25	Jul-23-25	Jul-23-25	Jul-23-25	0	0	▼ Jul-23-25, BERNARDS KEY MILESTONES											
BER-1030	STRUCTURE COMPLETE (MS 3)	187	0		Jul-23-25		Jul-23-25	0	0	◆ STRUCTURE COMPLETE (MS 3)											
Project Duration		0	365	Oct-07-24	Apr-21-26	Oct-07-24 A	Apr-21-26	0	0	▼ Apr-21-26, Project Duration											
PD-MS1	Construction Duration (Complete by April 7, 2026) Work Days	0	365	Oct-07-24	Apr-21-26	Oct-07-24 A	Apr-21-26	0	0	Construction Duration (Complete by April 7, 2026) Work Days											
Construction Administration and Purchasing		47	40	Oct-07-24	Jun-13-25	Oct-07-24 A	Jul-15-25	0	-21	Jul-15-25, Construction Administration and Purchasing											
C-ADMIN13	Owner Utility Approvals and Coordination	47	40	Oct-07-24	Jun-13-25	Oct-07-24 A	Jul-15-25	0	-21	Owner Utility Approvals and Coordination											
Submittals / Procurement		66	220	Jan-23-25	Dec-09-25	Jan-23-25 A	Dec-09-25	0	0	Dec-09-25, Submittals / Procurement											
Deferred Approvals		25	92	Mar-27-25	Jul-29-25	Mar-27-25 A	Aug-28-25	0	-22	Aug-28-25, Deferred Approvals											
Fire Sprinkler Systems		20	20	Mar-27-25	Jul-09-25	Mar-27-25 A	Aug-07-25	0	-29	Aug-07-25, Fire Sprinkler Systems											
DA-FS3	Fire Sprinkler Systems- CCA/CSFM Approval (A/B/C)	20	20	Mar-27-25	Jul-09-25	Mar-27-25 A	Aug-07-25	0	-29	Fire Sprinkler Systems- CCA/CSFM Approval (A/B/C)											
Fire Alarm/Voice Evac		25	40	Jun-03-25	Jul-29-25	Jul-03-25	Aug-28-25	-22	-22	Aug-28-25, Fire Alarm/Voice Evac											
DA-FA4	Fire Alarm Systems- Procurement (A/B/C)	25	40	Jun-03-25	Jul-29-25	Jul-03-25	Aug-28-25	-22	-22	Fire Alarm Systems- Procurement (A/B/C)											
EV Chargers		39	28	Jun-02-25	Jul-07-25	Jul-01-25	Aug-08-25	-21	-24	Aug-08-25, EV Chargers											
DA-EV1	EV Chargers- Preparation	39	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21	EV Chargers- Preparation											
DA-EV2	EV Chargers- AOR Approval	63	10	Jun-28-25	Jul-07-25	Jul-30-25	Aug-08-25	-32	-32	EV Chargers- AOR Approval											
Submittals		66	220	Jan-23-25	Dec-09-25	Jan-23-25 A	Dec-09-25	0	0	Dec-09-25, Submittals											
Division 4-Masonry		73	40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21	Aug-26-25, Division 4-Masonry											
040513, 040516, 042200 Masonry Mortar PD, SD's, Samples, Mock-Up		73	40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21	Aug-26-25, 040513, 040516, 042200 Masonry Mortar PD, SD's, Samples, Mock-Up											
SUB-CMU3	Masonry Submittals - Procurement	73	40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21	Masonry Submittals - Procurement											
Division 5-Metals		128	50	May-01-25	Aug-11-25	May-01-25 A	Aug-11-25	0	0	Aug-11-25, Division 5-Metals											
051200, 05300, 055000, 055133a, 055200 Str Stl, Decking, Lad, Rail PD, SD's, WPS', PQR's-2		128	50	May-01-25	Aug-11-25	May-01-25 A	Aug-11-25	0	0	Aug-11-25, 051200, 05300, 055000, 055133a, 055200 Str Stl, Decking, Lad, Rail PD, SD's, WPS', PQR's-2											
SUB-STEEL84	Steel Submittals - Fabrication - Package A	128	45	May-01-25	Aug-04-25	May-01-25 A	Aug-04-25	0	0	Steel Submittals - Fabrication - Package A											
SUB-STEEL74	Steel Submittals- Delivery to the Site - Package A	128	5	Aug-05-25	Aug-11-25	Aug-05-25	Aug-11-25	0	0	Steel Submittals- Delivery to the Site - Package A											
051200, 05300, 055000, 055133a, 055200 Str Stl, Decking, Lad, Rail PD, SD's, WPS', PQR's-1		79	50	May-01-25	Aug-11-25	May-01-25 A	Aug-11-25	0	0	Aug-11-25, 051200, 05300, 055000, 055133a, 055200 Str Stl, Decking, Lad, Rail PD, SD's, WPS', PQR's-1											
SUB-STEEL44	Steel Submittals - Fabrication - Package B	79	45	May-01-25	Aug-04-25	May-01-25 A	Aug-04-25	0	0	Steel Submittals - Fabrication - Package B											
SUB-STEEL34	Steel Submittals- Delivery to the Site - Package B	79	5	Aug-05-25	Aug-11-25	Aug-05-25	Aug-11-25	0	0	Steel Submittals- Delivery to the Site - Package B											
Division 6-Woods and Plastics		66	81	May-02-25	Aug-28-25	May-02-25 A	Oct-01-25	0	-18	Oct-01-25, Division 6-Woods and Plastics											
061000 Rough Carpentry -Certs, PD		19	28	Jun-02-25	Jul-07-25	Jul-01-25	Aug-08-25	-21	-24	Aug-08-25, 061000 Rough Carpentry -Certs, PD											
SUB-RCAR1	Rough Carpentry Submittals- Preparation	22	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21	Rough Carpentry Submittals- Preparation											
SUB-RCAR2	Rough Carpentry Submittals - AOR Approval	30	10	Jun-28-25	Jul-07-25	Jul-30-25	Aug-08-25	-32	-32	Rough Carpentry Submittals - AOR Approval											
064116 Plastic Laminate Clad Arch. Cabinets - PD, SD's, Samples		112	50	May-02-25	Jul-21-25	May-02-25 A	Jul-21-25	0	0	Jul-21-25, 064116 Plastic Laminate Clad Arch. Cabinets - PD, SD's, Samples											
SUB-CASE3	Casework Submittals - Fabrication	112	50	May-02-25	Jul-14-25	May-02-25 A	Jul-14-25	0	0	Casework Submittals - Fabrication											
SUB-CASE4	Casework Submittals- Delivery to the Site	112	5	Jul-15-25	Jul-21-25	Jul-15-25	Jul-21-25	0	0	Casework Submittals- Delivery to the Site											
066119 Quartz Surfacing -PD, SD's, SamplesB		107	50	May-02-25	Jul-28-25	May-02-25 A	Jul-28-25	0	0	Jul-28-25, 066119 Quartz Surfacing -PD, SD's, SamplesB											
SUB-QUARTZ3	Quartz Surfacing Submittals - Fabrication	107	50	May-02-25	Jul-14-25	May-02-25 A	Jul-14-25	0	0	Quartz Surfacing Submittals - Fabrication											
SUB-QUARTZ4	Quartz Surfacing Submittals- Delivery to the Site (* +10 Days after Ca	107	10	Jul-15-25	Jul-28-25	Jul-15-25	Jul-28-25	0	0	Quartz Surfacing Submittals- Delivery to the Site (* +10 Days after Casework Install)											
066413 Fiberglass Reinforced Plastic Wall Panels (FRP) - PD, SD's, Samples		81	40	Jun-05-25	Jul-31-25	Jul-01-25	Aug-26-25	-18	-18	Aug-26-25, 066413 Fiberglass Reinforced Plastic Wall Panels (FRP) - PD, SD's, Samples											
SUB-FRP3	FRP Submittals - Fabrication	81	40	Jun-05-25	Jul-31-25	Jul-01-25	Aug-26-25	-18	-18	FRP Submittals - Fabrication											
066416 Fiber Reinforced Laminate Wall Panels (FRL)- PD, SD's, Samples		61	60	Jun-05-25	Aug-28-25	Jul-01-25	Oct-01-25	-18	-18	Oct-01-25, 066416 Fiber Reinforced Laminate Wall Panels (FRL)- PD, SD's, Samples											
SUB-FRL3	FRL Submittals - Fabrication	61	60	Jun-05-25	Aug-28-25	Jul-01-25	Oct-01-25	-18	-18	FRL Submittals - Fabrication											
Division 7-Thermal and Moisture Protection		70	28	Jun-02-25	Jul-07-25	Jul-01-25	Aug-08-25	-21	-24	Aug-08-25, Division 7-Thermal and Moisture Protection											
071326, 072726, 074263 CASM , SASM, Wall Cladding Rainscreen - PD, SD's, Mock-up		92	5	Jun-02-25	Jun-06-25	Jul-02-25	Jul-09-25	-22	-22	Jul-09-25, 071326, 072726, 074263 CASM , SASM, Wall Cladding Rainscreen - PD, SD's, Mock-up											
SUB-INSUL4	CASM/SASM/Rain Screen Protection Submittals Delivery to the Site	92	5	Jun-02-25	Jun-06-25	Jul-02-25	Jul-09-25	-22	-22	CASM/SASM/Rain Screen Protection Submittals Delivery to the Site											
072800- Concrete Slab Vapor Emission and Alkalinity Control - PD		39	28	Jun-02-25	Jul-07-25	Jul-01-25	Aug-08-25	-21	-24	Aug-08-25, 072800- Concrete Slab Vapor Emission and Alkalinity Control - PD											
SUB-CONVB1	Vapor and Emissions Control Submittals- Preparation	39	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21	Vapor and Emissions Control Submittals- Preparation											
SUB-CONVB2	Vapor and Emissions Control - AOR Approval	63	10	Jun-28-25	Jul-07-25	Jul-30-25	Aug-08-25	-32	-32	Vapor and Emissions Control - AOR Approval											
076200 Sheet Metal Flashing and Trim - PD, SD's, Samples and Mock-up		92	5	Jun-03-25	Jun-09-25	Jul-02-25	Jul-09-25	-21	-21	Jul-09-25, 076200 Sheet Metal Flashing and Trim - PD, SD's, Samples and Mock-up											
SUB-SMFL4	Sheet Metal Flashing Submittals - Delivery to the Site	92	5	Jun-03-25	Jun-09-25	Jul-02-25	Jul-09-25	-21	-21	Sheet Metal Flashing Submittals - Delivery to the Site											
079200 Sealants and Caulking -PD and Samples		73	25	Jun-02-25	Jul-07-25	Jul-01-25	Aug-05-25	-21	-21	Aug-05-25, 079200 Sealants and Caulking -PD and Samples											
SUB-SEAL3	Sealants Submittals - Procurement	73	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21	Sealants Submittals - Procurement											
SUB-SEAL4	Sealants Submittals - Delivery to the Site	73	5	Jun-30-25	Jul-07-25	Jul-30-25	Aug-05-25	-21	-21	Sealants Submittals - Delivery to the Site											
Division 8-Openings		92	73	May-13-25	Aug-26-25	May-13-25 A	Oct-02-25	0	-21	Oct-02-25, Division 8-Openings											

4-Week Lookahead

Activity ID	Activity Name	Total Float	Orig Dur	BL Start	BL-Finish	Start	Finish	V-Start	V-Finish	2025							2026				
										Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
	230050, 230593, 230800 Basic HVAC Mat and Methods, TAB and CMXing PD, SD's, Loads, Access	86	5	Jul-09-25	Jul-15-25	Jul-09-25	Jul-15-25	0	0												
	SUB-MECHG4 Mechanical General Submittals - Delivery to the Site	86	5	Jul-09-25	Jul-15-25	Jul-09-25	Jul-15-25	0	0												
	230923 Direct Digital Control System for HVAC - SD's	90	5	Jun-03-25	Jun-09-25	Jul-02-25	Jul-09-25	-21	-21												
	SUB-MECHDDC4 Mechanical DDC Submittals - Delivery to the Site	90	5	Jun-03-25	Jun-09-25	Jul-02-25	Jul-09-25	-21	-21												
	237200 Air to Air Energy Recovery Ventilator -PD, SD's	55	160	Mar-07-25	Dec-09-25	Mar-07-25 A	Dec-09-25	0	0												
	SUB-MECHAERV3 Mechanical AIR Recovery VentilatoSubmittals - Procurement	55	160	Mar-07-25	Dec-09-25	Mar-07-25 A	Dec-09-25	0	0												
	237313 Modular Indoor Air Handline Units -PD, SD's, Engineering	145	100	Jan-23-25	Jul-31-25	Jan-23-25 A	Jul-31-25	0	0												
	SUB-MECHAHU3 Mechanical AHU Submittals - Procurement	145	100	Jan-23-25	Jul-24-25	Jan-23-25 A	Jul-24-25	0	0												
	SUB-MECHAHU4 Mechanical AHU Submittals - Delivery to the Site	145	5	Jul-25-25	Jul-31-25	Jul-25-25	Jul-31-25	0	0												
	237313 VRV Heating and Cooling Air Rotation Units -SD's, PD	112	50	Jun-02-25	Aug-11-25	Jul-01-25	Sep-10-25	-21	-21												
	SUB-MECHVRV3 Mechanical VRV Submittals - Procurement	112	50	Jun-02-25	Aug-11-25	Jul-01-25	Sep-10-25	-21	-21												
	Division 26-Electrical	96	220	Feb-21-25	Oct-16-25	Feb-21-25 A	Oct-16-25	0	0												
	260519,260523,260526,260533,260536,260800 LV,Cntl,Grd,PC,Cab,RW's,Boxes,Cbl Ty,CXing-I	66	5	Jun-03-25	Jun-09-25	Jul-02-25	Jul-09-25	-21	-21												
	SUB-ELG4 Electrical GeneralSubmittals - Delivery to the Site	66	5	Jun-03-25	Jun-09-25	Jul-02-25	Jul-09-25	-21	-21												
	260573.16, 260573.19 Coordination Studies and Arc Flash Hazard Analysis - PD and Studies	99	28	Jun-02-25	Jul-07-25	Jul-01-25	Aug-08-25	-21	-24												
	SUB-COARC1 Coordination and Arc Flash Studies - Preparation	100	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21												
	SUB-COARC2 Coordination and Arc Flash Studies- AOR Approval	153	10	Jun-28-25	Jul-07-25	Jul-30-25	Aug-08-25	-32	-32												
	262213,262413,262416,262726,263600,264313LVD Xfmr,SwB,PnIB,Encl CB,XferSwit,Surge P	122	337	Feb-21-25	Oct-09-25	Feb-21-25 A	Oct-09-25	0	0												
	SUB-ELPNL3 Electrical Switchgear- Procurement	122	337	Feb-21-25	Oct-09-25	Feb-21-25 A	Oct-09-25	0	0												
	262816, 263353 Wiring Devices, UPS's- PD,	67	40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21												
	SUB-ELWDUPS3 Electrical Wiring Devices and UPS Submittals - Procurement	67	40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21												
	263213.13 Diesel Emergency Engine Generators -PD, Shop Drawings	96	130	Feb-27-25	Oct-16-25	Feb-27-25 A	Oct-16-25	0	0												
	SUB-ELGEN3 Electrical Generator Submittals - Procurement	96	130	Feb-27-25	Oct-16-25	Feb-27-25 A	Oct-16-25	0	0												
	260923,260943.16,265119,265213LCDDevices,Add Cntrl,LEDandE ExitLight -PD,SD's,Point L,Sr	137	5	Jul-02-25	Jul-09-25	Jul-02-25	Jul-09-25	0	0												
	SUB-ELLTG4 Electrical Lighting Submittals - Delivery to the Site	137	5	Jul-02-25	Jul-09-25	Jul-02-25	Jul-09-25	0	0												
	Division 27-Communications	134	28	Jun-02-25	Jul-07-25	Jul-01-25	Aug-08-25	-21	-24												
	270553, 271323, 271513 Id for Com Systems , Fiber Optic and Copper Cabling -PD and SD's	39	28	Jun-02-25	Jul-07-25	Jul-01-25	Aug-08-25	-21	-24												
	SUB-COMC1 Com System Cabling Submittals- Preparation	39	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21												
	SUB-COMC2 Com System Cabling Submittals - AOR Approval	63	10	Jun-28-25	Jul-07-25	Jul-30-25	Aug-08-25	-32	-32												
	271100, 271116 Com EquipRoom Fittings, Racks,Frames and Enclosures-PD and SD's	134	28	Jun-02-25	Jul-07-25	Jul-01-25	Aug-08-25	-21	-24												
	SUB-COME1 Com System Equipment Submittals- Preparation	136	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21												
	SUB-COME2 Com System Equipment Submittals -AOR Approval	206	10	Jun-28-25	Jul-07-25	Jul-30-25	Aug-08-25	-32	-32												
	Division 32-Exterior Improvements	128	40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21												
	320000, 320523, 321613 Offsite Improve, Cement and Concrete, Curb and Gutter- Samples, PC	115	28	Jun-02-25	Jul-07-25	Jul-01-25	Aug-08-25	-21	-24												
	SUB-OFFS1 Offsite Improvement Submittals - Preparation	117	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21												
	SUB-OFFS2 Offsite Improvement Submittals- AOR Approval	178	10	Jun-28-25	Jul-07-25	Jul-30-25	Aug-08-25	-32	-32												
	321123,321216,321300 Aggregate Base Courses, Asphalt and Rigid Paving	143	25	Jun-02-25	Jul-07-25	Jul-01-25	Aug-05-25	-21	-21												
	SUB-ASRGDPV3 Asphalt and Rigid Paving Submittals- Procurement	143	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21												
	SUB-ASRGDPV4 Asphalt and Rigid Paving Submittals- Delivery to the Site	143	5	Jun-30-25	Jul-07-25	Jul-30-25	Aug-05-25	-21	-21												
	321723, 321726 Pavement Markings and Tactile Warning Surfaces- PD, SD's	73	40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21												
	SUB-PAVE3 Pavement Marking and Tactile Surfaces Submittals - Procurement	73	40	Jun-02-25	Jul-28-25	Jul-01-25	Aug-26-25	-21	-21												
	323113,323119 Chain Link and Decorative Metal Fencing and Gates PD, Samples, Engineering	80	28	Jun-02-25	Jul-07-25	Jul-01-25	Aug-08-25	-21	-24												
	SUB-FENC1 Chain Link Fencing and Metal Gates Submittals- Preparation	80	20	Jun-02-25	Jun-27-25	Jul-01-25	Jul-29-25	-21	-21												
	SUB-FENC2 Chain Link Fencing and Metal Gates Submittals -AOR Approval	124	10	Jun-28-25	Jul-07-25	Jul-30-25	Aug-08-25	-32	-32												
	320100,321543,328000,329300,323300 Land Plant,Mat,Irr, Maint, DG and SiteFurn-PD,Smpl,Sched, SD's	83	30	Jun-02-25	Jul-14-25	Jul-01-25	Aug-12-25	-21	-21												
	SUB-LAND3 Landscaping Submittals- Procurement	83	30	Jun-02-25	Jul-14-25	Jul-01-25	Aug-12-25	-21	-21												
	Division 33-Utilities	42	5	Jun-03-25	Jun-09-25	Jul-02-25	Jul-09-25	-21	-21												
	331000, 331100 Water Utilities and Distribution- PD, SD's, Samples, Reports	42	5	Jun-03-25	Jun-09-25	Jul-02-25	Jul-09-25	-21	-21												
	SUB-SUW4 Site Utilities Water - Delivery to the Site	42	5	Jun-03-25	Jun-09-25	Jul-02-25	Jul-09-25	-21	-21												
	Construction	72	121	Jun-03-25	Nov-17-25	Jun-09-25 A	Dec-12-25	-4	-17												
	Fragnets	14	26	Jun-03-25	Jul-09-25	Jul-02-25	Aug-07-25	-21	-21												
	ASI-04 - Dry System	14	26	Jun-03-25	Jul-09-25	Jul-02-25	Aug-07-25	-21	-21												
	FRAG-ASI04-1120 OSFM Review of Shop Drawings	14	26	Jun-03-25	Jul-09-25	Jul-02-25	Aug-07-25	-21	-21												
	LACounty Water Works Permit Process	30	27	Jun-03-25	Jul-10-25	Jul-02-25	Aug-08-25	-21	-21												
	FRAG-LACWW-1010 Water Line material procurement	26	20	Jun-03-25	Jun-30-25	Jul-02-25	Jul-30-25	-21	-21												

 Project Baseline Bar  Critical Remaining Work
 Actual Work  Milestone
 Remaining Work  Summary

4-Week Lookahead

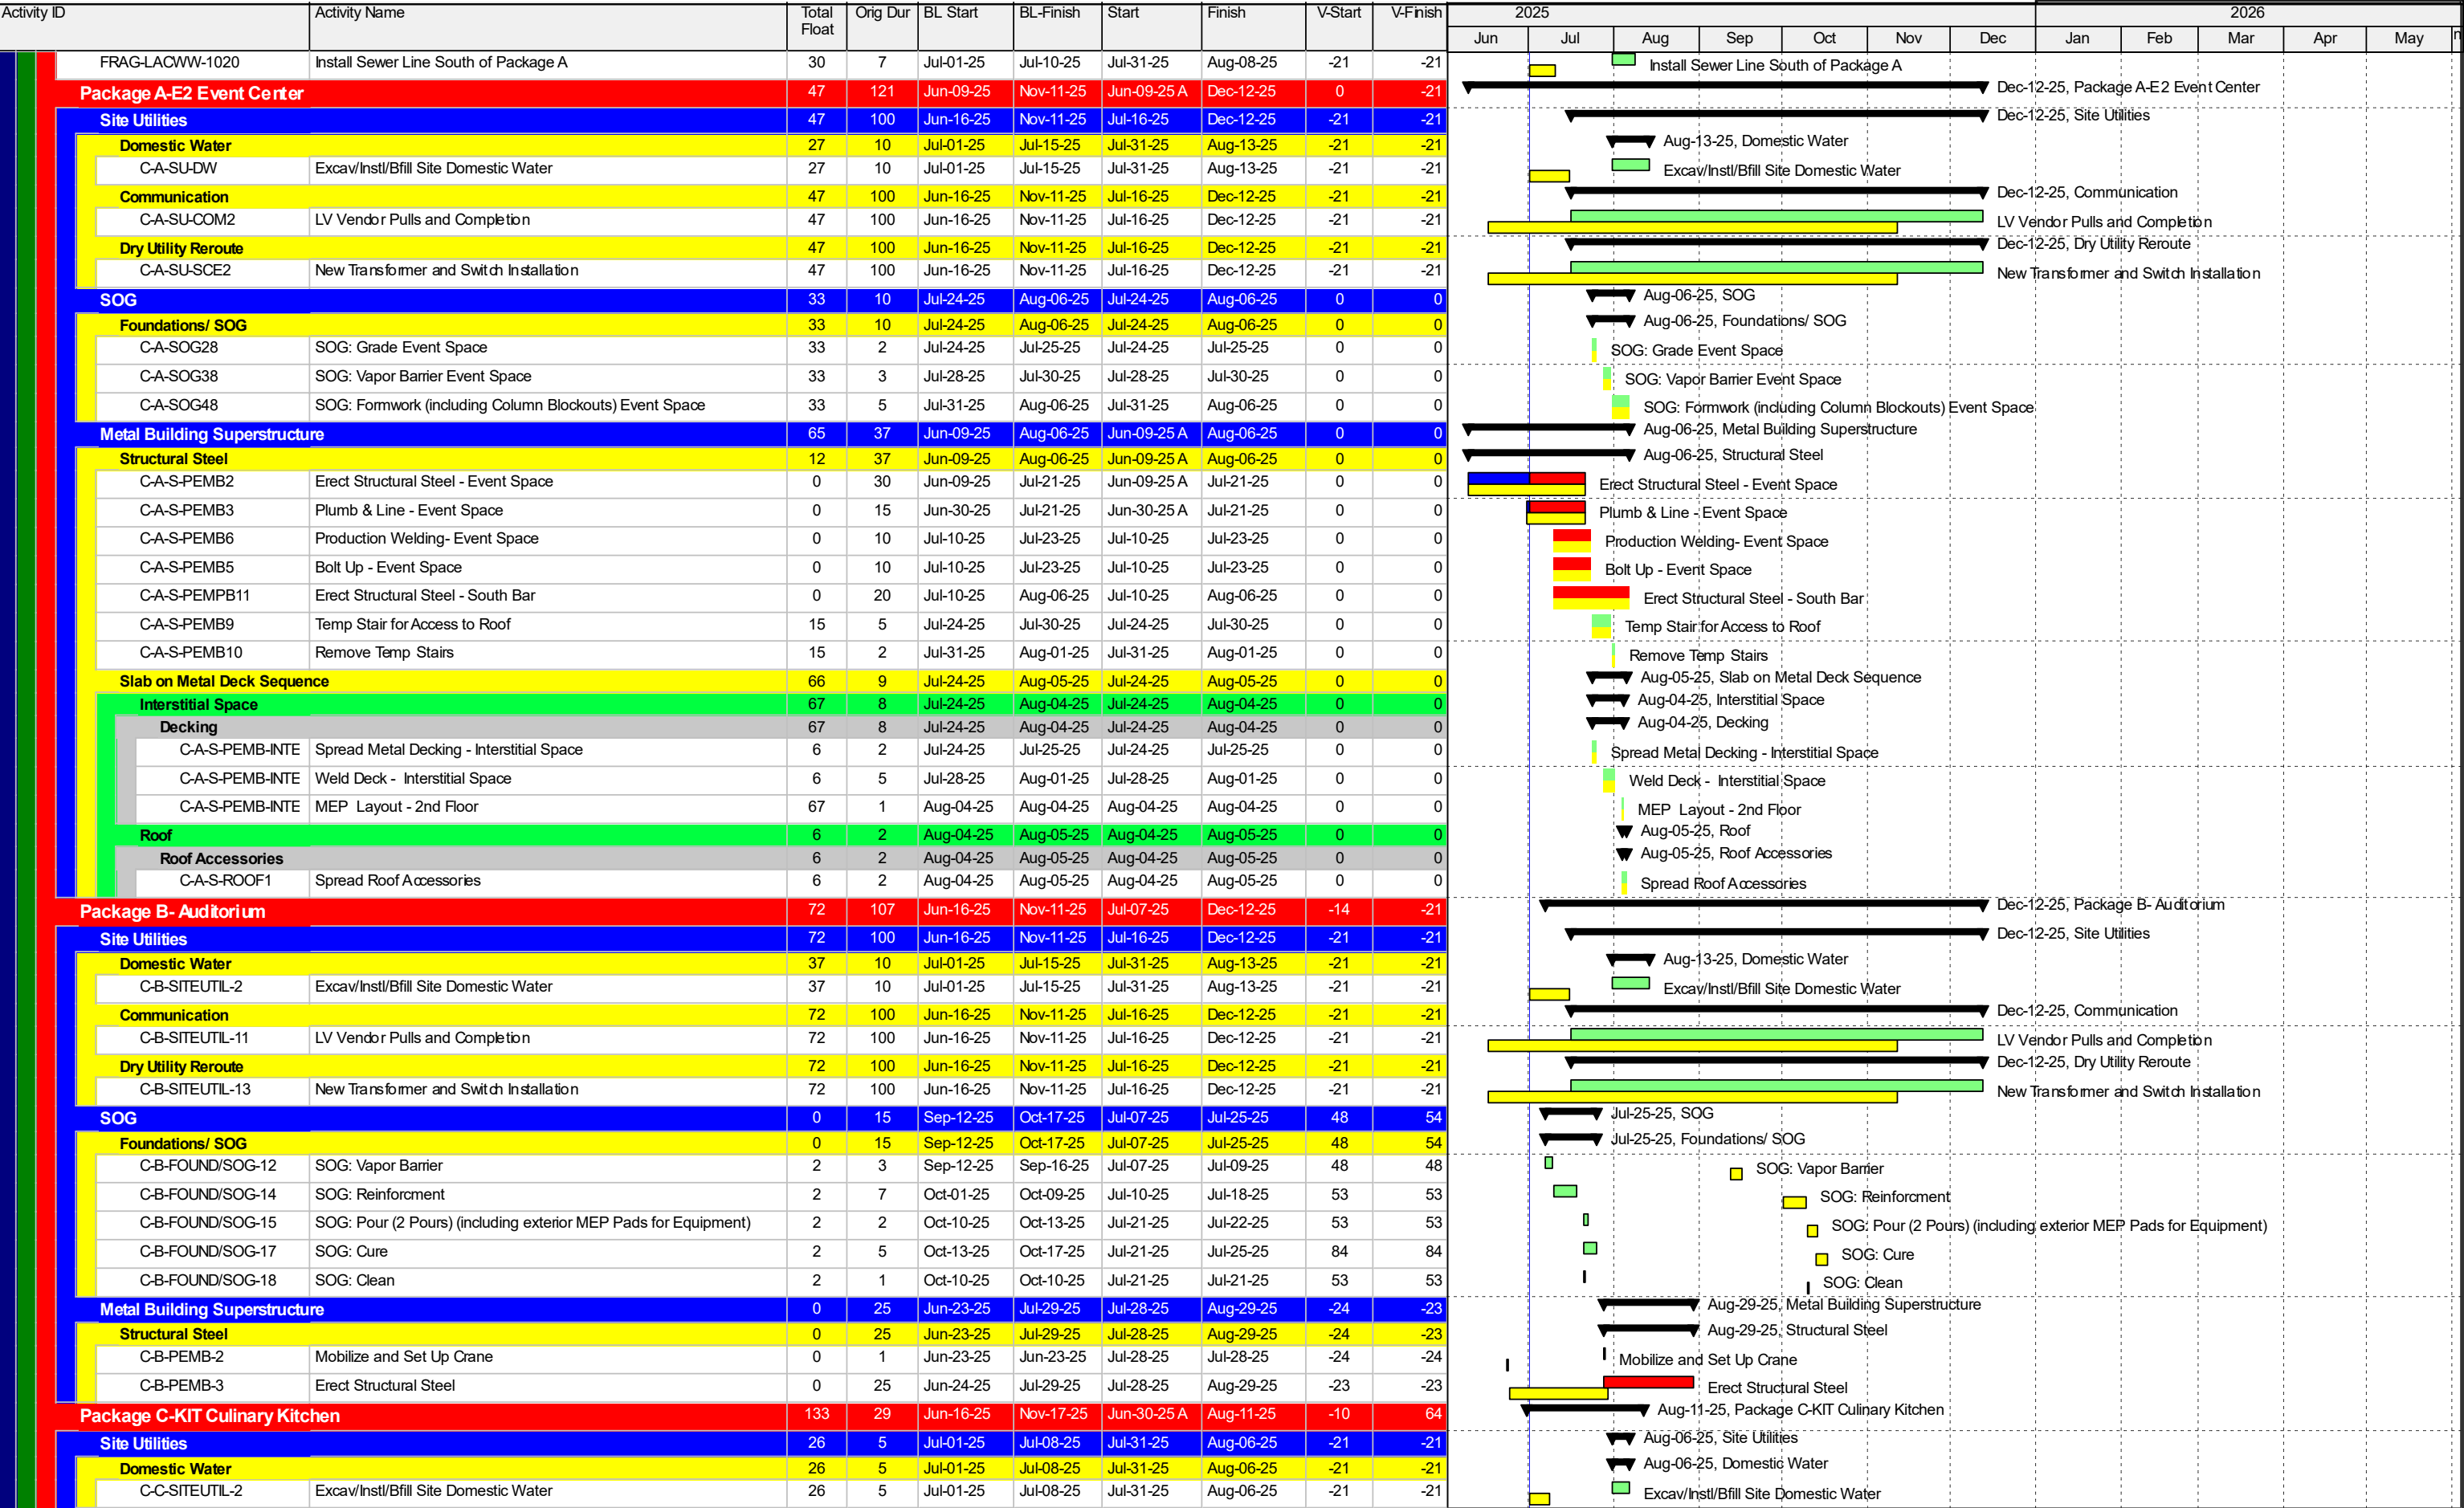



Multi-Agency Regional Resiliency Center (M.A.R.R.C.) - June 2025

4-Week Lookahead

Activity ID	Activity Name	Total Float	Orig Dur	BL Start	BL-Finish	Start	Finish	V-Start	V-Finish	2025						2026						
										Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	
Interior Build Out		133	29	Jun-16-25	Nov-17-25	Jun-30-25 A	Aug-11-25	-10	64	Aug-11-25, Interior Build Out												
	Area A "Men's Room, Women's Room, Janitorial, Water Heat, Laundry, Restrooms"		137	20	Oct-17-25	Nov-13-25	Jul-09-25	Aug-05-25	66	66	Aug-05-25, Area A "Men's Room, Women's Room, Janitorial, Water Heat, Laundry, Restrooms"											
	Mechanical Room C117-1		137	20	Oct-17-25	Nov-13-25	Jul-09-25	Aug-05-25	66	66	Aug-05-25, Mechanical Room C117-1											
	C-C-INTBO-A-MECH3	Plywood Backing	137	5	Oct-17-25	Oct-23-25	Jul-09-25	Jul-15-25	66	66	Plywood Backing											
	C-C-INTBO-A-MECH4	Mech. Room Fit Out with Equipment	137	5	Oct-24-25	Oct-30-25	Jul-16-25	Jul-22-25	66	66	Mech. Room Fit Out with Equipment											
	C-C-INTBO-A-MECH5	Equipment Installation	137	5	Oct-31-25	Nov-06-25	Jul-23-25	Jul-29-25	66	66	Equipment Installation											
	C-C-INTBO-A-MECH6	Terminations and Testing	137	5	Nov-07-25	Nov-13-25	Jul-30-25	Aug-05-25	66	66	Terminations and Testing											
	Area B " Elec Room, Fire Riser, Kitchen, Scullery, Dry Storage, Refer, Demo Kit, Assembly"		128	29	Jun-16-25	Nov-17-25	Jun-30-25 A	Aug-11-25	-10	64	Aug-11-25, Area B " Elec Room, Fire Riser, Kitchen, Scullery, Dry Storage, Refer, Demo Kit, Assembly"											
	Finishes		98	29	Oct-07-25	Nov-17-25	Jun-30-25 A	Aug-11-25	64	64	Aug-11-25, Finishes											
	Kitchen		98	29	Oct-07-25	Nov-17-25	Jun-30-25 A	Aug-11-25	64	64	Aug-11-25, Kitchen											
	C-C-INTBO-B-KIT-1	Install Insulated Slabs for Walk-ins	98	15	Oct-07-25	Oct-27-25	Jun-30-25 A	Jul-21-25	64	64	Install Insulated Slabs for Walk-ins											
	C-C-INTBO-B-KIT-2	Install Walk-in Cooler/Freezers - Line Sets and Condensers	98	15	Oct-28-25	Nov-17-25	Jul-22-25	Aug-11-25	64	64	Install Walk-in Cooler/Freezers - Line Sets and Condensers											
	Electrical Room C116		146	5	Jun-16-25	Jun-20-25	Jul-02-25	Jul-09-25	-12	-12	Jul-09-25, Electrical Room C116											
	C-C-INTBO-B-ELEC3	Plywood Backing	146	5	Jun-16-25	Jun-20-25	Jul-02-25	Jul-09-25	-12	-12	Plywood Backing											
	Fire Riser Room C115		151	5	Jun-16-25	Jun-20-25	Jul-02-25	Jul-09-25	-12	-12	Jul-09-25, Fire Riser Room C115											
	C-C-INTBO-B-FIRE3	Fire Riser Room Fit Out with Equipment	151	5	Jun-16-25	Jun-20-25	Jul-02-25	Jul-09-25	-12	-12	Fire Riser Room Fit Out with Equipment											

Project Baseline Bar

Actual Work

Remaining Work

Critical Remaining Work

◆

◆ Milestone

▬

Summary
