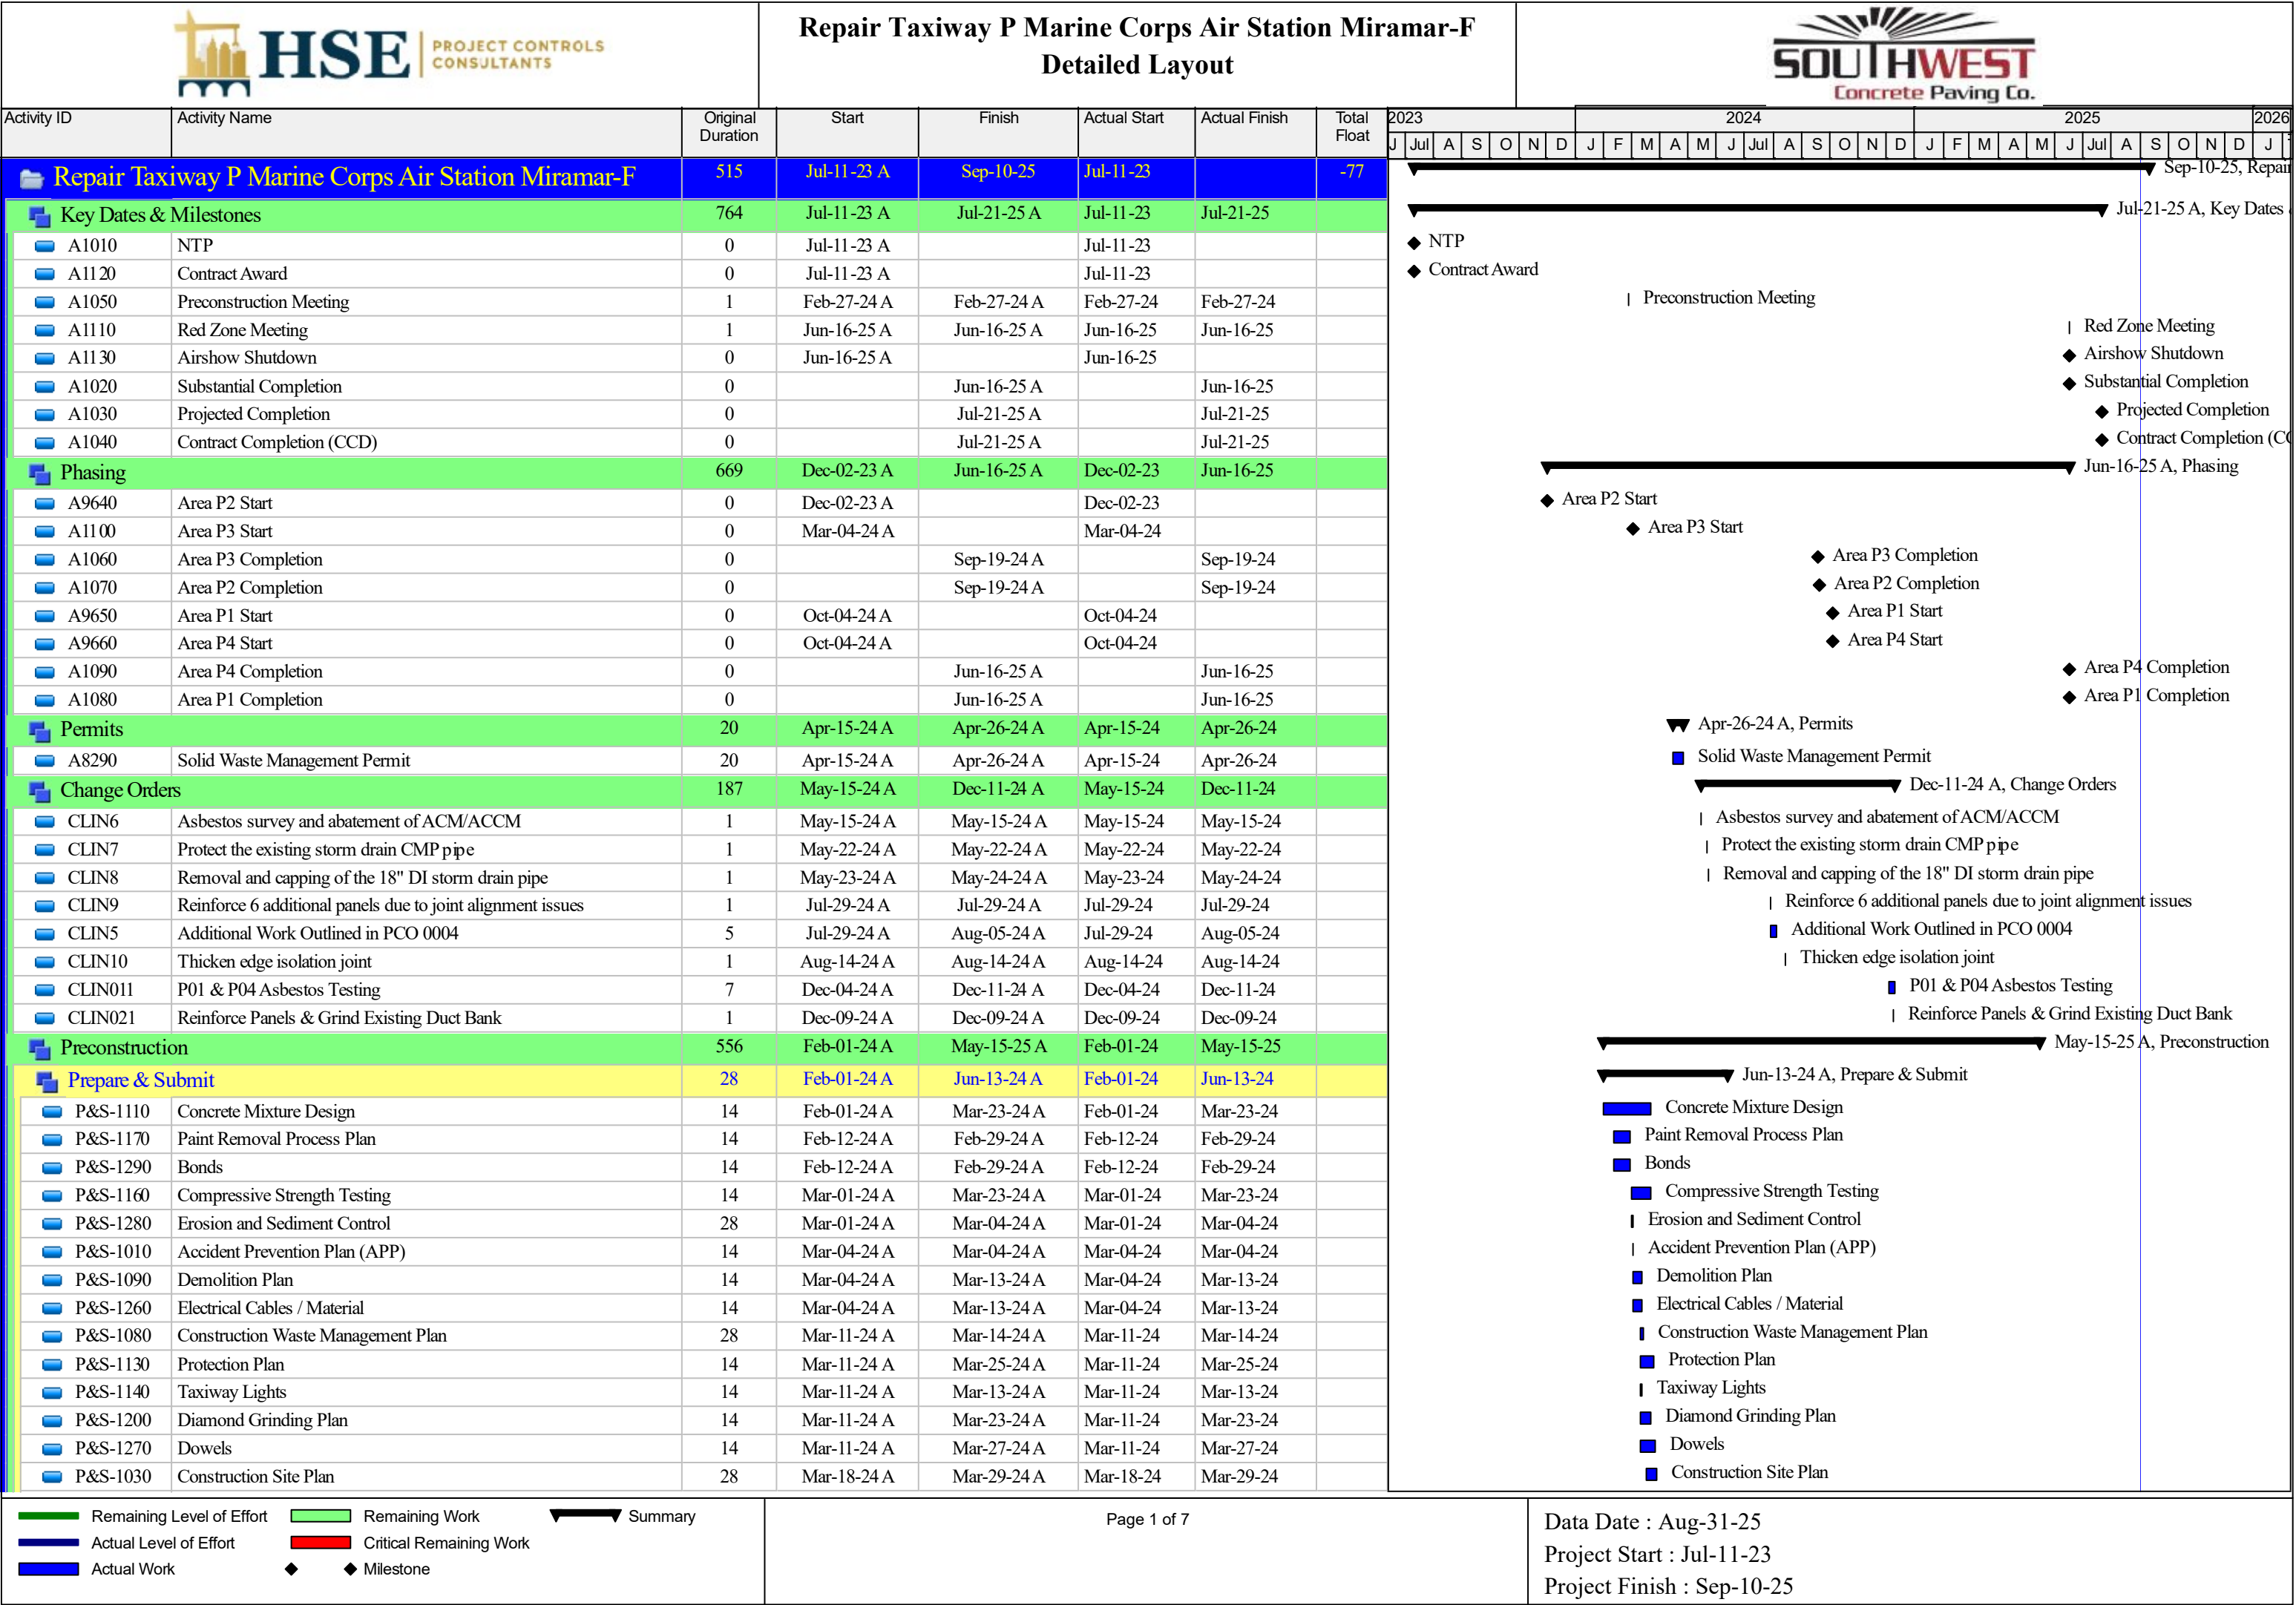










Data Date : Aug-31-25
Project Start : Jul-11-23
Project Finish : Sep-10-25

Data Date : Aug-31-25
Project Start : Jul-11-23
Project Finish : Sep-10-25

Data Date : Aug-31-25
Project Start : Jul-11-23
Project Finish : Sep-10-25

Data Date : Aug-31-25
Project Start : Jul-11-23
Project Finish : Sep-10-25

			Repair Taxiway P Marine Corps Air Station Miramar-F Detailed Layout																																					
Activity ID	Activity Name	Original Duration	Start	Finish	Actual Start	Actual Finish	Total Float	2023							2024							2025							2026											
								J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	
	 A10110 ReFeed ReConnect Existing Lighted Sign	3	Sep-16-24 A	Sep-16-24 A	Sep-16-24	Sep-16-24																																		
	 HMA	37	Jul-12-24 A	Sep-17-24 A	Jul-12-24	Sep-17-24																																		
	 A8580 Asphalt Emulsion - P3	1	Jul-12-24 A	Jul-26-24 A	Jul-12-24	Jul-26-24																																		
	 A8570 PCC Pavement & Joints - P3	36	Jul-29-24 A	Aug-30-24 A	Jul-29-24	Aug-30-24																																		
	 A8510 Seal Asphalt Cracks Shoulders - P3	8	Aug-06-24 A	Aug-08-24 A	Aug-06-24	Aug-08-24																																		
	 A8590 Asphalt Surface Treatment - P3	2	Sep-04-24 A	Sep-04-24 A	Sep-04-24	Sep-04-24																																		
	 A8600 Asphalt Pavement 1st Lift - P3	3	Sep-05-24 A	Sep-05-24 A	Sep-05-24	Sep-05-24																																		
	 A8620 Asphalt Pavement 2nd Lift - P3	3	Sep-06-24 A	Sep-06-24 A	Sep-06-24	Sep-06-24																																		
	 A8520 Asphalt Fog Coat Shoulders - P3	1	Sep-17-24 A	Sep-17-24 A	Sep-17-24	Sep-17-24																																		
	 Stripping	2	Sep-16-24 A	Sep-17-24 A	Sep-16-24	Sep-17-24																																		
	 A9680 Remove Temp Stripe	2	Sep-16-24 A	Sep-17-24 A	Sep-16-24	Sep-17-24																																		
	 A10060 Install Perm Stripe	2	Sep-16-24 A	Sep-17-24 A	Sep-16-24	Sep-17-24																																		
	 Punchlist	79	Sep-19-24 A	Sep-19-24 A	Sep-19-24	Sep-19-24																																		
	 A9560 Pre-Final Inspection - P3	1	Sep-19-24 A	Sep-19-24 A	Sep-19-24	Sep-19-24																																		
	 A9570 Punch List Repair - P3	1	Sep-19-24 A	Sep-19-24 A	Sep-19-24	Sep-19-24																																		
	 A9860 Remove Low Pro Barricades - P3	1	Sep-19-24 A	Sep-19-24 A	Sep-19-24	Sep-19-24																																		
	 A9870 Final Inspection - P3	1	Sep-19-24 A	Sep-19-24 A	Sep-19-24	Sep-19-24																																		
	 Phase 2 & 3 Panel Repair	18	May-19-25 A	Jun-18-25 A	May-19-25	Jun-18-25																																		
	 A10160 Traffic Control	1	May-19-25 A	May-20-25 A	May-19-25	May-20-25																																		
	 A10170 Demo Saw	2	May-20-25 A	May-20-25 A	May-20-25	May-20-25																																		
	 A10180 Demo Panel	2	May-20-25 A	May-22-25 A	May-20-25	May-22-25																																		
	 A10190 Prep Panels/Drill & Dowel	2	May-27-25 A	May-28-25 A	May-27-25	May-28-25																																		
	 A10200 Pour Panels	1	May-29-25 A	May-29-25 A	May-29-25	May-29-25																																		
	 A10210 Cure Time	18	May-29-25 A	Jun-13-25 A	May-29-25	Jun-13-25																																		
	 A10220 Re Stripe	1	Jun-13-25 A	Jun-15-25 A	Jun-13-25	Jun-15-25																																		
	 A10230 Remove Traffic Control	1	Jun-16-25 A	Jun-18-25 A	Jun-16-25	Jun-18-25																																		
	 Area P4	162	Oct-04-24 A	May-20-25 A	Oct-04-24	May-20-25																																		
	 Site Preperation	8	Oct-07-24 A	Oct-10-24 A	Oct-07-24	Oct-10-24																																		
 A9260 Erosion Control - P4	2	Oct-07-24 A	Oct-10-24 A	Oct-07-24	Oct-10-24																																			
 A9270 MOT - P4	2	Oct-07-24 A	Oct-07-24 A	Oct-07-24	Oct-07-24																																			
 A9300 Install Low Profile Barricade - P4	2	Oct-07-24 A	Oct-07-24 A	Oct-07-24	Oct-07-24																																			
 A9310 Temp. Non Movement Boundary - P4	2	Oct-07-24 A	Oct-10-24 A	Oct-07-24	Oct-10-24																																			
 A9380 Protect Existing Utilities - P4	2	Oct-07-24 A	Oct-10-24 A	Oct-07-24	Oct-10-24																																			
 A9280 Temp. Bypass Lighting - P4	2	Oct-08-24 A	Oct-10-24 A	Oct-08-24	Oct-10-24																																			
 Demolition	51	Oct-08-24 A	Feb-03-25 A	Oct-08-24	Feb-03-25																																			
 A9320 Remove Existing Pavement Markings / Existing Striping - P4	4	Oct-08-24 A	Oct-10-24 A	Oct-08-24	Oct-10-24																																			
 A9550 Remove Existing Lighting - P4	6	Oct-08-24 A	Oct-10-24 A	Oct-08-24	Oct-10-24																																			
 A9330 Sawcut Existing PCC Pavement - P4	7	Oct-16-24 A	Oct-28-24 A	Oct-16-24	Oct-28-24																																			
 A9340 Sawcut Existing Asphalt Pavement - P4	8	Oct-17-24 A	Oct-19-24 A	Oct-17-24	Oct-19-24																																			
 A9350 Demolish Existing PCC Pavement - P4	8	Oct-21-24 A	Nov-19-24 A	Oct-21-24	Nov-19-24																																			
 A9800 PCC Removal / Off-Haul - P4	10	Nov-05-24 A	Dec-20-24 A	Nov-05-24	Dec-20-24																																			
 A9360 Demolish Existing Asphalt Pavement - P4	8	Nov-22-24 A	Jan-23-25 A	Nov-22-24	Jan-23-25																																			
 A9370 Demolish Existing Airfield Lighting Utility - P4	8	Nov-22-24 A	Feb-03-25 A	Nov-22-24	Feb-03-25																																			
 A9390 Contaminated Soil Removal - P4	16	Dec-06-24 A	Dec-09-24 A	Dec-06-24	Dec-09-24																																			
 Construction	118	Oct-04-24 A	May-16-25 A	Oct-04-24	May-16-25																																			
 Pavement Repair	118	Oct-04-24 A	May-16-25 A	Oct-04-24	May-16-25																																			

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Page 6 of 7

Data Date : Aug-31-25
Project Start : Jul-11-23
Project Finish : Sep-10-25

Data Date : Aug-31-25
Project Start : Jul-11-23
Project Finish : Sep-10-25
