

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 2 of 99
Data date : Oct-31-2025

Page 2 of 99

Data date : Oct-31-2025




INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 3 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

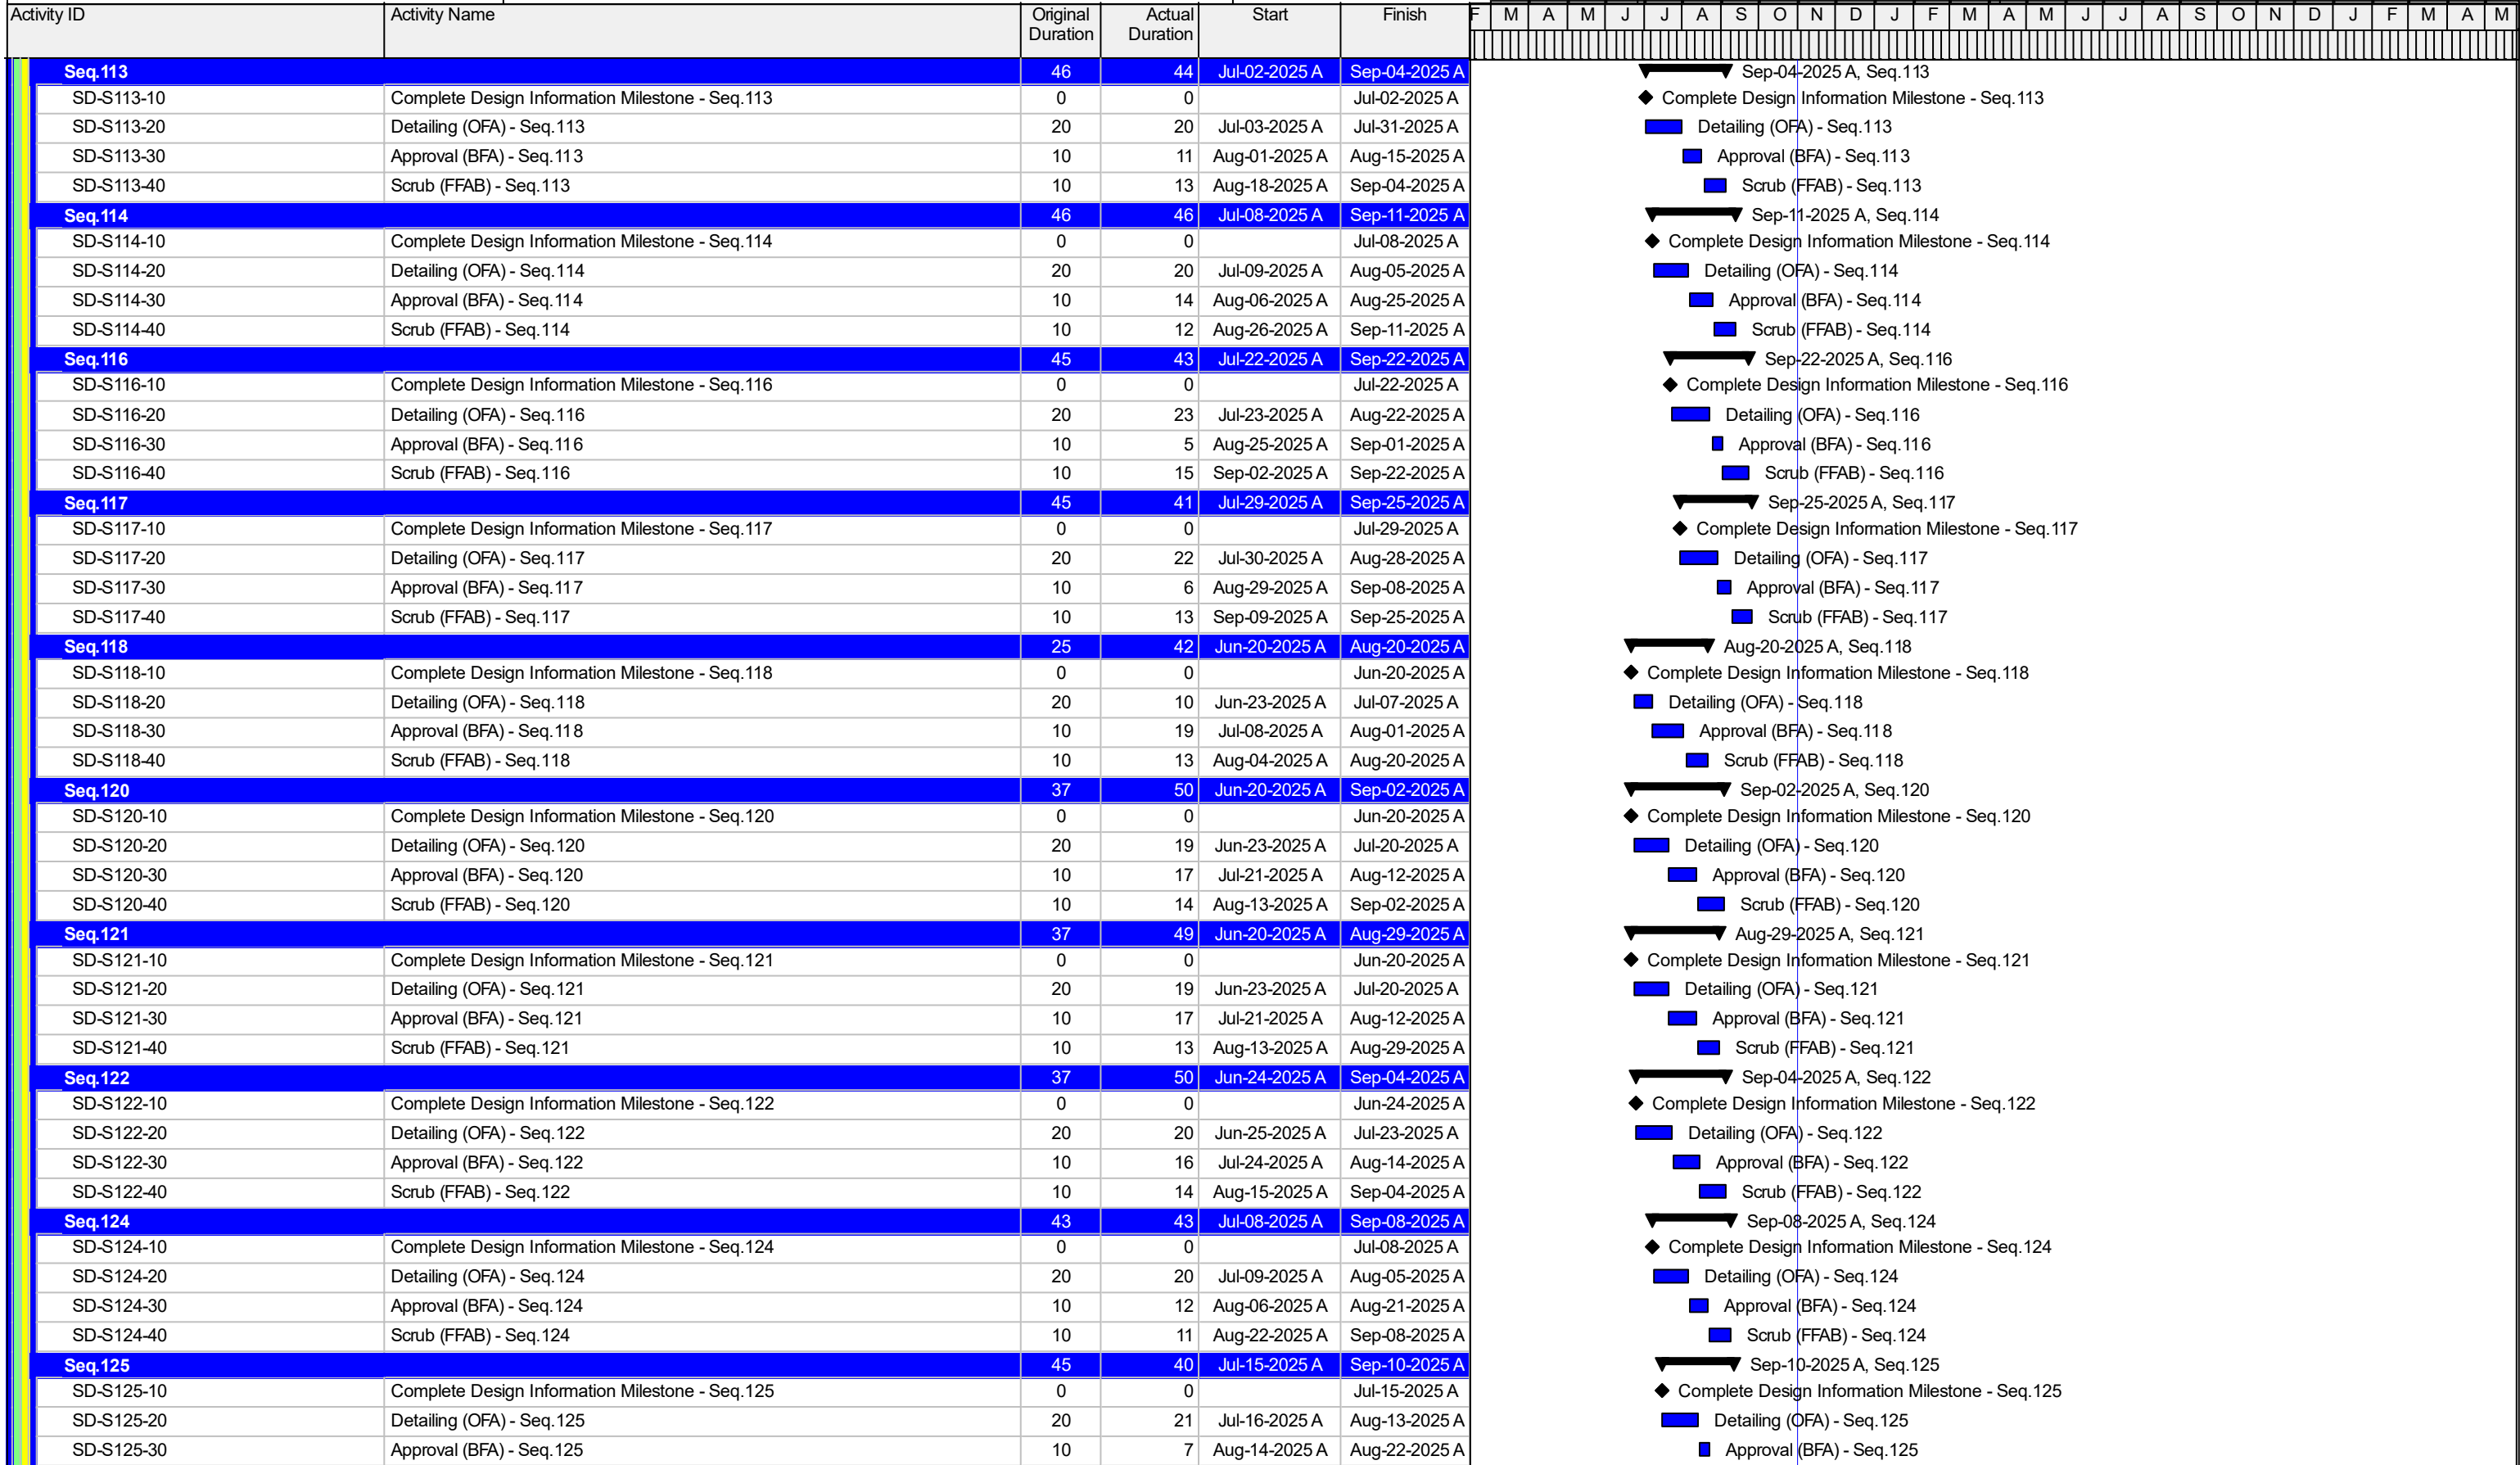

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 4 of 99
Data date : Oct-31-2025

Page 4 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 5 of 99
Data date : Oct-31-2025

Page 5 of 99

Data date : Oct-31-2025




INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 6 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

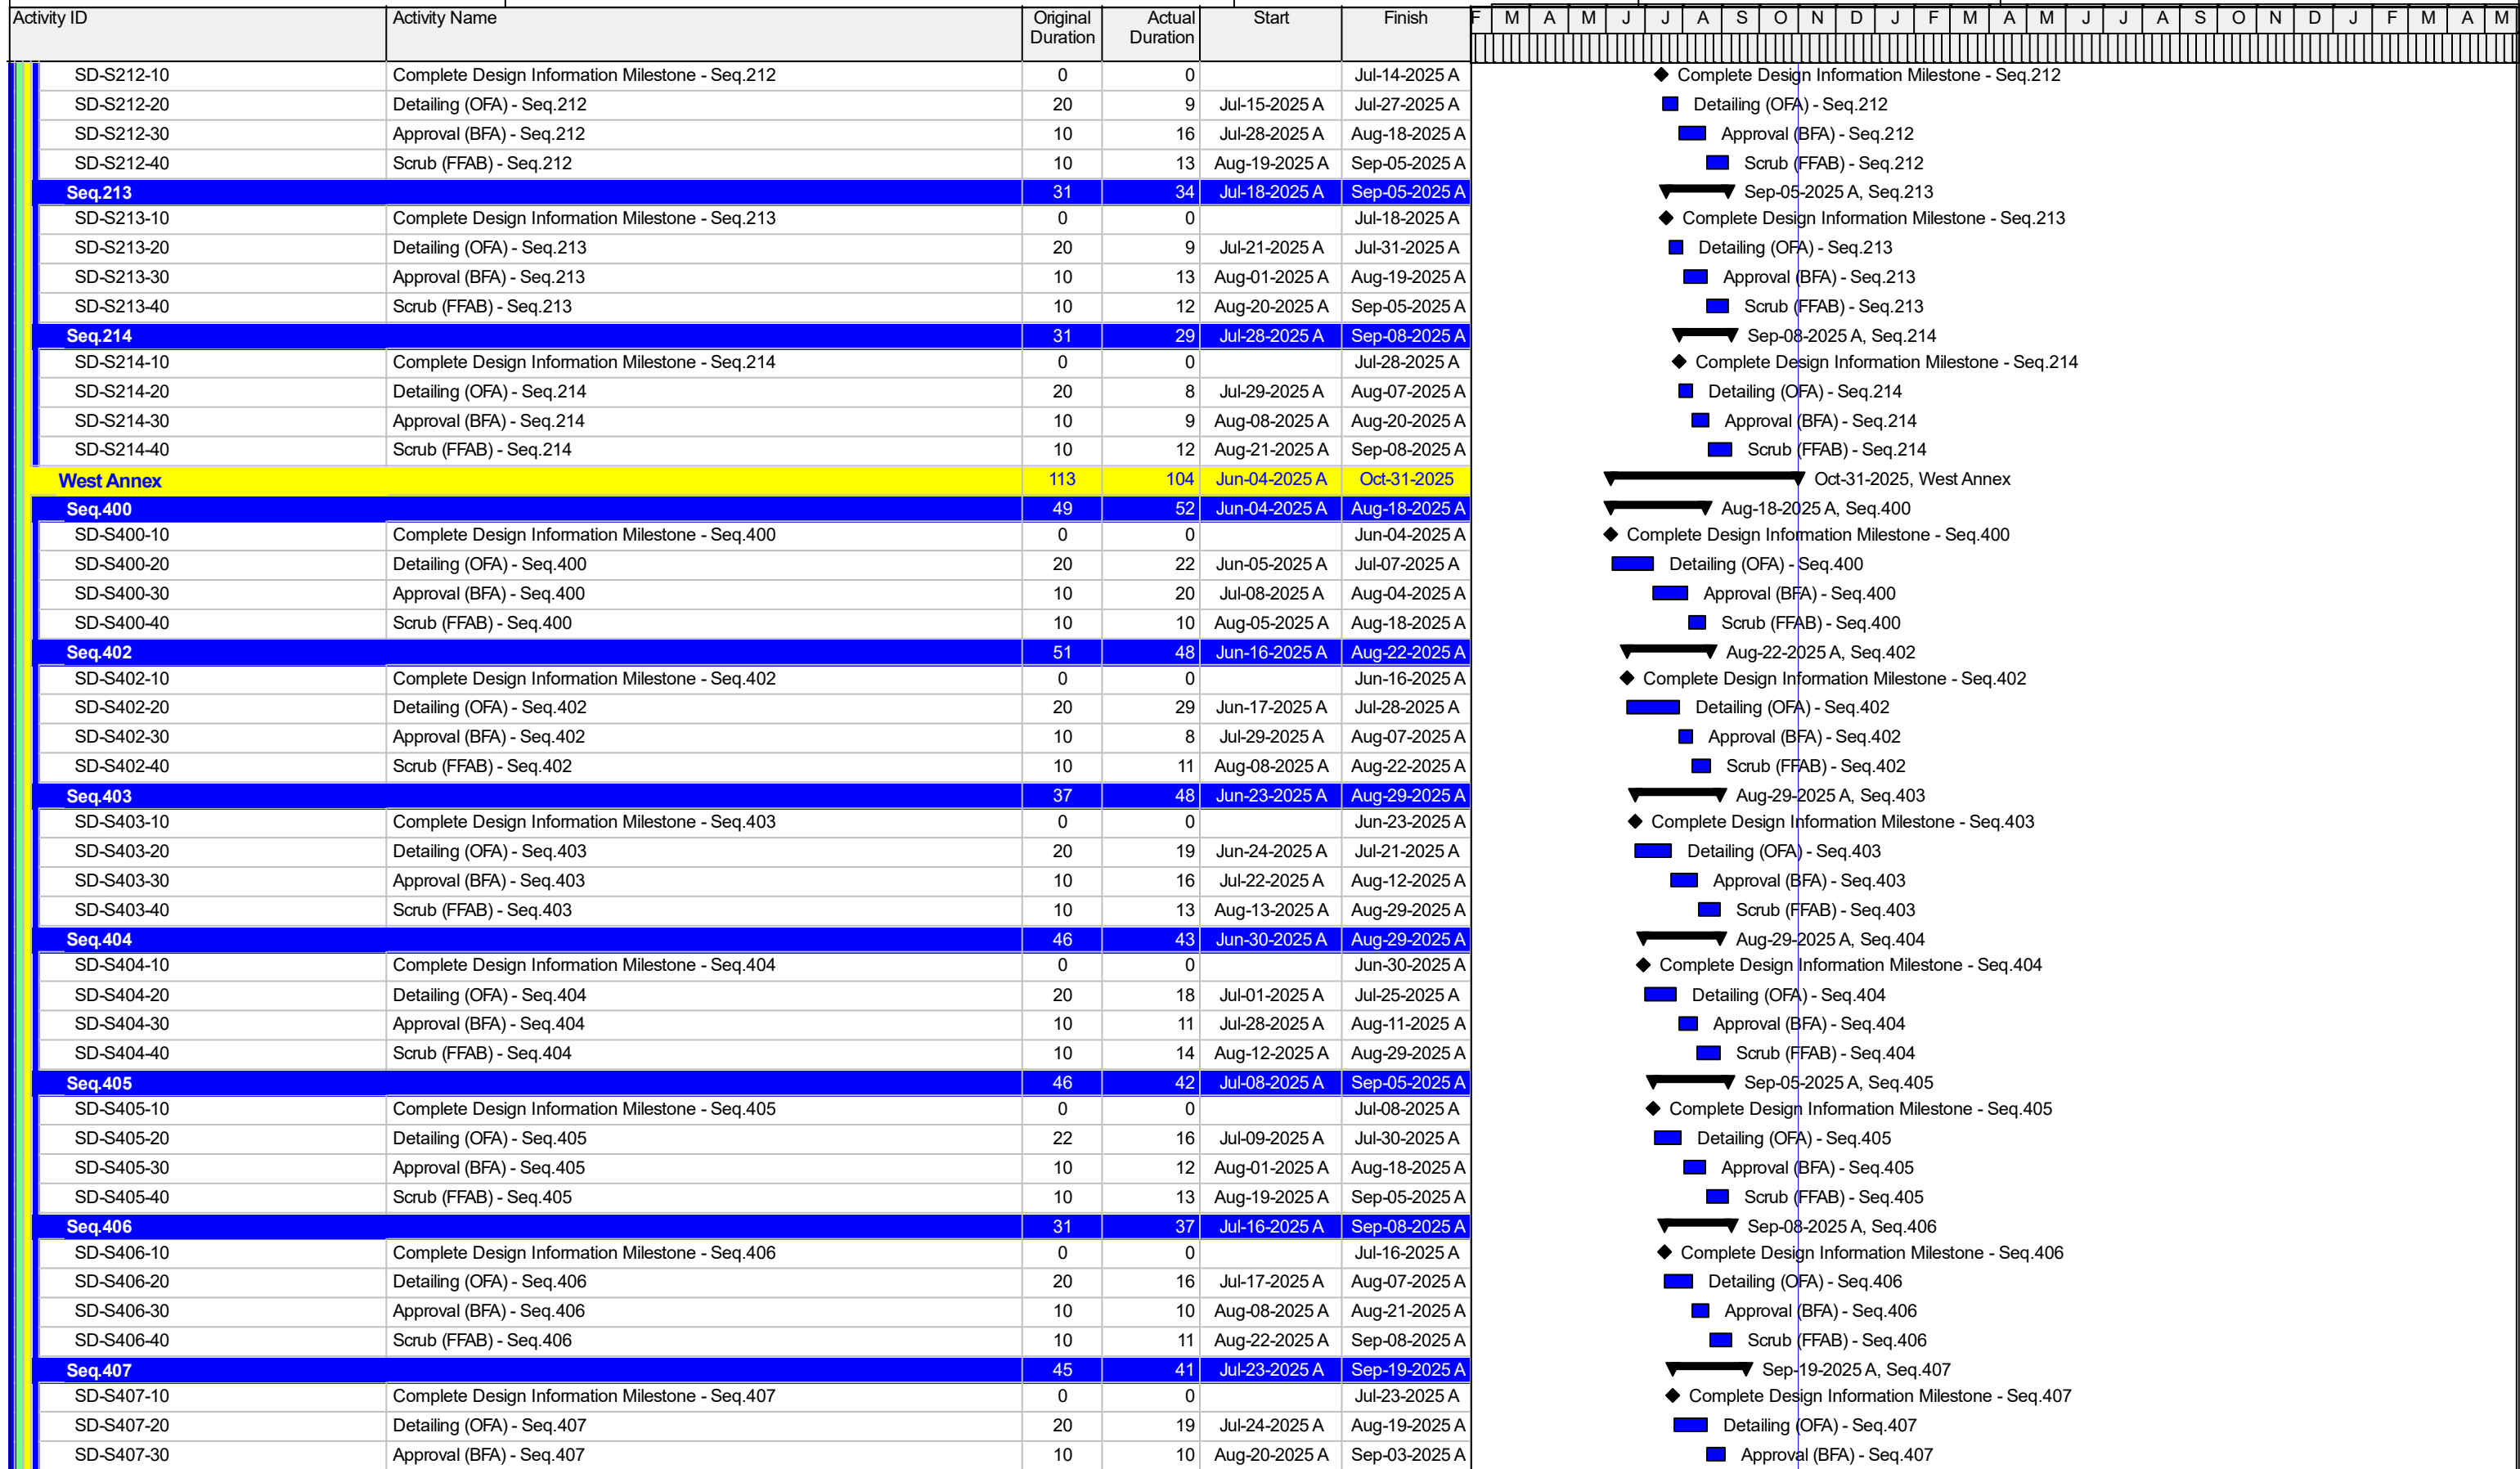


INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 10 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

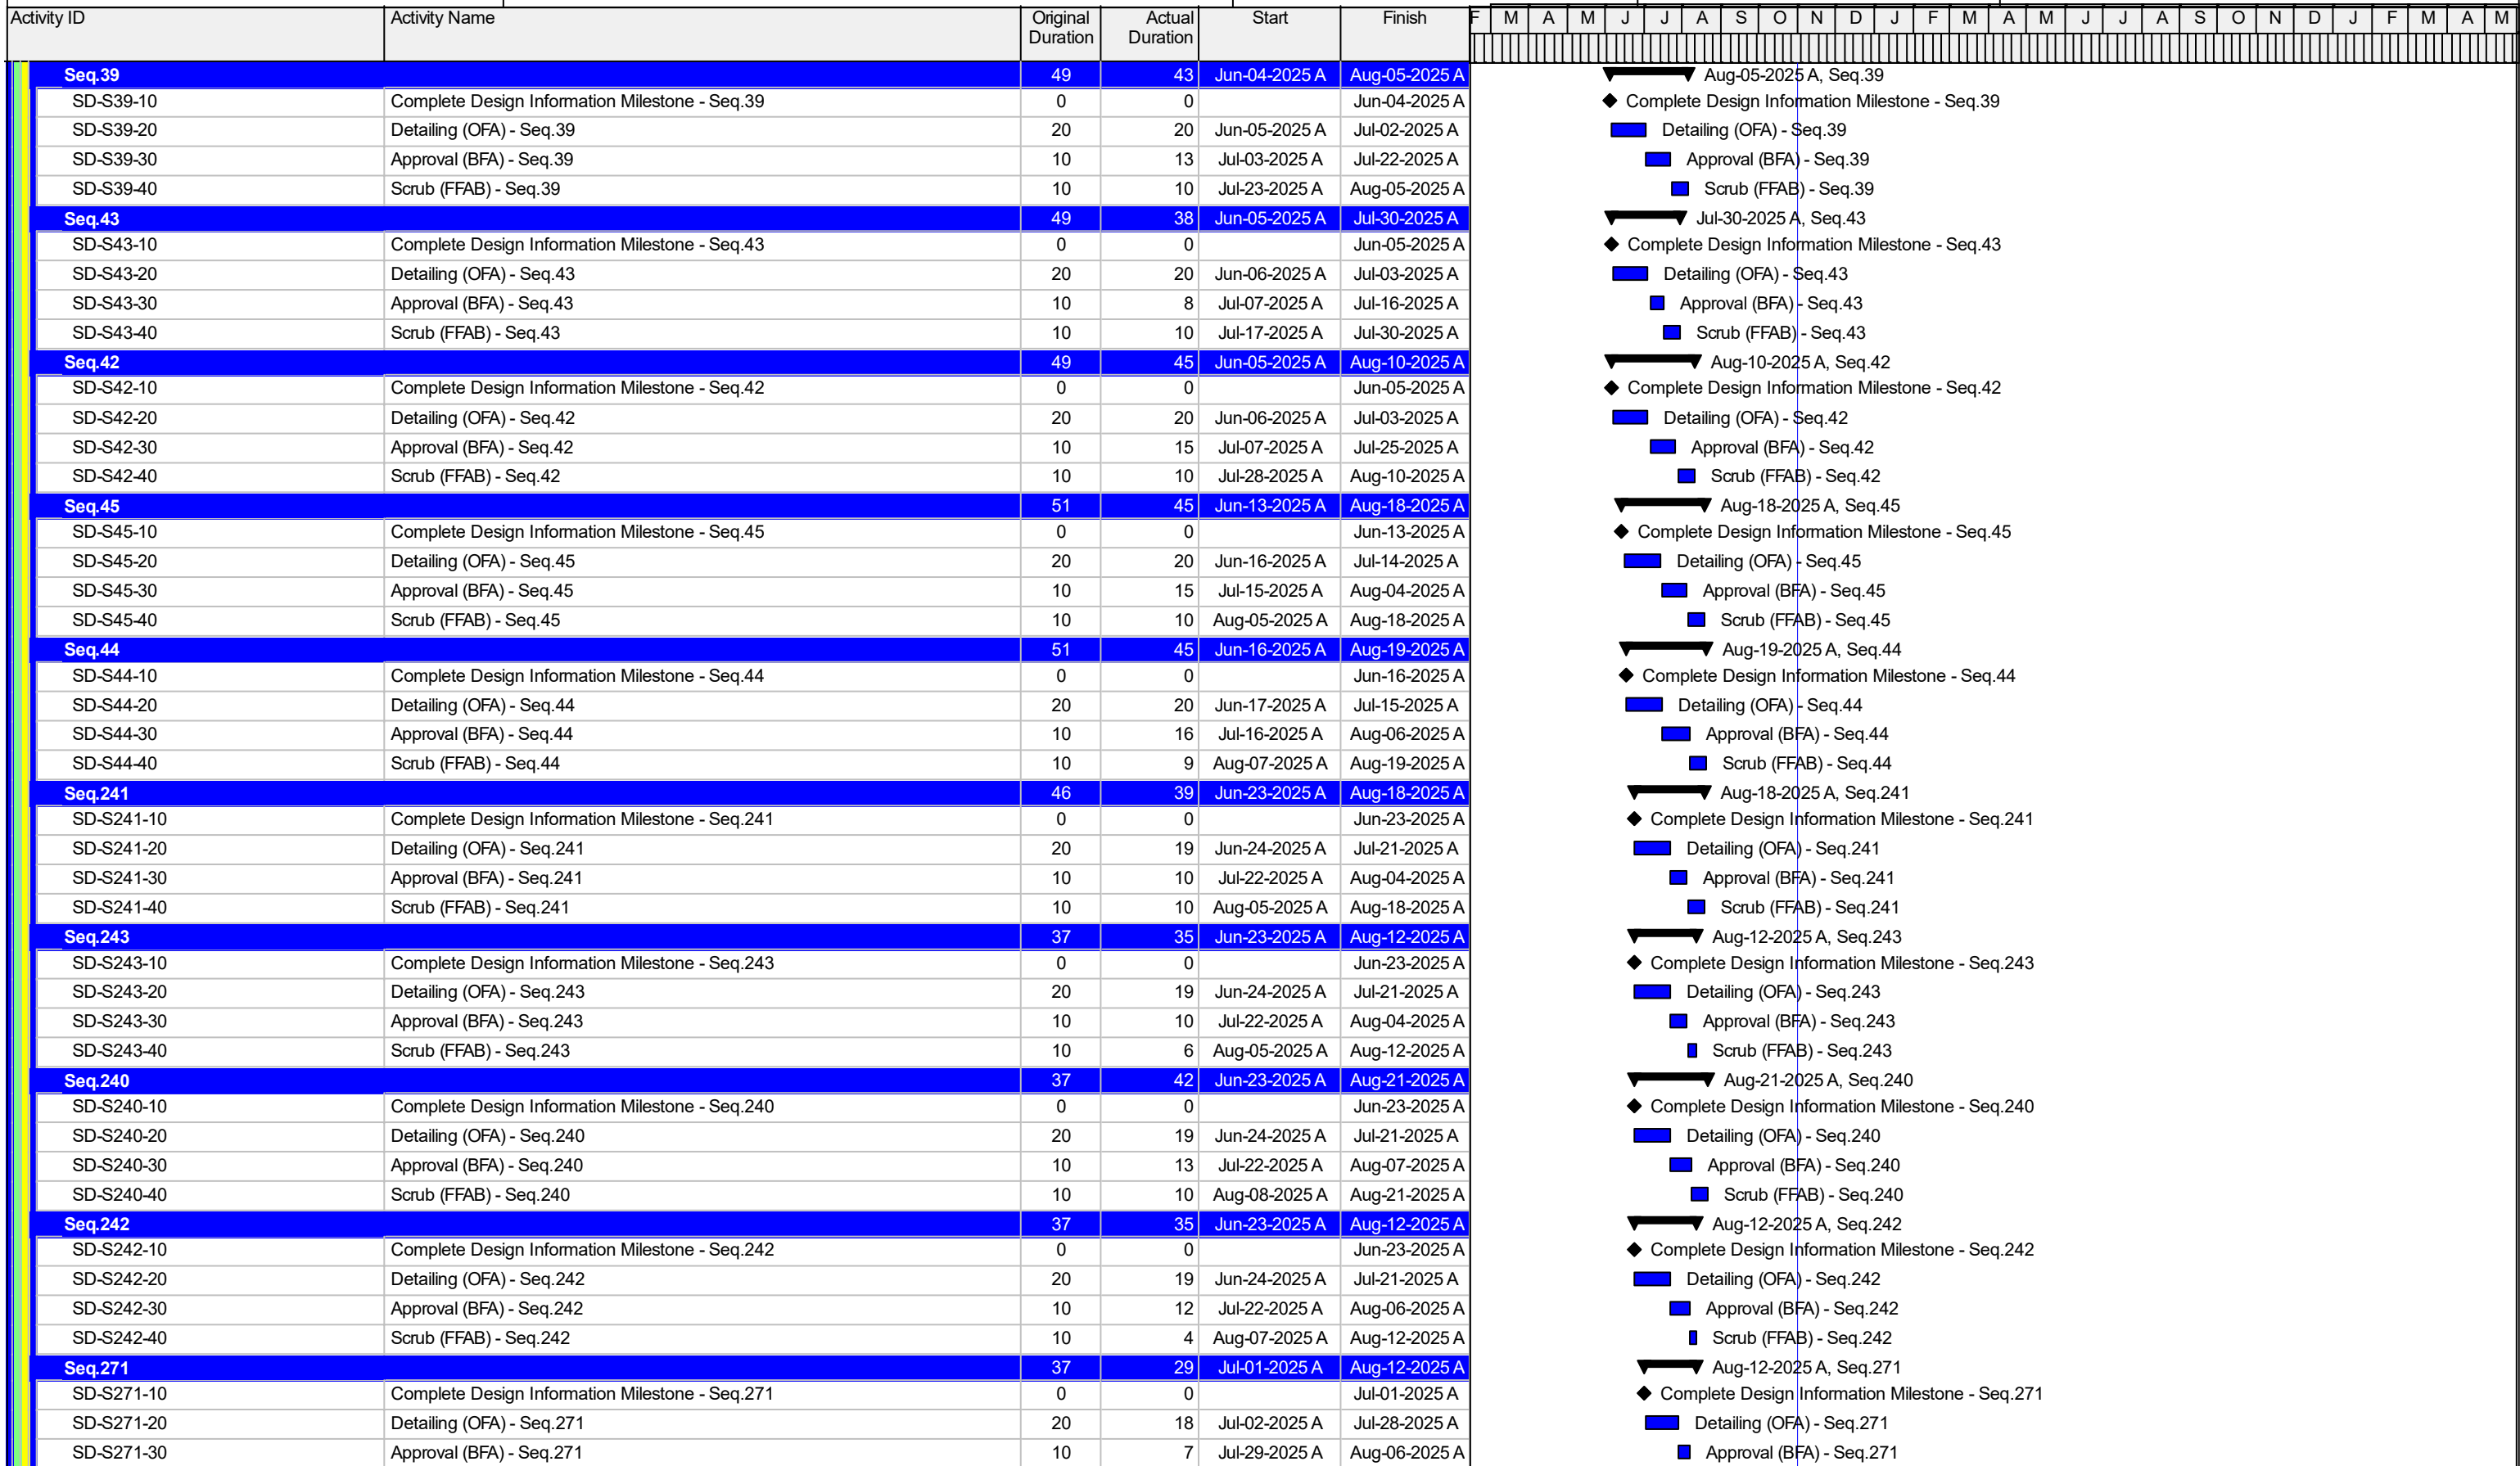

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 12 of 99
Data date : Oct-31-2025

Page 12 of 99

Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary




Activity ID		Activity Name	Original Duration	Actual Duration	Start	Finish	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M
	SD-S342-30	Approval (BFA) - Seq.342	10	13	Aug-04-2025 A	Aug-20-2025 A																												
	SD-S342-40	Scrub (FFAB) - Seq.342	10	10	Aug-21-2025 A	Sep-04-2025 A																												
	Seq.344		46	40	Jul-09-2025 A	Sep-04-2025 A																												
	SD-S344-10	Complete Design Information Milestone - Seq.344	0	0		Jul-09-2025 A																												
	SD-S344-20	Detailing (OFA) - Seq.344	20	17	Jul-10-2025 A	Aug-03-2025 A																												
	SD-S344-30	Approval (BFA) - Seq.344	10	13	Aug-04-2025 A	Aug-20-2025 A																												
	SD-S344-40	Scrub (FFAB) - Seq.344	10	10	Aug-21-2025 A	Sep-04-2025 A																												
	Seq.347		31	38	Jul-16-2025 A	Sep-09-2025 A																												
	SD-S347-10	Complete Design Information Milestone - Seq.347	0	0		Jul-16-2025 A																												
	SD-S347-20	Detailing (OFA) - Seq.347	20	19	Jul-17-2025 A	Aug-12-2025 A																												
	SD-S347-30	Approval (BFA) - Seq.347	10	8	Aug-13-2025 A	Aug-22-2025 A																												
	SD-S347-40	Scrub (FFAB) - Seq.347	10	11	Aug-25-2025 A	Sep-09-2025 A																												
	Seq.349		31	40	Jul-16-2025 A	Sep-11-2025 A																												
	SD-S349-10	Complete Design Information Milestone - Seq.349	0	0		Jul-16-2025 A																												
	SD-S349-20	Detailing (OFA) - Seq.349	20	17	Jul-17-2025 A	Aug-10-2025 A																												
	SD-S349-30	Approval (BFA) - Seq.349	10	12	Aug-11-2025 A	Aug-26-2025 A																												
	SD-S349-40	Scrub (FFAB) - Seq.349	10	11	Aug-27-2025 A	Sep-11-2025 A																												
	Seq.351		31	41	Jul-16-2025 A	Sep-12-2025 A																												
	SD-S351-10	Complete Design Information Milestone - Seq.351	0	0		Jul-16-2025 A																												
	SD-S351-20	Detailing (OFA) - Seq.351	20	17	Jul-17-2025 A	Aug-10-2025 A																												
	SD-S351-30	Approval (BFA) - Seq.351	10	12	Aug-11-2025 A	Aug-26-2025 A			</																									

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 14 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

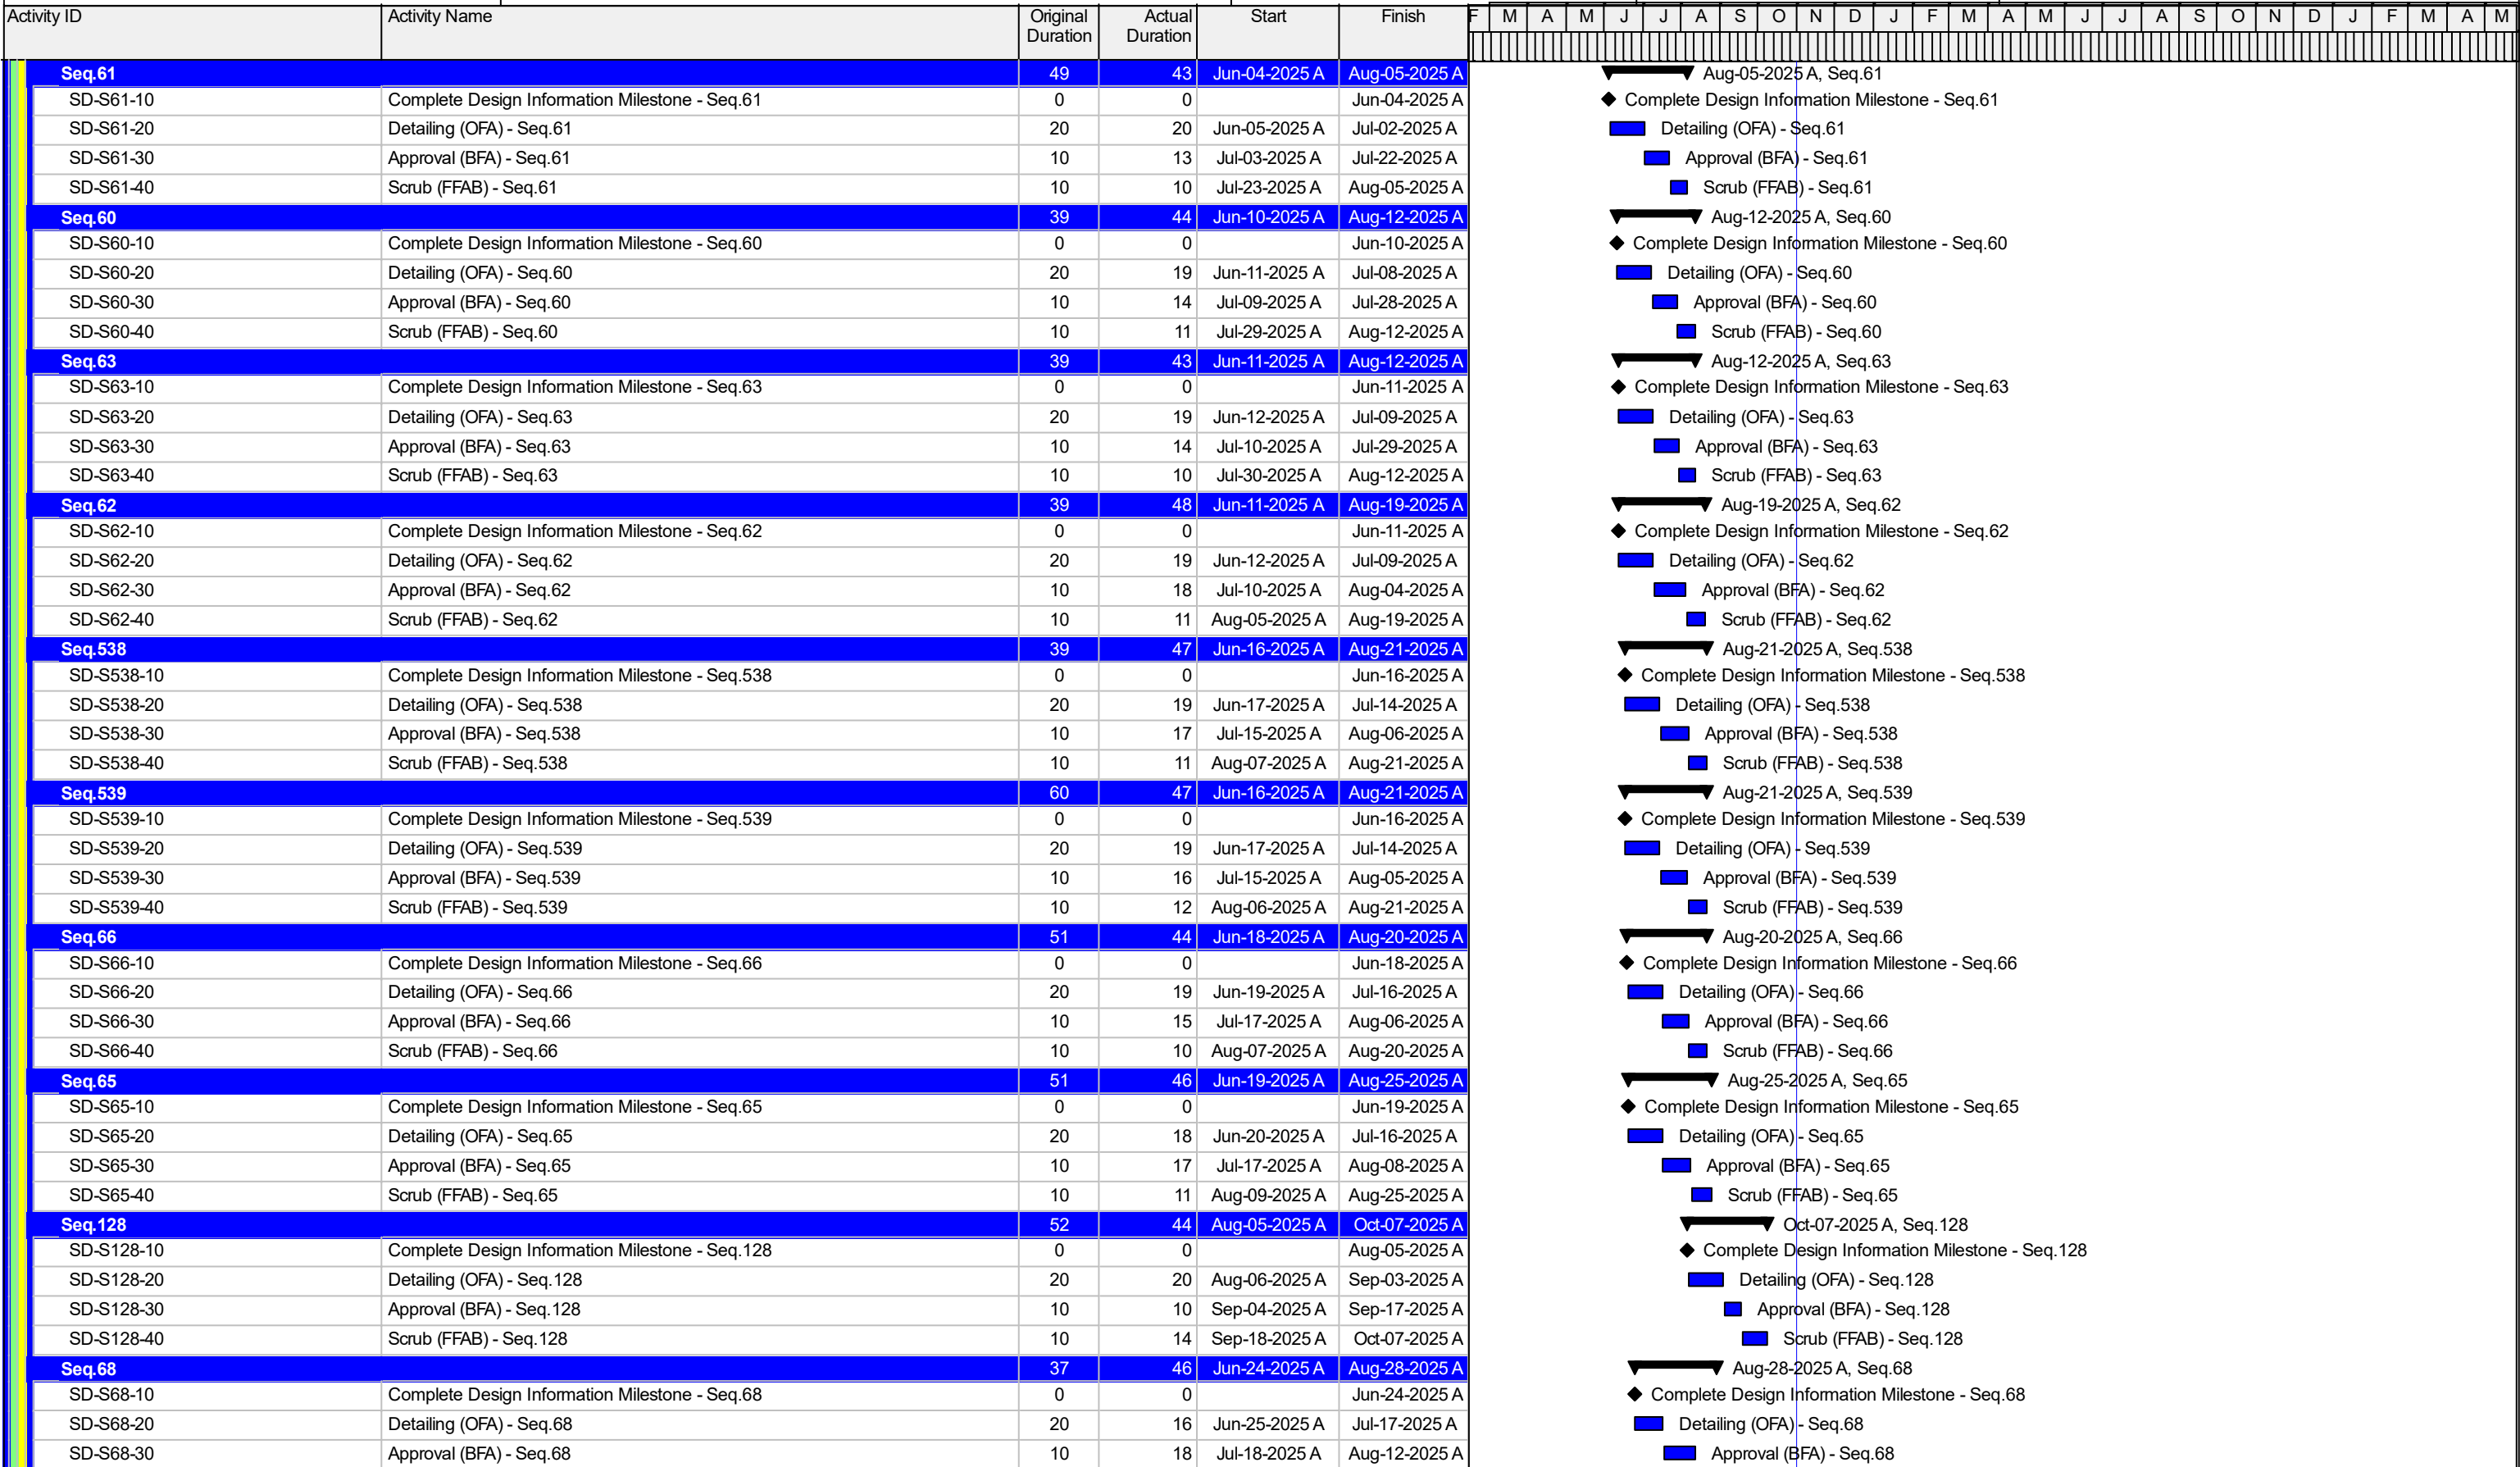

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 18 of 99
Data date : Oct-31-2025

Page 18 of 99

Data date : Oct-31-2025




INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 19 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

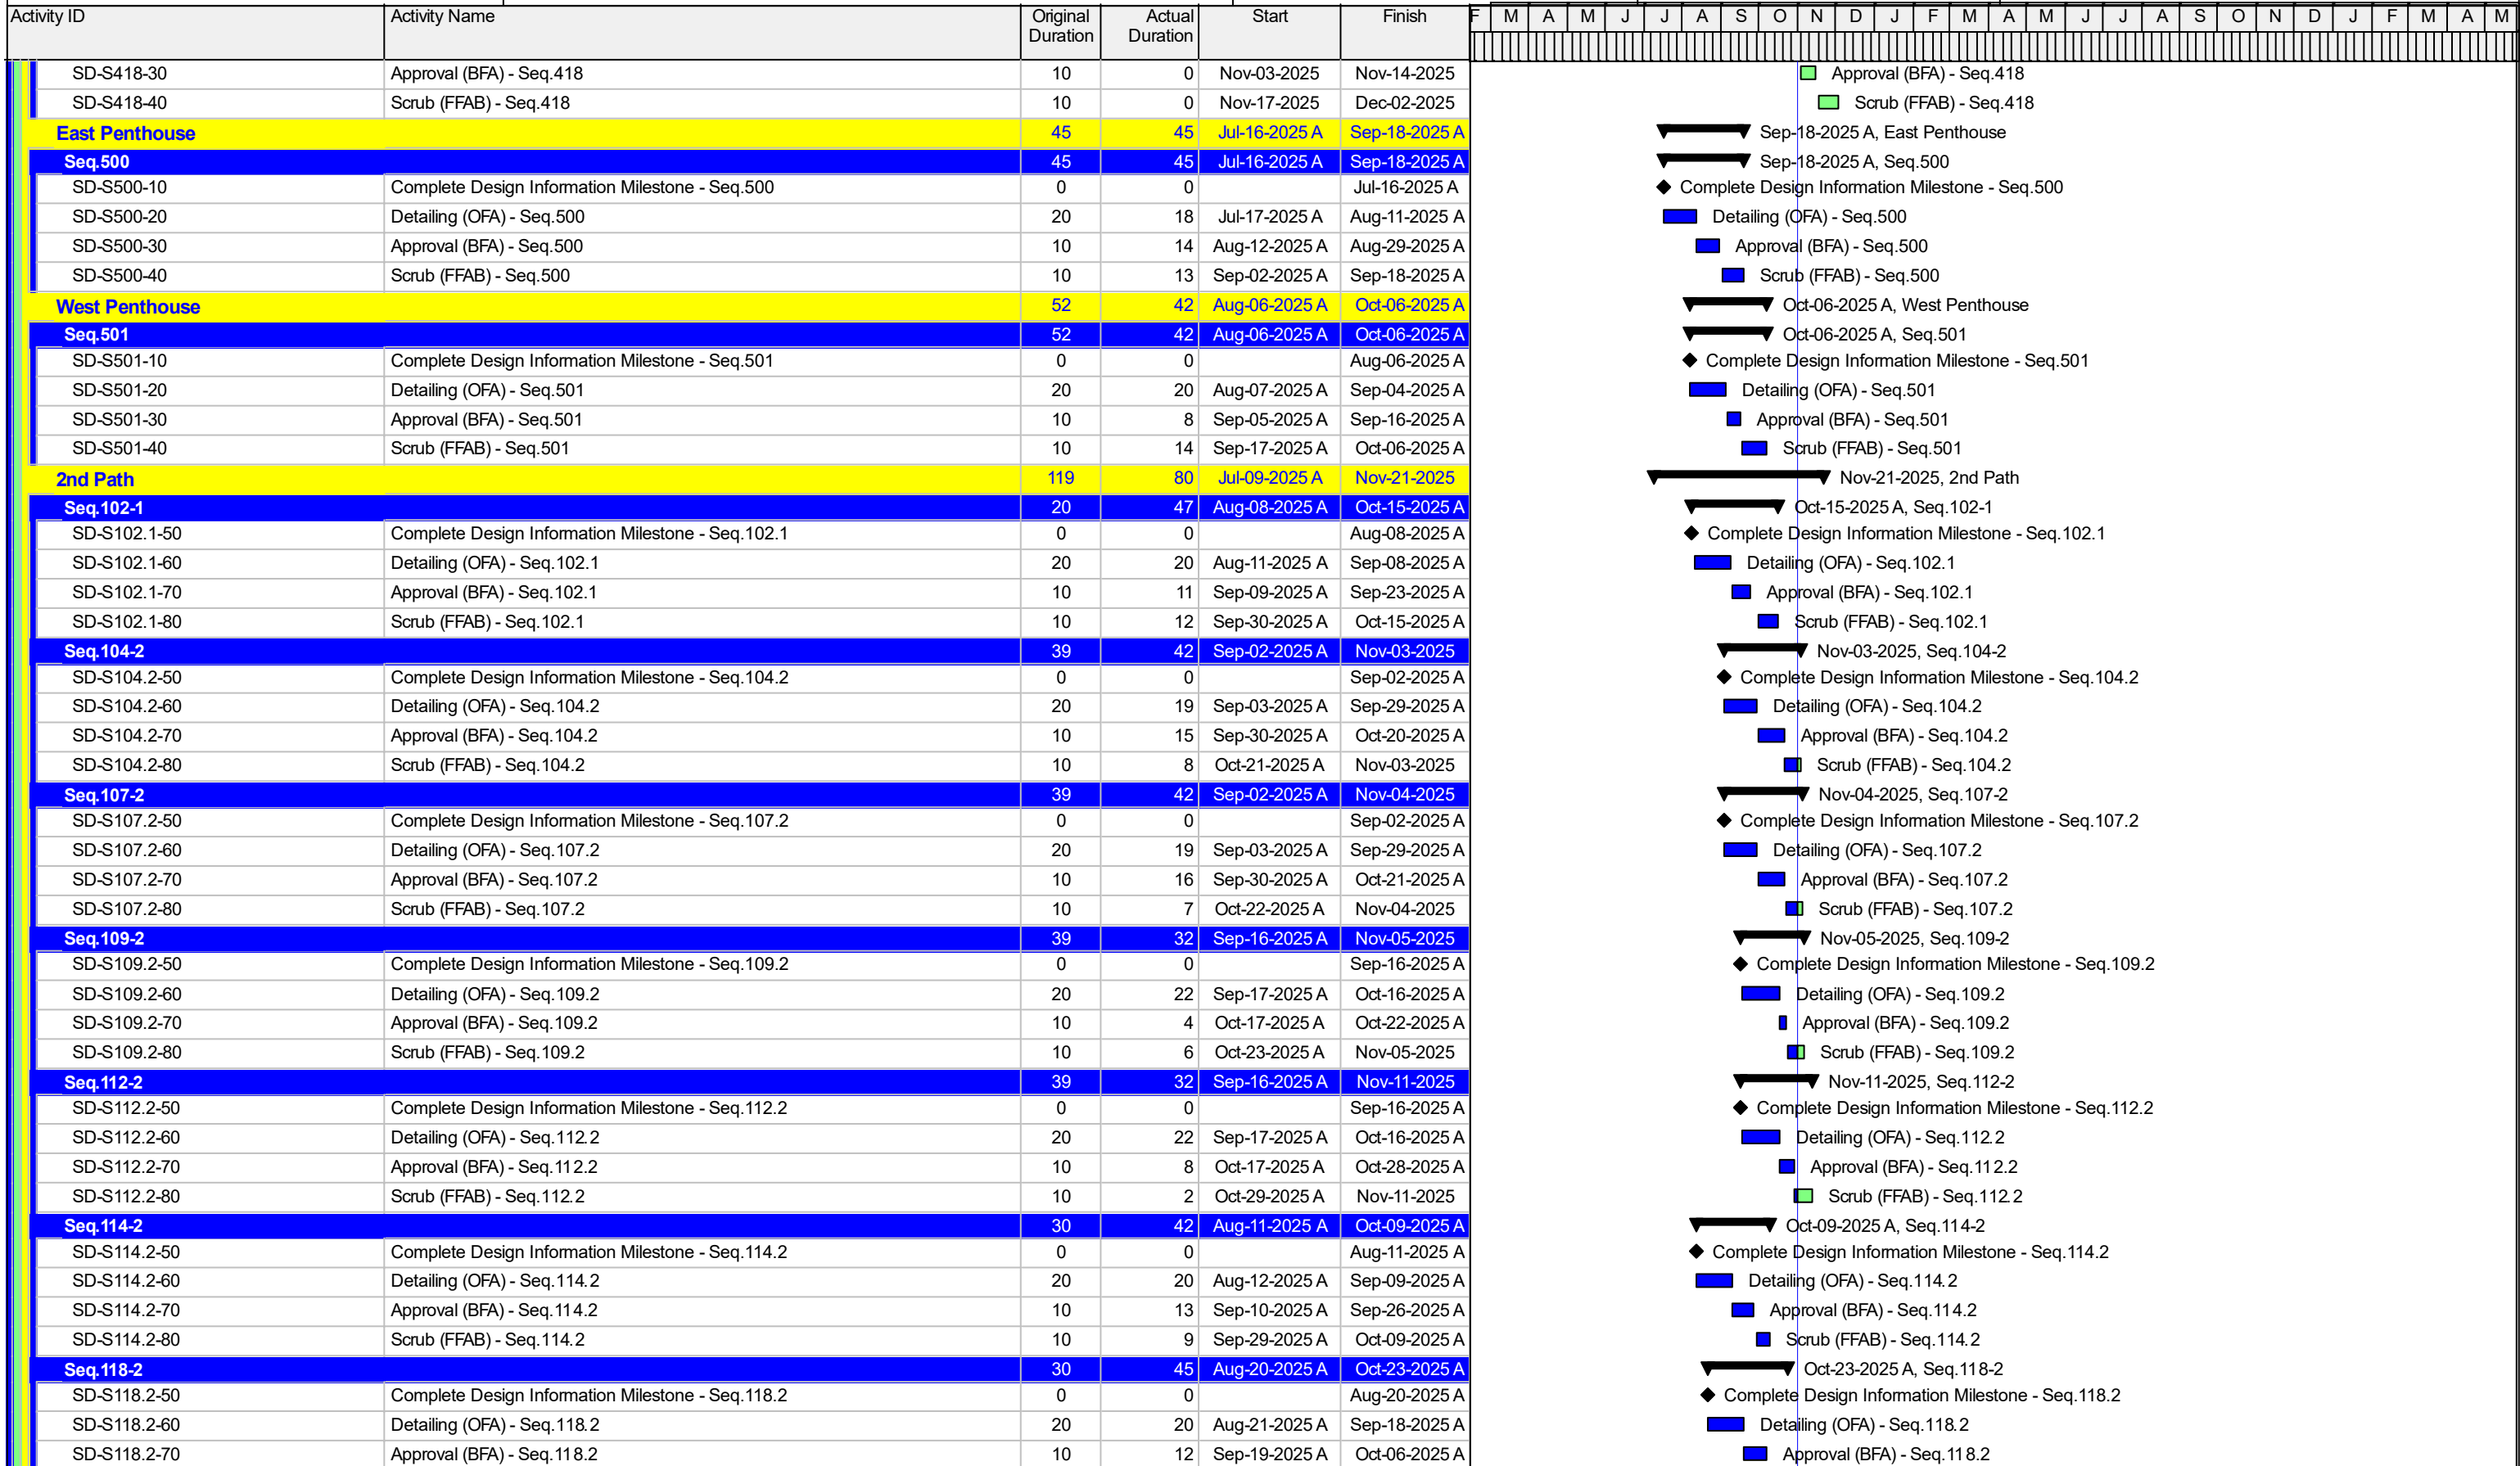

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 20 of 99
Data date : Oct-31-2025

Data date : Oct-31-2025

[illegible]

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 21 of 99
Data date : Oct-31-2025

Page 21 of 99

Data date : Oct-31-2025




INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 22 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

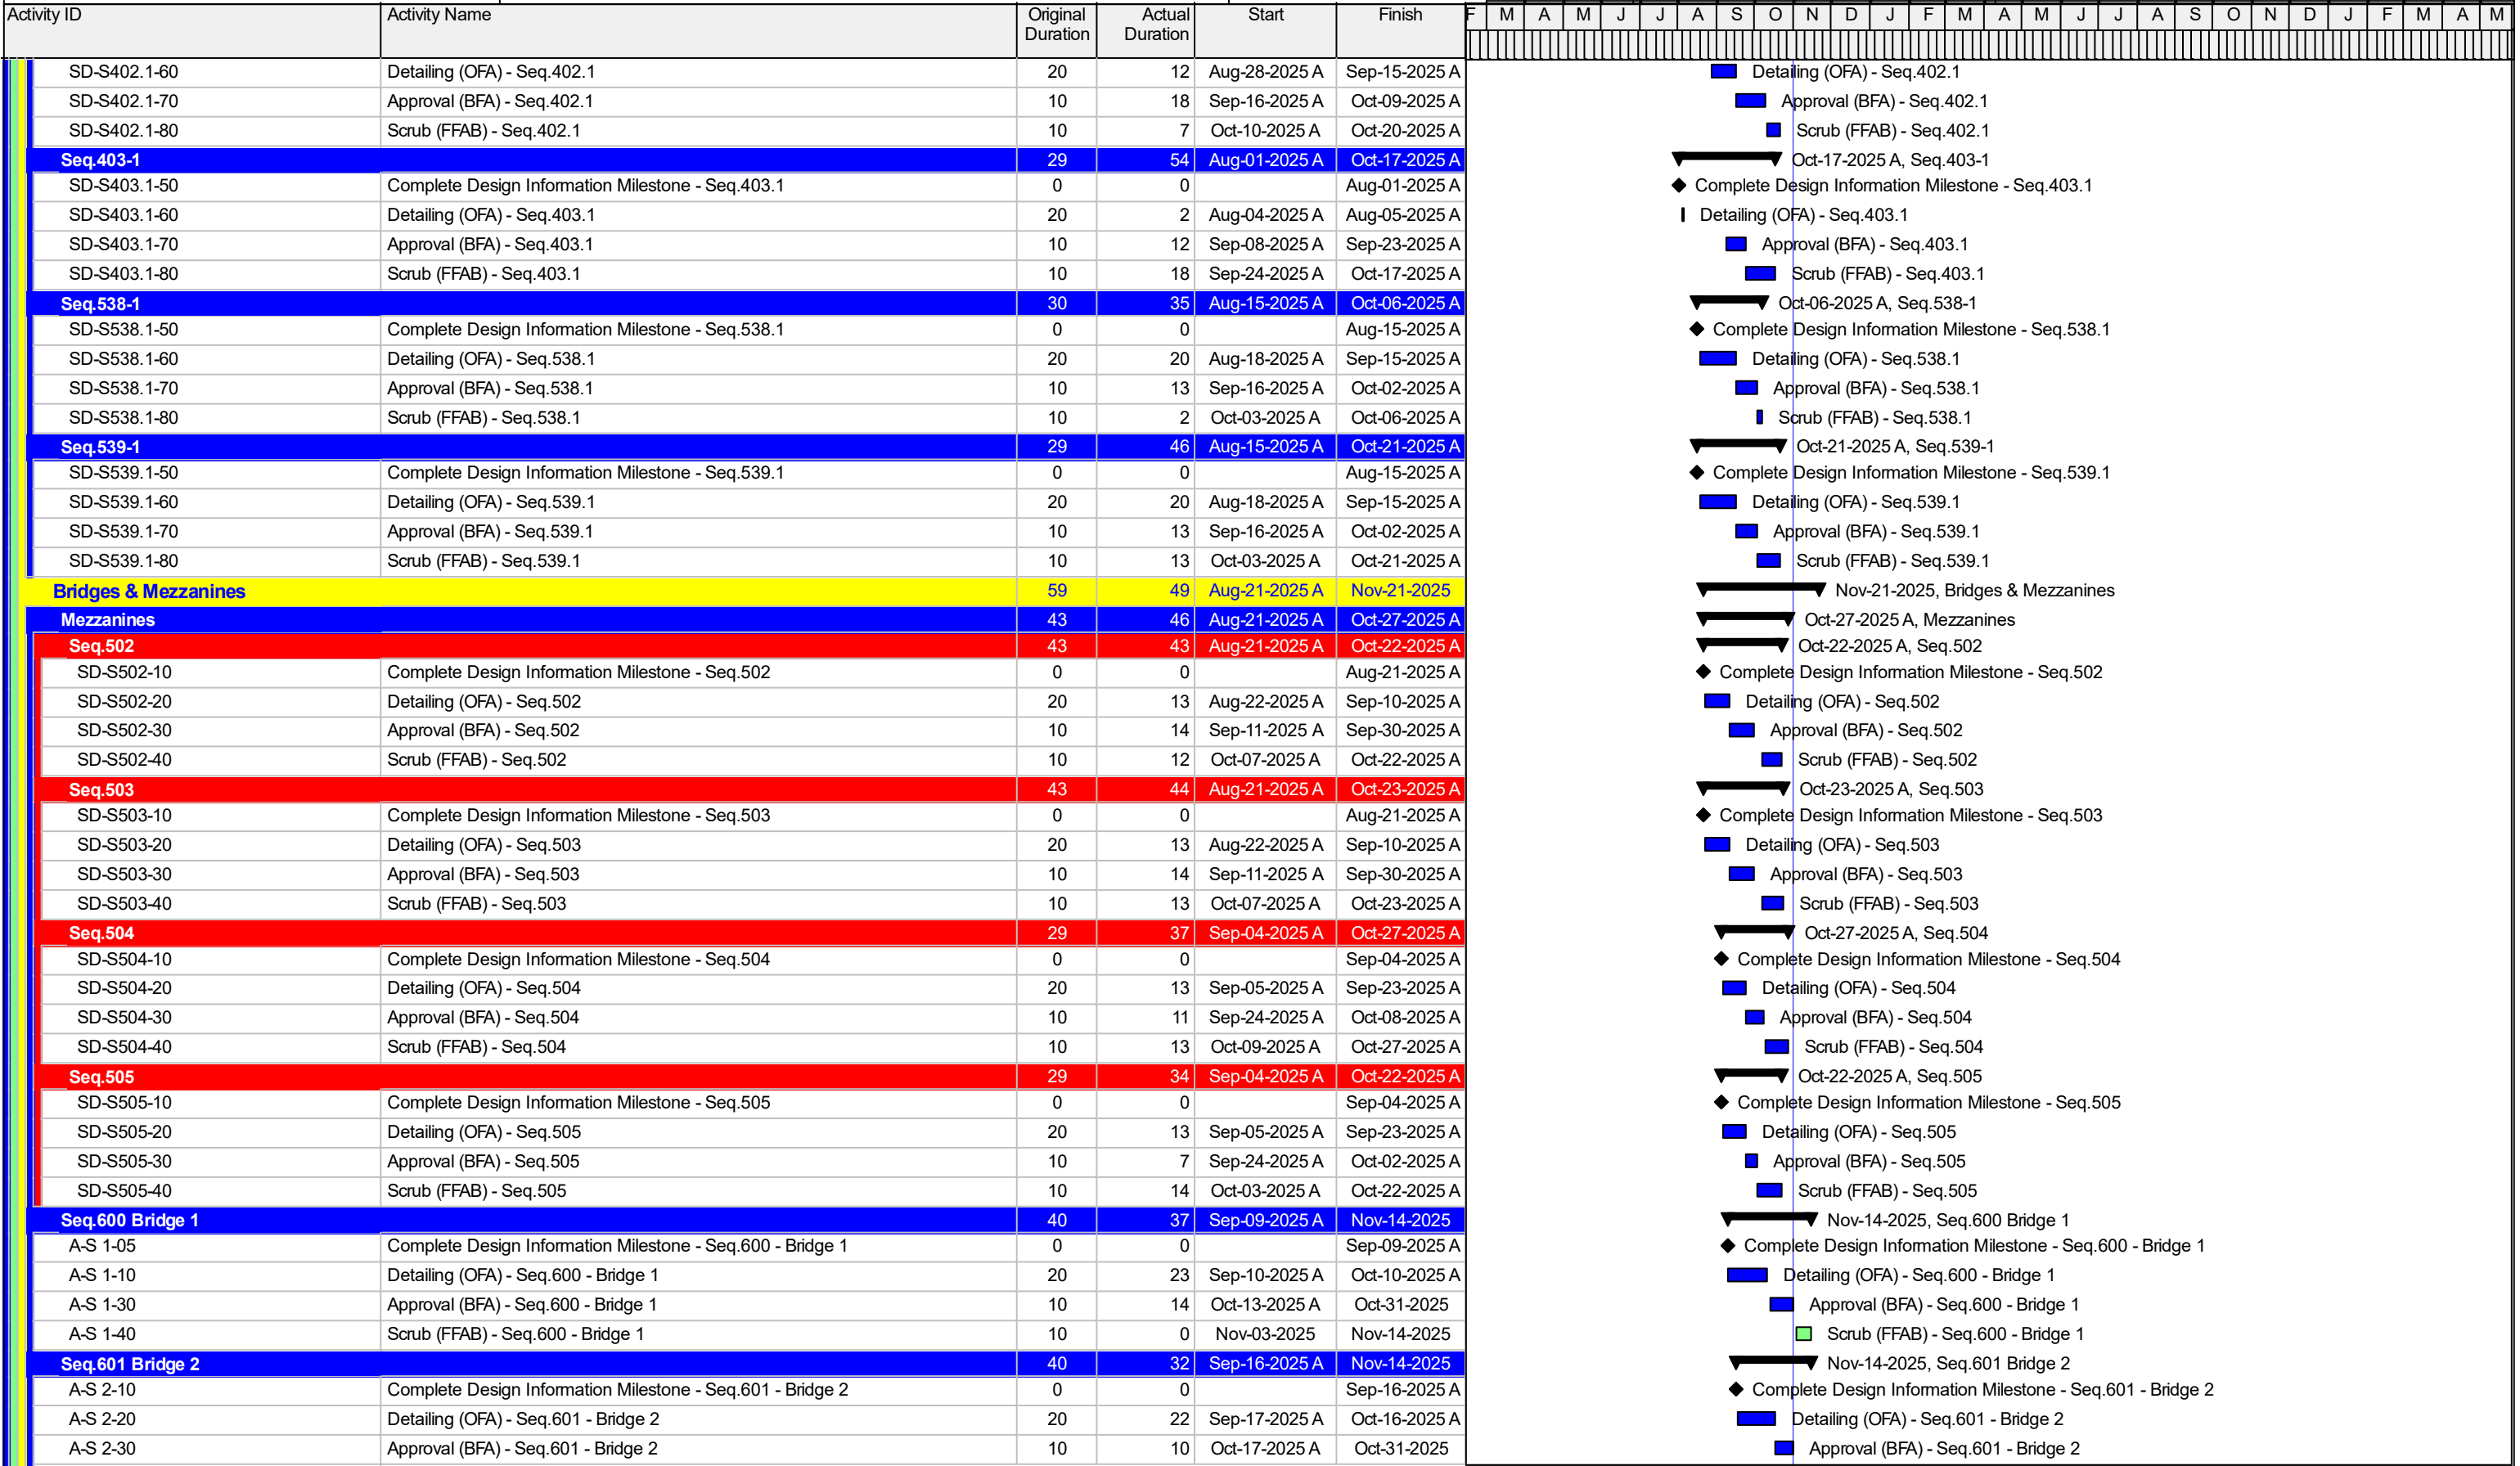

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 25 of 99
Data date : Oct-31-2025

Page 25 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 28 of 99
Data date : Oct-31-2025

Page 28 of 99

Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 29 of 99
Data date : Oct-31-2025

Page 29 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 30 of 99
Data date : Oct-31-2025

Page 30 of 99

Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

[illegible]

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 31 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



A DBM GLOBAL COMPANY

TSMC FAB3 Preliminary Schedule

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary



Activity ID	Activity Name	Original Duration	Actual Duration	Start	Finish	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M
Fab-1773	Delivery	5	0	Jan-15-2026	Jan-21-2026																												
Seq.402		101	48	Aug-25-2025 A	Jan-30-2026																												
Fab-0402	Fabrication Seq.402	76	48	Aug-25-2025 A	Jan-09-2026																												
Fab-1788	Prime Painting	10	0	Jan-12-2026	Jan-23-2026																												
Fab-1793	Delivery	5	0	Jan-26-2026	Jan-30-2026																												
Seq.403		82	43	Sep-01-2025 A	Jan-23-2026																												
Fab-0403	Fabrication Seq.403	82	43	Sep-01-2025 A	Dec-30-2025																												
Fab-1798	Prime Painting	10	0	Jan-05-2026	Jan-16-2026																												
Fab-1803	Delivery	5	0	Jan-19-2026	Jan-23-2026																												
Seq.404		98	43	Sep-01-2025 A	Feb-17-2026																												
Fab-0404	Fabrication Seq.404	84	43	Sep-01-2025 A	Jan-26-2026																												
Fab-1808	Prime Painting	10	0	Jan-27-2026	Feb-09-2026																												
Fab-1813	Delivery	5	0	Feb-10-2026	Feb-17-2026																												
Seq.405		90	39	Sep-08-2025 A	Feb-04-2026																												
Fab-0405	Fabrication Seq.405	87	39	Sep-08-2025 A	Jan-14-2026																												
Fab-1818	Prime Painting	10	0	Jan-15-2026	Jan-28-2026																												
Fab-1823	Delivery	5	0	Jan-29-2026	Feb-04-2026																												
Seq.406		104	38	Sep-09-2025 A	Feb-25-2026																												
Fab-0406	Fabrication Seq.406	88	38	Sep-09-2025 A	Feb-03-2026																												
Fab-1828	Prime Painting	10	0	Feb-04-2026	Feb-18-2026																												
Fab-1833	Delivery	5	0	Feb-19-2026	Feb-25-2026																												
Seq.407		80	30	Sep-19-2025 A	Feb-18-2026																												
Fab-0407	Fabrication Seq.407	80	30	Sep-19-2025 A	Jan-27-2026																												
Fab-1838	Prime Painting	10	0	Jan-28-2026	Feb-10-2026																												
Fab-1843	Delivery	5	0	Feb-11-2026	Feb-18-2026																												
Seq.408		95	26	Sep-25-2025 A	Mar-11-2026																												
Fab-0408	Fabrication Seq.408	82	26	Sep-25-2025 A	Feb-18-2026																												
Fab-1848	Prime Painting	10	0	Feb-19-2026	Mar-04-2026																												
Fab-1853	Delivery	5	0	Mar-05-2026	Mar-11-2026																												
Seq.409		77	14	Oct-11-2025 A	Feb-27-2026																												
Fab-0409	Fabrication Seq.409	67	14	Oct-11-2025 A	Feb-05-2026																												
Fab-1858	Prime Painting	10	0	Feb-06-2026	Feb-20-2026																												
Fab-1863	Delivery	5	0	Feb-23-2026	Feb-27-2026																												
Seq.410		91	11	Oct-16-2025 A	Mar-19-2026																												
Fab-0410	Fabrication Seq.410	71	11	Oct-16-2025 A	Feb-26-2026																												
Fab-1868	Prime Painting	10	0	Feb-27-2026	Mar-12-2026																												
Fab-1873	Delivery	5	0	Mar-13-2026	Mar-19-2026																												
Seq.411		86	19	Oct-04-2025 A	Mar-12-2026																												
Fab-0411	Fabrication Seq.411	74	19	Oct-04-2025 A	Feb-19-2026																												
Fab-1878	Prime Painting	10	0	Feb-20-2026	Mar-05-2026																												
Fab-1883	Delivery	5	0	Mar-06-2026	Mar-12-2026																												
Seq.412		101	7	Oct-22-2025 A	Apr-02-2026																												
Fab-0412	Fabrication Seq.412	75	7	Oct-22-2025 A	Mar-12-2026																												
Fab-1888	Prime Painting	10	0	Mar-13-2026	Mar-26-2026																												
Fab-1893	Delivery	5	0	Mar-27-2026	Apr-02-2026																												
Seq.413		92	0	Nov-03-2025	Mar-23-2026																												
Fab-0413	Fabrication Seq.413	77	0	Nov-03-2025	Mar-02-2026																												
Fab-1898	Prime Painting	10	0	Mar-03-2026	Mar-16-2026																												
Fab-1903	Delivery	5	0	Mar-17-2026	Mar-23-2026																												

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In forFabrication),and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the informationmilestone date is onlyused to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to theinformation milestone date will beevaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 34 of 99
Data date : Oct-31-2025

Page 34 of 99

Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.


S S SCHUFF STEEL A DBM GLOBAL COMPANY		TSMC FAB3 Preliminary Schedule				Page 35 of 99 Data date : Oct-31-2025		Actual Work Remaining Work Critical Remaining Work ◆ Milestone Summary		HSE PROJECT CONTROLS CONSULTANTS																							
Activity ID	Activity Name	Original Duration	Actual Duration	Start	Finish	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M
Fab-0043	Fabrication Seq.43	77	60	Jul-31-2025 A	Oct-23-2025 A																												
Fab-1688	Prime Painting	10	5	Oct-24-2025 A	Nov-11-2025																												
Fab-1693	Delivery	8	0	Nov-12-2025	Nov-21-2025																												
Seq.42		81	58	Aug-11-2025 A	Dec-12-2025																												
Fab-0042	Fabrication Seq.42	47	58	Aug-11-2025 A	Nov-19-2025																												
Fab-1698	Prime Painting	10	0	Nov-20-2025	Dec-05-2025																												
Fab-1703	Delivery	5	0	Dec-08-2025	Dec-12-2025																												
Seq.45		63	52	Aug-19-2025 A	Nov-21-2025																												
Fab-0045	Fabrication Seq.45	63	52	Aug-19-2025 A	Oct-30-2025 A																												
Fab-1708	Prime Painting	10	0	Oct-31-2025 A	Nov-10-2025																												
Fab-1713	Delivery	9	0	Nov-11-2025	Nov-21-2025																												
Seq.44		79	51	Aug-20-2025 A	Dec-23-2025																												
Fab-0044	Fabrication Seq.44	36	51	Aug-20-2025 A	Dec-02-2025																												
Fab-1718	Prime Painting	10	0	Dec-03-2025	Dec-16-2025																												
Fab-1723	Delivery	5	0	Dec-17-2025	Dec-23-2025																												
Seq.241		52	51	Aug-20-2025 A	Dec-01-2025																												
Fab-0241	Fabrication Seq.241	52	51	Aug-20-2025 A	Nov-06-2025																												
Fab-27923	Prime Painting	10	0	Nov-07-2025	Nov-20-2025																												
Fab-27933	Delivery	5	0	Nov-21-2025	Dec-01-2025																												
Seq.243		65	56	Aug-13-2025 A	Dec-03-2025																												
Fab-0243	Fabrication Seq.243	61	56	Aug-13-2025 A	Nov-10-2025																												
Fab-27493	Prime Painting	10	0	Nov-11-2025	Nov-24-2025																												
Fab-27503	Delivery	5	0	Nov-25-2025	Dec-03-2025																												
Seq.240		62	49	Aug-22-2025 A	Nov-26-2025																												
Fab-0240	Fabrication Seq.240	53	49	Aug-22-2025 A	Nov-05-2025																												
Fab-27513	Prime Painting	10	0	Nov-06-2025	Nov-19-2025																												
Fab-27523	Delivery	5	0	Nov-20-2025	Nov-26-2025																												
Seq.242		64	56	Aug-13-2025 A	Dec-02-2025																												
Fab-0242	Fabrication Seq.242	60	56	Aug-13-2025 A	Nov-07-2025																												
Fab-27453	Prime Painting	10	0	Nov-10-2025	Nov-21-2025																												
Fab-27463	Delivery	5	0	Nov-24-2025	Dec-02-2025																												
Seq.271		67	44	Aug-29-2025 A	Dec-05-2025																												
Fab-0271	Fabrication Seq.271	67	44	Aug-29-2025 A	Nov-12-2025																												

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 36 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

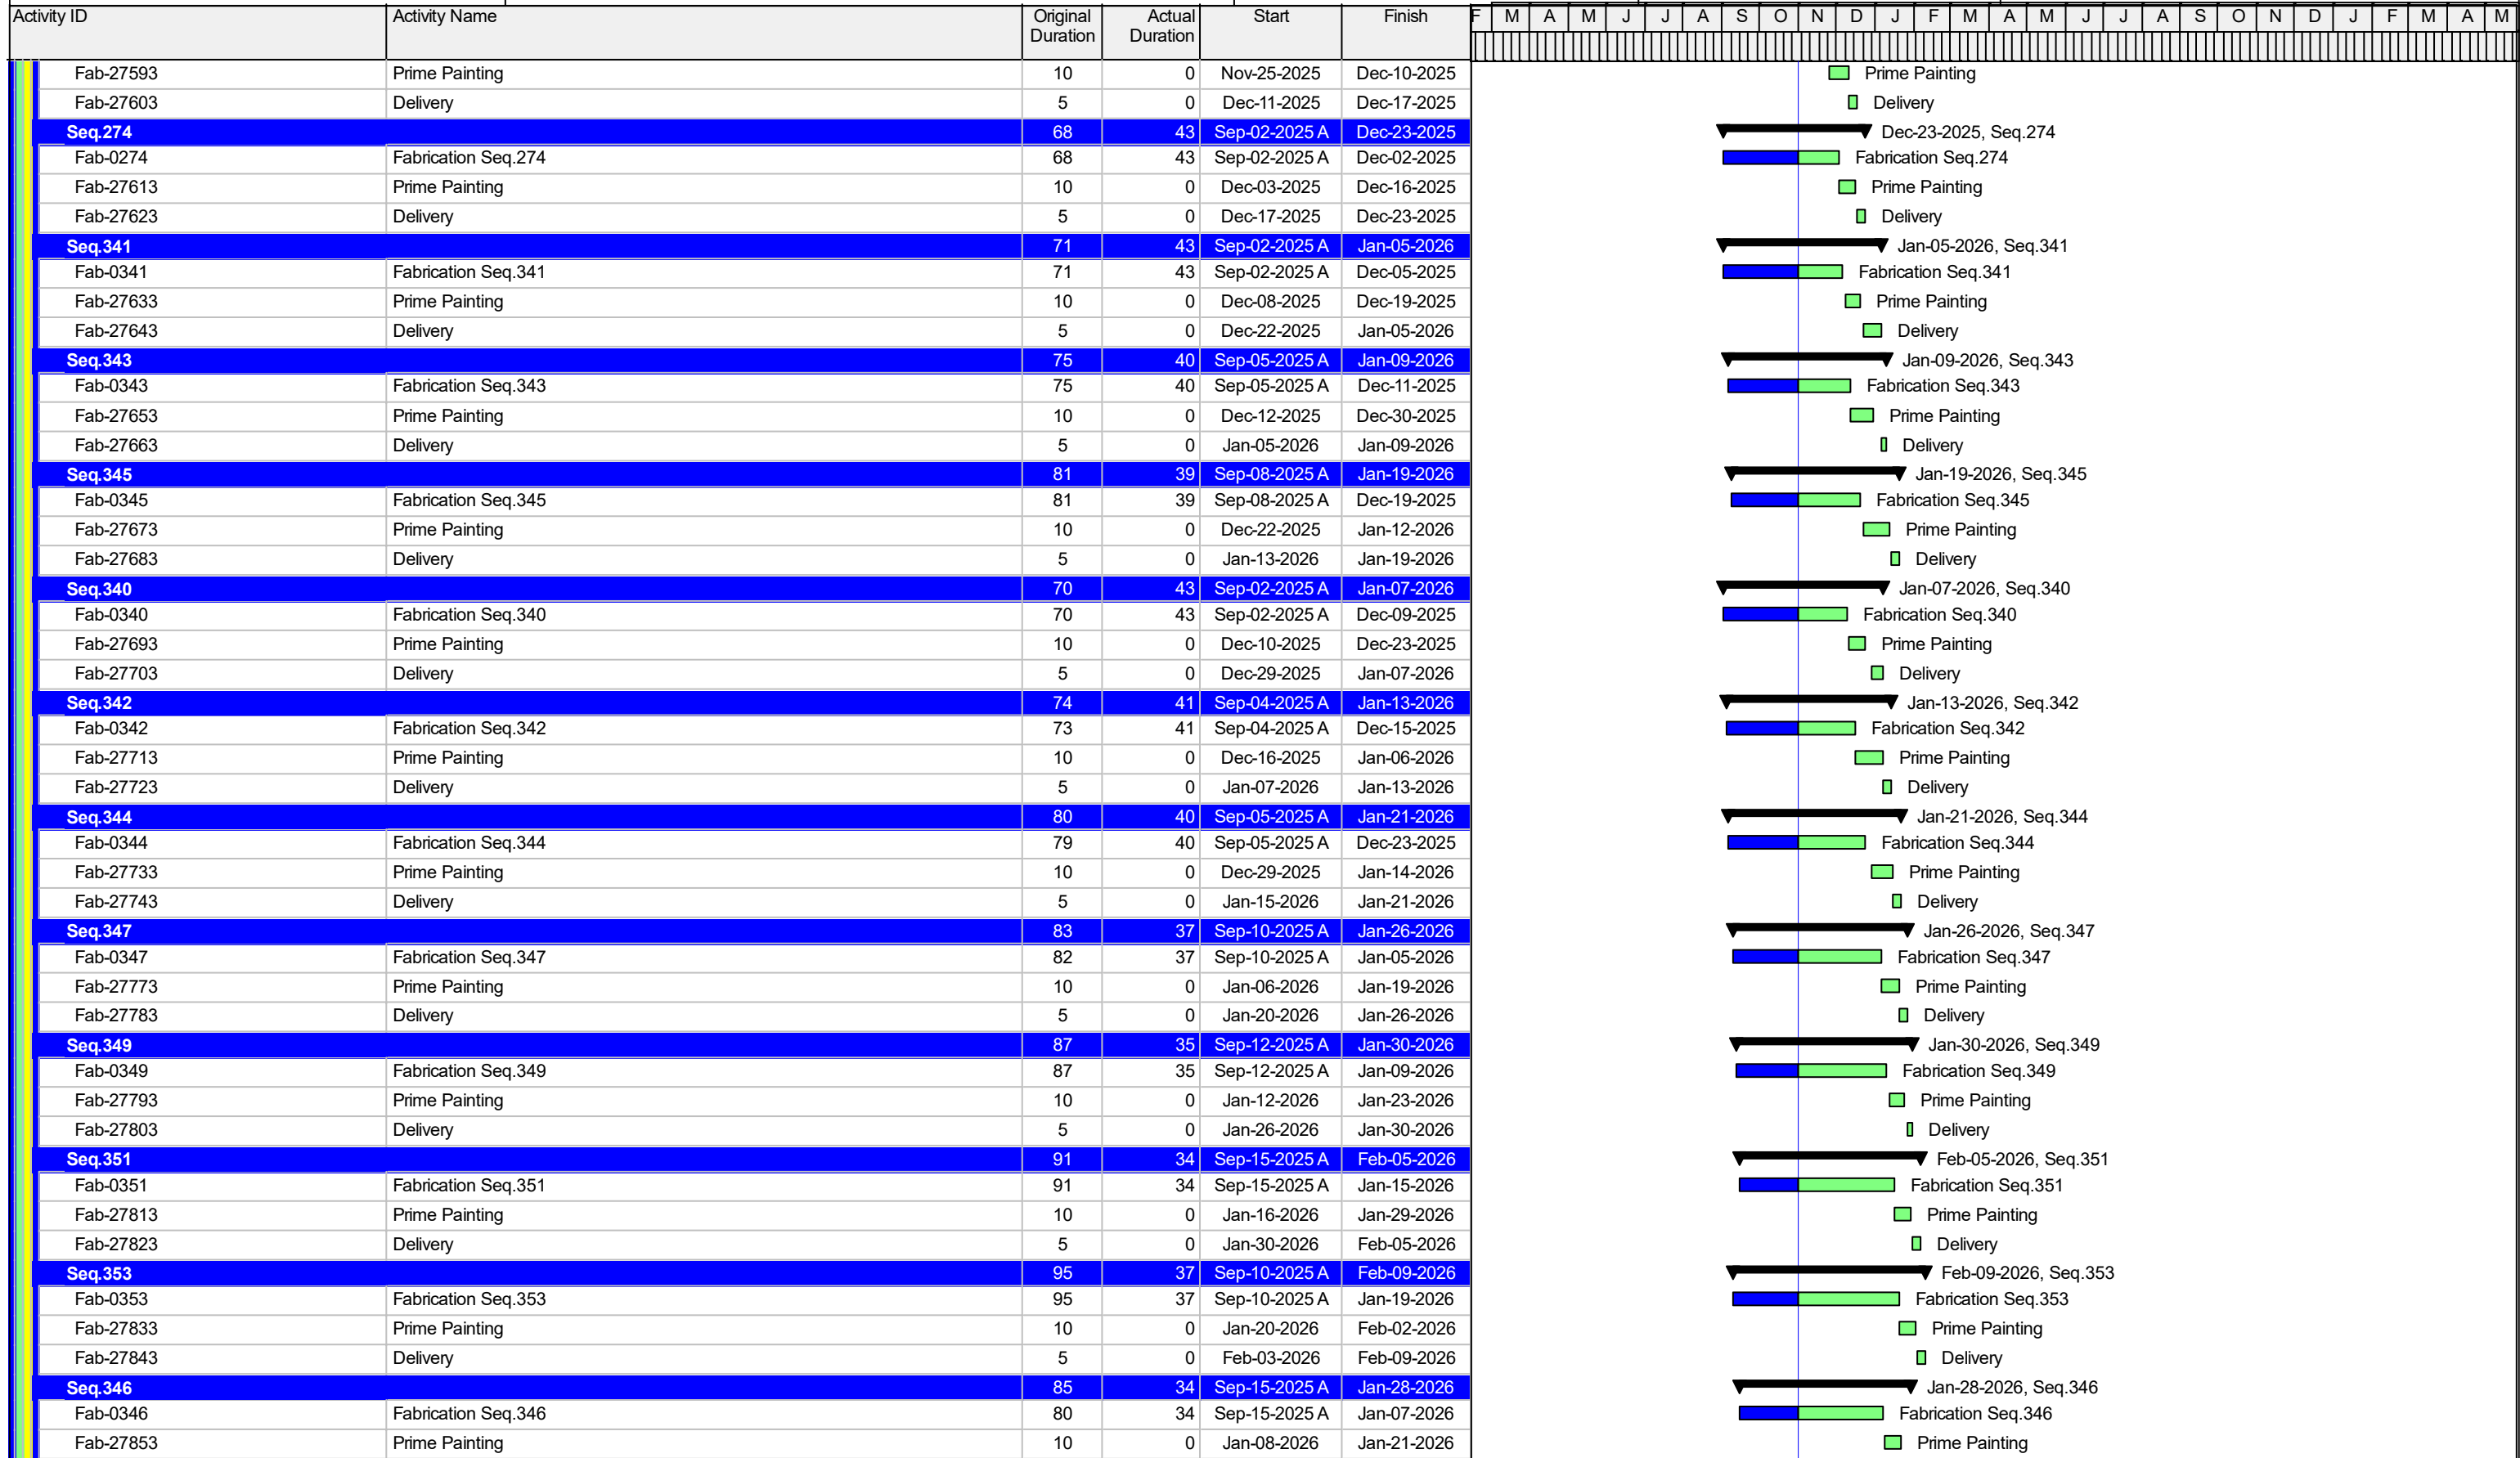

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.

S S SCHUFF STEEL A DBM GLOBAL COMPANY		TSMC FAB3 Preliminary Schedule				Page 37 of 99 Data date : Oct-31-2025		Actual Work Remaining Work Critical Remaining Work Milestone Summary		HSE PROJECT CONTROLS CONSULTANTS																							
Activity ID	Activity Name	Original Duration	Actual Duration	Start	Finish	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M
	Fab-27863	5	0	Jan-22-2026	Jan-28-2026																												
	Seq.348	89	36	Sep-11-2025 A	Feb-03-2026																												
	Fab-0348	84	36	Sep-11-2025 A	Jan-13-2026																												
	Fab-27873	10	0	Jan-14-2026	Jan-27-2026																												
	Fab-27883	5	0	Jan-28-2026	Feb-03-2026																												
	Seq.350	93	37	Sep-10-2025 A	Feb-09-2026																												
	Fab-0350	88	37	Sep-10-2025 A	Jan-19-2026																												
	Fab-27943	10	0	Jan-20-2026	Feb-02-2026																												
	Fab-27953	5	0	Feb-03-2026	Feb-09-2026																												
	Seq.352	99	36	Sep-11-2025 A	Feb-18-2026																												
	Fab-0352	94	36	Sep-11-2025 A	Jan-27-2026																												
	Fab-27963	10	0	Jan-28-2026	Feb-10-2026																												
	Fab-27973	5	0	Feb-11-2026	Feb-18-2026																												
	Fabrication and Delivery West Fab	203	82	Jul-08-2025 A	May-01-2026																												
	Seq.119	82	55	Aug-14-2025 A	Jan-05-2026																												
	Fab-0119	66	55	Aug-14-2025 A	Dec-05-2025																												
	Fab-2503	10	0	Dec-08-2025	Dec-19-2025																												
	Fab-2513	5	0	Dec-22-2025	Jan-05-2026																												
	Seq.53	92	82	Jul-08-2025 A	Nov-19-2025																												
	Fab-0053	79	81	Jul-08-2025 A	Oct-29-2025 A																												
	Fab-1988	8	1	Oct-30-2025 A	Nov-12-2025																												
	Fab-1993	5	0	Nov-13-2025	Nov-19-2025																												
	Seq.51	78	82	Jul-08-2025 A	Nov-19-2025																												
	Fab-0051	76	81	Jul-08-2025 A	Oct-29-2025 A																												
	Fab-1968	10	1	Oct-30-2025 A	Nov-12-2025																												
	Fab-1973	5	0	Nov-13-2025	Nov-19-2025																												
	Seq.50	91	76	Jul-16-2025 A	Jan-16-2026																												
	Fab-0050	76	76	Jul-16-2025 A	Dec-18-2025																												
	Fab-1958	10	0	Dec-19-2025	Jan-09-2026																												
	Fab-1963	5	0	Jan-12-2026	Jan-16-2026																												
	Seq.52	94	74	Jul-18-2025 A	Jan-21-2026																												
	Fab-0052	79	74	Jul-18-2025 A	Dec-23-2025																												
	Fab-1978	10	0	Dec-29-2025	Jan-14-2026																												
	Fab-1983	5	0	Jan-15-2026	Jan-21-2026																												
	Seq.56	73	66	Jul-30-2025 A	Dec-02-2025																												
	Fab-0056	69	66	Jul-30-2025 A	Nov-07-2025																												
	Fab-2018	10	0	Nov-10-2025	Nov-21-2025																												
	Fab-2023	5	0	Nov-24-2025	Dec-02-2025																												
	Seq.55	99	71	Jul-23-2025 A	Jan-28-2026																												
	Fab-0055	84	71	Jul-23-2025 A	Jan-07-2026																												
	Fab-2008	10	0	Jan-08-2026	Jan-21-2026																												
	Fab-2013	5	0	Jan-22-2026	Jan-28-2026																												
	Seq.123	82	43	Sep-02-2025 A	Jan-23-2026																												
	Fab-0123	80	43	Sep-02-2025 A	Dec-30-2025																												
	Fab-2623	10	0	Jan-05-2026	Jan-16-2026																												
	Fab-2633	5	0	Jan-19-2026	Jan-23-2026																												
	Seq.59	105	63	Aug-04-2025 A	Jan-23-2026																												
	Fab-0059	74	63	Aug-04-2025 A	Dec-30-2025																												
	Fab-2048	10	0	Jan-05-2026	Jan-16-2026																												

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In forFabrication),and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the informationmilestone date is onlused to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to theinformation milestone date will beevaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



A DBM GLOBAL COMPANY

TSMC FAB3 Preliminary Schedule

Page 38 of 99
Data date : Oct-31-2025

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary




Activity ID	Activity Name	Original Duration	Actual Duration	Start	Finish	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M
Fab-2053	Delivery	5	0	Jan-19-2026	Jan-23-2026																												
Seq.58		115	62	Aug-05-2025 A	Feb-06-2026																												
Fab-0058	Fabrication Seq.58	110	62	Aug-05-2025 A	Jan-16-2026																												
Fab-2038	Prime Painting	10	0	Jan-19-2026	Jan-30-2026																												
Fab-2043	Delivery	5	0	Feb-02-2026	Feb-06-2026																												
Seq.61		108	61	Aug-06-2025 A	Jan-28-2026																												
Fab-0061	Fabrication Seq.61	77	61	Aug-06-2025 A	Jan-07-2026																												
Fab-2078	Prime Painting	10	0	Jan-08-2026	Jan-21-2026																												
Fab-2083	Delivery	5	0	Jan-22-2026	Jan-28-2026																												
Seq.60		118	56	Aug-13-2025 A	Feb-12-2026																												
Fab-0060	Fabrication Seq.60	109	56	Aug-13-2025 A	Jan-22-2026																												
Fab-2058	Prime Painting	10	0	Jan-23-2026	Feb-05-2026																												
Fab-2063	Delivery	5	0	Feb-06-2026	Feb-12-2026																												
Seq.63		103	53	Aug-18-2025 A	Feb-03-2026																												
Fab-0063	Fabrication Seq.63	63	53	Aug-18-2025 A	Jan-13-2026																												
Fab-2088	Prime Painting	10	0	Jan-14-2026	Jan-27-2026																												
Fab-2093	Delivery	5	0	Jan-28-2026	Feb-03-2026																												
Seq.62		113	51	Aug-20-2025 A	Feb-18-2026																												
Fab-0062	Fabrication Seq.62	98	51	Aug-20-2025 A	Jan-27-2026																												
Fab-2068	Prime Painting	10	0	Jan-28-2026	Feb-10-2026																												
Fab-2073	Delivery	5	0	Feb-11-2026	Feb-18-2026																												
Seq.538		87	49	Aug-22-2025 A	Jan-12-2026																												
Fab-0538	Fabrication Seq.538	70	49	Aug-22-2025 A	Dec-12-2025																												
Fab-27193	Prime Painting	10	0	Dec-15-2025	Jan-05-2026																												
Fab-27203	Delivery	5	0	Jan-06-2026	Jan-12-2026																												
Seq.539		75	48	Aug-25-2025 A	Jan-14-2026																												
Fab-0539	Fabrication Seq.539	74	48	Aug-25-2025 A	Dec-16-2025																												
Fab-27213	Prime Painting	10	0	Dec-17-2025	Jan-07-2026																												
Fab-27223	Delivery	5	0	Jan-08-2026	Jan-14-2026																												
Seq.66		107	50	Aug-21-2025 A	Feb-09-2026																												
Fab-0066	Fabrication Seq.66	63	50	Aug-21-2025 A	Jan-19-2026																												
Fab-2118	Prime Painting	10	0	Jan-20-2026	Feb-02-2026																												
Fab-2123	Delivery	5	0	Feb-03-2026	Feb-09-2026																												
Seq.65		117	47	Aug-26-2025 A	Feb-24-2026																												
Fab-0065	Fabrication Seq.65	98	47	Aug-26-2025 A	Feb-02-2026																												
Fab-2108	Prime Painting	10	0	Feb-03-2026	Feb-17-2026																												
Fab-2113	Delivery	5	0	Feb-18-2026	Feb-24-2026																												
Seq.128		81	17	Oct-08-2025 A	Feb-19-2026																												
Fab-0128	Fabrication Seq.128	74	17	Oct-08-2025 A	Jan-28-2026																												
Fab-2773	Prime Painting	10	0	Jan-29-2026	Feb-11-2026																												
Fab-2783	Delivery	5	0	Feb-12-2026	Feb-19-2026																												
Seq.68		98	44	Aug-29-2025 A	Feb-17-2026																												
Fab-0068	Fabrication Seq.68	70	44	Aug-29-2025 A	Jan-26-2026																												
Fab-2138	Prime Painting	10	0	Jan-27-2026	Feb-09-2026																												
Fab-2143	Delivery	5	0	Feb-10-2026	Feb-17-2026																												
Seq.67		109	44	Aug-29-2025 A	Mar-04-2026																												
Fab-0067	Fabrication Seq.67	107	44	Aug-29-2025 A	Feb-10-2026																												
Fab-2128	Prime Painting	10	0	Feb-11-2026	Feb-25-2026																												
Fab-2133	Delivery	5	0	Feb-26-2026	Mar-04-2026																												

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 39 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

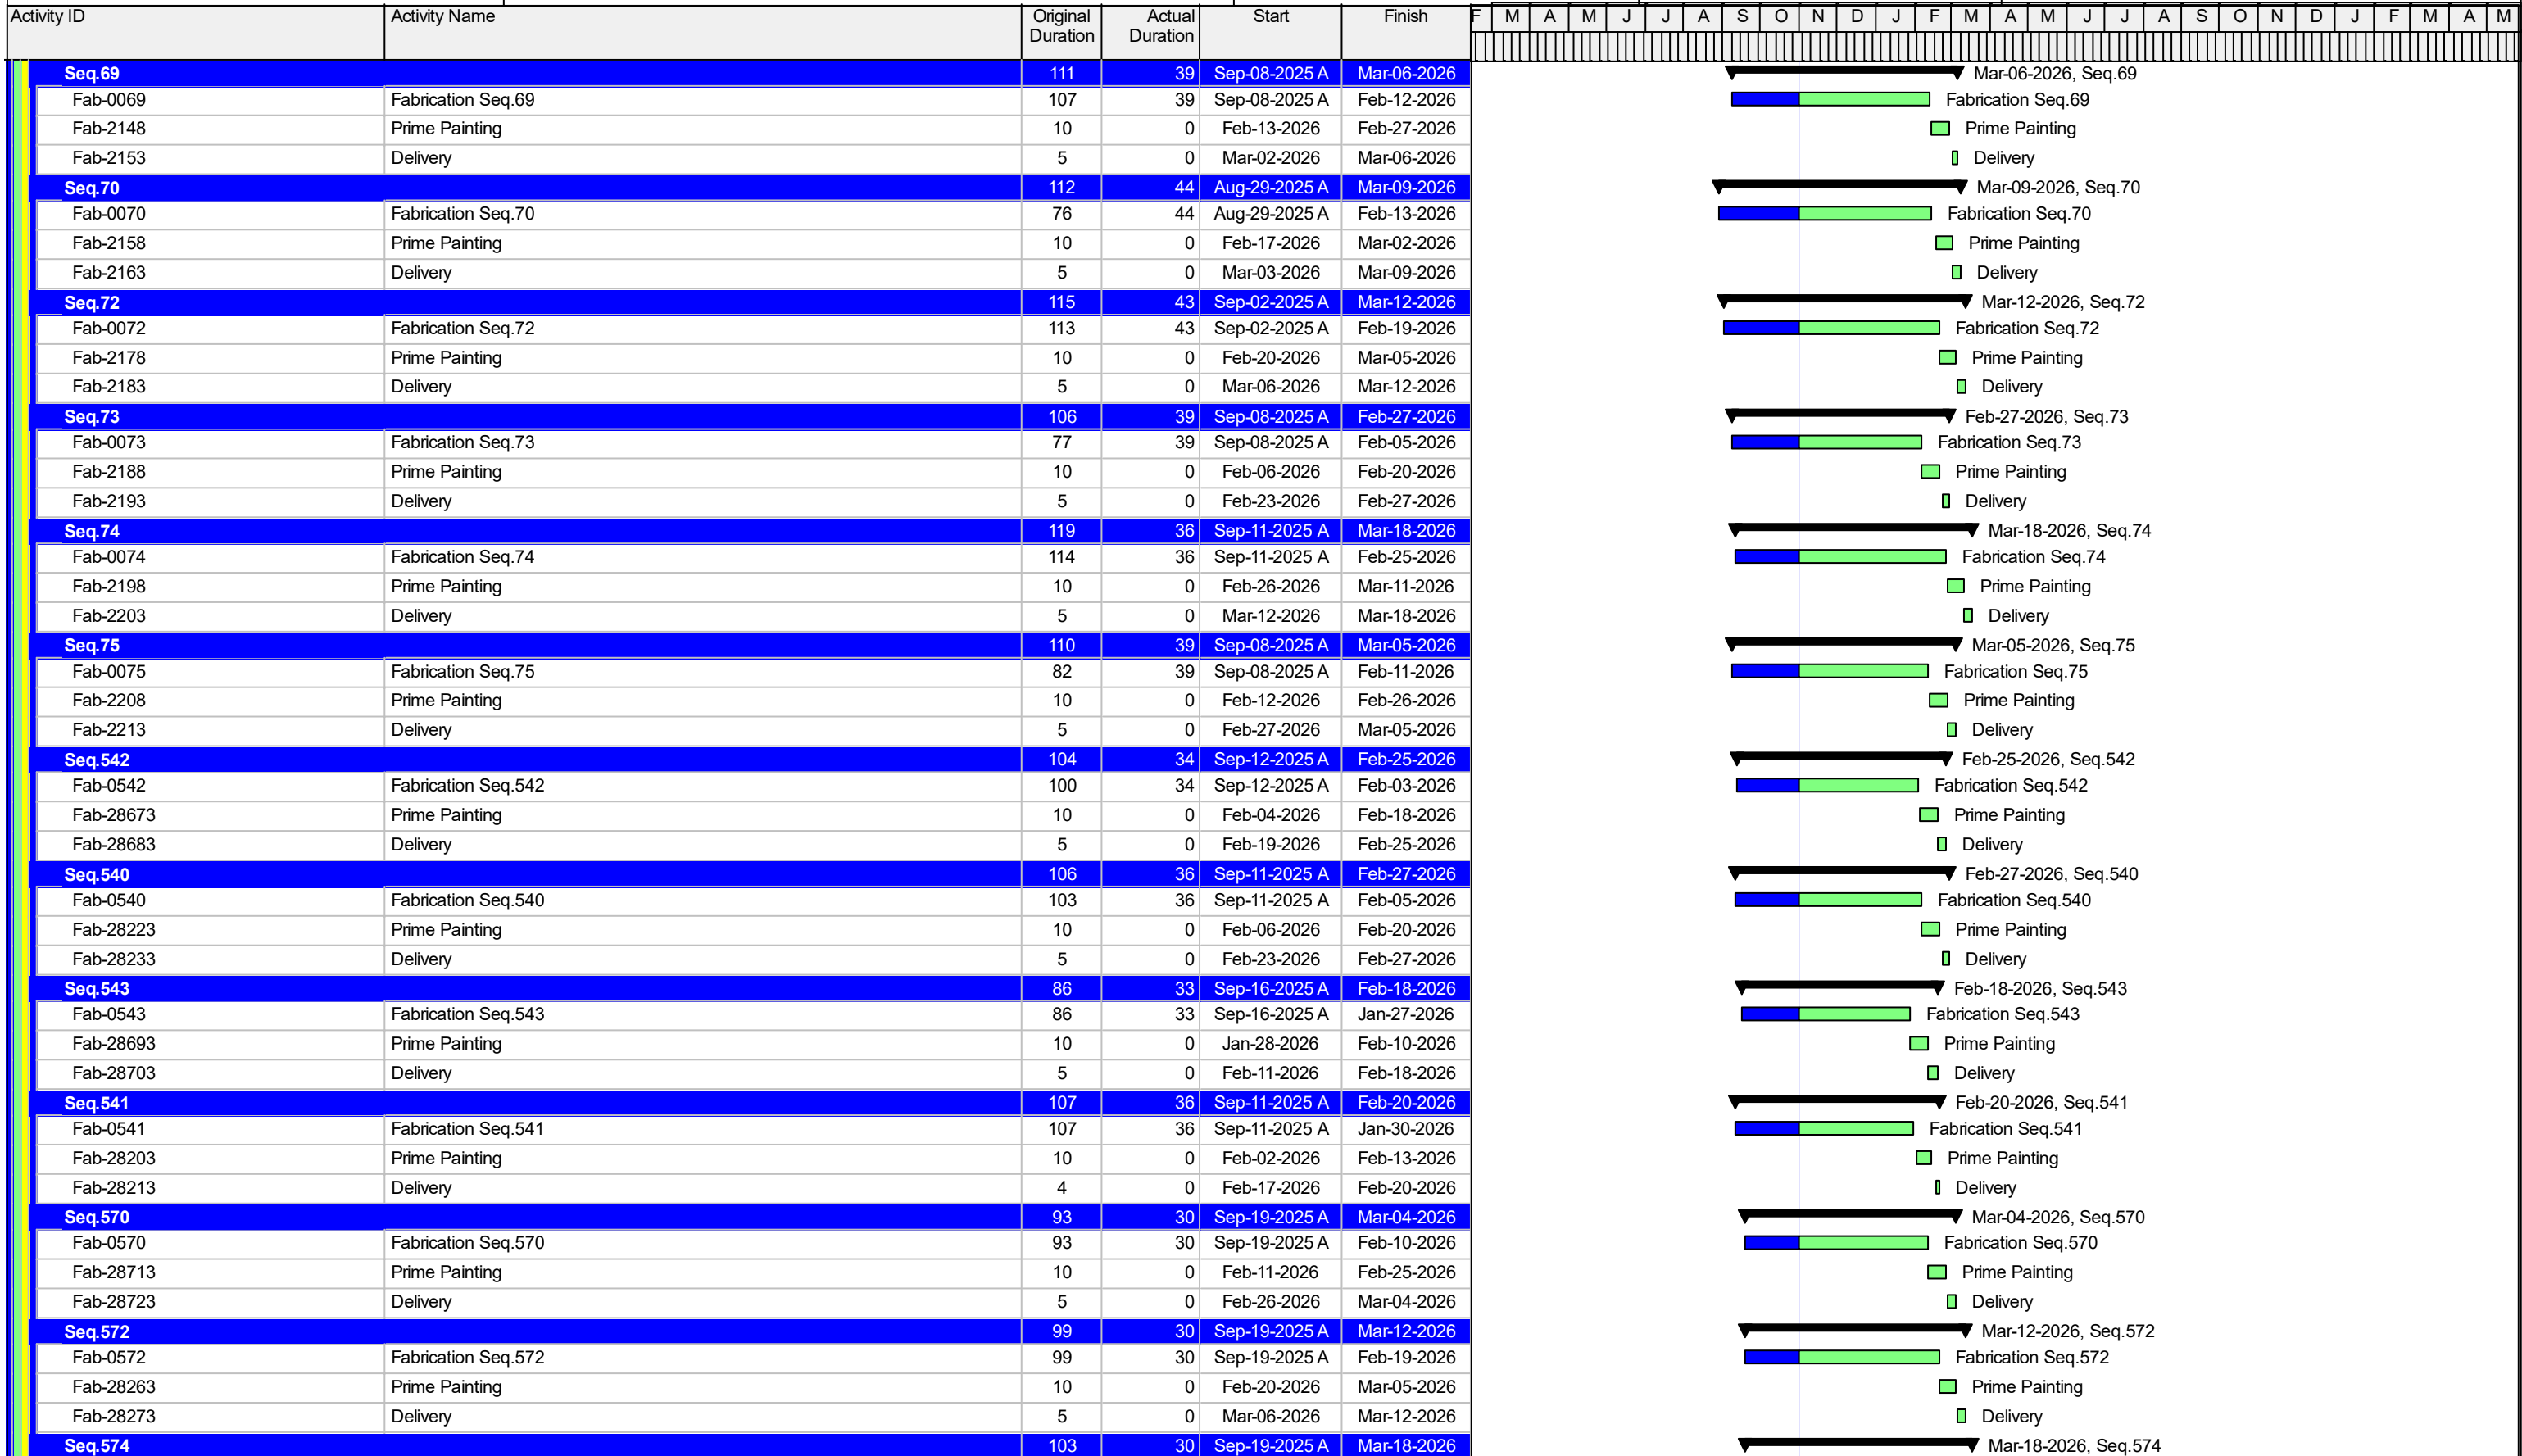


INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 40 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

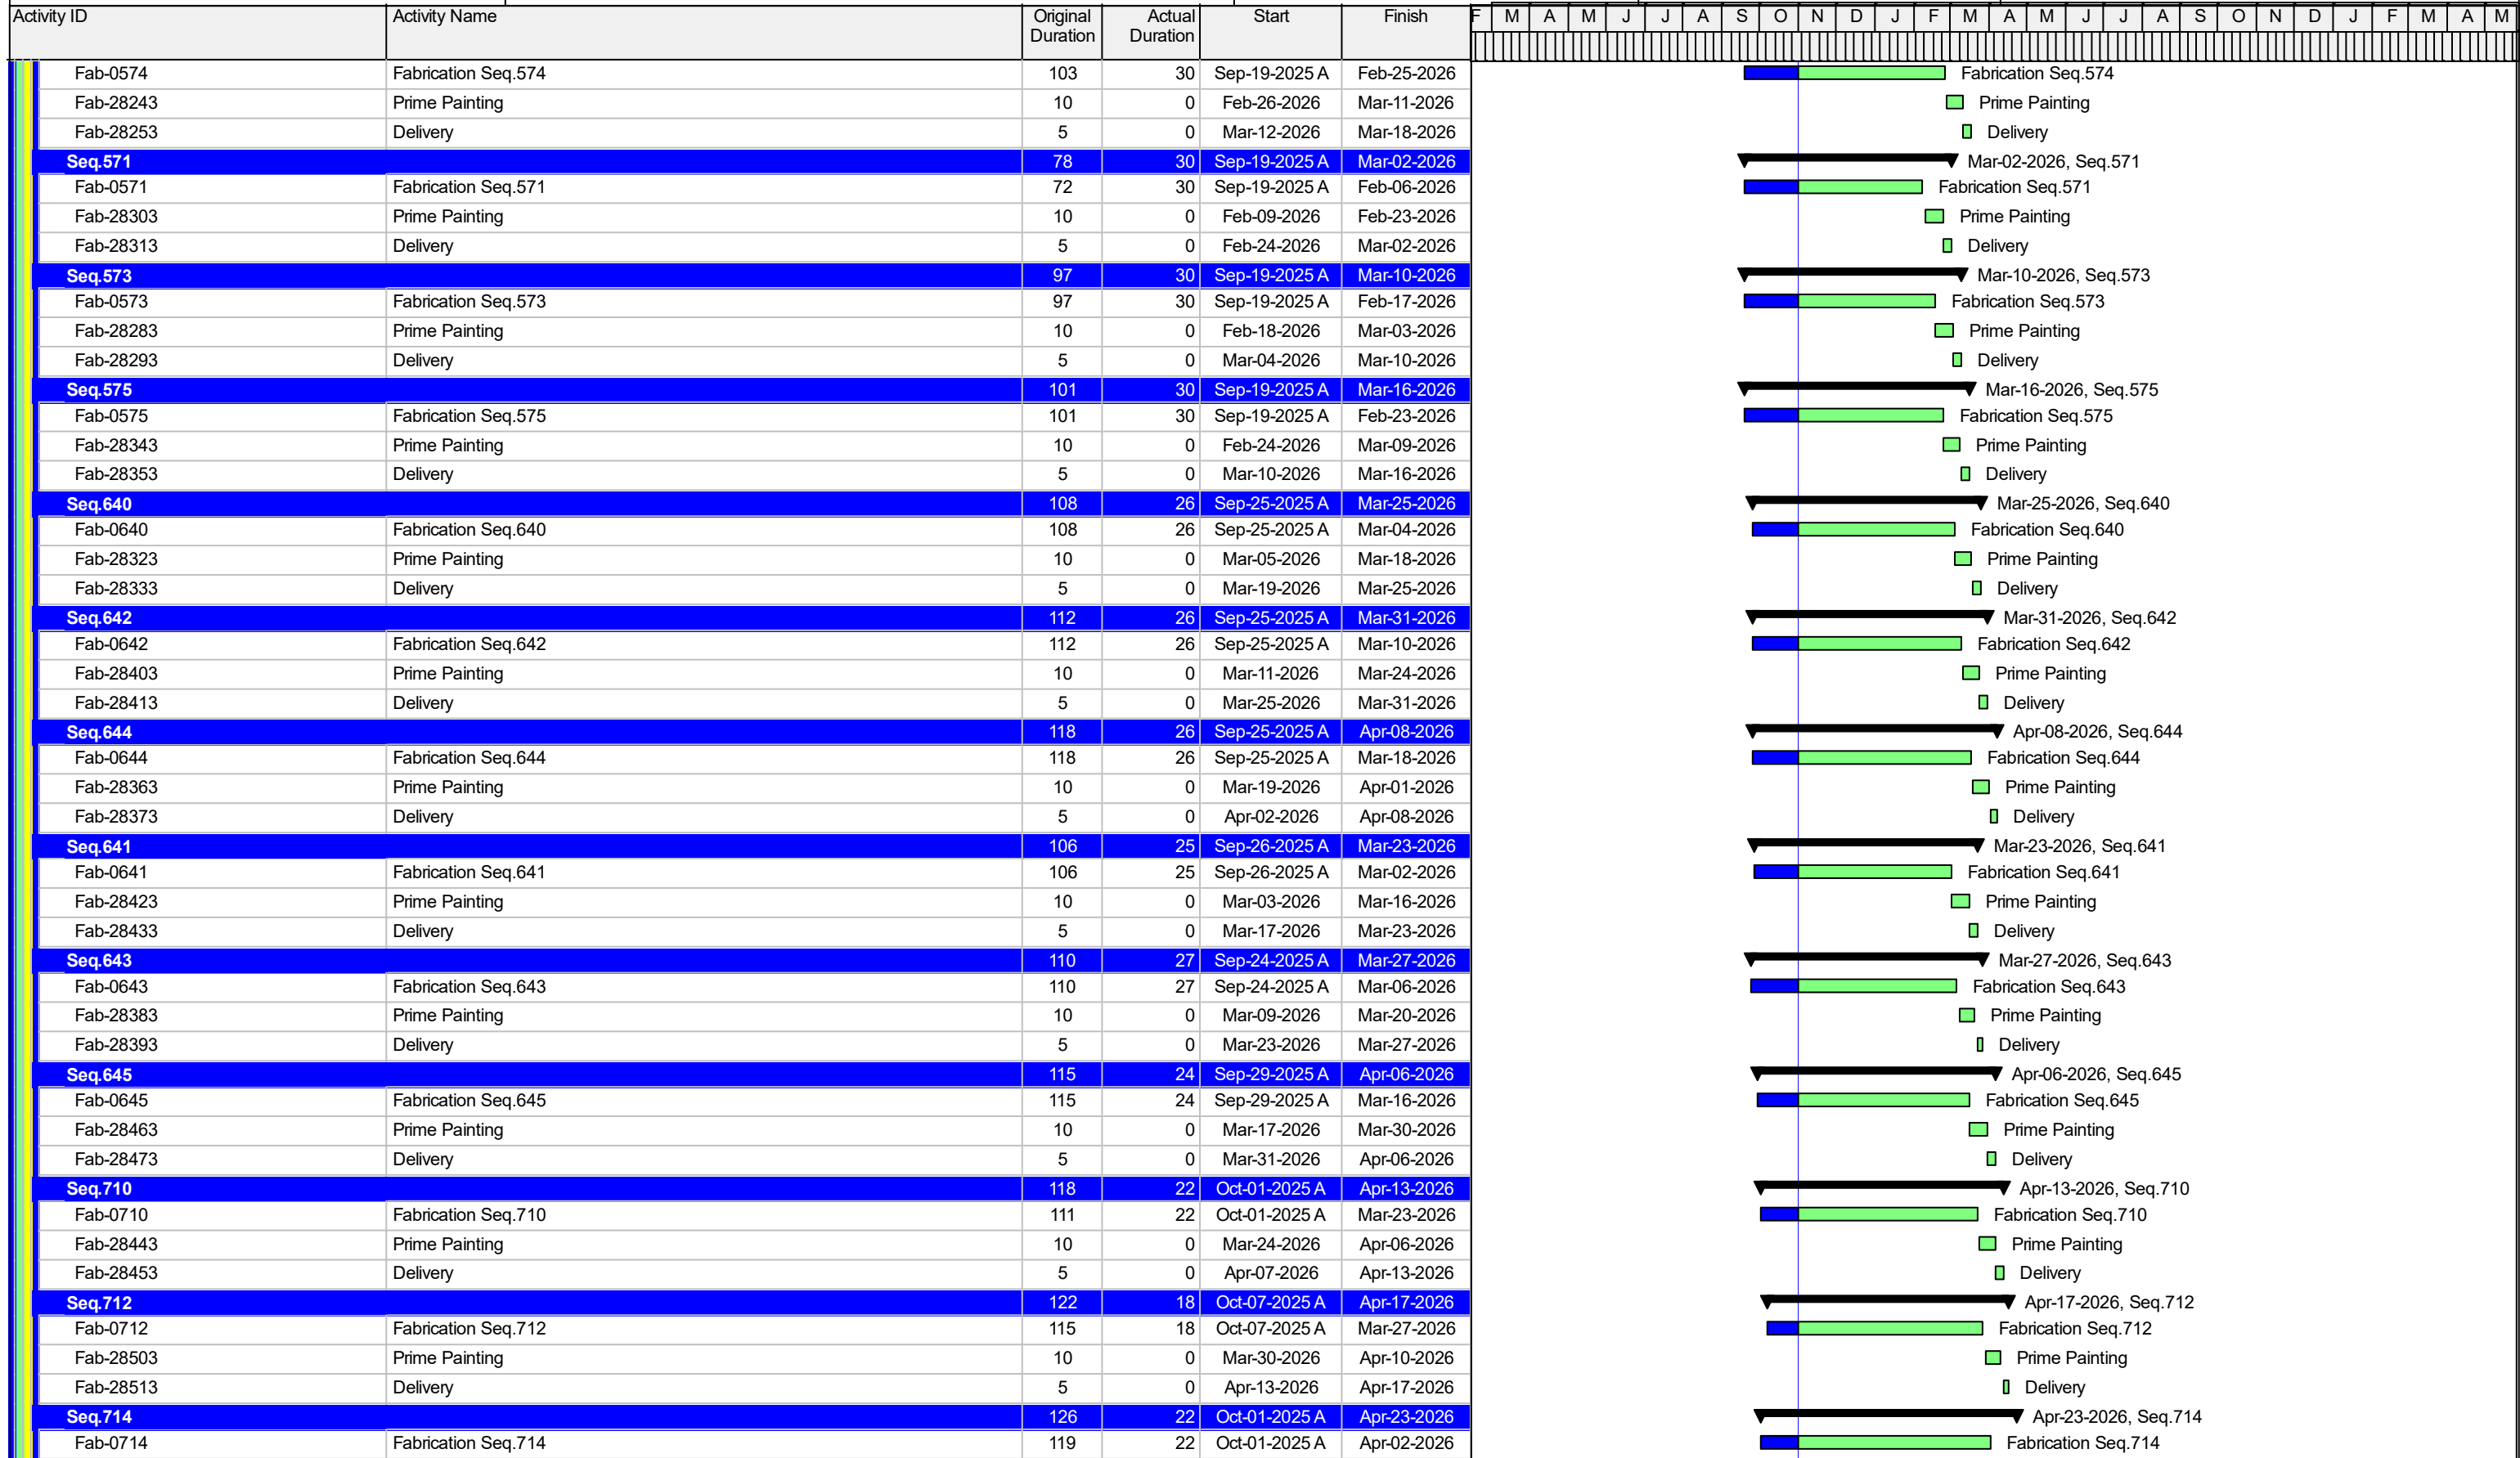

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



A DBM GLOBAL COMPANY

TSMC FAB3 Preliminary Schedule

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary



Activity ID	Activity Name	Original Duration	Actual Duration	Start	Finish	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M
Fab-28483	Prime Painting	10	0	Apr-03-2026	Apr-16-2026																												
Fab-28493	Delivery	5	0	Apr-17-2026	Apr-23-2026																												
Seq.716		135	25	Sep-26-2025 A	May-01-2026																												
Fab-0716	Fabrication Seq.716	135	25	Sep-26-2025 A	Apr-10-2026																												
Fab-28523	Prime Painting	10	0	Apr-13-2026	Apr-24-2026																												
Fab-28533	Delivery	5	0	Apr-27-2026	May-01-2026																												
Seq.711		120	18	Oct-07-2025 A	Apr-15-2026																												
Fab-0711	Fabrication Seq.711	113	18	Oct-07-2025 A	Mar-25-2026																												
Fab-28563	Prime Painting	10	0	Mar-26-2026	Apr-08-2026																												
Fab-28573	Delivery	5	0	Apr-09-2026	Apr-15-2026																												
Seq.713		124	19	Oct-06-2025 A	Apr-21-2026																												
Fab-0713	Fabrication Seq.713	117	19	Oct-06-2025 A	Mar-31-2026																												
Fab-28583	Prime Painting	10	0	Apr-01-2026	Apr-14-2026																												
Fab-28593	Delivery	5	0	Apr-15-2026	Apr-21-2026																												
Seq.715		128	16	Oct-09-2025 A	Apr-27-2026																												
Fab-0715	Fabrication Seq.715	121	16	Oct-09-2025 A	Apr-06-2026																												
Fab-28603	Prime Painting	10	0	Apr-07-2026	Apr-20-2026																												
Fab-28613	Delivery	5	0	Apr-21-2026	Apr-27-2026																												
Seq.717		120	17	Oct-08-2025 A	Apr-29-2026																												
Fab-0717	Fabrication Seq.717	114	17	Oct-08-2025 A	Apr-08-2026																												
Fab-28623	Prime Painting	10	0	Apr-09-2026	Apr-22-2026																												
Fab-28633	Delivery	5	0	Apr-23-2026	Apr-29-2026																												
Fabrication and Delivery South Annex - East		78	30	Sep-19-2025 A	Feb-12-2026																												
Seq.215		55	30	Sep-19-2025 A	Jan-06-2026																												
Fab-0215	Fabrication Seq.215	55	30	Sep-19-2025 A	Dec-08-2025																												
Fab-1248	Prime Painting	10	0	Dec-09-2025	Dec-22-2025																												
Fab-1253	Delivery	5	0	Dec-23-2025	Jan-06-2026																												
Seq.216		77	27	Sep-24-2025 A	Feb-11-2026																												
Fab-0216	Fabrication Seq.216	77	27	Sep-24-2025 A	Jan-21-2026																												
Fab-1258	Prime Painting	10	0	Jan-22-2026	Feb-04-2026																												
Fab-1263	Delivery	5	0	Feb-05-2026	Feb-11-2026																												
Seq.217		54	23	Sep-30-2025 A	Jan-12-2026																												
Fab-0217	Fabrication Seq.217	38	23	Sep-30-2025 A	Dec-12-2025																												
Fab-1268	Prime Painting	10	0	Dec-15-2025	Jan-05-2026																												
Fab-1340	Delivery	5	0	Jan-06-2026	Jan-12-2026																												
Seq.218		67	18	Oct-07-2025 A	Feb-12-2026																												
Fab-0218	Fabrication Seq.218	60	18	Oct-07-2025 A	Jan-22-2026																												
Fab-1278	Prime Painting	10	0	Jan-23-2026	Feb-05-2026																												
Fab-1283	Delivery	5	0	Feb-06-2026	Feb-12-2026																												
Fabrication and Delivery South Annex - West		109	0	Nov-17-2025	Apr-29-2026																												
Seq.415		92	0	Nov-17-2025	Apr-06-2026																												
Fab-0415	Fabrication Seq.415	77	0	Nov-17-2025	Mar-16-2026																												
Fab-1918	Prime Painting	10	0	Mar-17-2026	Mar-30-2026																												
Fab-1923	Delivery	5	0	Mar-31-2026	Apr-06-2026																												
Seq.416		107	0	Nov-17-2025	Apr-27-2026																												
Fab-0416	Fabrication Seq.416	92	0	Nov-17-2025	Apr-06-2026																												
Fab-1928	Prime Painting	10	0	Apr-07-2026	Apr-20-2026																												
Fab-1933	Delivery	5	0	Apr-21-2026	Apr-27-2026																												
Seq.417		99	0	Nov-21-2025	Apr-21-2026																												

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 42 of 99
Data date : Oct-31-2025

Page 42 of 99

Data date : Oct-31-2025




INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 44 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

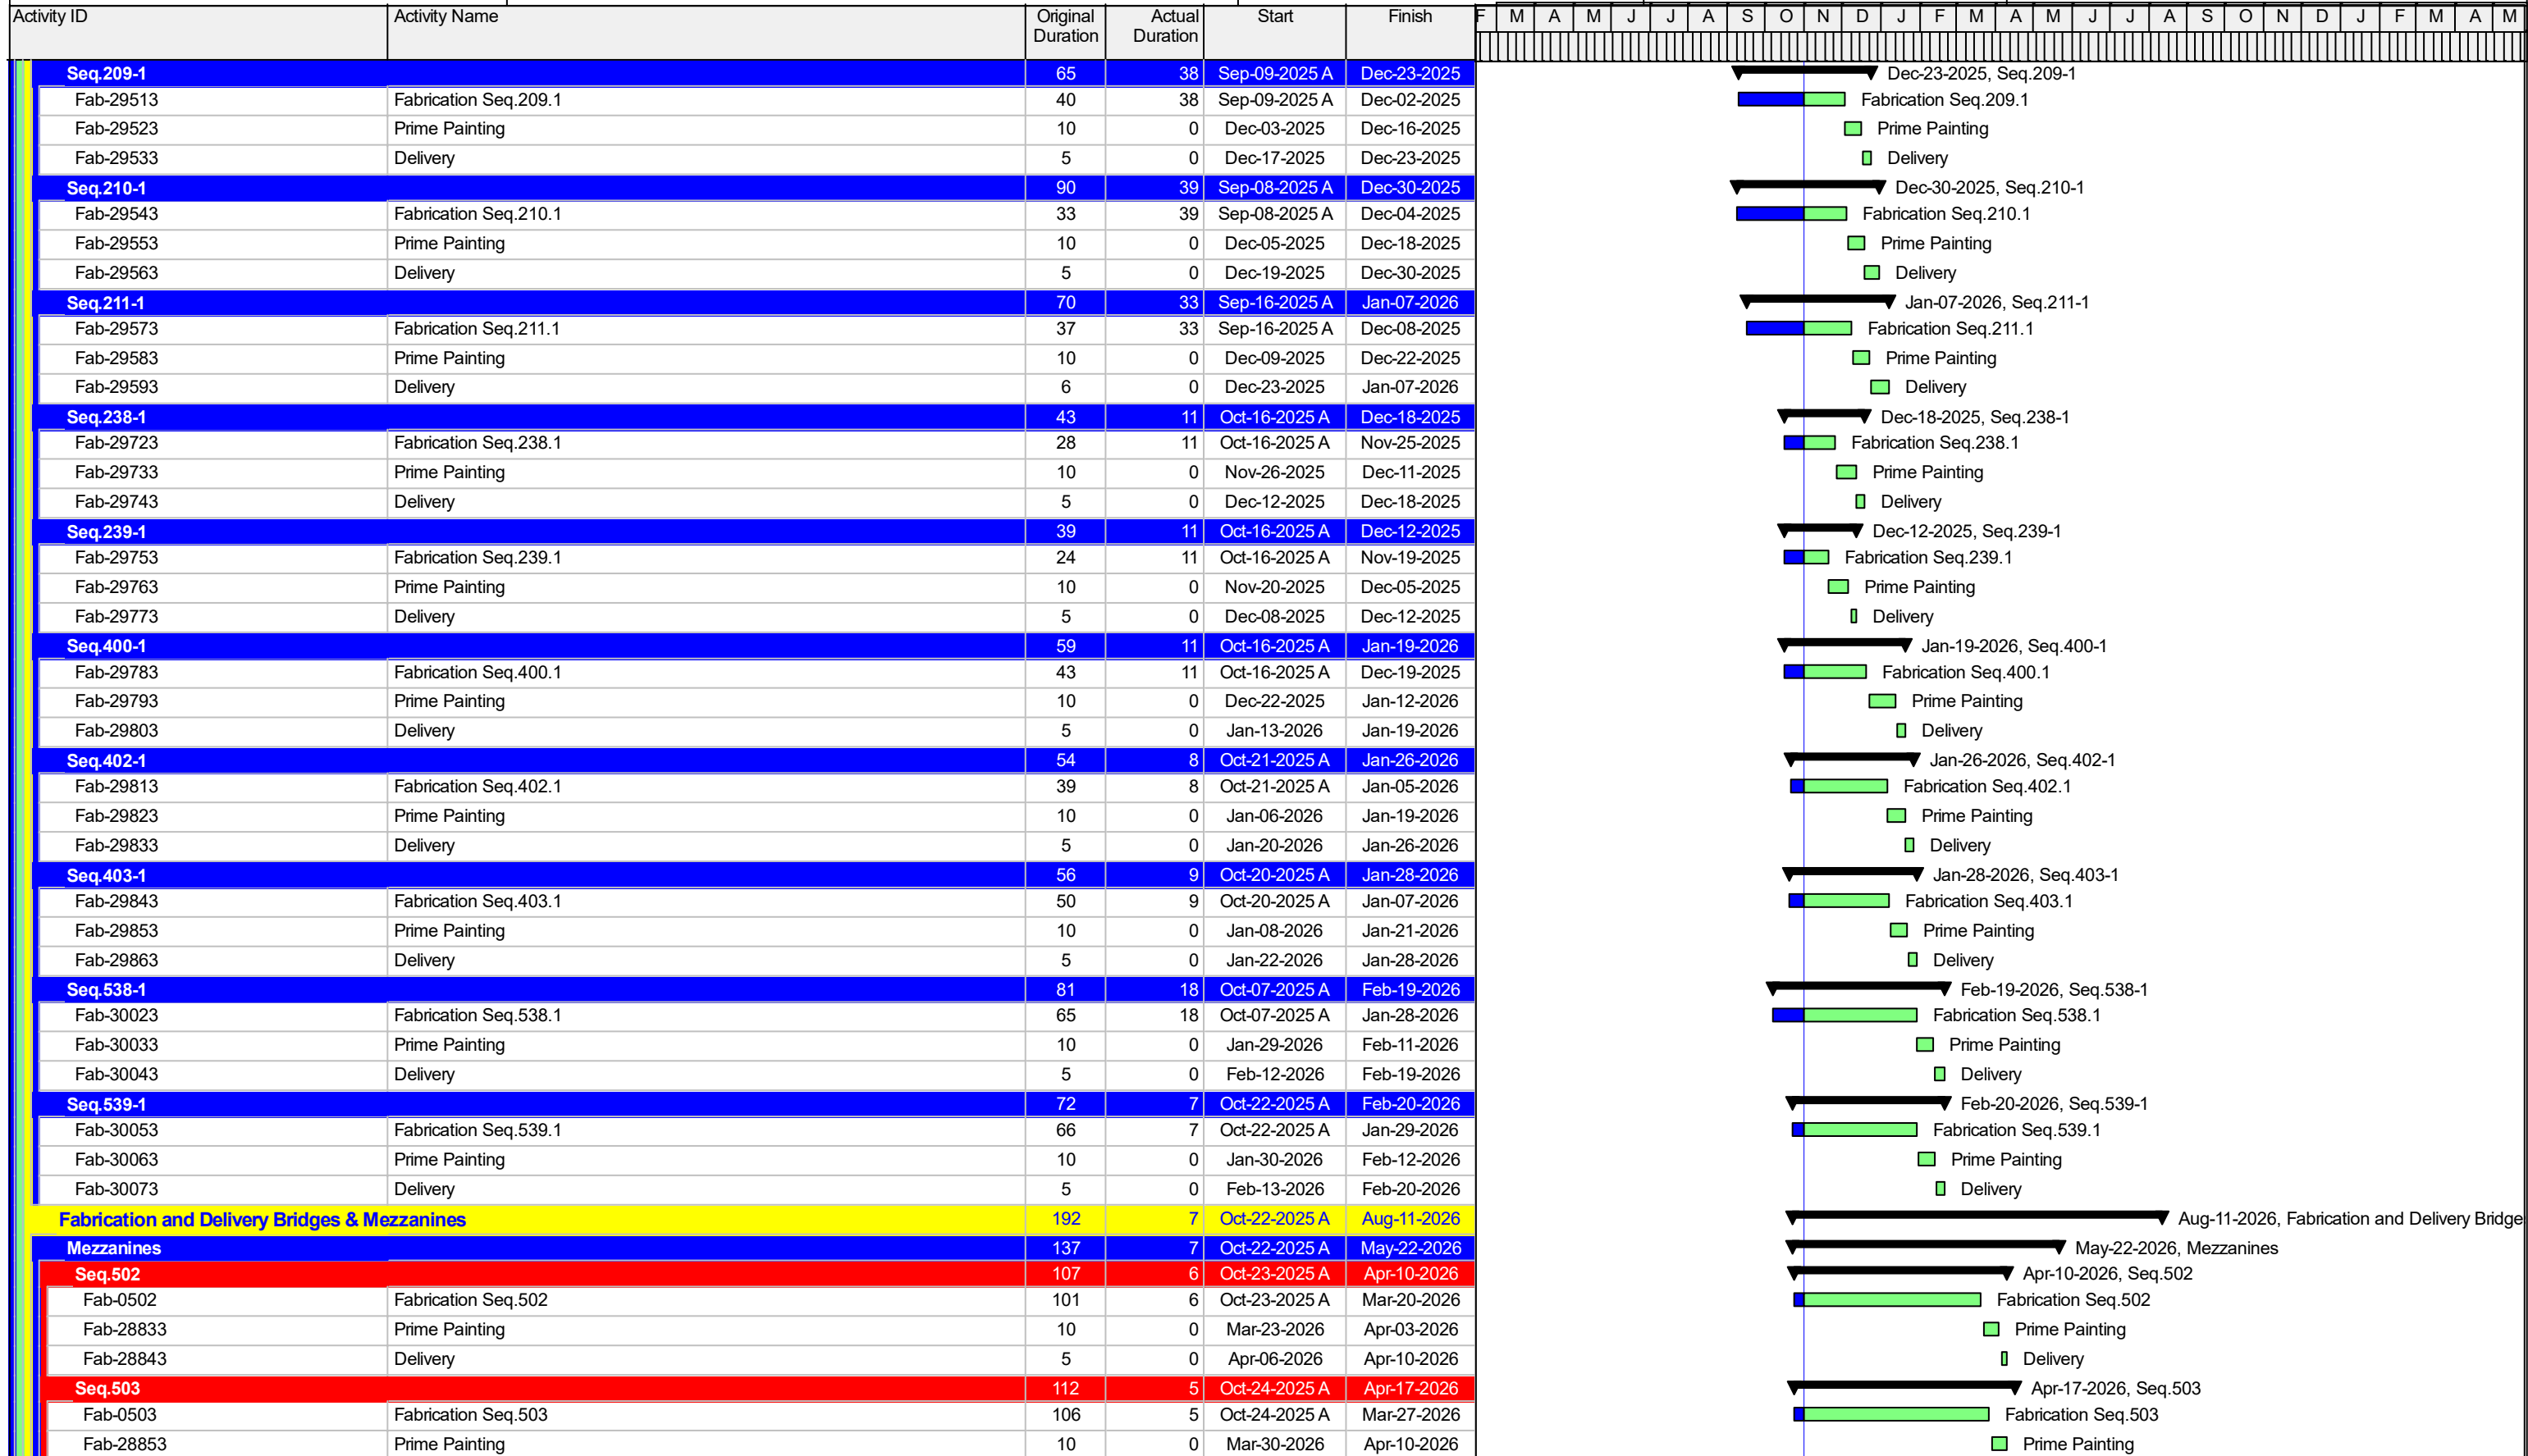

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



A DBM GLOBAL COMPANY

TSMC FAB3 Preliminary Schedule

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary



Activity ID	Activity Name	Original Duration	Actual Duration	Start	Finish	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M
	Fab-28863	Delivery	5	0	Apr-13-2026	Apr-17-2026																											
	Seq.504		116	3	Oct-28-2025 A	Apr-23-2026																											
	Fab-0504	Fabrication Seq.504	107	3	Oct-28-2025 A	Apr-02-2026																											
	Fab-28873	Prime Painting	10	0	Apr-03-2026	Apr-16-2026																											
	Fab-28883	Delivery	5	0	Apr-17-2026	Apr-23-2026																											
	Seq.505		137	7	Oct-22-2025 A	May-22-2026																											
	Fab-0505	Fabrication Seq.505	131	7	Oct-22-2025 A	May-01-2026																											
	Fab-28893	Prime Painting	10	0	May-04-2026	May-15-2026																											
	Fab-28903	Delivery	5	0	May-18-2026	May-22-2026																											
	Seq.600 Bridge 1		105	0	Mar-02-2026	Jul-28-2026																											
	Fab-2223	Fabrication Seq.600 - Bridge 1	90	0	Mar-02-2026	Jul-07-2026																											
	Fab-2233	Prime Painting	10	0	Jul-08-2026	Jul-21-2026																											
	Fab-2243	Delivery	5	0	Jul-22-2026	Jul-28-2026																											
	Seq.601 Bridge 2		105	0	Mar-02-2026	Jul-28-2026																											
	Fab-2253	Fabrication Seq.601 - Bridge 2	90	0	Mar-02-2026	Jul-07-2026																											
	Fab-2263	Prime Painting	10	0	Jul-08-2026	Jul-21-2026																											
	Fab-2273	Delivery	5	0	Jul-22-2026	Jul-28-2026																											
	Seq.602 Bridge 3		110	0	Mar-02-2026	Aug-04-2026																											
	Fab-2283	Fabrication Seq.602 - Bridge 3	95	0	Mar-02-2026	Jul-14-2026																											
	Fab-2293	Prime Painting	10	0	Jul-15-2026	Jul-28-2026																											
	Fab-2303	Delivery	5	0	Jul-29-2026	Aug-04-2026																											
	Seq.603 Bridge 4		115	0	Mar-02-2026	Aug-11-2026																											
	Fab-2433	Fabrication Seq.603 - Bridge 4	100	0	Mar-02-2026	Jul-21-2026																											
	Fab-2443	Prime Painting	10	0	Jul-22-2026	Aug-04-2026																											
	Fab-2453	Delivery	5	0	Aug-05-2026	Aug-11-2026																											
	Stairs Fabrication and Delivery		246	41	Sep-05-2025 A	Sep-16-2026																											
	Exterior Stairs Fabrication and Delivery		183	5	Oct-24-2025 A	Jul-29-2026																											
	STA-F38		44	0	Nov-07-2025	Jan-19-2026																											
	Fab-STA-F38-10	Fabrication STA-F38	39	0	Nov-07-2025*	Jan-12-2026																											
	Fab-STA-F38-20	Prime Painting	2	0	Jan-13-2026	Jan-14-2026																											
	Fab-STA-F38-30	Delivery	3	0	Jan-15-2026	Jan-19-2026																											
	STA-F01		40	0	Nov-05-2025	Jan-09-2026																											
	Fab-STA-F01-10	Fabrication STA-F01	35	0	Nov-05-2025	Dec-30-2025																											
	Fab-STA-F01-20	Prime Painting	2	0	Jan-05-2026	Jan-06-2026																											
	Fab-STA-F01-30	Delivery	3	0	Jan-07-2026	Jan-09-2026																											
	STA-F02		104	0	Dec-05-2025	May-08-2026																											
	Fab-STA-F02-10	Fabrication STA-F02	99	0	Dec-05-2025	May-01-2026																											
	Fab-STA-F02-20	Prime Painting	2	0	May-04-2026	May-05-2026																											
	Fab-STA-F02-30	Delivery	3	0	May-06-2026	May-08-2026																											
	STA-F39		158	0	Dec-09-2025	Jul-29-2026																											
	Fab-STA-F39-10	Fabrication STA-F39	153	0	Dec-09-2025	Jul-22-2026																											
	Fab-STA-F39-20	Prime Painting	2	0	Jul-23-2026	Jul-24-2026																											
	Fab-STA-F39-30	Delivery	3	0	Jul-27-2026	Jul-29-2026																											
	STA-F06		50	0	Nov-07-2025	Jan-27-2026																											
	Fab-STA-F06-10	Fabrication STA-F06	45	0	Nov-07-2025	Jan-20-2026																											
	Fab-STA-F06-20	Prime Painting	2	0	Jan-21-2026	Jan-22-2026																											
	Fab-STA-F06-30	Delivery	3	0	Jan-23-2026	Jan-27-2026																											
	STA-F12		66	5	Oct-24-2025 A	Feb-03-2026																											
	Fab-STA-F12-10	Fabrication STA-F12	66	5	Oct-24-2025 A	Jan-27-2026																											

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 46 of 99
Data date : Oct-31-2025

Page 46 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 48 of 99
Data date : Oct-31-2025

Page 48 of 99

Data date : Oct-31-2025




INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 49 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

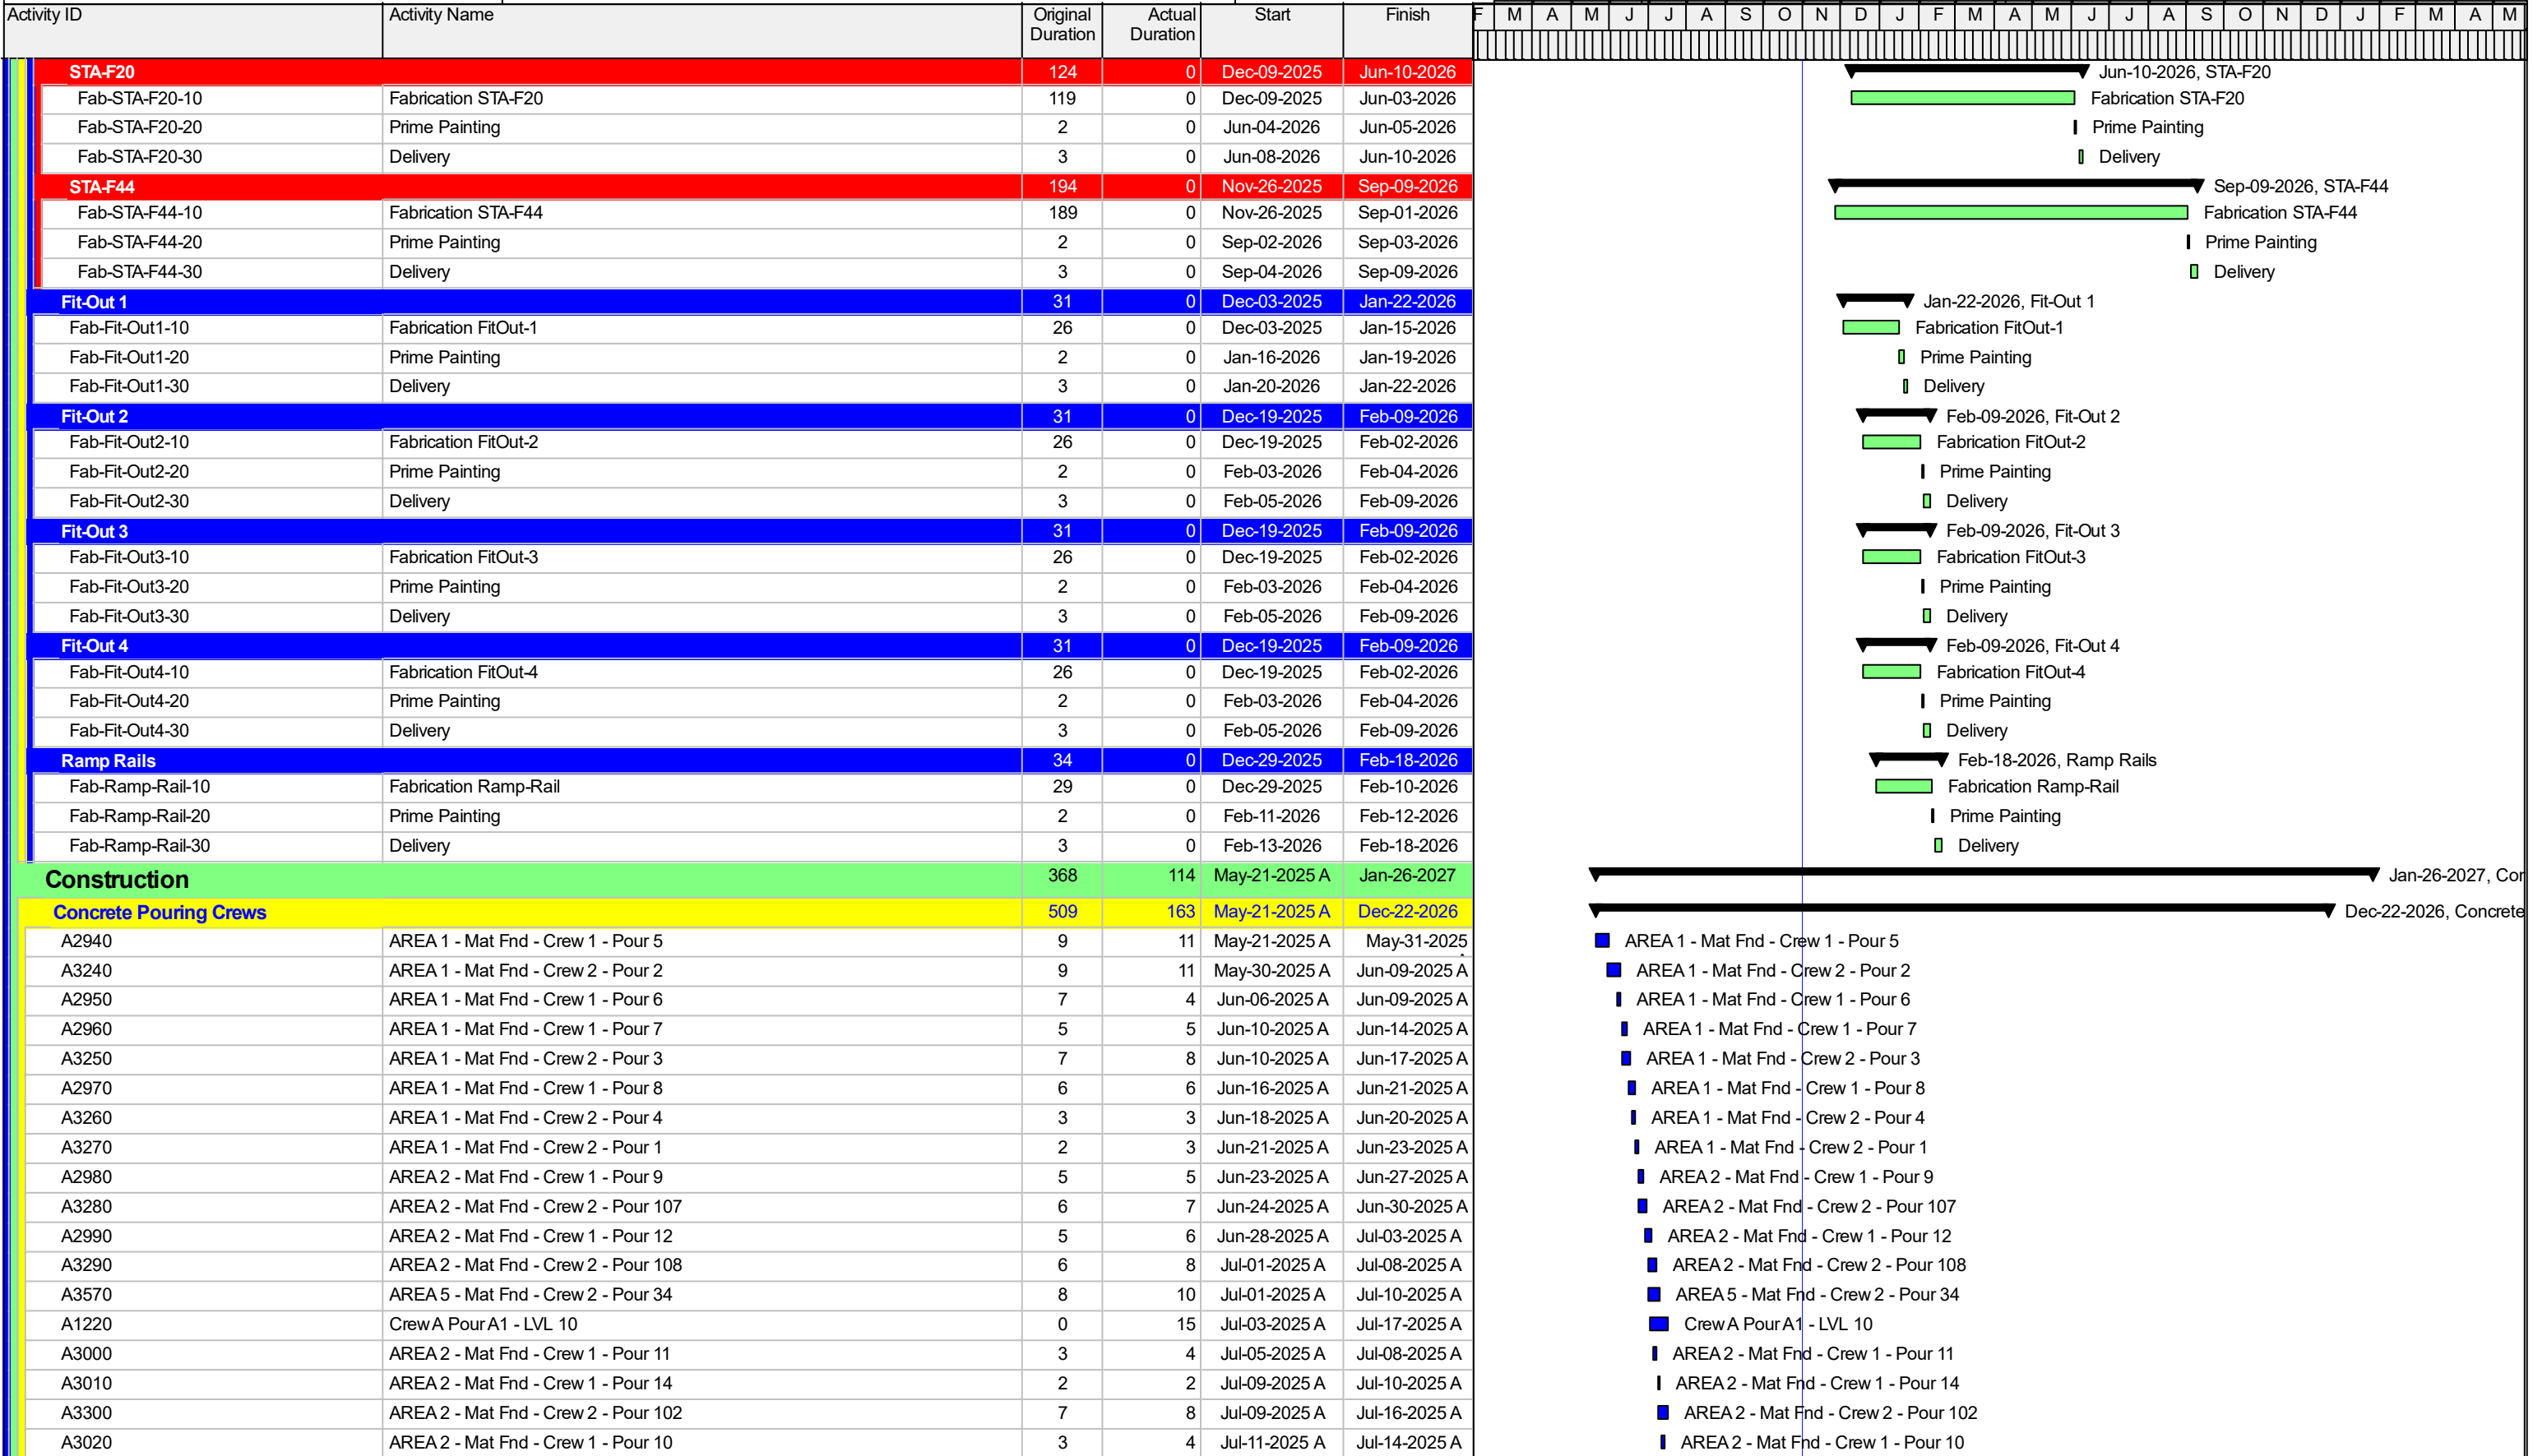

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 51 of 99
Data date : Oct-31-2025

Page 51 of 99

Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary




INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 52 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

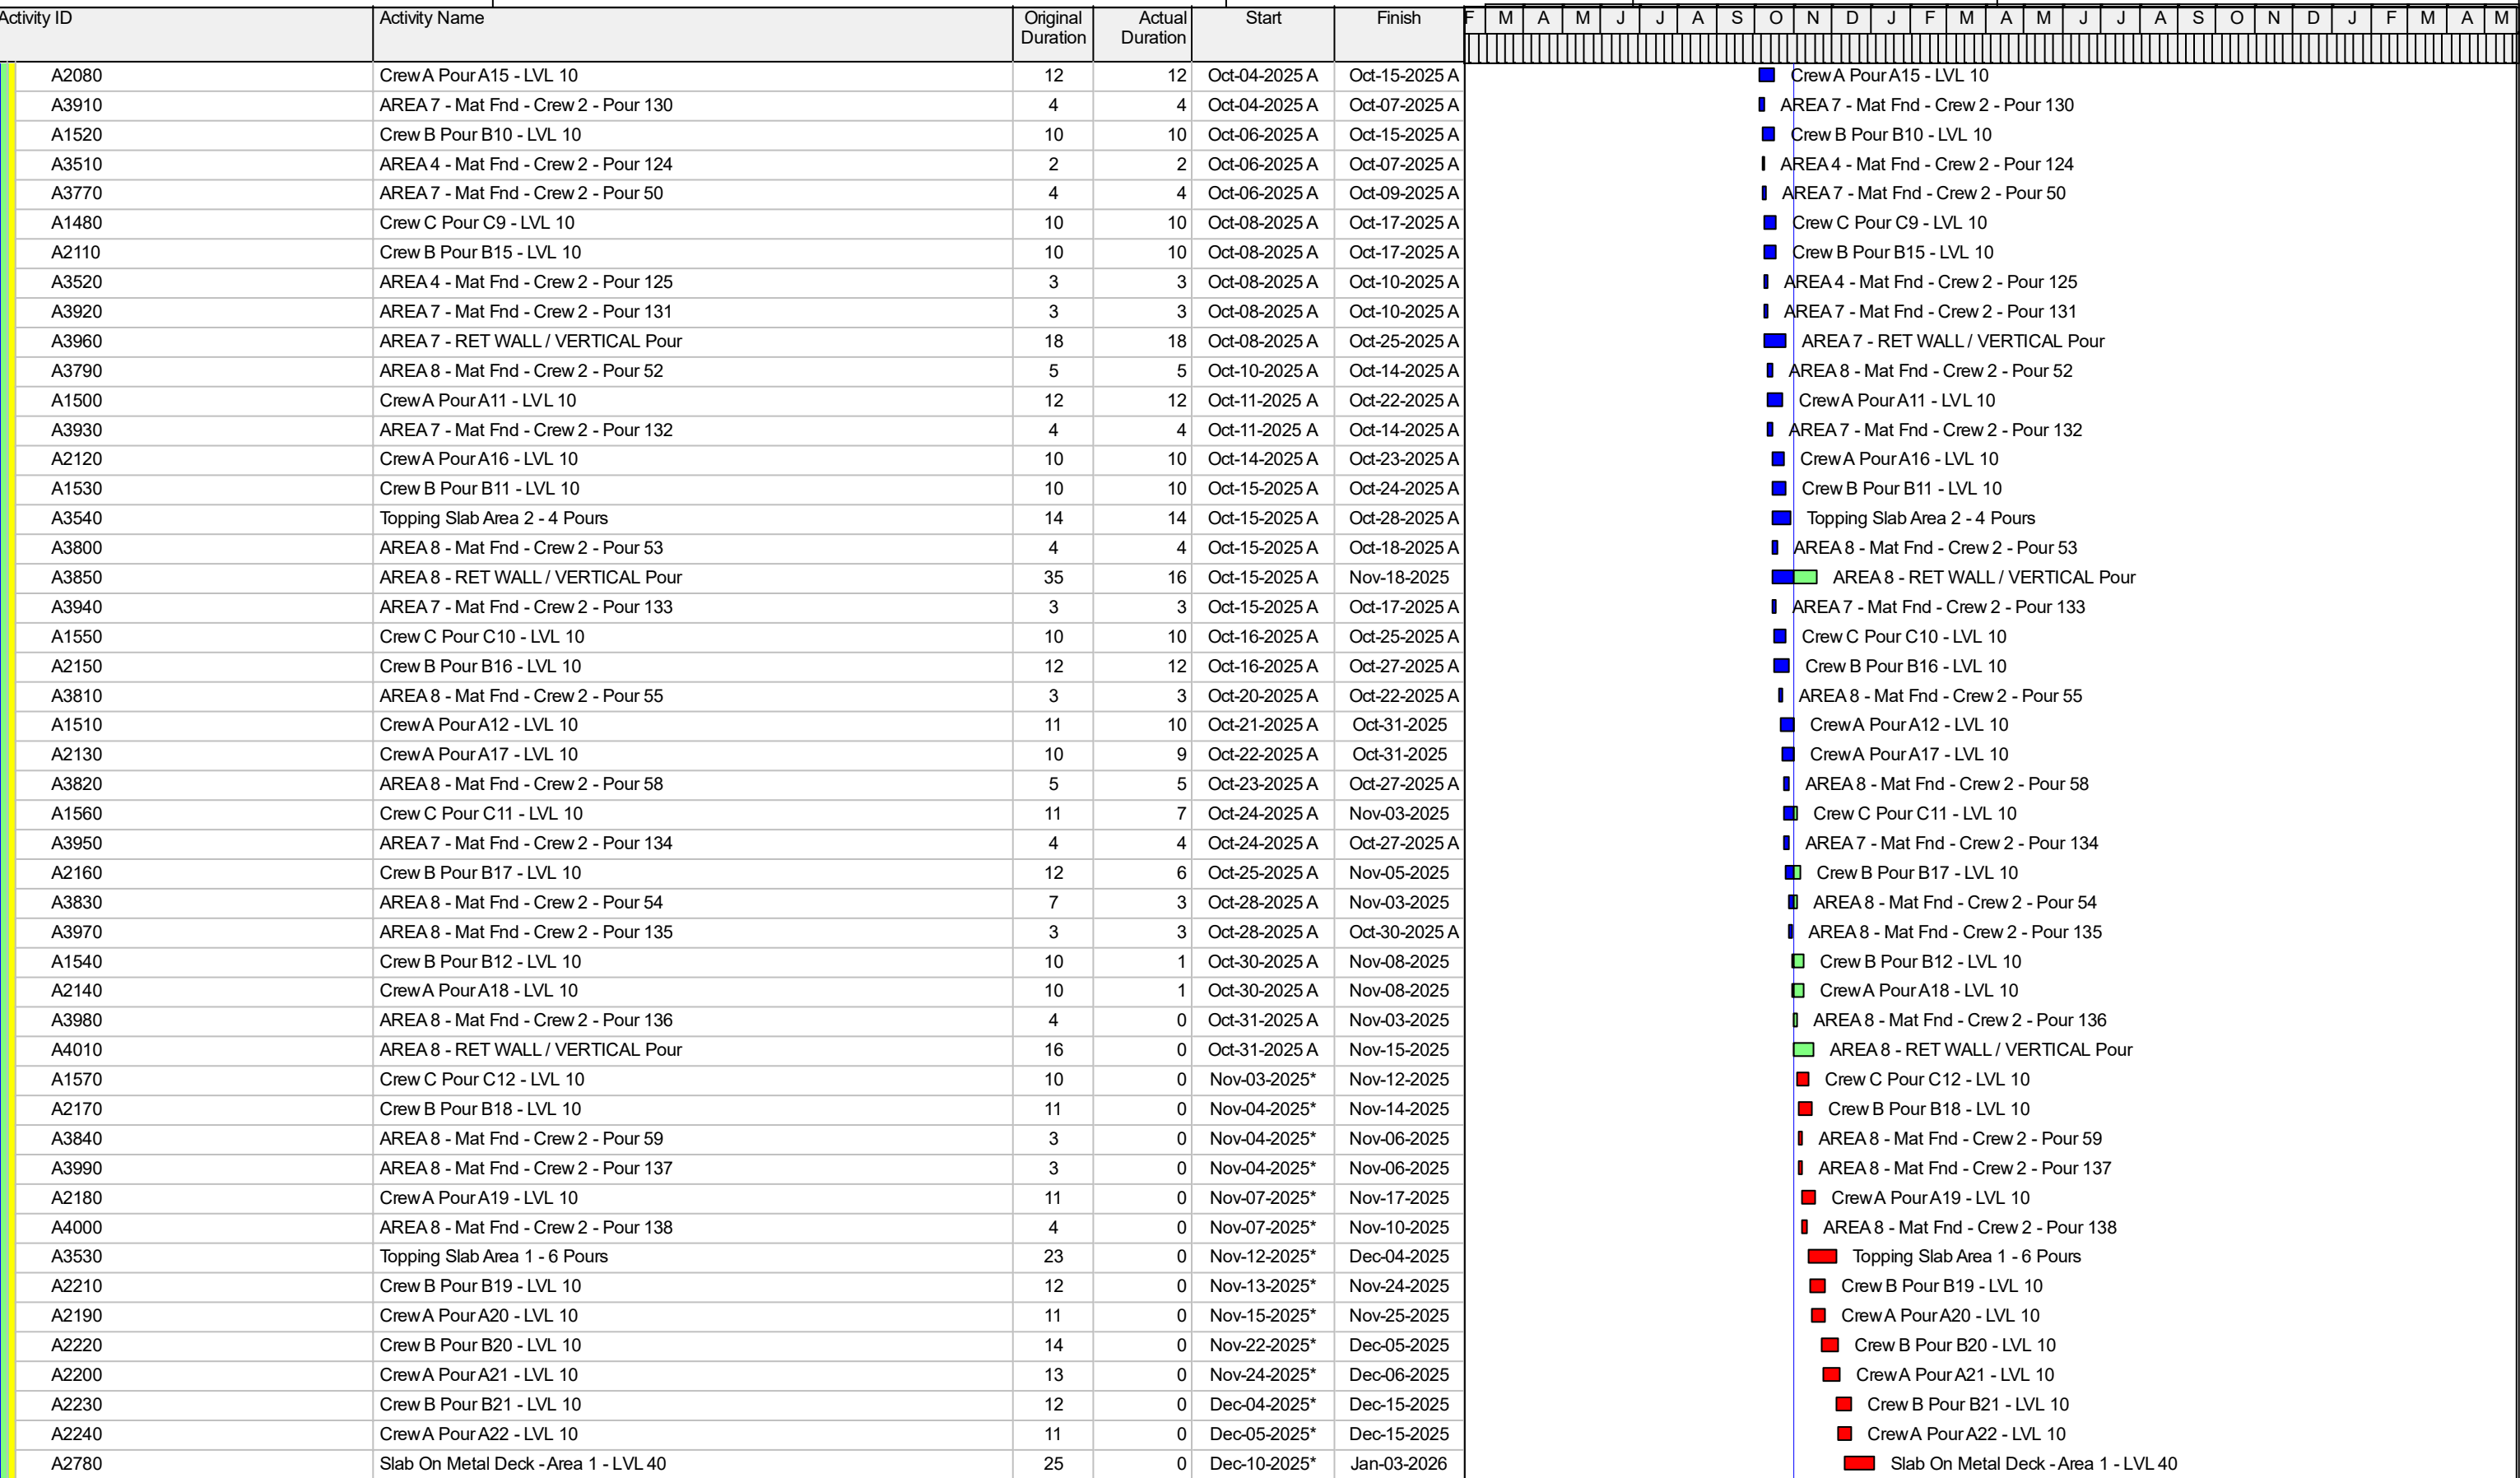


INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 53 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

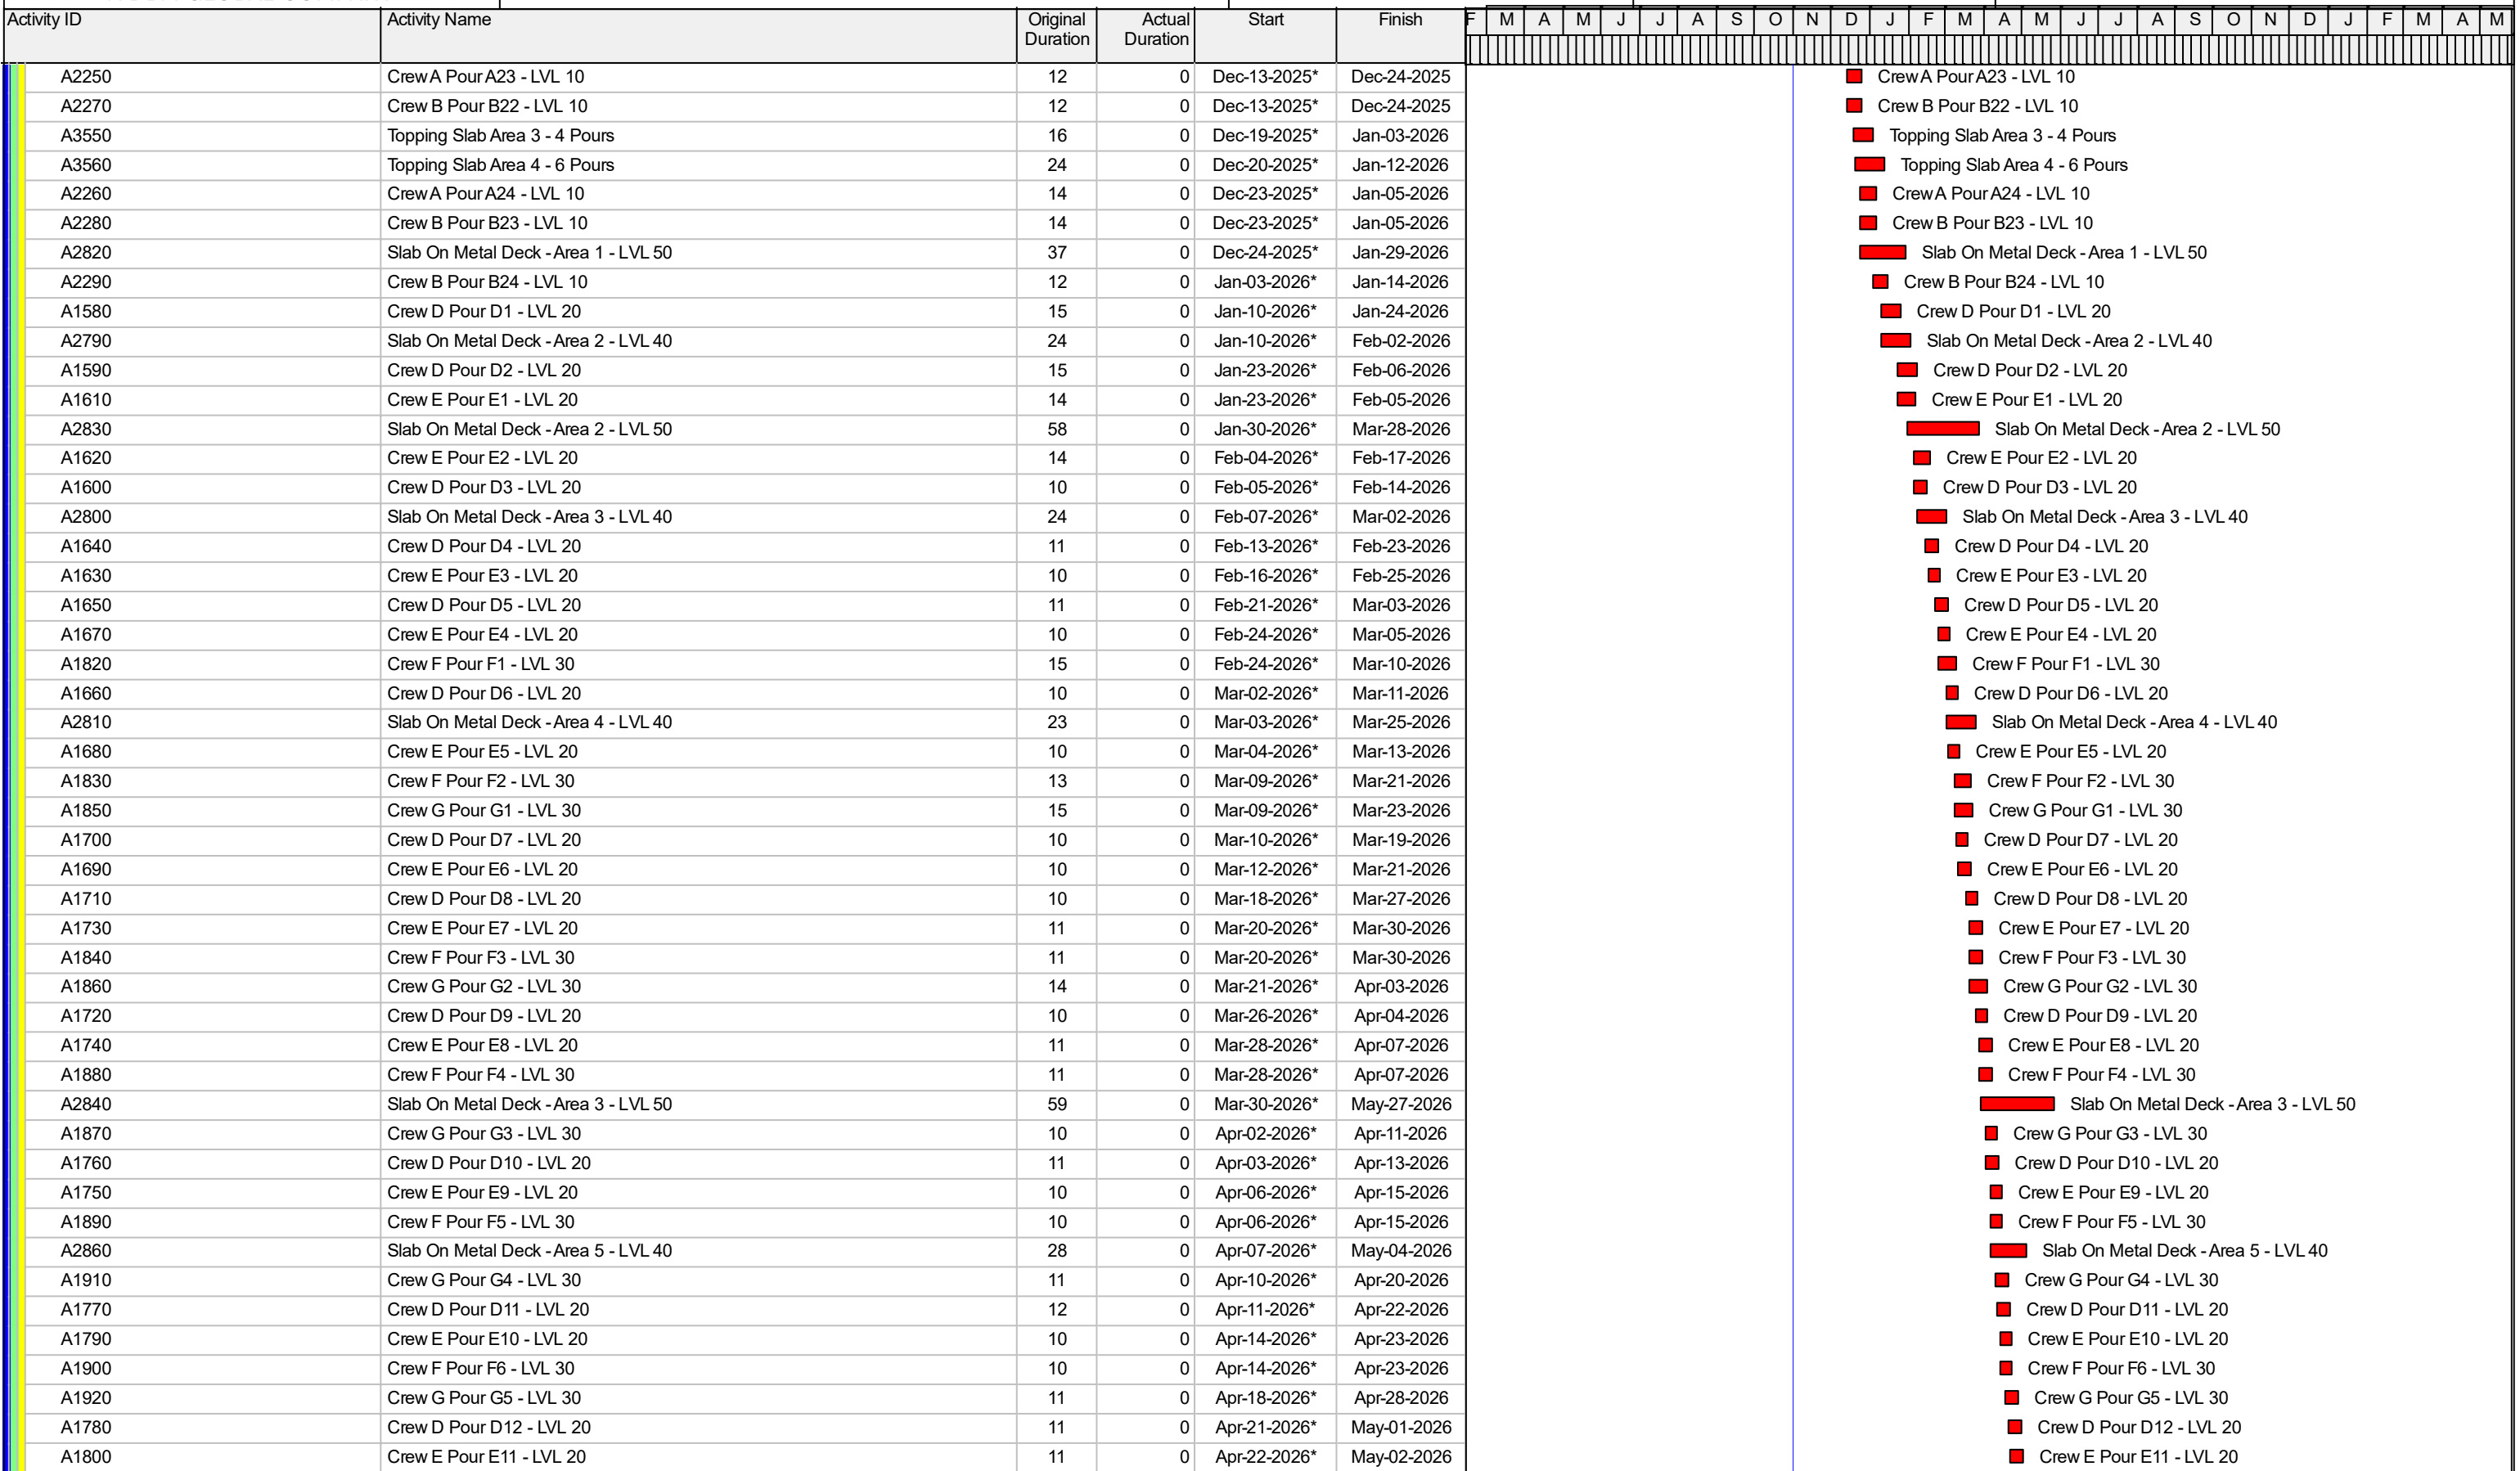


INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 54 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

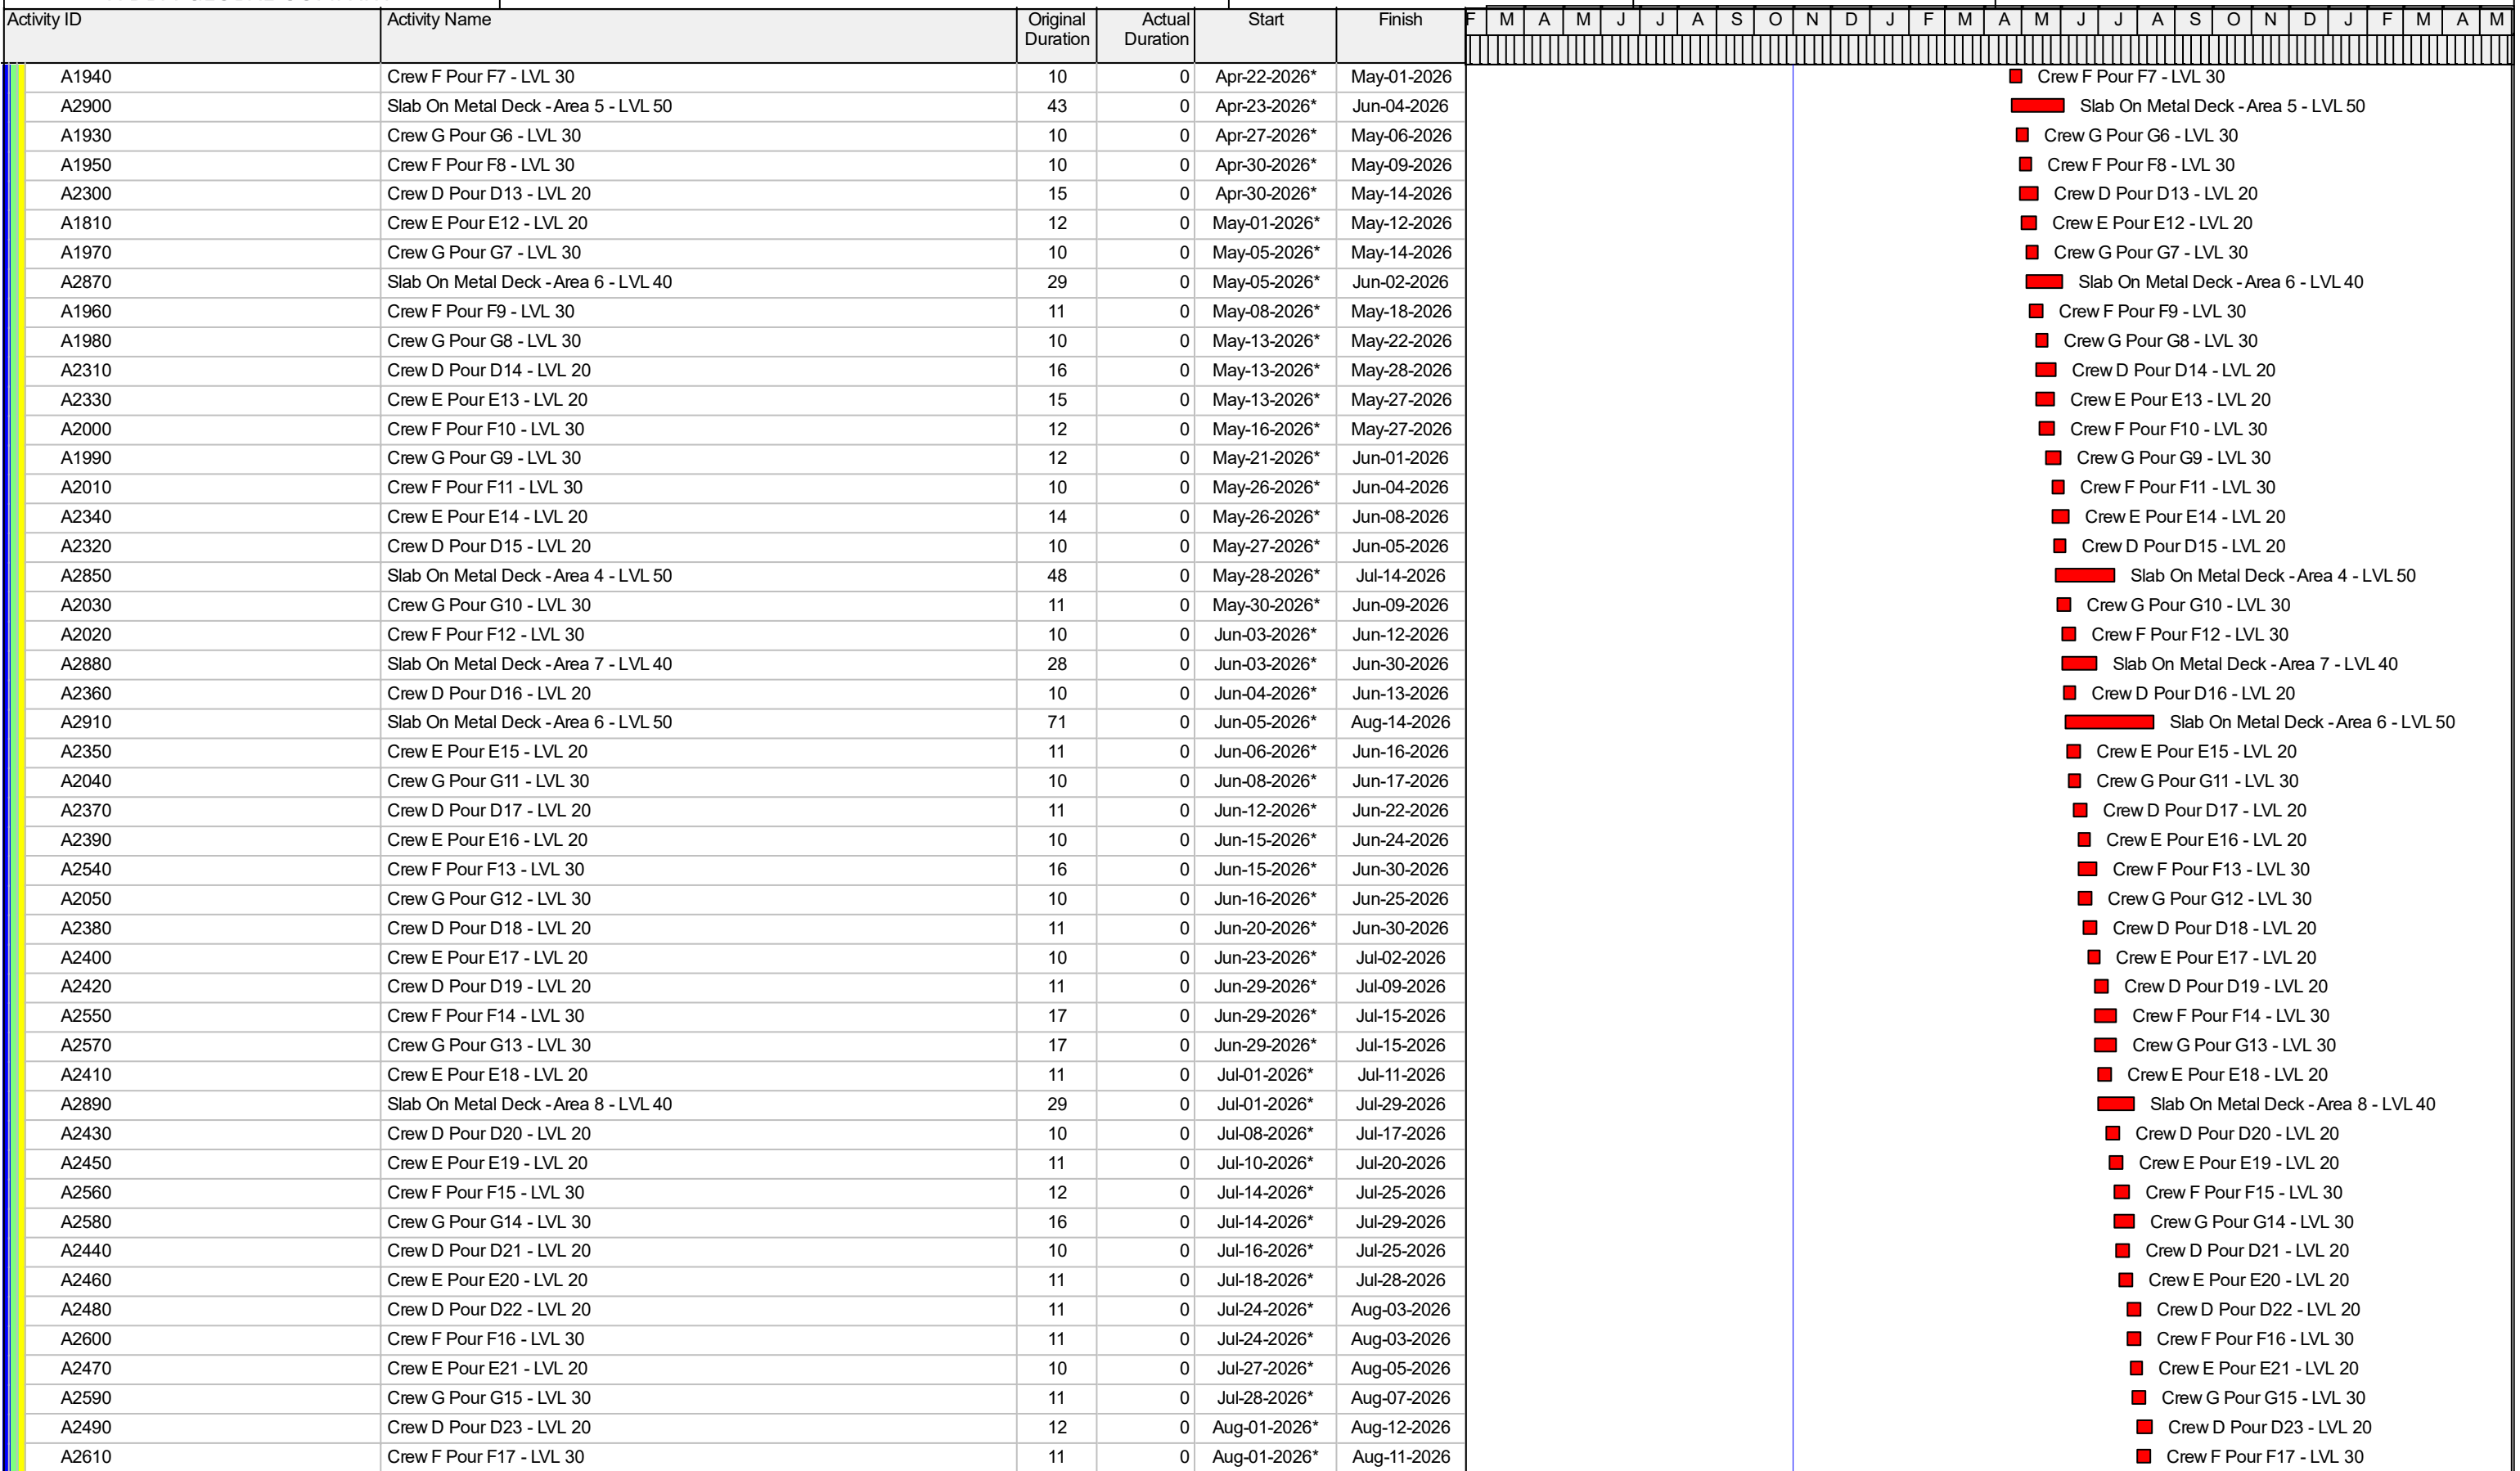


INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 55 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

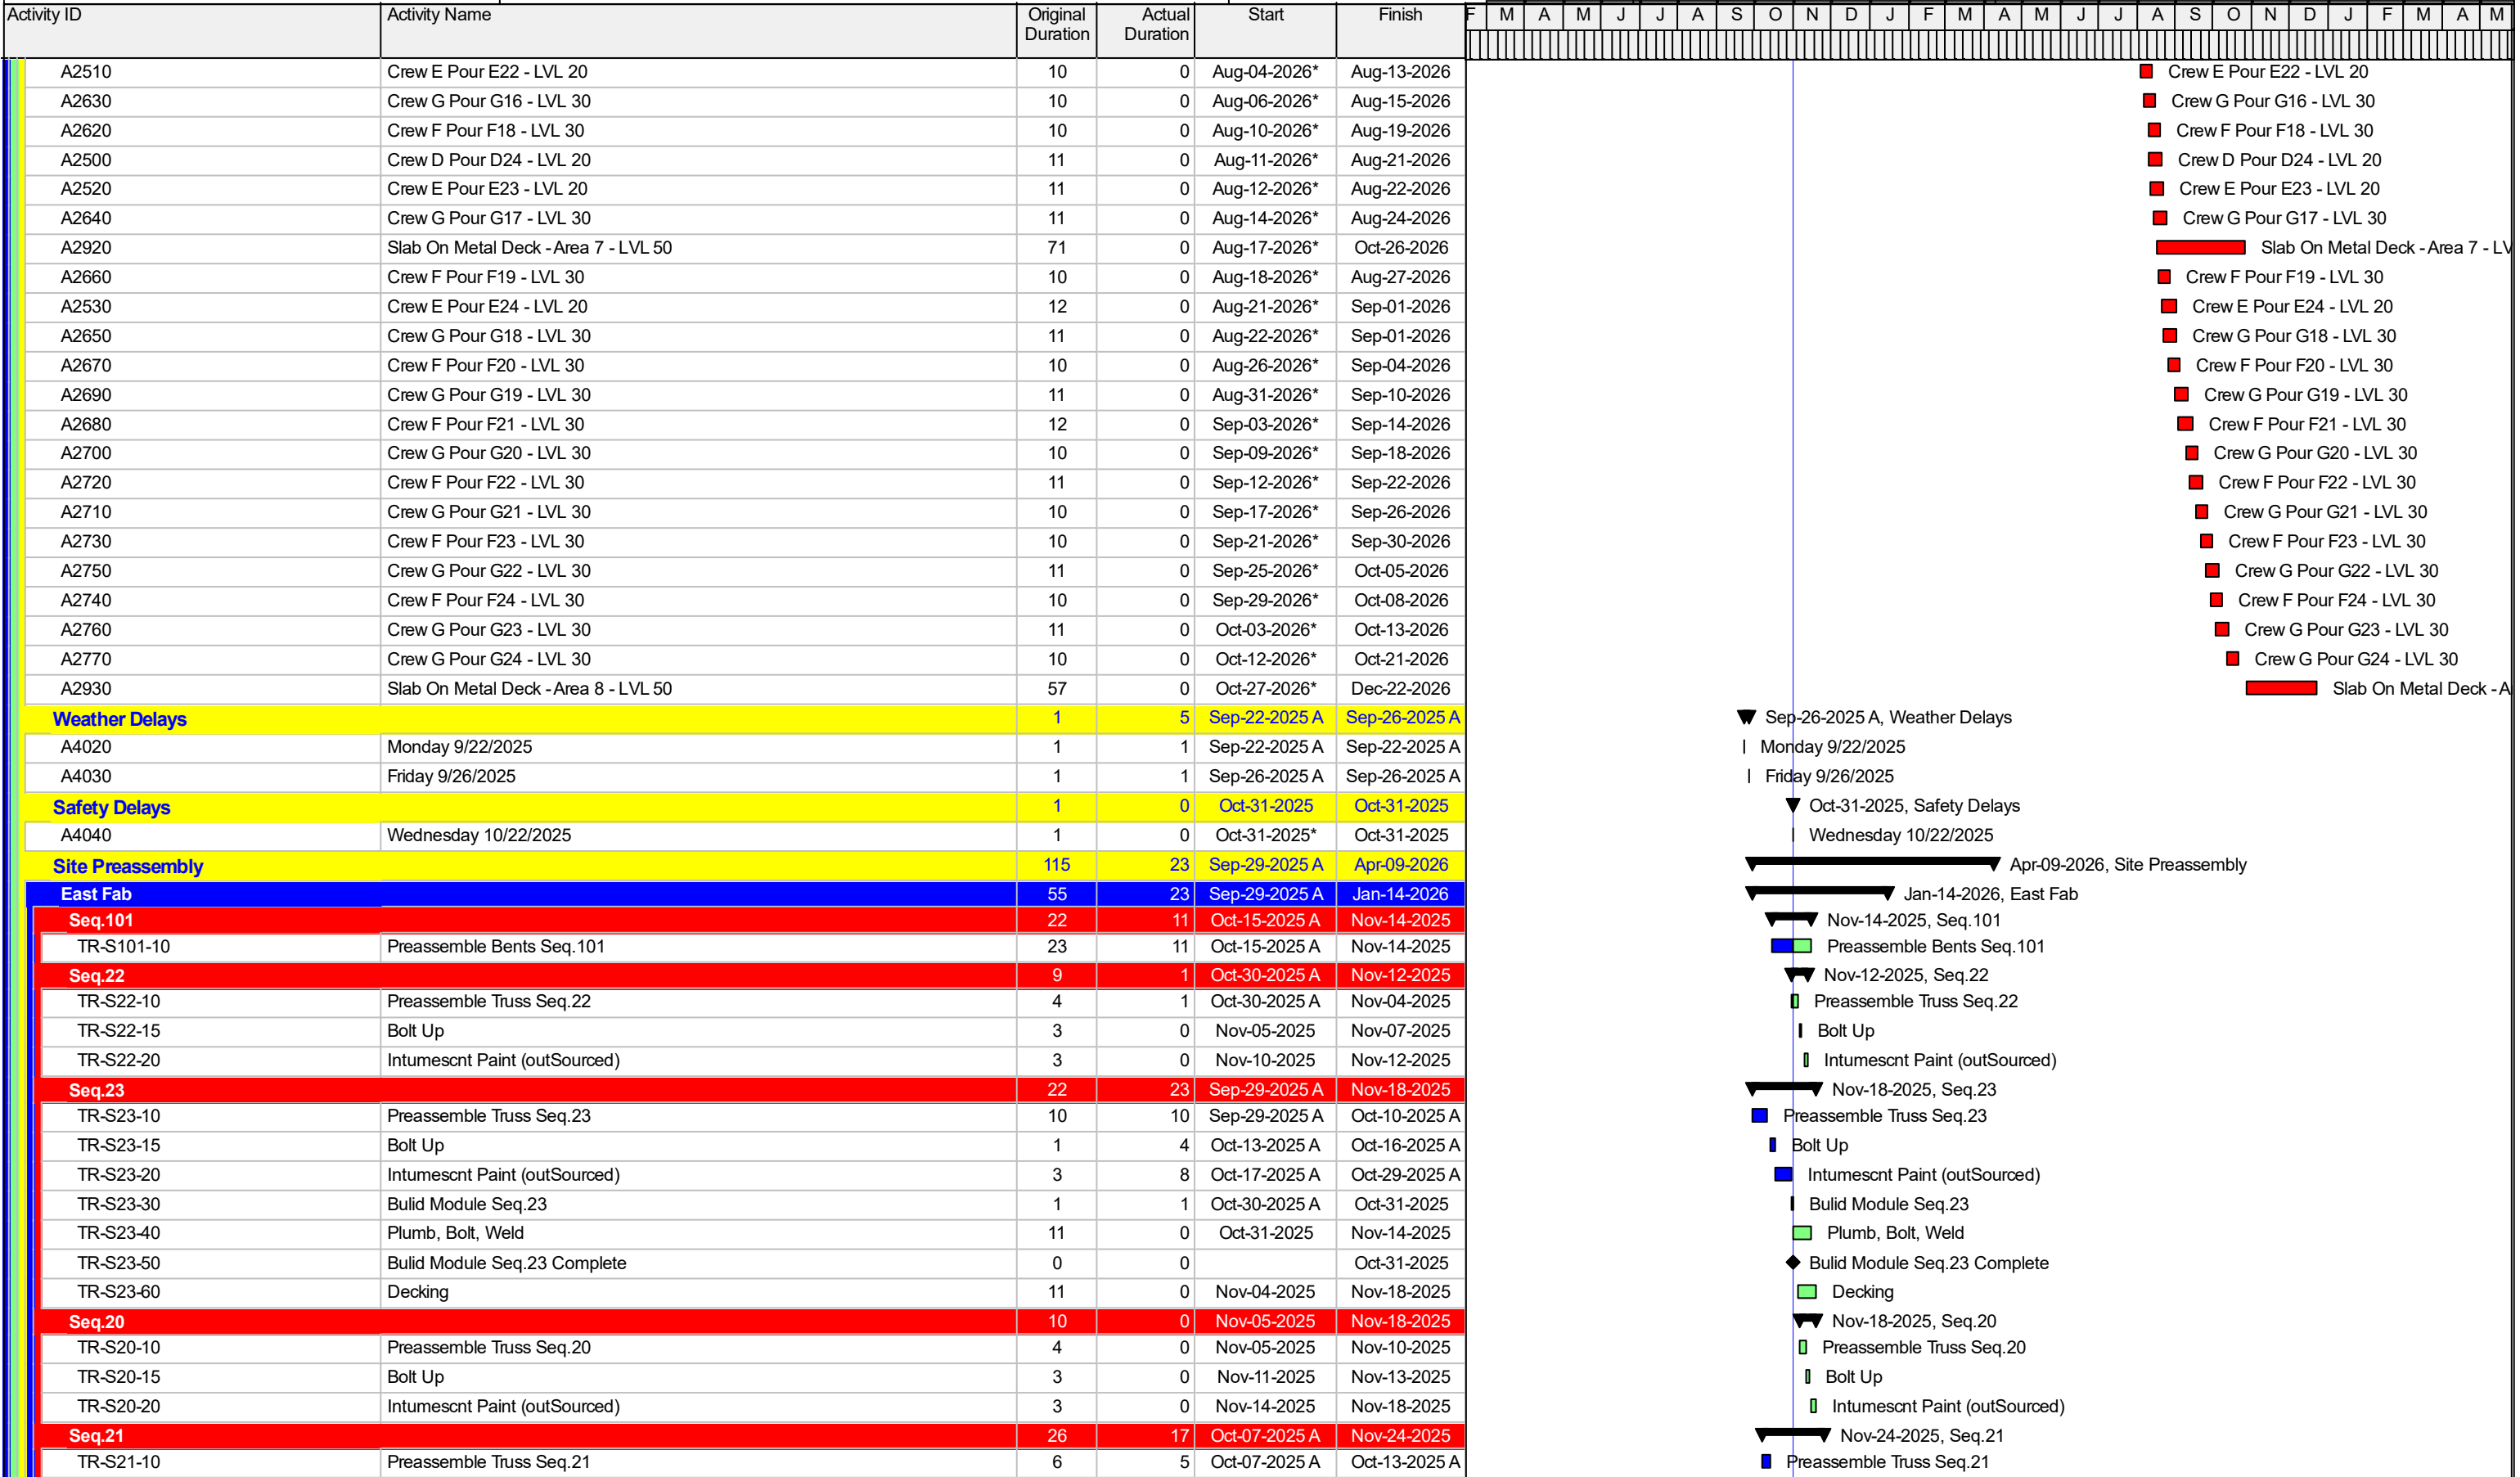

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 56 of 99
Data date : Oct-31-2025

Page 56 of 99

Data date : Oct-31-2025




INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 58 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

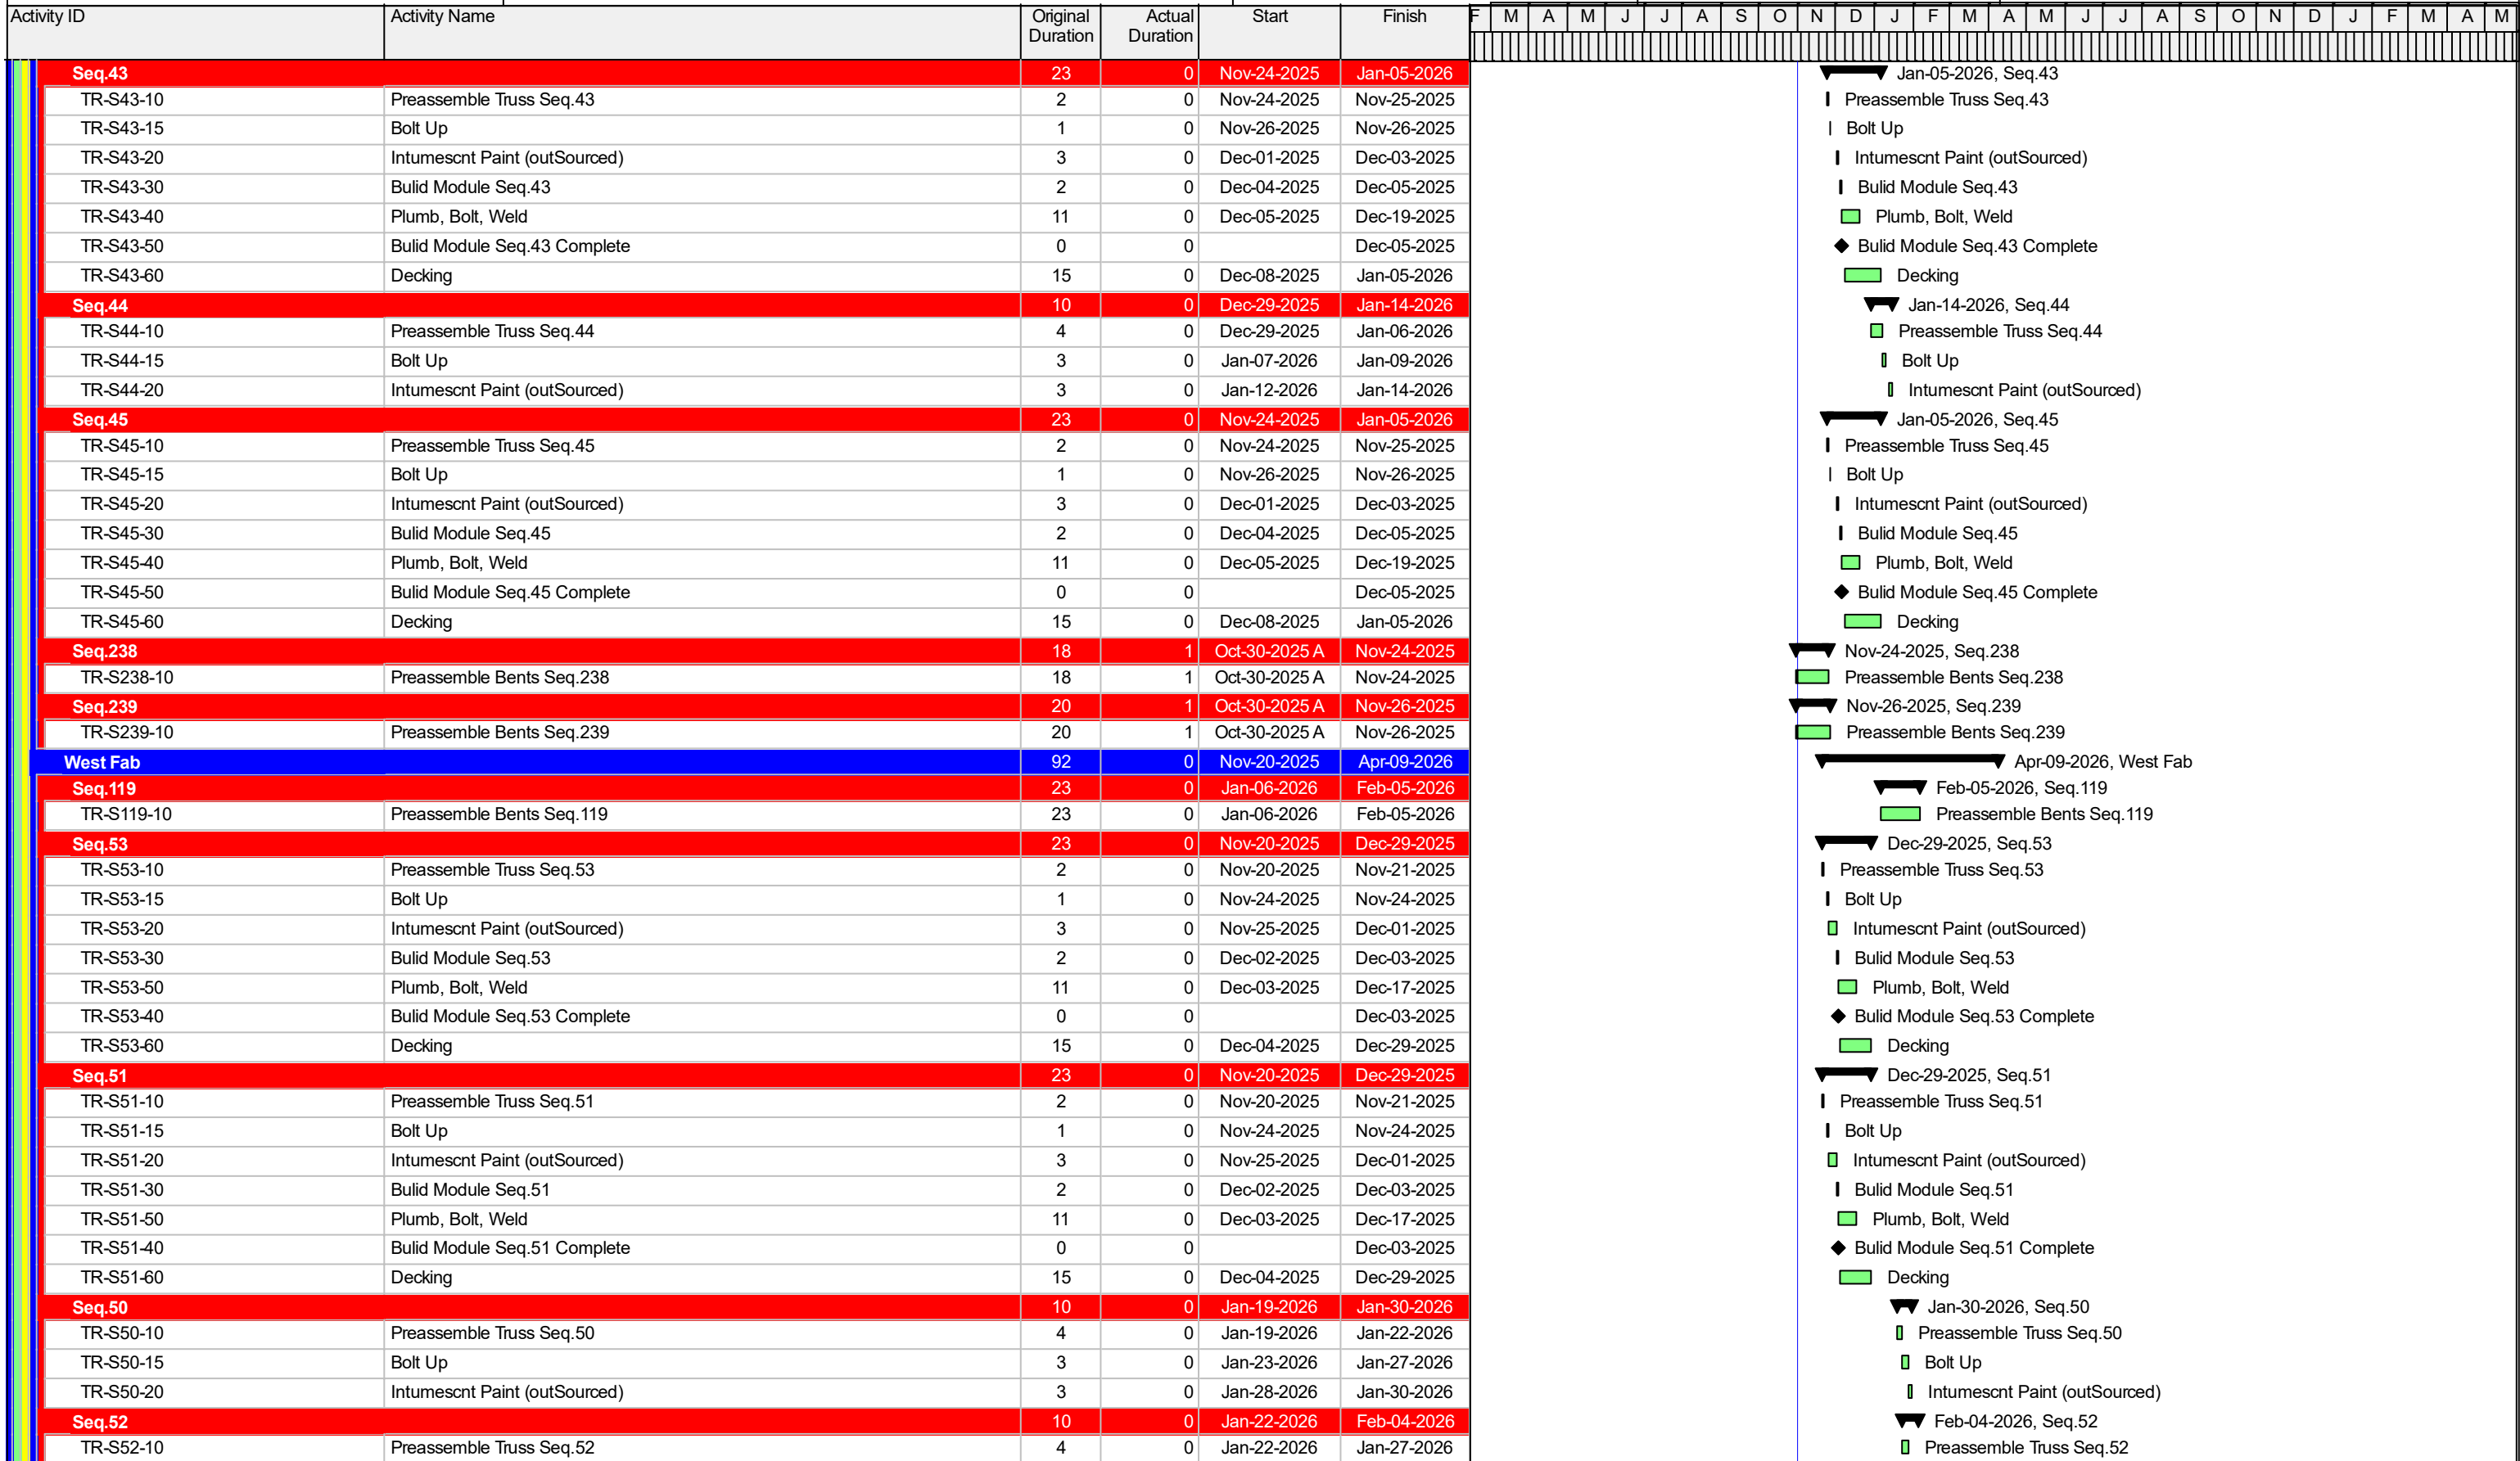

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 59 of 99
Data date : Oct-31-2025

Page 59 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 60 of 99
Data date : Oct-31-2025

Page 60 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 61 of 99
Data date : Oct-31-2025

Page 61 of 99

Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary




Activity ID		Activity Name	Original Duration	Actual Duration	Start	Finish	F M A M J J A S O N D J F M A M J J A S O N D J F M A M																												
TR-S73-30 TR-S73-50 TR-S73-40 TR-S73-60 Seq.74 TR-S74-10 TR-S74-15 TR-S74-20 Seq.75 TR-S75-10 TR-S75-15 TR-S75-20 TR-S75-30 TR-S75-50 TR-S75-40 TR-S75-60 Seq.538 TR-S538-10 Seq.539 TR-S539-10 East Crane 2 - East Crane 2 - East Annex Seq.200 Area1-Concrete Pour Con-S200-05 Seq.200 Area1 Con-S200-10 Con-S200-20 Con-S200-30 Con-S200-40 Con-S200-50 Seq.202 Area1 Con-S202-10 Con-S202-15 Con-S202-30 Con-S202-20 Con-S202-40 Con-S202-50 Seq.203 Area2-Concrete Pour Con-S203-05 Seq.203 Area2 Con-S203-10 Con-S203-15 Con-S203-20 Con-S203-30 Con-S203-40 Con-S203-50 Seq.204 Area2-Concrete Pour Con-S204-05	Bulid Module Seq.73	2	0	Mar-10-2026	Mar-11-2026	Bulid Module Seq.73																													
	TR-S73-50	Plumb, Bolt, Weld	11	0	Mar-11-2026	Mar-25-2026	█ Plumb, Bolt, Weld																												
	TR-S73-40	Bulid Module Seq.73 Complete	0	0		Mar-11-2026	◆ Bulid Module Seq.73 Complete																												
	TR-S73-60	Decking	15	0	Mar-12-2026	Apr-01-2026	█ Decking																												
	Seq.74			10	0	Mar-19-2026	Apr-01-2026	▼ Apr-01-2026, Seq.74																											
	TR-S74-10	Preassemble Truss Seq.74	4	0	Mar-19-2026	Mar-24-2026	█ Preassemble Truss Seq.74																												
	TR-S74-15	Bolt Up	3	0	Mar-25-2026	Mar-27-2026	█ Bolt Up																												
	TR-S74-20	Intumescent Paint (outsourced)	3	0	Mar-30-2026	Apr-01-2026	█ Intumescent Paint (outsourced)																												
	Seq.75			23	0	Mar-06-2026	Apr-07-2026	▼ Apr-07-2026, Seq.75																											
	TR-S75-10	Preassemble Truss Seq.75	2	0	Mar-06-2026	Mar-09-2026	█ Preassemble Truss Seq.75																												
	TR-S75-15	Bolt Up	1	0	Mar-10-2026	Mar-10-2026	Bolt Up																												
	TR-S75-20	Intumescent Paint (outsourced)	3	0	Mar-11-2026	Mar-13-2026	Intumescent Paint (outsourced)																												
	TR-S75-30	Bulid Module Seq.75	2	0	Mar-16-2026	Mar-17-2026	█ Bulid Module Seq.75																												
	TR-S75-50	Plumb, Bolt, Weld	11	0	Mar-17-2026	Mar-31-2026	█ Plumb, Bolt, Weld																												
	TR-S75-40	Bulid Module Seq.75 Complete	0	0		Mar-17-2026	◆ Bulid Module Seq.75 Complete																												
	TR-S75-60	Decking	15	0	Mar-18-2026	Apr-07-2026	█ Decking																												
	Seq.538			23	0	Jan-13-2026	Feb-12-2026	▼ Feb-12-2026, Seq.538																											
	TR-S538-10	Preassemble Bents Seq.538	23	0	Jan-13-2026	Feb-12-2026	█ Preassemble Bents Seq.538																												
	Seq.539			23	0	Jan-15-2026	Feb-17-2026	▼ Feb-17-2026, Seq.539																											
	TR-S539-10	Preassemble Bents Seq.539	23	0	Jan-15-2026	Feb-17-2026	█ Preassemble Bents Seq.539																												
	East			185	74	Jul-17-2025 A	May-01-2026	▼ May-01-2026, East																											
	Crane 2 - East			130	68	Jul-25-2025 A	Feb-13-2026	▼ Feb-13-2026, Crane 2 - East																											
	Crane 2 - East Annex			121	68	Jul-25-2025 A	Feb-02-2026	▼ Feb-02-2026, Crane 2 - East Annex																											
	Seq.200 Area1-Concrete Pour			0	0	Jul-25-2025 A	Jul-25-2025 A	▼ Jul-25-2025 A, Seq.200 Area1-Concrete Pour																											
	Con-S200-05	Crew A Pour A2 - LVL 10	0	0		Jul-25-2025 A	◆ Crew A Pour A2 - LVL 10																												
	Seq.200 Area1			32	22	Aug-26-2025 A	Sep-29-2025 A	▼ Sep-29-2025 A, Seq.200 Area1																											
	Con-S200-10	Erection Seq.200	4	4	Aug-26-2025 A	Aug-29-2025 A	█ Erection Seq.200																												
	Con-S200-20	Erection Seq.200 completed	0	0		Aug-29-2025 A	◆ Erection Seq.200 completed																												
	Con-S200-30	Plumb, Bolt, Weld Seq.200	13	13	Sep-02-2025 A	Sep-18-2025 A	█ Plumb, Bolt, Weld Seq.200																												
	Con-S200-40	Decking Seq.200	17	17	Sep-02-2025 A	Sep-25-2025 A	█ Decking Seq.200																												
	Con-S200-50	Turnover Seq.200	0	0	Sep-29-2025 A		◆ Turnover Seq.200																												
	Seq.202 Area1			24	22	Sep-18-2025 A	Oct-23-2025 A	▼ Oct-23-2025 A, Seq.202 Area1																											
	Con-S202-10	Erection Seq.202 - LVL 40	3	4	Sep-18-2025 A	Sep-24-2025 A	█ Erection Seq.202 - LVL 40																												
	Con-S202-15	Erection Seq.202 - LVL R1	2	2	Sep-29-2025 A	Sep-30-2025 A	Erection Seq.202 - LVL R1																												
	Con-S202-30	Plumb, Bolt, Weld Seq.202	15	15	Sep-30-2025 A	Oct-20-2025 A	█ Plumb, Bolt, Weld Seq.202																												
	Con-S202-20	Erection Seq.202 completed	0	0		Sep-30-2025 A	◆ Erection Seq.202 completed																												
	Con-S202-40	Decking Seq.202	15	15	Oct-01-2025 A	Oct-21-2025 A	█ Decking Seq.202																												
	Con-S202-50	Turnover Seq.202	0	0	Oct-23-2025 A		◆ Turnover Seq.202																												
	Seq.203 Area2-Concrete Pour			0	0	Aug-22-2025 A	Aug-22-2025 A	▼ Aug-22-2025 A, Seq.203 Area2-Concrete Pour																											
	Con-S203-05	Crew A Pour A4 - LVL 10	0	0		Aug-22-2025 A	◆ Crew A Pour A4 - LVL 10																												
	Seq.203 Area2			17	18	Sep-10-2025 A	Oct-08-2025 A	▼ Oct-08-2025 A, Seq.203 Area2																											
	Con-S203-10	Erection Seq.203 - LVL 20	2	2	Sep-10-2025 A																														

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 63 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

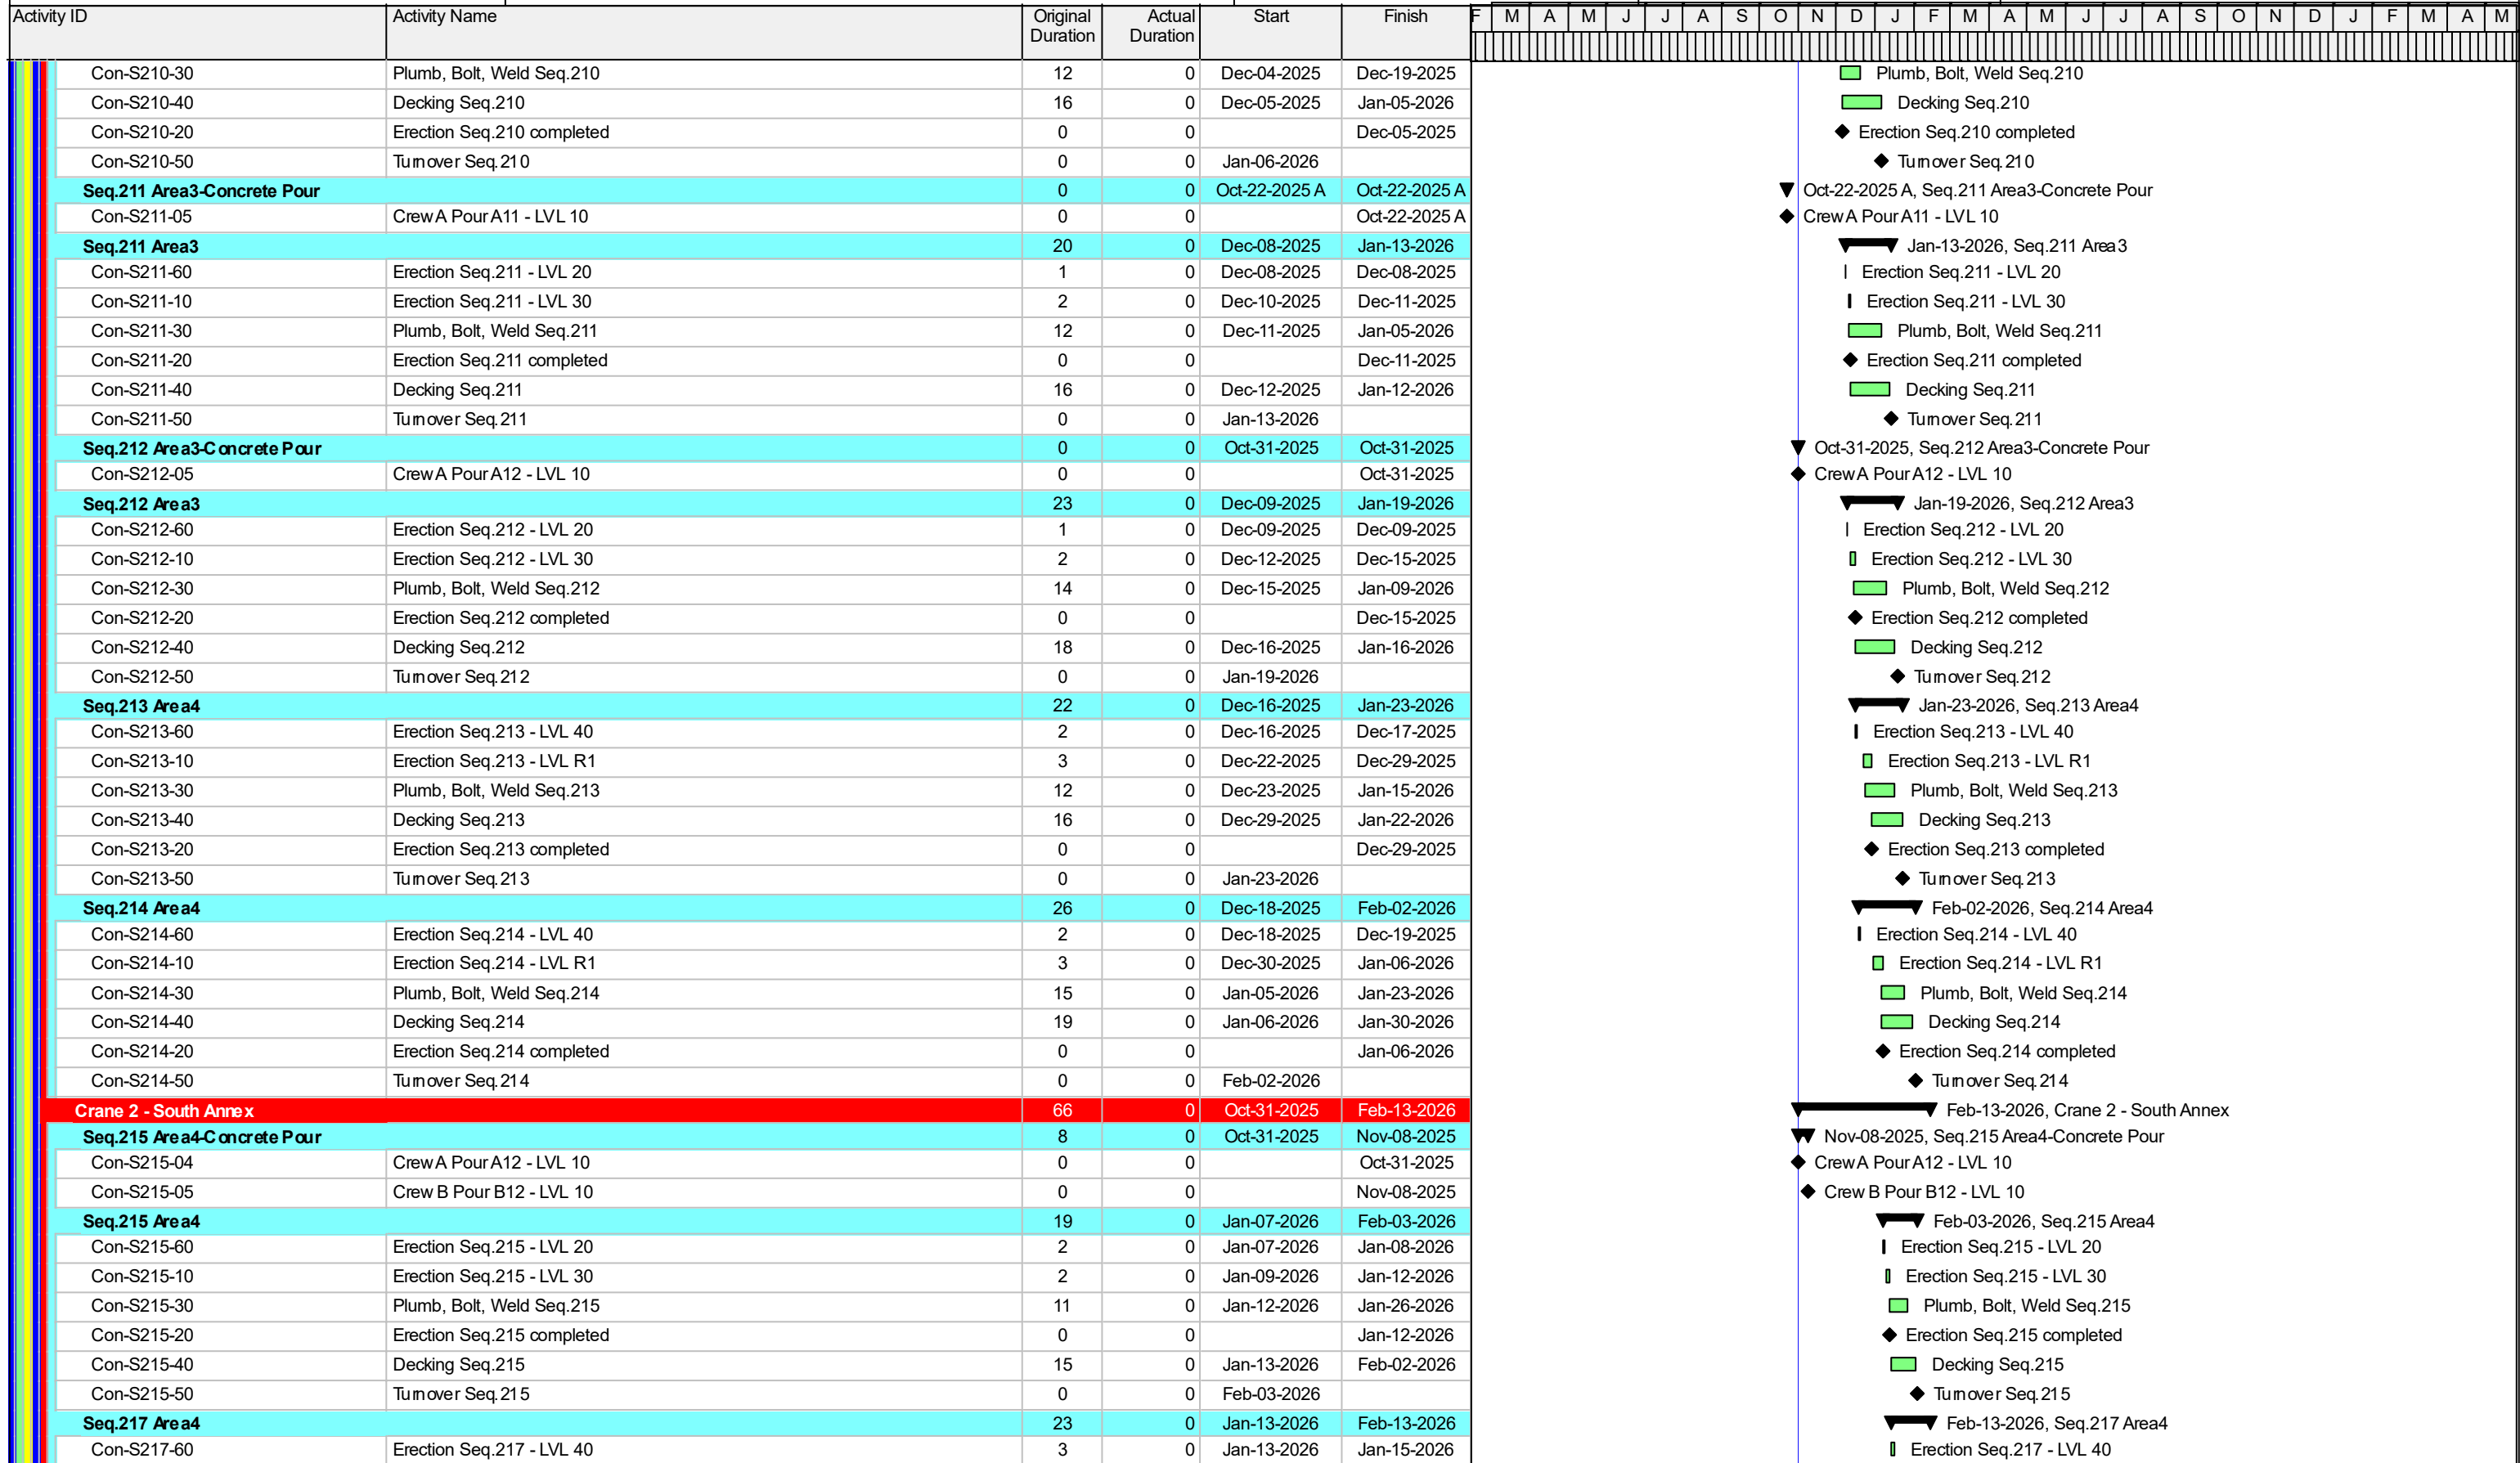

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 64 of 99
Data date : Oct-31-2025

Page 64 of 99

Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary



The Gantt chart displays the following tasks and milestones for the 10th floor construction:

- Apr-09-2026, Crane 1 - East** (Black bar)
- Apr-09-2026, Crane 1 - Center Annex** (Black bar)
- Aug-24-2025 A, Seq.100 Area1-Concrete Pour** (Downward arrow)
- Crew C Pour C2 - LVL 10** (Diamond)
- Oct-03-2025 A, Seq.100 Area1** (Downward arrow)
- Erection Seq.100** (Blue bar)
- Plumb, Bolt, Weld Seq.100** (Blue bar)
- Decking Seq.100** (Blue bar)
- Erection Seq.100 completed** (Diamond)
- Turnover Seq. 100** (Diamond)
- Nov-03-2025, Seq.102 Area1** (Downward arrow)
- Erection Seq.102 - LVL 40** (Blue bar)
- Erection Seq.102 - LVL R1** (Blue bar)
- Plumb, Bolt, Weld Seq.102** (Blue bar)
- Erection Seq.102 completed** (Diamond)
- Decking Seq.102** (Blue bar)
- Turnover Seq. 102** (Diamond)
- Sep-06-2025 A, Seq.103 Area2-Concrete Pour** (Downward arrow)
- Crew C Pour C4 - LVL 10** (Diamond)
- Nov-10-2025, Seq.103 Area2** (Downward arrow)
- Erection Seq.103 - LVL 20** (Blue bar)
- Erection Seq.103 - LVL 30** (Blue bar)
- Plumb, Bolt, Weld Seq.103** (Blue bar)
- Erection Seq.103 completed** (Diamond)
- Decking Seq.103** (Blue bar)
- Turnover Seq. 103** (Diamond)
- Dec-05-2025, Seq.106 Area2** (Downward arrow)
- Erection Seq.106 - LVL 40** (Blue bar)
- Erection Seq.106 - LVL R1** (Blue bar)
- Erection Seq.106 completed** (Diamond)
- Plumb, Bolt, Weld Seq.106** (Blue bar)
- Decking Seq.106** (Blue bar)
- Turnover Seq. 106** (Diamond)
- Dec-10-2025, Seq.107 Area2** (Downward arrow)
- Erection Seq.107 - LVL 40** (Blue bar)
- Erection Seq.107 - LVL R1** (Blue bar)
- Plumb, Bolt, Weld Seq.107** (Blue bar)
- Erection Seq.107 completed** (Diamond)
- Decking Seq.107** (Blue bar)
- Turnover Seq. 107** (Diamond)
- Oct-09-2025 A, Seq.108 Area3-Concrete Pour** (Downward arrow)
- Crew C Pour C8 - LVL 10** (Diamond)
- Dec-17-2025, Seq.108 Area3** (Downward arrow)
- Erection Seq.108 - LVL 20** (Blue bar)

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 65 of 99
Data date : Oct-31-2025

Page 65 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 66 of 99
Data date : Oct-31-2025

Page 66 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 67 of 99
Data date : Oct-31-2025

Page 67 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 68 of 99
Data date : Oct-31-2025

Page 68 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 69 of 99
Data date : Oct-31-2025

Page 69 of 99

Data date : Oct-31-2025



Activity ID		Activity Name	Original Duration	Actual Duration	Start	Finish																																																													
		Con-S20-40	Decking Seq.20	15	0	Dec-03-2025	Dec-23-2025																																																												
		Con-S20-50	Turnover Seq.20	0	0	Dec-29-2025																																																													
		Move Crane		1	0	Dec-03-2025	Dec-03-2025																																																												
		A1130	Move Crane	1	0	Dec-03-2025	Dec-03-2025																																																												
		Seq.26 Area 2		17	0	Dec-04-2025	Jan-06-2026																																																												
		Con-S26-10	Erection Seq.26	2	0	Dec-04-2025	Dec-05-2025																																																												
		Con-S26-20	Plumb, Bolt, Weld Seq.26	11	0	Dec-05-2025	Dec-19-2025																																																												
		Con-S26-15	Erection Seq.26 completed	0	0		Dec-05-2025																																																												
		Con-S26-40	Decking Seq.26	15	0	Dec-08-2025	Jan-05-2026																																																												
		Con-S26-60	Grating Seq 26	15	0	Dec-08-2025	Jan-05-2026																																																												
		Con-S26-50	Turnover Seq.26	0	0	Jan-06-2026																																																													
		Seq.25 Area 2		17	0	Dec-08-2025	Jan-08-2026																																																												
		Con-S25-10	Erection Seq.25	2	0	Dec-08-2025	Dec-09-2025																																																												
		Con-S25-15	Erection Seq.25 completed	0	0		Dec-09-2025																																																												
		Con-S25-20	Plumb, Bolt, Weld Seq.25	10	0	Dec-10-2025	Dec-23-2025																																																												
		Con-S25-40	Decking Seq.25	14	0	Dec-11-2025	Jan-07-2026																																																												
		Con-S25-70	Grating Seq 25	14	0	Dec-11-2025	Jan-07-2026																																																												
		Con-S25-50	Turnover Seq.25	0	0	Jan-08-2026																																																													
		Seq.105 Area2-Concrete Pour		0	3	Sep-24-2025 A	Sep-27-2025 A																																																												
		Con-S105-04	Crew A Pour A8 - LVL 10	0	0		Sep-24-2025 A																																																												
		Con-S105-05	Crew B Pour B8 - LVL 10	0	0		Sep-27-2025 A																																																												
		Seq.105 Area2		12	0	Dec-10-2025	Dec-30-2025																																																												
		Con-S105-10	Erection Seq.105	2	0	Dec-10-2025	Dec-11-2025																																																												
		Con-S105-20	Plumb, Bolt, Weld Seq.105	11	0	Dec-11-2025	Dec-30-2025																																																												
		Con-S105-15	Erection Seq.105 completed	0	0		Dec-11-2025																																																												
		Seq.29 Area 2		17	0	Dec-12-2025	Jan-14-2026																																																												
		Con-S29-10	Erection Seq.29	2	0	Dec-12-2025	Dec-15-2025																																																												
		Con-S29-20	Plumb, Bolt, Weld Seq.29	11	0	Dec-15-2025	Jan-06-2026																																																												
		Con-S29-15	Erection Seq.29 completed	0	0		Dec-15-2025																																																												
		Con-S29-40	Decking Seq.29	15	0	Dec-16-2025	Jan-13-2026																																																												
		Con-S29-45	Grating Seq.29	15	0	Dec-16-2025	Jan-13-2026																																																												
		Con-S29-50	Turnover Seq.29	0	0	Jan-14-2026																																																													
		Seq.28 Area 2		17	0	Dec-16-2025	Jan-16-2026																																																												
		Con-S28-10	Erection Seq.28	2	0	Dec-16-2025	Dec-17-2025																																																												
		Con-S28-20	Plumb, Bolt, Weld Seq.28	11	0	Dec-17-2025	Jan-08-2026																																																												
		Con-S28-15	Erection Seq.28 completed	0	0		Dec-17-2025																																																												
		Con-S28-40	Decking Seq.28	15	0	Dec-18-2025	Jan-15-2026																																																												
		Con-S28-45	Grating Seq.28	15	0	Dec-18-2025	Jan-15-2026																																																												
		Con-S28-50	Turnover Seq.28	0	0	Jan-16-2026																																																													
		Seq.31 Area 2		17	0	Dec-18-2025	Jan-20-2026																																																												
		Con-S31-10	Erection Seq.31	2	0	Dec-18-2025	Dec-19-2025																																																												
		Con-S31-20	Plumb, Bolt, Weld Seq.31	11	0	Dec-19-2025	Jan-12-2026																																																												
		Con-S31-15	Erection Seq.31 completed	0	0		Dec-19-2025																																																												
		Con-S31-40	Decking Seq.31	15	0	Dec-22-2025	Jan-19-2026																																																												
		Con-S31-45	Grating Seq.31	15	0	Dec-22-2025	Jan-19-2026																																																												
		Con-S31-50	Turnover Seq.31	0	0	Jan-20-2026																																																													
		Seq.30 Area 2		17	0	Dec-22-2025	Jan-22-2026																																																												
		Con-S30-10	Erection Seq.30	2	0	Dec-22-2025	Dec-23-2025																																																												
		Con-S30-20	Plumb, Bolt, Weld Seq.30	11	0	Dec-23-2025	Jan-14-2026																																																												

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 70 of 99
Data date : Oct-31-2025

Page 70 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 71 of 99
Data date : Oct-31-2025

Page 71 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



A DBM GLOBAL COMPANY

TSMC FAB3 Preliminary Schedule

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary



Activity ID	Activity Name	Original Duration	Actual Duration	Start	Finish	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M
Con-S44-45	Grating Seq.44	15	0	Feb-10-2026	Mar-03-2026																												
Con-S44-50	Turnover Seq. 44	0	0	Mar-04-2026																													
Crane 4 - East		177	26	Jul-17-2025 A	Apr-21-2026																												
Crane 4 - Center Annex		75	0	Aug-24-2025 A	Dec-18-2025																												
Seq.118 Area5-Concrete Pour		0	0	Aug-24-2025 A	Aug-24-2025 A																												
Con-S118-05	Crew C Pour C2 - LVL 10	0	0		Aug-24-2025 A																												
Seq.118 Area5		19	0	Nov-10-2025	Dec-09-2025																												
Con-S118-10	Erection Seq.118	3	0	Nov-10-2025*	Nov-12-2025																												
Con-S118-30	Plumb, Bolt, Weld Seq.118	13	0	Nov-11-2025	Dec-01-2025																												
Con-S118-40	Decking Seq.118	17	0	Nov-12-2025	Dec-08-2025																												
Con-S118-20	Erection Seq.118 completed	0	0		Nov-12-2025																												
Con-S118-50	Turnover Seq. 118	0	0	Dec-09-2025																													
Seq.120 Area5		23	0	Nov-13-2025	Dec-18-2025																												
Con-S120-10	Erection Seq.120	8	0	Nov-13-2025	Nov-24-2025																												
Con-S120-30	Plumb, Bolt, Weld Seq.120	17	0	Nov-14-2025	Dec-10-2025																												
Con-S120-40	Decking Seq.120	21	0	Nov-17-2025	Dec-17-2025																												
Con-S120-20	Erection Seq.120 completed	0	0		Nov-24-2025																												
Con-S120-50	Turnover Seq. 120	0	0	Dec-18-2025																													
Crane 4 - East Fab		177	17	Jul-17-2025 A	Apr-21-2026																												
Seq.238 Area1-Concrete Pour		18	25	Jul-17-2025 A	Aug-12-2025 A																												
Con-S238-03	Crew A Pour A1 - LVL 10	0	0		Jul-17-2025 A																												
Con-S238-04	Crew B Pour B1 - LVL 10	0	0		Jul-30-2025 A																												
Con-S238-05	Crew C Pour C1 - LVL 10	0	0		Aug-12-2025 A																												
Seq.238 Area1		12	0	Nov-25-2025	Dec-12-2025																												
Con-S238-10	Erection Seq.238	2	0	Nov-25-2025	Nov-26-2025																												
Con-S238-30	Plumb, Bolt, Weld Seq.238	11	0	Nov-26-2025	Dec-12-2025																												
Con-S238-20	Erection Seq.238 completed	0	0		Nov-26-2025																												
Seq.239 Area1-Concrete Pour		18	25	Jul-17-2025 A	Aug-12-2025 A																												
Con-S239-03	Crew A Pour A1 - LVL 10	0	0		Jul-17-2025 A																												
Con-S239-04	Crew B Pour B1 - LVL 10	0	0		Jul-30-2025 A																												
Con-S239-05	Crew C Pour C1 - LVL 10	0	0		Aug-12-2025 A																												
Seq.239 Area1		12	0	Dec-01-2025	Dec-16-2025																												
Con-S239-10	Erection Seq.239	1	0	Dec-01-2025	Dec-01-2025																												
Con-S239-20	Erection Seq.239 completed	0	0		Dec-01-2025																												
Con-S239-30	Plumb, Bolt, Weld Seq.239	11	0	Dec-02-2025	Dec-16-2025																												
Seq.241 Area1-Concrete Pour		0	0	Jan-10-2026	Jan-10-2026																												
Con-S241-60	Crew D Pour D1 - LVL 20	0	0	Jan-10-2026																													
Seq.241 Area1		17	0	Dec-02-2025	Dec-30-2025																												
Con-S241-10	Erection Seq.241	2	0	Dec-02-2025	Dec-03-2025																												
Con-S241-30	Plumb, Bolt, Weld Seq.241	11	0	Dec-03-2025	Dec-17-2025																												
Con-S241-20	Erection Seq.241 completed	0	0		Dec-03-2025																												
Con-S241-40	Decking Seq.241	15	0	Dec-04-2025	Dec-29-2025																												
Con-S241-50	Turnover Seq. 241	0	0	Dec-30-2025																													
Seq.243 Area1-Concrete Pour		0	0	Jan-23-2026	Jan-23-2026																												
Con-S243-60	Crew D Pour D2 - LVL 20	0	0	Jan-23-2026																													
Seq.243 Area1		17	0	Dec-04-2025	Jan-06-2026																												
Con-S243-10	Erection Seq.243	2	0	Dec-04-2025	Dec-05-2025																												
Con-S243-30	Plumb, Bolt, Weld Seq.243	11	0	Dec-05-2025	Dec-19-2025																												
Con-S243-20	Erection Seq.243 completed	0	0		Dec-05-2025																												

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 73 of 99
Data date : Oct-31-2025

Page 73 of 99

Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 74 of 99
Data date : Oct-31-2025

Page 74 of 99

Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 76 of 99
Data date : Oct-31-2025

Page 76 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 77 of 99
Data date : Oct-31-2025

Page 77 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 80 of 99
Data date : Oct-31-2025

Page 80 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

[illegible]

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 82 of 99
Data date : Oct-31-2025

Page 82 of 99

Data date : Oct-31-2025




INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 84 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

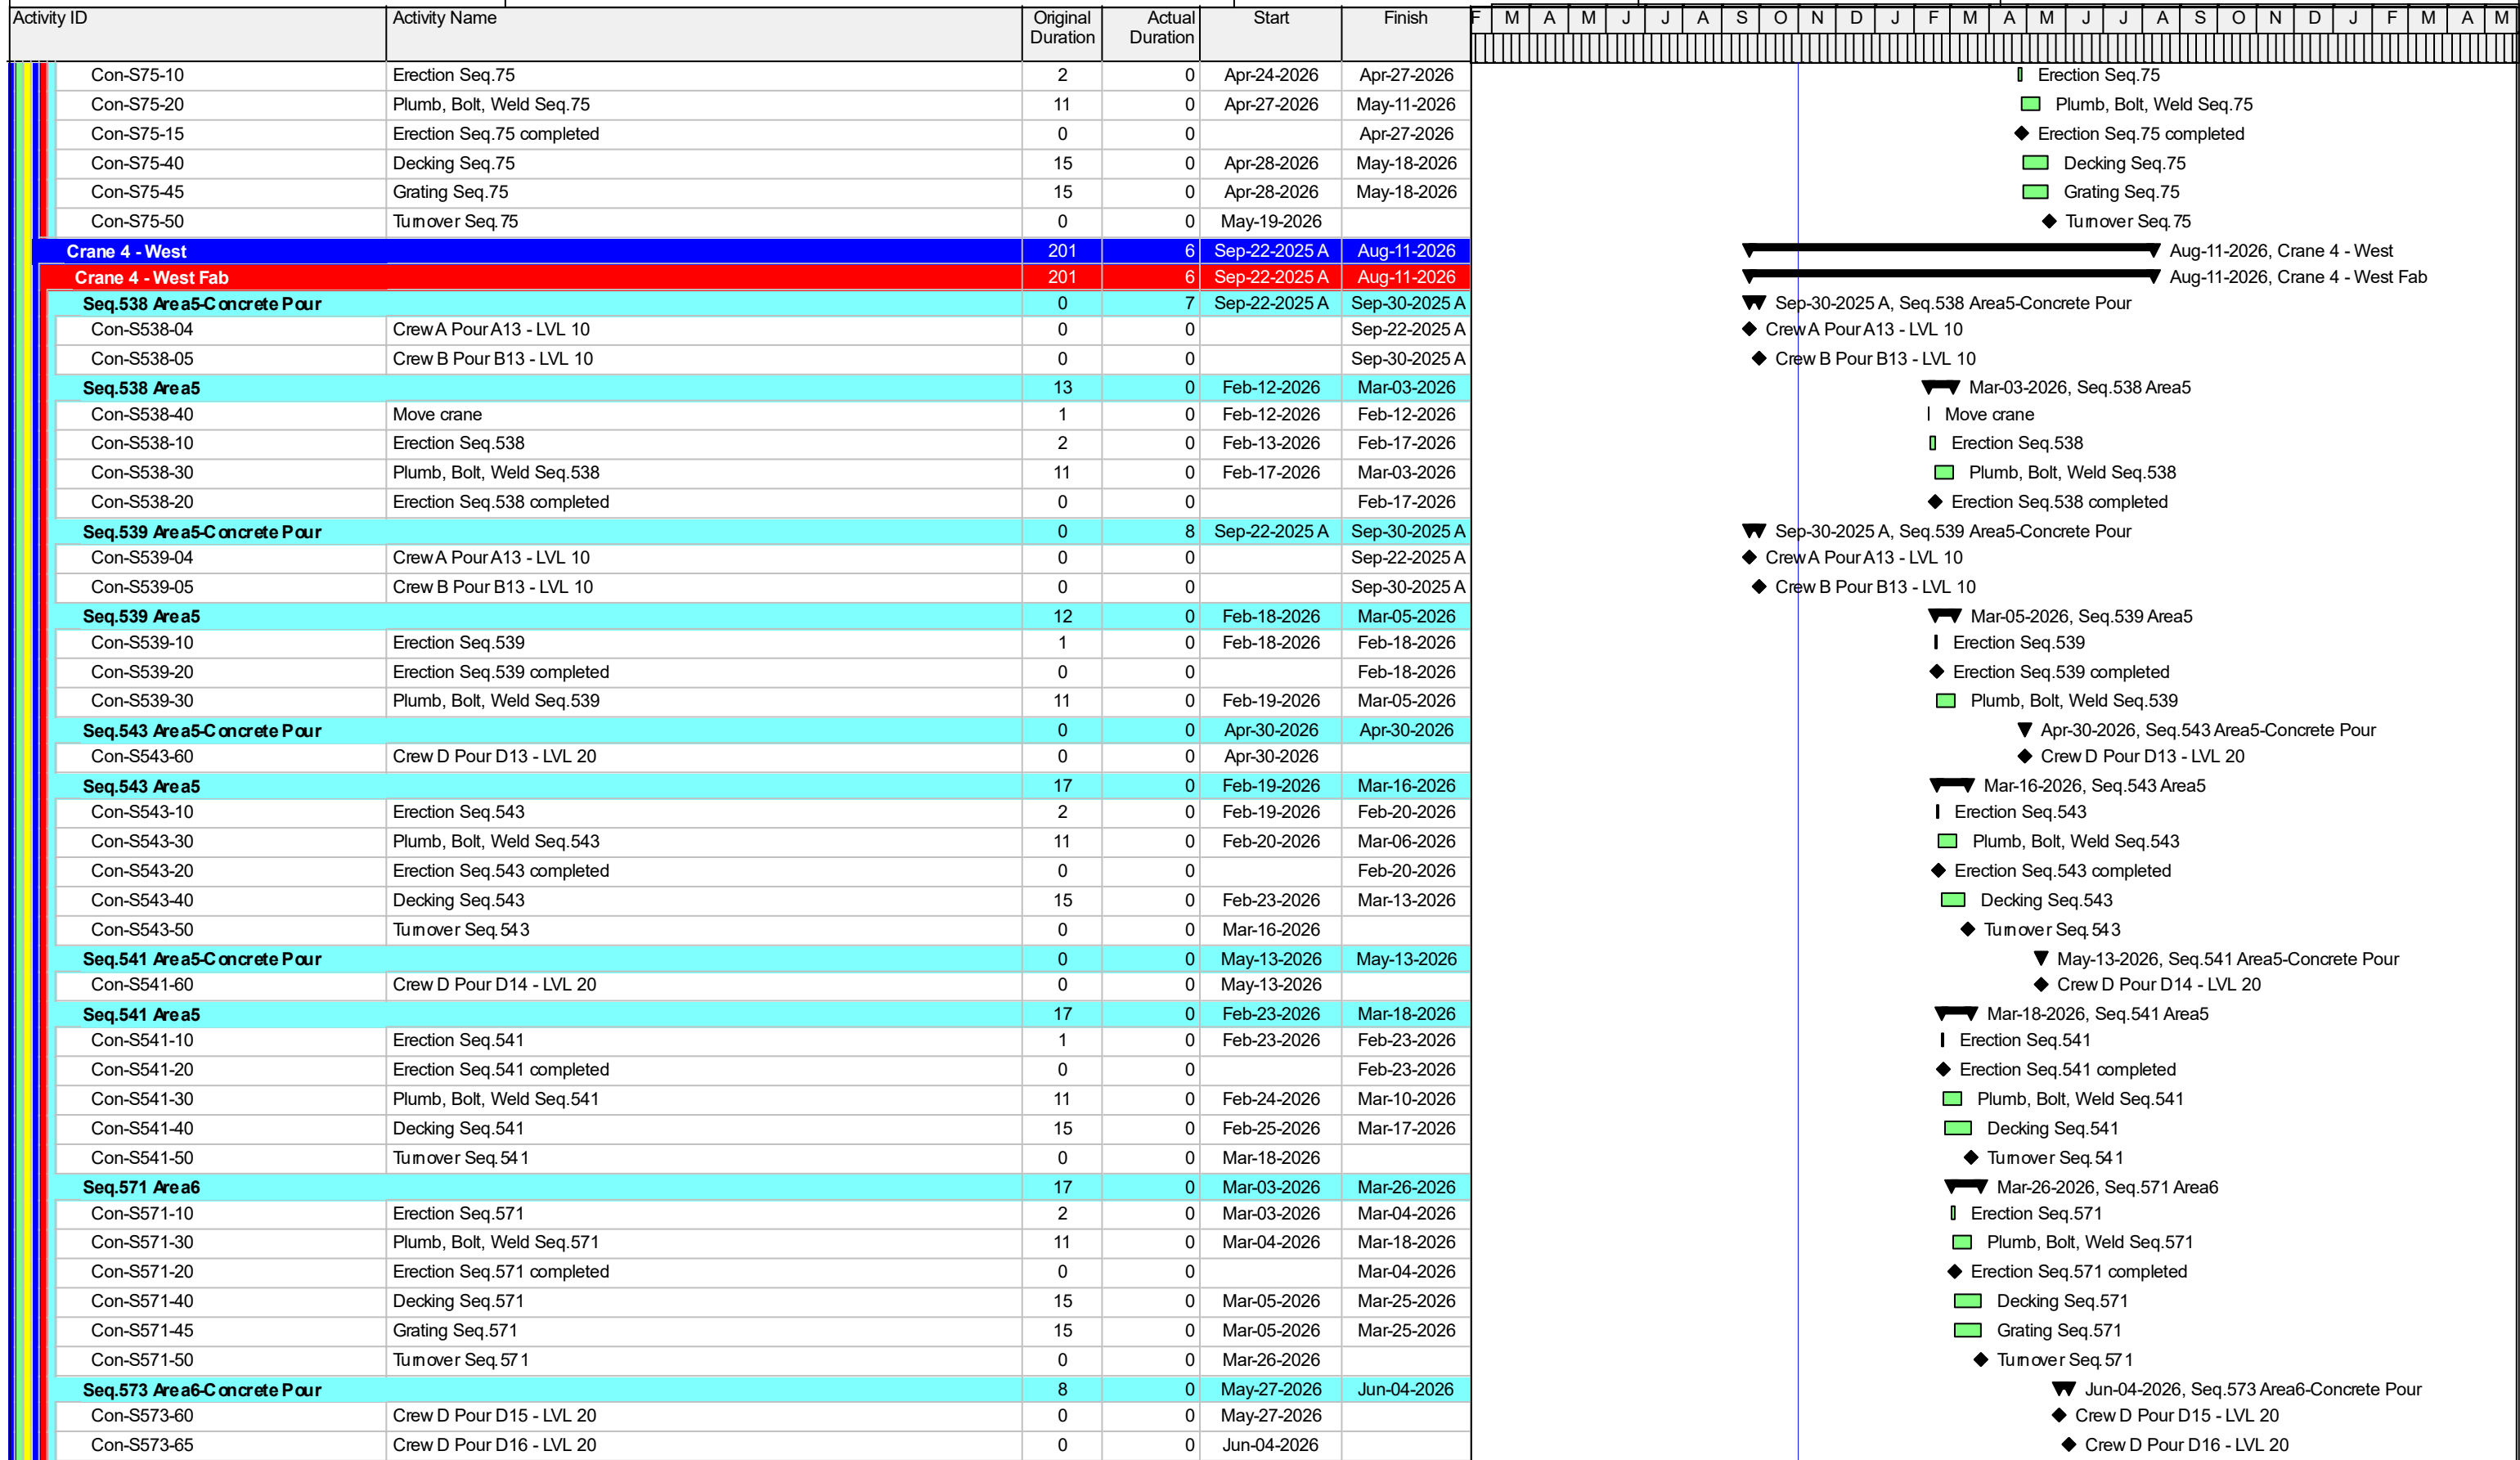

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 86 of 99
Data date : Oct-31-2025

Page 86 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.

S S SCHUFF STEEL A DBM GLOBAL COMPANY		TSMC FAB3 Preliminary Schedule				Page 87 of 99 Data date : Oct-31-2025		Actual Work Remaining Work Critical Remaining Work ◆ Milestone Summary		HSE PROJECT CONTROLS CONSULTANTS																							
Activity ID	Activity Name	Original Duration	Actual Duration	Start	Finish	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M
	Con-S540-65	Crew E Pour E14 - LVL 20	0	0	May-26-2026																												
	Seq.540 Area5		18	0	Mar-02-2026	Mar-26-2026																											
	Con-S540-10	Erection Seq.540	2	0	Mar-02-2026	Mar-03-2026																											
	Con-S540-30	Plumb, Bolt, Weld Seq.540	12	0	Mar-03-2026	Mar-18-2026																											
	Con-S540-20	Erection Seq.540 completed	0	0		Mar-03-2026																											
	Con-S540-40	Decking Seq.540	16	0	Mar-04-2026	Mar-25-2026																											
	Con-S540-50	Turnover Seq.540	0	0	Mar-26-2026																												
	Seq.570 Area6		18	0	Mar-05-2026	Mar-31-2026																											
	Con-S570-10	Erection Seq.570	2	0	Mar-05-2026	Mar-06-2026																											
	Con-S570-20	Erection Seq.570 completed	0	0		Mar-06-2026																											
	Con-S570-30	Plumb, Bolt, Weld Seq.570	12	0	Mar-09-2026	Mar-24-2026																											
	Con-S570-40	Decking Seq.570	16	0	Mar-09-2026	Mar-30-2026																											
	Con-S570-45	Grating Seq.570	16	0	Mar-09-2026	Mar-30-2026																											
	Con-S570-50	Turnover Seq.570	0	0	Mar-31-2026																												
	Seq.572 Area6-Concrete Pour		19	0	May-27-2026	Jun-15-2026																											
	Con-S572-60	Crew D Pour D15 - LVL 20	0	0	May-27-2026																												
	Con-S572-65	Crew D Pour D16 - LVL 20	0	0	Jun-04-2026																												
	Con-S572-70	Crew E Pour E15 - LVL 20	0	0	Jun-06-2026																												
	Con-S572-75	Crew E Pour E16 - LVL 20	0	0	Jun-15-2026																												
	Seq.572 Area6		18	0	Mar-13-2026	Apr-08-2026																											
	Con-S572-10	Erection Seq.572	2	0	Mar-13-2026	Mar-16-2026																											
	Con-S572-30	Plumb, Bolt, Weld Seq.572	12	0	Mar-16-2026	Mar-31-2026																											
	Con-S572-20	Erection Seq.572 completed	0	0		Mar-16-2026																											
	Con-S572-40	Decking Seq.572	16	0	Mar-17-2026	Apr-07-2026																											
	Con-S572-45	Grating Seq.572	16	0	Mar-17-2026	Apr-07-2026																											
	Con-S572-50	Turnover Seq.572	0	0	Apr-08-2026																												
	Seq.574 Area6		18	0	Mar-19-2026	Apr-14-2026																											
	Con-S574-10	Erection Seq.574	2	0	Mar-19-2026	Mar-20-2026																											
	Con-S574-30	Plumb, Bolt, Weld Seq.574	12	0	Mar-20-2026	Apr-06-2026																											
	Con-S574-20	Erection Seq.574 completed	0	0		Mar-20-2026																											
	Con-S574-40	Decking Seq.574	16	0	Mar-23-2026	Apr-13-2026																											
	Con-S574-45	Grating Seq.574	16	0	Mar-23-2026	Apr-13-2026																											
	Con-S574-50	Turnover Seq.574	0	0	Apr-14-2026																												
	Seq.640 Area6-Concrete Pour		11	0	Jun-12-2026	Jun-23-2026																											
	Con-S640-60	Crew D Pour D17 - LVL 20	0	0	Jun-12-2026																												
	Con-S640-65	Crew E Pour E17 - LVL 20	0	0	Jun-23-2026																												
	Seq.640 Area6		18	0	Mar-26-2026	Apr-21-2026																											
	Con-S640-10	Erection Seq.640	2	0	Mar-26-2026	Mar-27-2026																											
	Con-S640-30	Plumb, Bolt, Weld Seq.640	12	0	Mar-27-2026	Apr-13-2026																											
	Con-S640-20	Erection Seq.640 completed	0	0		Mar-27-2026																											
	Con-S640-40	Decking Seq.640	16	0	Mar-30-2026	Apr-20-2026																											
	Con-S640-45	Grating Seq.640	16	0	Mar-30-2026	Apr-20-2026																											
	Con-S640-50	Turnover Seq.640	0	0	Apr-21-2026																												
	Seq.642 Area7-Concrete Pour		20	0	Jun-20-2026	Jul-10-2026																											
	Con-S642-60	Crew D Pour D18 - LVL 20	0	0	Jun-20-2026																												
	Con-S642-65	Crew D Pour D19 - LVL 20	0	0	Jun-29-2026																												
	Con-S642-70	Crew E Pour E18 - LVL 20	0	0	Jul-01-2026																												
	Con-S642-75	Crew E Pour E19 - LVL 20	0	0	Jul-10-2026																												
	Seq.642 Area7		18	0	Apr-01-2026	Apr-27-2026																											

Actual Work

Remaining Work

Critical Remaining Work

◆ Milestone

Summary

HSE

PROJECT CONTROLS CONSULTANTS

INFORMATION MILESTONE

is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In forFabrication),and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the informationmilestone date is onlyused to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to theinformation milestone date will beevaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 88 of 99
Data date : Oct-31-2025

Page 88 of 99

Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 89 of 99
Data date : Oct-31-2025

Page 89 of 99

Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary




Activity ID		Activity Name		Original Duration	Actual Duration	Start	Finish	F M A M J J A S O N D J F M A M J J A S O N D J F M A M																											
1	Seq.716 Area8			17	0	May-04-2026	May-28-2026																												
	Con-S716-10	Erection Seq.716	2	0	May-04-2026	May-05-2026																													
	Con-S716-30	Plumb, Bolt, Weld Seq.716	13	0	May-05-2026	May-21-2026																													
	Con-S716-20	Erection Seq.716 completed	0	0		May-05-2026																													
	Con-S716-40	Decking Seq.716	15	0	May-06-2026	May-27-2026																													
	Con-S716-45	Grating Seq.716	15	0	May-06-2026	May-27-2026																													
	Con-S716-50	Turnover Seq.716	0	0	May-28-2026																														
	Crane 1 - South Annex			92	0	Jan-14-2026	May-27-2026																												
	Seq.416 Area8-Concrete Pour			0	0	Jan-14-2026	Jan-14-2026																												
	Con-S416-05	Crew B Pour B24 - LVL 10	0	0		Jan-14-2026																													
	Seq.416 Area8			17	0	Apr-28-2026	May-21-2026																												
	Con-S416-10	Erection Seq.416	2	0	Apr-28-2026	Apr-29-2026																													
	Con-S416-30	Plumb, Bolt, Weld Seq.416	11	0	Apr-29-2026	May-13-2026																													
	Con-S416-20	Erection Seq.416 completed	0	0		Apr-29-2026																													
	Con-S416-40	Decking Seq.416	15	0	Apr-30-2026	May-20-2026																													
	Con-S416-50	Turnover Seq.416	0	0	May-21-2026																														
	Seq.418 Area8			18	0	Apr-30-2026	May-27-2026																												
	Con-S418-10	Erection Seq.418	2	0	Apr-30-2026	May-01-2026																													
	Con-S418-30	Plumb, Bolt, Weld Seq.418	12	0	May-01-2026	May-18-2026																													
	Con-S418-20	Erection Seq.418 completed	0	0		May-01-2026																													
	Con-S418-40	Decking Seq.418	16	0	May-04-2026	May-26-2026																													
	Con-S418-50	Turnover Seq.418	0	0	May-27-2026																														
	2nd Path - Crane (TBD)			280	0	Dec-08-2025	Jan-26-2027																												
	Seq.102 Area1-1			14	0	Jan-06-2026	Jan-26-2026																												
	Con-S102.1-60	Erection Seq.102.1 - North Facade	4	0	Jan-06-2026	Jan-09-2026																													
	Con-S102.1-100	Erection Seq.102.1 completed	0	0		Jan-09-2026																													
	Con-S102.1-70	Plumb, Bolt, Weld Seq.102.1	10	0	Jan-12-2026	Jan-23-2026																													
	Con-S102.1-80	Turnover Seq.102.1	0	0	Jan-26-2026																														
	Seq.104 Area2-2			13	0	Mar-20-2026	Apr-08-2026																												
	Con-S104.2-60	Erection Seq.104.2 - Elevator Steel	3	0	Mar-20-2026*	Mar-24-2026																													
	Con-S104.2-100	Erection Seq.104.2 completed	0	0		Mar-24-2026																													
	Con-S104.2-70	Plumb, Bolt, Weld Seq.104.2	10	0	Mar-25-2026	Apr-07-2026																													
	Con-S104.2-80	Turnover Seq.104.2	0	0	Apr-08-2026																														
	Seq.107 Area2-2			13	0	Mar-25-2026	Apr-13-2026																												
	Con-S107.2-120	Erection Seq.107.2 - Elevator Steel	3	0	Mar-25-2026	Mar-27-2026																													
	Con-S107.2-110	Erection Seq.107.2 completed	0	0		Mar-27-2026																													
	Con-S107.2-80	Plumb, Bolt, Weld Seq.107.2	10	0	Mar-30-2026	Apr-10-2026																													
	Con-S107.2-90	Turnover Seq.107.2	0	0	Apr-13-2026																														
	Seq.109 Area3-2			13	0	Apr-22-2026	May-11-2026																												
	Con-S109.2-120	Erection Seq.109.2 - Elevator Steel	3	0	Apr-22-2026*	Apr-24-2026																													
	Con-S109.2-110	Erection Seq.109.2 completed	0	0		Apr-24-2026																													
	Con-S109.2-80	Plumb, Bolt, Weld Seq.109.2	10	0	Apr-27-2026	May-08-2026																													
	Con-S109.2-90	Turnover Seq.109.2	0	0	May-11-2026																														
	Seq.112 Area3-2			13	0	Apr-27-2026	May-14-2026																												
	Con-S112.2-120	Erection Seq.112.2 - Elevator Steel	3	0	Apr-27-2026	Apr-29-2026																													
	Con-S112.2-110	Erection Seq.112.2 completed	0	0		Apr-29-2026																													
	Con-S112.2-80	Plumb, Bolt, Weld Seq.112.2	10	0	Apr-30-2026	May-13-2026																													
	Con-S112.2-90	Turnover Seq.112.2	0	0	May-14-2026																														
	Seq.114 Area4-2			13	0	Jul-14-2026	Jul-31-2026																												

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 90 of 99
Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

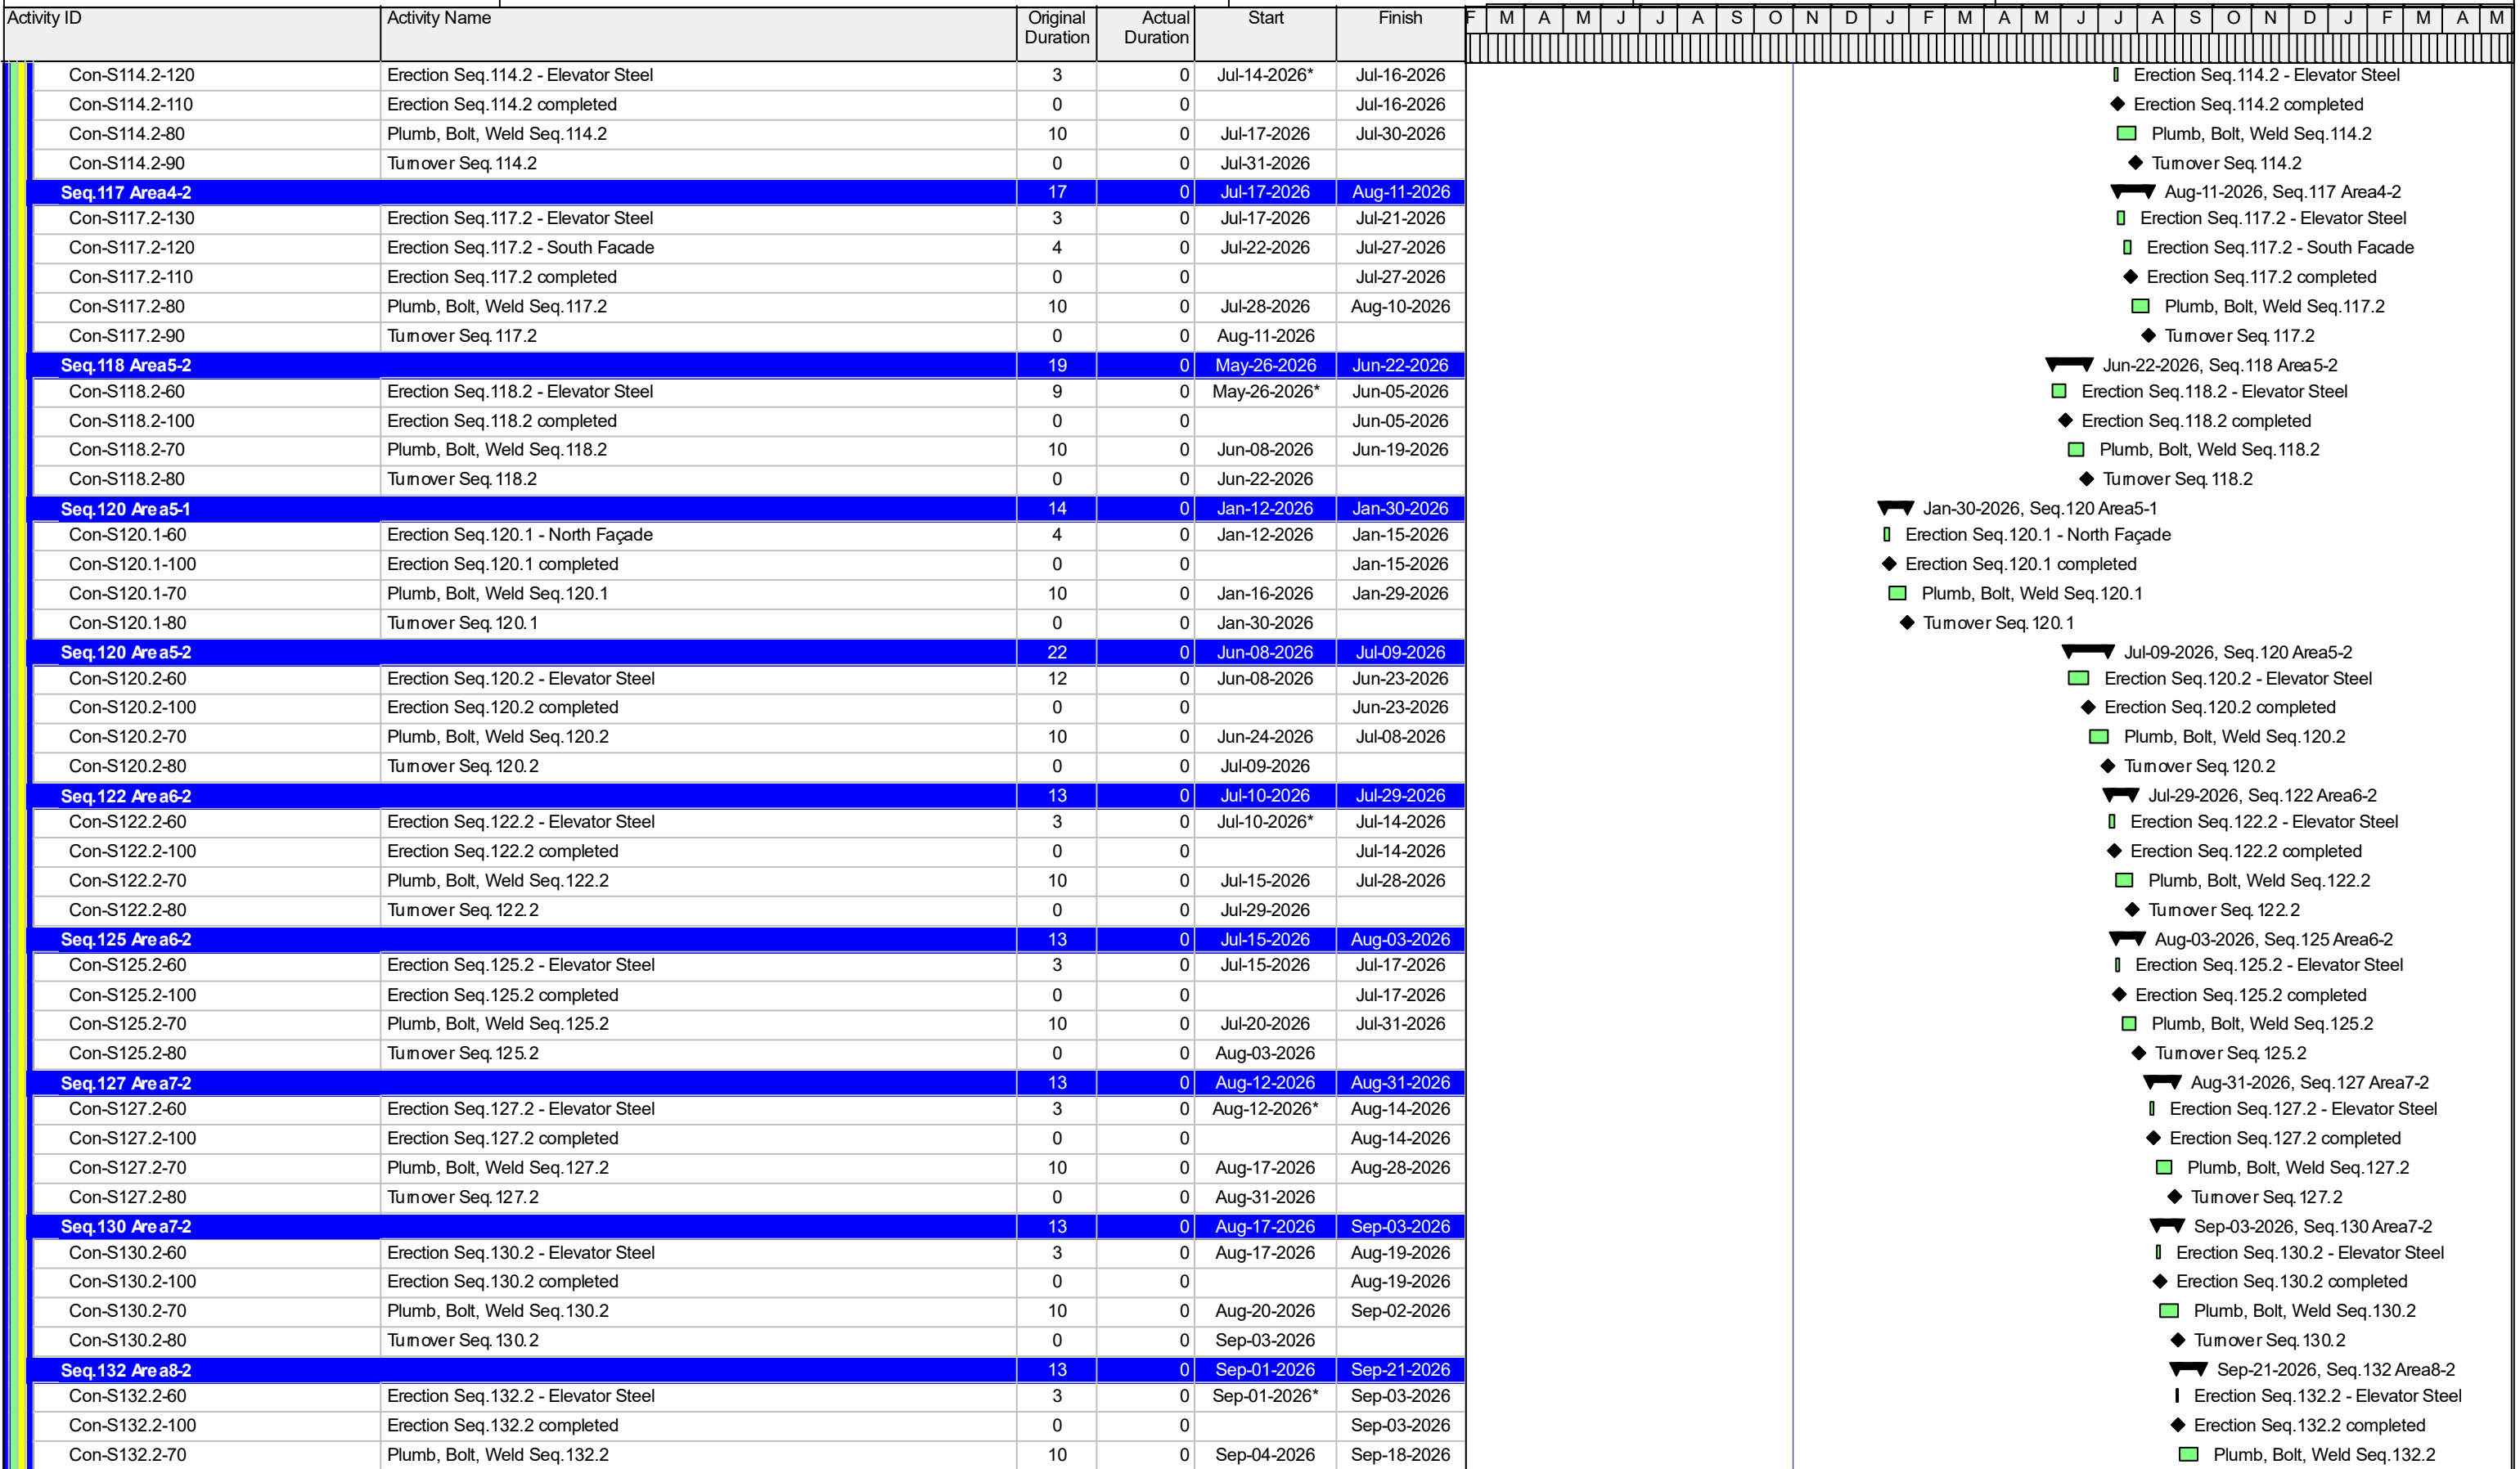

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 91 of 99
Data date : Oct-31-2025

Page 91 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.

S S SCHUFF STEEL A DBM GLOBAL COMPANY		TSMC FAB3 Preliminary Schedule				Page 92 of 99 Data date : Oct-31-2025		Actual Work Remaining Work Critical Remaining Work ◆ Milestone Summary		HSE PROJECT CONTROLS CONSULTANTS																								
Activity ID	Activity Name	Original Duration	Actual Duration	Start	Finish	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	
	Con-S207.1-110	Erection Seq.207.1 completed	0	0		Dec-23-2025																												
	Con-S207.1-80	Plumb, Bolt, Weld Seq.207.1	10	0	Dec-29-2025	Jan-14-2026																												
	Con-S207.1-90	Turnover Seq. 207.1	0	0	Jan-15-2026																													
	Seq.207 Area3-2		11	0	Mar-26-2026	Apr-10-2026																												
	Con-S207.2-160	Erection Seq.207.2 - Louvers	1	0	Mar-26-2026*	Mar-26-2026																												
	Con-S207.2-150	Erection Seq.207.2 completed	0	0		Mar-26-2026																												
	Con-S207.2-130	Plumb, Bolt, Weld Seq.207.2	10	0	Mar-27-2026	Apr-09-2026																												
	Con-S207.2-140	Turnover Seq. 207.2	0	0	Apr-10-2026																													
	Seq.208 Area3-1		11	0	Jan-05-2026	Jan-20-2026																												
	Con-S208.1-120	Erection Seq.208.1 - Canopy	1	0	Jan-05-2026	Jan-05-2026																												
	Con-S208.1-110	Erection Seq.208.1 completed	0	0		Jan-05-2026																												
	Con-S208.1-80	Plumb, Bolt, Weld Seq.208.1	10	0	Jan-06-2026	Jan-19-2026																												
	Con-S208.1-90	Turnover Seq. 208.1	0	0	Jan-20-2026																													
	Seq.208 Area3-2		11	0	Apr-13-2026	Apr-28-2026																												
	Con-S208.2-160	Erection Seq.208.2 - Blast Room	1	0	Apr-13-2026*	Apr-13-2026																												
	Con-S208.2-150	Erection Seq.208.2 completed	0	0		Apr-13-2026																												
	Con-S208.2-130	Plumb, Bolt, Weld Seq.208.2	10	0	Apr-14-2026	Apr-27-2026																												
	Con-S208.2-140	Turnover Seq. 208.2	0	0	Apr-28-2026																													
	Seq.209 Area3-1		12	0	Dec-29-2025	Jan-19-2026																												
	Con-S209.1-120	Erection Seq.209.1 - East Facade	2	0	Dec-29-2025	Dec-30-2025																												
	Con-S209.1-110	Erection Seq.209.1 completed	0	0		Dec-30-2025																												
	Con-S209.1-80	Plumb, Bolt, Weld Seq.209.1	10	0	Jan-05-2026	Jan-16-2026																												
	Con-S209.1-90	Turnover Seq. 209.1	0	0	Jan-19-2026																													
	Seq.210 Area3-1		12	0	Jan-06-2026	Jan-22-2026																												
	Con-S210.1-120	Erection Seq.210.1 - East Facade	2	0	Jan-06-2026	Jan-07-2026																												
	Con-S210.1-110	Erection Seq.210.1 completed	0	0		Jan-07-2026																												
	Con-S210.1-80	Plumb, Bolt, Weld Seq.210.1	10	0	Jan-08-2026	Jan-21-2026																												
	Con-S210.1-90	Turnover Seq. 210.1	0	0	Jan-22-2026																													
	Seq.211 Area3-1		11	0	Jan-08-2026	Jan-23-2026																												
	Con-S211.1-120	Erection Seq.211.1 - Canopy	1	0	Jan-08-2026	Jan-08-2026																												
	Con-S211.1-110	Erection Seq.211.1 completed	0	0		Jan-08-2026																												
	Con-S211.1-80	Plumb, Bolt, Weld Seq.211.1	10	0	Jan-09-2026	Jan-22-2026																												
	Con-S211.1-90	Turnover Seq. 211.1	0	0	Jan-23-2026																													
	Seq.212 Area3-2		11	0	May-01-2026	May-18-2026																												
	Con-S212.2-120	Erection Seq.212.2 - Louvers	1	0	May-01-2026*	May-01-2026																												
	Con-S212.2-110	Erection Seq.212.2 completed	0	0		May-01-2026																												
	Con-S212.2-80	Plumb, Bolt, Weld Seq.212.2	10	0	May-04-2026	May-15-2026																												
	Con-S212.2-90	Turnover Seq. 212.2	0	0	May-18-2026																													
	Seq.214 Area4-2		14	0	Jul-14-2026	Aug-03-2026																												
	Con-S214.2-120	Erection Seq.214.2 - South Facade	4	0	Jul-14-2026*	Jul-17-2026																												
	Con-S214.2-110	Erection Seq.214.2 completed	0	0		Jul-17-2026																												
	Con-S214.2-80	Plumb, Bolt, Weld Seq.214.2	10	0	Jul-20-2026	Jul-31-2026																												
	Con-S214.2-90	Turnover Seq. 214.2	0	0	Aug-03-2026																													
	Seq.217 Area4-2		14	0	Jul-20-2026	Aug-07-2026																												

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 93 of 99
Data date : Oct-31-2025

Page 93 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 94 of 99
Data date : Oct-31-2025

Page 94 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 95 of 99
Data date : Oct-31-2025

Page 95 of 99

Data date : Oct-31-2025



INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



Page 96 of 99
Data date : Oct-31-2025

Page 96 of 99

Data date : Oct-31-2025

 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary




INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



A DBM GLOBAL COMPANY

TSMC FAB3 Preliminary Schedule

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary

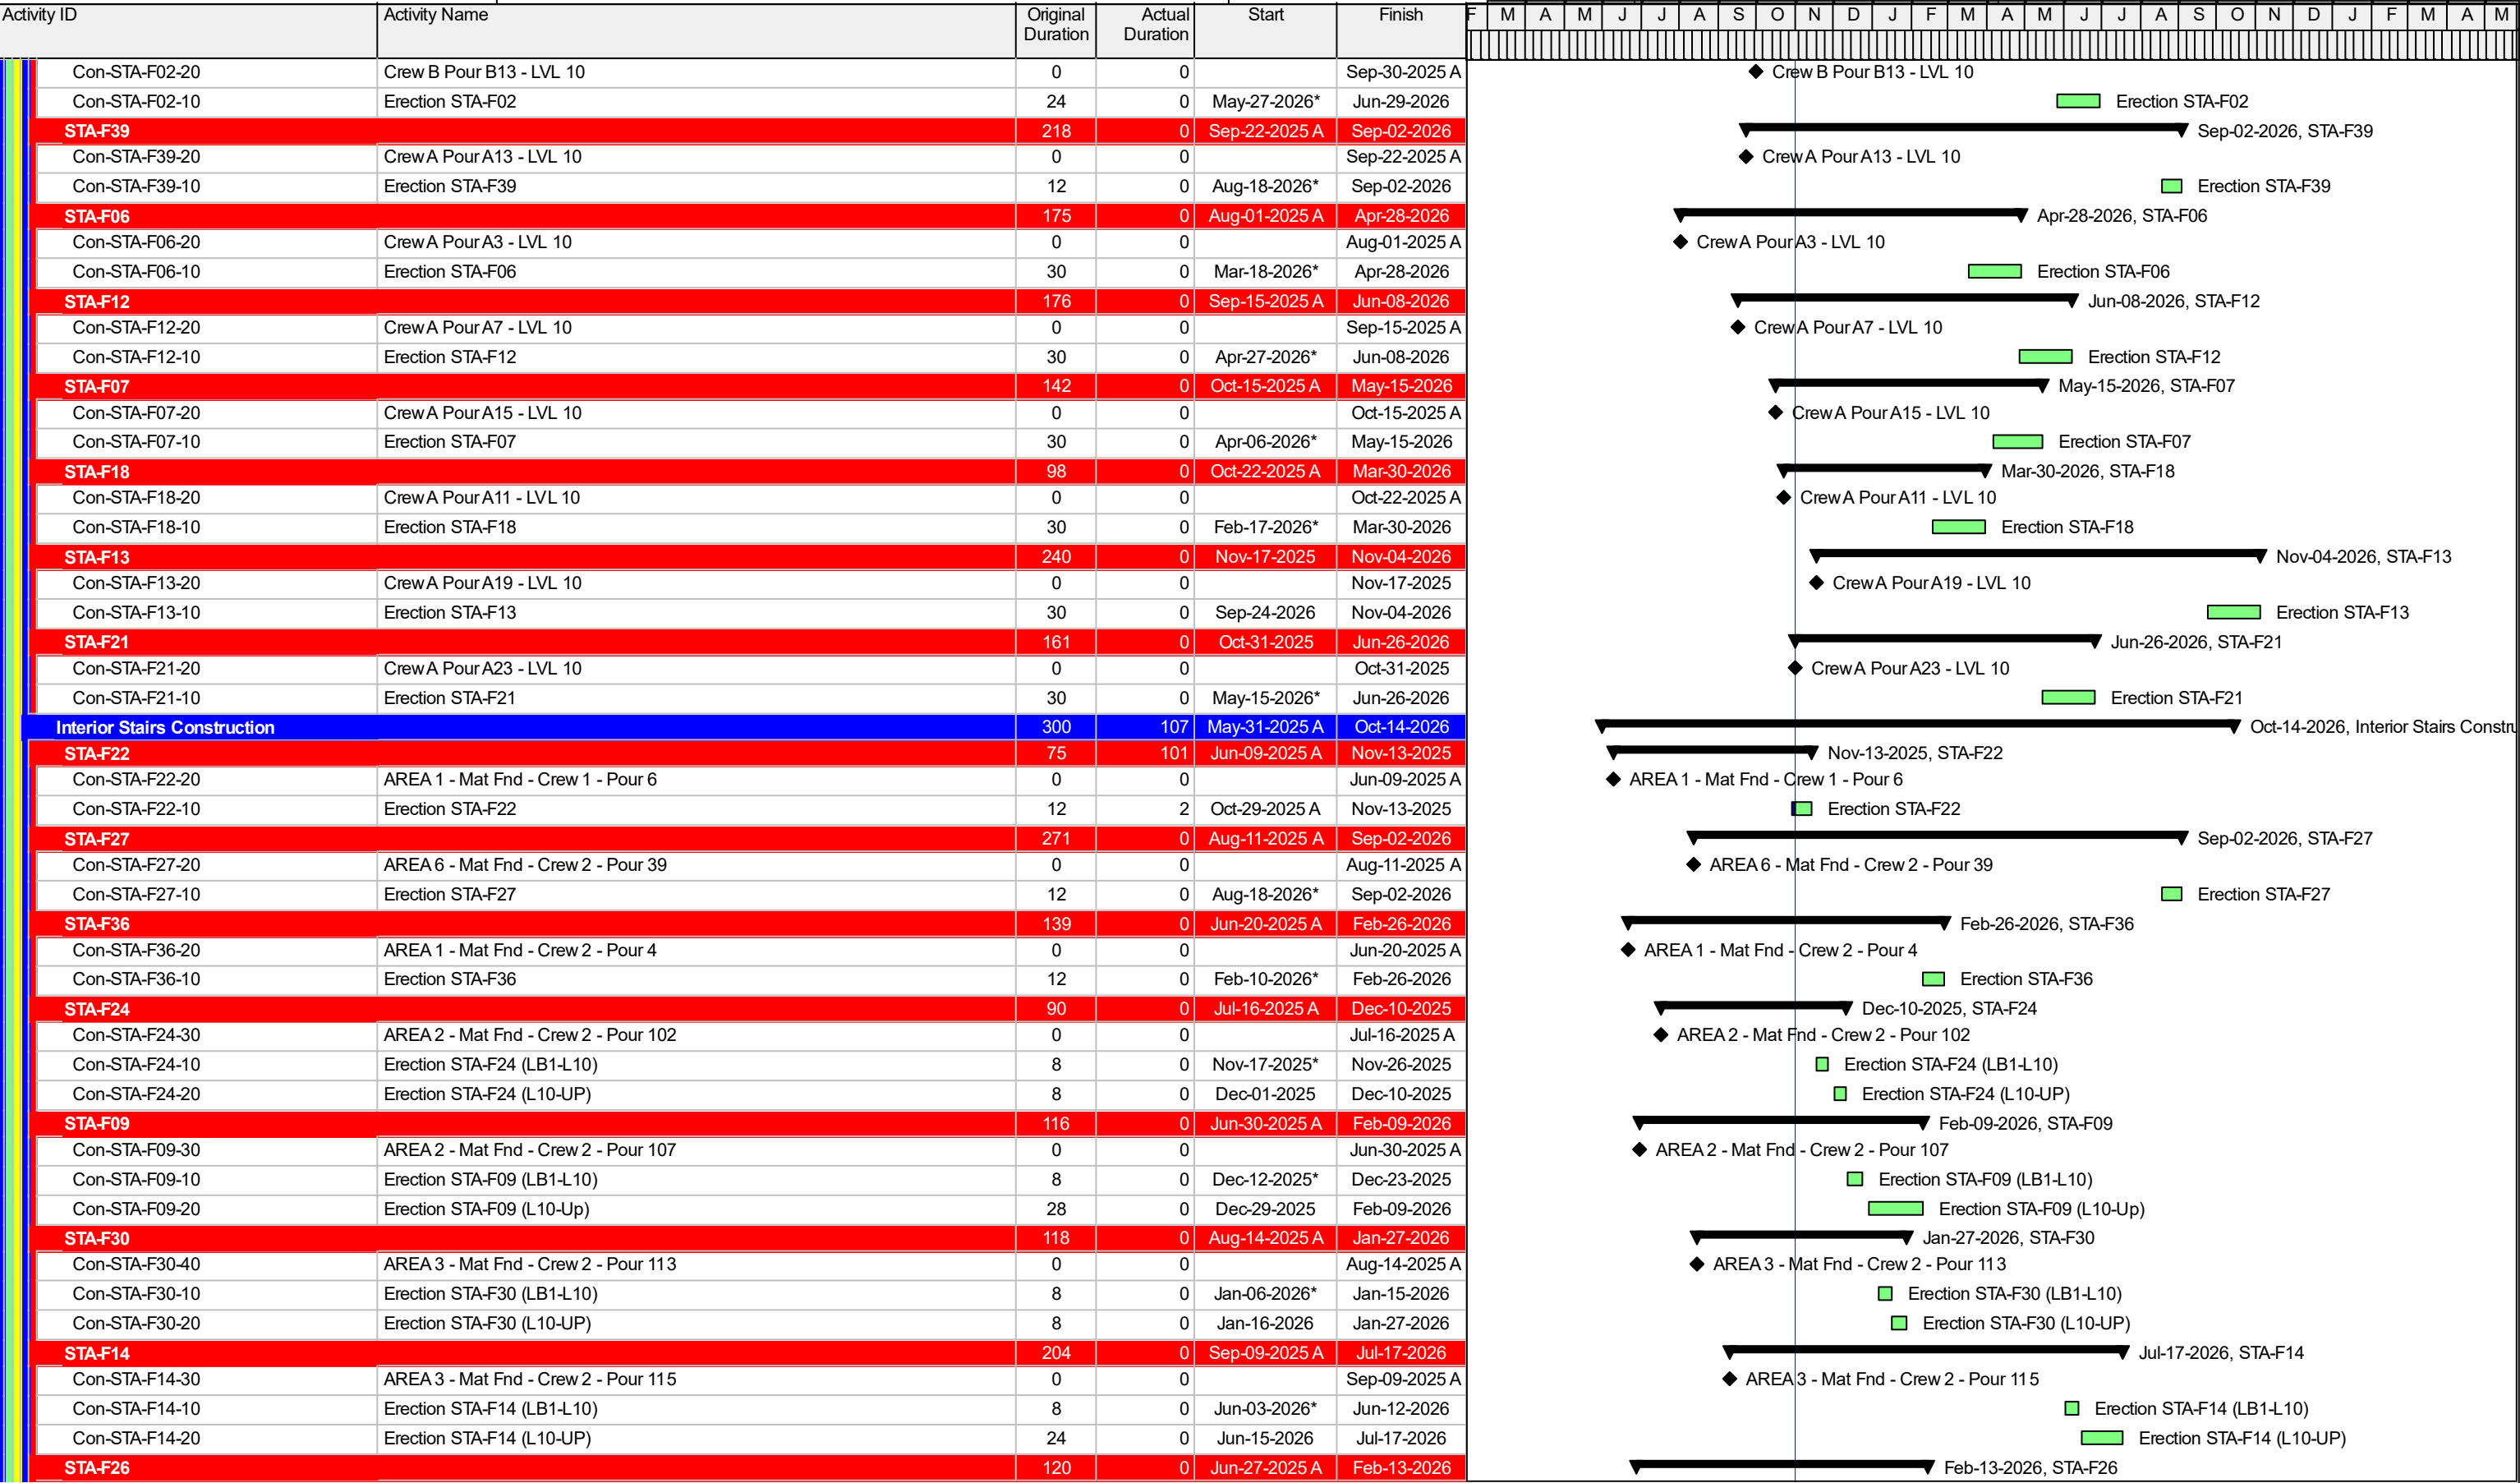

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.

Activity ID	Activity Name	Original Duration	Actual Duration	Start	Finish	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M
Con-STA-F26-20	AREA 2 - Mat Fnd - Crew 1 - Pour 9	0	0		Jun-27-2025 A																												
Con-STA-F26-10	Erection STA-F26	12	0	Jan-29-2026*	Feb-13-2026																												
STA-F28		137	0	Jul-22-2025 A	Feb-24-2026																												
Con-STA-F28-20	AREA 3 - Mat Fnd - Crew 1 - Pour 15	0	0		Jul-22-2025 A																												
Con-STA-F28-10	Erection STA-F28	12	0	Feb-06-2026*	Feb-24-2026																												
STA-F04		180	0	Jun-09-2025 A	Apr-24-2026																												
Con-STA-F04-30	AREA 1 - Mat Fnd - Crew 2 - Pour 2	0	0		Jun-09-2025 A																												
Con-STA-F04-10	Erection STA-F04 (LB1-L10)	12	0	Feb-18-2026*	Mar-05-2026																												
Con-STA-F04-20	Erection STA-F04 (L10-Up)	36	0	Mar-06-2026	Apr-24-2026																												
STA-F40		20	0	Apr-24-2026	May-21-2026																												
Con-STA-F40-10	Erection STA-F40 (L10-UP)	20	0	Apr-24-2026*	May-21-2026																												
STA-F08		152	0	May-31-2025 A	Mar-17-2026																												
Con-STA-F08-20	AREA 1 - Mat Fnd - Crew 1 - Pour 5	0	0		May-31-2025 A																												
Con-STA-F08-10	Erection STA-F08	20	0	Feb-18-2026*	Mar-17-2026																												
STA-F34		235	0	Aug-23-2025 A	Aug-11-2026																												
Con-STA-F34-20	AREA 4 - Mat Fnd - Crew 1 - Pour 24	0	0		Aug-23-2025 A																												
Con-STA-F34-10	Erection STA-F34	12	0	Jul-27-2026*	Aug-11-2026																												
STA-F16		193	0	Oct-13-2025 A	Jul-29-2026																												
Con-STA-F16-20	CrewA PourA10 - LVL 10	0	0		Oct-13-2025 A																												
Con-STA-F16-10	Erection STA-F16 (L10-UP)	24	0	Jun-25-2026*	Jul-29-2026																												
STA-F11		225	0	Oct-31-2025	Sep-29-2026																												
Con-STA-F11-20	CrewA Pour A17 - LVL 10	0	0		Oct-31-2025																												
Con-STA-F11-10	Erection STA-F11 (L10-UP)	24	0	Aug-26-2026*	Sep-29-2026																												
STA-F17		207	0	Dec-15-2025	Oct-14-2026																												
Con-STA-F17-20	Crew A Pour A22 - LVL 10	0	0		Dec-15-2025																												
Con-STA-F17-10	Erection STA-F17	24	0	Sep-11-2026*	Oct-14-2026																												
STA-F35		220	0	Nov-03-2025	Sep-23-2026																												
Con-STA-F35-20	AREA 8 - Mat Fnd - Crew 2 - Pour 54	0	0		Nov-03-2025																												
Con-STA-F35-10	Erection STA-F35	12	0	Sep-08-2026*	Sep-23-2026																												
STA-F03		152	0	Jul-17-2025 A	Mar-17-2026																												
Con-STA-F03-30	CrewA Pour A1 - LVL 10	0	0		Jul-17-2025 A																												
Con-STA-F03-10	Erection STA-F03 (LB1-L10)	12	0	Feb-11-2026*	Feb-27-2026																												
Con-STA-F03-20	Erection STA-F03 (L10-UP)	12	0	Mar-02-2026	Mar-17-2026																												
STA-F32		194	0	Sep-09-2025 A	Jul-02-2026																												
Con-STA-F32-30	AREA 3 - Mat Fnd - Crew 2 - Pour 115	0	0		Sep-09-2025 A																												
Con-STA-F32-10	Erection STA-F32 (LB1-L10)	8	0	Jun-11-2026*	Jun-22-2026																												
Con-STA-F32-20	Erection STA-F32 (L10-UP)	8	0	Jun-23-2026	Jul-02-2026																												
STA-F43		226	0	Sep-15-2025 A	Aug-18-2026																												
Con-STA-F43-20	AREA 4 - Mat Fnd - Crew 1 - Pour 30	0	0		Sep-15-2025 A																												
Con-STA-F43-10	Erection STA-F43	12	0	Aug-03-2026*	Aug-18-2026																												
STA-F41		227	0	Sep-18-2025 A	Aug-19-2026																												
Con-STA-F41-20	AREA 4 - Mat Fnd - Crew 1 - Pour 31	0	0		Sep-18-2025 A																												
Con-STA-F41-10	Erection STA-F41	12	0	Aug-04-2026*	Aug-19-2026																												
STA-F19		211	0	Sep-23-2025 A	Aug-24-2026																												
Con-STA-F19-30	AREA 4 - Mat Fnd - Crew 1 - Pour 32	0	0		Sep-23-2025 A																												
Con-STA-F19-10	Erection STA-F19 (LB1-L10)	12	0	Jul-06-2026*	Jul-21-2026																												
Con-STA-F19-20	Erection STA-F19 (L10-UP)	24	0	Jul-22-2026	Aug-24-2026																												
STA-F37		265	0	Jun-23-2025 A	Aug-25-2026																												
Con-STA-F37-40	AREA 1 - Mat Fnd - Crew 2 - Pour 1	0	0		Jun-23-2025 A																												
Con-STA-F37-10	Erection STA-F37	12	0	Aug-10-2026*	Aug-25-2026																												

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In forFabrication),and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the informationmilestone date is onlused to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to theinformation milestone date will beevaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.



A DBM GLOBAL COMPANY

TSMC FAB3 Preliminary Schedule

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary



Activity ID	Activity Name	Original Duration	Actual Duration	Start	Finish	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M
STA-F23		277	0	Aug-04-2025 A	Sep-11-2026																												
Con-STA-F23-20	AREA 5 - Mat Fnd - Crew 2 - Pour 36	0	0		Aug-04-2025 A																												
Con-STA-F23-10	Erection STA-F23	12	0	Aug-26-2026	Sep-11-2026																												
STA-F05		133	0	Sep-22-2025 A	May-04-2026																												
Con-STA-F05-30	CrewA Pour A13 - LVL 10	0	0		Sep-22-2025 A																												
Con-STA-F05-10	Erection STA-F05 (LB1-L10)	8	0	Mar-24-2026*	Apr-02-2026																												
Con-STA-F05-20	Erection STA-F05 (L10-UP)	22	0	Apr-03-2026	May-04-2026																												
STA-F10		198	0	Jul-08-2025 A	May-20-2026																												
Con-STA-F10-30	AREA 2 - Mat Fnd - Crew 2 - Pour 108	0	0		Jul-08-2025 A																												
Con-STA-F10-10	Erection STA-F10 (LB1-L10)	8	0	Apr-07-2026*	Apr-16-2026																												
Con-STA-F10-20	Erection STA-F10 (L10-UP)	24	0	Apr-17-2026	May-20-2026																												
STA-F25		177	0	Jul-22-2025 A	Apr-21-2026																												
Con-STA-F25-30	AREA 2 - Mat Fnd - Crew 2 - Pour 103	0	0		Jul-22-2025 A																												
Con-STA-F25-10	Erection STA-F25 (LB1-L10)	8	0	Mar-25-2026*	Apr-03-2026																												
Con-STA-F25-20	Erection STA-F25 (L10-UP)	12	0	Apr-06-2026	Apr-21-2026																												
STA-F31		203	0	Aug-14-2025 A	May-28-2026																												
Con-STA-F31-30	AREA 3 - Mat Fnd - Crew 2 - Pour 113	0	0		Aug-14-2025 A																												
Con-STA-F31-10	Erection STA-F31 (LB1-L10)	8	0	Apr-30-2026*	May-11-2026																												
Con-STA-F31-20	Erection STA-F31 (L10-UP)	12	0	May-12-2026	May-28-2026																												
STA-F29		245	0	Sep-04-2025 A	Sep-15-2026																												
Con-STA-F29-20	AREA 7 - Mat Fnd - Crew 2 - Pour 45	0	0		Sep-04-2025 A																												
Con-STA-F29-10	Erection STA-F29	12	0	Aug-28-2026*	Sep-15-2026																												
STA-F33		205	0	Sep-03-2025 A	Jul-20-2026																												
Con-STA-F33-30	AREA 3 - Mat Fnd - Crew 2 - Pour 116	0	0		Sep-03-2025 A																												
Con-STA-F33-10	Erection STA-F33 (LB1-L10)	8	0	Jun-22-2026*	Jul-01-2026																												
Con-STA-F33-20	Erection STA-F33 (L10-UP)	12	0	Jul-02-2026	Jul-20-2026																												
STA-F15		186	0	Sep-03-2025 A	Jun-22-2026																												
Con-STA-F15-30	AREA 3 - Mat Fnd - Crew 2 - Pour 116	0	0		Sep-03-2025 A																												
Con-STA-F15-10	Erection STA-F15 (LB1-L10)	8	0	May-07-2026*	May-18-2026																												
Con-STA-F15-20	Erection STA-F15 (L10-UP)	24	0	May-19-2026	Jun-22-2026																												
STA-F42		238	0	Sep-23-2025 A	Oct-01-2026																												
Con-STA-F42-20	AREA 4 - Mat Fnd - Crew 1 - Pour 32	0	0		Sep-23-2025 A																												
Con-STA-F42-10	Erection STA-F42	8	0	Sep-22-2026*	Oct-01-2026																												
STA-F20		215	0	Sep-23-2025 A	Aug-28-2026																												
Con-STA-F20-40	AREA 4 - Mat Fnd - Crew 1 - Pour 32	0	0		Sep-23-2025 A																												
Con-STA-F20-10	Erection STA-F20 (LB1-L10)	12	0	Jul-10-2026*	Jul-27-2026																												
Con-STA-F20-20	Erection STA-F20 (L10-UP)	24	0	Jul-28-2026	Aug-28-2026																												
STA-F44		236	0	Sep-29-2025 A	Sep-29-2026																												
Con-STA-F44-20	AREA 4 - Mat Fnd - Crew 1 - Pour 57	0	0		Sep-29-2025 A																												
Con-STA-F44-10	Erection STA-F44	12	0	Sep-14-2026*	Sep-29-2026																												
Fit-Out 1		3	0	Jan-23-2026	Jan-27-2026																												
Con-Fit-Out1-10	Erection Fit-Out 1	3	0	Jan-23-2026	Jan-27-2026																												
Fit-Out 2		3	0	Feb-10-2026	Feb-12-2026																												
Con-Fit-Out2-10	Erection Fit-Out 2	3	0	Feb-10-2026	Feb-12-2026																												
Fit-Out 3		3	0	Feb-10-2026	Feb-12-2026																												
Con-Fit-Out3-10	Erection Fit-Out 3	3	0	Feb-10-2026	Feb-12-2026																												
Fit-Out 4		3	0	Feb-10-2026	Feb-12-2026																												
Con-Fit-Out4-10	Erection Fit-Out 4	3	0	Feb-10-2026	Feb-12-2026																												
Ramp Rails		3	0	Feb-24-2026	Feb-26-2026																												
Con-Ramp-Rail-10	Erection Ramp-Rail	3	0	Feb-24-2026	Feb-26-2026																												

INFORMATION MILESTONE is the date that all outstanding design information/coordination is required including outstanding RFI's, etc. for each sequence. When information is provided beyond this date, it may affect drawings being IFA (In for Approval) and IFF (In for Fabrication), and subsequently impact Schuff's fabrication schedules and ultimately the start of erection or continuous erection. If encountered, Overtime or Schedule Delays will be recommended by Schuff as well as other impacts. It is important to note that the information milestone date is only used to facilitate the transfer and receipt of required design information for base contract steel scope, and does not provide an opportunity to incorporate new design information or added scope. Any new design information received prior to the information milestone date will be evaluated for additional impacts, separate from the above submittal forecast, on a case-by-case basis.
