

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID		Activity Name		Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																											
📁 HRL1 - Preliminary Schedule A1 - Rev.00 - Draft #05.3.1.B1				748d	29-May-26 A	03-Oct-28	6.02%	📅 03-Oct-28																											
📁 Project Milestones				589d	29-May-26 A	26-May-28	0%	📅 26-May-28, Project Milestones																											
📁 HRL1PM11		Project Start		0d	29-May-26 A		100%	◆ Project Start, 29-May-26 A																											
📁 HRL1PM16		30% Design Set Delivered		0d		04-Jun-26 A	100%	◆ 30% Design Set Delivered, 04-Jun-26 A																											
📁 HRL1PM13		Ready		0d		06-Aug-26	0%	◆ Ready, 06-Aug-26																											
📁 HRL1PM12		60% Design Set Delivered		0d		10-Aug-26 A	100%	◆ 60% Design Set Delivered, 10-Aug-26 A																											
📁 HRL1PM17		90% Design Set Delivered		0d		30-Sep-26*	0%	◆ 90% Design Set Delivered, 30-Sep-26*																											
📁 HRL1PM18		IFP Set Delivered		0d		27-Oct-26*	0%	◆ IFP Set Delivered, 27-Oct-26*																											
📁 HRL1PM19		IFC Set Delivered		0d		11-Nov-26*	0%	◆ IFC Set Delivered, 11-Nov-26*																											
📁 HRL1PM14		Early Floor Access		0d		11-Feb-27	0%	◆ Early Floor Access, 11-Feb-27																											
📁 HRL1PM10		Facility Ready		0d		08-Nov-27	0%	◆ Facility Ready, 08-Nov-27																											
📁 HRL1PM15		Floor Access		0d		12-Nov-27	0%	◆ Floor Access, 12-Nov-27																											
📁 HRL1PM20		Permanent Power to Substation		0d		30-Nov-27*	0%	◆ Permanent Power to Substation, 30-Nov-27*																											
📁 HRL1PM21		Building 1 Completion		0d		26-May-28	0%	◆ Building 1 Completion, 26-May-28																											
📁 HRL1PM22		Building 2 Completion		0d		26-May-28	0%	◆ Building 2 Completion, 26-May-28																											
📁 Building 1				163d	29-Nov-27	26-May-28	0%	📅 26-May-28, Building 1																											
📁 Building 1 - Data Hall 1				83d	29-Nov-27	28-Feb-28	0%	📅 28-Feb-28, Building 1 - Data Hall 1																											
📁 BLDG1.MS.120		Data Hall 1 - Early Floor Access (EFA)		0d		29-Nov-27*	0%	◆ Data Hall 1 - Early Floor Access (EFA), 29-Nov-27*																											
📁 BLDG1.MS.130		Data Hall 1 - Floor Access		0d		31-Dec-27*	0%	◆ Data Hall 1 - Floor Access, 31-Dec-27*																											
📁 BLDG1.MS.140		Data Hall 1 - Facility Ready (FR)		0d		28-Jan-28*	0%	◆ Data Hall 1 - Facility Ready (FR), 28-Jan-28*																											
📁 BLDG1.MS.150		Data Hall 1 - Substantial Completion		0d		28-Feb-28*	0%	◆ Data Hall 1 - Substantial Completion, 28-Feb-28*																											
📁 Building 1 - Data Hall 2				81d	31-Dec-27	31-Mar-28	0%	📅 31-Mar-28, Building 1 - Data Hall 2																											
📁 BLDG1.MS.160		Data Hall 2 - Early Floor Access (EFA)		0d		31-Dec-27*	0%	◆ Data Hall 2 - Early Floor Access (EFA), 31-Dec-27*																											
📁 BLDG1.MS.170		Data Hall 2 - Floor Access		0d		28-Jan-28*	0%	◆ Data Hall 2 - Floor Access, 28-Jan-28*																											
📁 BLDG1.MS.190		Data Hall 2 - Substantial Completion		0d		31-Mar-28*	0%	◆ Data Hall 2 - Substantial Completion, 31-Mar-28*																											
📁 BLDG1.MS.180		Data Hall 2 - Facility Ready (FR)		0d		31-Mar-28*	0%	◆ Data Hall 2 - Facility Ready (FR), 31-Mar-28*																											
📁 Building 1 - Data Hall 3				81d	28-Jan-28	28-Apr-28	0%	📅 28-Apr-28, Building 1 - Data Hall 3																											
📁 BLDG1.MS.200		Data Hall 3 - Early Floor Access (EFA)		0d		28-Jan-28*	0%	◆ Data Hall 3 - Early Floor Access (EFA), 28-Jan-28*																											
📁 BLDG1.MS.210		Data Hall 3 - Floor Access		0d		28-Feb-28*	0%	◆ Data Hall 3 - Floor Access, 28-Feb-28*																											
📁 BLDG1.MS.220		Data Hall 3 - Facility Ready (FR)		0d		28-Apr-28*	0%	◆ Data Hall 3 - Facility Ready (FR), 28-Apr-28*																											
📁 BLDG1.MS.230		Data Hall 3 - Substantial Completion		0d		28-Apr-28*	0%	◆ Data Hall 3 - Substantial Completion, 28-Apr-28*																											
📁 Building 1 - Data Hall 4				106d	28-Jan-28	26-May-28	0%	📅 26-May-28, Building 1 - Data Hall 4																											
📁 BLDG1.MS.240		Data Hall 4 - Early Floor Access (EFA)		0d		28-Jan-28*	0%	◆ Data Hall 4 - Early Floor Access (EFA), 28-Jan-28*																											
📁 BLDG1.MS.250		Data Hall 4 - Floor Access		0d		31-Mar-28*	0%	◆ Data Hall 4 - Floor Access, 31-Mar-28*																											
📁 BLDG1.MS.260		Data Hall 4 - Facility Ready (FR)		0d		28-Apr-28*	0%	◆ Data Hall 4 - Facility Ready (FR), 28-Apr-28*																											
📁 BLDG1.MS.270		Data Hall 4 - Substantial Completion		0d		26-May-28*	0%	◆ Data Hall 4 - Substantial Completion, 26-May-28*																											
📁 Building 2				163d	26-Nov-27	26-May-28	0%	📅 26-May-28, Building 2																											
📁 Building 2 - Data Hall 1				83d	26-Nov-27	28-Feb-28	0%	📅 28-Feb-28, Building 2 - Data Hall 1																											
📁 BLDG2.MS.100		Data Hall 1 - Early Floor Access (EFA)		0d		26-Nov-27*	0%	◆ Data Hall 1 - Early Floor Access (EFA), 26-Nov-27*																											
📁 BLDG2.MS.110		Data Hall 1 - Floor Access		0d		27-Dec-27*	0%	◆ Data Hall 1 - Floor Access, 27-Dec-27*																											
📁 BLDG2.MS.120		Data Hall 1 - Facility Ready (FR)		0d		28-Jan-28*	0%	◆ Data Hall 1 - Facility Ready (FR), 28-Jan-28*																											
📁 BLDG2.MS.130		Data Hall 1 - Substantial Completion		0d		28-Feb-28*	0%	◆ Data Hall 1 - Substantial Completion, 28-Feb-28*																											
📁 Building 2 - Data Hall 2				78d	31-Dec-27	28-Mar-28	0%	📅 28-Mar-28, Building 2 - Data Hall 2																											
📁 BLDG2.MS.140		Data Hall 2 - Early Floor Access (EFA)		0d		31-Dec-27*	0%	◆ Data Hall 2 - Early Floor Access (EFA), 31-Dec-27*																											

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID	Activity Name	Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																																																
BLDG2	BLDG2.MS.150	Data Hall 2 - Floor Access	0d		31-Jan-28*	0%																																																
	BLDG2.MS.160	Data Hall 2 - Facility Ready (FR)	0d		28-Mar-28*	0%																																																
	BLDG2.MS.170	Data Hall 2 - Substantial Completion	0d		28-Mar-28*	0%																																																
	Building 2 - Data Hall 3		81d	28-Jan-28	28-Apr-28	0%																																																
	BLDG2.MS.180	Data Hall 3 - Early Floor Access (EFA)	0d		28-Jan-28*	0%																																																
	BLDG2.MS.190	Data Hall 3 - Floor Access	0d		28-Feb-28*	0%																																																
	BLDG2.MS.200	Data Hall 3 - Facility Ready (FR)	0d		28-Apr-28*	0%																																																
	BLDG2.MS.210	Data Hall 3 - Substantial Completion	0d		28-Apr-28*	0%																																																
	Building 2 - Data Hall 4		106d	28-Jan-28	26-May-28	0%																																																
	BLDG2.MS.220	Data Hall 4 - Early Floor Access (EFA)	0d		28-Jan-28*	0%																																																
	BLDG2.MS.230	Data Hall 4 - Floor Access	0d		28-Mar-28*	0%																																																
	BLDG2.MS.240	Data Hall 4 - Facility Ready (FR)	0d		28-Apr-28*	0%																																																
	BLDG2.MS.250	Data Hall 4 - Substantial Completion	0d		26-May-28*	0%																																																
	Design		0d			0%																																																
	Building 1		0d			0%																																																
	Building 2		0d			0%																																																
	OFCI		487d	07-Aug-26	03-Feb-28	0%																																																
	Building 1		487d	07-Aug-26	03-Feb-28	0%																																																
	Data Hall 1		420d	07-Aug-26	19-Nov-27	0%																																																
	A3950	Fab & Del Pad Mount VFI SS + Submersible	314d	07-Aug-26*	23-Jul-27	0%																																																
	A4080	Fab & Del Air Cooled Chiller	251d	07-Aug-26*	14-May-27	0%																																																
	A4090	Fab & Del Fan Coil Wall	251d	07-Aug-26*	14-May-27	0%																																																
	A4100	Fab & Del Computer Room Air Handler – CRAH	201d	04-Sep-26*	16-Apr-27	0%																																																
	A4140	Fab & Del PEMB Total Material Only Supply	1d	16-Sep-26*	16-Sep-26	0%																																																
	A3940	Fab & Del Pad Mounted Switchgear	214d	21-Sep-26*	17-May-27	0%																																																
A4030	Fab & Del Low Voltage Switchgear – Mechanical	176d	02-Oct-26*	16-Apr-27	0%																																																	
A4040	Fab & Del Low Voltage Switchgear – IT Loads	176d	02-Oct-26*	16-Apr-27	0%																																																	
A4050	Fab & Del Low Voltage Switchgear –	176d	02-Oct-26*	16-Apr-27	0%																																																	
A4110	Fab & Del CRAC Condensing Unit	201d	05-Oct-26*	17-May-27	0%																																																	
A3960	Fab & Del MV Transformer - Solid Ground (double tap)	214d	22-Oct-26*	17-Jun-27	0%																																																	
A3980	Fab & Del Network UPS	151d	30-Oct-26*	16-Apr-27	0%																																																	
A3990	Fab & Del UPS	151d	30-Oct-26*	16-Apr-27	0%																																																	
A4000	Fab & Del Chiller UPS	151d	30-Oct-26*	16-Apr-27	0%																																																	
A4010	Fab & Del Admin UPS	151d	30-Oct-26*	16-Apr-27	0%																																																	
A4020	Fab & Del CDU UPS	151d	30-Oct-26*	16-Apr-27	0%																																																	
A4130	Fab & Del Hot Aisle Containment System	176d	03-Dec-26*	17-Jun-27	0%																																																	
A4060	Fab & Del ATS	139d	14-Dec-26*	17-May-27	0%																																																	
A4070	Fab & Del Busway	150d	31-Dec-26*	16-Jun-27	0%																																																	
A4120	Fab & Del Coolant Distribution Unit – CDU (OFOI)	150d	07-Jun-27*	19-Nov-27	0%																																																	
A3970	Fab & Del Generator	1d	17-Jun-27*	17-Jun-27	0%																																																	
Data Hall 2		434d	07-Aug-26	06-Dec-27	0%																																																	
A4160	Fab & Del Pad Mount VFI SS + Submersible	326d	07-Aug-26*	06-Aug-27	0%																																																	
A4240	Fab & Del Air Cooled Chiller	264d	07-Aug-26*	28-May-27	0%																																																	
A4250	Fab & Del Fan Coil Wall	264d	07-Aug-26*	28-May-27	0%																																																	
A4260	Fab & Del Computer Room Air Handler – CRAH	214d	04-Sep-26*	30-Apr-27	0%																																																	
A4150	Fab & Del Pad Mounted Switchgear	226d	21-Sep-26*	31-May-27	0%																																																	
A4200	Fab & Del Low Voltage Switchgear – Mechanical	189d	02-Oct-26*	30-Apr-27	0%																																																	

alston
CONSTRUCTION
MISSION CRITICAL

[illegible]

alston
CONSTRUCTION
MISSION CRITICAL

[illegible]

alston
CONSTRUCTION
MISSION CRITICAL

[illegible]

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID		Activity Name		Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																																																
Data Hall 1	OFCI-SZ04-FS-1430	Procurement -	UPS	175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																																
	OFCI-SZ04-FS-1470	Procurement -	RMU	105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																																
	OFCI-SZ04-FS-1380	Procurement -	TES Tank	280d	07-Aug-26	16-Jun-27	0%	Procurement - TES Tank																																																
	OFCI-SZ04-FS-1390	Procurement -	TES Tank	280d	07-Aug-26	16-Jun-27	0%	Procurement - TES Tank																																																
	Data Hall 1				280d	07-Aug-26	16-Jun-27	0%	16-Jun-27, Data Hall 1																																															
	OFCI-SZ04-FS-1000	Procurement -	RMU	105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																																
	OFCI-SZ04-FS-1010	Procurement -	RMU	105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																																
	OFCI-SZ04-FS-1020	Procurement -	UPS	175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																																
	OFCI-SZ04-FS-1030	Procurement -	UPS	175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																																
	OFCI-SZ04-FS-1040	Procurement -	UPS	175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																																
	OFCI-SZ04-FS-1050	Procurement -	RMU	105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																																
	OFCI-SZ04-FS-1060	Procurement -	Chiller	280d	07-Aug-26	16-Jun-27	0%	Procurement - Chiller																																																
	OFCI-SZ04-FS-1070	Procurement -	Chiller	280d	07-Aug-26	16-Jun-27	0%	Procurement - Chiller																																																
	OFCI-SZ04-FS-1080	Procurement -	UPS	175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																																
	OFCI-SZ04-FS-1090	Procurement -	RMU	105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																																
	OFCI-SZ04-FS-1100	Procurement -	TES Tank	280d	07-Aug-26	16-Jun-27	0%	Procurement - TES Tank																																																
	OFCI-SZ04-FS-1110	Procurement -	TES Tank	280d	07-Aug-26	16-Jun-27	0%	Procurement - TES Tank																																																
	Data Hall 2				280d	07-Aug-26	16-Jun-27	0%	16-Jun-27, Data Hall 2																																															
	OFCI-SZ04-FS-1320	Procurement -	RMU	105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																																
	OFCI-SZ04-FS-1330	Procurement -	RMU	105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																																
	OFCI-SZ04-FS-1280	Procurement -	UPS	175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																																
	OFCI-SZ04-FS-1290	Procurement -	UPS	175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																																
	OFCI-SZ04-FS-1300	Procurement -	UPS	175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																																
	OFCI-SZ04-FS-1340	Procurement -	RMU	105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																																
	OFCI-SZ04-FS-1240	Procurement -	Chiller	280d	07-Aug-26	16-Jun-27	0%	Procurement - Chiller																																																
	OFCI-SZ04-FS-1250	Procurement -	Chiller	280d	07-Aug-26	16-Jun-27	0%	Procurement - Chiller																																																
	OFCI-SZ04-FS-1310	Procurement -	UPS	175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																																
	OFCI-SZ04-FS-1350	Procurement -	RMU	105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																																
	OFCI-SZ04-FS-1260	Procurement -	TES Tank	280d	07-Aug-26	16-Jun-27	0%	Procurement - TES Tank																																																
	OFCI-SZ04-FS-1270	Procurement -	TES Tank	280d	07-Aug-26	16-Jun-27	0%	Procurement - TES Tank																																																
	Data Hall 4				280d	07-Aug-26	16-Jun-27	0%	16-Jun-27, Data Hall 4																																															
	OFCI-SZ04-FS-1560	Procurement -	RMU	105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																																
	OFCI-SZ04-FS-1570	Procurement -	RMU	105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																																
	OFCI-SZ04-FS-1520	Procurement -	UPS	175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																																
	OFCI-SZ04-FS-1530	Procurement -	UPS	175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																																
	OFCI-SZ04-FS-1540	Procurement -	UPS	175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																																
	OFCI-SZ04-FS-1580	Procurement -	RMU	105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																																
	OFCI-SZ04-FS-1480	Procurement -	Chiller	280d	07-Aug-26	16-Jun-27	0%	Procurement - Chiller																																																
	OFCI-SZ04-FS-1490	Procurement -	Chiller	280d	07-Aug-26	16-Jun-27	0%	Procurement - Chiller																																																
	OFCI-SZ04-FS-1550	Procurement -	UPS	175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																																
	OFCI-SZ04-FS-1590	Procurement -	RMU	105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																																
	OFCI-SZ04-FS-1500	Procurement -	TES Tank	280d	07-Aug-26	16-Jun-27	0%	Procurement - TES Tank																																																
	OFCI-SZ04-FS-1510	Procurement -																																																						

alston
CONSTRUCTION
MISSION CRITICAL

[illegible]

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID	Activity Name			Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																																															
Admin				280d	07-Aug-26	16-Jun-27	0%	16-Jun-27, Admin																																															
OFCI-SZ04-FS-1800	Procurement -	- RMU		105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																															
OFCI-SZ04-FS-1810	Procurement -	- RMU		105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																															
OFCI-SZ04-FS-1760	Procurement -	- UPS		175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																															
OFCI-SZ04-FS-1770	Procurement -	- UPS		175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																															
OFCI-SZ04-FS-1780	Procurement -	- UPS		175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																															
OFCI-SZ04-FS-1820	Procurement -	- RMU		105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																															
OFCI-SZ04-FS-1720	Procurement -	- Chiller		280d	07-Aug-26	16-Jun-27	0%	Procurement - Chiller																																															
OFCI-SZ04-FS-1730	Procurement -	- Chiller		280d	07-Aug-26	16-Jun-27	0%	Procurement - Chiller																																															
OFCI-SZ04-FS-1790	Procurement -	- UPS		175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																															
OFCI-SZ04-FS-1830	Procurement -	- RMU		105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																															
OFCI-SZ04-FS-1740	Procurement -	- TES Tank		280d	07-Aug-26	16-Jun-27	0%	Procurement - TES Tank																																															
OFCI-SZ04-FS-1750	Procurement -	- TES Tank		280d	07-Aug-26	16-Jun-27	0%	Procurement - TES Tank																																															
Data Hall 3				280d	07-Aug-26	16-Jun-27	0%	16-Jun-27, Data Hall 3																																															
OFCI-SZ04-FS-2040	Procurement -	- RMU		105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																															
OFCI-SZ04-FS-2050	Procurement -	- RMU		105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																															
OFCI-SZ04-FS-2000	Procurement -	- UPS		175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																															
OFCI-SZ04-FS-2010	Procurement -	- UPS		175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																															
OFCI-SZ04-FS-2020	Procurement -	- UPS		175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																															
OFCI-SZ04-FS-2060	Procurement -	- RMU		105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																															
OFCI-SZ04-FS-1960	Procurement -	- Chiller		280d	07-Aug-26	16-Jun-27	0%	Procurement - Chiller																																															
OFCI-SZ04-FS-1970	Procurement -	- Chiller		280d	07-Aug-26	16-Jun-27	0%	Procurement - Chiller																																															
OFCI-SZ04-FS-2030	Procurement -	- UPS		175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																															
OFCI-SZ04-FS-2070	Procurement -	- RMU		105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																															
OFCI-SZ04-FS-1980	Procurement -	- TES Tank		280d	07-Aug-26	16-Jun-27	0%	Procurement - TES Tank																																															
OFCI-SZ04-FS-1990	Procurement -	- TES Tank		280d	07-Aug-26	16-Jun-27	0%	Procurement - TES Tank																																															
Data Hall 1				280d	07-Aug-26	16-Jun-27	0%	16-Jun-27, Data Hall 1																																															
OFCI-SZ04-FS-1680	Procurement -	- RMU		105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																															
OFCI-SZ04-FS-1690	Procurement -	- RMU		105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																															
OFCI-SZ04-FS-1640	Procurement -	- UPS		175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																															
OFCI-SZ04-FS-1650	Procurement -	- UPS		175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																															
OFCI-SZ04-FS-1660	Procurement -	- UPS		175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																															
OFCI-SZ04-FS-1700	Procurement -	- RMU		105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																															
OFCI-SZ04-FS-1600	Procurement -	- Chiller		280d	07-Aug-26	16-Jun-27	0%	Procurement - Chiller																																															
OFCI-SZ04-FS-1610	Procurement -	- Chiller		280d	07-Aug-26	16-Jun-27	0%	Procurement - Chiller																																															
OFCI-SZ04-FS-1670	Procurement -	- UPS		175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																															
OFCI-SZ04-FS-1710	Procurement -	- RMU		105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																															
OFCI-SZ04-FS-1620	Procurement -	- TES Tank		280d	07-Aug-26	16-Jun-27	0%	Procurement - TES Tank																																															
OFCI-SZ04-FS-1630	Procurement -	- TES Tank		280d	07-Aug-26	16-Jun-27	0%	Procurement - TES Tank																																															
Data Hall 2				280d	07-Aug-26	16-Jun-27	0%	16-Jun-27, Data Hall 2																																															
OFCI-SZ04-FS-1920	Procurement -	- RMU		105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																															
OFCI-SZ04-FS-1930	Procurement -	- RMU		105d	07-Aug-26	02-Dec-26	0%	Procurement - RMU																																															
OFCI-SZ04-FS-1880	Procurement -	- UPS		175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																															
OFCI-SZ04-FS-1890	Procurement -	- UPS		175d	07-Aug-26	18-Feb-27	0%	Procurement - UPS																																															
OFCI-SZ04-FS-1900	Procurement -	- UPS																																																					

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID		Activity Name		Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																																																
Procurement	OFCI-SZ04-FS-1850	Procurement - Chiller		280d	07-Aug-26	16-Jun-27	0%																																																	
	OFCI-SZ04-FS-1910	Procurement - UPS		175d	07-Aug-26	18-Feb-27	0%																																																	
	OFCI-SZ04-FS-1950	Procurement - RMU		105d	07-Aug-26	02-Dec-26	0%																																																	
	OFCI-SZ04-FS-1860	Procurement - TES Tank		280d	07-Aug-26	16-Jun-27	0%																																																	
	OFCI-SZ04-FS-1870	Procurement - TES Tank		280d	07-Aug-26	16-Jun-27	0%																																																	
	Data Hall 4				280d	07-Aug-26	16-Jun-27	0%																																																
	OFCI-SZ04-FS-2160	Procurement - RMU		105d	07-Aug-26	02-Dec-26	0%																																																	
	OFCI-SZ04-FS-2170	Procurement - RMU		105d	07-Aug-26	02-Dec-26	0%																																																	
	OFCI-SZ04-FS-2120	Procurement - UPS		175d	07-Aug-26	18-Feb-27	0%																																																	
	OFCI-SZ04-FS-2130	Procurement - UPS		175d	07-Aug-26	18-Feb-27	0%																																																	
	OFCI-SZ04-FS-2140	Procurement - UPS		175d	07-Aug-26	18-Feb-27	0%																																																	
	OFCI-SZ04-FS-2180	Procurement - RMU		105d	07-Aug-26	02-Dec-26	0%																																																	
	OFCI-SZ04-FS-2080	Procurement - Chiller		280d	07-Aug-26	16-Jun-27	0%																																																	
	OFCI-SZ04-FS-2090	Procurement - Chiller		280d	07-Aug-26	16-Jun-27	0%																																																	
	OFCI-SZ04-FS-2150	Procurement - UPS		175d	07-Aug-26	18-Feb-27	0%																																																	
	OFCI-SZ04-FS-2190	Procurement - RMU		105d	07-Aug-26	02-Dec-26	0%																																																	
	OFCI-SZ04-FS-2100	Procurement - TES Tank		280d	07-Aug-26	16-Jun-27	0%																																																	
	OFCI-SZ04-FS-2110	Procurement - TES Tank		280d	07-Aug-26	16-Jun-27	0%																																																	
	Rev & App				139d	09-Nov-27	11-Apr-28	0%																																																
	OFCI-APP-FS-1310	OFCI - Rev & App - Chiller		13d	09-Nov-27	22-Nov-27	0%																																																	
	OFCI-APP-FS-1360	OFCI - Rev & App - TES Tank		13d	09-Nov-27	22-Nov-27	0%																																																	
OFCI-APP-FS-1330	OFCI - Rev & App - HACs		13d	10-Nov-27	23-Nov-27	0%																																																		
OFCI-APP-FS-1320	OFCI - Rev & App - MV SWGR		13d	23-Nov-27	06-Dec-27	0%																																																		
OFCI-APP-FS-1350	OFCI - Rev & App - FCUs		13d	17-Dec-27	30-Dec-27	0%																																																		
OFCI-APP-FS-1340	OFCI - Rev & App - CDUs		13d	20-Dec-27	31-Dec-27	0%																																																		
OFCI-APP-FS-1290	OFCI - Rev & App - UPS		13d	03-Feb-28	16-Feb-28	0%																																																		
OFCI-APP-FS-1300	OFCI - Rev & App - RMU		13d	29-Mar-28	11-Apr-28	0%																																																		
OFCI - ROJ Dates - Interiors				263d	07-Aug-26	27-May-27	0%																																																	
OFCI Procurement Interiors				263d	07-Aug-26	27-May-27	0%																																																	
Admin				263d	07-Aug-26	27-May-27	0%																																																	
OFCI-SZ04-FS.INT-130	Procurement - HACs		263d	07-Aug-26	27-May-27	0%																																																		
OFCI-SZ04-FS.INT-140	Procurement - FCUs		228d	07-Aug-26	19-Apr-27	0%																																																		
OFCI-SZ04-FS.INT-150	Procurement - CDUs		245d	07-Aug-26	07-May-27	0%																																																		
Data Hall 3				263d	07-Aug-26	27-May-27	0%																																																	
OFCI-SZ04-FS.INT-190	Procurement - HACs		263d	07-Aug-26	27-May-27	0%																																																		
OFCI-SZ04-FS.INT-200	Procurement - FCUs		228d	07-Aug-26	19-Apr-27	0%																																																		
OFCI-SZ04-FS.INT-210	Procurement - CDUs		245d	07-Aug-26	07-May-27	0%																																																		
Data Hall 1				263d	07-Aug-26	27-May-27	0%																																																	
OFCI-SZ04-FS.INT-100	Procurement - HACs		263d	07-Aug-26	27-May-27	0%																																																		
OFCI-SZ04-FS.INT-110	Procurement - FCUs		228d	07-Aug-26	19-Apr-27	0%																																																		
OFCI-SZ04-FS.INT-120	Procurement - CDUs		245d	07-Aug-26	07-May-27	0%																																																		

alston
CONSTRUCTION
MISSION CRITICAL


Activity ID	Activity Name	Original Duration	Start	Finish	Duration % Complete	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
■ OFCI-SZ04-FS.INT-240	Procurement - CDUs	245d	07-Aug-26	07-May-27	0%																																	
■ Prep & Sub		139d	26-Oct-27	28-Mar-28	0%																																	
■ OFCI-SUB-FS-1350	OFCI - Prep & Sub - Chiller	13d	26-Oct-27	08-Nov-27	0%																																	
■ OFCI-SUB-FS-1400	OFCI - Prep & Sub - TES Tank	13d	26-Oct-27	08-Nov-27	0%																																	
■ OFCI-SUB-FS-1370	OFCI - Prep & Sub - HACs	13d	27-Oct-27	09-Nov-27	0%																																	
■ OFCI-SUB-FS-1360	OFCI - Prep & Sub - MV SWGR	13d	09-Nov-27	22-Nov-27	0%																																	
■ OFCI-SUB-FS-1390	OFCI - Prep & Sub - FCUs	13d	03-Dec-27	16-Dec-27	0%																																	
■ OFCI-SUB-FS-1380	OFCI - Prep & Sub - CDUs	13d	06-Dec-27	17-Dec-27	0%																																	
■ OFCI-SUB-FS-1330	OFCI - Prep & Sub - UPS	13d	20-Jan-28	02-Feb-28	0%																																	
■ OFCI-SUB-FS-1340	OFCI - Prep & Sub - RMU	13d	15-Mar-28	28-Mar-28	0%																																	
■ PO		128d	25-Oct-27	14-Mar-28	0%																																	
■ OFCI-PO-FS-1390	OFCI - PO - Chiller	1d	25-Oct-27*	25-Oct-27	0%																																	
■ OFCI-PO-FS-1440	OFCI - PO - TES Tank	1d	25-Oct-27*	25-Oct-27	0%																																	
■ OFCI-PO-FS-1410	OFCI - PO - HACs	1d	26-Oct-27*	26-Oct-27	0%																																	
■ OFCI-PO-FS-1400	OFCI - PO - MV SWGR	1d	08-Nov-27*	08-Nov-27	0%																																	
■ OFCI-PO-FS-1430	OFCI - PO - FCUs	1d	02-Dec-27*	02-Dec-27	0%																																	
■ OFCI-PO-FS-1420	OFCI - PO - CDUs	1d	03-Dec-27*	03-Dec-27	0%																																	
■ OFCI-PO-FS-1370	OFCI - PO - UPS	1d	19-Jan-28*	19-Jan-28	0%																																	
■ OFCI-PO-FS-1380	OFCI - PO - RMU	1d	14-Mar-28*	14-Mar-28	0%																																	
■ Site / Civil / Utilities		231d	29-May-26 A	03-Mar-27	19.5%																																	
■ Delay Fragnets		24d	29-May-																																			

HRL1 - Preliminary Schedule A1 - Rev.00 - Draft
#05.3.1.B1



03-Sep-26

Activity ID	Activity Name	Original Duration	Start	Finish	Duration % Complete	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
FOU.B1.DH4.10	Interior UnderSlab Plumbing	25d	18-Nov-26	16-Dec-26	0%																																	
FOU.B1.DH4.15	Excavation for Footings	40d	18-Nov-26	01-Jan-27	0%																																	
FOU.B1.DH4.20	Footing Rebar Installation	40d	23-Nov-26	06-Jan-27	0%																																	
FOU.B1.DH4.25	Install Utility Foundation Sleeves	5d	24-Nov-26	30-Nov-26	0%																																	
FOU.B1.DH4.30	Interior underSlab electrical	20d	25-Nov-26	17-Dec-26	0%																																	
FOU.B1.DH4.35	Footing Grounding	1d	26-Nov-26	27-Nov-26	0%																																	
FOU.B1.DH4.40	Footing Concrete Placement	36d	30-Nov-26	08-Jan-27	0%																																	
FOU.B1.DH4.45	Backfill and Compaction	3d	08-Jan-27	12-Jan-27	0%																																	
Building 1 - Admin		5d	12-Oct-26	16-Oct-26	0%																																	
FOU.B1.ADM.10	Install Utility Foundation Sleeves	5d	12-Oct-26	16-Oct-26	0%																																	
Building1 Mechanical Yard		89d	23-Oct-26	01-Feb-27	0%																																	
FOU.B1.MY.10	Mechanical Yard Pad Buildout	31d	23-Oct-26	27-Nov-26	0%																																	
FOU.B1.MY.20	Mechanical Yard Pad Certification	3d	27-Nov-26	01-Dec-26	0%																																	
FOU.B1.MY.15	Mechanical Yard RAM Aggregate Piers	19d	01-Dec-26	22-Dec-26	0%																																	
FOU.B1.MY.25	Layout and Dig Spread Footings	7d	22-Dec-26	30-Dec-26	0%																																	
FOU.B1.MY.30	Install Formwork and Rebar for Spread Footings	7d	30-Dec-26	06-Jan-27	0%																																	
FOU.B1.MY.35	Install Grounding	5d	07-Jan-27	12-Jan-27	0%																																	
FOU.B1.MY.40	Place Concrete for Spread Footings	12d	13-Jan-27	26-Jan-27	0%																																	
FOU.B1.MY.45	Install Mechanical Steel Platform - Mezzanine	5d	26-Jan-27	01-Feb-27	0%																																	
FS Substation		8d	07-Aug-26	17-Aug-26	0%																																	
A21120	FS Substation Pad Build out	5d	07-Aug-26	12-Aug-26	0%																																	
A21130	FS Substation Ram Aggregate Piers	3d	13-Aug-26	17-Aug-26	0%																																	
Underground Utilities		0d			0%																																	
Building 1		0d			0%																																	
Building 1 - Exterior UG		0d			0%																																	
Building 1 - Data Hall 1 & Admin - Exterior UG		0d			0%																																	
Building 1 - Data Hall 2 - Exterior UG		0d			0%																																	
Building 1 - Data Hall 3 - Exterior UG		0d			0%																																	
Building 1 - Data Hall 4 - Exterior UG		0d			0%																																	
Building 1 - Interior UG		0d			0%																																	
Building 1 - Data Hall 1 & Admin - Interior UG		0d			0%																																	
Building 1 - Data Hall 2 - Interior UG		0d			0%																																	
Building 1 - Data Hall 3 - Interior UG		0d			0%																																	
Building 1 - Data Hall 4 - Interior UG		0d			0%																																	
Structural Steel / Envelope		170d	20-Nov-26	31-May-27	0%																																	
Building 1		170d	20-Nov-26	31-May-27	0%																																	
Building 1 - Data Hall 1		71d	20-Nov-26	09-Feb-27	0%																																	
B1.STRC.DH1.10	BLDG 1 - Data Hall 1 - Set Primary Steel	29d	20-Nov-26	23-Dec-26	0%																																	
B1.STRC.DH1.15	BLDG 1 - Data Hall 1 - Install Secondary Steel	28d	04-Dec-26	05-Jan-27	0%																																	
B1.STRC.DH1.20	BLDG 1 - Data Hall 1 - Roof Decking	4d	04-Jan-27	07-Jan-27	0%																																	
B1.STRC.DH1.25	BLDG 1 - Data Hall 1 - Precast Wall Panel	19d	15-Jan-27	05-Feb-27	0%																																	
B1.STRC.DH1.30	BLDG 1 - Data Hall 1 - Roof Membrane - WaterProof	3d	05-Feb-27	09-Feb-27	0%																																	
Building 1 - Data Hall 2		71d	06-Jan-27	26-Mar-27	0%																																	
B1.STRC.DH2.10	BLDG 1 - Data Hall 2 - Set Primary Steel	29d	06-Jan-27	08-Feb-27	0%																																	
B1.STRC.DH2.15	BLDG 1 - Data Hall 2 - Install Secondary Steel	28d	20-Jan-27	19-Feb-27	0%																																	
B1.STRC.DH2.20	BLDG 1 - Data Hall 2 - Roof Decking	4d	18-Feb-27	23-Feb-27	0%																																	
B1.STRC.DH2.25	BLDG 1 - Data Hall 2 - Precast Wall Panel	19d	03-Mar-27	24-Mar-27	0%																																	
B1.STRC.DH2.30	BLDG 1 - Data Hall 2 - Roof Membrane - WaterProof	3d	24-Mar-27	26-Mar-27	0%																																	

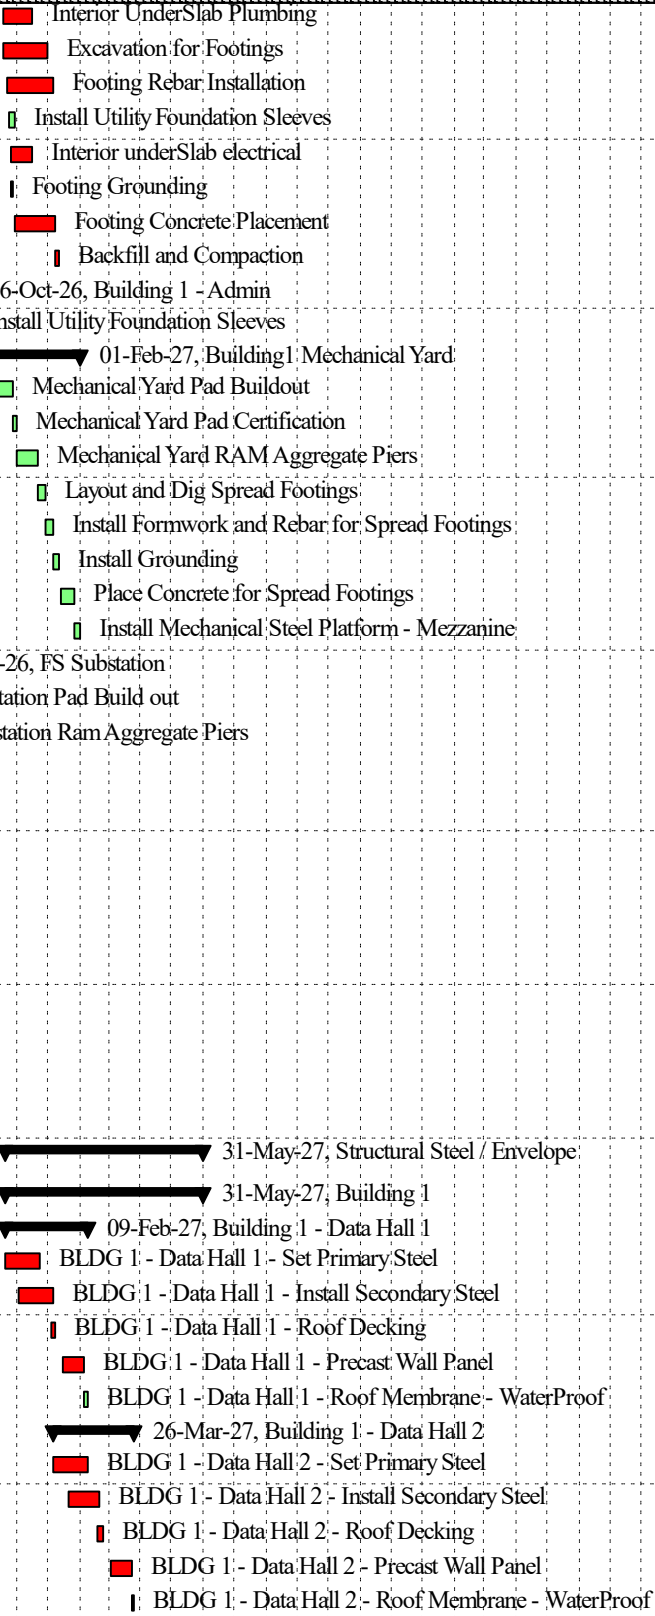

Actual Level of Effort Remaining Work Milestone
Actual Work Critical Remaining Work summary

Date	Revision	Checked	Approved
02-Sep-26	Preliminary Schedule	REDACTED	

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID		Activity Name	Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																											
1	Building 1 - Data Hall 3		71d	08-Feb-27	28-Apr-27	0%	28-Apr-27, Building 1 - Data Hall 3																											
	B1.STRC.DH3.10	BLDG 1 - Data Hall 3 - Set Primary Steel	29d	08-Feb-27	11-Mar-27	0%	BLDG 1 - Data Hall 3 - Set Primary Steel																											
	B1.STRC.DH3.15	BLDG 1 - Data Hall 3 - Install Secondary Steel	28d	22-Feb-27	24-Mar-27	0%	BLDG 1 - Data Hall 3 - Install Secondary Steel																											
	B1.STRC.DH3.20	BLDG 1 - Data Hall 3 - Roof Decking	4d	23-Mar-27	26-Mar-27	0%	BLDG 1 - Data Hall 3 - Roof Decking																											
	B1.STRC.DH3.25	BLDG 1 - Data Hall 3 - Precast Wall Panel	19d	05-Apr-27	26-Apr-27	0%	BLDG 1 - Data Hall 3 - Precast Wall Panel																											
	B1.STRC.DH3.30	BLDG 1 - Data Hall 3 - Roof Membrane - WaterProof	3d	26-Apr-27	28-Apr-27	0%	BLDG 1 - Data Hall 3 - Roof Membrane - WaterProof																											
	Building 1 - Data Hall 4		71d	11-Mar-27	31-May-27	0%	31-May-27, Building 1 - Data Hall 4																											
	B1.STRC.DH4.10	BLDG 1 - Data Hall 4 - Set Primary Steel	29d	11-Mar-27	13-Apr-27	0%	BLDG 1 - Data Hall 4 - Set Primary Steel																											
	B1.STRC.DH4.15	BLDG 1 - Data Hall 4 - Install Secondary Steel	28d	25-Mar-27	26-Apr-27	0%	BLDG 1 - Data Hall 4 - Install Secondary Steel																											
	B1.STRC.DH4.20	BLDG 1 - Data Hall 4 - Roof Decking	4d	23-Apr-27	28-Apr-27	0%	BLDG 1 - Data Hall 4 - Roof Decking																											
	B1.STRC.DH4.25	BLDG 1 - Data Hall 4 - Precast Wall Panel	19d	06-May-27	27-May-27	0%	BLDG 1 - Data Hall 4 - Precast Wall Panel																											
	B1.STRC.DH4.30	BLDG 1 - Data Hall 4 - Roof Membrane - WaterProof	3d	27-May-27	31-May-27	0%	BLDG 1 - Data Hall 4 - Roof Membrane - WaterProof																											
	Building 1 - Admin		61d	23-Dec-26	02-Mar-27	0%	02-Mar-27, Building 1 - Admin																											
	B1.STRC.ADM.10	BLDG 1 - ADMIN - Set Primary Steel	13d	23-Dec-26	06-Jan-27	0%	BLDG 1 - ADMIN - Set Primary Steel																											
	B1.STRC.ADM.15	BLDG 1 - ADMIN - Install Secondary Steel	13d	05-Jan-27	19-Jan-27	0%	BLDG 1 - ADMIN - Install Secondary Steel																											
	B1.STRC.ADM.20	BLDG 1 - ADMIN - Roof Decking	3d	19-Jan-27	21-Jan-27	0%	BLDG 1 - ADMIN - Roof Decking																											
	B1.STRC.ADM.25	BLDG 1 - ADMIN - Precast Wall Panel	19d	05-Feb-27	26-Feb-27	0%	BLDG 1 - ADMIN - Precast Wall Panel																											
	B1.STRC.ADM.30	BLDG 1 - Admin - Roof Membrane - WaterProof	3d	26-Feb-27	02-Mar-27	0%	BLDG 1 - Admin - Roof Membrane - WaterProof																											
	SOG		106d	07-Jan-27	06-May-27	0%	06-May-27, SOG																											
	Building 1		106d	07-Jan-27	06-May-27	0%	06-May-27, Building 1																											
	Building 1 - Data Hall 1		7d	07-Jan-27	15-Jan-27	0%	15-Jan-27, Building 1 - Data Hall 1																											
	B1.DH1.FND.150	F/R/P & Cure SOG	7d	07-Jan-27	15-Jan-27	0%	F/R/P & Cure SOG																											
	Building 1 - Data Hall 2		7d	23-Feb-27	03-Mar-27	0%	03-Mar-27, Building 1 - Data Hall 2																											
	B1.DH2.FND.150	F/R/P & Cure SOG	7d	23-Feb-27	03-Mar-27	0%	F/R/P & Cure SOG																											
	Building 1 - Data Hall 3		7d	26-Mar-27	05-Apr-27	0%	05-Apr-27, Building 1 - Data Hall 3																											
	B1.DH3.FND.150	F/R/P & Cure SOG	7d	26-Mar-27	05-Apr-27	0%	F/R/P & Cure SOG																											
	Building 1 - Data Hall 4		7d	28-Apr-27	06-May-27	0%	06-May-27, Building 1 - Data Hall 4																											
	B1.DH4.FND.150	F/R/P & Cure SOG	7d	28-Apr-27	06-May-27	0%	F/R/P & Cure SOG																											
	Building 1 - Admin		7d	21-Jan-27	29-Jan-27	0%	29-Jan-27, Building 1 - Admin																											
	B1.ADMIN.FND.150	F/R/P & Cure SOG	7d	21-Jan-27	29-Jan-27	0%	F/R/P & Cure SOG																											
	Equipment Pads		337d	07-Aug-26	19-Aug-27	0%	19-Aug-27, Equipment Pads																											
	Building 1		337d	07-Aug-26	19-Aug-27	0%	19-Aug-27, Building 1																											
	Electrical Yard		337d	07-Aug-26	19-Aug-27	0%	19-Aug-27, Electrical Yard																											
	Electrical Yard - Bldg 1 - DH1 & Admin		337d	07-Aug-26	19-Aug-27	0%	19-Aug-27, Electrical Yard - Bldg 1 - DH1 & Admin																											
	FOU.B1.EY.10	Electrical Yard Pad Buildout	31d	07-Aug-26	10-Sep-26	0%	Electrical Yard Pad Buildout																											
	FOU.B1.EY.15	Electrical Yard Pad Certification	3d	11-Sep-26	14-Sep-26	0%	Electrical Yard Pad Certification																											
	FOU.B1.EY.20	Electrical Yard RAM Aggregate Piers	19d	15-Sep-26	05-Oct-26	0%	Electrical Yard RAM Aggregate Piers																											
	FOU.B1.EY.25	Layout Underground	5d	03-Mar-27	09-Mar-27	0%	Layout Underground																											
	FOU.B1.EY.40	Excavation for Duct Banks	8d	24-Mar-27	01-Apr-27	0%	Excavation for Duct Banks																											
	FOU.B1.EY.45	UG Temporary Power	5d	24-Mar-27	30-Mar-27	0%	UG Temporary Power																											
FOU.B1.EY.50	Excavation Bedding	3d	01-Apr-27	05-Apr-27	0%	Excavation Bedding																												
FOU.B1.EY.56	Install Rebar for Duct Bank - Lower	5d	05-Apr-27	09-Apr-27	0%	Install Rebar for Duct Bank - Lower																												
FOU.B1.EY.60	Install Conduit and Duct Banks	25d	06-Apr-27	04-May-27	0%	Install Conduit and Duct Banks																												
FOU.B1.EY.66	Install Floor Boxes	25d	06-Apr-27	04-May-27	0%	Install Floor Boxes																												
FOU.B1.EY.70	Install Fiber Conduit	13d	08-Apr-27	22-Apr-27	0%	Install Fiber Conduit																												
FOU.B1.EY.67	Install Ground Grid	6d	09-Apr-27	16-Apr-27	0%	Install Ground Grid																												
FOU.B1.EY.80	Install Rebar for Duct Bank - Upper	5d	16-Apr-27	22-Apr-27	0%	Install Rebar for Duct Bank - Upper																												

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID	Activity Name	Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																																															
FOU.B1.EY.85	Grounding & Bonding	5d	22-Apr-27	28-Apr-27	0%																																																
FOU.B1.EY.90	Underground Inspection	1d	04-May-27	05-May-27	0%																																																
FOU.B1.EY.95	Concrete Encasement	9d	05-May-27	14-May-27	0%																																																
FOU.B1.EY.100	Backfill/Compaction	5d	14-May-27	20-May-27	0%																																																
FOU.B1.EY.105	Install Equipment Pad/Curing	9d	20-May-27	31-May-27	0%																																																
FOU.B1.EY.110	Install RMU	6d	31-May-27	07-Jun-27	0%																																																
FOU.B1.EY.115	Install Pad Mount VFI SS + Submersible	6d	31-May-27	07-Jun-27	0%																																																
FOU.B1.EY.120	Set MV Transformer - Solid Ground (double tap)	13d	31-May-27	14-Jun-27	0%																																																
FOU.B1.EY.125	Install/Set Generator 1.5 MW	8d	31-May-27	08-Jun-27	0%																																																
FOU.B1.EY.140	Set Admin UPS	9d	31-May-27	09-Jun-27	0%																																																
FOU.B1.EY.145	Set CDU UPS	9d	31-May-27	09-Jun-27	0%																																																
FOU.B1.EY.150	Set Low Voltage Switchgear – Mechanical	13d	31-May-27	14-Jun-27	0%																																																
FOU.B1.EY.155	Set Low Voltage Switchgear – IT Loads	13d	31-May-27	14-Jun-27	0%																																																
FOU.B1.EY.160	Set Low Voltage Switchgear –	13d	31-May-27	14-Jun-27	0%																																																
FOU.B1.EY.165	Anchor for Equipment	6d	31-May-27	07-Jun-27	0%																																																
FOU.B1.EY.170	Fibre Cable Pulling	5d	31-May-27	04-Jun-27	0%																																																
FOU.B1.EY.195	Pull Wire for RMU & Transformer	15d	07-Jun-27	23-Jun-27	0%																																																
FOU.B1.EY.180	Set Pad Mounted Switchgear	9d	07-Jun-27	16-Jun-27	0%																																																
FOU.B1.EY.185	Set ATS	15d	08-Jun-27	24-Jun-27	0%																																																
FOU.B1.EY.190	Set Network UPS	9d	14-Jun-27	23-Jun-27	0%																																																
FOU.B1.EY.205	Grounding and Bonding Of RMU & Transformer	9d	23-Jun-27	02-Jul-27	0%																																																
FOU.B1.EY.200	Pull Wire from Substation to Eletrical Yard & Testing	25d	24-Jun-27	22-Jul-27	0%																																																
FOU.B1.EY.210	RMU - Transformer Cable and Connections Testing	13d	02-Jul-27	16-Jul-27	0%																																																
FOU.B1.EY.215	Wire Termination	25d	22-Jul-27	19-Aug-27	0%																																																
Electrical Yard - Bldg 1 - DH2		138d	07-Aug-26	08-Jan-27	0%																																																
FOU.B1.EY.455	Layout Underground	5d	07-Aug-26	12-Aug-26	0%																																																
FOU.B1.EY.565	Electrical Yard Pad Buildout	31d	07-Aug-26	10-Sep-26	0%																																																
FOU.B1.EY.245	Excavation for Duct Banks	8d	13-Aug-26	20-Aug-26	0%																																																
FOU.B1.EY.495	UG Temporary Power	5d	13-Aug-26	18-Aug-26	0%																																																
FOU.B1.EY.235	Excavation Bedding	3d	21-Aug-26	24-Aug-26	0%																																																
FOU.B1.EY.465	Install Rebar for Duct Bank - Lower	5d	25-Aug-26	28-Aug-26	0%																																																
FOU.B1.EY.255	Install Conduit and Duct Banks	25d	26-Aug-26	23-Sep-26	0%																																																
FOU.B1.EY.555	Install Floor Boxes	25d	26-Aug-26	23-Sep-26	0%																																																
FOU.B1.EY.485	Install Fiber Conduit	13d	28-Aug-26	11-Sep-26	0%																																																
FOU.B1.EY.265	Install Ground Grid	6d	31-Aug-26	04-Sep-26	0%																																																
FOU.B1.EY.475	Install Rebar for Duct Bank - Upper	5d	07-Sep-26	10-Sep-26	0%																																																
FOU.B1.EY.505	Grounding & Bonding	5d	11-Sep-26	16-Sep-26	0%																																																
FOU.B1.EY.585	Electrical Yard Pad Certification	3d	11-Sep-26	14-Sep-26	0%																																																
FOU.B1.EY.575	Electrical Yard RAM Aggregate Piers	19d	15-Sep-26	05-Oct-26	0%																																																

alston
CONSTRUCTION
MISSION CRITICAL

[illegible]

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID		Activity Name	Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																																																
Electrical Yard - Bldg 1 - DH4	FOU.B1.EY.815	Set ATS	15d	28-Oct-26	13-Nov-26	0%	Set ATS																																																
	FOU.B1.EY.755	Set Network UPS	9d	03-Nov-26	12-Nov-26	0%	Set Network UPS																																																
	FOU.B1.EY.695	Grounding and Bonding Of RMU & Transformer	9d	12-Nov-26	23-Nov-26	0%	Grounding and Bonding Of RMU & Transformer																																																
	FOU.B1.EY.885	Pull Wire from Substation to Eletrical Yard & Testing	25d	13-Nov-26	11-Dec-26	0%	Pull Wire from Substation to Eletrical Yard & Testing																																																
	FOU.B1.EY.705	RMU - Transformer Cable and Connections Testing	13d	23-Nov-26	07-Dec-26	0%	RMU - Transformer Cable and Connections Testing																																																
	FOU.B1.EY.895	Wire Termination	25d	11-Dec-26	08-Jan-27	0%	Wire Termination																																																
	Electrical Yard - Bldg 1 - DH4			138d	07-Aug-26	08-Jan-27	0%	08-Jan-27, Electrical Yard - Bldg 1 - DH4																																															
	FOU.B1.EY.1195	Layout Underground	5d	07-Aug-26	12-Aug-26	0%	Layout Underground																																																
	FOU.B1.EY.1305	Electrical Yard Pad Buildout	31d	07-Aug-26	10-Sep-26	0%	Electrical Yard Pad Buildout																																																
	FOU.B1.EY.985	Excavation for Duct Banks	8d	13-Aug-26	20-Aug-26	0%	Excavation for Duct Banks																																																
	FOU.B1.EY.1235	UG Temporary Power	5d	13-Aug-26	18-Aug-26	0%	UG Temporary Power																																																
	FOU.B1.EY.975	Excavation Bedding	3d	21-Aug-26	24-Aug-26	0%	Excavation Bedding																																																
	FOU.B1.EY.1205	Install Rebar for Duct Bank - Lower	5d	25-Aug-26	28-Aug-26	0%	Install Rebar for Duct Bank - Lower																																																
	FOU.B1.EY.995	Install Conduit and Duct Banks	25d	26-Aug-26	23-Sep-26	0%	Install Conduit and Duct Banks																																																
	FOU.B1.EY.1295	Install Floor Boxes	25d	26-Aug-26	23-Sep-26	0%	Install Floor Boxes																																																
	FOU.B1.EY.1225	Install Fiber Conduit	13d	28-Aug-26	11-Sep-26	0%	Install Fiber Conduit																																																
	FOU.B1.EY.1005	Install Ground Grid	6d	31-Aug-26	04-Sep-26	0%	Install Ground Grid																																																
	FOU.B1.EY.1215	Install Rebar for Duct Bank - Upper	5d	07-Sep-26	10-Sep-26	0%	Install Rebar for Duct Bank - Upper																																																
	FOU.B1.EY.1245	Grounding & Bonding	5d	11-Sep-26	16-Sep-26	0%	Grounding & Bonding																																																
	FOU.B1.EY.1325	Electrical Yard Pad Certification	3d	11-Sep-26	14-Sep-26	0%	Electrical Yard Pad Certification																																																
	FOU.B1.EY.1315	Electrical Yard RAM Aggregate Piers	19d	15-Sep-26	05-Oct-26	0%	Electrical Yard RAM Aggregate Piers																																																
	FOU.B1.EY.1015	Underground Inspection	1d	23-Sep-26	24-Sep-26	0%	Underground Inspection																																																
	FOU.B1.EY.1025	Concrete Encasement	9d	24-Sep-26	05-Oct-26	0%	Concrete Encasement																																																
	FOU.B1.EY.1035	Backfill/Compaction	5d	05-Oct-26	09-Oct-26	0%	Backfill/Compaction																																																
	FOU.B1.EY.965	Install Equipment Pad/Curing	9d	09-Oct-26	20-Oct-26	0%	Install Equipment Pad/Curing																																																
	FOU.B1.EY.1045	Install RMU	6d	20-Oct-26	27-Oct-26	0%	Install RMU																																																
	FOU.B1.EY.1095	Install Pad Mount VFI SS + Submersible	6d	20-Oct-26	27-Oct-26	0%	Install Pad Mount VFI SS + Submersible																																																
	FOU.B1.EY.1105	Set MV Transformer - Solid Ground (double tap)	13d	20-Oct-26	03-Nov-26	0%	Set MV Transformer - Solid Ground (double tap)																																																
	FOU.B1.EY.1115	Install/Set Generator 1.5 MW	8d	20-Oct-26	28-Oct-26	0%	Install/Set Generator 1.5 MW																																																
	FOU.B1.EY.1135	Set Admin UPS	9d	20-Oct-26	29-Oct-26	0%	Set Admin UPS																																																
	FOU.B1.EY.1145	Set CDU UPS	9d	20-Oct-26	29-Oct-26	0%	Set CDU UPS																																																
	FOU.B1.EY.1155	Set Low Voltage Switchgear – Mechanical	13d	20-Oct-26	03-Nov-26	0%	Set Low Voltage Switchgear – Mechanical																																																
	FOU.B1.EY.1165	Set Low Voltage Switchgear – IT Loads	13d	20-Oct-26	03-Nov-26	0%	Set Low Voltage Switchgear – IT Loads																																																
	FOU.B1.EY.1175	Set Low Voltage Switchgear –	13d	20-Oct-26	03-Nov-26	0%	Set Low Voltage Switchgear –																																																
	FOU.B1.EY.1275	Anchor for Equipment	6d	20-Oct-26	27-Oct-26	0%	Anchor for Equipment																																																
	FOU.B1.EY.1285	Fibre Cable Pulling	5d	20-Oct-26	26-Oct-26	0%	Fibre Cable Pulling																																																
	FOU.B1.EY.1055	Pull Wire for RMU & Transformer	15d	27-Oct-26	12-Nov-26	0%	Pull Wire for RMU & Transformer																																																
	FOU.B1.EY.1085	Set Pad Mounted Switchgear	9d	27-Oct-26	05-Nov-26	0%	Set Pad Mounted Switchgear																																																
	FOU.B1.EY.1185	Set ATS	15d	28-Oct-26	13-Nov-26	0%	Set ATS																																																
	FOU.B1.EY.1125	Set Network UPS	9d	03-Nov-26	12-Nov-26	0%	Set Network UPS																																																
	FOU.B1.EY.1065	Grounding and Bonding Of RMU & Transformer	9d	12-Nov-26	23-Nov-26	0%	Grounding and Bonding Of RMU & Transformer																																																
	FOU.B1.EY.1255	Pull Wire from Substation to Eletrical Yard & Testing	25d	13-Nov-26	11-Dec-26	0%	Pull Wire from Substation to Eletrical Yard & Testing																																																
	FOU.B1.EY.1075	RMU - Transformer Cable and Connections Testing	13d	23-Nov-26	07-Dec-26	0%	RMU - Transformer Cable and Connections Testing																																																
	FOU.B1.EY.1265	Wire Termination	25d	11-Dec-26	08-Jan-27	0%	Wire Termination																																																
	Mechanical Yard			269d	07-Aug-26	03-Jun-27	0%	<																																															

alston
CONSTRUCTION
MISSION CRITICAL

[illegible]

HRL1 - Preliminary Schedule A1 - Rev.00 - Draft
#05.3.1.B1



03-Sep-26

Activity ID	Activity Name	Original Duration	Start	Finish	Duration % Complete	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	
MECHANICAL	MYB1DH3-19	Install Layout, Hangers and Piping Supports	28d	20-Nov-26	22-Dec-26	0%																																	
	MYB1DH3-22	Install Chiller Piping	38d	27-Nov-26	08-Jan-27	0%																																	
	MYB1DH3-18	Set Air Cooled Chiller	7d	01-Dec-26	08-Dec-26	0%																																	
	MYB1DH3-20	Set Pumps - Expan, TES Tanks	16d	09-Dec-26	25-Dec-26	0%																																	
	MYB1DH3-21	Controls - Instrumentation	6d	25-Dec-26	01-Jan-27	0%																																	
	MYB1DH3-23	Testing	6d	08-Jan-27	15-Jan-27	0%																																	
	MYB1DH3-25	Chiller Pipe Insulation	38d	15-Jan-27	26-Feb-27	0%																																	
	MYB1DH3-24	Flushing	8d	15-Jan-27	25-Jan-27	0%																																	
	Mechanical Yard - Bldg 1 - DH4			146d	27-Oct-26	08-Apr-27	0%																																
	MYB1DH4-10	Layout Underground Utilities	1d	27-Oct-26	28-Oct-26	0%																																	
	MYB1DH4-11	Install UG Mechanical Utilities & Start Excavation	4d	28-Oct-26	02-Nov-26	0%																																	
	MYB1DH4-12	Install UG Start Excavation	7d	28-Oct-26	04-Nov-26	0%																																	
	MYB1DH4-13	Layout & Install Grounding & Start Excavation	7d	30-Oct-26	06-Nov-26	0%																																	
	MYB1DH4-14	Layout and Dig Spread Footings	7d	06-Nov-26	16-Nov-26	0%																																	
	MYB1DH4-15	Install Formwork and Rebar for Spread Footings	7d	16-Nov-26	23-Nov-26	0%																																	
	MYB1DH4-16	Pour Concrete for Spread Footings	12d	23-Nov-26	07-Dec-26	0%																																	
	MYB1DH4-17	CHWP - Mezzanine Supports & Platform	28d	07-Dec-26	06-Jan-27	0%																																	
	MYB1DH4-19	Install Layout, Hangers and Piping Supports	28d	31-Dec-26	01-Feb-27	0%																																	
	MYB1DH4-22	Install Chiller Piping	38d	07-Jan-27	18-Feb-27	0%																																	
	MYB1DH4-18	Set Air Cooled Chiller	7d	11-Jan-27	18-Jan-27	0%																																	
	MYB1DH4-20	Set Pumps - Expan, TES Tanks	16d	18-Jan-27	04-Feb-27	0%																																	
	MYB1DH4-21	Controls - Instrumentation	6d	04-Feb-27	11-Feb-27	0%																																	
	MYB1DH4-23	Testing	6d	18-Feb-27	25-Feb-27	0%																																	
	MYB1DH4-25	Chiller Pipe Insulation	38d	25-Feb-27	08-Apr-27	0%																																	
MYB1DH4-24	Flushing	8d	25-Feb-27	05-Mar-27	0%																																		
MEP Fit Out			3d	07-Aug-26	10-Aug-26	0%																																	
RTUs			3d	07-Aug-26	10-Aug-26	0%																																	
A2890	Receive and stage	1d	07-Aug-26	07-Aug-26	0%																																		
A2900	Rig and set	1d	07-Aug-26	07-Aug-26	0%																																		
A2910	Complete curb & duct	3d	07-Aug-26	10-Aug-26	0%																																		
A2920	Complete piping & drains	3d	07-Aug-26	10-Aug-26	0%																																		
A2930	Inspect for TAB	1d	07-Aug-26	07-Aug-26	0%																																		
A2940	Startup/TAB	3d	07-Aug-26	10-Aug-26	0%																																		

Actual Level of Effort Remaining Work Milestone
Actual Work Critical Remaining Work summary

Date	Revision	Checked	Approved
02-Sep-26	Preliminary Schedule	REDACTED	

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID	Activity Name	Original Duration	Start	Finish	Duration % Complete																																				
						A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D			
Network HAC Supply & Manifold		20d	04-May-27	25-May-27	0%	25-May-27, Network HAC Supply & Manifold																																			
A3130	Receive materials	3d	04-May-27	05-May-27	0%	Receive materials																																			
A3140	Layout routing	3d	06-May-27	07-May-27	0%	Layout routing																																			
A3150	Install supports	3d	10-May-27	11-May-27	0%	Install supports																																			
A3160	Install manifolds	5d	12-May-27	17-May-27	0%	Install manifolds																																			
A3170	Tie-ins & pressure test	5d	18-May-27	21-May-27	0%	Tie-ins & pressure test																																			
A3180	Flush & turnover	3d	24-May-27	25-May-27	0%	Flush & turnover																																			
Air-Cooled Chillers		84d	17-Jun-27	17-Sep-27	0%	17-Sep-27, Air-Cooled Chillers																																			
A2590	Receive and stage chillers	15d	17-Jun-27	02-Jul-27	0%	Receive and stage chillers																																			
A2600	Rig and set chillers	15d	23-Jun-27	08-Jul-27	0%	Rig and set chillers																																			
A2610	Install supports, isolation and accessories	23d	29-Jun-27	22-Jul-27	0%	Install supports, isolation and accessories																																			
A2620	Complete supply/return piping tie-ins	44d	06-Jul-27	23-Aug-27	0%	Complete supply/return piping tie-ins																																			
A2630	Pressure test, flush and fill	29d	26-Jul-27	25-Aug-27	0%	Pressure test, flush and fill																																			
A2640	Startup and functional testing	44d	02-Aug-27	17-Sep-27	0%	Startup and functional testing																																			
Fan Coil Wall Units		62d	17-May-27	23-Jul-27	0%	23-Jul-27, Fan Coil Wall Units																																			
A2650	Receive and distribute units	8d	17-May-27	24-May-27	0%	Receive and distribute units																																			
A2660	Install wall units and supports	11d	25-May-27	04-Jun-27	0%	Install wall units and supports																																			
FO-B1-DH1-25	Install Fan Coil Wall	15d	25-May-27	09-Jun-27	0%	Install Fan Coil Wall																																			
A2670	Install piping connections	18d	07-Jun-27	24-Jun-27	0%	Install piping connections																																			
A2680	Install condensate and accessories	11d	25-Jun-27	07-Jul-27	0%	Install condensate and accessories																																			
A2690	Pressure test and inspect	7d	08-Jul-27	15-Jul-27	0%	Pressure test and inspect																																			
A2700	Startup and functional testing	7d	15-Jul-27	23-Jul-27	0%	Startup and functional testing																																			
CDU Manifolds		293d	10-May-27	31-Mar-28	0%	31-Mar-28, CDU Manifolds																																			
A3190	Receive & distribute	10d	10-May-27	19-May-27	0%	Receive & distribute																																			
A3200	Layout	10d	10-Dec-27	22-Dec-27	0%	Layout																																			
A3210	Install supports	15d	22-Dec-27	07-Jan-28	0%	Install supports																																			
A3220	Install manifolds & piping	30d	07-Jan-28	10-Feb-28	0%	Install manifolds & piping																																			
A3230	Tie-ins & testing	30d	10-Feb-28	15-Mar-28	0%	Tie-ins & testing																																			
A3240	Flush & turnover	15d	15-Mar-28	31-Mar-28	0%	Flush & turnover																																			
CDUs		10d	22-Nov-27	01-Dec-27	0%	01-Dec-27, CDUs																																			
A2950	Receive and distribute	1d	22-Nov-27	22-Nov-27	0%	Receive and distribute																																			
A2970	Install supply/return piping	4d	22-Nov-27	25-Nov-27	0%	Install supply/return piping																																			
A2980	Install SD83/hoses	2d	26-Nov-27	29-Nov-27	0%	Install SD83/hoses																																			
FO-B1-DH1-40	Install Coolant Distribution Unit – CDU (OFOI)	1d	29-Nov-27	30-Nov-27	0%	Install Coolant Distribution Unit – CDU (OFOI)																																			
A3000	Startup & testing	2d	30-Nov-27	01-Dec-27	0%	Startup & testing																																			
CHILLED WATER PIPING		106d	15-Apr-27	12-Aug-27	0%	12-Aug-27, CHILLED WATER PIPING																																			
FO-B1-DH1-135	Chilled Water Pipe Rough-in	45d	15-Apr-27	04-Jun-27	0%	Chilled Water Pipe Rough-in																																			
FO-B1-DH1-175	CHW Final Connection	25d	15-Jul-27	12-Aug-27	0%	CHW Final Connection																																			
FIRE SPRINKLER & FIRESTOP		233d	24-Feb-27	12-Nov-27	0%	12-Nov-27, FIRE SPRINKLER & FIRESTOP																																			
FO-B1-DH1-55	Sprinkler System Rough In	60d	24-Feb-27	03-May-27	0%	Sprinkler System Rough In																																			
FO-B1-DH1-95	Sprinkler System Trim Out	25d	11-Oct-27	08-Nov-27	0%	Sprinkler System Trim Out																																			
FO-B1-DH1-195	Firestop Install	20d	21-Oct-27	12-Nov-27	0%	Firestop Install																																			
CRAC Units		20d	15-Apr-27	07-May-27	0%	07-May-27, CRAC Units																																			
A2770	Receive and stage CRACs	3d	15-Apr-27	19-Apr-27	0%	Receive and stage CRACs																																			
FO-B1-DH1-50	Install CRAC Unit	5d	15-Apr-27	21-Apr-27	0%	Install CRAC Unit																																			
A2780	Set condensing units	3d	19-Apr-27	21-Apr-27	0%	Set condensing units																																			
A2790	Install refrigerant piping	5d	21-Apr-27	27-Apr-27	0%	Install refrigerant piping																																			

alston
CONSTRUCTION
MISSION CRITICAL

[illegible]

alston
CONSTRUCTION
MISSION CRITICAL

[illegible]

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID	Activity Name	Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																												
FO-EL-B1-DH1-360	Testing & Continuity Checks	8d	21-Jan-28	31-Jan-28	0%	Testing & Continuity Checks																												
	Cooling (White Space)	0d			0%																													
	Lighting & Small Power	0d			0%																													
	Low Voltage & Monitoring	0d			0%																													
	Equipment Supports & Grounding	0d			0%																													
	Hot Aisle Containment	0d			0%																													
	Hangers & Supports	0d			0%																													
	Wall Sleeves & Firestopping	0d			0%																													
	General Install Sequence	0d			0%																													
	ELECTRICAL & UPS ROOMS		195d	09-Feb-27	15-Sep-27	0%	15-Sep-27, ELECTRICAL & UPS ROOMS																											
	Utility & Medium Voltage	195d	09-Feb-27	15-Sep-27	0%	15-Sep-27, Utility & Medium Voltage																												
	FO-EL-B1-DH1-10	Mobilization & Layout	6d	09-Feb-27	16-Feb-27	0%	Mobilization & Layout																											
	FO-EL-B1-DH1-15	Utility transformer pad & primary gear	6d	16-Feb-27	23-Feb-27	0%	Utility transformer pad & primary gear																											
	FO-EL-B1-DH1-20	Building grounding grid/ring installation	6d	16-Feb-27	23-Feb-27	0%	Building grounding grid/ring installation																											
	FO-EL-B1-DH1-25	Trapeze / strut support framing	10d	16-Feb-27	26-Feb-27	0%	Trapeze / strut support framing																											
	FO-EL-B1-DH1-30	Wall sleeve installation	8d	23-Feb-27	03-Mar-27	0%	Wall sleeve installation																											
	FO-EL-B1-DH1-35	Cable tray & ladder rack supports	8d	26-Feb-27	08-Mar-27	0%	Cable tray & ladder rack supports																											
	FO-EL-B1-DH1-40	Utility metering equipment	4d	08-Mar-27	11-Mar-27	0%	Utility metering equipment																											
	FO-EL-B1-DH1-45	Conduit hangers & supports	10d	11-Mar-27	23-Mar-27	0%	Conduit hangers & supports																											
	FO-EL-B1-DH1-50	Conduit & Box Rough-In	13d	11-Mar-27	25-Mar-27	0%	Conduit & Box Rough-In																											
	FO-EL-B1-DH1-60	Medium voltage (MV) switchgear	10d	25-Mar-27	06-Apr-27	0%	Medium voltage (MV) switchgear																											
	FO-EL-B1-DH1-55	Fire caulking / firestopping of penetrations	6d	25-Mar-27	01-Apr-27	0%	Fire caulking / firestopping of penetrations																											
	FO-EL-B1-DH1-65	Cable Tray / Raceway Install	13d	25-Mar-27	08-Apr-27	0%	Cable Tray / Raceway Install																											
	FO-EL-B1-DH1-70	MV feeder cable installation	13d	08-Apr-27	22-Apr-27	0%	MV feeder cable installation																											
	FO-EL-B1-DH1-80	Main switchboard / MDB installation	10d	22-Apr-27	04-May-27	0%	Main switchboard / MDB installation																											
	FO-EL-B1-DH1-75	Unit substation / step-down transformers	6d	22-Apr-27	29-Apr-27	0%	Unit substation / step-down transformers																											
	FO-EL-B1-DH1-85	Distribution switchboard installation	13d	04-May-27	18-May-27	0%	Distribution switchboard installation																											
	FO-EL-B1-DH1-90	Generator paralleling switchgear	10d	18-May-27	28-May-27	0%	Generator paralleling switchgear																											
	FO-EL-B1-DH1-95	Automatic Transfer Switch (ATS) installation	8d	28-May-27	07-Jun-27	0%	Automatic Transfer Switch (ATS) installation																											
	FO-EL-B1-DH1-100	UPS output distribution board	8d	07-Jun-27	15-Jun-27	0%	UPS output distribution board																											
	FO-EL-B1-DH1-105	UPS module installation	13d	15-Jun-27	29-Jun-27	0%	UPS module installation																											
	FO-EL-B1-DH1-110	UPS battery system installation	13d	15-Jun-27	29-Jun-27	0%	UPS battery system installation																											
	FO-EL-B1-DH1-115	Static Transfer Switch (STS) installation	6d	29-Jun-27	06-Jul-27	0%	Static Transfer Switch (STS) installation																											
	FO-EL-B1-DH1-120	Panel Install & Termination	10d	06-Jul-27	16-Jul-27	0%	Panel Install & Termination																											
	FO-EL-B1-DH1-125	Sub-metering installation	6d	16-Jul-27	23-Jul-27	0%	Sub-metering installation																											
	FO-EL-B1-DH1-130	Surge Protective Device (SPD) installation	5d	23-Jul-27	29-Jul-27	0%	Surge Protective Device (SPD) installation																											
	FO-EL-B1-DH1-135	Feeder conduit & cable installation	9d	29-Jul-27	09-Aug-27	0%	Feeder conduit & cable installation																											
	FO-EL-B1-DH1-140	Wire Pull	13d	09-Aug-27	23-Aug-27	0%	Wire Pull																											
	FO-EL-B1-DH1-145	Pull & Terminate Wire To Switchboard	13d	11-Aug-27	25-Aug-27	0%	Pull & Terminate Wire To Switchboard																											
	FO-EL-B1-DH1-150	Testing & Continuity Checks	8d	23-Aug-27	31-Aug-27	0%	Testing & Continuity Checks																											
	FO-EL-B1-DH1-155	Lighting Fixture Install	6d	25-Aug-27	01-Sep-27	0%	Lighting Fixture Install																											
	FO-EL-B1-DH1-160	Device & Receptacle Trim-Out	6d	25-Aug-27	01-Sep-27	0%	Device & Receptacle Trim-Out																											
	FO-EL-B1-DH1-165	Utility service energization coordination	6d	01-Sep-27	08-Sep-27	0%	Utility service energization coordination																											
	FO-EL-B1-DH1-170	Testing	6d	08-Sep-27	15-Sep-27	0%	Testing																											
	Main Distribution		0d			0%																												
	Standby Power Switching		0d			0%																												
	UPS & Critical Power (Room)		0d			0%																												
Grounding & Protection		0d			0%																													

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID		Activity Name	Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																																															
Hangers & Supports			0d			0%																																																
Wall Sleeves & Firestopping			0d			0%																																																
General Install Sequence			0d			0%																																																
			95d	05-Feb-27	24-May-27	0%	24-May-27,																																															
FO-EL-B1-DH1-490	Mobilization & Layout	6d	05-Feb-27	12-Feb-27	0%	Mobilization & Layout																																																
FO-EL-B1-DH1-495	Conduit hangers & supports	5d	12-Feb-27	18-Feb-27	0%	Conduit hangers & supports																																																
FO-EL-B1-DH1-500	Conduit & Box Rough-In	19d	18-Feb-27	11-Mar-27	0%	Conduit & Box Rough-In																																																
FO-EL-B1-DH1-505	Level 01 Cable Tray / Raceway Install	13d	11-Mar-27	25-Mar-27	0%	Level 01 Cable Tray / Raceway Install																																																
FO-EL-B1-DH1-510	Wire Pull	15d	25-Mar-27	12-Apr-27	0%	Wire Pull																																																
FO-EL-B1-DH1-515	Panel Install & Termination	10d	12-Apr-27	22-Apr-27	0%	Panel Install & Termination																																																
FO-EL-B1-DH1-520	Lighting Fixture Install	13d	12-Apr-27	26-Apr-27	0%	Lighting Fixture Install																																																
CONFIDENTIAL			10d	22-Apr-27	04-May-27	0%																																																
FO-EL-B1-DH1-530	Device & Receptacle Trim-Out	10d	04-May-27	14-May-27	0%	Device & Receptacle Trim-Out																																																
FO-EL-B1-DH1-535	Testing & Continuity Checks	8d	14-May-27	24-May-27	0%	Testing & Continuity Checks																																																
GALLERY			129d	02-Mar-27	23-Jul-27	0%	23-Jul-27, GALLERY																																															
Critical Power Distribution			129d	02-Mar-27	23-Jul-27	0%	23-Jul-27, Critical Power Distribution																																															
FO-EL-B1-DH1-175	Mobilization & Layout	6d	02-Mar-27	09-Mar-27	0%	Mobilization & Layout																																																
FO-EL-B1-DH1-180	Trapeze / strut support framing	10d	09-Mar-27	19-Mar-27	0%	Trapeze / strut support framing																																																
FO-EL-B1-DH1-185	Cable tray & ladder rack supports	8d	19-Mar-27	29-Mar-27	0%	Cable tray & ladder rack supports																																																
FO-EL-B1-DH1-190	Conduit hangers & supports	10d	29-Mar-27	08-Apr-27	0%	Conduit hangers & supports																																																
FO-EL-B1-DH1-200	Critical power busway installation	15d	08-Apr-27	26-Apr-27	0%	Critical power busway installation																																																
FO-EL-B1-DH1-195	Wall sleeve installation	8d	08-Apr-27	16-Apr-27	0%	Wall sleeve installation																																																
FO-EL-B1-DH1-210	Conduit & Box Rough-In	19d	16-Apr-27	07-May-27	0%	Conduit & Box Rough-In																																																
FO-EL-B1-DH1-205	Cable Tray / Raceway Install	13d	16-Apr-27	30-Apr-27	0%	Cable Tray / Raceway Install																																																
FO-EL-B1-DH1-215	Remote Power Panel (RPP) installation	13d	26-Apr-27	10-May-27	0%	Remote Power Panel (RPP) installation																																																
FO-EL-B1-DH1-220	Fire caulking / firestopping of penetrations	6d	07-May-27	14-May-27	0%	Fire caulking / firestopping of penetrations																																																
FO-EL-B1-DH1-225	Facility PDU installation	13d	10-May-27	24-May-27	0%	Facility PDU installation																																																
FO-EL-B1-DH1-230	Wire Pull	15d	24-May-27	09-Jun-27	0%	Wire Pull																																																
FO-EL-B1-DH1-235	Panel Install & Termination	10d	09-Jun-27	21-Jun-27	0%	Panel Install & Termination																																																
FO-EL-B1-DH1-240	Lighting Fixture Install	13d	21-Jun-27	05-Jul-27	0%	Lighting Fixture Install																																																
FO-EL-B1-DH1-245	Device & Receptacle Trim-Out	10d	05-Jul-27	15-Jul-27	0%	Device & Receptacle Trim-Out																																																
FO-EL-B1-DH1-250	Testing & Continuity Checks	8d	15-Jul-27	23-Jul-27	0%	Testing & Continuity Checks																																																
Hangers & Supports			0d			0%																																																
Wall Sleeves & Firestopping			0d			0%																																																
General Install Sequence			0d			0%																																																
Building 1 - Data Hall 2			346d	24-Mar-27	14-Apr-28	0%	14-Apr-28, Building 1 - Data Hall 2																																															
WALL & CEILING FINISHES			231d	24-Mar-27	08-Dec-27	0%	08-Dec-27, WALL & CEILING FINISHES																																															
FO-B1-DH1-1205	Layout Interior Walls	5d	24-Mar-27	30-Mar-27	0%	Layout Interior Walls																																																
FO-B1-DH1-1215	Frame Interior Walls	60d	25-Mar-27	01-Jun-27	0%	Frame Interior Walls																																																
FO-B1-DH1-1225	Overhead Mechanical & Plumbing Rough-in	60d	06-Apr-27	11-Jun-27	0%	Overhead Mechanical & Plumbing Rough-in																																																
FO-B1-DH1-1245	Electrical Overhead Rough-in	50d	06-Apr-27	01-Jun-27	0%	Electrical Overhead Rough-in																																																
FO-B1-DH1-1125	Structural Ceiling	60d	24-Aug-27	29-Oct-27	0%	Structural Ceiling																																																
FO-B1-DH1-1255	Wall Frame Tap-out	30d	13-Oct-27	16-Nov-27	0%	Wall Frame Tap-out																																																
FO-B1-DH1-1265	Above Ceiling MEP Completion	30d	19-Oct-27	22-Nov-27	0%	Above Ceiling MEP Completion																																																
FO-B1-DH1-1295	Dry Wall Finishing	30d	25-Oct-27	26-Nov-27	0%	Dry Wall Finishing																																																
FO-B1-DH1-1325	MEP Trimout	30d	04-Nov-27	08-Dec-27	0%	MEP Trimout																																																
Network HAC Supply & Manifold			20d	28-May-27	18-Jun-27	0%	18-Jun-27, Network HAC Supply & Manifold																																															
A21740	Receive materials	3d	28-May-27	31-May-27	0%	Receive materials																																																

alston
CONSTRUCTION
MISSION CRITICAL

[illegible]

alston
CONSTRUCTION
MISSION CRITICAL

[illegible]

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID																																
Activity Name																																
Original Duration																																
Start																																
Finish																																
Duration % Complete																																
A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
FO-EL-B1-DH1-4625 Fire caulking / firestopping of penetrations6d09-Jun-2716-Jun-270%							Fire caulking / firestopping of penetrations																									
FO-EL-B1-DH1-4445 Conduit hangers & supports13d23-Jun-2707-Jul-270%							Conduit hangers & supports																									
FO-EL-B1-DH1-4565 Wire Pull15d23-Jun-2709-Jul-270%							Wire Pull																									
FO-EL-B1-DH1-4465 Lighting fixture & device support/backing8d07-Jul-2715-Jul-270%							Lighting fixture & device support/backing																									
FO-EL-B1-DH1-4575 Panel Install & Termination10d09-Jul-2721-Jul-270%							Panel Install & Termination																									
FO-EL-B1-DH1-4455 Emergency/egress lighting installation8d21-Jul-2729-Jul-270%							Emergency/egress lighting installation																									
CONFIDENTIAL 10d29-Jul-2710-Aug-270%																																
FO-EL-B1-DH1-4585 Lighting Fixture Install13d10-Aug-2724-Aug-270%							Lighting Fixture Install																									
CONFIDENTIAL 6d24-Aug-2731-Aug-270%																																
FO-EL-B1-DH1-4595 Device & Receptacle Trim-Out10d24-Aug-2703-Sep-270%							Device & Receptacle Trim-Out																									
CONFIDENTIAL 6d31-Aug-2707-Sep-270%																																
CONFIDENTIAL 8d07-Sep-2715-Sep-270%																																
FO-EL-B1-DH1-4525 Telecom/fiber entrance & structured cabling power10d15-Sep-2727-Sep-270%							Telecom/fiber entrance & structured cabling power																									
CONFIDENTIAL 8d27-Sep-2705-Oct-270%																																
FO-EL-B1-DH1-4605 Testing & Continuity Checks8d05-Oct-2713-Oct-270%							Testing & Continuity Checks																									
Lighting & Egress0d0%0%																																
Life Safety & Fire0d0%0%																																
Low Voltage & Security0d0%0%																																
Hangers & Supports0d0%0%																																
Wall Sleeves & Firestopping0d0%0%																																
General Install Sequence0d0%0%																																
DATA HALL — WHITE SPACE279d06-Apr-2714-Feb-280%							14-Feb-28, DATA HALL — WH																									
Rack Power Distribution279d06-Apr-2714-Feb-280%							14-Feb-28, Rack Power Distributi																									
FO-EL-B1-DH1-4345 Mobilization & Layout6d06-Apr-2713-Apr-270%							Mobilization & Layout																									
FO-EL-B1-DH1-4295 Trapeze / strut support framing10d13-Apr-2723-Apr-270%							Trapeze /strut support framing																									
FO-EL-B1-DH1-4305 Cable tray & ladder rack supports8d23-Apr-2703-May-270%							Cable tray & ladder rack supports																									
FO-EL-B1-DH1-4315 Conduit hangers & supports10d03-May-2713-May-270%							Conduit hangers & supports																									
FO-EL-B1-DH1-4325 Wall sleeve installation8d13-May-2721-May-270%							Wall sleeve installation																									
FO-EL-B1-DH1-4265 Critical power busway hanger system10d21-May-2702-Jun-270%							Critical power busway hanger system																									
FO-EL-B1-DH1-4355 Conduit & Box Rough-In19d21-May-2711-Jun-270%							Conduit & Box Rough-In																									
FO-EL-B1-DH1-4275 Rack/cabinet grounding & bonding8d11-Jun-2721-Jun-270%							Rack/cabinet grounding & bonding																									
FO-EL-B1-DH1-4365 Cable Tray / Raceway Install13d11-Jun-2725-Jun-270%							Cable Tray / Raceway Install																									
FO-EL-B1-DH1-4195 Rack power whip installation19d21-Jun-2712-Jul-270%							Rack power whip installation																									
FO-EL-B1-DH1-4375 Wire Pull15d25-Jun-2713-Jul-270%							Wire Pull																									
FO-EL-B1-DH1-4205 Cabinet-level rack PDU (rPDU) connections13d12-Jul-2726-Jul-270%							Cabinet-level rack PDU (rPDU) connections																									
FO-EL-B1-DH1-4215 CRAC/CRAH unit electrical connections13d12-Jul-2726-Jul-270%							CRAC/CRAH unit electrical connections																									
FO-EL-B1-DH1-4255 Electrical Power Monitoring System (EPMS)10d13-Jul-2723-Jul-270%							Electrical Power Monitoring System (EPMS)																									
FO-EL-B1-DH1-4385 Panel Install & Termination10d13-Jul-2723-Jul-270%							Panel Install & Termination																									
FO-EL-B1-DH1-4245 General receptacles/small power10d26-Jul-2705-Aug-270%							General receptacles/small power																									
FO-EL-B1-DH1-4335 Fire caulking / firestopping of penetrations6d26-Jul-2702-Aug-270%							Fire caulking / firestopping of penetrations																									
FO-EL-B1-DH1-4225 Normal interior lighting installation15d05-Aug-2723-Aug-270%							Normal interior lighting installation																									
FO-EL-B1-DH1-4235 Lighting control system installation6d23-Aug-2730-Aug-270%							Lighting control system installation																									
FO-EL-B1-DH1-4285 Hot Aisle Containment (HAC) install19d20-Dec-2710-Jan-280%							Hot Aisle Containment (HAC) install																									
FO-EL-B1-DH1-4395 Lighting Fixture Install13d11-Jan-2825-Jan-280%							Lighting Fixture Install																									
FO-EL-B1-DH1-4405 Device & Receptacle Trim-Out10d25-Jan-2804-Feb-280%							Device & Receptacle Trim-Out																									
FO-EL-B1-DH1-4415 Testing & Continuity Checks8d04-Feb-2814-Feb-280%							Testing & Continuity Checks																									
Cooling (White Space)0d0%																																
Lighting & Small Power0d0%																																

alston
CONSTRUCTION
MISSION CRITICAL

[illegible]

HRL1 - Preliminary Schedule A1 - Rev.00 - Draft
#05.3.1.B1




03-Sep-26

Activity ID	Activity Name	Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																							
		95d	20-May-27	03-Sep-27	0%																								
FO-EL-B1-DH1-4665	Mobilization & Layout	6d	20-May-27	27-May-27	0%	Mobilization & Layout																							
FO-EL-B1-DH1-4775	Conduit hangers & supports	5d	27-May-27	02-Jun-27	0%	Conduit hangers & supports																							
FO-EL-B1-DH1-4675	Conduit & Box Rough-In	19d	02-Jun-27	23-Jun-27	0%	Conduit & Box Rough-In																							
FO-EL-B1-DH1-4685	Level 01 Cable Tray / Raceway Install	13d	23-Jun-27	07-Jul-27	0%	Level 01 Cable Tray / Raceway Install																							
FO-EL-B1-DH1-4695	Wire Pull	15d	07-Jul-27	23-Jul-27	0%	Wire Pull																							
FO-EL-B1-DH1-4705	Panel Install & Termination	10d	23-Jul-27	04-Aug-27	0%	Panel Install & Termination																							
FO-EL-B1-DH1-4715	Lighting Fixture Install	13d	23-Jul-27	06-Aug-27	0%	Lighting Fixture Install																							
CONFIDENTIAL		10d	04-Aug-27	16-Aug-27	0%																								
FO-EL-B1-DH1-4725	Device & Receptacle Trim-Out	10d	16-Aug-27	26-Aug-27	0%	Device & Receptacle Trim-Out																							
FO-EL-B1-DH1-4735	Testing & Continuity Checks	8d	26-Aug-27	03-Sep-27	0%	Testing & Continuity Checks																							
GALLERY		130d	30-Mar-27	20-Aug-27	0%	20-Aug-27, GALLERY																							
Critical Power Distribution		130d	30-Mar-27	20-Aug-27	0%	20-Aug-27, Critical Power Distribution																							
FO-EL-B1-DH1-4115	Mobilization & Layout	6d	30-Mar-27	06-Apr-27	0%	Mobilization & Layout																							
FO-EL-B1-DH1-4065	Trapeze / strut support framing	10d	06-Apr-27	16-Apr-27	0%	Trapeze / strut support framing																							
FO-EL-B1-DH1-4075	Cable tray & ladder rack supports	8d	16-Apr-27	26-Apr-27	0%	Cable tray & ladder rack supports																							
FO-EL-B1-DH1-4085	Conduit hangers & supports	10d	26-Apr-27	06-May-27	0%	Conduit hangers & supports																							
FO-EL-B1-DH1-4035	Critical power busway installation	15d	06-May-27	24-May-27	0%	Critical power busway installation																							
FO-EL-B1-DH1-4095	Wall sleeve installation	8d	06-May-27	14-May-27	0%	Wall sleeve installation																							
FO-EL-B1-DH1-4125	Conduit & Box Rough-In	19d	14-May-27	04-Jun-27	0%	Conduit & Box Rough-In																							
FO-EL-B1-DH1-4135	Cable Tray / Raceway Install	13d	14-May-27	28-May-27	0%	Cable Tray / Raceway Install																							
FO-EL-B1-DH1-4045	Remote Power Panel (RPP) installation	13d	24-May-27	07-Jun-27	0%	Remote Power Panel (RPP) installation																							
FO-EL-B1-DH1-4105	Fire caulking / firestopping of penetrations	6d	04-Jun-27	11-Jun-27	0%	Fire caulking / firestopping of penetrations																							
FO-EL-B1-DH1-4055	Facility PDU installation	13d	07-Jun-27	21-Jun-27	0%	Facility PDU installation																							
FO-EL-B1-DH1-4145	Wire Pull	15d	21-Jun-27	07-Jul-27	0%	Wire Pull																							
FO-EL-B1-DH1-4155	Panel Install & Termination	10d	07-Jul-27	19-Jul-27	0%	Panel Install & Termination																							
FO-EL-B1-DH1-4165	Lighting Fixture Install	13d	19-Jul-27	02-Aug-27	0%	Lighting Fixture Install																							
FO-EL-B1-DH1-4175	Device & Receptacle Trim-Out	10d	02-Aug-27	12-Aug-27	0%	Device & Receptacle Trim-Out																							
FO-EL-B1-DH1-4185	Testing & Continuity Checks	8d	12-Aug-27	20-Aug-27	0%	Testing & Continuity Checks																							
Hangers & Supports		0d			0%																								
Wall Sleeves & Firestopping		0d			0%																								
General Install Sequence		0d			0%																								
Building 1 - Data Hall 3		324d	26-Apr-27	21-Apr-28	0%	21-Apr-28, Building 1 - D																							
WALL & CEILING FINISHES		229d	26-Apr-27	06-Jan-28	0%	06-Jan-28, WALL & CEILING FINIS																							
FO-B1-DH1-1485	Layout Interior Walls	5d	26-Apr-27	30-Apr-27	0%	Layout Interior Walls																							
FO-B1-DH1-1495	Frame Interior Walls	60d	27-Apr-27	02-Jul-27	0%	Frame Interior Walls																							
FO-B1-DH1-1505	Overhead Mechanical & Plumbing Rough-in	60d	07-May-27	14-Jul-27	0%	Overhead Mechanical & Plumbing Rough-in																							
FO-B1-DH1-1525	Electrical Overhead Rough-in	50d	07-May-27	02-Jul-27	0%	Electrical Overhead Rough-in																							
FO-B1-DH1-1405	Structural Ceiling	60d	22-Sep-27	29-Nov-27	0%	Structural Ceiling																							
FO-B1-DH1-1535	Wall Frame Tap-out	30d	11-Nov-27	15-Dec-27	0%	Wall Frame Tap-out																							
FO-B1-DH1-1545	Above Ceiling MEP Completion	30d	17-Nov-27	21-Dec-27	0%	Above Ceiling MEP Completion																							
FO-B1-DH1-1575	Dry Wall Finishing	30d	23-Nov-27	27-Dec-27	0%	Dry Wall Finishing																							
FO-B1-DH1-1605	MEP Trimout	30d	03-Dec-27	06-Jan-28	0%	MEP Trimout																							
Network HAC Supply & Manifold		20d	28-May-27	18-Jun-27	0%	18-Jun-27, Network HAC Supply & Manifold																							
A22260	Receive materials	3d	28-May-27	31-May-27	0%	Receive materials																							
A22270	Layout routing	3d	01-Jun-27	02-Jun-27	0%	Layout routing																							
A22280	Install supports	3d	03-Jun-27	04-Jun-27	0%	Install supports																							
A22290	Install manifolds	5d	07-Jun-27	10-Jun-27	0%	Install manifolds																							

Actual Level of Effort Remaining Work Milestone
Actual Work Critical Remaining Work summary

Date	Revision	Checked	Approved
02-Sep-26	Preliminary Schedule	REDACTED	

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID		Activity Name	Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																												
	 A22300	Tie-ins & pressure test	5d	11-Jun-27	16-Jun-27	0%	 Tie-ins & pressure test																												
	 A22310	Flush & turnover	3d	17-Jun-27	18-Jun-27	0%	 Flush & turnover																												
	 Air-Cooled Chillers			84d	29-Jun-27	29-Sep-27	0%	 29-Sep-27, Air-Cooled Chillers																											
	 A21860	Receive and stage chillers	15d	29-Jun-27	14-Jul-27	0%	 Receive and stage chillers																												
	 A21870	Rig and set chillers	15d	05-Jul-27	20-Jul-27	0%	 Rig and set chillers																												
	 A21880	Install supports, isolation and accessories	23d	09-Jul-27	03-Aug-27	0%	 Install supports, isolation and accessories																												
	 A21890	Complete supply/return piping tie-ins	44d	16-Jul-27	02-Sep-27	0%	 Complete supply/return piping tie-ins																												
	 A21900	Pressure test, flush and fill	29d	05-Aug-27	06-Sep-27	0%	 Pressure test, flush and fill																												
	 A21910	Startup and functional testing	44d	12-Aug-27	29-Sep-27	0%	 Startup and functional testing																												
	 Fan Coil Wall Units			62d	29-Jun-27	06-Sep-27	0%	 06-Sep-27, Fan Coil Wall Units																											
	 A21920	Receive and distribute units	8d	29-Jun-27	06-Jul-27	0%	 Receive and distribute units																												
	 A21930	Install wall units and supports	11d	07-Jul-27	19-Jul-27	0%	 Install wall units and supports																												
	 FO-B1-DH1-1425	Install Fan Coil Wall	15d	07-Jul-27	22-Jul-27	0%	 Install Fan Coil Wall																												
	 A21940	Install piping connections	18d	20-Jul-27	06-Aug-27	0%	 Install piping connections																												
	 A21950	Install condensate and accessories	11d	09-Aug-27	19-Aug-27	0%	 Install condensate and accessories																												
	 A21960	Pressure test and inspect	7d	20-Aug-27	27-Aug-27	0%	 Pressure test and inspect																												
	 A21970	Startup and functional testing	7d	27-Aug-27	06-Sep-27	0%	 Startup and functional testing																												
	 CDU Manifolds			217d	24-Aug-27	21-Apr-28	0%	 21-Apr-28, CDU Manifolds																											
	 A22320	Receive & distribute	10d	24-Aug-27	02-Sep-27	0%	 Receive & distribute																												
	 A22330	Layout	10d	31-Dec-27	12-Jan-28	0%	 Layout																												
	 A22340	Install supports	15d	12-Jan-28	28-Jan-28	0%	 Install supports																												
	 A22350	Install manifolds & piping	30d	28-Jan-28	02-Mar-28	0%	 Install manifolds & piping																												
	 A22360	Tie-ins & testing	30d	02-Mar-28	05-Apr-28	0%	 Tie-ins & testing																												
	 A22370	Flush & turnover	15d	05-Apr-28	21-Apr-28	0%	 Flush & turnover																												
	 CDUs			96d	02-Jul-27	19-Oct-27	0%	 19-Oct-27, CDUs																											
	 A22100	Receive and distribute	1d	02-Jul-27	05-Jul-27	0%	 Receive and distribute																												
	 A22110	Install supply/return piping	4d	08-Oct-27	13-Oct-27	0%	 Install supply/return piping																												
	 A22120	Install SD83/hoses	2d	13-Oct-27	14-Oct-27	0%	 Install SD83/hoses																												
	 FO-B1-DH1-1455	Install Coolant Distribution Unit – CDU (OFOI)	1d	15-Oct-27	15-Oct-27	0%	 Install Coolant Distribution Unit – CDU (OFOI)																												
	 A22130	Startup & testing	2d	15-Oct-27	19-Oct-27	0																													

alston
CONSTRUCTION
MISSION CRITICAL


Activity ID	Activity Name	Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																																												
A21990 FO-B1-DH1-1435 A22000 A22010 A22020 A22030 HOT AISLE CONTAINMENT A22200 A22210 FO-B1-DH1-1475 A22220 A22230 A22240 A22250 FO-B1-DH1-1595 STEAM HUMIDIFIERS A22140 A22150 FO-B1-DH1-1465 A22160 A22170 A22180 A22190 CONFIDENTIAL CONFIDENTIAL CONFIDENTIAL FIRE ALARM SYSTEM FO-B1-DH1-1365 FO-B1-DH1-1375 FO-B1-DH1-1385 BUILDING AUTOMATION SYSTEM FO-B1-DH1-1395 FO-B1-DH1-1335 CORRIDORS Raceway & Containment Supports FO-EL-B1-DH1-5595 FO-EL-B1-DH1-5695 FO-EL-B1-DH1-5705 FO-EL-B1-DH1-5715 FO-EL-B1-DH1-5675 FO-EL-B1-DH1-5485 FO-EL-B1-DH1-5605 FO-EL-B1-DH1-5495 FO-EL-B1-DH1-5615 FO-EL-B1-DH1-5685 FO-EL-B1-DH1-5505 FO-EL-B1-DH1-5625	Rig and set CRAHs	7d	02-Jun-27	10-Jun-27	0%	Rig and set CRAHs																																												
	Install Computer Room Air Handler – CRAH	15d	02-Jun-27	18-Jun-27	0%	Install Computer Room Air Handler – CRAH																																												
	Install CHW piping tie-ins	13d	10-Jun-27	24-Jun-27	0%	Install CHW piping tie-ins																																												
	Install condensate, valves & accessories	9d	24-Jun-27	05-Jul-27	0%	Install condensate, valves & accessories																																												
	Pressure test, flush & TAB prep	5d	05-Jul-27	09-Jul-27	0%	Pressure test, flush & TAB prep																																												
	Startup & functional testing	5d	09-Jul-27	15-Jul-27	0%	Startup & functional testing																																												
	HOT AISLE CONTAINMENT		147d	02-Aug-27	12-Jan-28	0%	12-Jan-28, HOT AISLE CONTAINMENT																																											
	Receive materials	10d	02-Aug-27	11-Aug-27	0%	Receive materials																																												
	Layout	10d	12-Aug-27	23-Aug-27	0%	Layout																																												
	Install HAC	30d	06-Sep-27	08-Oct-27	0%	Install HAC																																												
	Install framing	15d	22-Sep-27	08-Oct-27	0%	Install framing																																												
	Install panels/doors	20d	23-Nov-27	15-Dec-27	0%	Install panels/doors																																												
	Seal & adjust	15d	15-Dec-27	31-Dec-27	0%	Seal & adjust																																												
	Final inspection	10d	31-Dec-27	12-Jan-28	0%	Final inspection																																												
	HAC Final Completion	10d	31-Dec-27	12-Jan-28	0%	HAC Final Completion																																												
	STEAM HUMIDIFIERS		248d	30-Apr-27	02-Feb-28	0%	02-Feb-28, STEAM HUMIDIFIERS																																											
	Receive and distribute	5d	30-Apr-27	06-May-27	0%	Receive and distribute																																												
	Mount humidifiers	2d	27-Dec-27	28-Dec-27	0%	Mount humidifiers																																												
	Install Steam Humidifier	5d	27-Dec-27	31-Dec-27	0%	Install Steam Humidifier																																												
	Install water/steam piping	10d	28-Dec-27	07-Jan-28	0%	Install water/steam piping																																												
	Install drain assemblies	10d	07-Jan-28	19-Jan-28	0%	Install drain assemblies																																												
	Leak test	6d	19-Jan-28	26-Jan-28	0%	Leak test																																												
	Startup	6d	26-Jan-28	02-Feb-28	0%	Startup																																												
	CONFIDENTIAL		192d	19-May-27	21-Dec-27	0%																																												
	CONFIDENTIAL		30d	19-May-27	22-Jun-27	0%																																												
	CONFIDENTIAL		20d	29-Nov-27	21-Dec-27	0%																																												
	FIRE ALARM SYSTEM		167d	22-Jun-27	27-Dec-27	0%	27-Dec-27, FIRE ALARM SYSTEM																																											
	Fire Alarm Rough in	19d	22-Jun-27	13-Jul-27	0%	Fire Alarm Rough in																																												
	Fire Alarm Device Install	5d	13-Jul-27	19-Jul-27	0%	Fire Alarm Device Install																																												
Fire Alarm Functional Test	5d	21-Dec-27	27-Dec-27	0%	Fire Alarm Functional Test																																													
BUILDING AUTOMATION SYSTEM		50d	15-Dec-27	09-Feb-28	0%	09-Feb-28, BUILDING AUTOMATION SYSTEM																																												
Building Automation System (BAS) Rough in	30d	15-Dec-27	18-Jan-28	0%	Building Automation System (BAS) Rough in																																													
Building Automation System (BAS) tie-ins	20d	18-Jan-28	09-Feb-28	0%	Building Automation System (BAS) Tie-ins																																													
CORRIDORS		181d	02-Jul-27	21-Jan-28	0%	21-Jan-28, CORRIDORS																																												
Raceway & Containment Supports		181d	02-Jul-27	21-Jan-28	0%	21-Jan-28, Raceway & Containment Supports																																												
Mobilization & Layout	6d	02-Jul-27	09-Jul-27	0%	Mobilization & Layout																																													
Trapeze / strut support framing	10d	09-Jul-27	21-Jul-27	0%	Trapeze / strut support framing																																													
Cable tray & ladder rack supports	8d	21-Jul-27	29-Jul-27	0%	Cable tray & ladder rack supports																																													
Conduit hangers & supports	10d	22-Jul-27	03-Aug-27	0%	Conduit hangers & supports																																													
Wall sleeve installation	8d	03-Aug-27	11-Aug-27	0%	Wall sleeve installation																																													
Overhead trapeze/strut support framing	15d	11-Aug-27	27-Aug-27	0%	Overhead trapeze/strut support framing																																													
Conduit & Box Rough-In	19d	27-Aug-27	17-Sep-27	0%	Conduit & Box Rough-In																																													
Cable tray & ladder rack installation	13d	17-Sep-27	01-Oct-27	0%	Cable tray & ladder rack installation																																													
Cable Tray / Raceway Install	13d	17-Sep-27	01-Oct-27	0%	Cable Tray / Raceway Install																																													
Fire caulking / firestopping of penetrations	6d	17-Sep-27	24-Sep-27	0%	Fire caulking / firestopping of penetrations																																													
Conduit hangers & supports	13d	01-Oct-27	15-Oct-27	0%	Conduit hangers & supports																																													
Wire Pull	15d	01-Oct-27	19-Oct-27	0%	Wire Pull																																													

HRL1 - Preliminary Schedule A1 - Rev.00 - Draft
#05.3.1.B1



03-Sep-26

Activity ID	Activity Name	Original Duration	Start	Finish	Duration % Complete	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
FO-EL-B1-DH1-5525 FO-EL-B1-DH1-5635 FO-EL-B1-DH1-5515 CONFIDENTIAL FO-EL-B1-DH1-5645 CONFIDENTIAL FO-EL-B1-DH1-5655 CONFIDENTIAL CONFIDENTIAL FO-EL-B1-DH1-5585 CONFIDENTIAL FO-EL-B1-DH1-5665 Lighting & Egress Life Safety & Fire Low Voltage & Security Hangers & Supports Wall Sleeves & Firestopping General Install Sequence DATA HALL — WHITE SPACE Rack Power Distribution FO-EL-B1-DH1-5405 FO-EL-B1-DH1-5355 FO-EL-B1-DH1-5365 FO-EL-B1-DH1-5375 FO-EL-B1-DH1-5385 FO-EL-B1-DH1-5325 FO-EL-B1-DH1-5415 FO-EL-B1-DH1-5335 FO-EL-B1-DH1-5425 FO-EL-B1-DH1-5255 FO-EL-B1-DH1-5435 FO-EL-B1-DH1-5265 FO-EL-B1-DH1-5275 FO-EL-B1-DH1-5315 FO-EL-B1-DH1-5445 FO-EL-B1-DH1-5305 FO-EL-B1-DH1-5395 FO-EL-B1-DH1-5285 FO-EL-B1-DH1-5295 FO-EL-B1-DH1-5345 FO-EL-B1-DH1-5455 FO-EL-B1-DH1-5465 FO-EL-B1-DH1-5475 Cooling (White Space) Lighting & Small Power Low Voltage & Monitoring Equipment Supports & Grounding Hot Aisle Containment	Lighting fixture & device support/backing	8d	15-Oct-27	25-Oct-27	0%																																	
	Panel Install & Termination	10d	19-Oct-27	29-Oct-27	0%																																	
	Emergency/egress lighting installation	8d	29-Oct-27	08-Nov-27	0%																																	
	CONFIDENTIAL		10d	08-Nov-27	18-Nov-27	0%																																
	Lighting Fixture Install	13d	18-Nov-27	02-Dec-27	0%																																	
	CONFIDENTIAL		6d	02-Dec-27	09-Dec-27	0%																																
	Device & Receptacle Trim-Out	10d	02-Dec-27	14-Dec-27	0%																																	
	CONFIDENTIAL		6d	09-Dec-27	16-Dec-27	0%																																
	CONFIDENTIAL		8d	16-Dec-27	24-Dec-27	0%																																
	Telecom/fiber entrance & structured cabling power	10d	24-Dec-27	05-Jan-28	0%																																	
	CONFIDENTIAL		8d	05-Jan-28	13-Jan-28	0%																																
	Testing & Continuity Checks	8d	13-Jan-28	21-Jan-28	0%																																	
	Lighting & Egress		0d			0%																																
	Life Safety & Fire		0d			0%																																
	Low Voltage & Security		0d			0%																																
	Hangers & Supports		0d			0%																																
	Wall Sleeves & Firestopping		0d			0%																																
	General Install Sequence		0d			0%																																
	DATA HALL — WHITE SPACE		227d	02-Jul-27	14-Mar-28	0%																																
	Rack Power Distribution		227d	02-Jul-27	14-Mar-28	0%																																
	FO-EL-B1-DH1-5405	Mobilization & Layout	6d	02-Jul-27	09-Jul-27	0%																																
	FO-EL-B1-DH1-5355	Trapeze / strut support framing	10d	09-Jul-27	21-Jul-27	0%																																
	FO-EL-B1-DH1-5365	Cable tray & ladder rack supports	8d	21-Jul-27	29-Jul-27	0%																																
	FO-EL-B1-DH1-5375	Conduit hangers & supports	10d	29-Jul-27	10-Aug-27	0%																																
	FO-EL-B1-DH1-5385	Wall sleeve installation	8d	10-Aug-27	18-Aug-27	0%																																
	FO-EL-B1-DH1-5325	Critical power busway hanger system	10d	18-Aug-27	30-Aug-27	0%																																
	FO-EL-B1-DH1-5415	Conduit & Box Rough-In	19d	18-Aug-27	08-Sep-27	0%																																
	FO-EL-B1-DH1-5335	Rack/cabinet grounding & bonding	8d	08-Sep-27	16-Sep-27	0%																																
	FO-EL-B1-DH1-5425	Cable Tray / Raceway Install	13d	08-Sep-27	22-Sep-27	0%																																
	FO-EL-B1-DH1-5255	Rack power whip installation	19d	16-Sep-27	07-Oct-27	0%																																
	FO-EL-B1-DH1-5435	Wire Pull	15d	22-Sep-27	08-Oct-27	0%																																
	FO-EL-B1-DH1-5265	Cabinet-level rack PDU (rPDU) connections	13d	07-Oct-27	21-Oct-27	0%																																
FO-EL-B1-DH1-5275	CRAC/CRAH unit electrical connections	13d	07-Oct-27	21-Oct-27	0%																																	
FO-EL-B1-DH1-5315	Electrical Power Monitoring System (EPMS)	10d	08-Oct-27	20-Oct-27	0%																																	
FO-EL-B1-DH1-5445	Panel Install & Termination	10d	08-Oct-27	20-Oct-27	0%																																	
FO-EL-B1-DH1-5305	General receptacles/small power	10d	21-Oct-27	02-Nov-27	0%																																	
FO-EL-B1-DH1-5395	Fire caulking / firestopping of penetrations	6d	21-Oct-27	28-Oct-27	0%																	</																

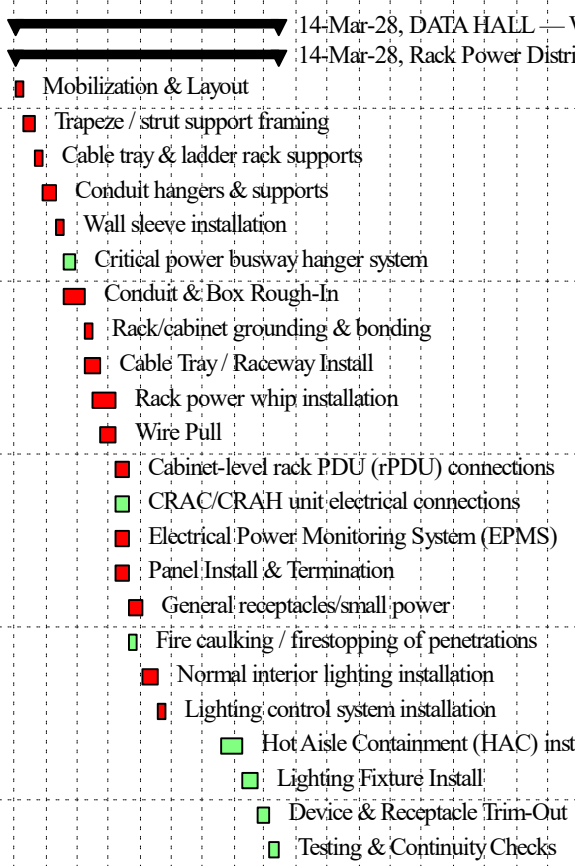

Actual Level of Effort Remaining Work Milestone
Actual Work Critical Remaining Work summary

Date	Revision	Checked	Approved
02-Sep-26	Preliminary Schedule	REDACTED	

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID		Activity Name	Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																																															
Hangers & Supports			0d			0%																																																
Wall Sleeves & Firestopping			0d			0%																																																
General Install Sequence			0d			0%																																																
ELECTRICAL & UPS ROOMS			195d	07-May-27	13-Dec-27	0%																																																
Utility & Medium Voltage			195d	07-May-27	13-Dec-27	0%																																																
FO-EL-B1-DH1-5015 Mobilization & Layout			6d	07-May-27	14-May-27	0%																																																
FO-EL-B1-DH1-4785 Utility transformer pad & primary gear			6d	14-May-27	21-May-27	0%																																																
FO-EL-B1-DH1-4945 Building grounding grid/ring installation			6d	14-May-27	21-May-27	0%																																																
FO-EL-B1-DH1-4965 Trapeze / strut support framing			10d	14-May-27	26-May-27	0%																																																
FO-EL-B1-DH1-4995 Wall sleeve installation			8d	21-May-27	31-May-27	0%																																																
FO-EL-B1-DH1-4975 Cable tray & ladder rack supports			8d	26-May-27	03-Jun-27	0%																																																
FO-EL-B1-DH1-4795 Utility metering equipment			4d	03-Jun-27	08-Jun-27	0%																																																
FO-EL-B1-DH1-4985 Conduit hangers & supports			10d	08-Jun-27	18-Jun-27	0%																																																
FO-EL-B1-DH1-5025 Conduit & Box Rough-In			13d	08-Jun-27	22-Jun-27	0%																																																
FO-EL-B1-DH1-4805 Medium voltage (MV) switchgear			10d	22-Jun-27	02-Jul-27	0%																																																
FO-EL-B1-DH1-5005 Fire caulking / firestopping of penetrations			6d	22-Jun-27	29-Jun-27	0%																																																
FO-EL-B1-DH1-5035 Cable Tray / Raceway Install			13d	22-Jun-27	06-Jul-27	0%																																																
FO-EL-B1-DH1-4815 MV feeder cable installation			13d	06-Jul-27	20-Jul-27	0%																																																
FO-EL-B1-DH1-4835 Main switchboard / MDB installation			10d	20-Jul-27	30-Jul-27	0%																																																
FO-EL-B1-DH1-4845 Unit substation / step-down transformers			6d	20-Jul-27	27-Jul-27	0%																																																
FO-EL-B1-DH1-4855 Distribution switchboard installation			13d	30-Jul-27	13-Aug-27	0%																																																
FO-EL-B1-DH1-4885 Generator paralleling switchgear			10d	13-Aug-27	25-Aug-27	0%																																																
FO-EL-B1-DH1-4895 Automatic Transfer Switch (ATS) installation			8d	25-Aug-27	02-Sep-27	0%																																																
FO-EL-B1-DH1-4925 UPS output distribution board			8d	02-Sep-27	10-Sep-27	0%																																																
FO-EL-B1-DH1-4905 UPS module installation			13d	10-Sep-27	24-Sep-27	0%																																																
FO-EL-B1-DH1-4915 UPS battery system installation			13d	10-Sep-27	24-Sep-27	0%																																																
FO-EL-B1-DH1-4935 Static Transfer Switch (STS) installation			6d	24-Sep-27	01-Oct-27	0%																																																
FO-EL-B1-DH1-5055 Panel Install & Termination			10d	01-Oct-27	13-Oct-27	0%																																																
FO-EL-B1-DH1-4875 Sub-metering installation			6d	13-Oct-27	20-Oct-27	0%																																																
FO-EL-B1-DH1-4955 Surge Protective Device (SPD) installation			5d	20-Oct-27	26-Oct-27	0%																																																
FO-EL-B1-DH1-4865 Feeder conduit & cable installation			9d	26-Oct-27	04-Nov-27	0%																																																
FO-EL-B1-DH1-5045 Wire Pull			13d	04-Nov-27	18-Nov-27	0%																																																
FO-EL-B1-DH1-5815 Pull & Terminate Wire To Switchboard			13d	08-Nov-27	22-Nov-27	0%																																																
FO-EL-B1-DH1-5085 Testing & Continuity Checks			8d	18-Nov-27	26-Nov-27	0%																																																
FO-EL-B1-DH1-5065 Lighting Fixture Install			6d	22-Nov-27	29-Nov-27	0%																																																
FO-EL-B1-DH1-5075 Device & Receptacle Trim-Out			6d	22-Nov-27	29-Nov-27	0%																																																
FO-EL-B1-DH1-4825 Utility service energization coordination			6d	29-Nov-27	06-Dec-27	0%																																																
FO-EL-B1-DH1-5825 Testing			6d	06-Dec-27	13-Dec-27	0%																																																
Main Distribution			0d			0%																																																
Standby Power Switching			0d			0%																																																
UPS & Critical Power (Room)			0d			0%																																																
Grounding & Protection			0d			0%																																																
Hangers & Supports			0d			0%																																																
Wall Sleeves & Firestopping			0d			0%																																																
General Install Sequence			0d			0%																																																
			95d	02-Jul-27	18-Oct-27	0%																																																
FO-EL-B1-DH1-5725 Mobilization & Layout			6d	02-Jul-27	09-Jul-27	0%																																																
FO-EL-B1-DH1-5835 Conduit hangers & supports			5d	09-Jul-27	15-Jul-27	0%																																																

alston
CONSTRUCTION
MISSION CRITICAL


[illegible]

HRL1 - Preliminary Schedule A1 - Rev.00 - Draft
#05.3.1.B1



03-Sep-26

Activity ID	Activity Name	Original Duration	Start	Finish	Duration % Complete	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
■ A22380	Receive and stage chillers	15d	28-Jul-27	12-Aug-27	0%																																	
■ A22390	Rig and set chillers	15d	03-Aug-27	18-Aug-27	0%																																	
■ A22400	Install supports, isolation and accessories	23d	09-Aug-27	01-Sep-27	0%																																	
■ A22410	Complete supply/return piping tie-ins	44d	16-Aug-27	01-Oct-27	0%																																	
■ A22420	Pressure test, flush and fill	29d	03-Sep-27	05-Oct-27	0%																																	
■ A22430	Startup and functional testing	44d	10-Sep-27	28-Oct-27	0%																																	
■ Fan Coil Wall Units		62d	28-Jul-27	05-Oct-27	0%																																	
■ A22440	Receive and distribute units	8d	28-Jul-27	04-Aug-27	0%																																	
■ A22450	Install wall units and supports	11d	05-Aug-27	17-Aug-27	0%																																	
■ FO-B1-DH1-1705	Install Fan Coil Wall	15d	05-Aug-27	20-Aug-27	0%																																	
■ A22460	Install piping connections	18d	18-Aug-27	06-Sep-27	0%																																	
■ A22470	Install condensate and accessories	11d	07-Sep-27	17-Sep-27	0%																																	
■ A22480	Pressure test and inspect	7d	20-Sep-27	27-Sep-27	0%																																	
■ A22490	Startup and functional testing	7d	27-Sep-27	05-Oct-27	0%																																	
■ CDU Manifolds		116d	03-Feb-28	13-Jun-28	0%																																	
■ A22840	Receive & distribute	10d	03-Feb-28	15-Feb-28	0%																																	
■ A22850	Layout	10d	22-Feb-28	03-Mar-28	0%																																	
■ A22860	Install supports	15d	03-Mar-28	21-Mar-28	0%																																	
■ A22870	Install manifolds & piping	30d	21-Mar-28	24-Apr-28	0%																																	
■ A22880	Tie-ins & testing	30d	24-Apr-28	26-May-28	0%																																	
■ A22890	Flush & turnover	15d	26-May-28	13-Jun-28	0%																																	
■ CDUs		100d	04-Aug-27	24-Nov-27	0%																																	
■ A22620	Receive and distribute	1d	04-Aug-27	05-Aug-27	0%																																	
■ A22630	Install supply/return piping	4d	08-Nov-27	11-Nov-27	0%																																	
■ A22640	Install SD83/hoses	2d	11-Nov-27	12-Nov-27	0%																																	
■ FO-B1-DH1-1735	Install Coolant Distribution Unit – CDU (OFOI)	1d	22-Nov-27	22-Nov-27	0%																																	
■ A22650	Startup & testing	2d	22-Nov-27	24-Nov-27	0%																																	
■ CHILLED WATER PIPING		112d	21-Jun-27	25-Oct-27	0%																																	
■ FO-B1-DH1-1795	Chilled Water Pipe Rough-in	45d	21-Jun-27	10-Aug-27	0%																																	
■ FO-B1-DH1-1845	CHW Final Connection	25d	27-Sep-27	25-Oct-27	0%																																	
■ FIRE SPRINKLER & FIRESTOP		198d	16-Jun-27	25-Jan-28	0%																																	
■ FO-B1-DH1-1625	Sprinkler System Rough In	60d	16-Jun-27	23-Aug-27	0%																																	
■ FO-B1-DH1-1695	Sprinkler System Trim Out	25d	22-Dec-27	19-Jan-28	0%																																	
■ FO-B1-DH1-1865	Firestop Install	20d	03-Jan-28	25-Jan-28	0%																																	
■ CRAC Units		20d	04-Aug-27	26-Aug-27	0%																																	
■ A22560	Receive and stage CRACs	3d	04-Aug-27	06-Aug-27	0%																																	
■ FO-B1-DH1-1725	Install CRAC Unit	5d	04-Aug-27	10-Aug-27	0%																																	
■ A22570	Set condensing units	3d	06-Aug-27	10-Aug-27	0%																																	
■ A22580	Install refrigerant piping	5d	10-Aug-27	16-Aug-27	0%																																	
■ A22590	Install drains & accessories	4d	16-Aug-27	19-Aug-27	0%																																	
■ A22600	Pressure test, evacuate & charge	3d	19-Aug-27	23-Aug-27	0%																																	
■ A22610	Startup & testing	4d	23-Aug-27	26-Aug-27	0%																																	
■ CRAH Units		50d	30-Jun-27	24-Aug-27	0%																																	
■ A22500	Receive and stage CRAHs	6d	30-Jun-27	06-Jul-27	0%																																	
■ A22510	Rig and set CRAHs	13d	07-Jul-27	20-Jul-27	0%																																	
■ FO-B1-DH1-1715	Install Computer Room Air Handler – CRAH	15d	07-Jul-27	22-Jul-27	0%																																	
■ A22520	Install CHW piping tie-ins	13d	21-Jul-27	03-Aug-27	0%																																	

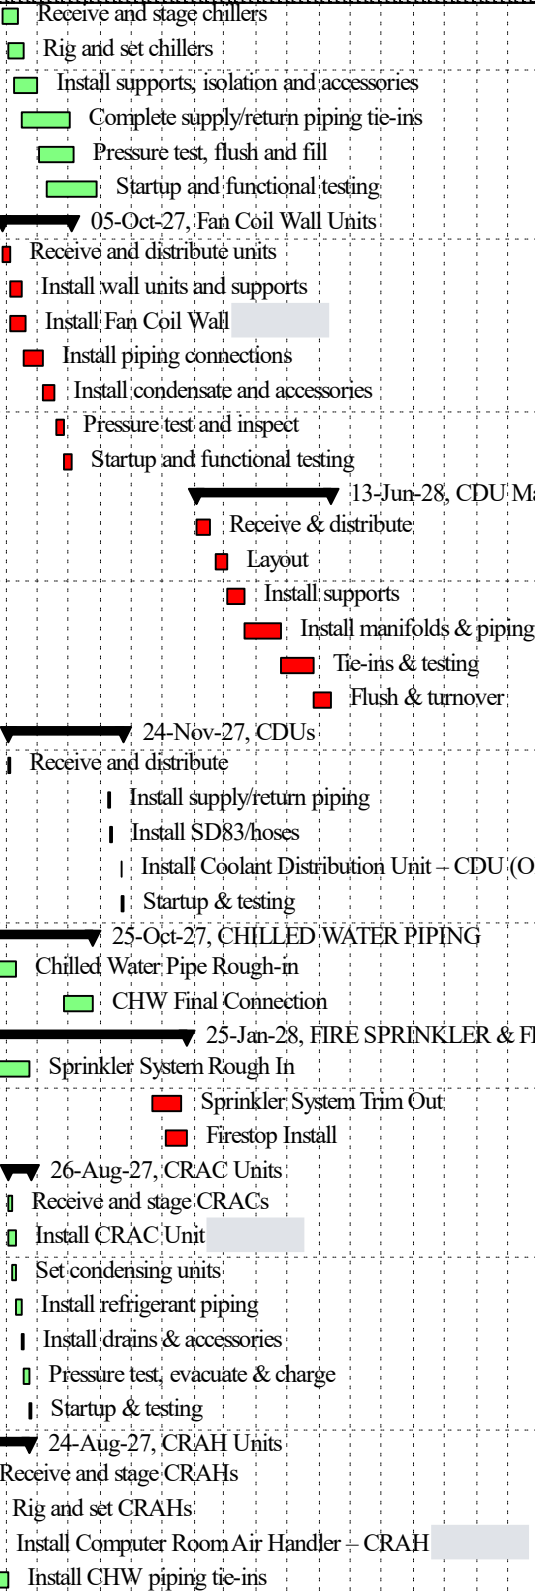

Actual Level of Effort Remaining Work Milestone
Actual Work Critical Remaining Work summary

Date	Revision	Checked	Approved
02-Sep-26	Preliminary Schedule	REDACTED	

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID	Activity Name	Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D																																													
	A22530	Install condensate, valves & accessories	9d	04-Aug-27	12-Aug-27	0%	Install condensate, valves & accessories																																												
	A22540	Pressure test, flush & TAB prep	5d	13-Aug-27	18-Aug-27	0%	Pressure test, flush & TAB prep																																												
	A22550	Startup & functional testing	5d	19-Aug-27	24-Aug-27	0%	Startup & functional testing																																												
	HOT AISLE CONTAINMENT			240d	28-May-27	22-Feb-28	0%	22-Feb-28, HOT AISLE CONTAINMENT																																											
	A22720	Receive materials	10d	28-May-27	08-Jun-27	0%	Receive materials																																												
	A22730	Layout	15d	09-Jun-27	25-Jun-27	0%	Layout																																												
	FO-B1-DH1-1755	Install HAC	30d	05-Oct-27	08-Nov-27	0%	Install HAC																																												
	A22740	Install framing	15d	21-Oct-27	08-Nov-27	0%	Install framing																																												
	A22750	Install panels/doors	20d	22-Dec-27	13-Jan-28	0%	Install panels/doors																																												
	A22760	Seal & adjust	15d	13-Jan-28	31-Jan-28	0%	Seal & adjust																																												
	A22770	Final inspection	10d	31-Jan-28	10-Feb-28	0%	Final inspection																																												
	FO-B1-DH1-1875	HAC Final Completion	20d	31-Jan-28	22-Feb-28	0%	HAC Final Completion																																												
	STEAM HUMIDIFIERS			399d	02-Jun-27	22-Aug-28	0%	22-Aug-28, STEAM HUMIDIFIERS																																											
	A22660	Receive and distribute	5d	02-Jun-27	08-Jun-27	0%	Receive and distribute																																												
	A22670	Mount humidifiers	2d	25-Jan-28	26-Jan-28	0%	Mount humidifiers																																												
	FO-B1-DH1-1745	Install Steam Humidifier	5d	25-Jan-28	31-Jan-28	0%	Install Steam Humidifier																																												
	A22680	Install water/steam piping	10d	26-Jan-28	07-Feb-28	0%	Install water/steam piping																																												
	A22690	Install drain assemblies	10d	07-Feb-28	17-Feb-28	0%	Install drain assemblies																																												
	A22700	Leak test	6d	17-Feb-28	24-Feb-28	0%	Leak test																																												
	A22710	Startup	6d	15-Aug-28	22-Aug-28	0%	Startup																																												
	CONFIDENTIAL			189d	21-Jun-27	19-Jan-28	0%																																												
	CONFIDENTIAL			30d	21-Jun-27	23-Jul-27	0%																																												
	CONFIDENTIAL			20d	28-Dec-27	19-Jan-28	0%																																												
	FIRE ALARM SYSTEM			164d	23-Jul-27	25-Jan-28	0%	25-Jan-28, FIRE ALARM SYSTEM																																											
	FO-B1-DH1-1645	Fire Alarm Rough in	19d	23-Jul-27	13-Aug-27	0%	Fire Alarm Rough in																																												
	FO-B1-DH1-1655	Fire Alarm Device Install	5d	13-Aug-27	19-Aug-27	0%	Fire Alarm Device Install																																												
	FO-B1-DH1-1665	Fire Alarm Functional Test	5d	19-Jan-28	25-Jan-28	0%	Fire Alarm Functional Test																																												
	BUILDING AUTOMATION SYSTEM			50d	13-Jan-28	09-Mar-28	0%	09-Mar-28, BUILDING AUTOMATION SYSTEM																																											
	FO-B1-DH1-1675	Building Automation System (BAS) Rough in	30d	13-Jan-28	16-Feb-28	0%	Building Automation System (BAS) Rough in																																												
FO-B1-DH1-1615	Building Automation System (BAS) tie-ins	20d	16-Feb-28	09-Mar-28	0%	Building Automation System (BAS) tie-ins																																													
CORRIDORS			181d	04-Aug-27	23-Feb-28	0%	23-Feb-28, CORRIDORS																																												
Raceway & Containment Supports			181d	04-Aug-27	23-Feb-28	0%	23-Feb-28, Raceway & Containment Supports																																												
FO-EL-B1-DH1-6655	Mobilization & Layout	6d	04-Aug-27	11-Aug-27	0%	Mobilization & Layout																																													
FO-EL-B1-DH1-6755	Trapeze / strut support framing	10d	11-Aug-27	23-Aug-27	0%	Trapeze / strut support framing																																													
FO-EL-B1-DH1-6765	Cable tray & ladder rack supports	8d	23-Aug-27	31-Aug-27	0%	Cable tray & ladder rack supports																																													
FO-EL-B1-DH1-6775	Conduit hangers & supports	10d	24-Aug-27	03-Sep-27	0%	Conduit hangers & supports																																													
FO-EL-B1-DH1-6735	Wall sleeve installation	8d	03-Sep-27	13-Sep-27	0%	Wall sleeve installation																																													
FO-EL-B1-DH1-6545	Overhead trapeze/strut support framing	15d	13-Sep-27	29-Sep-27	0%	Overhead trapeze/strut support framing																																													
FO-EL-B1-DH1-6665	Conduit & Box Rough-In	19d	29-Sep-27	20-Oct-27	0%	Conduit & Box Rough-In																																													
FO-EL-B1-DH1-6555	Cable tray & ladder rack installation	13d	20-Oct-27	03-Nov-27	0%	Cable tray & ladder rack installation																																													
FO-EL-B1-DH1-6675	Cable Tray / Raceway Install	13d	20-Oct-27	03-Nov-27	0%	Cable Tray / Raceway Install																																													
FO-EL-B1-DH1-6745	Fire caulking / firestopping of penetrations	6d	20-Oct-27	27-Oct-27	0%	Fire caulking / firestopping of penetrations																																													
FO-EL-B1-DH1-6565	Conduit hangers & supports	13d	03-Nov-27	17-Nov-27	0%	Conduit hangers & supports																																													
FO-EL-B1-DH1-6685	Wire Pull	15d	03-Nov-27	19-Nov-27	0%	Wire Pull																																													
FO-EL-B1-DH1-6585	Lighting fixture & device support/backing	8d	17-Nov-27	25-Nov-27	0%	Lighting fixture & device support/backing																																													
FO-EL-B1-DH1-6695	Panel Install & Termination	10d	19-Nov-27	01-Dec-27	0%	Panel Install & Termination																																													
FO-EL-B1-DH1-6575	Emergency/egress lighting installation	8d	01-Dec-27																																																

alston
CONSTRUCTION
MISSION CRITICAL

[illegible]

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID		Activity Name		Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																																															
ELECTRICAL & UPS ROOMS				195d	09-Jun-27	13-Jan-28	0%	13-Jan-28, ELECTRICAL & UPS ROOMS																																															
Utility & Medium Voltage				195d	09-Jun-27	13-Jan-28	0%	13-Jan-28, Utility & Medium Voltage																																															
FO-EL-B1-DH1-6075 Mobilization & Layout				6d	09-Jun-27	16-Jun-27	0%	Mobilization & Layout																																															
FO-EL-B1-DH1-5845 Utility transformer pad & primary gear				6d	16-Jun-27	23-Jun-27	0%	Utility transformer pad & primary gear																																															
FO-EL-B1-DH1-6005 Building grounding grid/ring installation				6d	16-Jun-27	23-Jun-27	0%	Building grounding grid/ring installation																																															
FO-EL-B1-DH1-6025 Trapeze / strut support framing				10d	16-Jun-27	28-Jun-27	0%	Trapeze / strut support framing																																															
FO-EL-B1-DH1-6055 Wall sleeve installation				8d	23-Jun-27	01-Jul-27	0%	Wall sleeve installation																																															
FO-EL-B1-DH1-6035 Cable tray & ladder rack supports				8d	28-Jun-27	06-Jul-27	0%	Cable tray & ladder rack supports																																															
FO-EL-B1-DH1-5855 Utility metering equipment				4d	06-Jul-27	09-Jul-27	0%	Utility metering equipment																																															
FO-EL-B1-DH1-6045 Conduit hangers & supports				10d	09-Jul-27	21-Jul-27	0%	Conduit hangers & supports																																															
FO-EL-B1-DH1-6085 Conduit & Box Rough-In				13d	09-Jul-27	23-Jul-27	0%	Conduit & Box Rough-In																																															
FO-EL-B1-DH1-5865 Medium voltage (MV) switchgear				10d	23-Jul-27	04-Aug-27	0%	Medium voltage (MV) switchgear																																															
FO-EL-B1-DH1-6065 Fire caulking / firestopping of penetrations				6d	23-Jul-27	30-Jul-27	0%	Fire caulking / firestopping of penetrations																																															
FO-EL-B1-DH1-6095 Cable Tray / Raceway Install				13d	23-Jul-27	06-Aug-27	0%	Cable Tray / Raceway Install																																															
FO-EL-B1-DH1-5875 MV feeder cable installation				13d	06-Aug-27	20-Aug-27	0%	MV feeder cable installation																																															
FO-EL-B1-DH1-5895 Main switchboard / MDB installation				10d	20-Aug-27	01-Sep-27	0%	Main switchboard / MDB installation																																															
FO-EL-B1-DH1-5905 Unit substation / step-down transformers				6d	20-Aug-27	27-Aug-27	0%	Unit substation / step-down transformers																																															
FO-EL-B1-DH1-5915 Distribution switchboard installation				13d	01-Sep-27	15-Sep-27	0%	Distribution switchboard installation																																															
FO-EL-B1-DH1-5945 Generator paralleling switchgear				10d	15-Sep-27	27-Sep-27	0%	Generator paralleling switchgear																																															
FO-EL-B1-DH1-5955 Automatic Transfer Switch (ATS) installation				8d	27-Sep-27	05-Oct-27	0%	Automatic Transfer Switch (ATS) installation																																															
FO-EL-B1-DH1-5985 UPS output distribution board				8d	05-Oct-27	13-Oct-27	0%	UPS output distribution board																																															
FO-EL-B1-DH1-5965 UPS module installation				13d	13-Oct-27	27-Oct-27	0%	UPS module installation																																															
FO-EL-B1-DH1-5975 UPS battery system installation				13d	13-Oct-27	27-Oct-27	0%	UPS battery system installation																																															
FO-EL-B1-DH1-5995 Static Transfer Switch (STS) installation				6d	27-Oct-27	03-Nov-27	0%	Static Transfer Switch (STS) installation																																															
FO-EL-B1-DH1-6115 Panel Install & Termination				10d	03-Nov-27	15-Nov-27	0%	Panel Install & Termination																																															
FO-EL-B1-DH1-5935 Sub-metering installation				6d	15-Nov-27	22-Nov-27	0%	Sub-metering installation																																															
FO-EL-B1-DH1-6015 Surge Protective Device (SPD) installation				5d	22-Nov-27	26-Nov-27	0%	Surge Protective Device (SPD) installation																																															
FO-EL-B1-DH1-5925 Feeder conduit & cable installation				9d	26-Nov-27	07-Dec-27	0%	Feeder conduit & cable installation																																															
FO-EL-B1-DH1-6105 Wire Pull				13d	07-Dec-27	21-Dec-27	0%	Wire Pull																																															
FO-EL-B1-DH1-6875 Pull & Terminate Wire To Switchboard				13d	09-Dec-27	23-Dec-27	0%	Pull & Terminate Wire To Switchboard																																															
FO-EL-B1-DH1-6145 Testing & Continuity Checks				8d	21-Dec-27	29-Dec-27	0%	Testing & Continuity Checks																																															
FO-EL-B1-DH1-6125 Lighting Fixture Install				6d	23-Dec-27	30-Dec-27	0%	Lighting Fixture Install																																															
FO-EL-B1-DH1-6135 Device & Receptacle Trim-Out				6d	23-Dec-27	30-Dec-27	0%	Device & Receptacle Trim-Out																																															
FO-EL-B1-DH1-5885 Utility service energization coordination				6d	30-Dec-27	06-Jan-28	0%	Utility service energization coordination																																															
FO-EL-B1-DH1-6885 Testing				6d	06-Jan-28	13-Jan-28	0%	Testing																																															
Main Distribution				0d			0%																																																
Standby Power Switching				0d			0%																																																
UPS & Critical Power (Room)				0d			0%																																																
Grounding & Protection				0d			0%																																																
Hangers & Supports				0d			0%																																																
Wall Sleeves & Firestopping				0d			0%																																																
General Install Sequence				0d			0%																																																
				95d	02-Jun-27	16-Sep-27	0%	16-Sep-27,																																															
FO-EL-B1-DH1-6785 Mobilization & Layout				6d	02-Jun-27	09-Jun-27	0%	Mobilization & Layout																																															
FO-EL-B1-DH1-6895 Conduit hangers & supports				5d	09-Jun-27	15-Jun-27	0%	Conduit hangers & supports																																															
FO-EL-B1-DH1-6795 Conduit & Box Rough-In				19d	15-Jun-27	06-Jul-27	0%	Conduit & Box Rough-In																																															
FO-EL-B1-DH1-6805 Level 01 Cable Tray / Raceway Install				13d	06-Jul-27																																																		

alston
CONSTRUCTION
MISSION CRITICAL

[illegible]

HRL1 - Preliminary Schedule A1 - Rev.00 - Draft
#05.3.1.B1



03-Sep-26

Activity ID	Activity Name	Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																							
Area A- Branch Circuit & Device Rough-In		25d	11-Mar-27	08-Apr-27	0%																								
A23210	Branch Circuit Conduit Rough-In – Area A (Overhead & In-Wall)	20d	11-Mar-27	02-Apr-27	0%																								
A23220	Branch Circuit Wire Pull – Area A	15d	17-Mar-27	02-Apr-27	0%																								
A23230	Receptacle & Device Box Rough-In – Area A (Standard & GFI)	15d	23-Mar-27	08-Apr-27	0%																								
Area B – Branch Circuit & Device Rough-In		25d	11-Mar-27	08-Apr-27	0%																								
A23240	Branch Circuit Conduit Rough-In – Area B (Overhead & In-Wall)	20d	11-Mar-27	02-Apr-27	0%																								
A23250	Branch Circuit Wire Pull – Area B	15d	17-Mar-27	02-Apr-27	0%																								
A23260	Receptacle & Device Box Rough-In – Area B (Standard & GFI)	15d	23-Mar-27	08-Apr-27	0%																								
Equipment Power Rough-In		15d	23-Mar-27	08-Apr-27	0%																								
A23290	Plumbing Equipment Power Rough-In – WH-1, BP-1	5d	23-Mar-27	29-Mar-27	0%																								
A23300	EV Charger Rough-In (CHGR-1, CHGR-2)	5d	23-Mar-27	29-Mar-27	0%																								
A23280	Mechanical Equipment Power Rough-In – EUH-A101–A105, FCU-A101, UH-A106, EF-	10d	29-Mar-27	08-Apr-27	0%																								
A23270	Mechanical Equipment Power Rough-In – CRAC-003 / CRAC-004	5d	31-Mar-27	06-Apr-27	0%																								
Low-Voltage, Security & Fire Alarm Rough-In		10d	23-Mar-27	02-Apr-27	0%																								
CONFIDENTIAL		10d	23-Mar-27	02-Apr-27	0%																								
A23320	Fire Alarm Device Rough-In Coordination (NAC, ASD, APS)	10d	23-Mar-27	02-Apr-27	0%																								
A23330	Low-Voltage / AV Rough-In – FOC AV Rack, TV Mounts, WB1 Wall Boxes	10d	23-Mar-27	02-Apr-27	0%																								
Close-In Coordination		5d	14-Apr-27	20-Apr-27	0%																								
A23340	Ceiling Grid & Drywall Close-In Coordination (Electrical Sign-Off)	5d	14-Apr-27	20-Apr-27	0%																								
Trim-Out & Terminations		25d	02-Apr-27	30-Apr-27	0%																								
A23370	Panelboard Termination & Circuit Labeling	5d	02-Apr-27	08-Apr-27	0%																								
CONFIDENTIAL		5d	02-Apr-27	08-Apr-27	0%																								
A23400	Fire Alarm Device Trim & Termination	5d	02-Apr-27	08-Apr-27	0%																								
A23410	AV / Low-Voltage Device Trim & Termination	5d	02-Apr-27	08-Apr-27	0%																								
A23380	Equipment Final Connections – Mechanical Equipment (CRAC, EUH, FCU, VAV, EF, UH)	10d	08-Apr-27	20-Apr-27	0%																								
A23350	Device & Fixture Trim-Out – Area A (Receptacles, Switches, Cover Plates)	10d	20-Apr-27	30-Apr-27	0%																								
A23360	Device & Fixture Trim-Out – Area B (Receptacles, Switches, Cover Plates)	10d	20-Apr-27	30-Apr-27	0%																								
MECHANICAL FIT OUT		67d	26-Feb-27	12-May-27	0%																								
Mobilization (Area A & B)		5d	26-Feb-27	04-Mar-27	0%																								
A22900	Mobilization & Interior Layout – Area A & B	5d	26-Feb-27	04-Mar-27	0%																								
AREAA (Offices, Data Hall, Corridors, MDF)		55d	01-Mar-27	30-Apr-27	0%																								
Area A- Framing		20d	01-Mar-27	23-Mar-27	0%																								
A22910	Interior Wall Framing – Area A (Offices, Data Hall, Corridors, MDF)	20d	01-Mar-27	23-Mar-27	0%																								
Overhead MEP Rough-In		20d	11-Mar-27	02-Apr-27	0%																								
A22920	Overhead MEP Rough-In – Supply Air Trunk Mains – Area A	20d	11-Mar-27	02-Apr-27	0%																								
A22930	Overhead MEP Rough-In – Return Air Trunk Mains – Area A	15d	17-Mar-27	02-Apr-27	0%																								
Area A– Terminal & Equipment Installation		20d	17-Mar-27	08-Apr-27	0%																								
A22950	Electric Unit Heater Installation – Loading Office (EUH-A104)	5d	17-Mar-27	23-Mar-27	0%																								
A22960	Supplemental Cooling Unit Installation – PCU-A105	5d	17-Mar-27	23-Mar-27	0%																								
A22940	VAV Box Installation – Area A (VAV-A101 thru VAV-A113)	15d	23-Mar-27	08-Apr-27	0%																								
Area A– Duct Run-Outs & Terminal Devices		15d	29-Mar-27	14-Apr-27	0%																								
A22970	Duct Run-Outs & Supply Diffuser Rough-In – Area A	15d	29-Mar-27	14-Apr-27	0%																								
A22980	Return / Exhaust Grille Rough-In – Area A	10d	02-Apr-27	14-Apr-27	0%																								
Boundary Protection & Specialties		5d	02-Apr-27	08-Apr-27	0%																								
A23120	Main Bar Installation – Critical Boundary Penetrations	5d	02-Apr-27	08-Apr-27	0%																								
MDF Room Equipment Installation		10d	29-Mar-27	08-Apr-27	0%																								
A23110	CRAC Unit Installation – (CRAC-003, CRAC-004) on 18" Floor Stands	10d	29-Mar-27	08-Apr-27	0%																								
Area A– Close-In		15d	14-Apr-27	30-Apr-27	0%																								

Actual Level of Effort Remaining Work Milestone
Actual Work Critical Remaining Work summary

Date	Revision	Checked	Approved
02-Sep-26	Preliminary Schedule	REDACTED	

alston
CONSTRUCTION
MISSION CRITICAL

Activity ID	Activity Name	Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																																																
MECHANICAL	 A22990	Ceiling Grid & Drywall Close-In – Area A	15d	14-Apr-27	30-Apr-27	0%	 Ceiling Grid & Drywall Close-In – Area A																																															
	 Area A – Trim-Out		10d	20-Apr-27	30-Apr-27	0%	 30-Apr-27, Area A – Trim-Out																																															
	 A23000	Diffuser & Grille Final Trim-Out – Area A	10d	20-Apr-27	30-Apr-27	0%	 Diffuser & Grille Final Trim-Out – Area A																																															
	 AREA B (Offices, Storage, Shred, Restrooms)		55d	01-Mar-27	30-Apr-27	0%	 30-Apr-27, AREA B (Offices, Storage, Shred, Restrooms)																																															
	 Area B - Framing		20d	01-Mar-27	23-Mar-27	0%	 23-Mar-27, Area B - Framing																																															
	 A23010	Interior Wall Framing – Area B (Offices, Storage, Shred, Restrooms)	20d	01-Mar-27	23-Mar-27	0%	 Interior Wall Framing – Area B (Offices, Storage, Shred, Restrooms)																																															
	 Overhead MEP Rough-In		20d	11-Mar-27	02-Apr-27	0%	 02-Apr-27, Overhead MEP Rough-In																																															
	 A23020	Overhead MEP Rough-In – Supply Air Trunk Mains – Area B	20d	11-Mar-27	02-Apr-27	0%	 Overhead MEP Rough-In – Supply Air Trunk Mains – Area B																																															
	 A23030	Overhead MEP Rough-In – Return Air Trunk Mains – Area B	15d	17-Mar-27	02-Apr-27	0%	 Overhead MEP Rough-In – Return Air Trunk Mains – Area B																																															
	 Area B – Terminal & Equipment Installation		25d	11-Mar-27	08-Apr-27	0%	 08-Apr-27, Area B – Terminal & Equipment Installation																																															
	 A23060	Condensing Unit Installation – Exterior Pads (ACCU, Area B)	10d	11-Mar-27	23-Mar-27	0%	 Condensing Unit Installation – Exterior Pads (ACCU, Area B)																																															
	 A23050	Fan Coil Unit Installation – Storage (FCU-B101)	5d	17-Mar-27	23-Mar-27	0%	 Fan Coil Unit Installation – Storage (FCU-B101)																																															
	 A23040	VAV Box Installation – Area B (VAV-B111 thru VAV-B123)	15d	23-Mar-27	08-Apr-27	0%	 VAV Box Installation – Area B (VAV-B111 thru VAV-B123)																																															
	 Area B – Duct Run-Outs & Terminal Devices		15d	29-Mar-27	14-Apr-27	0%	 14-Apr-27, Area B – Duct Run-Outs & Terminal Devices																																															
	 A23070	Duct Run-Outs & Supply Diffuser Rough-In – Area B	15d	29-Mar-27	14-Apr-27	0%	 Duct Run-Outs & Supply Diffuser Rough-In – Area B																																															
	 A23080	Return / Exhaust Grille Rough-In – Area B	10d	02-Apr-27	14-Apr-27	0%	 Return / Exhaust Grille Rough-In – Area B																																															
	 Area B – Close-In		15d	14-Apr-27	30-Apr-27	0%	 30-Apr-27, Area B – Close-In																																															
	 A23090	Ceiling Grid & Drywall Close-In – Area B	15d	14-Apr-27	30-Apr-27	0%	 Ceiling Grid & Drywall Close-In – Area B																																															
	 Area B – Trim-Out		10d	20-Apr-27	30-Apr-27	0%	 30-Apr-27, Area B – Trim-Out																																															
	 A23100	Diffuser & Grille Final Trim-Out – Area B	10d	20-Apr-27	30-Apr-27	0%	 Diffuser & Grille Final Trim-Out – Area B																																															
	 System-Wide Ductwork Specialties		35d	17-Mar-27	26-Apr-27	0%	 26-Apr-27, System-Wide Ductwork Specialties																																															
	 A23150	Acoustic Duct Liner Installation – First 10 ft from RTU Supply/Return	5d	17-Mar-27	23-Mar-27	0%	 Acoustic Duct Liner Installation – First 10 ft from RTU Supply/Return																																															
	 A23130	Exhaust Air Ductwork Rough-In – Area A & B (E1/E2 Grille Runs)	15d	23-Mar-27	08-Apr-27	0%	 Exhaust Air Ductwork Rough-In – Area A & B (E1/E2 Grille Runs)																																															
	 A23140	Transfer Air / Outdoor Air Duct Rough-In	10d	23-Mar-27	02-Apr-27	0%	 Transfer Air / Outdoor Air Duct Rough-In																																															
	 A23170	Birdscreen Installation – Transfer Air & Louver Openings	5d	29-Mar-27	02-Apr-27	0%	 Birdscreen Installation – Transfer Air & Louver Openings																																															
	 A23180	Flexible Connections – Vibration-Isolated Equipment (CRAC, ACCU, FCU)	5d	02-Apr-27	08-Apr-27	0%	 Flexible Connections – Vibration-Isolated Equipment (CRAC, ACCU, FCU)																																															
	 A23160	Manual Balancing Damper Installation – Area A & B	10d	14-Apr-27	26-Apr-27	0%	 Manual Balancing Damper Installation – Area A & B																																															
	 Controls & BAS																																																					

HRL1 - Preliminary Schedule A1 - Rev.00 - Draft
#05.3.1.B1



03-Sep-26

Activity ID		Activity Name	Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
	A10200	Generator paralleling switchgear	10d	13-Nov-26	24-Nov-26	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																

- Generator paralleling switchgear
- Automatic Transfer Switch (ATS) installation
- UPS output distribution board
- UPS module installation
- UPS battery system installation
- Static Transfer Switch (STS) installation
- Panel Install & Termination
- Sub-metering installation
- Surge Protective Device (SPD) installation
- Feeder conduit & cable installation
- Wire Pull
- Pull & Terminate Wire To Switchboard
- Testing & Continuity Checks
- Lighting Fixture Install
- Device & Receptacle Trim-Out
- Utility service energization coordination
- Testing

29-Dec-26, GALLERY
29-Dec-26, Critical Power Distribution

- Mobilization & Layout
- Trapeze / strut support framing
- Cable tray & ladder rack supports
- Conduit hangers & supports
- Critical power busway installation
- Wall sleeve installation
- Conduit & Box Rough-In
- Cable Tray / Raceway Install
- Remote Power Panel (RPP) installation
- Fire caulking / firestopping of penetrations
- Facility PDU installation
- Wire Pull
- Panel Install & Termination
- Lighting Fixture Install
- Device & Receptacle Trim-Out
- Testing & Continuity Checks

30-Dec-26, DATA HALL — WHITE SPACE
30-Dec-26, Rack Power Distribution

- Hot Aisle Containment (HAC) install

Actual Level of Effort Remaining Work Milestone
Actual Work Critical Remaining Work summary


Date	Revision	Checked	Approved
02-Sep-26	Preliminary Schedule	REDACTED	

HRL1 - Preliminary Schedule A1 - Rev.00 - Draft
#05.3.1.B1



03-Sep-26

Activity ID	Activity Name	Original Duration	Start	Finish	Duration % Complete	A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															

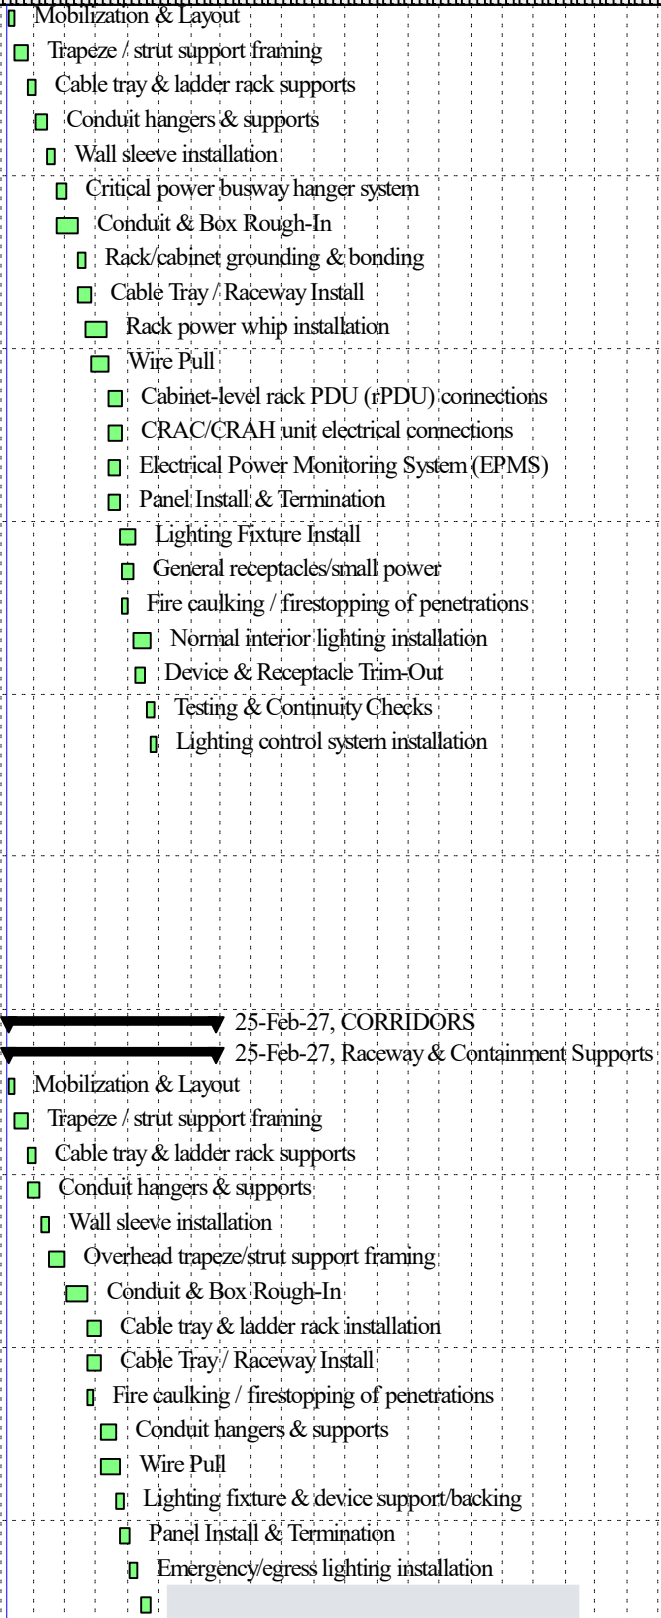

Actual Level of Effort Remaining Work Milestone
Actual Work Critical Remaining Work summary

Date	Revision	Checked	Approved
02-Sep-26	Preliminary Schedule	REDACTED	

alston
CONSTRUCTION
MISSION CRITICAL

[illegible]

alston
CONSTRUCTION
MISSION CRITICAL

[illegible]
