


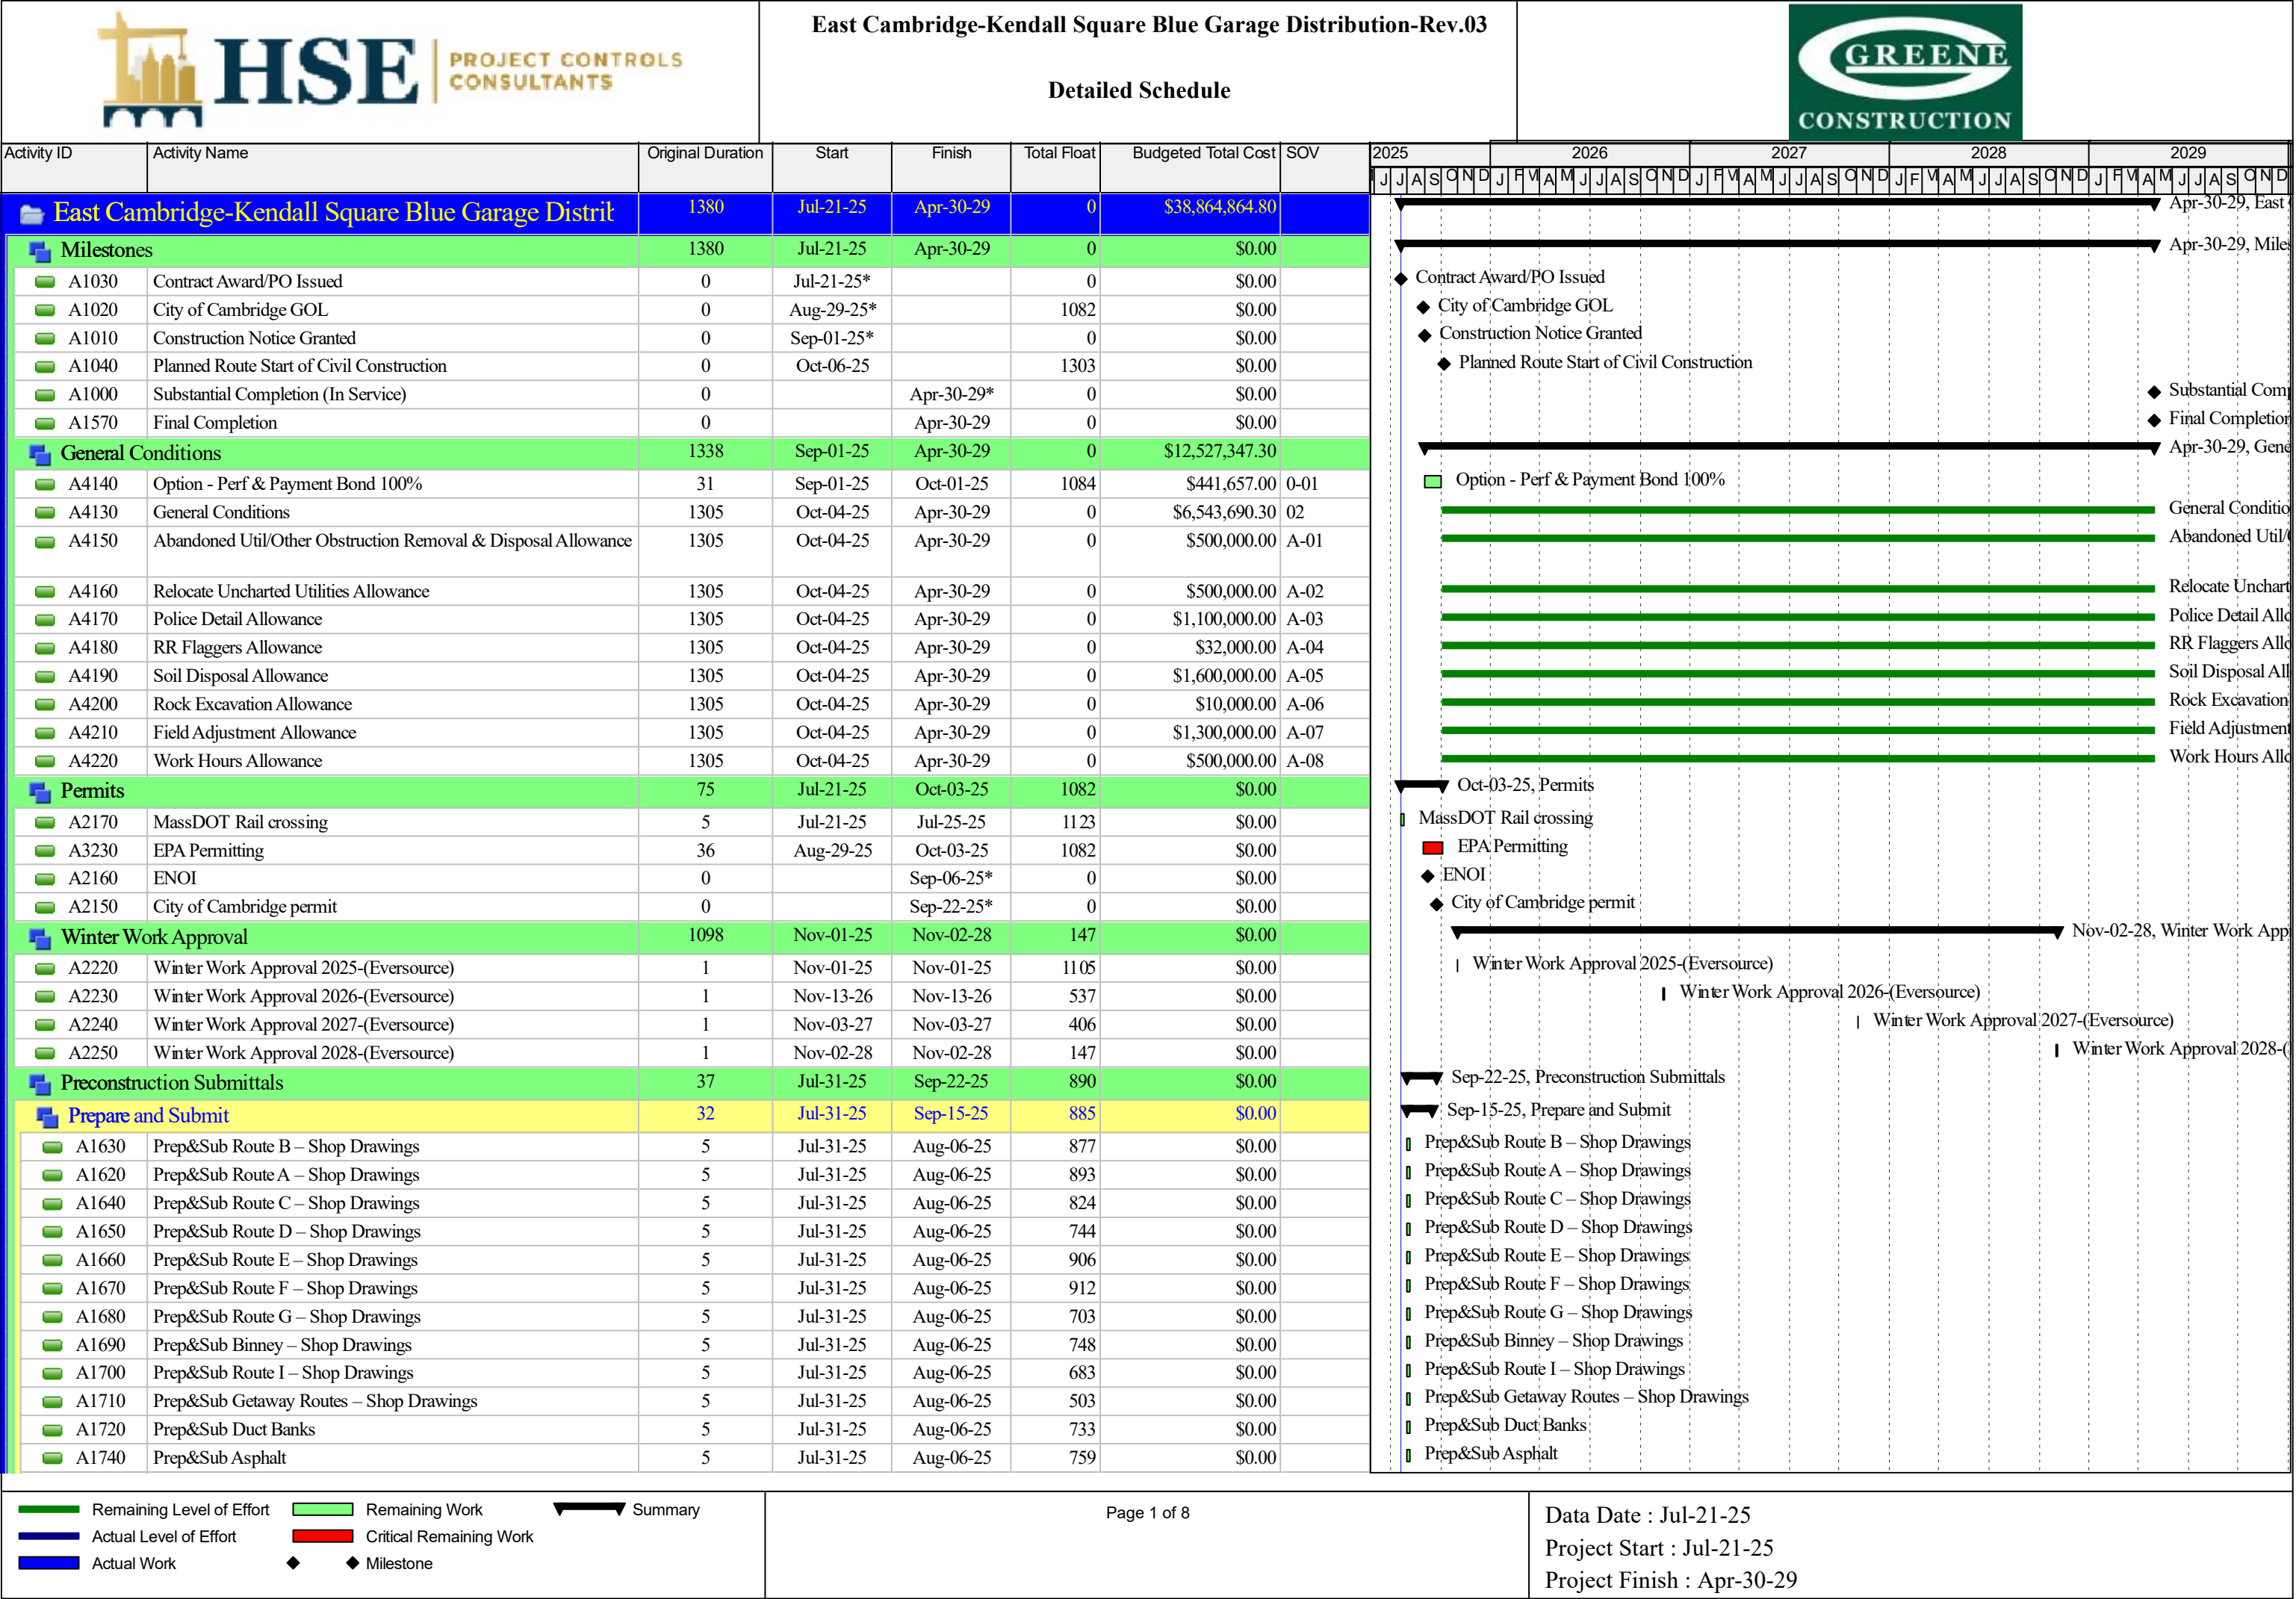

Remaining Level of Effort Actual Level of Effort Actual Work Remaining Work Critical Remaining Work ◆ Milestone Summary	Page 3 of 8	Data Date : Jul-21-25 Project Start : Jul-21-25 Project Finish : Apr-30-29
---	-------------	--

Detailed Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Budgeted Total Cost	SOV	2025												2026												2027												2028												2029																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
								J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
Route A	 A2780	Route A-Vault Installation (#1)	5	Jun-16-28	Jun-23-28	190	\$90,677.48	04																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		

	Route A-Vault Installation (#1)
	Route A-Duct Bank Installation (215 LF)
	Route A-Proofing
	Route A-Final Restoration
	Jul-18-28, Close Out
	Route A-As Built Drawings
	Route A-Post Construction Photos and
	Route A-Close Out Survey
	Route A-Punch List
	Route A-Demobilization
	Aug-10-28, Route B
	Aug-01-28, Civil Works
	Route B-Planned Route Start
	Route B-City Of Cambridge Permit
	Route B-ACM NTWP permit
	Route B-Duct Bank Abandonment (Eversource)
	Route B-G Greene Released to Start Civil Work
	Route B-Enabling work & Pre-Construction Photos
	Route B-Duct Banks Removal (405 LF)
	Route B-Temporary Restoration
	Route B-Duct Bank Installation (405 LF)
	Route B-Proofing
	Route B-Final Restoration
	Aug-10-28, Close Out
	Route B-As Built Drawings
	Route B-Post Construction Photos and
	Route B-Close Out Survey
	Route B-Punch List
	Route B-Demobilization
	Oct-26-28, Route C
	Oct-18-28, Civil Works
	Route C-Planned Route Start
	Route C-City Of Cambridge Permit
	Route C-ACM NTWP permit
	Route C--Duct Bank Abandonment (Eversource)
	Route C-G Greene Released to Start Civil Work
	Route C-Enabling work & Pre-Construction Photos
	Route C-Duct Banks Removal (940 LF)
	Route C-Temporary Restoration
	Route C-Duct Bank Installation (940 LF)
	Route C-Proofing
	Route C-Final Restoration
	Oct-26-28, Close Out
	Route C-As Built Drawings

			East Cambridge-Kendall Square Blue Garage Distribution-Rev.03																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
Detailed Schedule																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Budgeted Total Cost	SOV	2025					2026					2027					2028					2029																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
								J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
A3930	Route C-Post Construction Photos and Video	5	Oct-19-28	Oct-25-28	121	\$0.00																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							</



Detailed Schedule

Activity ID	Activity Name		Original Duration	Start	Finish	Total Float	Budgeted Total Cost	SOV	2025					2026					2027					2028					2029							
									J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S
	📁 Civil Works		25	Oct-16-28	Nov-09-28	154	\$40,589.33																												▼ Nov-09-28, Civil Works	
	🟢 A3450	Route F-Planned Route Start	0	Oct-16-28*		0	\$0.00																											◆ Route F-Planned Route Start		
	🟢 A3460	Route F-City Of Cambridge Permit	1	Oct-16-28	Oct-16-28	105	\$0.00																											Route F-City Of Cambridge Per		
	🟢 A4790	Route F-ACM NTWP permit	1	Oct-17-28	Oct-17-28	105	\$0.00																											Route F-ACM NTWP permit		
	🟢 A4380	Route F-Duct Bank Abandonment (Eversource)	10	Oct-18-28	Oct-31-28	105	\$0.00																											▢ Route F-Duct Bank Abandonm		
	🟢 A4670	Route F-G Greene Released to Start Civil Work	1	Nov-01-28	Nov-01-28	154	\$0.00																											Route F-G Greene Released to		
	🟢 A3170	Route F-Duct Banks Removal (25 LF)	2	Nov-02-28	Nov-03-28	105	\$3,139.91	03																										Route F-Duct Banks Removal		
	🟢 A4550	Route F-Temporary Restoration	4	Nov-02-28	Nov-07-28	105	\$2,586.10	04																											■ Route F-Temporary Restoratio	
	🟢 A3190	Route F-Duct Bank Installation (25 LF)	2	Nov-06-28	Nov-07-28	105	\$29,522.90	04																										Route F-Duct Bank Installatio		
	🟢 A3210	Route F-Final Restoration	2	Nov-08-28	Nov-09-28	105	\$5,340.42	05																											Route F-Final Restoration	
	📁 Close Out		6	Nov-10-28	Nov-17-28	105	\$0.00																												▼ Nov-17-28, Close Out	
	🟢 A4070	Route F-As Built Drawings	5	Nov-10-28	Nov-16-28	105	\$0.00																												▢ Route F-As Built Drawings	
	🟢 A4080	Route F-Post Construction Photos and Video	5	Nov-10-28	Nov-16-28	105	\$0.00																												▢ Route F-Post Construction Ph	
	🟢 A4090	Route F-Close Out Survey	5	Nov-10-28	Nov-16-28	105	\$0.00																												▢ Route F-Close Out Survey	
	🟢 A4100	Route F-Punch List	5	Nov-10-28	Nov-16-28	105	\$0.00																												▢ Route F-Punch List	
	🟢 A4110	Route F-Demobilization	1	Nov-17-28	Nov-17-28	105	\$0.00																												Route F-Demobilization	
	📁 CClose Out		6	Apr-23-29	Apr-30-29	0	\$0.00																												▼ Apr-30-29, CClose	
	🟢 A4120	Final Inspection	1	Apr-23-29	Apr-23-29	0	\$0.00																												Final Inspection	
	🟢 A2120	Final Punch List	5	Apr-24-29	Apr-30-29	0	\$0.00																													▢ Final Punch List
