










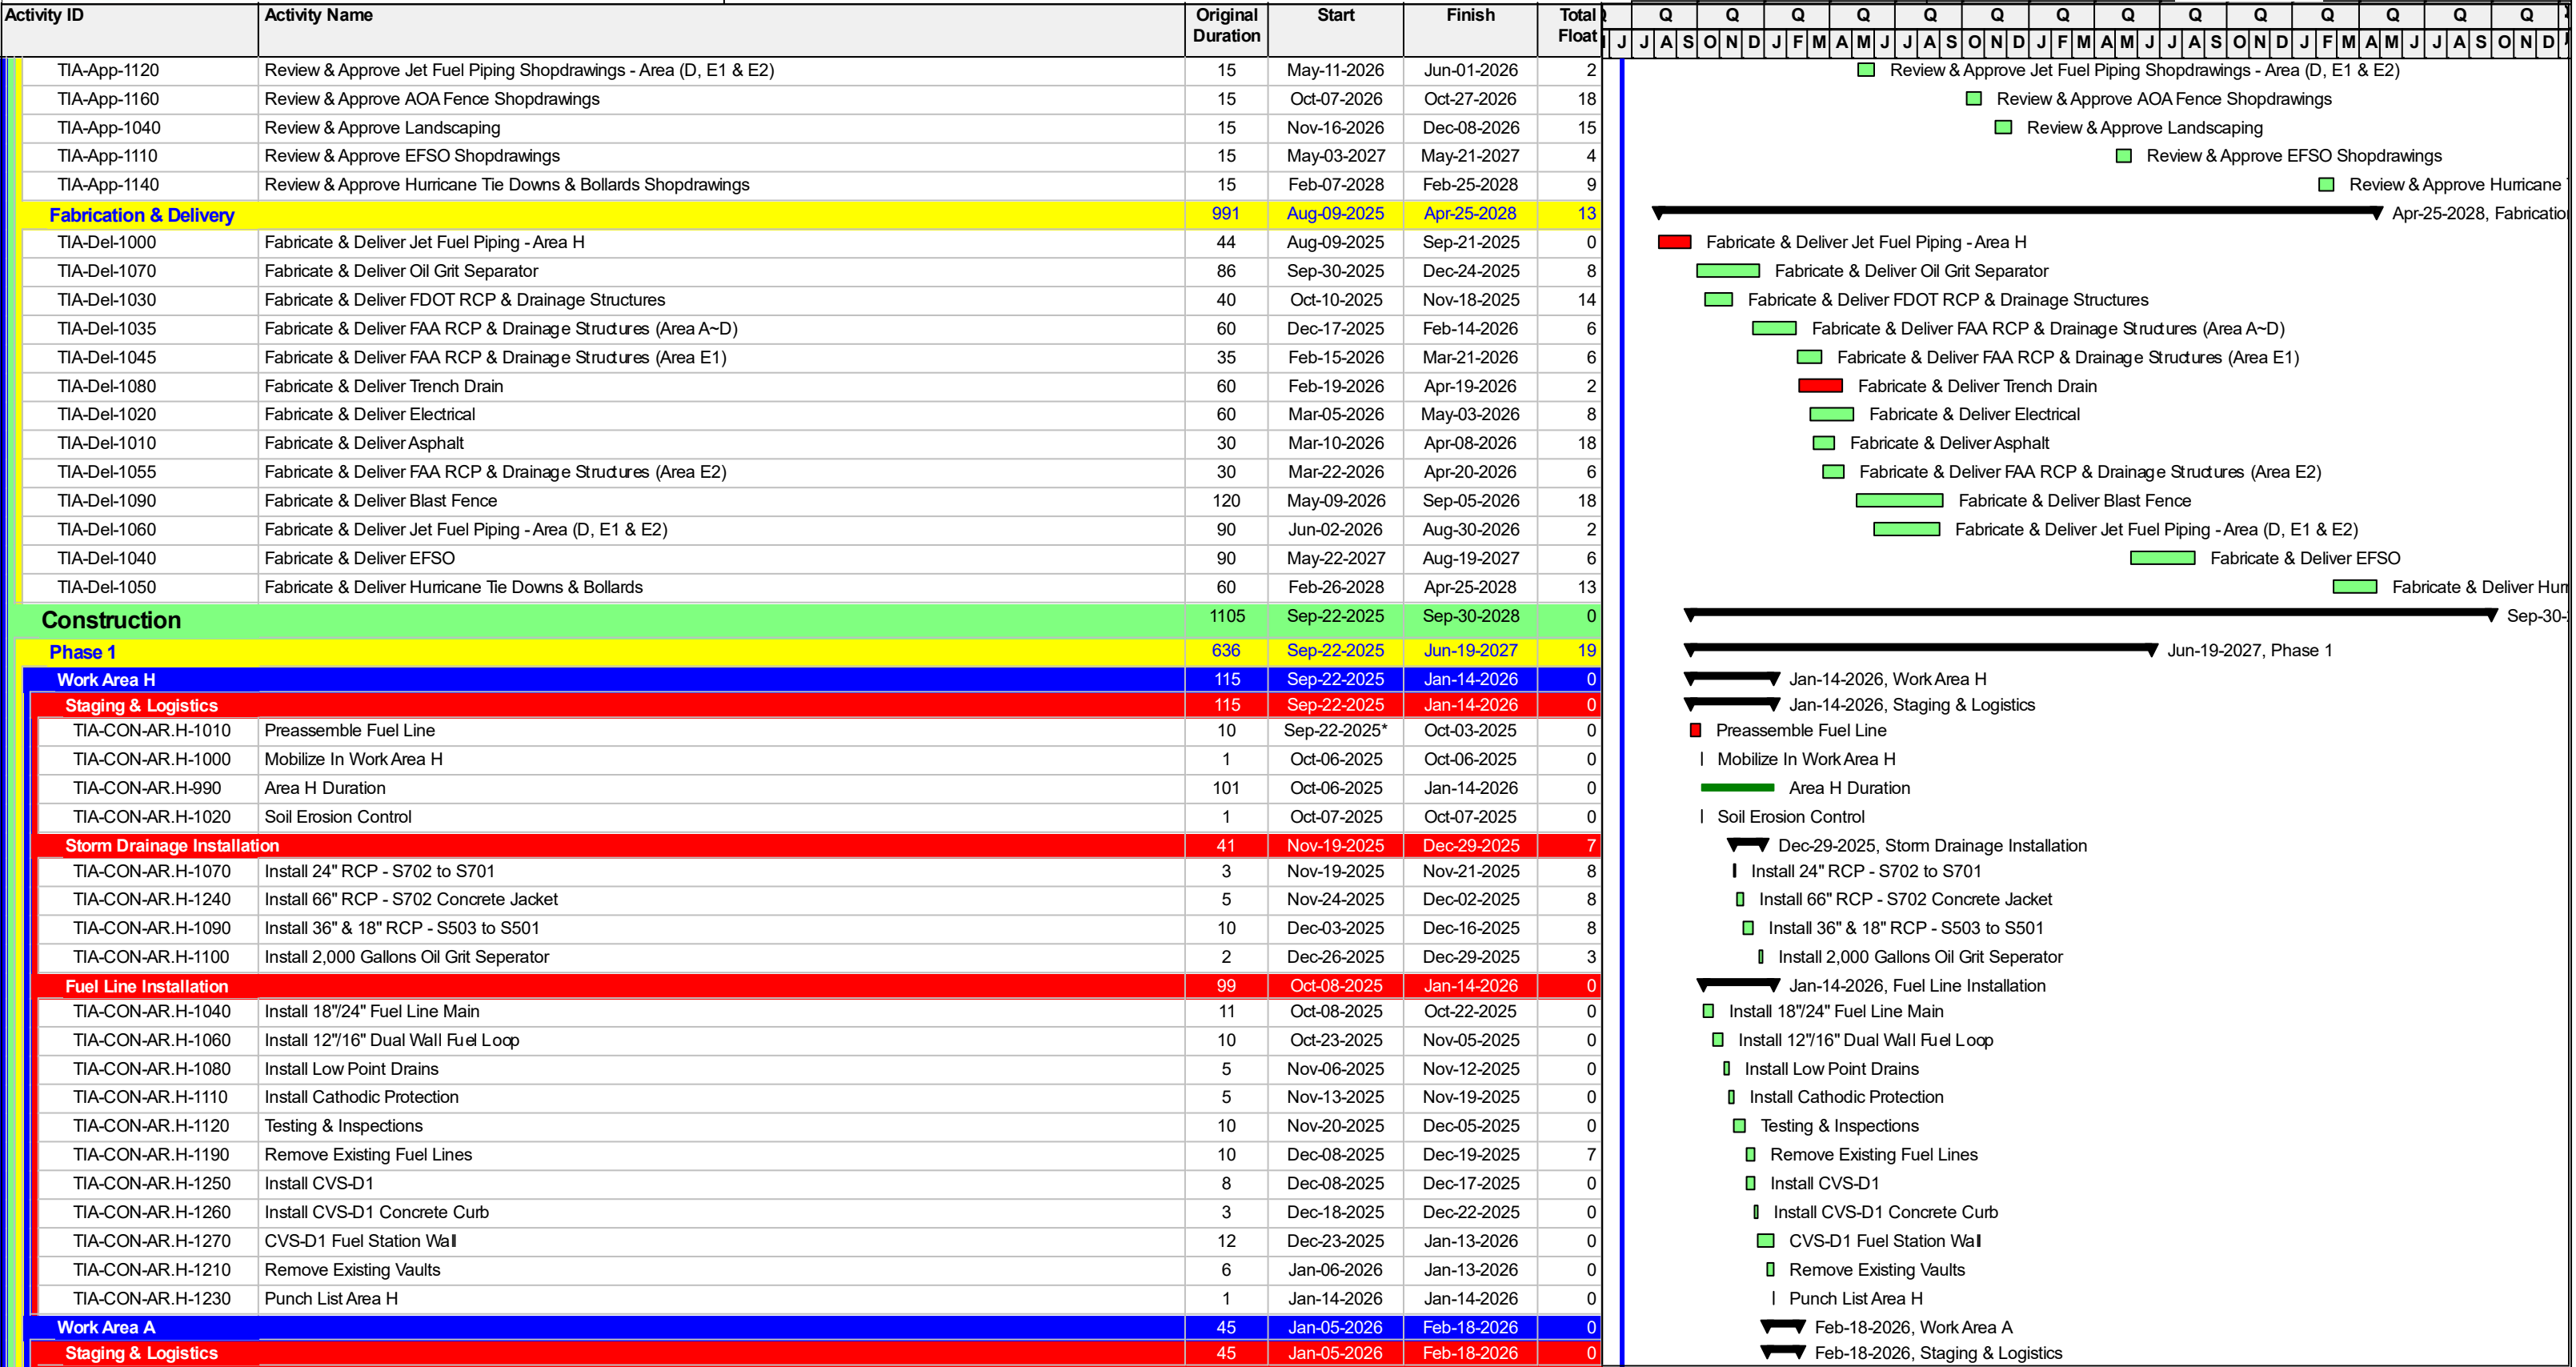

TIA Airside D Apron Baseline Schedule Rev.02
Detailed Schedule Layout



Activity ID	Activity Name	Original Duration	Start	Finish	Total Float																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
						J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M



Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Page 7 of 16

Data Date: Jun-19-2025

Project Start: Jun-19-2025

Project Finish: Oct-15-2028

TASK filter: All Activities



[illegible]



Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Page 11 of 16

Data Date: Jun-19-2025

Project Start: Jun-19-2025

Project Finish: Oct-15-2028

TASK filter: All Activities



Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Page 12 of 16

Data Date: Jun-19-2025

Project Start: Jun-19-2025

Project Finish: Oct-15-2028

TASK filter: All Activities

		TIA Airside D Apron Baseline Schedule Rev.02 Detailed Schedule Layout																																	
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float																														
Apron Concrete Pavement		245	Oct-12-2026	Sep-30-2027	0	Sep-30-2027, Apron Concrete Pavement																													
TIA-CON-AR.E1-1300	Subgrade Grading - E1-1	8	Oct-12-2026	Oct-21-2026	65	Subgrade Grading - E1-1																													
TIA-CON-AR.E1-1320	Place & Compact 6" Crushed Concrete - E1-1	8	Oct-22-2026	Nov-02-2026	69	Place & Compact 6" Crushed Concrete - E1-1																													
TIA-CON-AR.E1-1330	Subgrade Grading - E1-2	6	Oct-22-2026	Oct-29-2026	65	Subgrade Grading - E1-2																													
TIA-CON-AR.E1-1350	Place & Compact 6" Crushed Concrete - E1-2	8	Oct-30-2026	Nov-10-2026	65	Place & Compact 6" Crushed Concrete - E1-2																													
TIA-CON-AR.E1-1360	Subgrade Grading - E1-3	6	Oct-30-2026	Nov-06-2026	65	Subgrade Grading - E1-3																													
TIA-CON-AR.E1-1370	Fine Grading - E1-1	8	Nov-03-2026	Nov-12-2026	69	Fine Grading - E1-1																													
TIA-CON-AR.E1-1400	Subgrade Grading - E1-4	8	Nov-09-2026	Nov-18-2026	65	Subgrade Grading - E1-4																													
TIA-CON-AR.E1-1420	Place & Compact 6" Crushed Concrete - E1-3	6	Nov-11-2026	Nov-18-2026	65	Place & Compact 6" Crushed Concrete - E1-3																													
TIA-CON-AR.E1-1430	Fine Grading - E1-2	8	Nov-11-2026	Nov-20-2026	99	Fine Grading - E1-2																													
TIA-CON-AR.E1-1480	Place & Compact 6" Crushed Concrete - E1-4	6	Nov-19-2026	Nov-30-2026	65	Place & Compact 6" Crushed Concrete - E1-4																													
TIA-CON-AR.E1-1460	Subgrade Grading - E1-5	5	Nov-19-2026	Nov-25-2026	66	Subgrade Grading - E1-5																													
TIA-CON-AR.E1-1490	Fine Gradine - E1-3	5	Nov-19-2026	Nov-25-2026	66	Fine Gradine - E1-3																													
TIA-CON-AR.E1-1520	Place & Compact 6" Crushed Concrete - E1-5	6	Nov-30-2026	Dec-07-2026	125	Place & Compact 6" Crushed Concrete - E1-5																													
TIA-CON-AR.E1-1540	Fine Grading - E1-4	5	Dec-01-2026	Dec-07-2026	65	Fine Grading - E1-4																													
TIA-CON-AR.E1-1580	Fine Grading - E1-5	5	Dec-08-2026	Dec-14-2026	128	Fine Grading - E1-5																													
TIA-CON-AR.E1-1500	Subgrade Grading - E1-6	5	Jan-04-2027	Jan-08-2027	45	Subgrade Grading - E1-6																													
TIA-CON-AR.E1-1550	Place & Compact 6" Crushed Concrete - E1-6	6	Jan-11-2027	Jan-18-2027	45	Place & Compact 6" Crushed Concrete - E1-6																													
TIA-CON-AR.E1-1610	Fine Grading - E1-6	5	Jan-19-2027	Jan-25-2027	45	Fine Grading - E1-6																													
TIA-CON-AR.E1-1760	Pour 6" Lean Concrete - E1-1	14	Mar-30-2027	Apr-16-2027	0	Pour 6" Lean Concrete - E1-1																													
TIA-CON-AR.E1-1780	Pour 6" Lean Concrete - E1-2	14	Apr-19-2027	May-06-2027	0	Pour 6" Lean Concrete - E1-2																													
TIA-CON-AR.E1-1790	Lean Concrete Cure Time - E1-1	5	Apr-19-2027	Apr-23-2027	19	Lean Concrete Cure Time - E1-1																													
TIA-CON-AR.E1-1830	Form & Pour 18" Concrete Pavement - E1-1A	10	Apr-26-2027	May-07-2027	19	Form & Pour 18" Concrete Pavement - E1-1A																													
TIA-CON-AR.E1-1850	Pour 6" Lean Concrete - E1-3	14	May-07-2027	May-26-2027	0	Pour 6" Lean Concrete - E1-3																													
TIA-CON-AR.E1-1860	Lean Concrete Cure Time - E1-2	5	May-07-2027	May-13-2027	25	Lean Concrete Cure Time - E1-2																													
TIA-CON-AR.E1-1870	Form & Pour 18" Concrete Pavement - E1-1B	10	May-10-2027	May-21-2027	19	Form & Pour 18" Concrete Pavement - E1-1B																													
TIA-CON-AR.E1-1880	18" Concrete Pavement Cure Time - E1-1A	5	May-10-2027	May-14-2027	49	18" Concrete Pavement Cure Time - E1-1A																													
TIA-CON-AR.E1-1900	Form & Pour 18" Concrete Pavement - E1-2A	10	May-24-2027	Jun-07-2027	19	Form & Pour 18" Concrete Pavement - E1-2A																													
TIA-CON-AR.E1-1910	18" Concrete Pavement Cure Time - E1-1B	5	May-24-2027	May-28-2027	39	18" Concrete Pavement Cure Time - E1-1B																													
TIA-CON-AR.E1-1940	Pour 6" Lean Concrete - E1-4	15	May-27-2027	Jun-17-2027	0	Pour 6" Lean Concrete - E1-4																													
TIA-CON-AR.E1-1950	Lean Concrete Cure Time - E1-3	5	May-27-2027	Jun-03-2027	11	Lean Concrete Cure Time - E1-3																													
TIA-CON-AR.E1-2000	Form & Pour 18" Concrete Pavement - E1-3A	10	Jun-04-2027	Jun-17-2027	11	Form & Pour 18" Concrete Pavement - E1-3A																													
TIA-CON-AR.E1-1980	Form & Pour 18" Concrete Pavement - E1-2B	10	Jun-08-2027	Jun-21-2027	19	Form & Pour 18" Concrete Pavement - E1-2B																													
TIA-CON-AR.E1-1990	18" Concrete Pavement Cure Time - E1-2A	5	Jun-08-2027	Jun-14-2027	29	18" Concrete Pavement Cure Time - E1-2A																													
TIA-CON-AR.E1-2010	Lean Concrete Cure Time - E1-4	5	Jun-18-2027	Jun-24-2027	4	Lean Concrete Cure Time - E1-4																													
TIA-CON-AR.E1-2020	Pour 6" Lean Concrete - E1-5	15	Jun-18-2027	Jul-09-2027	0	Pour 6" Lean Concrete - E1-5																													
TIA-CON-AR.E1-2040	Form & Pour 18" Concrete Pavement - E1-3B	10	Jun-18-2027	Jul-01-2027	11	Form & Pour 18" Concrete Pavement - E1-3B																													
TIA-CON-AR.E1-2050	18" Concrete Pavement Cure Time - E1-3A	5	Jun-18-2027	Jun-24-2027	21	18" Concrete Pavement Cure Time - E1-3A																													
TIA-CON-AR.E1-2030	18" Concrete Pavement Cure Time - E1-2B	5	Jun-22-2027	Jun-28-2027	19	18" Concrete Pavement Cure Time - E1-2B																													
TIA-CON-AR.E1-2070	Form & Pour 18" Concrete Pavement - E1-4A	10	Jun-25-2027	Jul-09-2027	4	Form & Pour 18" Concrete Pavement - E1-4A																													
TIA-CON-AR.E1-2080	18" Concrete Pavement Cure Time - E1-3B	5	Jul-02-2027	Jul-09-2027	11	18" Concrete Pavement Cure Time - E1-3B																													
TIA-CON-AR.E1-2130	Saw & Seal Concrete Pavement Joints - E1-1~E1-3	4	Jul-12-2027	Jul-15-2027	11	Saw & Seal Concrete Pavement Joints - E1-1~E1-3																													
TIA-CON-AR.E1-2090	Pour 6" Lean Concrete - E1-6	15	Jul-12-2027	Jul-30-2027	0	Pour 6" Lean Concrete - E1-6																													
TIA-CON-AR.E1-2100	Lean Concrete Cure Time - E1-5	5	Jul-12-2027	Jul-16-2027	20	Lean Concrete Cure Time - E1-5																													
TIA-CON-AR.E1-2110	Form & Pour 18" Concrete Pavement - E1-4B	11	Jul-12-2027	Jul-26-2027	4	Form & Pour 18" Concrete Pavement - E1-4B																													
TIA-CON-AR.E1-2120	18" Concrete Pavement Cure Time - E1-4A	5	Jul-12-2027	Jul-16-2027	47	18" Concrete Pavement Cure Time - E1-4A																													

Remaining Level of Effort

 Actual Level of Effort

 Actual Work

Remaining Work

 Critical Remaining Work

Milestone

 Milestone

Summary

Page 13 of 16

Data Date: Jun-19-2025

Project Start: Jun-19-2025

Project Finish: Oct-15-2028

TASK filter: All Activities



Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Page 14 of 16

Data Date: Jun-19-2025

Project Start: Jun-19-2025

Project Finish: Oct-15-2028

TASK filter: All Activities



Remaining Level of Effort Actual Level of Effort Actual Work Remaining Work Critical Remaining Work Milestone	Summary Page 15 of 16	Data Date: Jun-19-2025 Project Start: Jun-19-2025 Project Finish: Oct-15-2028 TASK filter: All Activities
--	--	---

