Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PRINCETON ELEMENTRY SCHOOL									
Total		459	459	0	20MAY11	30AUG12	20MAY11	30AUG12	0
PRE CONSTRUCTION									
GMP									
ADMINISTRATION									
GMP2000	START PRINCETON	0	0	0	20MAY11*		20MAY11*		0
GMP2130	BIDDING GMP	17	17	0	20MAY11	13JUN11	20MAY11	13JUN11	0
GMP2140	RECEIVED ADD #1	1	1	0	14JUN11	14JUN11	14JUN11	14JUN11	0
GMP2150	PRICE ADD #1	8	8	0	15JUN11	24JUN11	15JUN11	24JUN11	0
GMP2160	ADD #1 GMP NEGOTIATIONS	27	27	0	27JUN11	03AUG11	27JUN11	03AUG11	0
OCPS ACTIVITIES									
ADMINISTRATION									
OCPS2000	SCHOOL OUT	0	0	0	08JUN11*		08JUN11*		0
OCPS2010	SELECTIVE DEMO TO PORTABLES	5	5	0	08JUN11	14JUN11	20JUN11	24JUN11	8
OCPS2020	OCPS MOVE OUT	9	9	0	08JUN11	20JUN11	20JUN11	30JUN11	8
OCPS2030	OCPS REMOVE LEASED PORTABLES	3	3	0	21JUN11	23JUN11	01JUL11	06JUL11	8
OCPS2040	INSTALL SWITCH IDF	1	1	0	19JUN12	19JUN12	10JUL12	10JUL12	14
OCPS2050	OWNER INSTALL COMPUTERS	15	15	0	13JUL12	02AUG12	24JUL12	13AUG12	7
PER2040	ST. JOHNS WATER MANAGEMENT	54	54	0	23MAY11	05AUG11	31MAY11	15AUG11	6
PER2060	DEP FRONT END	1	1	0	20MAY11	20MAY11	30MAY11	30MAY11	6
PERMITTING									
PREP SITE									
PER01.1000	TEMP OFFICE TRAILER BUILDING	3	3	0	23JUN11	27JUN11	18JUL11	20JUL11	16
PER01.1010	TEMP OFFICE TRAILER ELECTRICAL	3	3	0	09AUG11	11AUG11	24AUG11	26AUG11	11
PER01.1020	TEMP OFFICE TRAILER PLUMBING	3	3	0	09AUG11	11AUG11	24AUG11	26AUG11	11
PER01.1030	BUILDING	3	3	0	04AUG11	08AUG11	01SEP11	06SEP11	20
PER02.1010	EARLY DEMOLITION	3	3	0	24JUN11	28JUN11	18JUL11	20JUL11	15
PER02.1020	IRRIGATION	3	3	0	25AUG11	29AUG11	19SEP11	21SEP11	16
PER02.1030	PLAYGROUND	3	3	0	25AUG11	29AUG11	19SEP11	21SEP11	16
PER02.1040	SITE	2	2	0	05AUG11	08AUG11	12AUG11	15AUG11	5
PER02.1050	FENCING & GATES	3	3	0	25AUG11	29AUG11	22SEP11	26SEP11	19
PER02.1060	TEMP FENCE	3	3	0	24JUN11	28JUN11	06JUL11	08JUL11	7
PER02.1070	BUILDING DEMOLITION	3	3	0	24JUN11	28JUN11	18JUL11	20JUL11	15
PER02.1075	SELECTIVE DEMOLITION	3	3	0	11AUG11	15AUG11	15AUG11	17AUG11	2
PER07.1000	ROOF	3	3	0	18AUG11	22AUG11	14SEP11	16SEP11	18
PER15.1000	GAS	3	3	0	09AUG11	11AUG11	01SEP11	06SEP11	17
PER15.1010	KITCHEN HOOD	3	3	0	11AUG11	15AUG11	09SEP11	13SEP11	20
PER15.1020	FIRE LINES, HYDRANTS, PIV, FDC	3	3	0	05AUG11	09AUG11	01SEP11	06SEP11	19

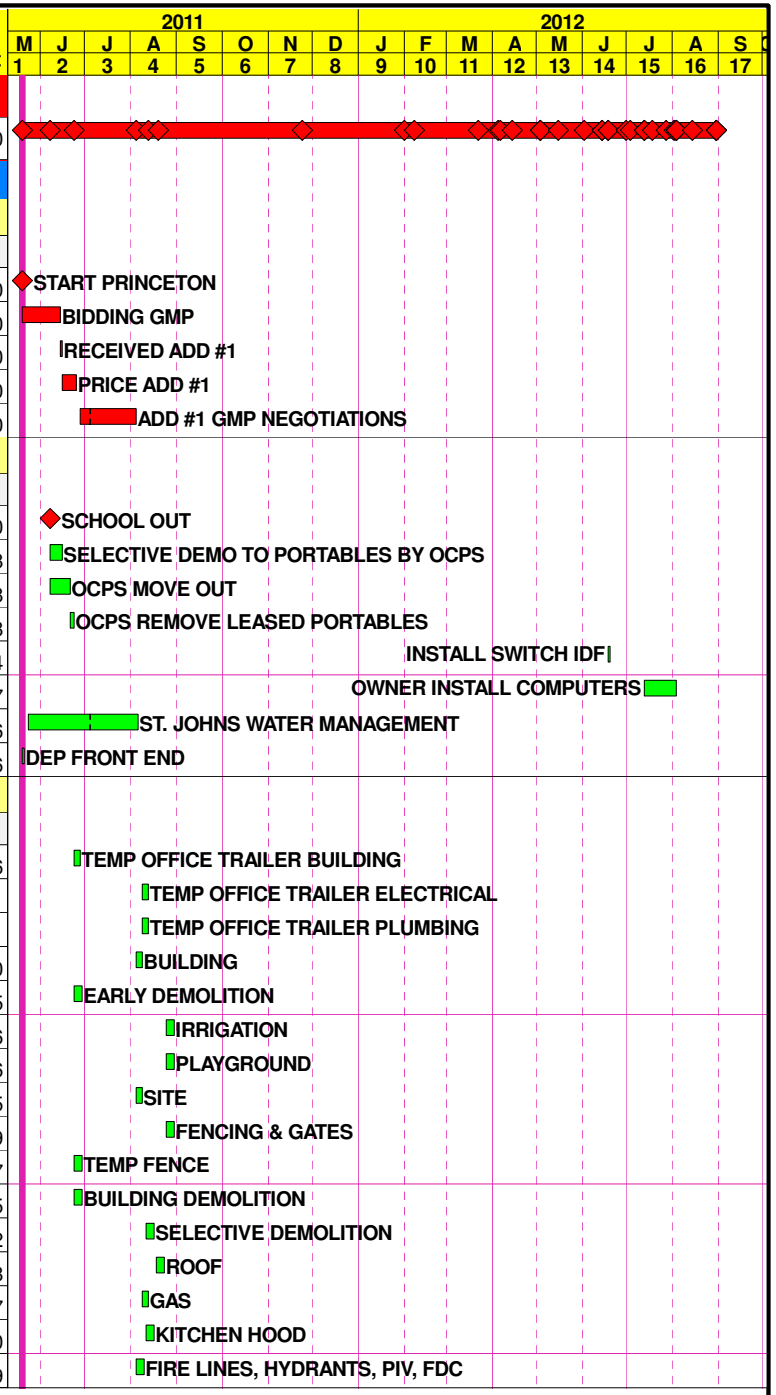

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

Sheet 1 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PER15.1030	FIRE SPRINKLER	3	3	0	11AUG11	15AUG11	09SEP11	13SEP11	20
PER15.1040	PHONE / VOICE / DATA /CATV	3	3	0	09AUG11	11AUG11	01SEP11	06SEP11	17
PER15.1050	MECHANICAL	3	3	0	09AUG11	11AUG11	01SEP11	06SEP11	17
PER15.1060	PLUMBING	3	3	0	09AUG11	11AUG11	01SEP11	06SEP11	17
PER16.1000	LIGHTNING PROTECTION	3	3	0	09AUG11	11AUG11	29AUG11	31AUG11	14
PER16.1010	SMART BOARDS	3	3	0	12AUG11	16AUG11	01SEP11	06SEP11	14
PER16.1020	SECURITY	3	3	0	12AUG11	16AUG11	01SEP11	06SEP11	14
PER16.1030	AUDIO VISUAL	3	3	0	12AUG11	16AUG11	01SEP11	06SEP11	14
PER16.1040	IT / SWITCH / MODEM	3	3	0	12AUG11	16AUG11	01SEP11	06SEP11	14
PER16.1050	FIRE ALARM	3	3	0	12AUG11	16AUG11	01SEP11	06SEP11	14
PER16.1060	ELECTRICAL	3	3	0	12AUG11	16AUG11	01SEP11	06SEP11	14
PER16.1070	TEMP POWER	3	3	0	09AUG11	11AUG11	19AUG11	23AUG11	8
GENERAL MILESTONES									
ADMINISTRATION									
GMS2000	CONSTRUCTION NTP EARLY SITE	0	0	0	23JUN11		05JUL11		7
GMS2005	CONSTRUCTION NTP MAIN	0	0	0	04AUG11		04AUG11		0
GMS2007	EARLY SITE AND DEMOLITION	0	0	0		11AUG11		15AUG11	2
GMS2010	PERMANENT POWER AVAILABLE TO	0	0	0		07FEB12		28FEB12	15
GMS2020	ALL UTILITY CONNECTIONS MADE	0	0	0		31JAN12		10FEB12	8
GMS2030	FDEP CLEARANCE	0	0	0		01AUG12		29AUG12	20
GMS2035	ALL BUILDINGS ENERGIZED	0	0	0		14JUN12		29JUN12	11
GMS2040	OCPS COMMISSIONING MEETING	0	0	0		29JUN12*		29JUN12*	0
GMS2045	SUB CONTRACTOR COMPLETION	0	0	0		02AUG12		30AUG12	20
GMS2050	PROJECT SUBSTANTIALLY	0	0	0		03AUG12		30AUG12	19
GMS2060	SWITCH AND MODEM	0	0	0		18JUN12		13JUL12	18
GMS2075	DEP	25	25	0	20MAY11	23JUN11	30MAY11	01JUL11	6
GMS2080	FFE / OWNER TRANSITIONING	0	0	0		12JUL12		23JUL12	7
GMS2085	TEACHERS ARRIVE	0	0	0		13AUG12*		13AUG12*	0
GMS2090	BUILDING 1A BCCO REQ DOC'S	0	0	0		17JUL12		06AUG12	14
GMS2100	BUILDING 1B BCCO REQ DOC'S	0	0	0		02JUL12		19JUL12	12
GMS2110	BUILDING 2 BCCO REQ DOC'S	0	0	0		02AUG12		30AUG12	20
GMS2120	BUILDING 3 REQ BCCO DOC'S	0	0	0		03MAY12		31MAY12	19
GMS2130	BUILDING 4 BCCO REQ DOC'S	0	0	0		02MAY12		17MAY12	11
GMS2140	CONNECTOR BCCO REQ DOC'S	0	0	0		01JUN12		13JUN12	8
GMS2150	SITE BCCO REQ BCCO DOC'S	0	0	0		27JUL12		15AUG12	13
GMS2160	COMPLETION & PUNCH LISTS	0	0	0		29AUG12		30AUG12	1
GMS2165	OAC FINAL WALK THROUGH	0	0	0		29AUG12		30AUG12	1
GMS2170	PRINCETON COMPLETED	0	0	0		30AUG12		30AUG12	0

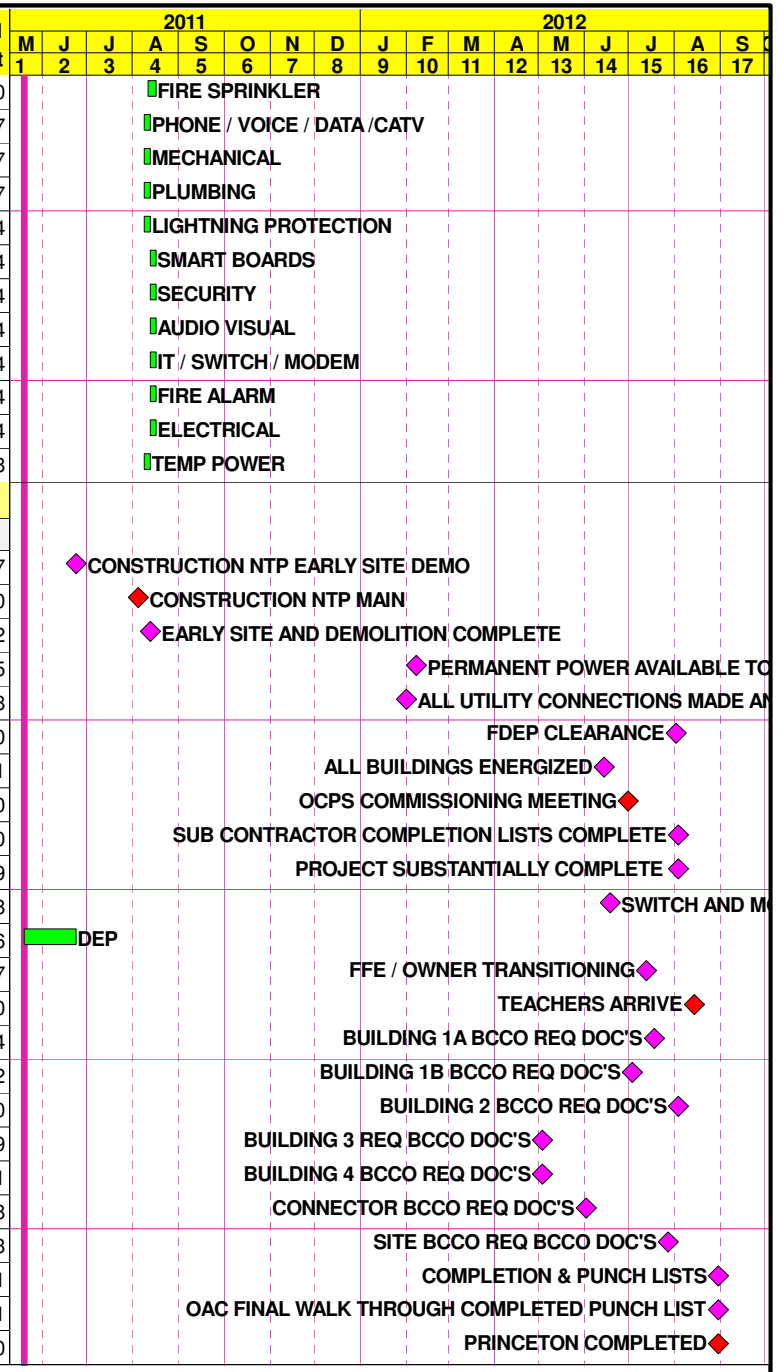

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
BID BUYOUT & AWARD									
EARLY SITE & DEMO									
ADMINISTRATION									
ESD2000	BID EARLY DEMO PACKAGE	1	1	0	20MAY11	20MAY11	17JUN11	17JUN11	20
ESD2010	SCOPE EARLY DEMO PACKAGE	10	10	0	23MAY11	03JUN11	20JUN11	01JUL11	20
ESD2020	AWARD EARLY DEMO PACKAGE	1	1	0	23JUN11	23JUN11	05JUL11	05JUL11	7
ESD2030	BID TREE REMOVAL EARLY DEMO	1	1	0	20MAY11	20MAY11	10JUN11	10JUN11	15
ESD2040	SCOPE TREE REMOVAL EARLY	10	10	0	23MAY11	03JUN11	13JUN11	24JUN11	15
ESD2050	AWARD TREE REMOVAL EARLY	5	5	0	06JUN11	10JUN11	27JUN11	01JUL11	15
REMAINING BUYOUT									
ADMINISTRATION									
BA02141910	BID SELECTIVE DEMO	1	1	0	13JUN11	13JUN11	22JUL11	22JUL11	28
BA02141920	SCOPE SELECTIVE DEMO	10	10	0	14JUN11	27JUN11	25JUL11	05AUG11	28
BA02141930	AWARD SELECTIVE DEMO	5	5	0	04AUG11	10AUG11	08AUG11	12AUG11	2
BA033010	BID CONCRETE	1	1	0	13JUN11	13JUN11	06JUL11	06JUL11	16
BA033020	SCOPE CONCRETE	10	10	0	14JUN11	27JUN11	07JUL11	20JUL11	16
BA033030	AWARD CONCRETE	5	5	0	04AUG11	10AUG11	08AUG11	12AUG11	2
BA03471310	BID TILT UP CONCRETE	1	1	0	13JUN11	13JUN11	16AUG11	16AUG11	45
BA03471320	SCOPE TILT UP CONCRETE	10	10	0	14JUN11	27JUN11	17AUG11	30AUG11	45
BA03471330	AWARD TILT UP CONCRETE	1	1	0	04AUG11	04AUG11	31AUG11	31AUG11	19
BA03521610	BID LT WT ROOF CONCRETE	1	1	0	13JUN11	13JUN11	28DEC11	28DEC11	137
BA03521620	SCOPE LT WT ROOF CONCRETE	10	10	0	14JUN11	27JUN11	29DEC11	12JAN12	137
BA03521630	AWARD LT WT ROOF CONCRETE	5	5	0	04AUG11	10AUG11	13JAN12	19JAN12	111
BA04000010	BID MASONRY	1	1	0	13JUN11	13JUN11	02SEP11	02SEP11	58
BA04000020	SCOPE MASONRY	10	10	0	14JUN11	27JUN11	06SEP11	19SEP11	58
BA04000030	AWARD MASONRY	5	5	0	04AUG11	10AUG11	20SEP11	26SEP11	32
BA05120010	BID STRUCTURAL STEEL	1	1	0	13JUN11	13JUN11	12AUG11	12AUG11	43
BA05120020	SCOPE STRUCTURAL STEEL	10	10	0	14JUN11	27JUN11	15AUG11	26AUG11	43
BA05120030	AWARD STRUCTURAL STEEL	3	3	0	04AUG11	08AUG11	29AUG11	31AUG11	17
BA05730010	BID LT DECORATIVE METAL RAILS	1	1	0	13JUN11	13JUN11	10FEB12	10FEB12	168
BA05730020	SCOPE DECORATIVE METAL RAILS	10	10	0	14JUN11	27JUN11	13FEB12	24FEB12	168
BA05730030	AWARD DECORATIVE METAL RAILS	10	10	0	04AUG11	17AUG11	27FEB12	09MAR12	142
BA06100010	BID ROUGH CARPENTRY	1	1	0	13JUN11	13JUN11	02AUG11	02AUG11	35
BA06100020	SCOPE ROUGH CARPENTRY	10	10	0	14JUN11	27JUN11	03AUG11	16AUG11	35
BA06100030	AWARD ROUGH CARPENTRY	10	10	0	04AUG11	17AUG11	17AUG11	30AUG11	9
BA06402310	BID INT ARCH WOODWORK	1	1	0	13JUN11	13JUN11	05DEC11	05DEC11	121
BA06402320	SCOPE INT ARCH WOODWORK	10	10	0	14JUN11	27JUN11	06DEC11	19DEC11	121
BA06402330	AWARD INT ARCH WOODWORK	10	10	0	04AUG11	17AUG11	20DEC11	04JAN12	95
BA07141610	BID WATERPROOFING	1	1	0	13JUN11	13JUN11	29JUL11	29JUL11	33

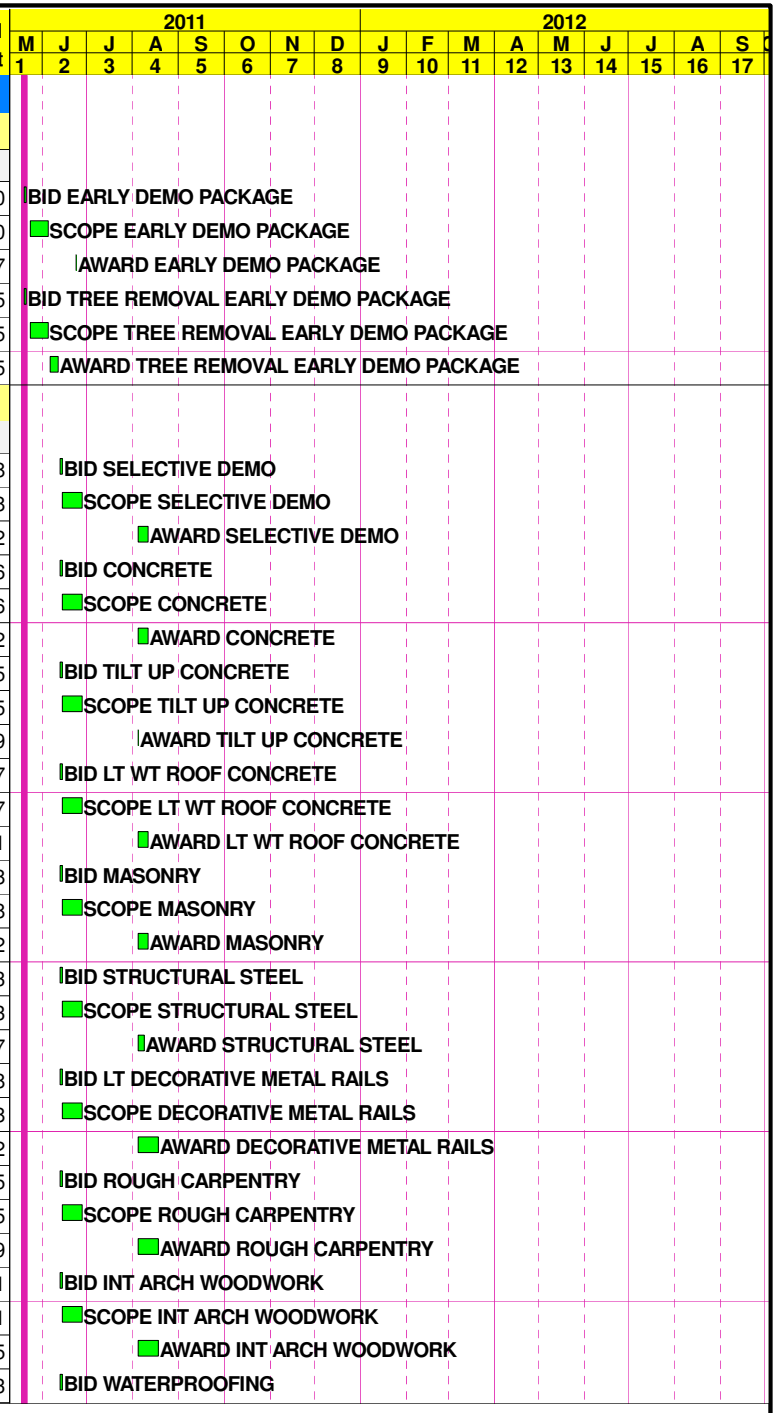

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
BA07141620	SCOPE WATERPROOFING	10	10	0	14JUN11	27JUN11	01AUG11	12AUG11	33
BA07141630	AWARD WATERPROOFING	5	5	0	04AUG11	10AUG11	15AUG11	19AUG11	7
BA07210010	BID THERMAL INSULATION	1	1	0	13JUN11	13JUN11	28NOV11	28NOV11	116
BA07210020	SCOPE THERMAL INSULATION	10	10	0	14JUN11	27JUN11	29NOV11	12DEC11	116
BA07210030	AWARD THERMAL INSULATION	15	15	0	04AUG11	24AUG11	13DEC11	04JAN12	90
BA07321310	BID ROOF TILES	1	1	0	13JUN11	13JUN11	15AUG11	15AUG11	44
BA07321320	SCOPE ROOF TILES	10	10	0	14JUN11	27JUN11	16AUG11	29AUG11	44
BA07321330	AWARD ROOF TILES	10	10	0	04AUG11	17AUG11	30AUG11	13SEP11	18
BA07540010	BID MEMBRANE ROOFING	1	1	0	13JUN11	13JUN11	15AUG11	15AUG11	44
BA07540020	SCOPE MEMBRANE ROOFING	10	10	0	14JUN11	27JUN11	16AUG11	29AUG11	44
BA07540030	AWARD MEMBRANE ROOFING	10	10	0	04AUG11	17AUG11	30AUG11	13SEP11	18
BA07723310	BID ROOF HATCHES	1	1	0	13JUN11	13JUN11	01NOV11	01NOV11	99
BA07723320	SCOPE ROOF HATCHES	10	10	0	14JUN11	27JUN11	02NOV11	15NOV11	99
BA07723330	AWARD ROOF HATCHES	15	15	0	04AUG11	24AUG11	16NOV11	08DEC11	73
BA07810010	BID SPRAY FIRE PROOFING	1	1	0	13JUN11	13JUN11	12DEC11	12DEC11	126
BA07810020	SCOPE SPRAY FIRE PROOFING	10	10	0	14JUN11	27JUN11	13DEC11	27DEC11	126
BA07810030	AWARD SPRAY FIRE PROOFING	5	5	0	04AUG11	10AUG11	28DEC11	04JAN12	100
BA07840010	BID FIRE STOPPING	1	1	0	13JUN11	13JUN11	13DEC11	13DEC11	127
BA07840020	SCOPE FIRE STOPPING	10	10	0	14JUN11	27JUN11	14DEC11	28DEC11	127
BA07840030	AWARD FIRE STOPPING	5	5	0	04AUG11	10AUG11	29DEC11	05JAN12	101
BA08110010	BID INSTALL DOORS	1	1	0	13JUN11	13JUN11	08FEB12	08FEB12	166
BA08110020	SCOPE INSTALL DOORS	10	10	0	14JUN11	27JUN11	09FEB12	22FEB12	166
BA08110030	AWARD INSTALL DOORS	15	15	0	04AUG11	24AUG11	23FEB12	14MAR12	140
BA08111310	BID DOORS & HDWR	1	1	0	13JUN11	13JUN11	02AUG11	02AUG11	35
BA08111320	SCOPE DOORS & HDWR	10	10	0	14JUN11	27JUN11	03AUG11	16AUG11	35
BA08111330	AWARD DOORS & HDWR	5	5	0	04AUG11	10AUG11	17AUG11	23AUG11	9
BA08311410	BID STOREFRONTS	1	1	0	13JUN11	13JUN11	13OCT11	13OCT11	86
BA08311420	SCOPE STORE FRONTS	10	10	0	14JUN11	27JUN11	14OCT11	27OCT11	86
BA08311430	AWARD STOREFRONTS	5	5	0	04AUG11	10AUG11	28OCT11	03NOV11	60
BA08511310	BID WINDOWS	1	1	0	13JUN11	13JUN11	15AUG11	15AUG11	44
BA08511320	SCOPE WINDOWS	10	10	0	14JUN11	27JUN11	16AUG11	29AUG11	44
BA08511330	AWARD WINDOWS	5	5	0	04AUG11	10AUG11	30AUG11	06SEP11	18
BA09010010	BID PAINT	1	1	0	13JUN11	13JUN11	22NOV11	22NOV11	114
BA09010020	SCOPE PAINT	10	10	0	14JUN11	27JUN11	23NOV11	08DEC11	114
BA09010030	AWARD PAINT	10	10	0	04AUG11	17AUG11	09DEC11	22DEC11	88
BA09211610	BID DRYWALL FRAMING	1	1	0	13JUN11	13JUN11	06SEP11	06SEP11	59
BA09211620	SCOPE DRYWALL FRAMING	10	10	0	14JUN11	27JUN11	07SEP11	20SEP11	59
BA09211630	AWARD DRYWALL FRAMING	5	5	0	04AUG11	10AUG11	21SEP11	27SEP11	33
BA09240010	BID PLASTER	1	1	0	13JUN11	13JUN11	15FEB12	15FEB12	171

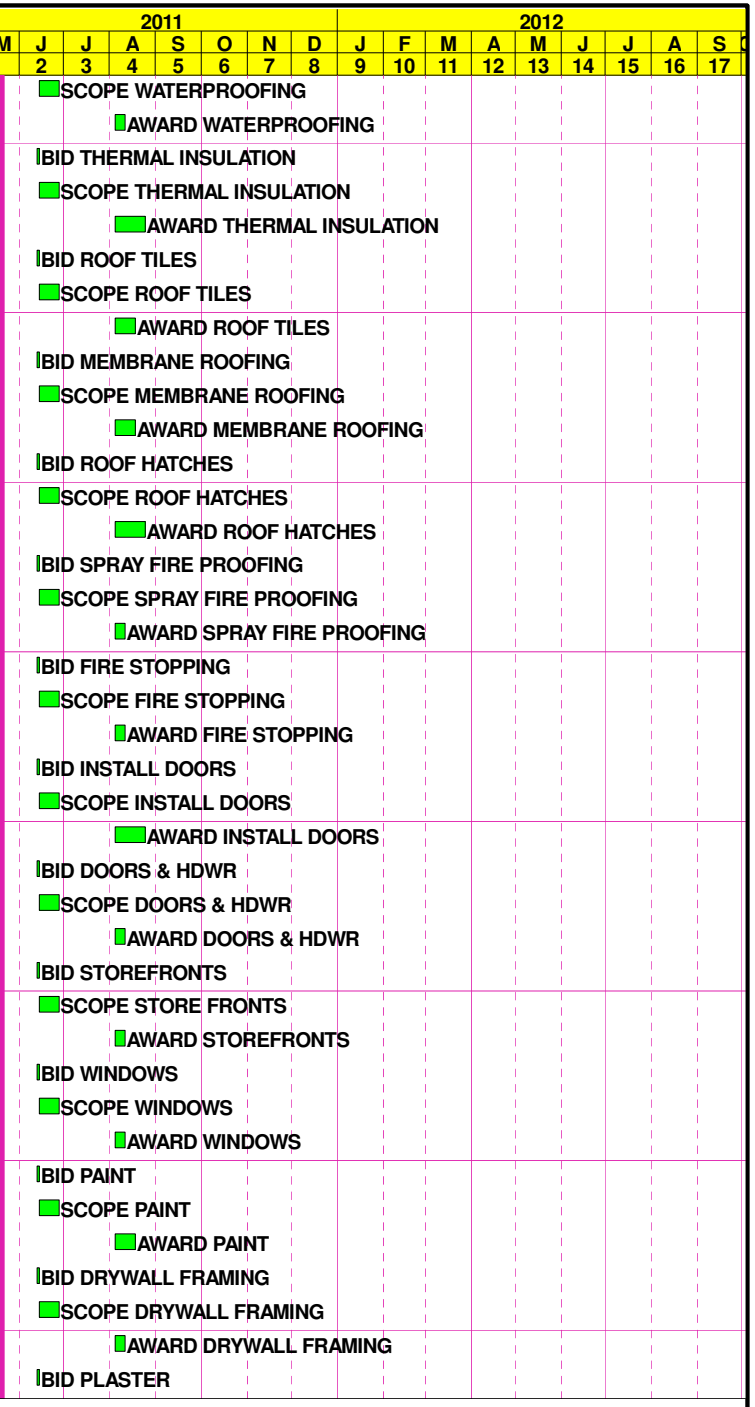

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
BA09240020	SCOPE PLASTER	10	10	0	14JUN11	27JUN11	16FEB12	29FEB12	171
BA09240030	AWARD PLASTER	10	10	0	04AUG11	17AUG11	01MAR12	14MAR12	145
BA09300010	BID TILE	1	1	0	13JUN11	13JUN11	01NOV11	01NOV11	99
BA09300020	SCOPE TILE	10	10	0	14JUN11	27JUN11	02NOV11	15NOV11	99
BA09300030	AWARD TILE	10	10	0	04AUG11	17AUG11	16NOV11	01DEC11	73
BA09511310	BID ACT CEILING	1	1	0	13JUN11	13JUN11	06DEC11	06DEC11	122
BA09511320	SCOPE ACT CEILING	10	10	0	14JUN11	27JUN11	07DEC11	20DEC11	122
BA09511330	AWARD ACT CEILING	10	10	0	04AUG11	17AUG11	21DEC11	05JAN12	96
BA09651610	BID FLOORING	1	1	0	13JUN11	13JUN11	08FEB12	08FEB12	166
BA09651620	SCOPE FLOORING	10	10	0	14JUN11	27JUN11	09FEB12	22FEB12	166
BA09651630	AWARD FLOORING	10	10	0	04AUG11	17AUG11	23FEB12	07MAR12	140
BA10000010	BID DIVISION 10	1	1	0	13JUN11	13JUN11	07SEP11	07SEP11	60
BA10000020	SCOPE DIVISION 10	10	10	0	14JUN11	27JUN11	08SEP11	21SEP11	60
BA10000030	AWARD DIVISION 10	15	15	0	04AUG11	24AUG11	22SEP11	12OCT11	34
BA10110010	BID VIS DISP	1	1	0	13JUN11	13JUN11	18JAN12	18JAN12	151
BA10110020	SCOPE VIS DISP	10	10	0	14JUN11	27JUN11	19JAN12	01FEB12	151
BA10110030	AWARD VIS DISP	15	15	0	04AUG11	24AUG11	02FEB12	22FEB12	125
BA10140010	BID SIGNAGE	1	1	0	13JUN11	13JUN11	17JAN12	17JAN12	150
BA10140020	SCOPE SIGNAGE	10	10	0	14JUN11	27JUN11	18JAN12	31JAN12	150
BA10140030	AWARD SIGNAGE	15	15	0	04AUG11	24AUG11	01FEB12	21FEB12	124
BA10732610	BID ALUM WALKWAY	1	1	0	13JUN11	13JUN11	10JAN12	10JAN12	145
BA10732620	SCOPE ALUM WALKWAY	10	10	0	14JUN11	27JUN11	11JAN12	24JAN12	145
BA10732630	AWARD ALUM WALKWAY	10	10	0	04AUG11	17AUG11	25JAN12	07FEB12	119
BA11400010	BID FOOD SERVICE	1	1	0	13JUN11	13JUN11	17AUG11	17AUG11	46
BA11400020	SCOPE FOOD SERVICE	10	10	0	14JUN11	27JUN11	18AUG11	31AUG11	46
BA11400030	AWARD FOOD SERVICE	5	5	0	04AUG11	10AUG11	01SEP11	08SEP11	20
BA11614310	BID STAGE CURTAINS	1	1	0	13JUN11	13JUN11	18JAN12	18JAN12	151
BA11614320	SCOPE STAGE CURTAINS	10	10	0	14JUN11	27JUN11	19JAN12	01FEB12	151
BA11614330	AWARD STAGE CURTAINS	15	15	0	04AUG11	24AUG11	02FEB12	22FEB12	125
BA11681310	BID PLAY EQ	1	1	0	13JUN11	13JUN11	11AUG11	11AUG11	42
BA11681320	SCOPE PLAY EQ	10	10	0	14JUN11	27JUN11	12AUG11	25AUG11	42
BA11681330	AWARD PLAY EQ	15	15	0	04AUG11	24AUG11	26AUG11	16SEP11	16
BA12142710	BID KILNS	1	1	0	13JUN11	13JUN11	13FEB12	13FEB12	169
BA12142720	SCOPE KILNS	10	10	0	14JUN11	27JUN11	14FEB12	27FEB12	169
BA12142730	AWARD KILNS	15	15	0	04AUG11	24AUG11	28FEB12	19MAR12	143
BA12211310	BID BLINDS	1	1	0	13JUN11	13JUN11	01FEB12	01FEB12	161
BA12211320	SCOPE BLINDS	10	10	0	14JUN11	27JUN11	02FEB12	15FEB12	161
BA12211330	AWARD BLINDS	15	15	0	04AUG11	24AUG11	16FEB12	07MAR12	135
BA12320010	BID CASEWORK	1	1	0	13JUN11	13JUN11	29NOV11	29NOV11	117

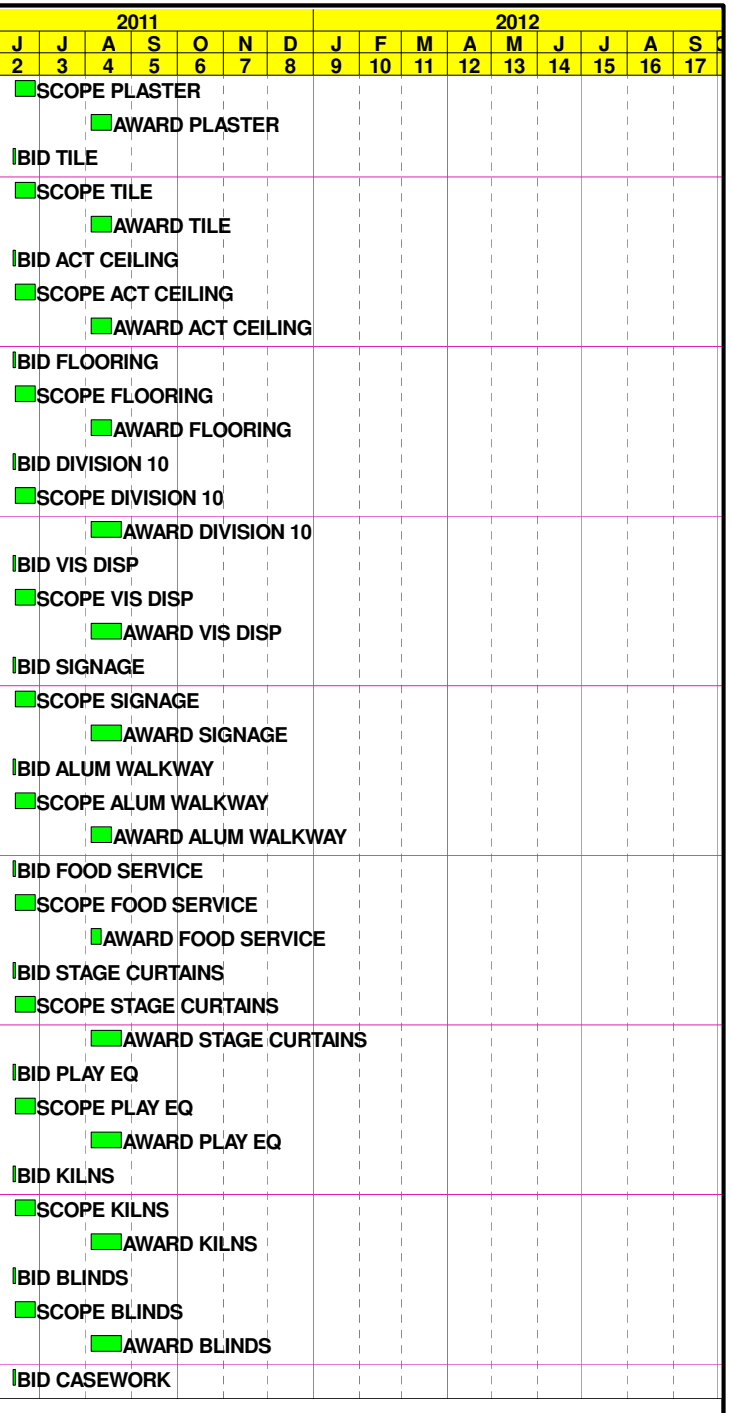

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
BA12320020	SCOPE CASEWORK	10	10	0	14JUN11	27JUN11	30NOV11	13DEC11	117
BA12320030	AWARD CASEWORK	10	10	0	04AUG11	17AUG11	14DEC11	28DEC11	91
BA14240010	BID ELEVATORS	1	1	0	13JUN11	13JUN11	29SEP11	29SEP11	76
BA14240020	SCOPE ELEVATORS	10	10	0	14JUN11	27JUN11	30SEP11	13OCT11	76
BA14240030	AWARD ELEVATORS	5	5	0	04AUG11	10AUG11	14OCT11	20OCT11	50
BA21050010	BID FIRE SPRINKLERS	1	1	0	13JUN11	13JUN11	17AUG11	17AUG11	46
BA21050020	SCOPE FIRE SPRINKLERS	10	10	0	14JUN11	27JUN11	18AUG11	31AUG11	46
BA21050030	AWARD FIRE SPRINKLERS	5	5	0	04AUG11	10AUG11	01SEP11	08SEP11	20
BA22050010	BID PLUMBING	1	1	0	13JUN11	13JUN11	27JUN11	27JUN11	10
BA22050020	SCOPE PLUMBING	10	10	0	14JUN11	27JUN11	28JUN11	12JUL11	10
BA22050030	AWARD PLUMBING	3	3	0	04AUG11	08AUG11	08AUG11	10AUG11	2
BA23051310	BID MECHANICAL	1	1	0	13JUN11	13JUN11	27JUL11	27JUL11	31
BA23051320	SCOPE MECHANICAL	10	10	0	14JUN11	27JUN11	28JUL11	10AUG11	31
BA23051330	AWARD MECHANICAL	3	3	0	04AUG11	08AUG11	11AUG11	15AUG11	5
BA23059310	BID T&B	1	1	0	13JUN11	13JUN11	23FEB12	23FEB12	177
BA23059320	SCOPE T&B	10	10	0	14JUN11	27JUN11	24FEB12	08MAR12	177
BA23059330	AWARD T&B	15	15	0	04AUG11	24AUG11	09MAR12	29MAR12	151
BA26050010	BID ELECTRICAL	1	1	0	13JUN11	13JUN11	27JUN11	27JUN11	10
BA26050020	SCOPE ELECTRICAL	10	10	0	14JUN11	27JUN11	28JUN11	12JUL11	10
BA26050030	AWARD ELECTRICAL	3	3	0	04AUG11	08AUG11	04AUG11	08AUG11	0
BA31100010	BID SITE	1	1	0	13JUN11	13JUN11	27JUN11	27JUN11	10
BA31100020	SCOPE SITE	10	10	0	14JUN11	27JUN11	28JUN11	12JUL11	10
BA31100030	AWARD SITE	1	1	0	04AUG11	04AUG11	04AUG11	04AUG11	0
BA31311610	BID TERMITE	1	1	0	13JUN11	13JUN11	27JUL11	27JUL11	31
BA31311620	SCOPE TERMITE	10	10	0	14JUN11	27JUN11	28JUL11	10AUG11	31
BA31311630	AWARD TERMITE	3	3	0	04AUG11	08AUG11	11AUG11	15AUG11	5
BA32311310	BID CHAIN LINK	1	1	0	13JUN11	13JUN11	16AUG11	16AUG11	45
BA32311320	SCOPE CHAIN LINK	10	10	0	14JUN11	27JUN11	17AUG11	30AUG11	45
BA32311330	AWARD CHAIN LINK	15	15	0	04AUG11	24AUG11	31AUG11	21SEP11	19
BA32311910	BID DECO FENCE	1	1	0	13JUN11	13JUN11	17FEB12	17FEB12	173
BA32311920	SCOPE DECO FENCE	10	10	0	14JUN11	27JUN11	20FEB12	02MAR12	173
BA32311930	AWARD DECO FENCE	15	15	0	04AUG11	24AUG11	05MAR12	23MAR12	147
BA32840010	BID LANDSCAPE	1	1	0	13JUN11	13JUN11	11AUG11	11AUG11	42
BA32840020	SCOPE LANDSCAPE	10	10	0	14JUN11	27JUN11	12AUG11	25AUG11	42
BA32840030	AWARD LANDSCAPE	15	15	0	04AUG11	24AUG11	26AUG11	16SEP11	16
PROCUREMENT									
ADMINISTRATION									
PR02141910	RECEIVE SELECTIVE DEMO	10	10	0	11AUG11	24AUG11	23AUG11	06SEP11	8

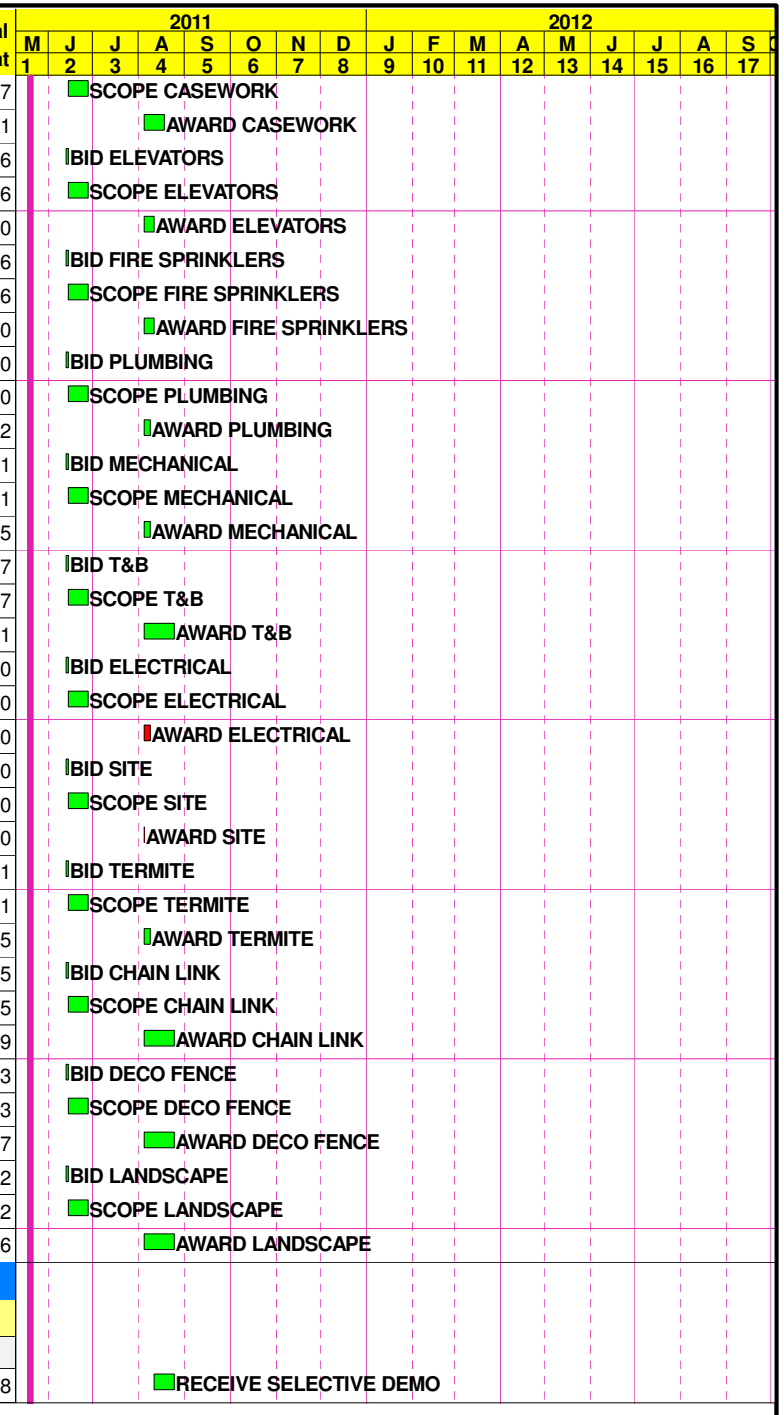

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

Sheet 6 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR02141920	DOSTER REVIEW SELECTIVE DEMO	5	5	0	25AUG11	31AUG11	07SEP11	13SEP11	8
PR02141930	A&E APPROVE SELECTIVE DEMO	10	10	0	01SEP11	15SEP11	14SEP11	27SEP11	8
PR02141940	BCCO APPROVE SELECTIVE DEMO	5	5	0	16SEP11	22SEP11	28SEP11	04OCT11	8
PR02141950	FAB SELECTIVE DEMO	5	5	0	23SEP11	29SEP11	05OCT11	11OCT11	8
PR02141960	DELIVER SELECTIVE DEMO	1	1	0	30SEP11	30SEP11	12OCT11	12OCT11	8
PR0330010	RECEIVE CONCRETE	10	10	0	11AUG11	24AUG11	15AUG11	26AUG11	2
PR0330020	DOSTER REVIEW CONCRETE	5	5	0	25AUG11	31AUG11	29AUG11	02SEP11	2
PR0330030	A&E APPROVE CONCRETE	10	10	0	01SEP11	15SEP11	06SEP11	19SEP11	2
PR0330040	BCCO APPROVE CONCRETE	5	5	0	16SEP11	22SEP11	20SEP11	26SEP11	2
PR0330050	FAB CONCRETE	5	5	0	23SEP11	29SEP11	27SEP11	03OCT11	2
PR0330060	DELIVER CONCRETE	1	1	0	30SEP11	30SEP11	04OCT11	04OCT11	2
PR03450010	RECEIVE PRECAST ARCH	10	10	0	11AUG11	24AUG11	16FEB12	29FEB12	130
PR03450020	DOSTER REVIEW PRECAST ARCH	5	5	0	25AUG11	31AUG11	01MAR12	07MAR12	130
PR03450030	A&E APPROVE PRECAST ARCH	10	10	0	01SEP11	15SEP11	08MAR12	21MAR12	130
PR03450040	BCCO APPROVE PRECAST ARCH	5	5	0	16SEP11	22SEP11	22MAR12	28MAR12	130
PR03450050	FAB PRECAST ARCH CONCRETE	40	40	0	23SEP11	17NOV11	29MAR12	23MAY12	130
PR03450060	DELIVER PRECAST ARCH	1	1	0	18NOV11	18NOV11	24MAY12	24MAY12	130
PR03471310	RECEIVE TILT CONCRETE	10	10	0	05AUG11	18AUG11	15SEP11	28SEP11	28
PR03471320	DOSTER REVIEW TILT CONCRETE	5	5	0	19AUG11	25AUG11	29SEP11	05OCT11	28
PR03471330	A&E APPROVE TILT CONCRETE	10	10	0	26AUG11	09SEP11	06OCT11	19OCT11	28
PR03471340	BCCO APPROVE TILT CONCRETE	5	5	0	12SEP11	16SEP11	20OCT11	26OCT11	28
PR03471350	FAB TILT CONCRETE	30	30	0	19SEP11	28OCT11	27OCT11	09DEC11	28
PR03471360	DELIVER TILT CONCRETE	1	1	0	31OCT11	31OCT11	12DEC11	12DEC11	28
PR03521610	RECEIVE LT WT ROOF CONCRETE	10	10	0	11AUG11	24AUG11	20JAN12	02FEB12	111
PR03521620	DOSTER REVIEW LT WT ROOF	5	5	0	25AUG11	31AUG11	03FEB12	09FEB12	111
PR03521630	A&E APPROVE LT WT ROOF	10	10	0	01SEP11	15SEP11	10FEB12	23FEB12	111
PR03521640	BCCO APPROVE LT WT ROOF	5	5	0	16SEP11	22SEP11	24FEB12	01MAR12	111
PR03521650	FAB LT WT ROOF CONCRETE	10	10	0	23SEP11	06OCT11	02MAR12	15MAR12	111
PR03521660	DELIVER LT WT ROOF CONCRETE	1	1	0	07OCT11	07OCT11	16MAR12	16MAR12	111
PR03541610	RECEIVE UNDERLAYMENT	10	10	0	18AUG11	31AUG11	29MAR12	11APR12	155
PR03541620	DOSTER REVIEW UNDERLAYMENT	5	5	0	01SEP11	08SEP11	12APR12	18APR12	155
PR03541630	A&E APPROVE UNDERLAYMENT	10	10	0	09SEP11	22SEP11	19APR12	02MAY12	155
PR03541640	BCCO APPROVE UNDERLAYMENT	5	5	0	23SEP11	29SEP11	03MAY12	09MAY12	155
PR03541650	FAB LT UNDERLAYMENT CONCRETE	5	5	0	30SEP11	06OCT11	10MAY12	16MAY12	155
PR03541660	DELIVER UNDERLAYMENT	1	1	0	07OCT11	07OCT11	17MAY12	17MAY12	155
PR04200010	RECEIVE UNIT MASONRY	10	10	0	11AUG11	24AUG11	27SEP11	10OCT11	32
PR04200020	DOSTER REVIEW UNIT MASONRY	5	5	0	25AUG11	31AUG11	11OCT11	17OCT11	32
PR04200030	A&E APPROVE UNIT MASONRY	10	10	0	01SEP11	15SEP11	18OCT11	31OCT11	32
PR04200040	BCCO APPROVE UNIT MASONRY	5	5	0	16SEP11	22SEP11	01NOV11	07NOV11	32

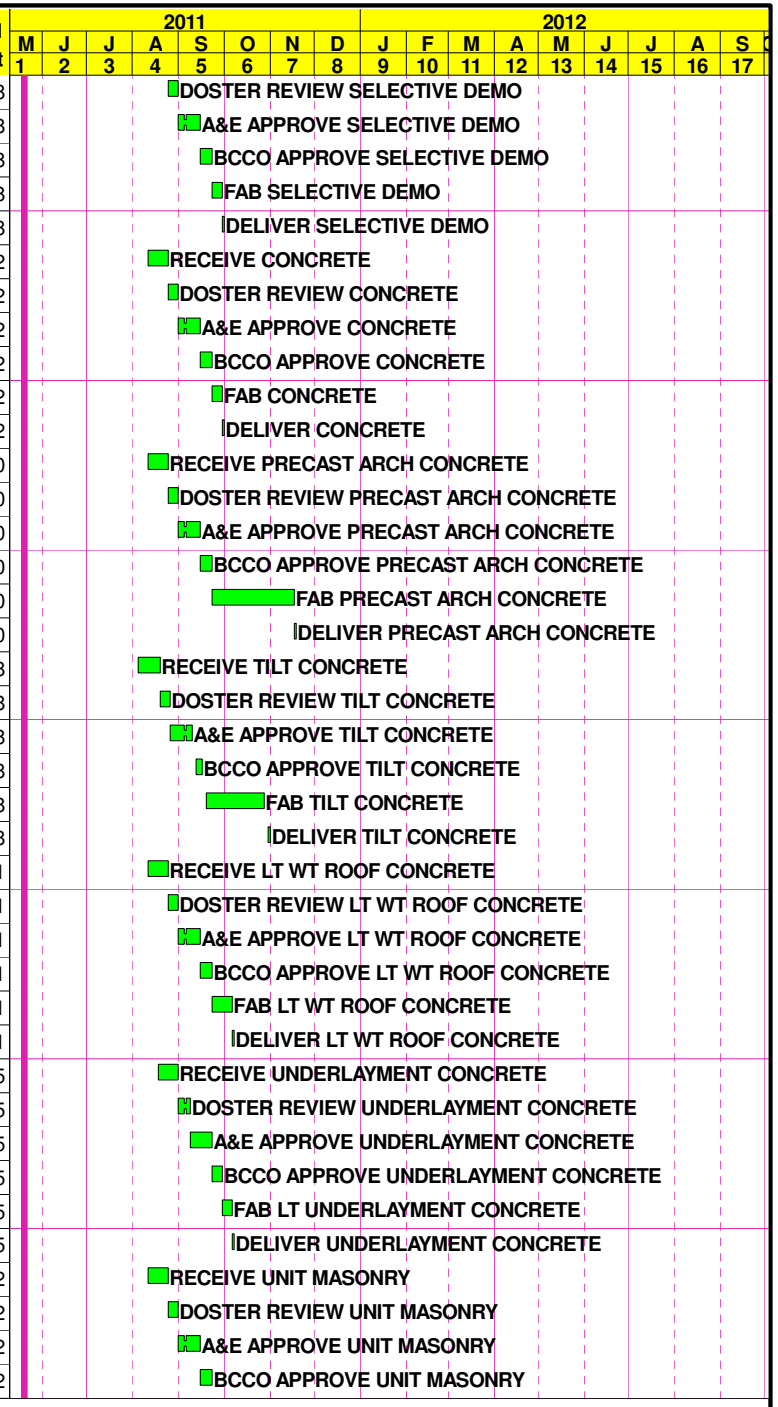

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR04200050	FAB LT UNIT MASONRY	20	20	0	23SEP11	20OCT11	08NOV11	07DEC11	32
PR04200060	DELIVER UNIT MASONRY	1	1	0	21OCT11	21OCT11	08DEC11	08DEC11	32
PR04211310	RECEIVE BRICK VENEER MASONRY	10	10	0	05AUG11	18AUG11	22SEP11	05OCT11	33
PR04211320	DOSTER REVIEW BRICK VENEER	5	5	0	19AUG11	25AUG11	06OCT11	12OCT11	33
PR04211330	A&E APPROVE BRICK VENEER	10	10	0	26AUG11	09SEP11	13OCT11	26OCT11	33
PR04211340	BCCO APPROVE BRICK VENEER	5	5	0	12SEP11	16SEP11	27OCT11	02NOV11	33
PR04211350	FAB BRICK VENEER MASONRY	10	10	0	19SEP11	30SEP11	03NOV11	16NOV11	33
PR04211360	DELIVER BRICK VENEER MASONRY	1	1	0	03OCT11	03OCT11	17NOV11	17NOV11	33
PR05120010	RECEIVE STRUCTURAL STEEL	10	10	0	09AUG11	22AUG11	01SEP11	15SEP11	17
PR05120020	DOSTER REVIEW STRUCTURAL	5	5	0	23AUG11	29AUG11	16SEP11	22SEP11	17
PR05120030	A&E APPROVE STRUCTURAL STEEL	10	10	0	30AUG11	13SEP11	23SEP11	06OCT11	17
PR05120040	BCCO APPROVE STRUCTURAL	5	5	0	14SEP11	20SEP11	07OCT11	13OCT11	17
PR05120050	FAB STRUCTURAL STEEL	50	50	0	21SEP11	01DEC11	14OCT11	27DEC11	17
PR05120060	DELIVER STRUCTURAL STEEL	1	1	0	02DEC11	02DEC11	28DEC11	28DEC11	17
PR05210010	RECEIVE JOIST	10	10	0	09AUG11	22AUG11	12OCT11	25OCT11	45
PR05210020	DOSTER REVIEW JOIST	5	5	0	23AUG11	29AUG11	26OCT11	01NOV11	45
PR05210030	A&E APPROVE JOIST	10	10	0	30AUG11	13SEP11	02NOV11	15NOV11	45
PR05210040	BCCO APPROVE JOIST	5	5	0	14SEP11	20SEP11	16NOV11	22NOV11	45
PR05210050	FAB JOIST	30	30	0	21SEP11	01NOV11	23NOV11	09JAN12	45
PR05210060	DELIVER JOIST	1	1	0	02NOV11	02NOV11	10JAN12	10JAN12	45
PR05310010	RECEIVE DECKING	10	10	0	09AUG11	22AUG11	31OCT11	11NOV11	58
PR05310020	DOSTER REVIEW DECKING	5	5	0	23AUG11	29AUG11	14NOV11	18NOV11	58
PR05310030	A&E APPROVE DECKING	10	10	0	30AUG11	13SEP11	21NOV11	06DEC11	58
PR05310040	BCCO APPROVE DECKING	5	5	0	14SEP11	20SEP11	07DEC11	13DEC11	58
PR05310050	FAB DECKING	30	30	0	21SEP11	01NOV11	14DEC11	26JAN12	58
PR05310060	DELIVER DECKING	1	1	0	02NOV11	02NOV11	27JAN12	27JAN12	58
PR05400010	RECEIVE COLD FORM METAL FRAME	10	10	0	11AUG11	24AUG11	12OCT11	25OCT11	43
PR05400020	DOSTER REVIEW COLD FORM	5	5	0	25AUG11	31AUG11	26OCT11	01NOV11	43
PR05400030	A&E APPROVE COLD FORM METAL	10	10	0	01SEP11	15SEP11	02NOV11	15NOV11	43
PR05400040	BCCO APPROVE COLD FORM METAL	5	5	0	16SEP11	22SEP11	16NOV11	22NOV11	43
PR05400050	FAB COLD FORM METAL FRAME	30	30	0	23SEP11	03NOV11	23NOV11	09JAN12	43
PR05400060	DELIVER COLD FORM METAL FRAME	1	1	0	04NOV11	04NOV11	10JAN12	10JAN12	43
PR05500010	RECEIVE METAL FABRICATIONS	10	10	0	09AUG11	22AUG11	02NOV11	15NOV11	60
PR05500020	DOSTER REVIEW METAL	5	5	0	23AUG11	29AUG11	16NOV11	22NOV11	60
PR05500030	A&E APPROVE METAL	10	10	0	30AUG11	13SEP11	23NOV11	08DEC11	60
PR05500040	BCCO APPROVE METAL	5	5	0	14SEP11	20SEP11	09DEC11	15DEC11	60
PR05500050	FAB METAL FABRICATIONS	15	15	0	21SEP11	11OCT11	16DEC11	09JAN12	60
PR05500060	DELIVER METAL FABRICATIONS	1	1	0	12OCT11	12OCT11	10JAN12	10JAN12	60
PR05510010	RECEIVE METAL STAIRS	10	10	0	09AUG11	22AUG11	16NOV11	01DEC11	70

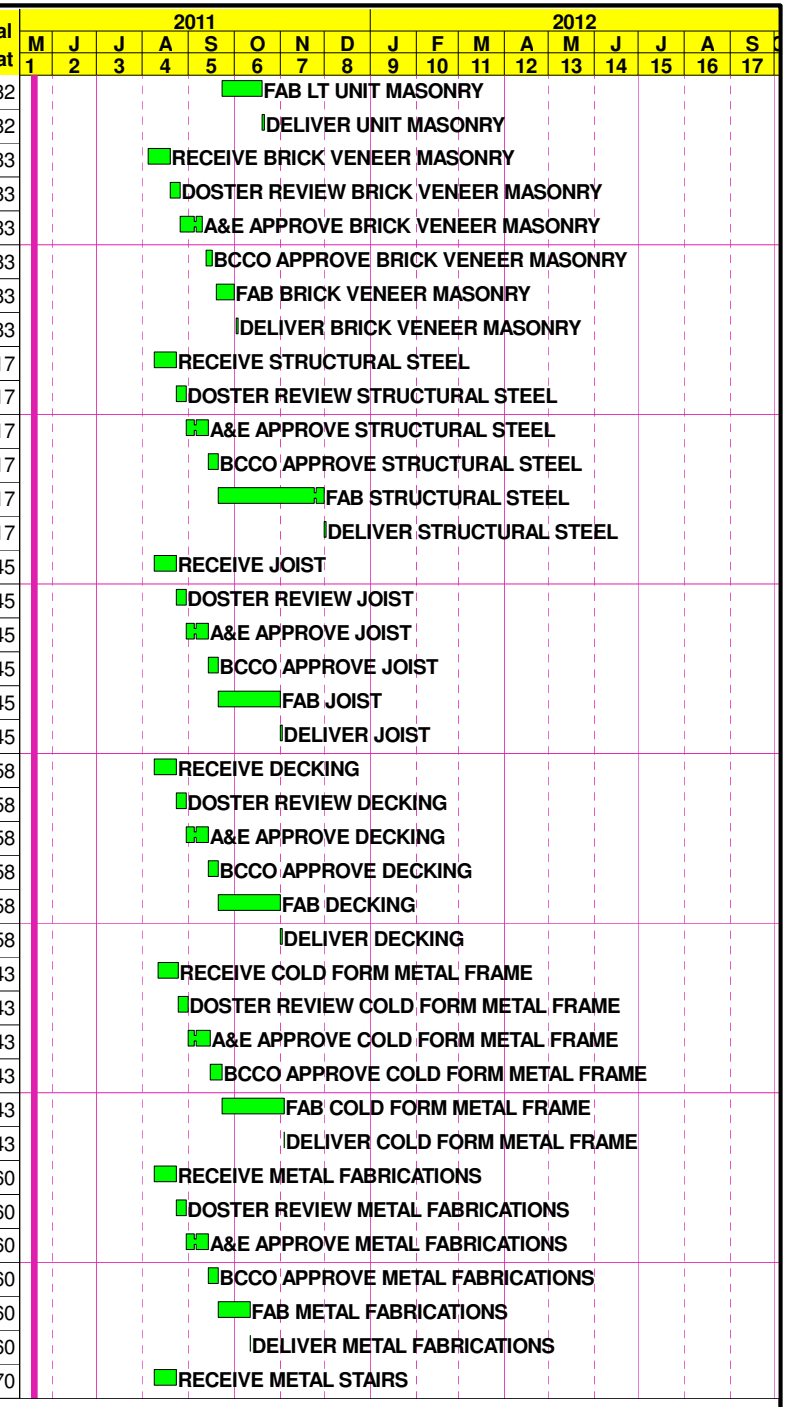

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR05510020	DOSTER REVIEW METAL STAIRS	5	5	0	23AUG11	29AUG11	02DEC11	08DEC11	70
PR05510030	A&E APPROVE METAL STAIRS	10	10	0	30AUG11	13SEP11	09DEC11	22DEC11	70
PR05510040	BCCO APPROVE METAL STAIRS	5	5	0	14SEP11	20SEP11	23DEC11	30DEC11	70
PR05510050	FAB METAL STAIRS	40	40	0	21SEP11	15NOV11	03JAN12	27FEB12	70
PR05510060	DELIVER METAL STAIRS	1	1	0	16NOV11	16NOV11	28FEB12	28FEB12	70
PR05730010	RECEIVE DECO RAILS	10	10	0	18AUG11	31AUG11	12MAR12	23MAR12	142
PR05730020	DOSTER REVIEW DECO RAILS	5	5	0	01SEP11	08SEP11	26MAR12	30MAR12	142
PR05730030	A&E APPROVE DECO RAILS	10	10	0	09SEP11	22SEP11	02APR12	13APR12	142
PR05730040	BCCO APPROVE DECO RAILS	5	5	0	23SEP11	29SEP11	16APR12	20APR12	142
PR05730050	FAB DECO RAILS	30	30	0	30SEP11	10NOV11	23APR12	04JUN12	142
PR05730060	DELIVER DECO RAILS	1	1	0	11NOV11	11NOV11	05JUN12	05JUN12	142
PR06100010	RECEIVE ROUGH CARPENTRY	10	10	0	18AUG11	31AUG11	31AUG11	14SEP11	9
PR06100020	DOSTER REVIEW ROUGH	5	5	0	01SEP11	08SEP11	15SEP11	21SEP11	9
PR06100030	A&E APPROVE ROUGH CARPENTRY	10	10	0	09SEP11	22SEP11	22SEP11	05OCT11	9
PR06100040	BCCO APPROVE ROUGH	5	5	0	23SEP11	29SEP11	06OCT11	12OCT11	9
PR06100050	FAB ROUGH CARPENTRY	5	5	0	30SEP11	06OCT11	13OCT11	19OCT11	9
PR06100060	DELIVER ROUGH CARPENTRY	1	1	0	07OCT11	07OCT11	20OCT11	20OCT11	9
PR06160010	RECEIVE SHEATHING	10	10	0	18AUG11	31AUG11	30DEC11	13JAN12	92
PR06160020	DOSTER REVIEW SHEATHING	5	5	0	01SEP11	08SEP11	16JAN12	20JAN12	92
PR06160030	A&E APPROVE SHEATHING	10	10	0	09SEP11	22SEP11	23JAN12	03FEB12	92
PR06160040	BCCO APPROVE SHEATHING	5	5	0	23SEP11	29SEP11	06FEB12	10FEB12	92
PR06160050	FAB SHEATHING	5	5	0	30SEP11	06OCT11	13FEB12	17FEB12	92
PR06160060	DELIVER SHEATHING	1	1	0	07OCT11	07OCT11	20FEB12	20FEB12	92
PR06402310	RECEIVE INT ARCH WOODWORK	10	10	0	18AUG11	31AUG11	05JAN12	18JAN12	95
PR06402320	DOSTER REVIEW INT ARCH	5	5	0	01SEP11	08SEP11	19JAN12	25JAN12	95
PR06402330	A&E APPROVE INT ARCH	10	10	0	09SEP11	22SEP11	26JAN12	08FEB12	95
PR06402340	BCCO APPROVE INTARCH	5	5	0	23SEP11	29SEP11	09FEB12	15FEB12	95
PR06402350	FAB INT ARCH WOODWORK	60	60	0	30SEP11	27DEC11	16FEB12	09MAY12	95
PR06402360	DELIVER INT ARCH WOODWORK	1	1	0	28DEC11	28DEC11	10MAY12	10MAY12	95
PR07015010	RECEIVE PREP FOR RE-ROOF	10	10	0	18AUG11	31AUG11	22DEC11	06JAN12	87
PR07015020	DOSTER REVIEW PREP FOR	5	5	0	01SEP11	08SEP11	09JAN12	13JAN12	87
PR07015030	A&E APPROVE PREP FOR RE-ROOF	10	10	0	09SEP11	22SEP11	16JAN12	27JAN12	87
PR07015040	BCCO APPROVE PREP FOR	5	5	0	23SEP11	29SEP11	30JAN12	03FEB12	87
PR07015050	FAB PREP FOR RE-ROOF	10	10	0	30SEP11	13OCT11	06FEB12	17FEB12	87
PR07015060	DELIVER PREP FOR RE- ROOF	1	1	0	14OCT11	14OCT11	20FEB12	20FEB12	87
PR07141610	RECEIVE WP ABOVE GRADE	10	10	0	11AUG11	24AUG11	07SEP11	20SEP11	18
PR07141620	DOSTER REVIEW WP ABOVE GRADE	5	5	0	25AUG11	31AUG11	21SEP11	27SEP11	18
PR07141630	A&E APPROVE WP ABOVE GRADE	10	10	0	01SEP11	15SEP11	28SEP11	11OCT11	18
PR07141640	BCCO APPROVE WP ABOVE GRADE	5	5	0	16SEP11	22SEP11	12OCT11	18OCT11	18

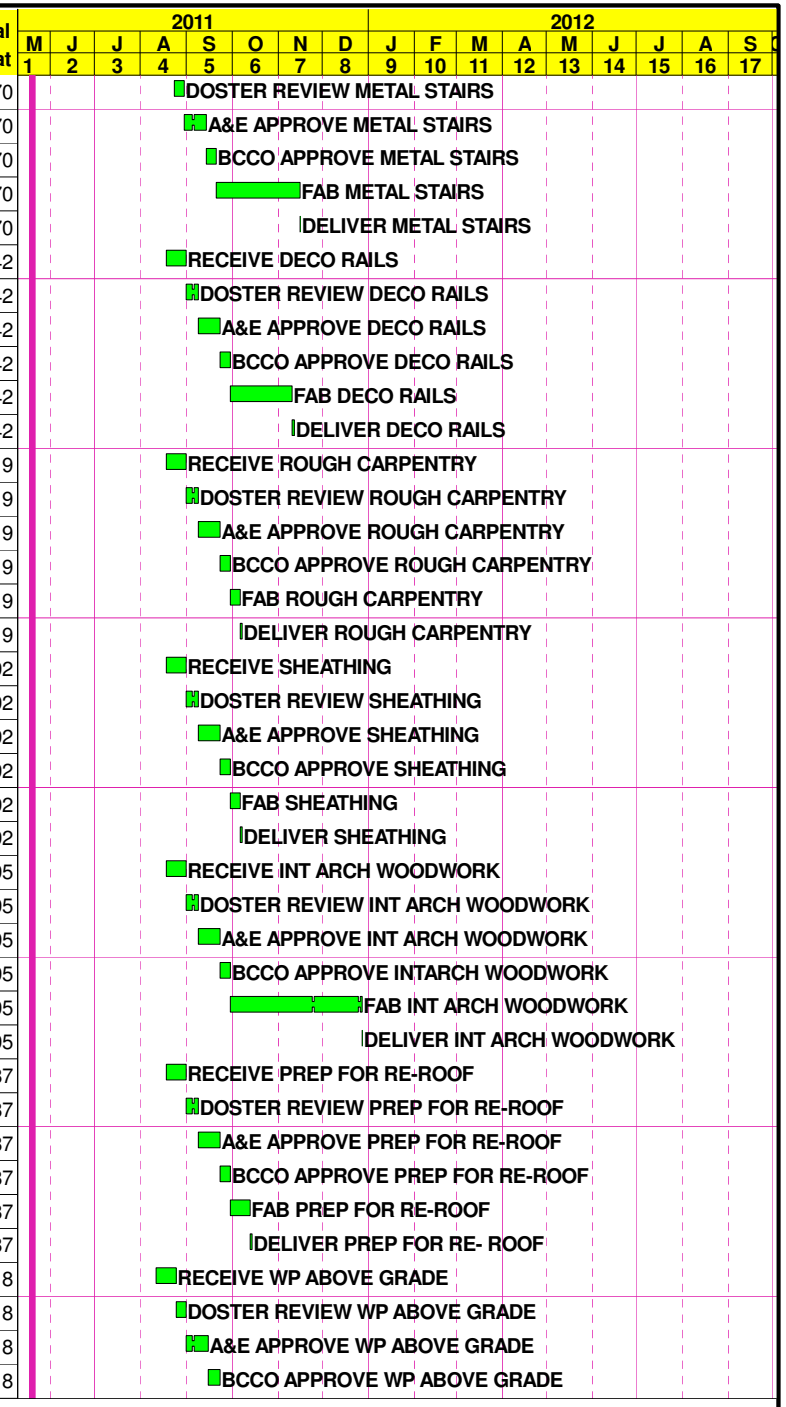

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR07141650	FAB WP ABOVE GRADE	10	10	0	23SEP11	06OCT11	19OCT11	01NOV11	18
PR07141660	DELIVER WP ABOVE GRADE	1	1	0	07OCT11	07OCT11	02NOV11	02NOV11	18
PR07141810	RECEIVE WP BELOW GRADE	10	10	0	11AUG11	24AUG11	22AUG11	02SEP11	7
PR07141820	DOSTER REVIEW WP BELOW GRADE	5	5	0	25AUG11	31AUG11	06SEP11	12SEP11	7
PR07141830	A&E APPROVE WP BELOW GRADE	10	10	0	01SEP11	15SEP11	13SEP11	26SEP11	7
PR07141840	BCCO APPROVE WP BELOW GRADE	5	5	0	16SEP11	22SEP11	27SEP11	03OCT11	7
PR07141850	FAB WP BELOW GRADE	5	5	0	23SEP11	29SEP11	04OCT11	10OCT11	7
PR07141860	DELIVER WP BELOW GRADE	1	1	0	30SEP11	30SEP11	11OCT11	11OCT11	7
PR07171610	RECEIVE BENTONITE	10	10	0	11AUG11	24AUG11	23AUG11	06SEP11	8
PR07171620	DOSTER REVIEW BENTONITE	5	5	0	25AUG11	31AUG11	07SEP11	13SEP11	8
PR07171630	A&E APPROVE BENTONITE	10	10	0	01SEP11	15SEP11	14SEP11	27SEP11	8
PR07171640	BCCO APPROVE BENTONITE	5	5	0	16SEP11	22SEP11	28SEP11	04OCT11	8
PR07171650	FAB BENTONITE	5	5	0	23SEP11	29SEP11	05OCT11	11OCT11	8
PR07171660	DELIVER BENTONITE	1	1	0	03OCT11	03OCT11	12OCT11	12OCT11	7
PR07210010	RECEIVE THERMAL INSULATION	10	10	0	25AUG11	08SEP11	05JAN12	18JAN12	90
PR07210020	DOSTER REVIEW THERMAL	5	5	0	09SEP11	15SEP11	19JAN12	25JAN12	90
PR07210030	A&E APPROVE THERMAL	10	10	0	16SEP11	29SEP11	26JAN12	08FEB12	90
PR07210040	BCCO APPROVE THERMAL	5	5	0	30SEP11	06OCT11	09FEB12	15FEB12	90
PR07210050	FAB THERMAL INSULATION	10	10	0	07OCT11	20OCT11	16FEB12	29FEB12	90
PR07210060	DELIVER THERMAL INSULATION	1	1	0	21OCT11	21OCT11	01MAR12	01MAR12	90
PR07211010	RECEIVE FOAM INSULATION	10	10	0	11AUG11	24AUG11	05MAR12	16MAR12	142
PR07211020	DOSTER REVIEW FOAM INSULATION	5	5	0	25AUG11	31AUG11	19MAR12	23MAR12	142
PR07211030	A&E APPROVE FOAM INSULATION	10	10	0	01SEP11	15SEP11	26MAR12	06APR12	142
PR07211040	BCCO APPROVE FOAM INSULATION	5	5	0	16SEP11	22SEP11	09APR12	13APR12	142
PR07211050	FAB FOAM INSULATION	10	10	0	23SEP11	06OCT11	16APR12	27APR12	142
PR07211060	DELIVER FOAM INSULATION	1	1	0	07OCT11	07OCT11	30APR12	30APR12	142
PR07321310	RECEIVE CLAY TILE	10	10	0	18AUG11	31AUG11	08NOV11	21NOV11	57
PR07321320	DOSTER REVIEW CLAY TILE	5	5	0	01SEP11	08SEP11	22NOV11	30NOV11	57
PR07321330	A&E APPROVE CLAY TILE	10	10	0	09SEP11	22SEP11	01DEC11	14DEC11	57
PR07321340	BCCO APPROVE CLAY TILE	5	5	0	23SEP11	29SEP11	15DEC11	21DEC11	57
PR07321350	FAB CLAY TILE	40	40	0	30SEP11	28NOV11	22DEC11	17FEB12	57
PR07321360	DELIVER CLAY TILE	1	1	0	29NOV11	29NOV11	20FEB12	20FEB12	57
PR07540010	RECEIVE MEMBRANE ROOFING	10	10	0	18AUG11	31AUG11	23JAN12	03FEB12	107
PR07540020	DOSTER REVIEW MEMBRANE	5	5	0	01SEP11	08SEP11	06FEB12	10FEB12	107
PR07540030	A&E APPROVE MEMBRANE ROOFING	10	10	0	09SEP11	22SEP11	13FEB12	24FEB12	107
PR07540040	BCCO APPROVE MEMBRANE	5	5	0	23SEP11	29SEP11	27FEB12	02MAR12	107
PR07540050	FAB MEMBRANE ROOFING	10	10	0	30SEP11	13OCT11	05MAR12	16MAR12	107
PR07540060	DELIVER MEMBRANE ROOFING	1	1	0	14OCT11	14OCT11	19MAR12	19MAR12	107
PR07620010	RECEIVE METAL FLASHING	10	10	0	18AUG11	31AUG11	11JAN12	24JAN12	99

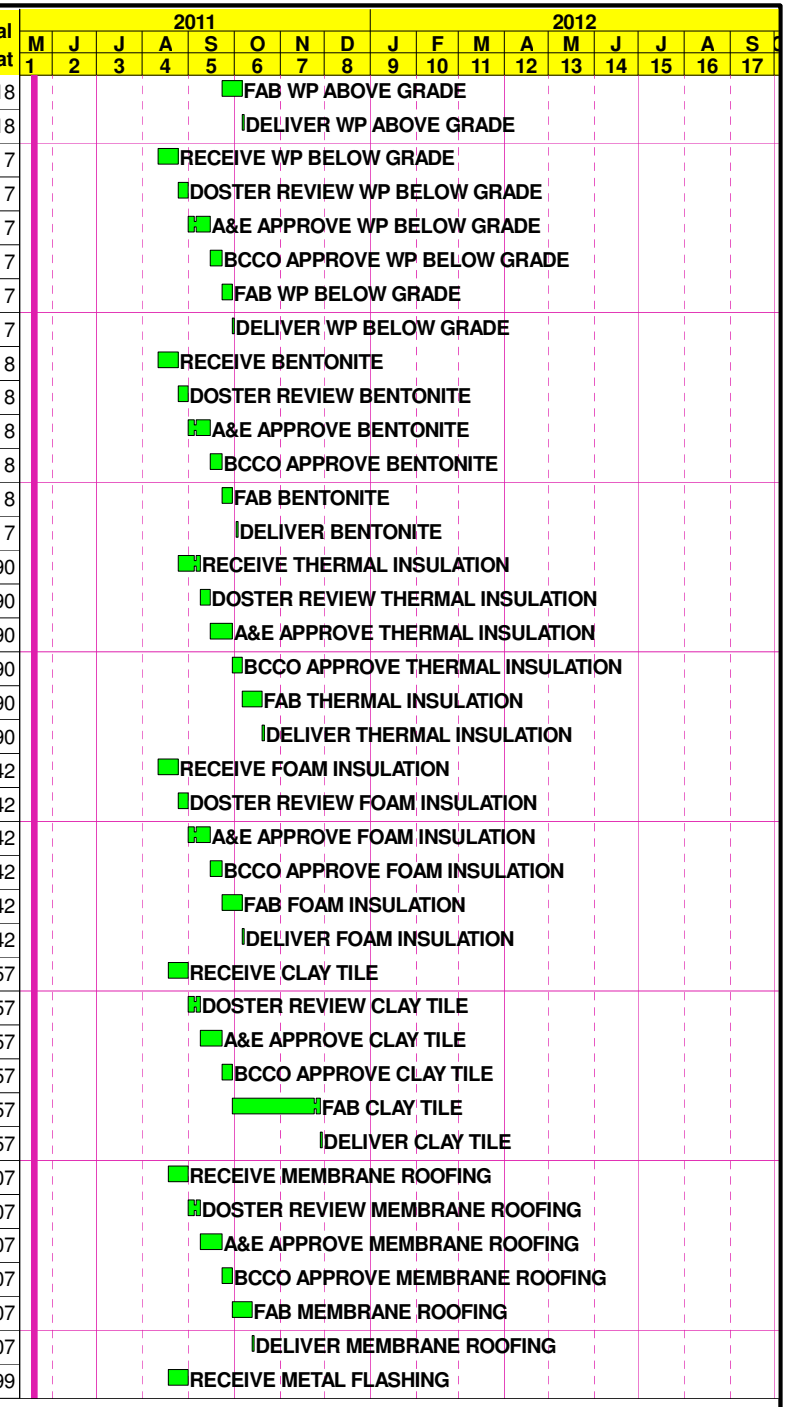

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

Sheet 10 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR07620020	DOSTER REVIEW METAL FLASHING	5	5	0	01SEP11	08SEP11	25JAN12	31JAN12	99
PR07620030	A&E APPROVE METAL FLASHING	10	10	0	09SEP11	22SEP11	01FEB12	14FEB12	99
PR07620040	BCCO APPROVE METAL FLASHING	5	5	0	23SEP11	29SEP11	15FEB12	21FEB12	99
PR07620050	FAB METAL FLASHING	10	10	0	30SEP11	13OCT11	22FEB12	06MAR12	99
PR07620060	DELIVER METAL FLASHING	1	1	0	14OCT11	14OCT11	07MAR12	07MAR12	99
PR07710010	RECEIVE ROOF SPECIALTIES	10	10	0	18AUG11	31AUG11	04JAN12	17JAN12	94
PR07710020	DOSTER REVIEW ROOF	5	5	0	01SEP11	08SEP11	18JAN12	24JAN12	94
PR07710030	A&E APPROVE ROOF SPECIALTIES	10	10	0	09SEP11	22SEP11	25JAN12	07FEB12	94
PR07710040	BCCO APPROVE ROOF SPECIALTIES	5	5	0	23SEP11	29SEP11	08FEB12	14FEB12	94
PR07710050	FAB ROOF SPECIALTIES	15	15	0	30SEP11	20OCT11	15FEB12	06MAR12	94
PR07710060	DELIVER ROOF SPECIALTIES	1	1	0	21OCT11	21OCT11	07MAR12	07MAR12	94
PR07723310	RECEIVE ROOF HATCHES	10	10	0	25AUG11	08SEP11	09DEC11	22DEC11	73
PR07723320	DOSTER REVIEW ROOF HATCHES	5	5	0	09SEP11	15SEP11	23DEC11	30DEC11	73
PR07723330	A&E APPROVE ROOF HATCHES	10	10	0	16SEP11	29SEP11	03JAN12	16JAN12	73
PR07723340	BCCO APPROVE ROOF HATCHES	5	5	0	30SEP11	06OCT11	17JAN12	23JAN12	73
PR07723350	FAB ROOF HATCHES	30	30	0	07OCT11	17NOV11	24JAN12	05MAR12	73
PR07723360	DELIVER ROOF HATCHES	1	1	0	18NOV11	18NOV11	06MAR12	06MAR12	73
PR07810010	RECEIVE APPLIED FIREPROOFING	10	10	0	11AUG11	24AUG11	05JAN12	18JAN12	100
PR07810020	DOSTER REVIEW APPLIED	5	5	0	25AUG11	31AUG11	19JAN12	25JAN12	100
PR07810030	A&E APPROVE APPLIED	10	10	0	01SEP11	15SEP11	26JAN12	08FEB12	100
PR07810040	BCCO APPROVE APPLIED	5	5	0	16SEP11	22SEP11	09FEB12	15FEB12	100
PR07810050	FAB APPLIED FIREPROOFING	10	10	0	23SEP11	06OCT11	16FEB12	29FEB12	100
PR07810060	DELIVER APPLIED FIREPROOFING	1	1	0	07OCT11	07OCT11	01MAR12	01MAR12	100
PR07840010	RECEIVE FIRE STOPPING	10	10	0	11AUG11	24AUG11	06JAN12	19JAN12	101
PR07840020	DOSTER REVIEW FIRE STOPPING	5	5	0	25AUG11	31AUG11	20JAN12	26JAN12	101
PR07840030	A&E APPROVE FIRE STOPPING	10	10	0	01SEP11	15SEP11	27JAN12	09FEB12	101
PR07840040	BCCO APPROVE FIRE STOPPING	5	5	0	16SEP11	22SEP11	10FEB12	16FEB12	101
PR07840050	FAB FIRE STOPPING	15	15	0	23SEP11	13OCT11	17FEB12	08MAR12	101
PR07840060	DELIVER FIRE STOPPING	1	1	0	14OCT11	14OCT11	09MAR12	09MAR12	101
PR07920010	RECEIVE JOINT SEALANTS	10	10	0	11AUG11	24AUG11	28OCT11	10NOV11	55
PR07920020	DOSTER REVIEW JOINT SEALANTS	5	5	0	25AUG11	31AUG11	11NOV11	17NOV11	55
PR07920030	A&E APPROVE JOINT SEALANTS	10	10	0	01SEP11	15SEP11	18NOV11	05DEC11	55
PR07920040	BCCO APPROVE JOINT SEALANTS	5	5	0	16SEP11	22SEP11	06DEC11	12DEC11	55
PR07920050	FAB JOINT SEALANTS	10	10	0	23SEP11	06OCT11	13DEC11	27DEC11	55
PR07920060	DELIVER JOINT SEALANTS	1	1	0	07OCT11	07OCT11	28DEC11	28DEC11	55
PR07950010	RECEIVE EXP JOINTS	10	10	0	11AUG11	24AUG11	14OCT11	27OCT11	45
PR07950020	DOSTER REVIEW EXP JOINTS	5	5	0	25AUG11	31AUG11	28OCT11	03NOV11	45
PR07950030	A&E APPROVE EXP JOINTS	10	10	0	01SEP11	15SEP11	04NOV11	17NOV11	45
PR07950040	BCCO APPROVE EXP JOINTS	5	5	0	16SEP11	22SEP11	18NOV11	28NOV11	45

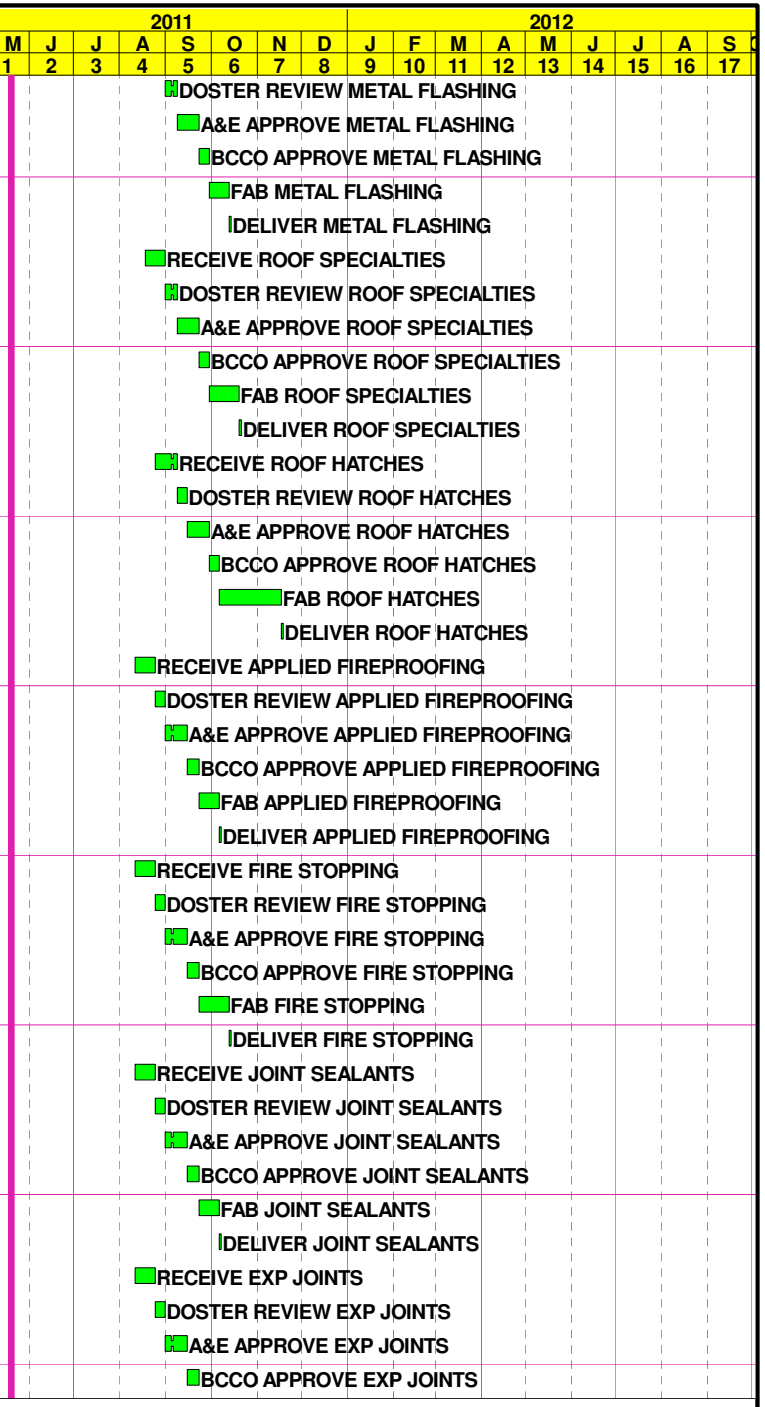

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

Sheet 11 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR07950050	FAB EXP JOINTS	20	20	0	23SEP11	20OCT11	29NOV11	27DEC11	45
PR07950060	DELIVER EXP JOINTS	1	1	0	21OCT11	21OCT11	28DEC11	28DEC11	45
PR08111310	RECEIVE HOLLOW METAL DOOR	10	10	0	11AUG11	24AUG11	24AUG11	07SEP11	9
PR08111320	DOSTER REVIEW HOLLOW METAL	5	5	0	25AUG11	31AUG11	08SEP11	14SEP11	9
PR08111330	A&E APPROVE HALLOW METAL	10	10	0	01SEP11	15SEP11	15SEP11	28SEP11	9
PR08111340	BCCO APPROVE HOLLOW METAL	5	5	0	16SEP11	22SEP11	29SEP11	05OCT11	9
PR08111350	FAB HOLLOW METAL DOOR AND	30	30	0	23SEP11	03NOV11	06OCT11	16NOV11	9
PR08111360	DELIVER HOLLOW METAL DOOR	1	1	0	04NOV11	04NOV11	17NOV11	17NOV11	9
PR08141610	RECEIVE WOOD DOORS	10	10	0	11AUG11	24AUG11	26JAN12	08FEB12	115
PR08141620	DOSTER REVIEW WOOD DOORS	5	5	0	25AUG11	31AUG11	09FEB12	15FEB12	115
PR08141630	A&E APPROVE WOOD DOORS	10	10	0	01SEP11	15SEP11	16FEB12	29FEB12	115
PR08141640	BCCO APPROVE WOOD DOORS	5	5	0	16SEP11	22SEP11	01MAR12	07MAR12	115
PR08141650	FAB WOOD DOORS	60	60	0	23SEP11	19DEC11	08MAR12	31MAY12	115
PR08141660	DELIVER WOOD DOORS	1	1	0	20DEC11	20DEC11	01JUN12	01JUN12	115
PR08311310	RECEIVE ACCESS DOORS	10	10	0	09AUG11	22AUG11	29DEC11	12JAN12	98
PR08311320	DOSTER REVIEW ACCESS DOORS	5	5	0	23AUG11	29AUG11	13JAN12	19JAN12	98
PR08311330	A&E APPROVE ACCESS DOORS	10	10	0	30AUG11	13SEP11	20JAN12	02FEB12	98
PR08311340	BCCO APPROVE ACCESS DOORS	5	5	0	14SEP11	20SEP11	03FEB12	09FEB12	98
PR08311350	FAB ACCESS DOORS	10	10	0	21SEP11	04OCT11	10FEB12	23FEB12	98
PR08311360	DELIVER ACCESS DOORS	5	5	0	05OCT11	11OCT11	24FEB12	01MAR12	98
PR08411310	RECEIVE STORE FRONTS	10	10	0	11AUG11	24AUG11	04NOV11	17NOV11	60
PR08411320	DOSTER REVIEW STORE FRONTS	5	5	0	25AUG11	31AUG11	18NOV11	28NOV11	60
PR08411330	A&E APPROVE STORE FRONTS	10	10	0	01SEP11	15SEP11	29NOV11	12DEC11	60
PR08411340	BCCO APPROVE STORE FRONTS	5	5	0	16SEP11	22SEP11	13DEC11	19DEC11	60
PR08411350	FAB STORE FRONTS	50	50	0	23SEP11	05DEC11	20DEC11	29FEB12	60
PR08411360	DELIVER STORE FRONTS	1	1	0	06DEC11	06DEC11	01MAR12	01MAR12	60
PR08511310	RECEIVE ALUM WINDOWS	10	10	0	11AUG11	24AUG11	07SEP11	20SEP11	18
PR08511320	DOSTER REVIEW ALUM WINDOWS	5	5	0	25AUG11	31AUG11	21SEP11	27SEP11	18
PR08511330	A&E APPROVE ALUM WINDOWS	10	10	0	01SEP11	15SEP11	28SEP11	11OCT11	18
PR08511340	BCCO APPROVE ALUM WINDOWS	5	5	0	16SEP11	22SEP11	12OCT11	18OCT11	18
PR08511350	FAB ALUM WINDOWS	50	50	0	23SEP11	05DEC11	19OCT11	30DEC11	18
PR08511360	DELIVER ALUM WINDOWS	1	1	0	06DEC11	06DEC11	03JAN12	03JAN12	18
PR08711110	RECEIVE DOOR HDWR	10	10	0	11AUG11	24AUG11	23FEB12	07MAR12	135
PR08711120	DOSTER REVIEW DOOR HRWR	5	5	0	25AUG11	31AUG11	08MAR12	14MAR12	135
PR08711130	A&E APPROVE DOOR HDWR	10	10	0	01SEP11	15SEP11	15MAR12	28MAR12	135
PR08711140	BCCO APPROVE DOOR HDWR	5	5	0	16SEP11	22SEP11	29MAR12	04APR12	135
PR08711150	FAB DOOR HDWR	40	40	0	23SEP11	17NOV11	05APR12	31MAY12	135
PR08711160	DELIVER DOOR HDWR	1	1	0	18NOV11	18NOV11	01JUN12	01JUN12	135
PR08800010	RECEIVE GLAZING	10	10	0	11AUG11	24AUG11	16DEC11	30DEC11	88

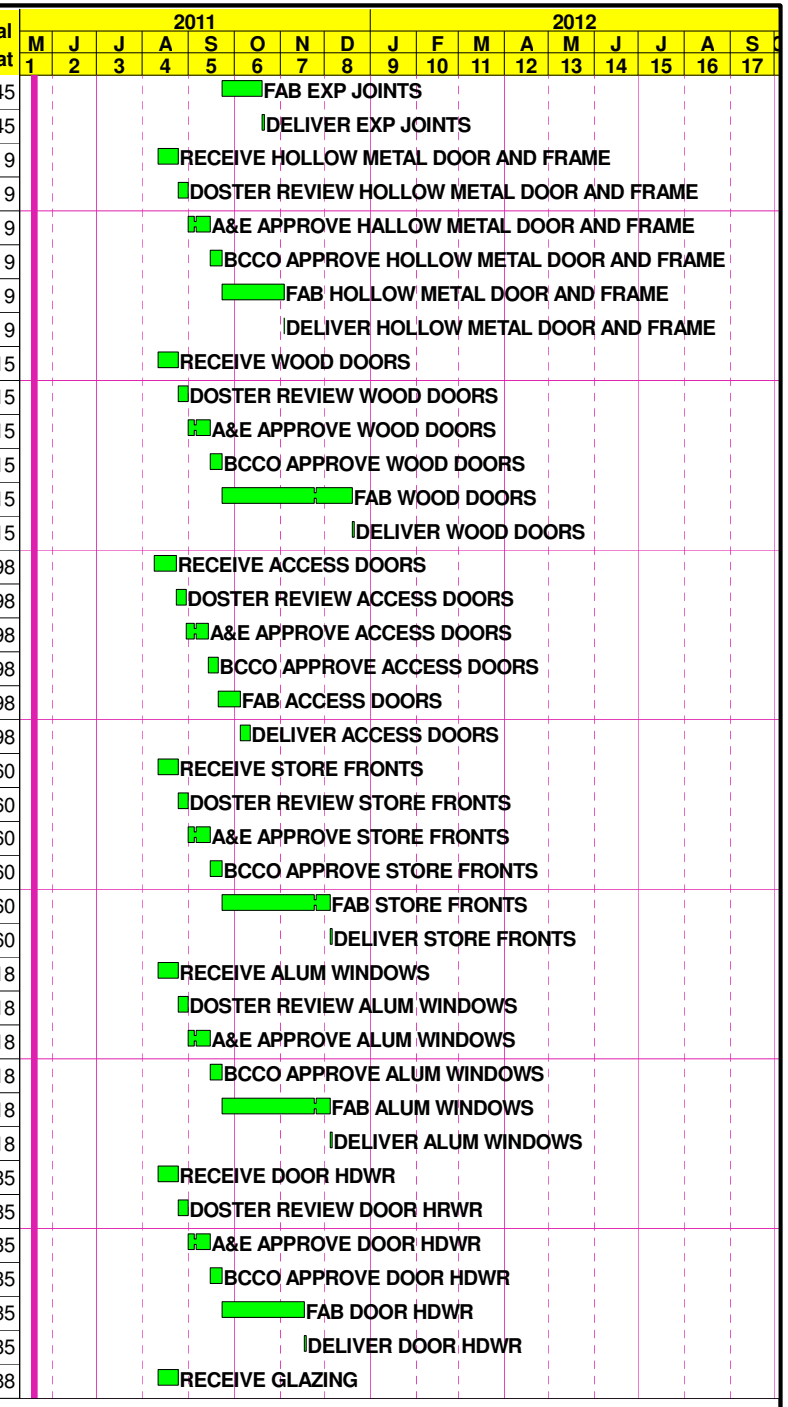

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

Sheet 12 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR08800020	DOSTER REVIEW GLAZING	5	5	0	25AUG11	31AUG11	03JAN12	09JAN12	88
PR08800030	A&E APPROVE GLAZING	10	10	0	01SEP11	15SEP11	10JAN12	23JAN12	88
PR08800040	BCCO APPROVE GLAZING	5	5	0	16SEP11	22SEP11	24JAN12	30JAN12	88
PR08800050	FAB GLAZING	15	15	0	23SEP11	13OCT11	31JAN12	20FEB12	88
PR08800060	DELIVER GLAZING	1	1	0	14OCT11	14OCT11	21FEB12	21FEB12	88
PR08900010	RECEIVE LOUVERS AND VENTS	10	10	0	09AUG11	22AUG11	16SEP11	29SEP11	27
PR08900020	DOSTER REVIEW LOUVERS AND	5	5	0	23AUG11	29AUG11	30SEP11	06OCT11	27
PR08900030	A&E APPROVE LOUVERS AND	10	10	0	30AUG11	13SEP11	07OCT11	20OCT11	27
PR08900040	BCCO APPROVE LOUVERS AND	5	5	0	14SEP11	20SEP11	21OCT11	27OCT11	27
PR08900050	FAB LOUVERS AND VENTS	40	40	0	21SEP11	15NOV11	28OCT11	27DEC11	27
PR08900060	DELIVER LOUVERS AND VENTS	1	1	0	16NOV11	16NOV11	28DEC11	28DEC11	27
PR09019010	RECEIVE RE-PAINT	10	10	0	18AUG11	31AUG11	22FEB12	06MAR12	129
PR09019020	DOSTER REVIEW RE-PAINT	5	5	0	01SEP11	08SEP11	07MAR12	13MAR12	129
PR09019030	A&E APPROVE RE-PAINT	10	10	0	09SEP11	22SEP11	14MAR12	27MAR12	129
PR09019040	BCCO APPROVE RE-PAINT	5	5	0	23SEP11	29SEP11	28MAR12	03APR12	129
PR09019050	FAB RE-PAINT	10	10	0	30SEP11	13OCT11	04APR12	17APR12	129
PR09019060	DELIVER RE-PAINT	1	1	0	14OCT11	14OCT11	18APR12	18APR12	129
PR09211610	RECEIVE GYP BOARD ASS	10	10	0	11AUG11	24AUG11	28SEP11	11OCT11	33
PR09211620	DOSTER REVIEW- GYP BOARD ASS	5	5	0	25AUG11	31AUG11	12OCT11	18OCT11	33
PR09211630	A&E APPROVE GYP BOARD ASS	10	10	0	01SEP11	15SEP11	19OCT11	01NOV11	33
PR09211640	BCCO APPROVE GYP BOARD ASS	5	5	0	16SEP11	22SEP11	02NOV11	08NOV11	33
PR09211650	FAB GYP BOARD ASS	10	10	0	23SEP11	06OCT11	09NOV11	22NOV11	33
PR09211660	DELIVER GYP BOARD ASS	1	1	0	07OCT11	07OCT11	23NOV11	23NOV11	33
PR09211710	RECEIVE SHAFT WALL	10	10	0	11AUG11	24AUG11	28SEP11	11OCT11	33
PR09211720	DOSTER REVIEW SHAFT WALL	5	5	0	25AUG11	31AUG11	12OCT11	18OCT11	33
PR09211730	A&E APPROVE SHAFT WALL	10	10	0	01SEP11	15SEP11	19OCT11	01NOV11	33
PR09211740	BCCO APPROVE SHAFT WALL	5	5	0	16SEP11	22SEP11	02NOV11	08NOV11	33
PR09211750	FAB SHAFT WALL	10	10	0	23SEP11	06OCT11	09NOV11	22NOV11	33
PR09211760	DELIVER SHAFT WALL	1	1	0	07OCT11	07OCT11	23NOV11	23NOV11	33
PR09240010	RECEIVE PLASTER	10	10	0	18AUG11	31AUG11	15MAR12	28MAR12	145
PR09240020	DOSTER REVIEW PLASTER	5	5	0	01SEP11	08SEP11	29MAR12	04APR12	145
PR09240030	A&E APPROVE PLASTER	10	10	0	09SEP11	22SEP11	05APR12	18APR12	145
PR09240040	BCCO APPROVE PLASTER	5	5	0	23SEP11	29SEP11	19APR12	25APR12	145
PR09240050	FAB PLASTER	10	10	0	30SEP11	13OCT11	26APR12	09MAY12	145
PR09240060	DELIVER PLASTER	1	1	0	14OCT11	14OCT11	10MAY12	10MAY12	145
PR09300010	RECEIVE TILING	10	10	0	18AUG11	31AUG11	02DEC11	15DEC11	73
PR09300020	DOSTER REVIEW TILING	5	5	0	01SEP11	08SEP11	16DEC11	22DEC11	73
PR09300030	A&E APPROVE TILING	10	10	0	09SEP11	22SEP11	23DEC11	09JAN12	73
PR09300040	BCCO APPROVE TILING	5	5	0	23SEP11	29SEP11	10JAN12	16JAN12	73

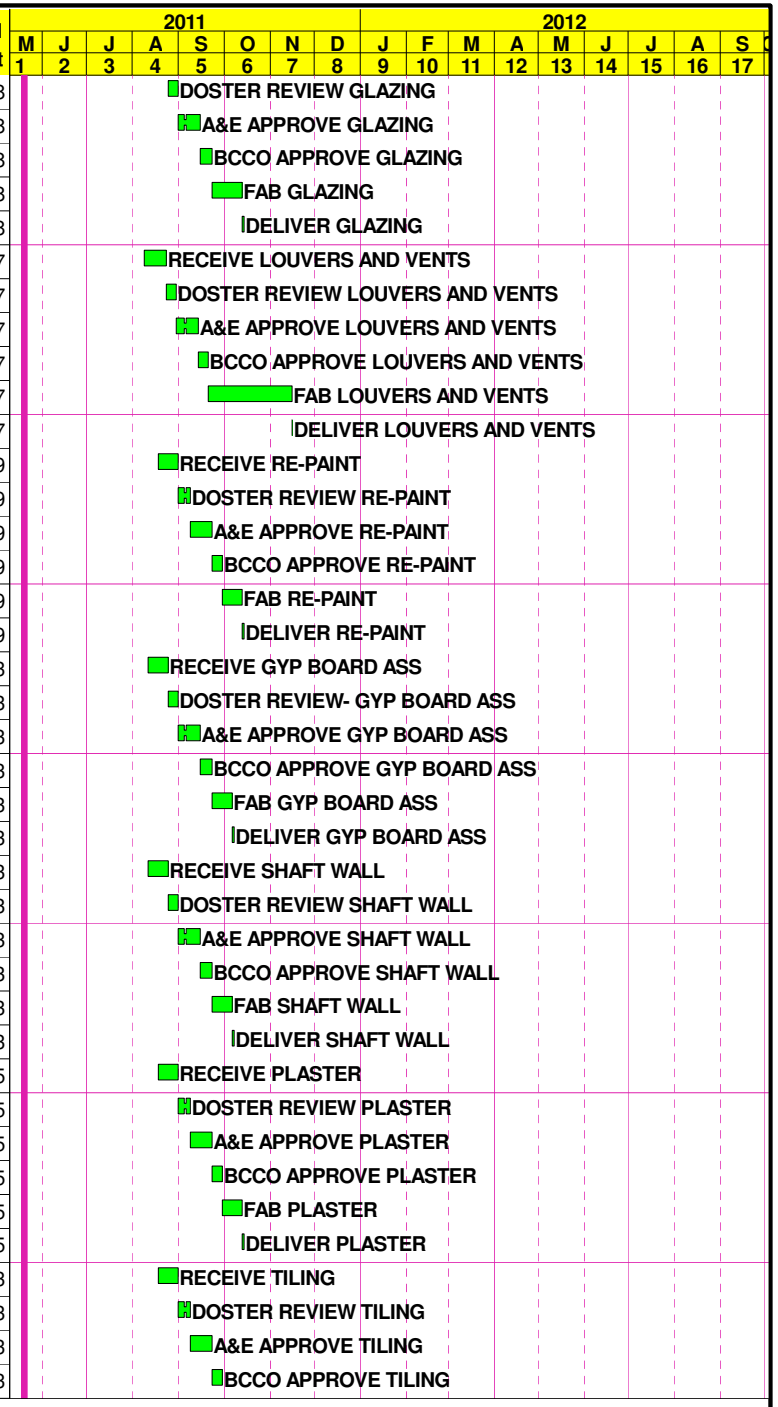

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR09300050	FAB TILING	30	30	0	30SEP11	10NOV11	17JAN12	27FEB12	73
PR09300060	DELIVER TILING	1	1	0	11NOV11	11NOV11	28FEB12	28FEB12	73
PR09511310	RECEIVE ACT	10	10	0	18AUG11	31AUG11	06JAN12	19JAN12	96
PR09511320	DOSTER REVIEW ACT	5	5	0	01SEP11	08SEP11	20JAN12	26JAN12	96
PR09511330	A&E APPROVE ACT	10	10	0	09SEP11	22SEP11	27JAN12	09FEB12	96
PR09511340	BCCO APPROVE ACT	5	5	0	23SEP11	29SEP11	10FEB12	16FEB12	96
PR09511350	FAB ACT	15	15	0	30SEP11	20OCT11	17FEB12	08MAR12	96
PR09511360	DELIVER ACT	1	1	0	21OCT11	21OCT11	09MAR12	09MAR12	96
PR09651610	RECEIVE SHEET FLOORING	10	10	0	18AUG11	31AUG11	08MAR12	21MAR12	140
PR09651620	DOSTER REVIEW SHEET FLOORING	5	5	0	01SEP11	08SEP11	22MAR12	28MAR12	140
PR09651630	A&E APPROVE SHEET FLOORING	10	10	0	09SEP11	22SEP11	29MAR12	11APR12	140
PR09651640	BCCO APPROVE SHEET FLOORING	5	5	0	23SEP11	29SEP11	12APR12	18APR12	140
PR09651650	FAB SHEET FLOORING	20	20	0	30SEP11	27OCT11	19APR12	16MAY12	140
PR09651660	DELIVER SHEET FLOORING	1	1	0	28OCT11	28OCT11	17MAY12	17MAY12	140
PR09651910	RECEIVE VCT	10	10	0	18AUG11	31AUG11	08MAR12	21MAR12	140
PR09651920	DOSTER REVIEW VCT	5	5	0	01SEP11	08SEP11	22MAR12	28MAR12	140
PR09651930	A&E APPROVE VCT	10	10	0	09SEP11	22SEP11	29MAR12	11APR12	140
PR09651940	BCCO APPROVE VCT	5	5	0	23SEP11	29SEP11	12APR12	18APR12	140
PR09651950	FAB VCT	20	20	0	30SEP11	27OCT11	19APR12	16MAY12	140
PR09651960	DELIVER VCT	1	1	0	28OCT11	28OCT11	17MAY12	17MAY12	140
PR09681310	RECEIVE CARPET TILE	10	10	0	18AUG11	31AUG11	16MAR12	29MAR12	146
PR09681320	DOSTER REVIEW CARPET TILE	5	5	0	01SEP11	08SEP11	30MAR12	05APR12	146
PR09681330	A&E APPROVE CARPET TILE	10	10	0	09SEP11	22SEP11	06APR12	19APR12	146
PR09681340	BCCO APPROVE CARPET TILE	5	5	0	23SEP11	29SEP11	20APR12	26APR12	146
PR09681350	FAB CARPET TILE	20	20	0	30SEP11	27OCT11	27APR12	24MAY12	146
PR09681360	DELIVER CARPET TILE	1	1	0	28OCT11	28OCT11	25MAY12	25MAY12	146
PR09841310	RECEIVE SOUND PANELS	10	10	0	18AUG11	31AUG11	20MAR12	02APR12	148
PR09841320	DOSTER REVIEW SOUND PANELS	5	5	0	01SEP11	08SEP11	03APR12	09APR12	148
PR09841330	A&E APPROVE SOUND PANELS	10	10	0	09SEP11	22SEP11	10APR12	23APR12	148
PR09841340	BCCO APPROVE SOUND PANELS	5	5	0	23SEP11	29SEP11	24APR12	30APR12	148
PR09841350	FAB SOUND PANELS	20	20	0	30SEP11	27OCT11	01MAY12	29MAY12	148
PR09841360	DELIVER SOUND PANELS	1	1	0	28OCT11	28OCT11	30MAY12	30MAY12	148
PR09900010	RECEIVE PAINT	10	10	0	18AUG11	31AUG11	23DEC11	09JAN12	88
PR09900020	DOSTER REVIEW PAINT	5	5	0	01SEP11	08SEP11	10JAN12	16JAN12	88
PR09900030	A&E APPROVE PAINT	10	10	0	09SEP11	22SEP11	17JAN12	30JAN12	88
PR09900040	BCCO APPROVE PAINT	5	5	0	23SEP11	29SEP11	31JAN12	06FEB12	88
PR09900050	FAB PAINT	10	10	0	30SEP11	13OCT11	07FEB12	20FEB12	88
PR09900060	DELIVER PAINT	1	1	0	14OCT11	14OCT11	21FEB12	21FEB12	88
PR10110010	RECEIVE VISUAL DISPLAYS	10	10	0	25AUG11	08SEP11	08MAR12	21MAR12	135

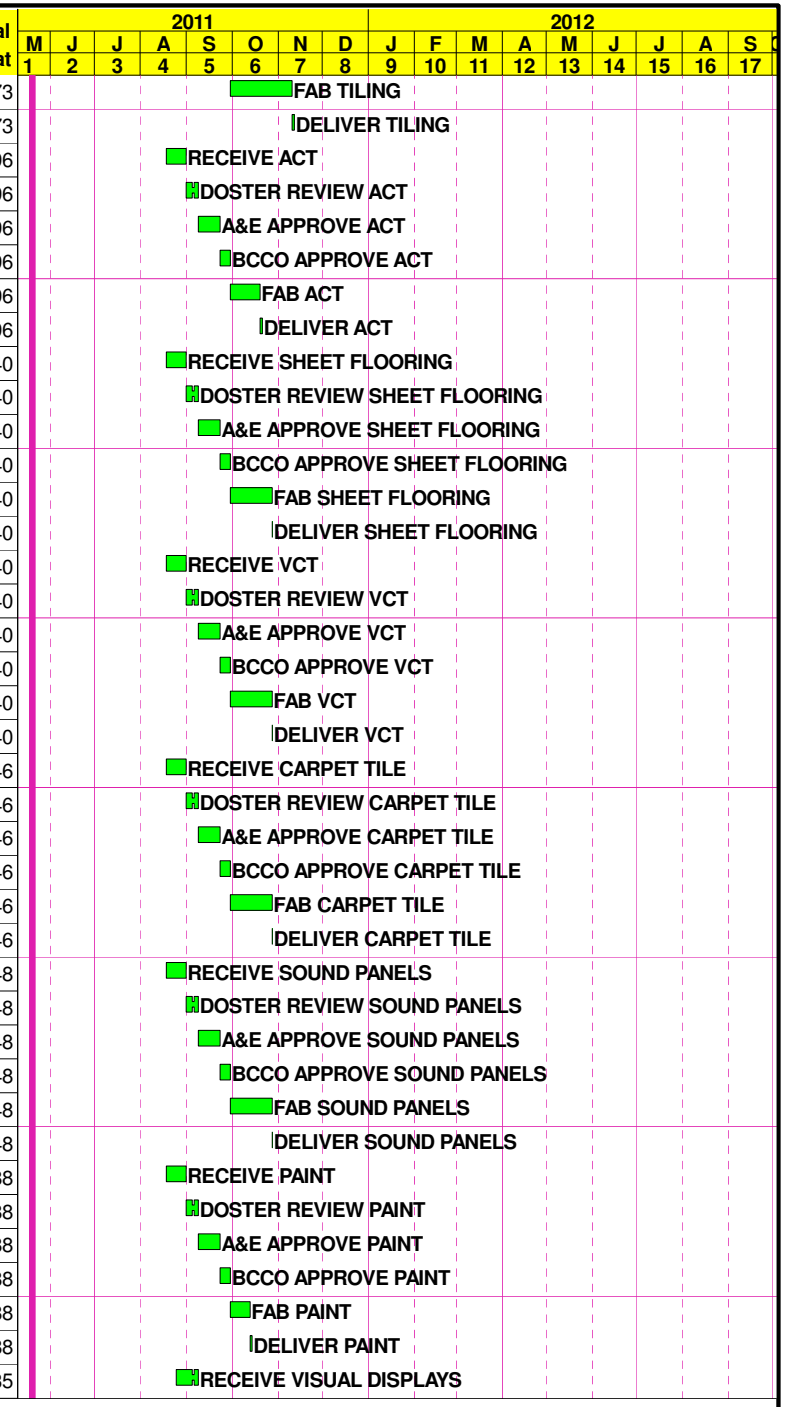

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR10110020	DOSTER REVIEW VISUAL DISPLAYS	5	5	0	09SEP11	15SEP11	22MAR12	28MAR12	135
PR10110030	A&E APPROVE VISUAL DISPLAYS	10	10	0	16SEP11	29SEP11	29MAR12	11APR12	135
PR10110040	BCCO APPROVE VISUAL DISPLAYS	5	5	0	30SEP11	06OCT11	12APR12	18APR12	135
PR10110050	FAB VISUAL DISPLAYS	20	20	0	07OCT11	03NOV11	19APR12	16MAY12	135
PR10110060	DELIVER VISUAL DISPLAYS	1	1	0	04NOV11	04NOV11	17MAY12	17MAY12	135
PR10120010	RECEIVE DISPLAY CASE	10	10	0	25AUG11	08SEP11	23FEB12	07MAR12	125
PR10120020	DOSTER REVIEW DISPLAY CASE	5	5	0	09SEP11	15SEP11	08MAR12	14MAR12	125
PR10120030	A&E APPROVE DISPLAY CASE	10	10	0	16SEP11	29SEP11	15MAR12	28MAR12	125
PR10120040	BCCO APPROVE DISPLAY CASE	5	5	0	30SEP11	06OCT11	29MAR12	04APR12	125
PR10120050	FAB DISPLAY CASE	30	30	0	07OCT11	17NOV11	05APR12	16MAY12	125
PR10120060	DELIVER DISPLAY CASE	1	1	0	18NOV11	18NOV11	17MAY12	17MAY12	125
PR10140010	RECEIVE SIGNAGE	10	10	0	25AUG11	08SEP11	23FEB12	07MAR12	125
PR10140020	DOSTER REVIEW SIGNAGE	5	5	0	09SEP11	15SEP11	08MAR12	14MAR12	125
PR10140030	A&E APPROVE SIGNAGE	10	10	0	16SEP11	29SEP11	15MAR12	28MAR12	125
PR10140040	BCCO APPROVE SIGNAGE	5	5	0	30SEP11	06OCT11	29MAR12	04APR12	125
PR10140050	FAB SIGNAGE	30	30	0	07OCT11	17NOV11	05APR12	16MAY12	125
PR10140060	DELIVER SIGNAGE	1	1	0	18NOV11	18NOV11	17MAY12	17MAY12	125
PR10143310	RECEIVE ILLUMINATED SIGN	10	10	0	25AUG11	08SEP11	22FEB12	06MAR12	124
PR10143320	DOSTER REVIEW ILLUMINATED SIGN	5	5	0	09SEP11	15SEP11	07MAR12	13MAR12	124
PR10143330	A&E APPROVE ILLUMINATED SIGN	10	10	0	16SEP11	29SEP11	14MAR12	27MAR12	124
PR10143340	BCCO APPROVE ILLUMINATED SIGN	5	5	0	30SEP11	06OCT11	28MAR12	03APR12	124
PR10143350	FAB ILLUMINATED SIGN	50	50	0	07OCT11	19DEC11	04APR12	13JUN12	124
PR10143360	DELIVER ILLUMINATED SIGN	1	1	0	20DEC11	20DEC11	14JUN12	14JUN12	124
PR10211310	RECEIVE TOILET COMPARTMENTS	10	10	0	25AUG11	08SEP11	07MAR12	20MAR12	134
PR10211320	DOSTER REVIEW TOILET	5	5	0	09SEP11	15SEP11	21MAR12	27MAR12	134
PR10211330	A&E APPROVE TOILET	10	10	0	16SEP11	29SEP11	28MAR12	10APR12	134
PR10211340	BCCO APPROVE TOILET	5	5	0	30SEP11	06OCT11	11APR12	17APR12	134
PR10211350	FAB TOILET COMPARTMENTS	30	30	0	07OCT11	17NOV11	18APR12	30MAY12	134
PR10211360	DELIVER TOILET COMPARTMENTS	1	1	0	18NOV11	18NOV11	31MAY12	31MAY12	134
PR10260010	RECEIVE WALL DOOR PROTECT	10	10	0	25AUG11	08SEP11	23FEB12	07MAR12	125
PR10260020	DOSTER REVIEW WALL DOOR	5	5	0	09SEP11	15SEP11	08MAR12	14MAR12	125
PR10260030	A&E APPROVE WALL DOOR	10	10	0	16SEP11	29SEP11	15MAR12	28MAR12	125
PR10260040	BCCO APPROVE WALL DOOR	5	5	0	30SEP11	06OCT11	29MAR12	04APR12	125
PR10260050	FAB WALL DOOR PROTECT	30	30	0	07OCT11	17NOV11	05APR12	16MAY12	125
PR10260060	DELIVER WALL DOOR PROTECT	1	1	0	18NOV11	18NOV11	17MAY12	17MAY12	125
PR10281310	RECEIVE TOILET ACC.	10	10	0	25AUG11	08SEP11	23FEB12	07MAR12	125
PR10281320	DOSTER REVIEW TOILET ACC.	5	5	0	09SEP11	15SEP11	08MAR12	14MAR12	125
PR10281330	A&E APPROVE TOILET ACC.	10	10	0	16SEP11	29SEP11	15MAR12	28MAR12	125
PR10281340	BCCO APPROVE TOILET ACC.	5	5	0	30SEP11	06OCT11	29MAR12	04APR12	125

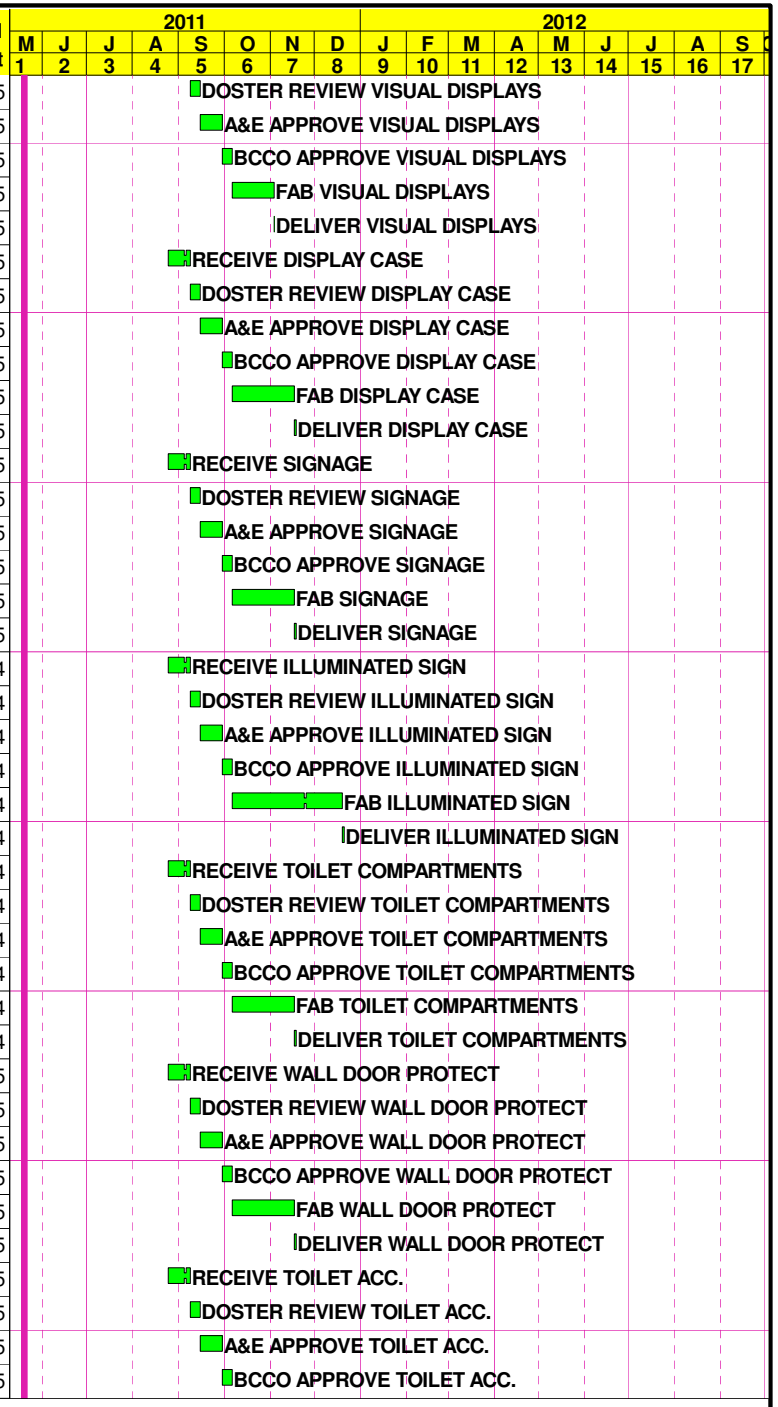

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR10281350	FAB TOILET ACC.	30	30	0	07OCT11	17NOV11	05APR12	16MAY12	125
PR10281360	DELIVER TOILET ACC.	1	1	0	18NOV11	18NOV11	17MAY12	17MAY12	125
PR10411610	RECEIVE EMER KEY CAB	10	10	0	25AUG11	08SEP11	08FEB12	21FEB12	114
PR10411620	DOSTER REVIEW EMER KEY CAB	5	5	0	09SEP11	15SEP11	22FEB12	28FEB12	114
PR10411630	A&E APPROVE EMER KEY CAB	10	10	0	16SEP11	29SEP11	29FEB12	13MAR12	114
PR10411640	BCCO APPROVE EMER CAB	5	5	0	30SEP11	06OCT11	14MAR12	20MAR12	114
PR10411650	FAB EMER KEY CAB	20	20	0	07OCT11	03NOV11	21MAR12	17APR12	114
PR10411660	DELIVER EMER KEY CAB	1	1	0	04NOV11	04NOV11	18APR12	18APR12	114
PR10440010	RECEIVE FIRE PROTECT	10	10	0	25AUG11	08SEP11	15MAR12	28MAR12	140
PR10440020	DOSTER REVIEW FIRE PROTECT	5	5	0	09SEP11	15SEP11	29MAR12	04APR12	140
PR10440030	A&E APPROVE FIRE PROTECT	10	10	0	16SEP11	29SEP11	05APR12	18APR12	140
PR10440040	BCCO APPROVE FIRE PROTECT	5	5	0	30SEP11	06OCT11	19APR12	25APR12	140
PR10440050	FAB FIRE PROTECT SPECIALTIES	15	15	0	07OCT11	27OCT11	26APR12	16MAY12	140
PR10440060	DELIVER FIRE PROTECT	1	1	0	28OCT11	28OCT11	17MAY12	17MAY12	140
PR10511310	RECEIVE LOCKERS	10	10	0	25AUG11	08SEP11	19OCT11	01NOV11	38
PR10511320	DOSTER REVIEW LOCKERS	5	5	0	09SEP11	15SEP11	02NOV11	08NOV11	38
PR10511330	A&E APPROVE LOCKERS	10	10	0	16SEP11	29SEP11	09NOV11	22NOV11	38
PR10511340	BCCO APPROVE LOCKERS	5	5	0	30SEP11	06OCT11	23NOV11	01DEC11	38
PR10511350	FAB LOCKERS	60	60	0	07OCT11	04JAN12	02DEC11	27FEB12	38
PR10511360	DELIVER LOCKERS	1	1	0	05JAN12	05JAN12	28FEB12	28FEB12	38
PR10732610	RECEIVE WALKWAY COVERINGS	10	10	0	18AUG11	31AUG11	08FEB12	21FEB12	119
PR10732620	DOSTER REVIEW WALKWAY	5	5	0	01SEP11	08SEP11	22FEB12	28FEB12	119
PR10732630	A&E APPROVE WALKWAY	10	10	0	09SEP11	22SEP11	29FEB12	13MAR12	119
PR10732640	BCCO APPROVE WALKWAY	5	5	0	23SEP11	29SEP11	14MAR12	20MAR12	119
PR10732650	FAB WALKWAY COVERINGS	40	40	0	30SEP11	28NOV11	21MAR12	15MAY12	119
PR10732660	DELIVER WALKWAY COVERINGS	1	1	0	29NOV11	29NOV11	16MAY12	16MAY12	119
PR10750010	RECEIVE FLAG POLE	10	10	0	25AUG11	08SEP11	14NOV11	29NOV11	56
PR10750020	DOSTER REVIEW FLAG POLE	5	5	0	09SEP11	15SEP11	30NOV11	06DEC11	56
PR10750030	A&E APPROVE FLAG POLE	10	10	0	16SEP11	29SEP11	07DEC11	20DEC11	56
PR10750040	BCCO APPROVE FLAG POLE	5	5	0	30SEP11	06OCT11	21DEC11	28DEC11	56
PR10750050	FAB FLAG POLE	20	20	0	07OCT11	03NOV11	29DEC11	26JAN12	56
PR10750060	DELIVER FLAG POLE	1	1	0	04NOV11	04NOV11	27JAN12	27JAN12	56
PR11400010	RECEIVE FOOD SERVICE	10	10	0	11AUG11	24AUG11	20DEC11	04JAN12	90
PR11400020	DOSTER REVIEW FOOD SERVICE	5	5	0	25AUG11	31AUG11	05JAN12	11JAN12	90
PR11400030	A&E APPROVE FOOD SERVICE	10	10	0	01SEP11	15SEP11	12JAN12	25JAN12	90
PR11400040	BCCO APPROVE FOOD SERVICE	5	5	0	16SEP11	22SEP11	26JAN12	01FEB12	90
PR11400050	FAB FOOD SERVICE	60	60	0	23SEP11	19DEC11	02FEB12	25APR12	90
PR11400060	DELIVER FOOD SERVICE	3	3	0	20DEC11	22DEC11	26APR12	30APR12	90
PR11521310	RECEIVE PROJECTION SCREEN	10	10	0	25AUG11	08SEP11	29DEC11	12JAN12	86

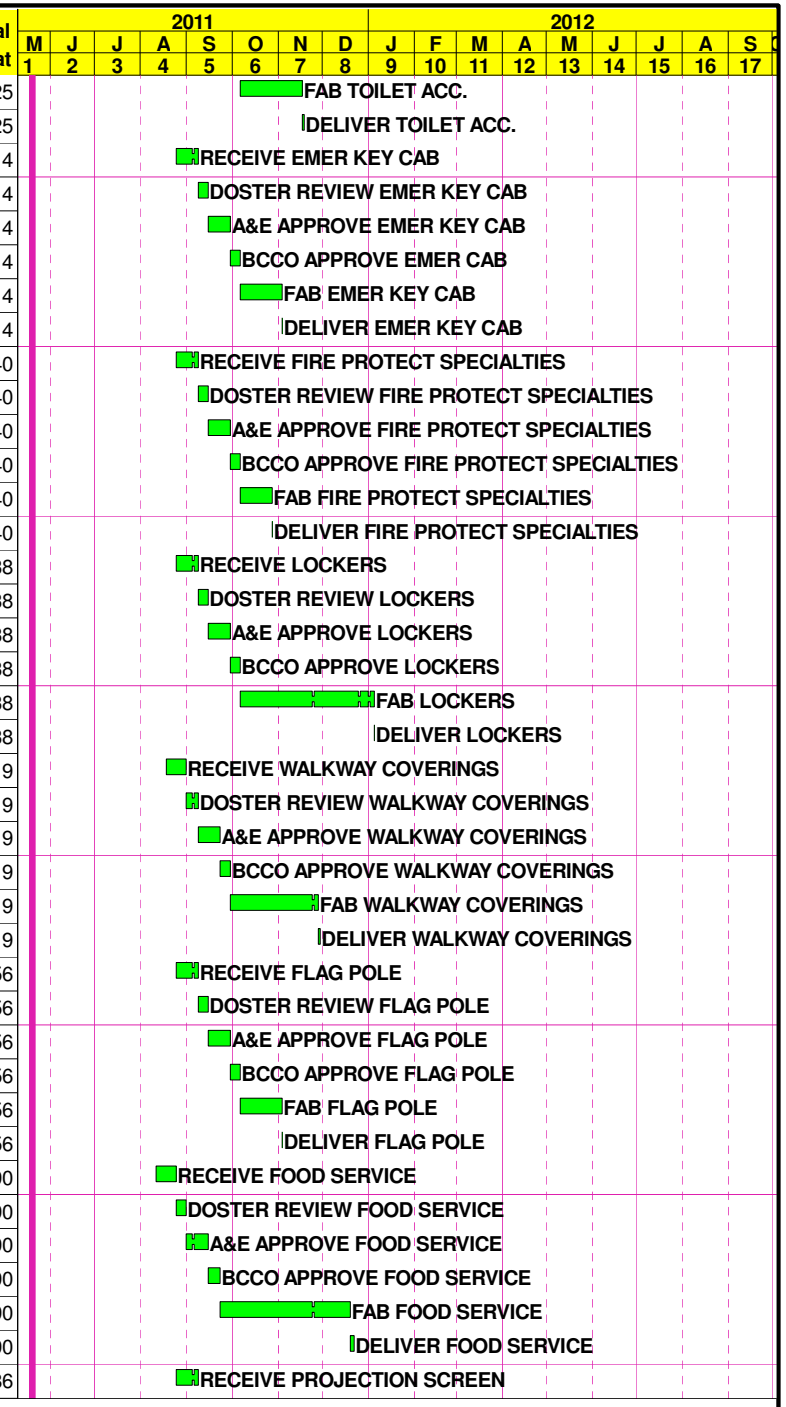

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR11521320	DOSTER REVIEW PROJECTION	5	5	0	09SEP11	15SEP11	13JAN12	19JAN12	86
PR11521330	A&E APPROVE PROJECTION	10	10	0	16SEP11	29SEP11	20JAN12	02FEB12	86
PR11521340	BCCO APPROVE PROJECTION	5	5	0	30SEP11	06OCT11	03FEB12	09FEB12	86
PR11521350	FAB PROJECTION SCREEN	20	20	0	07OCT11	03NOV11	10FEB12	08MAR12	86
PR11521360	DELIVER PROJECTION SCREEN	1	1	0	04NOV11	04NOV11	09MAR12	09MAR12	86
PR11614310	RECEIVE STAGE CURTAINS	10	10	0	25AUG11	08SEP11	23FEB12	07MAR12	125
PR11614320	DOSTER REVIEW STAGE CURTAINS	5	5	0	09SEP11	15SEP11	08MAR12	14MAR12	125
PR11614330	A&E APPROVE STAGE CURTAINS	10	10	0	16SEP11	29SEP11	15MAR12	28MAR12	125
PR11614340	BCCO APPROVE STAGE CURTAINS	5	5	0	30SEP11	06OCT11	29MAR12	04APR12	125
PR11614350	FAB STAGE CURTAINS	30	30	0	07OCT11	17NOV11	05APR12	16MAY12	125
PR11614360	DELIVER STAGE CURTAINS	1	1	0	18NOV11	18NOV11	17MAY12	17MAY12	125
PR11660010	RECEIVE ATHLETIC EQ	10	10	0	25AUG11	08SEP11	25APR12	08MAY12	169
PR11660020	DOSTER REVIEW ATHLETIC EQ	5	5	0	09SEP11	15SEP11	09MAY12	15MAY12	169
PR11660030	A&E APPROVE ATHLETIC EQ	10	10	0	16SEP11	29SEP11	16MAY12	30MAY12	169
PR11660040	BCCO APPROVE ATHLETIC EQ	5	5	0	30SEP11	06OCT11	31MAY12	06JUN12	169
PR11660050	FAB ATHLETIC EQ	30	30	0	07OCT11	17NOV11	07JUN12	19JUL12	169
PR11660060	DELIVER ATHLETIC EQ	1	1	0	18NOV11	18NOV11	20JUL12	20JUL12	169
PR11661010	RECEIVE COURTS & FIELDS	10	10	0	05AUG11	18AUG11	26OCT11	08NOV11	57
PR11661020	DOSTER REVIEW COURTS & FIELDS	5	5	0	19AUG11	25AUG11	09NOV11	15NOV11	57
PR11661030	A&E APPROVE COURTS & FIELDS	10	10	0	26AUG11	09SEP11	16NOV11	01DEC11	57
PR11661040	BCCO APPROVE COURTS & FIELDS	5	5	0	12SEP11	16SEP11	02DEC11	08DEC11	57
PR11661050	FAB COURTS & FIELDS	15	15	0	19SEP11	07OCT11	09DEC11	30DEC11	57
PR11661060	DELIVER COURTS & FIELDS	1	1	0	10OCT11	10OCT11	03JAN12	03JAN12	57
PR11681310	RECEIVE PLAY EQ	10	10	0	25AUG11	08SEP11	05DEC11	16DEC11	69
PR11681320	DOSTER REVIEW PLAY EQ	5	5	0	09SEP11	15SEP11	19DEC11	23DEC11	69
PR11681330	A&E APPROVE PLAY EQ	10	10	0	16SEP11	29SEP11	27DEC11	10JAN12	69
PR11681340	BCCO APPROVE PLAY EQ	5	5	0	30SEP11	06OCT11	11JAN12	17JAN12	69
PR11681350	FAB PLAY EQ	30	30	0	07OCT11	17NOV11	18JAN12	28FEB12	69
PR11681360	DELIVER PLAY EQ	1	1	0	18NOV11	18NOV11	29FEB12	29FEB12	69
PR12142710	RECEIVE KILNS	10	10	0	25AUG11	08SEP11	20MAR12	02APR12	143
PR12142720	DOSTER REVIEW KILNS	5	5	0	09SEP11	15SEP11	03APR12	09APR12	143
PR12142730	A&E APPROVE KILNS	10	10	0	16SEP11	29SEP11	10APR12	23APR12	143
PR12142740	BCCO APPROVE KILNS	5	5	0	30SEP11	06OCT11	24APR12	30APR12	143
PR12142750	FAB KILNS	20	20	0	07OCT11	03NOV11	01MAY12	29MAY12	143
PR12142760	DELIVER KILNS	1	1	0	04NOV11	04NOV11	30MAY12	30MAY12	143
PR12211310	RECEIVE BLINDS	10	10	0	25AUG11	08SEP11	08MAR12	21MAR12	135
PR12211320	DOSTER REVIEW- BLINDS	5	5	0	09SEP11	15SEP11	22MAR12	28MAR12	135
PR12211330	A&E APPROVE BLINDS	10	10	0	16SEP11	29SEP11	29MAR12	11APR12	135
PR12211340	BCCO APPROVE BLINDS	5	5	0	30SEP11	06OCT11	12APR12	18APR12	135

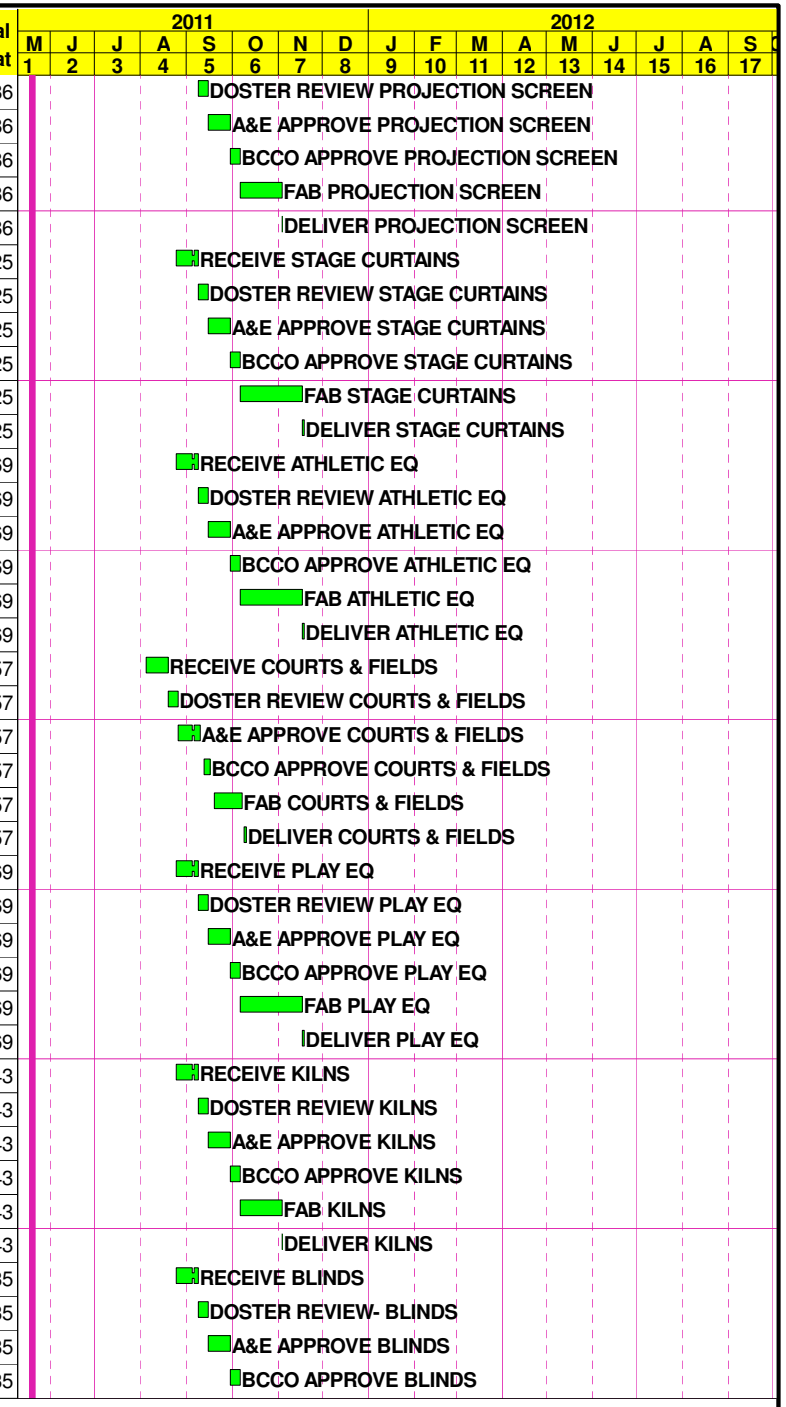

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

Sheet 17 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR12211350	FAB BLINDS	20	20	0	07OCT11	03NOV11	19APR12	16MAY12	135
PR12211360	DELIVER BLINDS	1	1	0	04NOV11	04NOV11	17MAY12	17MAY12	135
PR12320010	RECEIVE CASEWORK	10	10	0	18AUG11	31AUG11	29DEC11	12JAN12	91
PR12320020	DOSTER REVIEW CASEWORK	5	5	0	01SEP11	08SEP11	13JAN12	19JAN12	91
PR12320030	A&E APPROVE CASEWORK	10	10	0	09SEP11	22SEP11	20JAN12	02FEB12	91
PR12320040	BCCO APPROVE CASEWORK	5	5	0	23SEP11	29SEP11	03FEB12	09FEB12	91
PR12320050	FAB CASEWORK	60	60	0	30SEP11	27DEC11	10FEB12	03MAY12	91
PR12320060	DELIVER CASEWORK	5	5	0	28DEC11	04JAN12	04MAY12	10MAY12	91
PR12931310	RECEIVE BIKE / SKATE RACK	10	10	0	25AUG11	08SEP11	15MAR12	28MAR12	140
PR12931320	DOSTER REVIEW BIKE / SKATE	5	5	0	09SEP11	15SEP11	29MAR12	04APR12	140
PR12931330	A&E APPROVE BIKE / SKATE RACK	10	10	0	16SEP11	29SEP11	05APR12	18APR12	140
PR12931340	BCCO APPROVE BIKE / SKATE RACK	5	5	0	30SEP11	06OCT11	19APR12	25APR12	140
PR12931350	FAB BIKE / SKATE RACK	20	20	0	07OCT11	03NOV11	26APR12	23MAY12	140
PR12931360	DELIVER BIKE / SKATE RACK	1	1	0	04NOV11	04NOV11	24MAY12	24MAY12	140
PR14240010	RECEIVE ELEVATOR	10	10	0	11AUG11	24AUG11	21OCT11	03NOV11	50
PR14240020	DOSTER REVIEW ELEVATOR	5	5	0	25AUG11	31AUG11	04NOV11	10NOV11	50
PR14240030	A&E APPROVE ELEVATOR	10	10	0	01SEP11	15SEP11	11NOV11	28NOV11	50
PR14240040	BCCO APPROVE ELEVATOR	5	5	0	16SEP11	22SEP11	29NOV11	05DEC11	50
PR14240050	FAB ELEVATOR	60	60	0	23SEP11	19DEC11	06DEC11	29FEB12	50
PR14240060	DELIVER ELEVATOR	1	1	0	20DEC11	20DEC11	01MAR12	01MAR12	50
PR21050010	RECEIVE COMMON FIRE	10	10	0	11AUG11	24AUG11	29SEP11	12OCT11	34
PR21050020	DOSTER REVIEW COMMON FIRE	5	5	0	25AUG11	31AUG11	13OCT11	19OCT11	34
PR21050030	A&E APPROVE COMMON FIRE	10	10	0	01SEP11	15SEP11	20OCT11	02NOV11	34
PR21050040	BCCO APPROVE COMMON FIRE	5	5	0	16SEP11	22SEP11	03NOV11	09NOV11	34
PR21050050	FAB COMMON FIRE SUPPRESSION	10	10	0	23SEP11	06OCT11	10NOV11	23NOV11	34
PR21050060	DELIVER COMMON FIRE	1	1	0	07OCT11	07OCT11	28NOV11	28NOV11	34
PR21131310	RECEIVE WET SPRINKLERS	10	10	0	11AUG11	24AUG11	22SEP11	05OCT11	29
PR21131320	DOSTER REVIEW WET SPRINKLERS	5	5	0	25AUG11	31AUG11	06OCT11	12OCT11	29
PR21131330	A&E APPROVE WET SPRINKLERS	10	10	0	01SEP11	15SEP11	13OCT11	26OCT11	29
PR21131340	BCCO APPROVE WET SPRINKLERS	5	5	0	16SEP11	22SEP11	27OCT11	02NOV11	29
PR21131350	FAB WET SPRINKLERS	15	15	0	23SEP11	13OCT11	03NOV11	23NOV11	29
PR21131360	DELIVER WET SPRINKLERS	1	1	0	14OCT11	14OCT11	28NOV11	28NOV11	29
PR22050010	RECEIVE COMMON PLUMBING	10	10	0	09AUG11	22AUG11	11AUG11	24AUG11	2
PR22050020	DOSTER REVIEW COMMON	5	5	0	23AUG11	29AUG11	25AUG11	31AUG11	2
PR22050030	A&E APPROVE COMMON PLUMBING	10	10	0	30AUG11	13SEP11	01SEP11	15SEP11	2
PR22050040	BCCO APPROVE COMMON	5	5	0	14SEP11	20SEP11	16SEP11	22SEP11	2
PR22050050	FAB COMMON PLUMBING	10	10	0	21SEP11	04OCT11	23SEP11	06OCT11	2
PR22050060	DELIVER COMMON PLUMBING	1	1	0	05OCT11	05OCT11	07OCT11	07OCT11	2
PR22051910	RECEIVE METERS AND GAUGES	10	10	0	09AUG11	22AUG11	08NOV11	21NOV11	64

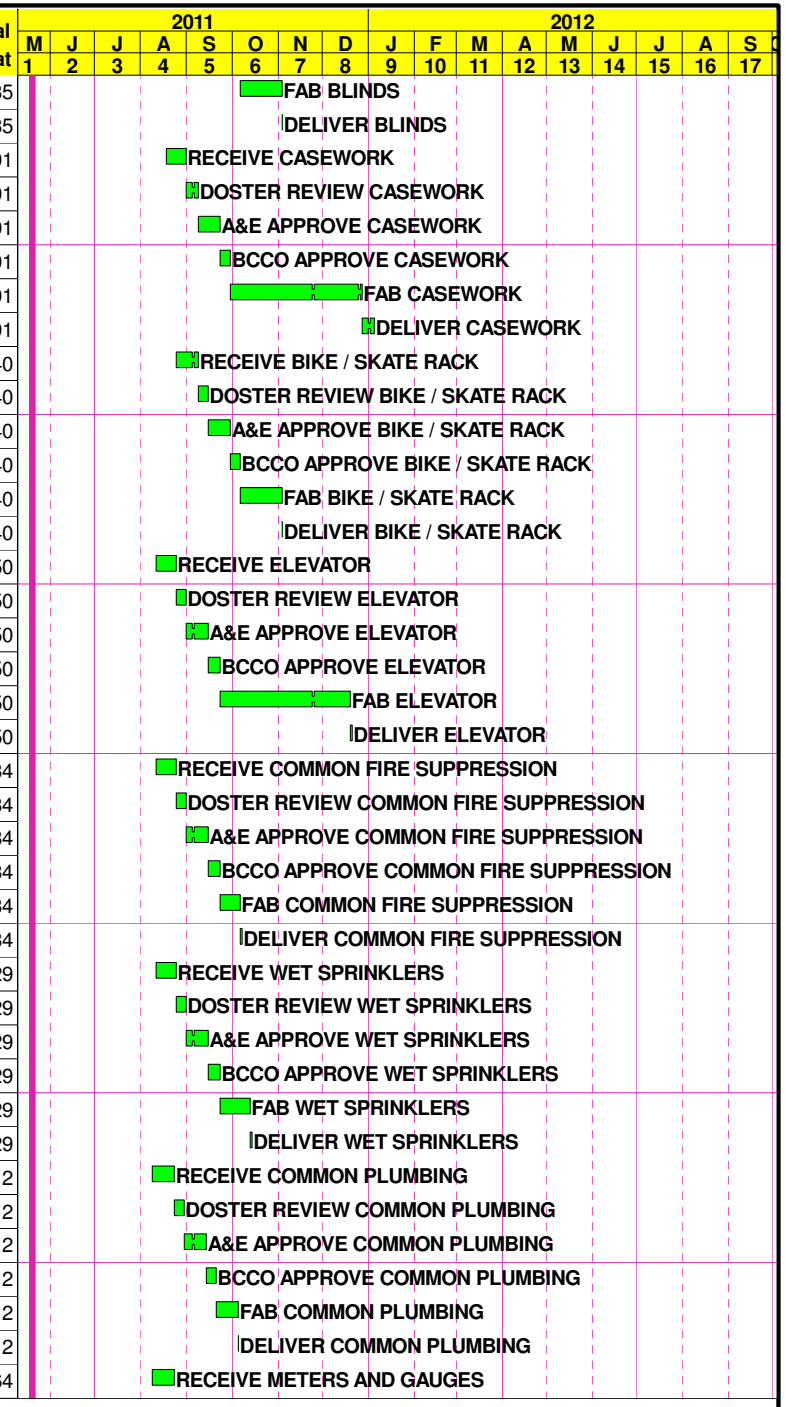

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR22051920	DOSTER REVIEW METERS AND	5	5	0	23AUG11	29AUG11	22NOV11	30NOV11	64
PR22051930	A&E APPROVE METERS AND	10	10	0	30AUG11	13SEP11	01DEC11	14DEC11	64
PR22051940	BCCO APPROVE METERS AND	5	5	0	14SEP11	20SEP11	15DEC11	21DEC11	64
PR22051950	FAB METERS AND GAUGES	20	20	0	21SEP11	18OCT11	22DEC11	20JAN12	64
PR22051960	DELIVER METERS AND GAUGES	1	1	0	19OCT11	19OCT11	23JAN12	23JAN12	64
PR22052310	RECEIVE VALVES	10	10	0	09AUG11	22AUG11	20OCT11	02NOV11	51
PR22052320	DOSTER REVIEW VALVES	5	5	0	23AUG11	29AUG11	03NOV11	09NOV11	51
PR22052330	A&E APPROVE VALVES	10	10	0	30AUG11	13SEP11	10NOV11	23NOV11	51
PR22052340	BCCO APPROVE VALVES	5	5	0	14SEP11	20SEP11	28NOV11	02DEC11	51
PR22052350	FAB VALVES	20	20	0	21SEP11	18OCT11	05DEC11	03JAN12	51
PR22052360	DELIVER VALVES	1	1	0	19OCT11	19OCT11	04JAN12	04JAN12	51
PR22052910	RECEIVE PLUMBING SUPPORTS	10	10	0	09AUG11	22AUG11	12OCT11	25OCT11	45
PR22052920	DOSTER REVIEW PLUMBING	5	5	0	23AUG11	29AUG11	26OCT11	01NOV11	45
PR22052930	A&E APPROVE PLUMBING	10	10	0	30AUG11	13SEP11	02NOV11	15NOV11	45
PR22052940	BCCO APPROVE PLUMBING	5	5	0	14SEP11	20SEP11	16NOV11	22NOV11	45
PR22052950	FAB PLUMBING SUPPORTS	10	10	0	21SEP11	04OCT11	23NOV11	08DEC11	45
PR22052960	DELIVER PLUMBING SUPPORTS	1	1	0	05OCT11	05OCT11	09DEC11	09DEC11	45
PR22053310	RECEIVE ID PLUMBING	10	10	0	09AUG11	22AUG11	12MAR12	23MAR12	149
PR22053320	DOSTER REVIEW ID PLUMBING	5	5	0	23AUG11	29AUG11	26MAR12	30MAR12	149
PR22053330	A&E APPROVED PLUMBING	10	10	0	30AUG11	13SEP11	02APR12	13APR12	149
PR22053340	BCCO APPROVE ID PLUMBING	5	5	0	14SEP11	20SEP11	16APR12	20APR12	149
PR22053350	FAB PLUMBING	20	20	0	21SEP11	18OCT11	23APR12	18MAY12	149
PR22053360	DELIVER ID PLUMBING	1	1	0	19OCT11	19OCT11	21MAY12	21MAY12	149
PR22070010	RECEIVE PLUMBING INSULATION	10	10	0	09AUG11	22AUG11	03NOV11	16NOV11	61
PR22070020	DOSTER REVIEW PLUMBING	5	5	0	23AUG11	29AUG11	17NOV11	23NOV11	61
PR22070030	A&E APPROVE PLUMBING	10	10	0	30AUG11	13SEP11	28NOV11	09DEC11	61
PR22070040	BCCO APPROVE PLUMBING	5	5	0	14SEP11	20SEP11	12DEC11	16DEC11	61
PR22070050	FAB PLUMBING INSULATION	10	10	0	21SEP11	04OCT11	19DEC11	03JAN12	61
PR22070060	DELIVER PLUMBING INSULATION	1	1	0	05OCT11	05OCT11	04JAN12	04JAN12	61
PR22110010	RECEIVE DOM WATER PIPING	10	10	0	09AUG11	22AUG11	22NOV11	07DEC11	74
PR22110020	DOSTER REVIEW DOM WATER	5	5	0	23AUG11	29AUG11	08DEC11	14DEC11	74
PR22110030	A&E APPROVE DOM WATER PIPING	10	10	0	30AUG11	13SEP11	15DEC11	29DEC11	74
PR22110040	BCCO APPROVE DOM WATER	5	5	0	14SEP11	20SEP11	30DEC11	06JAN12	74
PR22110050	FAB DOM WATER PIPING	10	10	0	21SEP11	04OCT11	09JAN12	20JAN12	74
PR22110060	DELIVER DOM WATER PIPING	1	1	0	05OCT11	05OCT11	23JAN12	23JAN12	74
PR22112310	RECEIVE PUMPS	10	10	0	09AUG11	22AUG11	11OCT11	24OCT11	44
PR22112320	DOSTER REVIEW PUMPS	5	5	0	23AUG11	29AUG11	25OCT11	31OCT11	44
PR22112330	A&E APPROVE PUMPS	10	10	0	30AUG11	13SEP11	01NOV11	14NOV11	44
PR22112340	BCCO APPROVE PUMPS	5	5	0	14SEP11	20SEP11	15NOV11	21NOV11	44

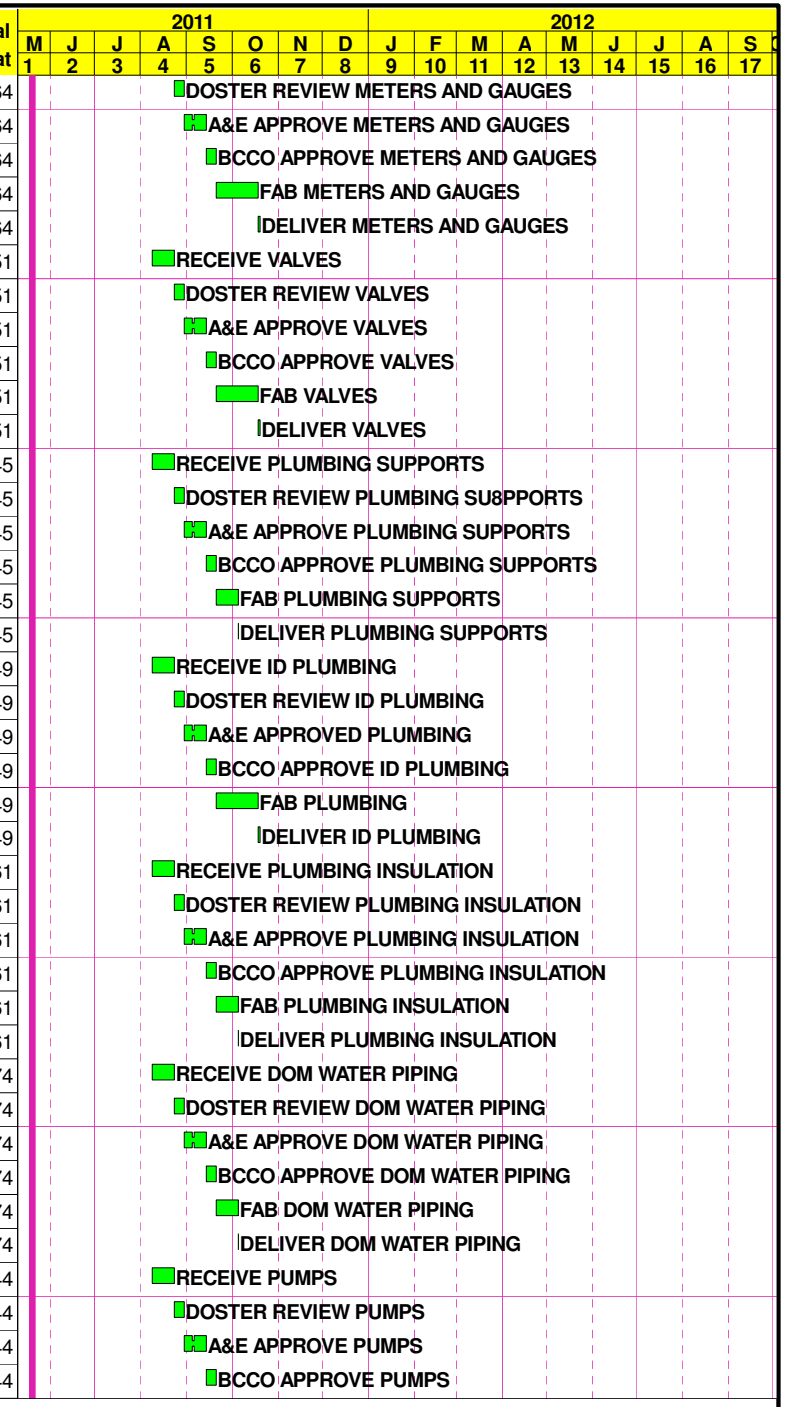

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0 Sheet 19 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR22112350	FAB PUMPS	40	40	0	21SEP11	15NOV11	22NOV11	20JAN12	44
PR22112360	DELIVER PUMPS	1	1	0	16NOV11	16NOV11	23JAN12	23JAN12	44
PR22131310	RECEIVE SAN SEWERS	1	1	0	05AUG11	05AUG11	08AUG11	08AUG11	1
PR22131320	DOSTER REVIEW SAN SEWERS	1	1	0	08AUG11	08AUG11	09AUG11	09AUG11	1
PR22131330	A&E APPROVE SAN SEWERS	5	5	0	09AUG11	15AUG11	10AUG11	16AUG11	1
PR22131340	BCCO APPROVE SAN SEWERS	5	5	0	16AUG11	22AUG11	17AUG11	23AUG11	1
PR22131350	FAB SAN SEWERS	10	10	0	23AUG11	06SEP11	24AUG11	07SEP11	1
PR22131360	DELIVER SAN SEWERS	1	1	0	07SEP11	07SEP11	08SEP11	08SEP11	1
PR22131610	RECEIVE SAN PIPING	1	1	0	05AUG11	05AUG11	08AUG11	08AUG11	1
PR22131620	DOSTER REVIEW SAN PIPING	1	1	0	08AUG11	08AUG11	09AUG11	09AUG11	1
PR22131630	A&E APPROVE SAN PIPING	5	5	0	09AUG11	15AUG11	10AUG11	16AUG11	1
PR22131640	BCCO APPROVE SAN PIPING	5	5	0	16AUG11	22AUG11	17AUG11	23AUG11	1
PR22131650	FAB SAN PIPING	10	10	0	23AUG11	06SEP11	24AUG11	07SEP11	1
PR22131660	DELIVER SAN PIPING	1	1	0	07SEP11	07SEP11	08SEP11	08SEP11	1
PR22132310	RECEIVE SAN INTERCEPTORS	10	10	0	09AUG11	22AUG11	30NOV11	13DEC11	78
PR22132320	DOSTER REVIEW SAN	5	5	0	23AUG11	29AUG11	14DEC11	20DEC11	78
PR22132330	A&E APPROVE SAN INTERCEPTORS	10	10	0	30AUG11	13SEP11	21DEC11	05JAN12	78
PR22132340	BCCO APPROVE SAN	5	5	0	14SEP11	20SEP11	06JAN12	12JAN12	78
PR22132350	FAB SAN INTERCEPTORS	15	15	0	21SEP11	11OCT11	13JAN12	02FEB12	78
PR22132360	DELIVER SAN INTERCEPTORS	1	1	0	12OCT11	12OCT11	03FEB12	03FEB12	78
PR22141310	RECEIVE STORM DRAINAGE	1	1	0	05AUG11	05AUG11	08AUG11	08AUG11	1
PR22141320	DOSTER REVIEW STORM DRAINAGE	1	1	0	08AUG11	08AUG11	09AUG11	09AUG11	1
PR22141330	A&E APPROVE STORM DRAINAGE	5	5	0	09AUG11	15AUG11	10AUG11	16AUG11	1
PR22141340	BCCO APPROVE STORM DRAINAGE	5	5	0	16AUG11	22AUG11	17AUG11	23AUG11	1
PR22141350	FAB STORM DRAINAGE	10	10	0	23AUG11	06SEP11	24AUG11	07SEP11	1
PR22141360	DELIVER STORM DRAINAGE	1	1	0	07SEP11	07SEP11	08SEP11	08SEP11	1
PR22142910	RECEIVE SUMP PUMPS	10	10	0	09AUG11	22AUG11	03FEB12	16FEB12	123
PR22142920	DOSTER REVIEW SUMP PUMPS	5	5	0	23AUG11	29AUG11	17FEB12	23FEB12	123
PR22142930	A&E APPROVE SUMP PUMPS	10	10	0	30AUG11	13SEP11	24FEB12	08MAR12	123
PR22142940	BCCO APPROVE SUMP PUMPS	5	5	0	14SEP11	20SEP11	09MAR12	15MAR12	123
PR22142950	FAB SUMP PUMPS	15	15	0	21SEP11	11OCT11	16MAR12	05APR12	123
PR22142960	DELIVER SUMP PUMPS	1	1	0	12OCT11	12OCT11	06APR12	06APR12	123
PR22330010	RECEIVE WATER HEATERS	10	10	0	09AUG11	22AUG11	07OCT11	20OCT11	42
PR22330020	DOSTER REVIEW WATER HEATERS	5	5	0	23AUG11	29AUG11	21OCT11	27OCT11	42
PR22330030	A&E APPROVE WATER HEATERS	10	10	0	30AUG11	13SEP11	28OCT11	10NOV11	42
PR22330040	BCCO APPROVE WATER HEATERS	5	5	0	14SEP11	20SEP11	11NOV11	17NOV11	42
PR22330050	FAB WATER HEATERS	20	20	0	21SEP11	18OCT11	18NOV11	19DEC11	42
PR22330060	DELIVER WATER HEATERS	1	1	0	19OCT11	19OCT11	20DEC11	20DEC11	42
PR22400010	RECEIVE PLUMBING FIXTURES	10	10	0	09AUG11	22AUG11	27FEB12	09MAR12	139

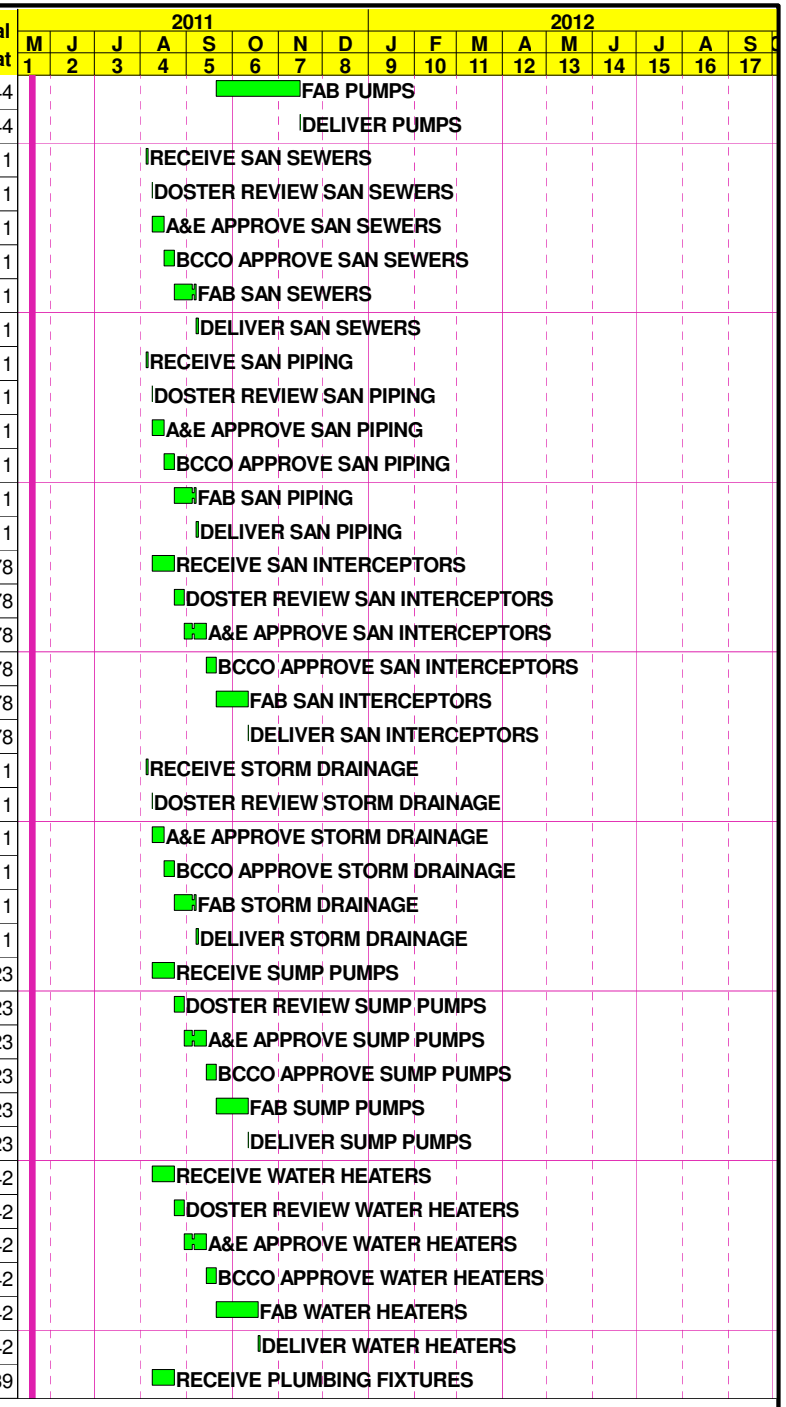

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR22400020	DOSTER REVIEW PLUMBING	5	5	0	23AUG11	29AUG11	12MAR12	16MAR12	139
PR22400030	A&E APPROVE PLUMBING FIXTURES	10	10	0	30AUG11	13SEP11	19MAR12	30MAR12	139
PR22400040	BCCO APPROVE PLUMBING	5	5	0	14SEP11	20SEP11	02APR12	06APR12	139
PR22400050	FAB PLUMBING FIXTURES	30	30	0	21SEP11	01NOV11	09APR12	18MAY12	139
PR22400060	DELIVER PLUMBING FIXTURES	1	1	0	02NOV11	02NOV11	21MAY12	21MAY12	139
PR22470010	RECEIVE WATER COOLERS	10	10	0	09AUG11	22AUG11	08MAR12	21MAR12	147
PR22470020	DOSTER REVIEW WATER COOLERS	5	5	0	23AUG11	29AUG11	22MAR12	28MAR12	147
PR22470030	A&E APPROVE WATER COOLERS	10	10	0	30AUG11	13SEP11	29MAR12	11APR12	147
PR22470040	BCCO APPROVE WATER COOLERS	5	5	0	14SEP11	20SEP11	12APR12	18APR12	147
PR22470050	FAB WATER COOLERS	20	20	0	21SEP11	18OCT11	19APR12	16MAY12	147
PR22470060	DELIVER WATER COOLERS	1	1	0	19OCT11	19OCT11	17MAY12	17MAY12	147
PR23051310	RECEIVE COMMON MECH	10	10	0	09AUG11	22AUG11	12OCT11	25OCT11	45
PR23051320	DOSTER REVIEW COMMON MECH	5	5	0	23AUG11	29AUG11	26OCT11	01NOV11	45
PR23051330	A&E APPROVE COMMO0N MECH	10	10	0	30AUG11	13SEP11	02NOV11	15NOV11	45
PR23051340	BCCO APPROVE COMMON MECH	5	5	0	14SEP11	20SEP11	16NOV11	22NOV11	45
PR23051350	FAB COMMON MECH	10	10	0	21SEP11	04OCT11	23NOV11	08DEC11	45
PR23051360	DELIVER COMMON MECH	1	1	0	05OCT11	05OCT11	09DEC11	09DEC11	45
PR23051910	RECEIVE METERS & GAUGES	10	10	0	09AUG11	22AUG11	15NOV11	30NOV11	69
PR23051920	DOSTER REVIEW- METERS &	5	5	0	23AUG11	29AUG11	01DEC11	07DEC11	69
PR23051930	A&E APPROVE METERS & GAUGES	10	10	0	30AUG11	13SEP11	08DEC11	21DEC11	69
PR23051940	BCCO APPROVE METERS & GAUGES	5	5	0	14SEP11	20SEP11	22DEC11	29DEC11	69
PR23051950	FAB METERS & GAUGES	15	15	0	21SEP11	11OCT11	30DEC11	20JAN12	69
PR23051960	DELIVER METERS & GAUGES	1	1	0	12OCT11	12OCT11	23JAN12	23JAN12	69
PR23052310	RECEIVE VALVES	10	10	0	09AUG11	22AUG11	21SEP11	04OCT11	30
PR23052320	DOSTER REVIEW- VALVES	5	5	0	23AUG11	29AUG11	05OCT11	11OCT11	30
PR23052330	A&E APPROVE VALVES	10	10	0	30AUG11	13SEP11	12OCT11	25OCT11	30
PR23052340	BCCO APPROVE VALVES	5	5	0	14SEP11	20SEP11	26OCT11	01NOV11	30
PR23052350	FAB VALVES	15	15	0	21SEP11	11OCT11	02NOV11	22NOV11	30
PR23052360	DELIVER VALVES	1	1	0	12OCT11	12OCT11	23NOV11	23NOV11	30
PR23052910	RECEIVE HANGERS SUPPORTS	10	10	0	09AUG11	22AUG11	06DEC11	19DEC11	82
PR23052920	DOSTER REVIEW HANGERS	5	5	0	23AUG11	29AUG11	20DEC11	27DEC11	82
PR23052930	A&E APPROVE HANGERS SUPPORTS	10	10	0	30AUG11	13SEP11	28DEC11	11JAN12	82
PR23052940	BCCO APPROVE HANGERS	5	5	0	14SEP11	20SEP11	12JAN12	18JAN12	82
PR23052950	FAB HANGERS SUPPORTS	10	10	0	21SEP11	04OCT11	19JAN12	01FEB12	82
PR23052960	DELIVER HANGERS SUPPORTS	1	1	0	05OCT11	05OCT11	02FEB12	02FEB12	82
PR23059310	RECEIVE T&B	10	10	0	25AUG11	08SEP11	30MAR12	12APR12	151
PR23059320	DOSTER REVIEW T&B	5	5	0	09SEP11	15SEP11	13APR12	19APR12	151
PR23059330	A&E APPROVE T&B	10	10	0	16SEP11	29SEP11	20APR12	03MAY12	151
PR23059340	BCCO APPROVE T&B	5	5	0	30SEP11	06OCT11	04MAY12	10MAY12	151

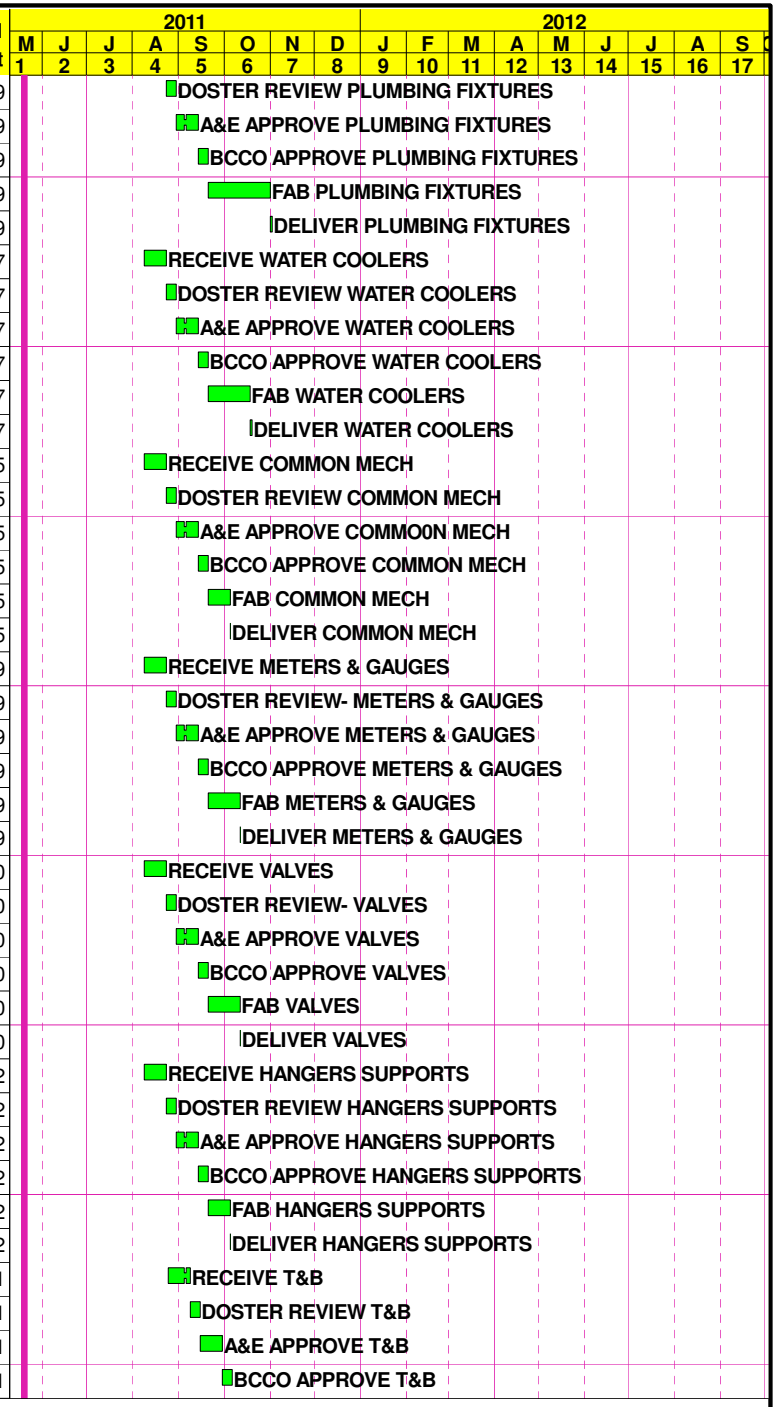

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

Sheet 21 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR23059350	FAB T&B	10	10	0	07OCT11	20OCT11	11MAY12	24MAY12	151
PR23059360	DELIVER T&B	1	1	0	21OCT11	21OCT11	25MAY12	25MAY12	151
PR23071310	RECEIVE DUCT INSULATION	10	10	0	09AUG11	22AUG11	01NOV11	14NOV11	59
PR23071320	DOSTER REVIEW DUCT INSULATION	5	5	0	23AUG11	29AUG11	15NOV11	21NOV11	59
PR23071330	A&E APPROVE DUCT INSULATION	10	10	0	30AUG11	13SEP11	22NOV11	07DEC11	59
PR23071340	BCCO APPROVE DUCT INSULATION	5	5	0	14SEP11	20SEP11	08DEC11	14DEC11	59
PR23071350	FAB DUCT INSULATION	10	10	0	21SEP11	04OCT11	15DEC11	29DEC11	59
PR23071360	DELIVER DUCT INSULATION	1	1	0	05OCT11	05OCT11	30DEC11	30DEC11	59
PR23071910	RECEIVE PIPING INSULATION	10	10	0	09AUG11	22AUG11	01NOV11	14NOV11	59
PR23071920	DOSTER REVIEW PIPING	5	5	0	23AUG11	29AUG11	15NOV11	21NOV11	59
PR23071930	A&E APPROVE PIPING INSULATION	10	10	0	30AUG11	13SEP11	22NOV11	07DEC11	59
PR23071940	BCCO APPROVE PIPING INSULATION	5	5	0	14SEP11	20SEP11	08DEC11	14DEC11	59
PR23071950	FAB PIPING INSULATION	10	10	0	21SEP11	04OCT11	15DEC11	29DEC11	59
PR23071960	DELIVER PIPING INSULATION	1	1	0	05OCT11	05OCT11	30DEC11	30DEC11	59
PR23090010	RECEIVE CONTROLS	10	10	0	09AUG11	22AUG11	18OCT11	31OCT11	49
PR23090020	DOSTER REVIEW CONTROLS	5	5	0	23AUG11	29AUG11	01NOV11	07NOV11	49
PR23090030	A&E APPROVE CONTROLS	10	10	0	30AUG11	13SEP11	08NOV11	21NOV11	49
PR23090040	BCCO APPROVE CONTROLS	5	5	0	14SEP11	20SEP11	22NOV11	30NOV11	49
PR23090050	FAB CONTROLS	20	20	0	21SEP11	18OCT11	01DEC11	29DEC11	49
PR23090060	DELIVER CONTROLS	1	1	0	19OCT11	19OCT11	30DEC11	30DEC11	49
PR23212310	RECEIVE PUMPS	10	10	0	09AUG11	22AUG11	25OCT11	07NOV11	54
PR23212320	DOSTER REVIEW PUMPS	5	5	0	23AUG11	29AUG11	08NOV11	14NOV11	54
PR23212330	A&E APPROVE PUMPS	10	10	0	30AUG11	13SEP11	15NOV11	30NOV11	54
PR23212340	BCCO APPROVE PUMPS	5	5	0	14SEP11	20SEP11	01DEC11	07DEC11	54
PR23212350	FAB PUMPS	30	30	0	21SEP11	01NOV11	08DEC11	20JAN12	54
PR23212360	DELIVER PUMPS	1	1	0	02NOV11	02NOV11	23JAN12	23JAN12	54
PR23311310	RECEIVE DUCT	10	10	0	09AUG11	22AUG11	18OCT11	31OCT11	49
PR23311320	DOSTER REVIEW DUCT	5	5	0	23AUG11	29AUG11	01NOV11	07NOV11	49
PR23311330	A&E APPROVE DUCT	10	10	0	30AUG11	13SEP11	08NOV11	21NOV11	49
PR23311340	BCCO APPROVE DUCT	5	5	0	14SEP11	20SEP11	22NOV11	30NOV11	49
PR23311350	FAB DUCT	20	20	0	21SEP11	18OCT11	01DEC11	29DEC11	49
PR23311360	DELIVER DUCT	1	1	0	19OCT11	19OCT11	30DEC11	30DEC11	49
PR23360010	RECEIVE AIR TERM	10	10	0	09AUG11	22AUG11	22AUG11	02SEP11	9
PR23360020	DOSTER REVIEW AIR TERM	5	5	0	23AUG11	29AUG11	06SEP11	12SEP11	9
PR23360030	A&E APPROVE AIR TERM	10	10	0	30AUG11	13SEP11	13SEP11	26SEP11	9
PR23360040	BCCO APPROVE AIR TERM	5	5	0	14SEP11	20SEP11	27SEP11	03OCT11	9
PR23360050	FAB AIR TERM	60	60	0	21SEP11	15DEC11	04OCT11	29DEC11	9
PR23360060	DELIVER AIR TERM	1	1	0	16DEC11	16DEC11	30DEC11	30DEC11	9
PR23642610	RECEIVE CHILLERS	10	10	0	09AUG11	22AUG11	08NOV11	21NOV11	64

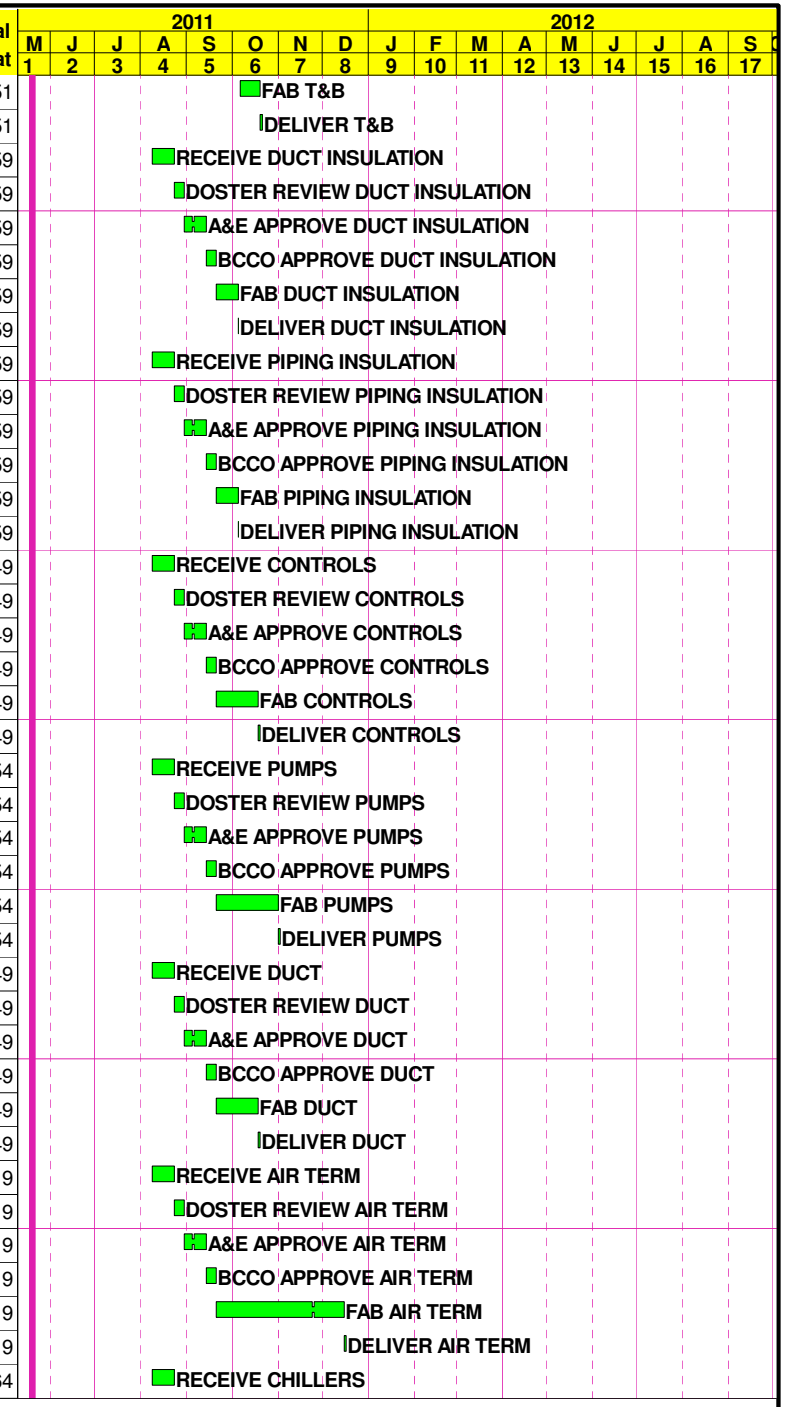

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

Sheet 22 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR23642620	DOSTER REVIEW CHILLERS	5	5	0	23AUG11	29AUG11	22NOV11	30NOV11	64
PR23642630	A&E APPROVE CHILLERS	10	10	0	30AUG11	13SEP11	01DEC11	14DEC11	64
PR23642640	BCCO APPROVE CHILLERS	5	5	0	14SEP11	20SEP11	15DEC11	21DEC11	64
PR23642650	FAB CHILLERS	60	60	0	21SEP11	15DEC11	22DEC11	16MAR12	64
PR23642660	DELIVER CHILLERS	1	1	0	16DEC11	16DEC11	19MAR12	19MAR12	64
PR23731310	RECEIVE AHU	10	10	0	09AUG11	22AUG11	13SEP11	26SEP11	24
PR23731320	DOSTER REVIEW AHU	5	5	0	23AUG11	29AUG11	27SEP11	03OCT11	24
PR23731330	A&E APPROVE AHU	10	10	0	30AUG11	13SEP11	04OCT11	17OCT11	24
PR23731340	BCCO APPROVE AHU	5	5	0	14SEP11	20SEP11	18OCT11	24OCT11	24
PR23731350	FAB AHU	60	60	0	21SEP11	15DEC11	25OCT11	20JAN12	24
PR23731360	DELIVER AHU	1	1	0	16DEC11	16DEC11	23JAN12	23JAN12	24
PR23812610	RECEIVE SPLIT SYS	10	10	0	09AUG11	22AUG11	13SEP11	26SEP11	24
PR23812620	DOSTER REVIEW- SPLIT SYS	5	5	0	23AUG11	29AUG11	27SEP11	03OCT11	24
PR23812630	A&E APPROVE SPILT SYS	10	10	0	30AUG11	13SEP11	04OCT11	17OCT11	24
PR23812640	BCCO APPROVE SPLIT SYS	5	5	0	14SEP11	20SEP11	18OCT11	24OCT11	24
PR23812650	FAB SPLIT SYS	60	60	0	21SEP11	15DEC11	25OCT11	20JAN12	24
PR23812660	DELIVER SPLIT SYS	1	1	0	16DEC11	16DEC11	23JAN12	23JAN12	24
PR26050010	RECEIVE COMMON ELE	10	10	0	09AUG11	22AUG11	28SEP11	11OCT11	35
PR26050020	DOSTER REVIEW COMMON ELE	5	5	0	23AUG11	29AUG11	12OCT11	18OCT11	35
PR26050030	A&E APPROVE COMMON ELE	10	10	0	30AUG11	13SEP11	19OCT11	01NOV11	35
PR26050040	BCCO APPROVE COMMON ELE	5	5	0	14SEP11	20SEP11	02NOV11	08NOV11	35
PR26050050	FAB COMMON ELE	10	10	0	21SEP11	04OCT11	09NOV11	22NOV11	35
PR26050060	DELIVER COMMON ELE	1	1	0	05OCT11	05OCT11	23NOV11	23NOV11	35
PR26051910	RECEIVE LOW VOLT	10	10	0	09AUG11	22AUG11	28SEP11	11OCT11	35
PR26051920	DOSTER REVIEW LOW VOLT	5	5	0	23AUG11	29AUG11	12OCT11	18OCT11	35
PR26051930	A&E APPROVE LOW VOLT	10	10	0	30AUG11	13SEP11	19OCT11	01NOV11	35
PR26051940	BCCO APPROVE LOW VOLT	5	5	0	14SEP11	20SEP11	02NOV11	08NOV11	35
PR26051950	FAB LOW VOLT	10	10	0	21SEP11	04OCT11	09NOV11	22NOV11	35
PR26051960	DELIVER LOW VOLT	1	1	0	05OCT11	05OCT11	23NOV11	23NOV11	35
PR26052910	RECEIVE HANGERS SUPPORTS	10	10	0	09AUG11	22AUG11	06DEC11	19DEC11	82
PR26052920	DOSTER REVIEW HANGERS	5	5	0	23AUG11	29AUG11	20DEC11	27DEC11	82
PR26052930	A&E APPROVE HANGER SUPPORTS	10	10	0	30AUG11	13SEP11	28DEC11	11JAN12	82
PR26052940	BCCO APPROVE HANGERS	5	5	0	14SEP11	20SEP11	12JAN12	18JAN12	82
PR26052950	FAB HANGERS SUPPORTS	10	10	0	21SEP11	04OCT11	19JAN12	01FEB12	82
PR26052960	DELIVER HANGERS SUPPORTS	1	1	0	05OCT11	05OCT11	02FEB12	02FEB12	82
PR26055310	RECEIVE ID	10	10	0	09AUG11	22AUG11	21MAR12	03APR12	156
PR26055320	DOSTER REVIEW ID	5	5	0	23AUG11	29AUG11	04APR12	10APR12	156
PR26055330	A&E APPROVE ID	10	10	0	30AUG11	13SEP11	11APR12	24APR12	156
PR26055340	BCCO APPROVE ID	5	5	0	14SEP11	20SEP11	25APR12	01MAY12	156

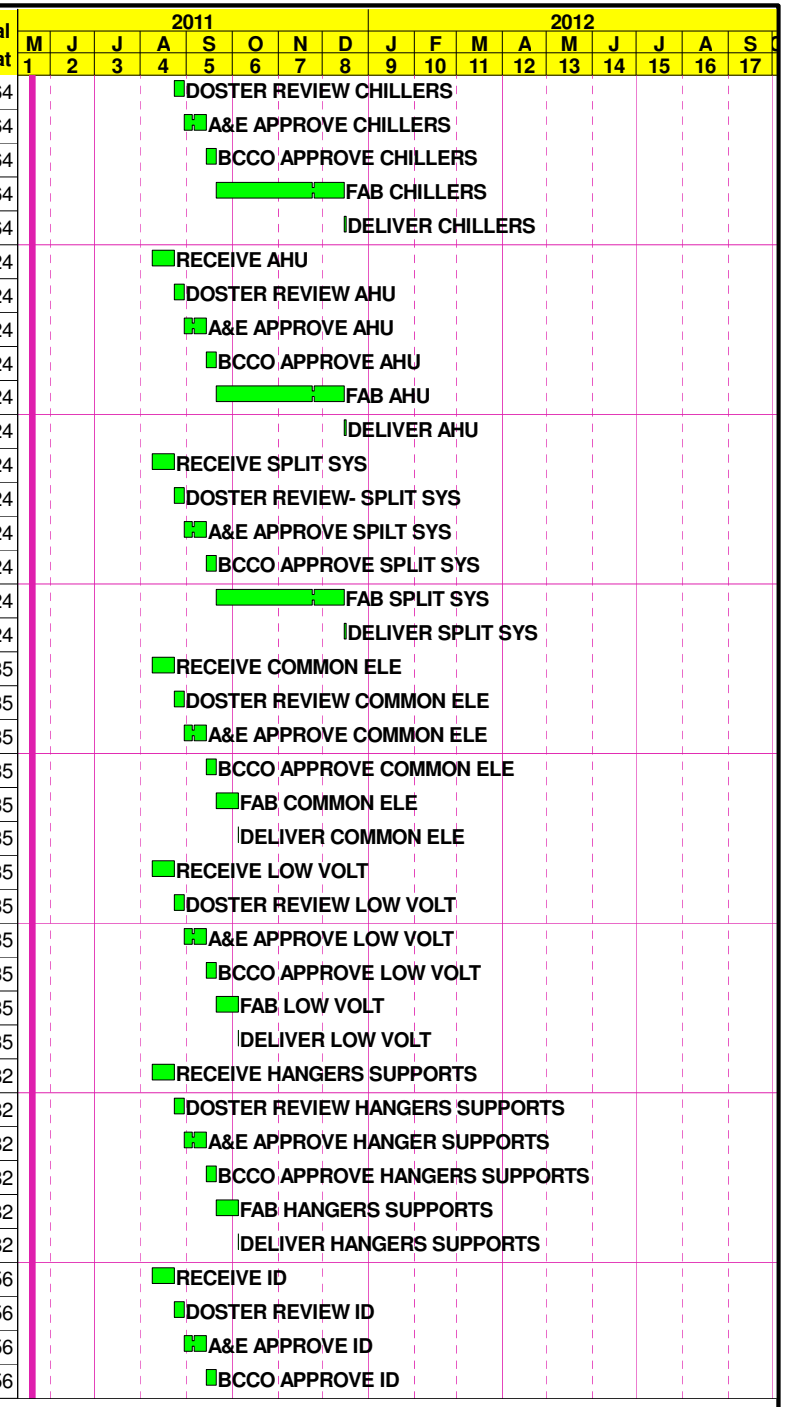

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR26055350	FAB ID	20	20	0	21SEP11	18OCT11	02MAY12	30MAY12	156
PR26055360	DELIVER ID	1	1	0	19OCT11	19OCT11	31MAY12	31MAY12	156
PR26057310	RECEIVE CORD STUDY	10	10	0	09AUG11	22AUG11	01DEC11	14DEC11	79
PR26057320	DOSTER REVIEW CORD STUDY	5	5	0	23AUG11	29AUG11	15DEC11	21DEC11	79
PR26057330	A&E APPROVE CORD STUDY	10	10	0	30AUG11	13SEP11	22DEC11	06JAN12	79
PR26057340	BCCO APPROVE CORD STUDY	5	5	0	14SEP11	20SEP11	09JAN12	13JAN12	79
PR26057350	FAB CORD STUDY	20	20	0	21SEP11	18OCT11	16JAN12	10FEB12	79
PR26057360	DELIVER CORD STUDY	1	1	0	19OCT11	19OCT11	13FEB12	13FEB12	79
PR26220010	RECEIVE TRANSFORMERS	10	10	0	09AUG11	22AUG11	09SEP11	22SEP11	22
PR26220020	DOSTER REVIEW TRANSFORMERS	5	5	0	23AUG11	29AUG11	23SEP11	29SEP11	22
PR26220030	A&E APPROVE TRANSFORMERS	10	10	0	30AUG11	13SEP11	30SEP11	13OCT11	22
PR26220040	BCCO APPROVE TRANS FORMERS	5	5	0	14SEP11	20SEP11	14OCT11	20OCT11	22
PR26220050	FAB TRANSFORMERS	40	40	0	21SEP11	15NOV11	21OCT11	19DEC11	22
PR26220060	DELIVER TRANSFORMERS	1	1	0	16NOV11	16NOV11	20DEC11	20DEC11	22
PR26241610	RECEIVE PANELS	10	10	0	09AUG11	22AUG11	01DEC11	14DEC11	79
PR26241620	DOSTER REVIEW PANELS	5	5	0	23AUG11	29AUG11	15DEC11	21DEC11	79
PR26241630	A&E APPROVE PANELS	10	10	0	30AUG11	13SEP11	22DEC11	06JAN12	79
PR26241640	BCCO APPROVE PANELS	5	5	0	14SEP11	20SEP11	09JAN12	13JAN12	79
PR26241650	FAB PANELS	20	20	0	21SEP11	18OCT11	16JAN12	10FEB12	79
PR26241660	DELIVER PANELS	1	1	0	19OCT11	19OCT11	13FEB12	13FEB12	79
PR26291310	RECEIVE ENCLOSED CONTROLLERS	10	10	0	09AUG11	22AUG11	01DEC11	14DEC11	79
PR26291320	DOSTER REVIEW ENCLOSED	5	5	0	23AUG11	29AUG11	15DEC11	21DEC11	79
PR26291330	A&E APPROVE ENCLOSED	10	10	0	30AUG11	13SEP11	22DEC11	06JAN12	79
PR26291340	BCCO APPROVE ENCLOSED	5	5	0	14SEP11	20SEP11	09JAN12	13JAN12	79
PR26291350	FAB ENCLOSED CONTROLLERS	20	20	0	21SEP11	18OCT11	16JAN12	10FEB12	79
PR26291360	DELIVER ENCLOSED CONTROLLERS	1	1	0	19OCT11	19OCT11	13FEB12	13FEB12	79
PR26292310	RECEIVE VFD	10	10	0	09AUG11	22AUG11	25OCT11	07NOV11	54
PR26292320	DOSTER REVIEW VFD	5	5	0	23AUG11	29AUG11	08NOV11	14NOV11	54
PR26292330	A&E APPROVE VFD	10	10	0	30AUG11	13SEP11	15NOV11	30NOV11	54
PR26292340	BCCO APPROVE VFD	5	5	0	14SEP11	20SEP11	01DEC11	07DEC11	54
PR26292350	FAB VFD	30	30	0	21SEP11	01NOV11	08DEC11	20JAN12	54
PR26292360	DELIVER VFD	1	1	0	02NOV11	02NOV11	23JAN12	23JAN12	54
PR26411310	RECEIVE LT PROTECTION	10	10	0	09AUG11	22AUG11	09AUG11	22AUG11	0
PR26411320	DOSTER REVIEW LT PROTECTION	5	5	0	23AUG11	29AUG11	23AUG11	29AUG11	0
PR26411330	A&E APPROVE LT PROTECTION	10	10	0	30AUG11	13SEP11	30AUG11	13SEP11	0
PR26411340	BCCO APPROVE LT PROTECTION	5	5	0	14SEP11	20SEP11	14SEP11	20SEP11	0
PR26411350	FAB LT PROTECTION	10	10	0	21SEP11	04OCT11	19APR12	02MAY12	147
PR26411355	FAB UG LT PROTECTION	1	1	0	21SEP11	21SEP11	21SEP11	21SEP11	0
PR26411360	DELIVER LT PROTECTION	1	1	0	05OCT11	05OCT11	03MAY12	03MAY12	147

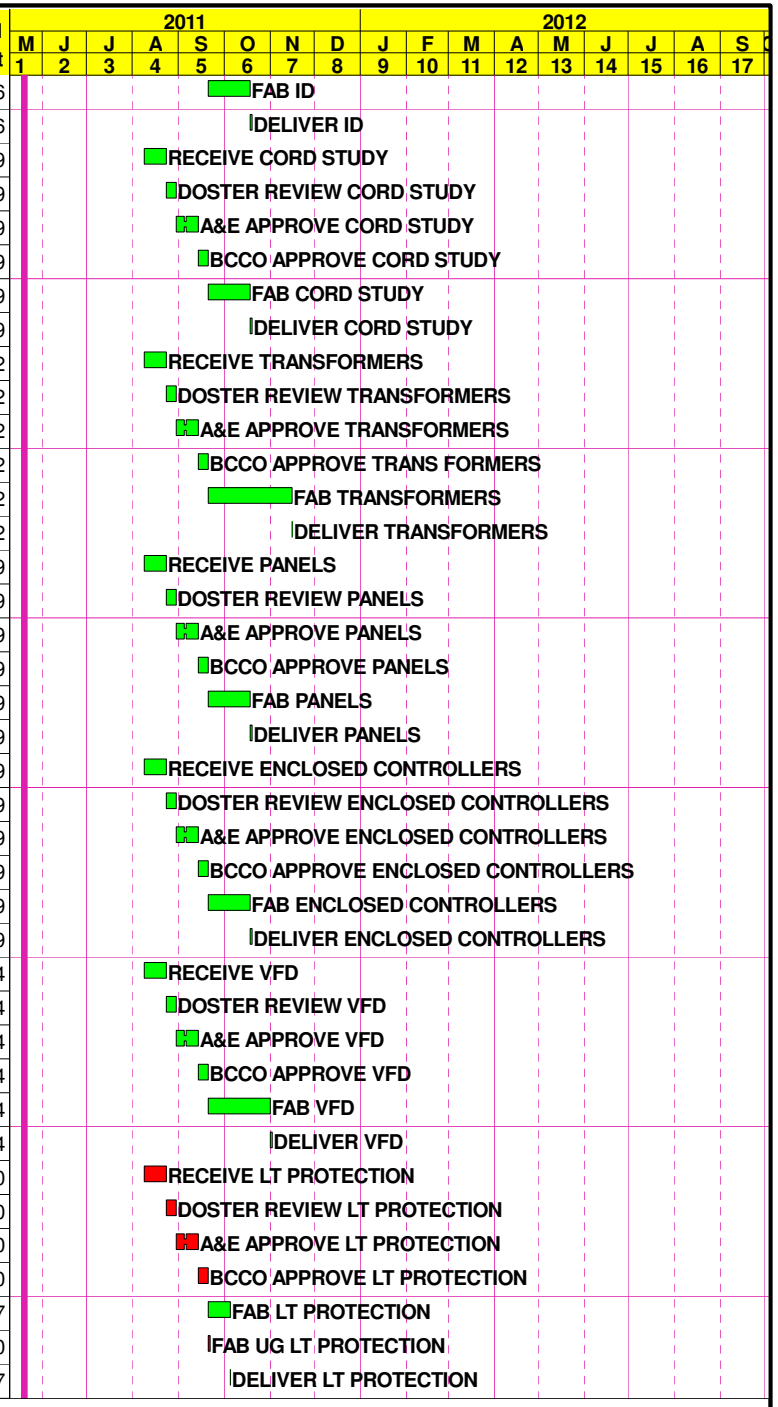

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

Sheet 24 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR26411365	DELIVER LT PROTECTION UG	1	1	0	22SEP11	22SEP11	22SEP11	22SEP11	0
PR26510010	RECEIVE INT LIGHTING	10	10	0	09AUG11	22AUG11	30NOV11	13DEC11	78
PR26510020	DOSTER REVIEW INT LIGHTING	5	5	0	23AUG11	29AUG11	14DEC11	20DEC11	78
PR26510030	A&E APPROVE INT LIGHTING	10	10	0	30AUG11	13SEP11	21DEC11	05JAN12	78
PR26510040	BCCO APPROVE IN LIGHTING	5	5	0	14SEP11	20SEP11	06JAN12	12JAN12	78
PR26510050	FAB INT LIGHTING	40	40	0	21SEP11	15NOV11	13JAN12	08MAR12	78
PR26510060	DELIVER INT LIGHTING	1	1	0	16NOV11	16NOV11	09MAR12	09MAR12	78
PR26560010	RECEIVE EXT LIGHTING	10	10	0	09AUG11	22AUG11	22DEC11	06JAN12	94
PR26560020	DOSTER REVIEW EXT LIGHTING	5	5	0	23AUG11	29AUG11	09JAN12	13JAN12	94
PR26560030	A&E APPROVE EXT LIGHTING	10	10	0	30AUG11	13SEP11	16JAN12	27JAN12	94
PR26560040	BCCO APPROVE EXT LIGHTING	5	5	0	14SEP11	20SEP11	30JAN12	03FEB12	94
PR26560050	FAB EXT LIGHTING	40	40	0	21SEP11	15NOV11	06FEB12	30MAR12	94
PR26560060	DELIVER EXT LIGHTING	1	1	0	16NOV11	16NOV11	02APR12	02APR12	94
PR27050010	RECEIVE COM COMMON	10	10	0	09AUG11	22AUG11	28SEP11	11OCT11	35
PR27050020	DOSTER REVIEW COM COMMON	5	5	0	23AUG11	29AUG11	12OCT11	18OCT11	35
PR27050030	A&E APPROVE COM COMMON	10	10	0	30AUG11	13SEP11	19OCT11	01NOV11	35
PR27050040	BCCO APPROVE COM COMMON	5	5	0	14SEP11	20SEP11	02NOV11	08NOV11	35
PR27050050	FAB COM COMMON	10	10	0	21SEP11	04OCT11	09NOV11	22NOV11	35
PR27050060	DELIVER COM COMMON	1	1	0	05OCT11	05OCT11	23NOV11	23NOV11	35
PR27412010	RECEIVE AV EQ	10	10	0	09AUG11	22AUG11	19OCT11	01NOV11	50
PR27412020	DOSTER REVIEW AV EQ	5	5	0	23AUG11	29AUG11	02NOV11	08NOV11	50
PR27412030	A&E APPROVE AV EQ	10	10	0	30AUG11	13SEP11	09NOV11	22NOV11	50
PR27412040	BCCO APPROVE AV EQ	5	5	0	14SEP11	20SEP11	23NOV11	01DEC11	50
PR27412050	FAB AV EQ	60	60	0	21SEP11	15DEC11	02DEC11	27FEB12	50
PR27412060	DELIVER AV EQ	1	1	0	16DEC11	16DEC11	28FEB12	28FEB12	50
PR27416010	RECEIVE MULTIMEDIA SYS	10	10	0	09AUG11	22AUG11	12JAN12	25JAN12	107
PR27416020	DOSTER REVIEW MULTIMEDIA SYS	5	5	0	23AUG11	29AUG11	26JAN12	01FEB12	107
PR27416030	A&E APPROVE MULTIMEDIA SYS	10	10	0	30AUG11	13SEP11	02FEB12	15FEB12	107
PR27416040	BCCO APPROVE MULTIMEDIA SYS	5	5	0	14SEP11	20SEP11	16FEB12	22FEB12	107
PR27416050	FAB MULTI MEDIA SYS	60	60	0	21SEP11	15DEC11	23FEB12	16MAY12	107
PR27416060	DELIVER MULTI MEDIA SYS	1	1	0	16DEC11	16DEC11	17MAY12	17MAY12	107
PR27512310	RECEIVE INTERCOM	10	10	0	09AUG11	22AUG11	30NOV11	13DEC11	78
PR27512320	DOSTER REVIEW INTERCOM	5	5	0	23AUG11	29AUG11	14DEC11	20DEC11	78
PR27512330	A&E APPROVE INTERCOM	10	10	0	30AUG11	13SEP11	21DEC11	05JAN12	78
PR27512340	BCCO APPROVE INTERCOM	5	5	0	14SEP11	20SEP11	06JAN12	12JAN12	78
PR27512350	FAB INTERCOM	40	40	0	21SEP11	15NOV11	13JAN12	08MAR12	78
PR27512360	DELIVER INTERCOM	1	1	0	16NOV11	16NOV11	09MAR12	09MAR12	78
PR28131010	RECEIVE ACCESS CONT	10	10	0	09AUG11	22AUG11	14SEP11	27SEP11	25
PR28131020	DOSTER REVIEW ACCESS CONT	5	5	0	23AUG11	29AUG11	28SEP11	04OCT11	25

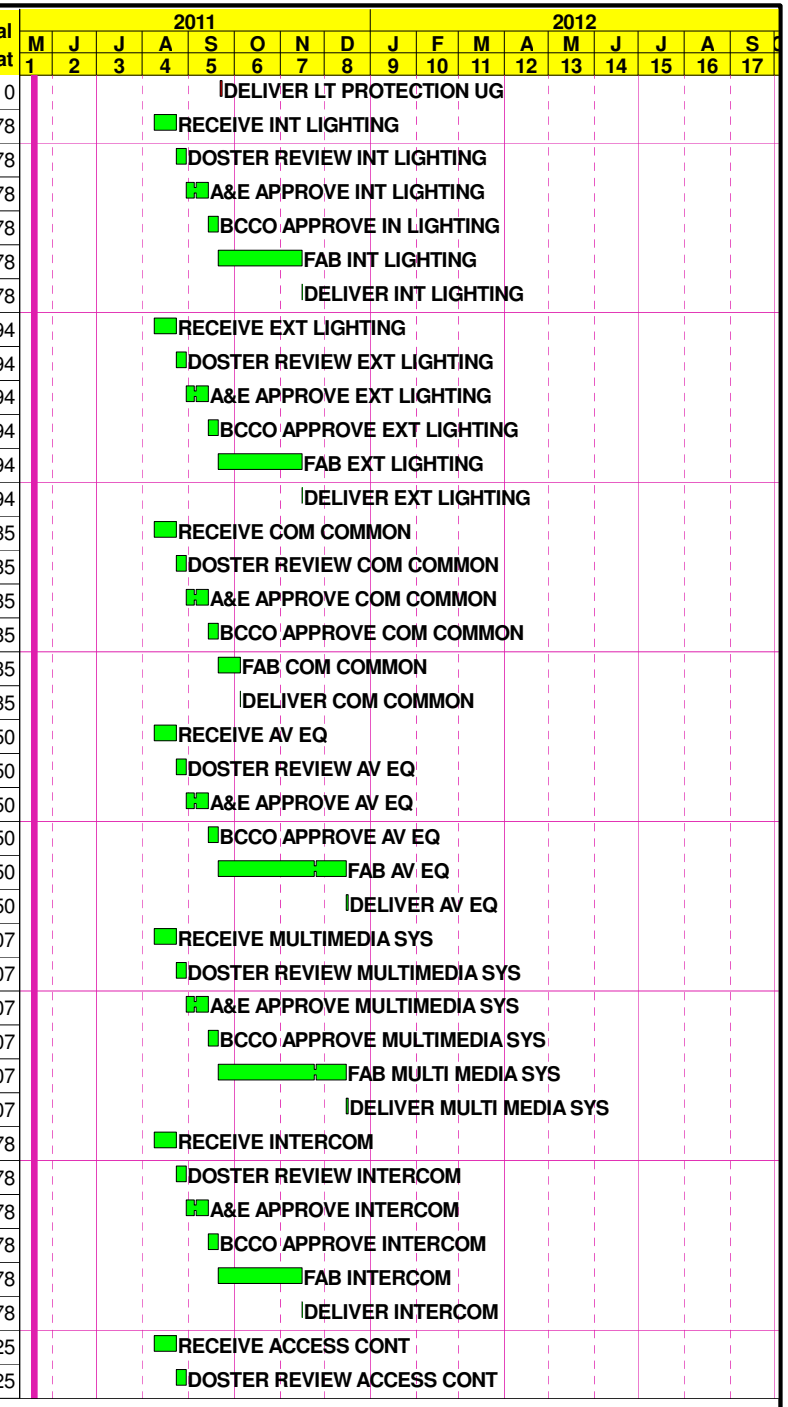

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR28131030	A&E APPROVE ACCESS CONT	10	10	0	30AUG11	13SEP11	05OCT11	18OCT11	25
PR28131040	BCCO APROVE ACCESS CONT	5	5	0	14SEP11	20SEP11	19OCT11	25OCT11	25
PR28131050	FAB ACCESS CONT	20	20	0	21SEP11	18OCT11	26OCT11	22NOV11	25
PR28131060	DELIVER ACCESS CONT	1	1	0	19OCT11	19OCT11	23NOV11	23NOV11	25
PR28131510	RECEIVE CCTV	10	10	0	09AUG11	22AUG11	14SEP11	27SEP11	25
PR28131520	DOSTER REVIEW CCTV	5	5	0	23AUG11	29AUG11	28SEP11	04OCT11	25
PR28131530	A&E APPROVE CCTV	10	10	0	30AUG11	13SEP11	05OCT11	18OCT11	25
PR28131540	BCCO APPROVE CCTV	5	5	0	14SEP11	20SEP11	19OCT11	25OCT11	25
PR28131550	FAB CCTV	20	20	0	21SEP11	18OCT11	26OCT11	22NOV11	25
PR28131560	DELIVER CCTV	1	1	0	19OCT11	19OCT11	23NOV11	23NOV11	25
PR28161610	RECEIVE SECURITY	10	10	0	14JUN11	27JUN11	09JAN12	20JAN12	143
PR28161620	DOSTER REVIEW SECURITY	5	5	0	28JUN11	05JUL11	23JAN12	27JAN12	143
PR28161630	A&E APPROVE SECURITY	10	10	0	06JUL11	19JUL11	30JAN12	10FEB12	143
PR28161640	BCCO APPROVE SECURITY	5	5	0	20JUL11	26JUL11	13FEB12	17FEB12	143
PR28161650	FAB SECURITY	20	20	0	27JUL11	23AUG11	20FEB12	16MAR12	143
PR28161660	DELIVER SECURITY	1	1	0	24AUG11	24AUG11	08MAY12	08MAY12	179
PR28310010	RECEIVE FIRE ALARM	10	10	0	09AUG11	22AUG11	08MAR12	21MAR12	147
PR28310020	DOSTER REVIEW FIRE ALARM	5	5	0	23AUG11	29AUG11	22MAR12	28MAR12	147
PR28310030	A&E APPROVE FIRE ALARM	10	10	0	30AUG11	13SEP11	29MAR12	11APR12	147
PR28310040	BCCO APPROVE FIRE ALARM	5	5	0	14SEP11	20SEP11	12APR12	18APR12	147
PR28310050	FAB FIRE ALARM	20	20	0	21SEP11	18OCT11	19APR12	16MAY12	147
PR28310060	DELIVER FIRE ALARM	1	1	0	19OCT11	19OCT11	17MAY12	17MAY12	147
PR31311610	RECEIVE TERMITE	3	3	0	09AUG11	11AUG11	16AUG11	18AUG11	5
PR31311620	DOSTER REVIEW TERMITE	2	2	0	12AUG11	15AUG11	19AUG11	22AUG11	5
PR31311630	A&E APPROVE TERMITE	10	10	0	16AUG11	29AUG11	23AUG11	06SEP11	5
PR31311640	BCCO APPROVE TERMITE	5	5	0	30AUG11	06SEP11	07SEP11	13SEP11	5
PR31311650	FAB TERMITE	2	2	0	07SEP11	08SEP11	14SEP11	15SEP11	5
PR31311660	DELIVER TERMITE	1	1	0	09SEP11	09SEP11	16SEP11	16SEP11	5
PR32121610	RECEIVE ASPHALT	10	10	0	05AUG11	18AUG11	23DEC11	09JAN12	97
PR32121620	DOSTER REVIEW ASPHALT	5	5	0	19AUG11	25AUG11	10JAN12	16JAN12	97
PR32121630	A&E APPROVE ASPHALT	10	10	0	26AUG11	09SEP11	17JAN12	30JAN12	97
PR32121640	BCCO APPROVE ASPHALT	5	5	0	12SEP11	16SEP11	31JAN12	06FEB12	97
PR32121650	FAB ASPHALT	10	10	0	19SEP11	30SEP11	07FEB12	20FEB12	97
PR32121660	DELIVER ASPHALT	1	1	0	03OCT11	03OCT11	21FEB12	21FEB12	97
PR32311310	RECEIVE FENCING	10	10	0	25AUG11	08SEP11	18APR12	01MAY12	164
PR32311320	DOSTER REVIEW FENCING	5	5	0	09SEP11	15SEP11	02MAY12	08MAY12	164
PR32311330	A&E APPROVE FENCING	10	10	0	16SEP11	29SEP11	09MAY12	22MAY12	164
PR32311340	BCCO APPROVE FENCING	5	5	0	30SEP11	06OCT11	23MAY12	30MAY12	164
PR32311350	FAB FENCING	20	20	0	07OCT11	03NOV11	31MAY12	27JUN12	164

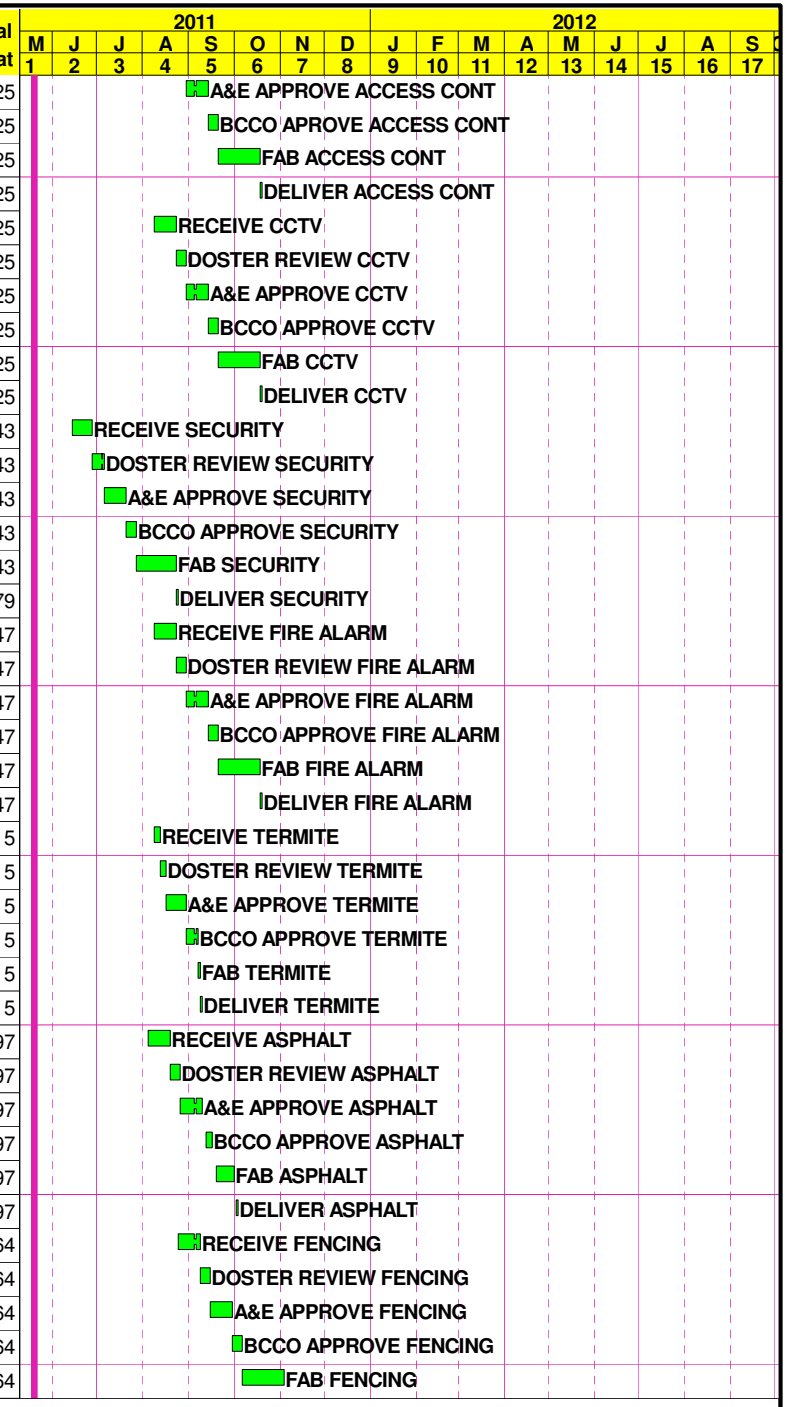

Start Date 20MAY11
Finish Date 30AUG12
Data Date 20MAY11
Run Date 12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0 Sheet 26 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR32311360	DELIVER FENCING	1	1	0	04NOV11	04NOV11	28JUN12	28JUN12	164
PR32311910	RECEIVE DEC FENCE	10	10	0	25AUG11	08SEP11	26MAR12	06APR12	147
PR32311920	DOSTER REVIEW DEC FENCE	5	5	0	09SEP11	15SEP11	09APR12	13APR12	147
PR32311930	A&E APPROVE DEC FENCE	10	10	0	16SEP11	29SEP11	16APR12	27APR12	147
PR32311940	BCCO APPROVE DEC FENCE	5	5	0	30SEP11	06OCT11	30APR12	04MAY12	147
PR32311950	FAB DEC FENCE	20	20	0	07OCT11	03NOV11	07MAY12	04JUN12	147
PR32311960	DELIVER DEC FENCE	1	1	0	04NOV11	04NOV11	05JUN12	05JUN12	147
PR32840010	RECEIVE IRRIGATION	10	10	0	25AUG11	08SEP11	28NOV11	09DEC11	64
PR32840020	DOSTER REVIEW IRRIGATION	5	5	0	09SEP11	15SEP11	12DEC11	16DEC11	64
PR32840030	A&E APPROVE IRRIGATION	10	10	0	16SEP11	29SEP11	19DEC11	03JAN12	64
PR32840040	BCCO APPROVE IRRIGATION	5	5	0	30SEP11	06OCT11	04JAN12	10JAN12	64
PR32840050	FAB IRRIGATION	10	10	0	07OCT11	20OCT11	11JAN12	24JAN12	64
PR32840060	DELIVER IRRIGATION	1	1	0	21OCT11	21OCT11	25JAN12	25JAN12	64
PR32920010	RECEIVE GRASSES	10	10	0	25AUG11	08SEP11	09DEC11	22DEC11	73
PR32920020	DOSTER REVIEW- GRASSES	5	5	0	09SEP11	15SEP11	23DEC11	30DEC11	73
PR32920030	A&E APPROVE GRASSES	10	10	0	16SEP11	29SEP11	03JAN12	16JAN12	73
PR32920040	BCCO APPROVE GRASSES	5	5	0	30SEP11	06OCT11	17JAN12	23JAN12	73
PR32920050	FAB GRASSES	15	15	0	07OCT11	27OCT11	24JAN12	13FEB12	73
PR32920060	DELIVER GRASSES	1	1	0	28OCT11	28OCT11	14FEB12	14FEB12	73
PR32930010	RECEIVE PLANTS	10	10	0	25AUG11	08SEP11	09DEC11	22DEC11	73
PR32930020	DOSTER REVIEW PLANTS	5	5	0	09SEP11	15SEP11	23DEC11	30DEC11	73
PR32930030	A&E APPROVE PLANTS	10	10	0	16SEP11	29SEP11	03JAN12	16JAN12	73
PR32930040	BCCO APPROVE PLANTS	5	5	0	30SEP11	06OCT11	17JAN12	23JAN12	73
PR32930050	FAB PLANTS	15	15	0	07OCT11	27OCT11	24JAN12	13FEB12	73
PR32930060	DELIVER PLANTS	1	1	0	28OCT11	28OCT11	14FEB12	14FEB12	73
PR33410010	RECEIVE STORM UTILITY	1	1	0	05AUG11	05AUG11	15AUG11	15AUG11	6
PR33410020	DOSTER REVIEW STORM UTILITY	1	1	0	08AUG11	08AUG11	16AUG11	16AUG11	6
PR33410030	A&E APPROVE STORM UTILITY	5	5	0	09AUG11	15AUG11	17AUG11	23AUG11	6
PR33410040	BCCO APPROVE STORM UTILITY	5	5	0	16AUG11	22AUG11	24AUG11	30AUG11	6
PR33410050	FAB STORM UTILITY	5	5	0	23AUG11	29AUG11	31AUG11	07SEP11	6
PR33410060	DELIVER STORM UTILITY	1	1	0	30AUG11	30AUG11	08SEP11	08SEP11	6
PR33411010	RECEIVE EXFILTRATION	10	10	0	05AUG11	18AUG11	30AUG11	13SEP11	17
PR33411020	DOSTER REVIEW EXFILTRATION	5	5	0	19AUG11	25AUG11	14SEP11	20SEP11	17
PR33411030	A&E APPROVE EXFILTRATION	10	10	0	26AUG11	09SEP11	21SEP11	04OCT11	17
PR33411040	BCCO APPROVE EXFILTRATION	5	5	0	12SEP11	16SEP11	05OCT11	11OCT11	17
PR33411050	FAB EXFILTRATION	10	10	0	19SEP11	30SEP11	12OCT11	25OCT11	17
PR33411060	DELIVER EXFILTRATION	1	1	0	03OCT11	03OCT11	26OCT11	26OCT11	17
PR33412010	RECEIVE SHEET PILING	10	10	0	05AUG11	18AUG11	18AUG11	31AUG11	9
PR33412020	DOSTER REVIEW SHEET PILING	5	5	0	19AUG11	25AUG11	01SEP11	08SEP11	9

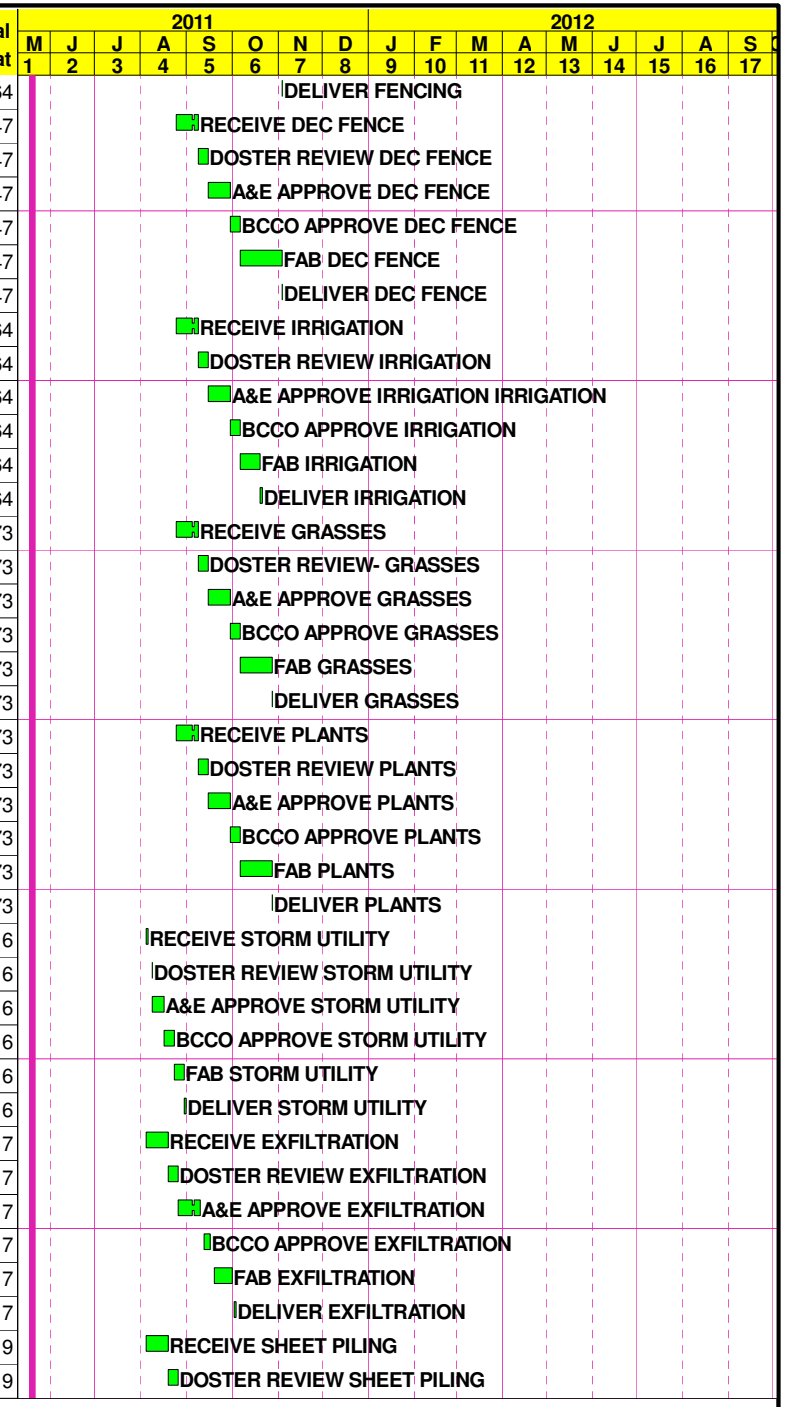

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

Sheet 27 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
PR33412030	A&E APPROVE SHEET PILING	10	10	0	26AUG11	09SEP11	09SEP11	22SEP11	9
PR33412040	BCCO APPROVE SHEET PILING	5	5	0	12SEP11	16SEP11	23SEP11	29SEP11	9
PR33412050	FAB SHEET PILING	10	10	0	19SEP11	30SEP11	30SEP11	13OCT11	9
PR33412060	DELIVER SHEET PILING	1	1	0	03OCT11	03OCT11	14OCT11	14OCT11	9
PR33413010	RECEIVE IMPORT FILL	1	1	0	05AUG11	05AUG11	05AUG11	05AUG11	0
PR33413020	DOSTER REVIEW IMPORT FILL	1	1	0	08AUG11	08AUG11	08AUG11	08AUG11	0
PR33413030	A&E APPROVE IMPORT FILL	10	10	0	09AUG11	22AUG11	09AUG11	22AUG11	0
PR33413040	BCCO APPROVE IMPORT FILL	5	5	0	23AUG11	29AUG11	23AUG11	29AUG11	0
PR33413050	FAB IMPORT FILL	1	1	0	30AUG11	30AUG11	30AUG11	30AUG11	0
PR33413060	DELIVER IMPORT FILL	1	1	0	31AUG11	31AUG11	31AUG11	31AUG11	0
CONSTRUCTION									
SITE									
EARLY SITE & DEMOLITION									
SDE2000	REMOVE PORTABLES BY OCPS	6	6	0	28JUN11	06JUL11	13JUL11	20JUL11	10
SDE2010	DEMOLISH PORTABLES P-006, P-023,	2	2	0	08AUG11	09AUG11	09AUG11	10AUG11	1
SDE2020	DEMOLISH BLD 2	4	4	0	19JUL11	22JUL11	28JUL11	02AUG11	7
SDE2030	DEMOLISH BLD 4	2	2	0	25JUL11	26JUL11	03AUG11	04AUG11	7
SDE2040	DEMOLISH BLD 5	1	1	0	26JUL11	26JUL11	10AUG11	10AUG11	11
SDE2050	DEMOLISH BLD 7	2	2	0	29JUL11	01AUG11	09AUG11	10AUG11	7
SDE2060	DEMOLISH BLD 9	2	2	0	27JUL11	28JUL11	05AUG11	08AUG11	7
SDE2070	DEMOLISH PARTIAL KITCHEN	5	5	0	12JUL11	18JUL11	04AUG11	10AUG11	17
SDE2075	REMOVE TREES	5	5	0	12JUL11	18JUL11	21JUL11	27JUL11	7
SDE2090	REMOVE ALL FOOTINGS AND	2	2	0	10AUG11	11AUG11	11AUG11	12AUG11	1
SDE2120	REMOVE EXISTING FENCING	2	2	0	29JUN11	30JUN11	11JUL11	12JUL11	7
SPS2000	LOCATE UTILITIES	2	2	0	24JUN11	27JUN11	07JUL11	08JUL11	8
SPS2020	INSTALL PARAMETER 8'-0" FENCING	3	3	0	29JUN11	01JUL11	11JUL11	13JUL11	7
SPS2030	SWPP APPROVED & IN PLACE	5	5	0	01JUL11	08JUL11	13JUL11	19JUL11	7
SPS2040	IDENTIFY TREES TO REMAIN	2	2	0	05JUL11	06JUL11	18JUL11	19JUL11	9
SPS2050	DISCONNECT UTILITIES TO	3	3	0	28JUN11	30JUN11	15JUL11	19JUL11	12
SPS2100	INSTALL TEMP WEATHER	2	2	0	24JUN11	27JUN11	11JUL11	12JUL11	10
SPS2110	TREE PROTECTION	2	2	0	07JUL11	08JUL11	02AUG11	03AUG11	18
PREP SITE									
SPS2010	MOBILIZE CM TRAILER	0	0	0		19AUG11		26AUG11	5
SPS2060	TEMP POWER TO SITE	3	3	0	17AUG11	19AUG11	24AUG11	26AUG11	5
SPS2070	TEMP POWER TO BUILDING 1A	2	2	0	22AUG11	23AUG11	29AUG11	30AUG11	5
SPS2080	DISCONNECT UTILITIES TO	1	1	0	24AUG11	24AUG11	31AUG11	31AUG11	5
SPS2090	DISCONNECT POWER TO EXISTING	1	1	0	22AUG11	22AUG11	31AUG11	31AUG11	7
SPS2130	INSTALL FDOT SOIL TRACKING	1	1	0	05AUG11	05AUG11	08AUG11	08AUG11	1

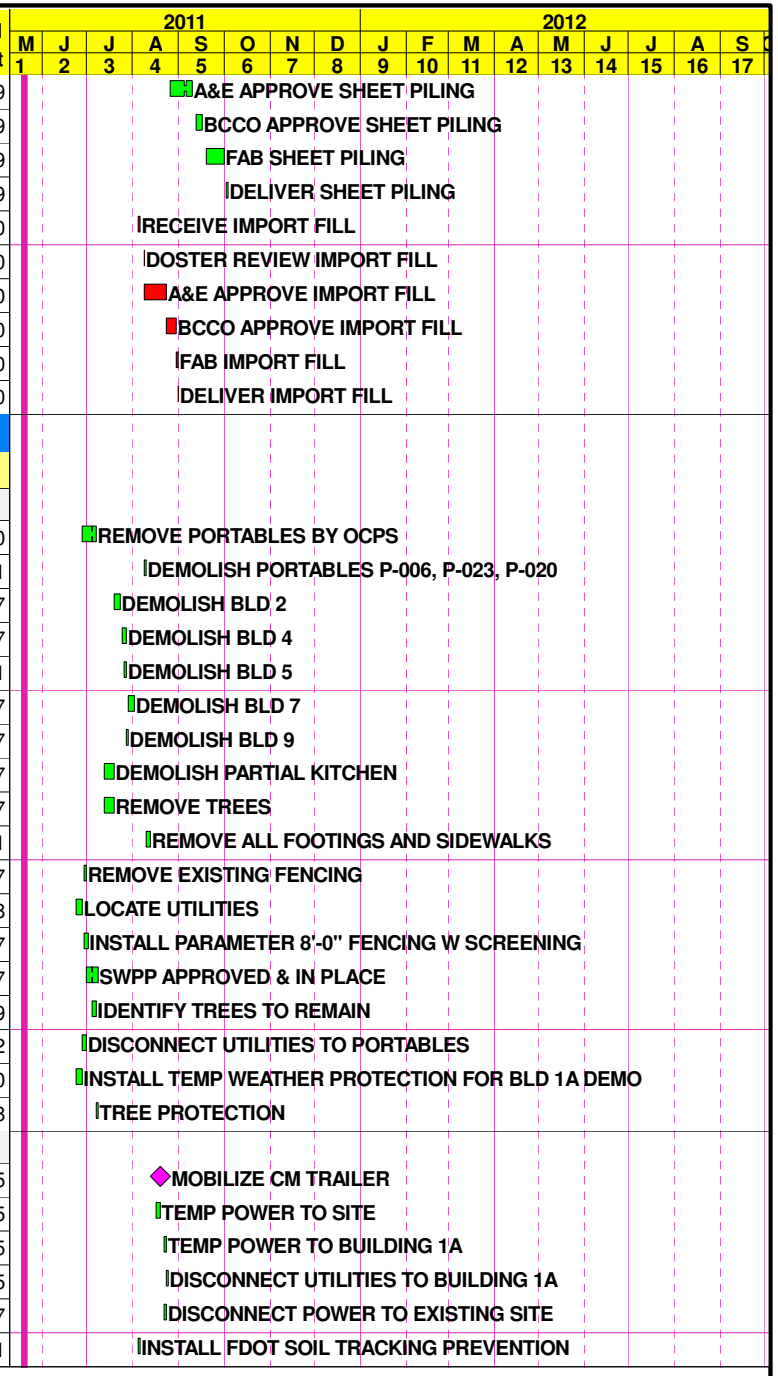

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

Sheet 28 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
SITE DEMOLITION									
SDE2080	REMOVE TREE STUMPS	5	5	0	15AUG11	19AUG11	16AUG11	22AUG11	1
SDE2100	REMOVE UNDERGROUND UTILITIES	10	10	0	22AUG11	02SEP11	23AUG11	06SEP11	1
SDE2110	REMOVE ARIAL UTILITIES	3	3	0	23AUG11	25AUG11	01SEP11	06SEP11	7
SDE2130	REMOVE PARKING WEST	2	2	0	06SEP11	07SEP11	07SEP11	08SEP11	1
SDE2140	REMOVE PARKING EAST	2	2	0	08SEP11	09SEP11	22SEP11	23SEP11	10
SDE2150	REMOVE GREASE TRAP	2	2	0	12SEP11	13SEP11	26SEP11	27SEP11	10
SDE2160	REMOVE MDP, TRANS, & PADS	2	2	0	06SEP11	07SEP11	07SEP11	08SEP11	1
DEVELOP SITE / UTILITIES									
SDS1000	IMPORT FILL FOR BLD PAD 2B	10	10	0	01SEP11	15SEP11	01SEP11	15SEP11	0
SDS1003	INSTALL STORM E&W BLD 2	5	5	0	08SEP11	14SEP11	09SEP11	15SEP11	1
SDS1005	PREP AND GRADE CASTING BED	3	3	0	03OCT11	05OCT11	05OCT11	07OCT11	2
SDS1010	INSTALL SANITARY STORM E BLD2	5	5	0	08SEP11	14SEP11	09SEP11	15SEP11	1
SDS1011	PREP AND GRADE CASTING BED	3	3	0	03OCT11	05OCT11	05OCT11	07OCT11	2
SDS1012	REMOVE CASTING BEDS	1	1	0	11JAN12	11JAN12	24JAN12	24JAN12	9
SDS1013	INSTALL REMAINING STROM	10	10	0	11JAN12	24JAN12	23JAN12	03FEB12	8
SDS1014	INSTALL REMAINING SANITARY	5	5	0	25JAN12	31JAN12	06FEB12	10FEB12	8
SDS1015	INSTALL GREASE TRAP	2	2	0	30JAN12	31JAN12	15FEB12	16FEB12	12
SDS1020	INSTALL CHILL WATER LOOPS	5	5	0	15SEP11	21SEP11	28SEP11	04OCT11	9
SDS1024	OPEN CUT SANITARY	5	5	0	15SEP11	21SEP11	06OCT11	12OCT11	15
SDS1034	OPEN CUT DOMESTIC WATER MAIN	5	5	0	22SEP11	28SEP11	13OCT11	19OCT11	15
SDS1070	EXCAVATE DRY POND	3	3	0	15SEP11	19SEP11	06OCT11	10OCT11	15
SDS1080	STABILIZE DRY POND	2	2	0	20SEP11	21SEP11	11OCT11	12OCT11	15
SDS1090	INSTALL DOMESTIC WATER	5	5	0	11JAN12	17JAN12	24JAN12	30JAN12	9
SDS1100	INSTALL FIRE LOOP	5	5	0	11JAN12	17JAN12	24JAN12	30JAN12	9
SDS1110	INSTALL IRRIGATION LINE SLEEVES	3	3	0	10JAN12	12JAN12	23JAN12	25JAN12	9
SDS1120	INSTALL FLAG POLE FOUNDATION	2	2	0	10JAN12	11JAN12	26JAN12	27JAN12	12
SDS1125	ROUGH AND PLACE OUC	1	1	0	01FEB12	01FEB12	21FEB12	21FEB12	14
SDS1127	CONDUIT MDP BLD TO OUC TRANS	1	1	0	03FEB12	03FEB12	22FEB12	22FEB12	13
SDS1129	PULL MDP FEEDS FROM OUC	1	1	0	06FEB12	06FEB12	23FEB12	23FEB12	13
SDS1130	INSTALL PRIMARY AND SEC ELE TO	5	5	0	17JAN12	23JAN12	26JAN12	01FEB12	7
SDS1140	INSTALL DATA COM UG FROM POS	1	1	0	10JAN12	10JAN12	23JAN12	23JAN12	9
SDS1160	SET OUC TRANSFORMERS	1	1	0	07FEB12	07FEB12	28FEB12	28FEB12	15
EXFILTRATION									
SEX1000	MOB SET UP SHEET PILE RIG	5	5	0	04OCT11	10OCT11	17OCT11	21OCT11	9
SEX1005	INSTALL SHORING	20	20	0	11OCT11	07NOV11	24OCT11	18NOV11	9
SEX1010	EXCAVATE FOR EXFILTRATION BLD	8	8	0	14OCT11	25OCT11	27OCT11	07NOV11	9
SEX1020	INSTALL EXFILTRATION BLD 1A	15	15	0	26OCT11	15NOV11	08NOV11	30NOV11	9
SEX1030	EXCAVATE EXFILTRATION BALL	7	7	0	16NOV11	28NOV11	01DEC11	09DEC11	9

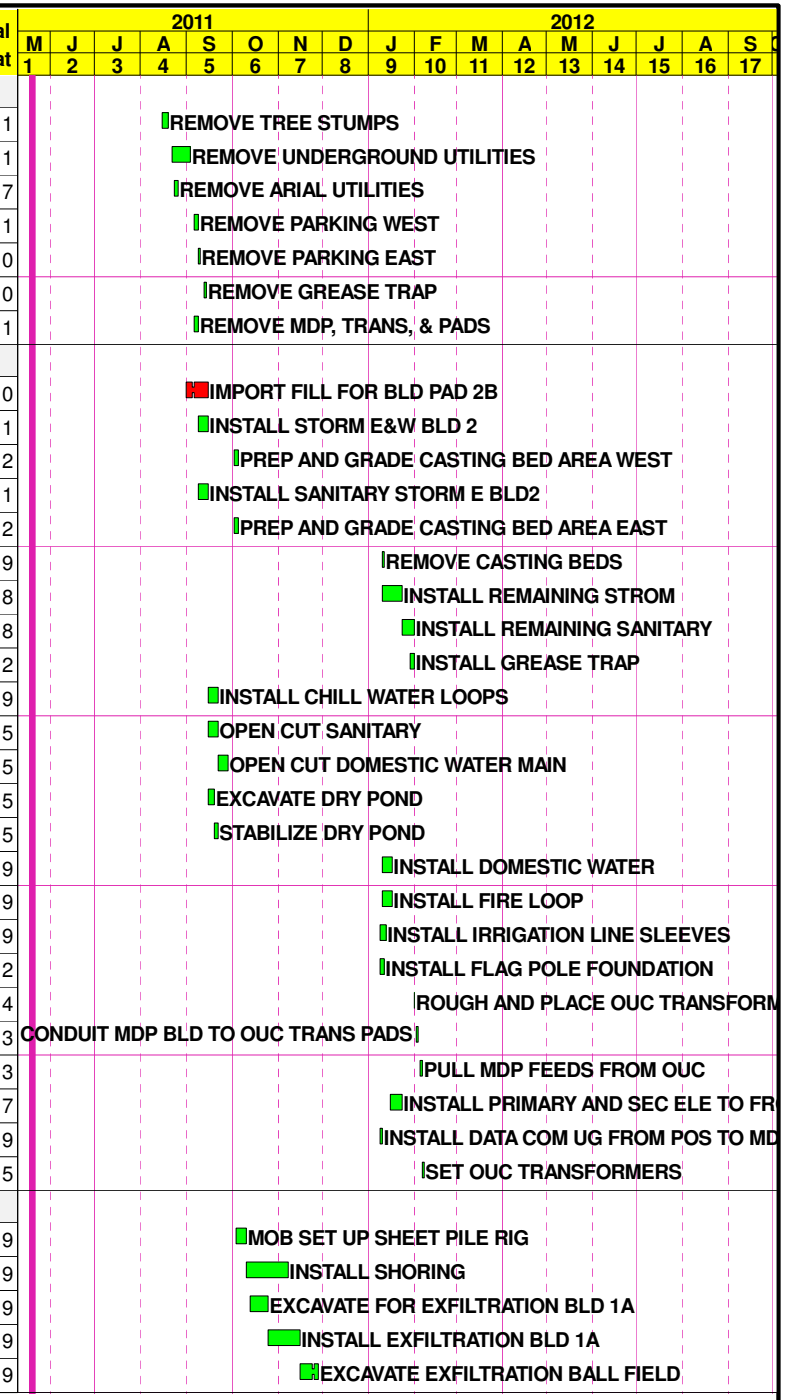

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
SEX1040	INSTALL EXFILTRATION SYSTEMS	15	15	0	29NOV11	19DEC11	12DEC11	03JAN12	9
SITE IMPROVEMENTS									
SIM2000	BALANCE SITE	10	10	0	23DEC11	09JAN12	05JAN12	18JAN12	7
SIM2010	INSTALL SITE LIGHTING	2	2	0	11JAN12	12JAN12	24JAN12	25JAN12	9
SIM2020	ROUGH IN UG FA AND SITE	5	5	0	10JAN12	16JAN12	19JAN12	25JAN12	7
SIM2030	FRP WALL FOR NEW ENTRIES EAST	5	5	0	08SEP11	14SEP11	26SEP11	30SEP11	12
SIM2040	CLIP PARKING EAST	2	2	0	01FEB12	02FEB12	17FEB12	20FEB12	12
SIM2050	STABILIZE SUB GRADE EAST	2	2	0	03FEB12	06FEB12	21FEB12	22FEB12	12
SIM2060	INSTALL BASE EAST	2	2	0	07FEB12	08FEB12	23FEB12	24FEB12	12
SIM2070	INSTALL CURBING AND ISLANDS	2	2	0	09FEB12	10FEB12	27FEB12	28FEB12	12
SIM2080	1ST LIFT ASPHALT EAST	1	1	0	13FEB12	13FEB12	29FEB12	29FEB12	12
SIM2090	2ND LIFT ASPHALT EAST	1	1	0	14FEB12	14FEB12	01MAR12	01MAR12	12
SIM2100	CLIP WEST ENTRANCE	2	2	0	17JAN12	18JAN12	30JAN12	31JAN12	9
SIM2110	CUT AND PLACE NEW ENTRY WALLS	5	5	0	19JAN12	25JAN12	01FEB12	07FEB12	9
SIM2120	STABILIZE SUB GRADE WEST	2	2	0	26JAN12	27JAN12	08FEB12	09FEB12	9
SIM2130	INSTALL BASE WEST	2	2	0	01FEB12	02FEB12	13FEB12	14FEB12	8
SIM2140	INSTALL CURBING WEST	2	2	0	03FEB12	06FEB12	15FEB12	16FEB12	8
SIM2150	1ST LIFT ASPHALT WEST	1	1	0	07FEB12	07FEB12	22FEB12	22FEB12	11
SIM2160	2ND LIFT ASPHALT WEST	1	1	0	08FEB12	08FEB12	23FEB12	23FEB12	11
SIM2170	ROUGH IN CANOPY DRAINS	5	5	0	11JAN12	17JAN12	30JAN12	03FEB12	13
SIM2180	TIE IN CANOPY DRAINS	3	3	0	28JUN12	02JUL12	18JUL12	20JUL12	13
SIM2190	RECONSTRUCT BASE BALL FIELD	10	10	0	20DEC11	04JAN12	04JAN12	17JAN12	9
SIM2200	STRIPING AND SIGNAGE	5	5	0	15FEB12	21FEB12	02MAR12	08MAR12	12
SIM2210	PLAY EQUIPMENT	3	3	0	09FEB12	13FEB12	01MAR12	05MAR12	15
SIM2220	FLAG POLE	2	2	0	12JAN12	13JAN12	30JAN12	31JAN12	12
SIM2230	COURTYARD HARDSCAPE	16	16	0	03JUL12	25JUL12	23JUL12	13AUG12	13
SIM2240	REMAINING PARAMETER	10	10	0	06JUN12	19JUN12	15JUN12	28JUN12	7
SIM2250	INSTALL NEW SITE FENCING	10	10	0	20JUN12	03JUL12	29JUN12	13JUL12	7
SIM2260	INSTALL NEW F/A DEVICES PIV, BF	2	2	0	20MAR12	21MAR12	30MAR12	02APR12	8
SIM2270	INSTALL SITE LIGHTING	3	3	0	22MAR12	26MAR12	03APR12	05APR12	8
LANDSCAPING									
LAS2000	INSTALL IRRIGATION PIPING	7	7	0	13JAN12	23JAN12	26JAN12	03FEB12	9
LAS2010	INSTALL IRRIGATION TIMER	2	2	0	24JAN12	25JAN12	06FEB12	07FEB12	9
LAS2020	FINE GRADE	5	5	0	26JAN12	01FEB12	08FEB12	14FEB12	9
LAS2030	INSTALL PLANTS	5	5	0	02FEB12	08FEB12	15FEB12	21FEB12	9
LAS2040	INSTALL SOD	5	5	0	02FEB12	08FEB12	15FEB12	21FEB12	9
LAS2050	INSTALL MULCH	3	3	0	02FEB12	06FEB12	15FEB12	17FEB12	9
TESTING & INSPECTIONS									
STN2000	DENSITIES PARKING WEST	1	1	0	30JAN12	30JAN12	10FEB12	10FEB12	9

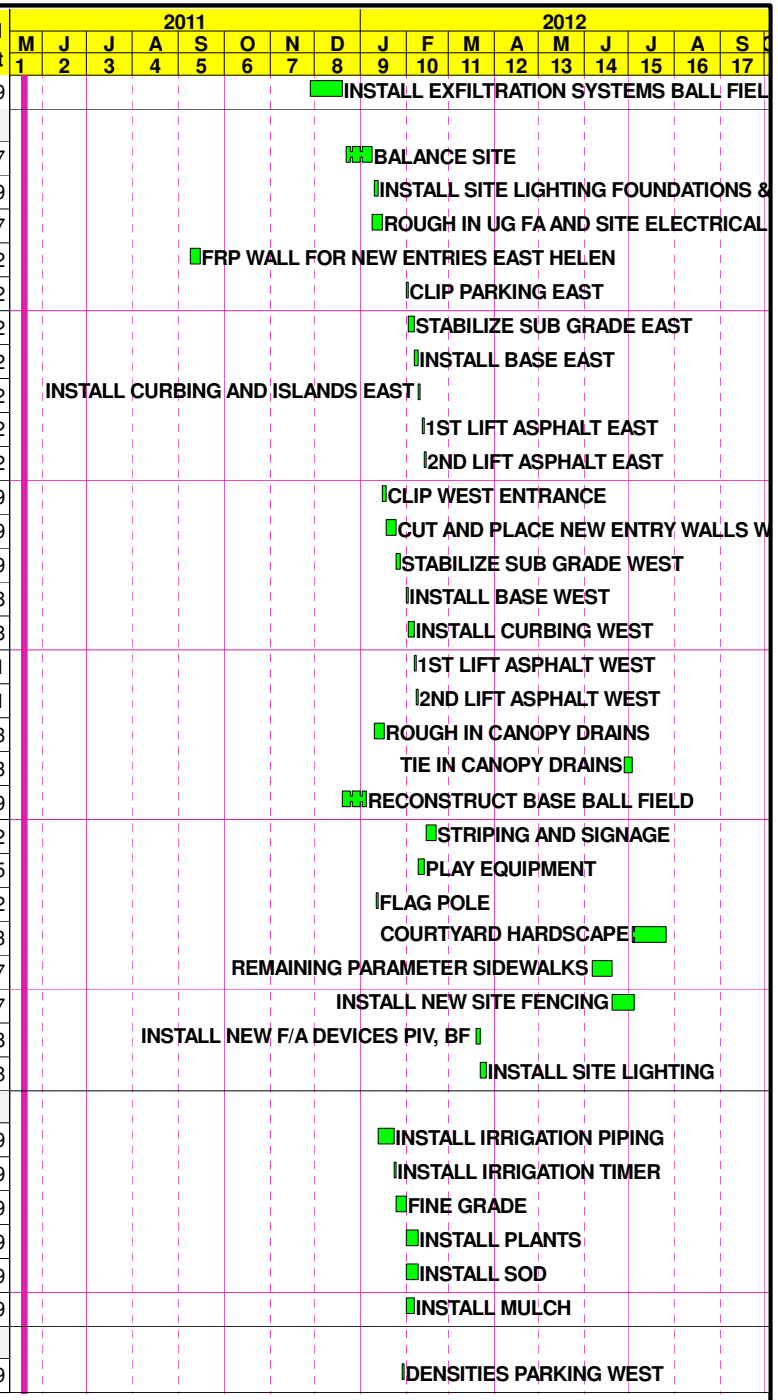

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
STN2010	DENSITIES PARKING EAST	1	1	0	07FEB12	07FEB12	23FEB12	23FEB12	12
STN2020	HYDRO FIRE	1	1	0	18JAN12	18JAN12	03FEB12	03FEB12	12
STN2030	HYDRO DOM WATER	1	1	0	18JAN12	18JAN12	03FEB12	03FEB12	12
STN2040	BACT DOM WATER	1	1	0	01FEB12	01FEB12	14FEB12	14FEB12	9
STN2050	LAMP STORM CERTIFY	1	1	0	25JAN12	25JAN12	13FEB12	13FEB12	13
STN2060	FLOW FIRE HYDRANTS	1	1	0	19MAR12	19MAR12	29MAR12	29MAR12	8
STN2070	BCCO PRE DEMO WALK THROUGH	1	1	0	11JUL11	11JUL11	20JUL11	20JUL11	7
STN2080	EXFILTRATION SET SOUTH	1	1	0	16NOV11	16NOV11	01DEC11	01DEC11	9
STN2090	EXFILTRATION SET NORTH	1	1	0	22DEC11	22DEC11	04JAN12	04JAN12	7
STN2100	BCCO EARLY DEMO PACKAGE	1	1	0	12AUG11	12AUG11	15AUG11	15AUG11	1
STN9000	FINAL SITE	1	1	0	26JUL12	26JUL12	14AUG12	14AUG12	13
REQUIRED DOCUMENTS									
SRD2000	SITE FINAL W / ATTACHED BCCO	1	1	0	27JUL12	27JUL12	15AUG12	15AUG12	13
SRD2010	FIRE SPRINKLER FINAL NFPA 13	1	1	0	20MAR12	20MAR12	30MAR12	30MAR12	8
SRD2020	FIRE ALARM NFPA 72 FORM	1	1	0	22MAR12	22MAR12	03APR12	03APR12	8
SRD2030	PLUMBING BACT TEST @ SAMPLE	10	10	0	03FEB12	16FEB12	15FEB12	28FEB12	8
SRD2050	ELECTRICAL FINAL	1	1	0	27MAR12	27MAR12	10APR12	10APR12	10
SRD2070	COMMUNICATION SYSTEM FINAL	1	1	0	17JAN12	17JAN12	02FEB12	02FEB12	12
SRD2090	IRRIGATION	1	1	0	26JAN12	26JAN12	13FEB12	13FEB12	12
SRD2100	LIGHTNING PROTECTION UL	10	10	0	18JUN12	29JUN12	16JUL12	27JUL12	19
SRD2120	SITE UG WATER PAPERS FLUSH	1	1	0	20MAR12	20MAR12	30MAR12	30MAR12	8
SRD2140	FIRE ALARM MONITORING	1	1	0	28MAR12	28MAR12	11APR12	11APR12	10
COMPLETION & PUNCH									
SPL2000	DOSTER PRE PUNCH LIST	5	5	0	11JUL12	17JUL12	16JUL12	20JUL12	3
SPL2010	COMPLETE DOSTER PRE PUNCH	10	10	0	18JUL12	31JUL12	23JUL12	03AUG12	3
SPL2020	COMPLETE OCPS QAQC LIST	5	5	0	01AUG12	07AUG12	06AUG12	10AUG12	3
SPL2030	OWNER ARCHITECT GENERATE	3	3	0	08AUG12	10AUG12	13AUG12	15AUG12	3
SPL2040	RECEIVE OWNER FINAL PUNCH LIST	1	1	0	13AUG12	13AUG12	16AUG12	16AUG12	3
SPL2050	COMPLETE OWNER ARCHITECT	10	10	0	14AUG12	27AUG12	17AUG12	30AUG12	3
BLDG 1A RENOVATION									
MILESTONES									
1AMS2010	SHELL / DRYING	0	0	0		05APR12		16APR12	7
1AMS2020	ENERGIZE	0	0	0		13APR12		08MAY12	17
1AMS2030	CONDITIONED AIR	1	1	0	25APR12	25APR12	09MAY12	09MAY12	10
1AMS2040	FFE	0	0	0		12JUL12		23JUL12	7
1AMS2050	SUBSTANTIAL COMPLETE	1	1	0	23JUL12	23JUL12	07AUG12	07AUG12	11
1AMS2060	SUB COMPLETION LIST COMPLETE	1	1	0	03JUL12	03JUL12	30JUL12	30JUL12	18
1AMS2070	OWNER ARCHITECT PUNCH	1	1	0	15AUG12	15AUG12	30AUG12	30AUG12	11

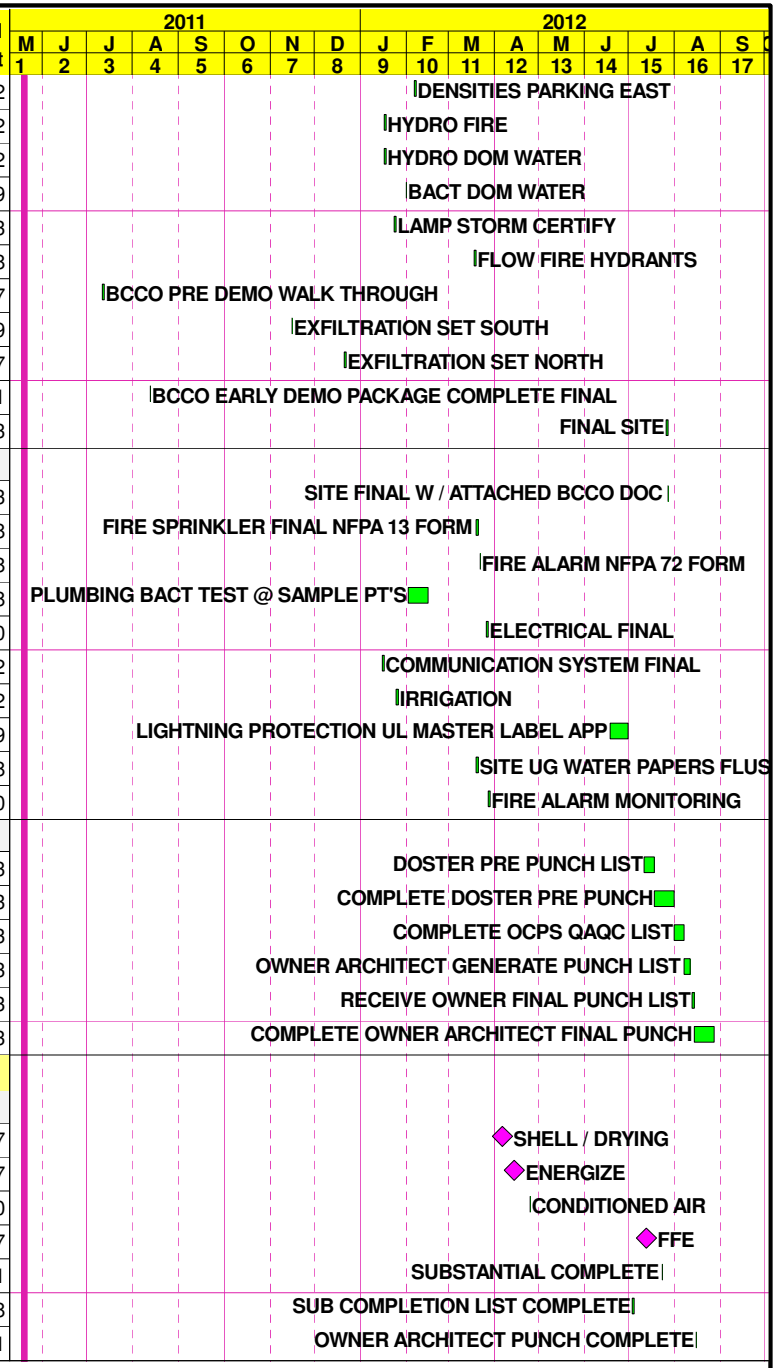

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
UNDERGROUND									
1AUG2000	SELECTIVE DEMO FOR NEW	3	3	0	03OCT11	05OCT11	13OCT11	17OCT11	8
1AUG2010	FRP NEW FOUNDATIONS	3	3	0	06OCT11	10OCT11	18OCT11	20OCT11	8
1AUG2020	NEW MEP CONNECTIONS	10	10	0	18JAN12	31JAN12	31JAN12	13FEB12	9
1AUG2030	NEW CWS CWR LINES	5	5	0	22SEP11	28SEP11	13OCT11	19OCT11	15
1AUG2040	NEW MDP SERVICE	7	7	0	24JAN12	01FEB12	03FEB12	13FEB12	8
1AUG2050	NEW COMMUNICATIONS SERVICE	7	7	0	11JAN12	19JAN12	06FEB12	14FEB12	18
STRUCTURE									
1AMS2080	LAYOUT CORNERS B1A / B1B	1	1	0	11AUG11	11AUG11	09SEP11	09SEP11	20
1AST2000	NEW STEEL SUPPORTS FOR	5	5	0	11OCT11	17OCT11	21OCT11	27OCT11	8
1AST2030	EXCAVATE FOUNDATIONS	3	3	0	15NOV11	17NOV11	29NOV11	01DEC11	8
1AST2040	INSTALL REINFORCING STEEL	2	2	0	18NOV11	21NOV11	02DEC11	05DEC11	8
1AST2050	PLACE FOUNDATION	2	2	0	23NOV11	28NOV11	07DEC11	08DEC11	8
1AST2055	FRP COLUMNS ATTACHED TO EXIST	5	5	0	29NOV11	05DEC11	09DEC11	15DEC11	8
1AST2060	INSTALL STEM WALLS / FILL CELL	3	3	0	29NOV11	01DEC11	09DEC11	13DEC11	8
1AST2070	BACKFILL STEM WALLS	2	2	0	02DEC11	05DEC11	14DEC11	15DEC11	8
1AST2080	FINE GRADE	2	2	0	06DEC11	07DEC11	16DEC11	19DEC11	8
1AST2090	PEST CONTROL SPRAY	1	1	0	08DEC11	08DEC11	20DEC11	20DEC11	8
1AST2100	INSTALL VAPOR BARRIER &	1	1	0	13DEC11	13DEC11	22DEC11	22DEC11	7
1AST2110	PLACE SOG	1	1	0	15DEC11	15DEC11	27DEC11	27DEC11	7
1AST2120	1ST LIFT CMU	3	3	0	16DEC11	20DEC11	28DEC11	30DEC11	7
1AST2130	2ND LIFT CMU	3	3	0	22DEC11	27DEC11	04JAN12	06JAN12	7
1AST2140	FRP 2.0 TIE BEAM	3	3	0	29DEC11	03JAN12	10JAN12	12JAN12	7
1AST2150	INSTALL STEEL FOR 2.0 ELEVATED	3	3	0	04JAN12	06JAN12	13JAN12	17JAN12	7
1AST2160	DECKING	2	2	0	10JAN12	11JAN12	19JAN12	20JAN12	7
1AST2170	MEP SLEEVES	2	2	0	12JAN12	13JAN12	23JAN12	24JAN12	7
1AST2180	REINFORCING STEEL	2	2	0	16JAN12	17JAN12	25JAN12	26JAN12	7
1AST2190	PLACE 2.0 SLAB	1	1	0	18JAN12	18JAN12	27JAN12	27JAN12	7
1AST2200	2.0 1ST LIFT CMU	3	3	0	19JAN12	23JAN12	30JAN12	01FEB12	7
1AST2205	2.0 2ND LIFT CMU	3	3	0	24JAN12	26JAN12	02FEB12	06FEB12	7
1AST2210	FRP ROOF TIE BEAM	3	3	0	27JAN12	31JAN12	07FEB12	09FEB12	7
1AST2220	PARAPET & LINTEL	2	2	0	01FEB12	02FEB12	10FEB12	13FEB12	7
1AST2230	INSTALL STEEL FOR ROOF	2	2	0	03FEB12	06FEB12	14FEB12	15FEB12	7
1AST2240	FRAME MEP OPENINGS	2	2	0	07FEB12	08FEB12	16FEB12	17FEB12	7
1AST2250	DECKING	1	1	0	09FEB12	09FEB12	20FEB12	20FEB12	7
1AST2260	FOUNDATIONS COURTYARD STAIRS	2	2	0	10FEB12	13FEB12	22FEB12	23FEB12	8
1AST2270	PLACE STEM WALLS FOR STAIRS	3	3	0	14FEB12	16FEB12	24FEB12	28FEB12	8
1AST2280	BACK FILL STEM WALLS FOR STAIRS	1	1	0	17FEB12	17FEB12	29FEB12	29FEB12	8
1AST2290	PEST CONTROL STAIRS	1	1	0	20FEB12	20FEB12	01MAR12	01MAR12	8

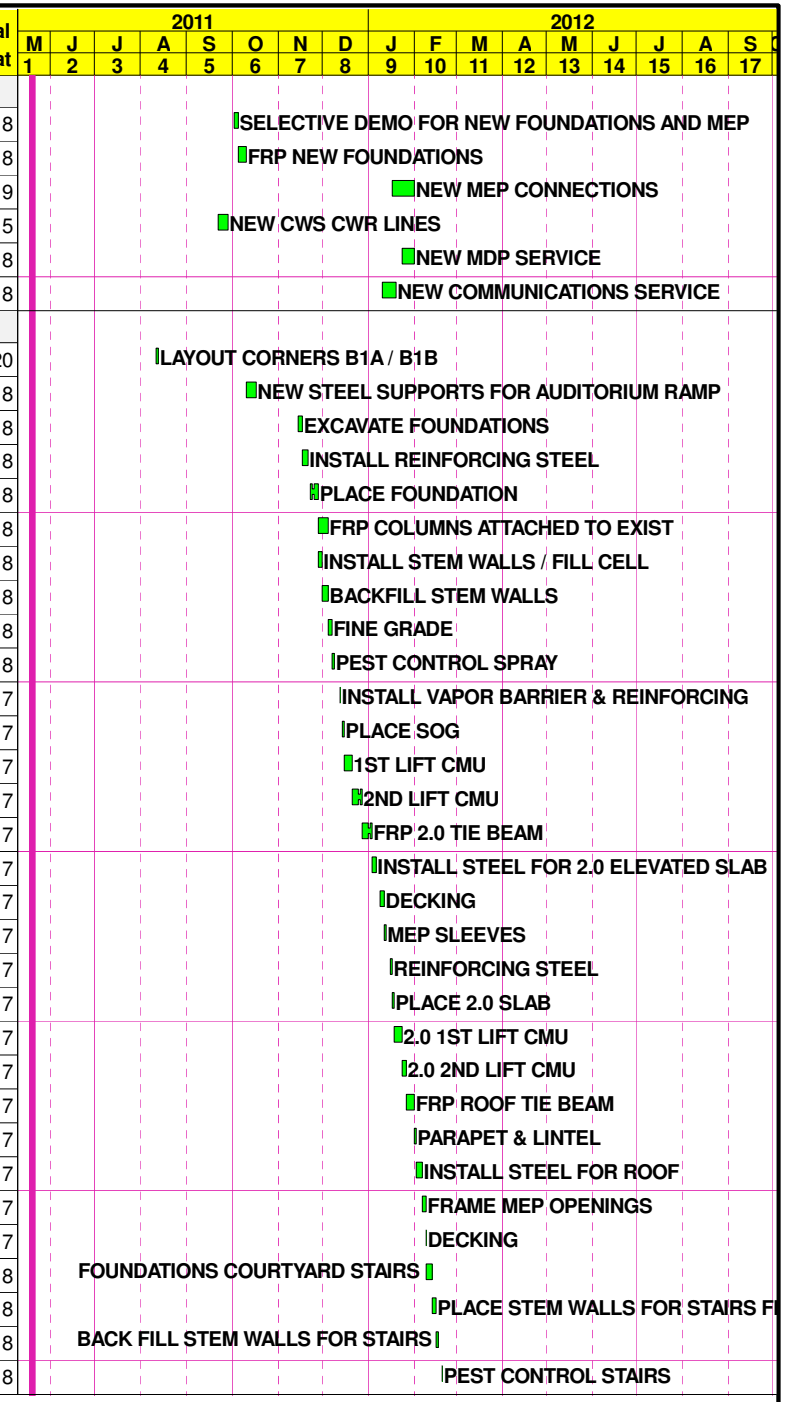

Start Date 20MAY11
Finish Date 30AUG12
Data Date 20MAY11
Run Date 12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
1AST2300	REINFORCING STEEL	1	1	0	21FEB12	21FEB12	02MAR12	02MAR12	8
1AST2310	FRP COURTYARD STAIRS	3	3	0	22FEB12	24FEB12	05MAR12	07MAR12	8
ROOF									
1ARF2030	ROOF TOP DRAINS AND MEP	1	1	0	15FEB12	15FEB12	02MAR12	02MAR12	12
1ARF2040	INSTALL ROOF TOP CURBS	2	2	0	10FEB12	13FEB12	01MAR12	02MAR12	14
1ARF2050	INSTALL TAPER INSULATION	1	1	0	16FEB12	16FEB12	05MAR12	05MAR12	12
1ARF2060	INSTALL LIGHT WEIGHT CONCRETE	1	1	0	20FEB12	20FEB12	07MAR12	07MAR12	12
1ARF2070	INSTALL ROOFING MATERIALS	5	5	0	21FEB12	27FEB12	08MAR12	14MAR12	12
1ARF2080	INSTALL PARAPET CAPS	2	2	0	06APR12	09APR12	17APR12	18APR12	7
1ARF2090	INSTALL MEP EQUIPMENT	2	2	0	10APR12	11APR12	25APR12	26APR12	11
1ARF2100	INSTALL LIGHTNING PROTECTION	2	2	0	12APR12	13APR12	27APR12	30APR12	11
1ARF3000	SELECTIVE DEMOLITION ROOF	1	1	0	10FEB12	10FEB12	07MAR12	07MAR12	18
1ARF3010	REMOVE OLD ROOF	20	20	0	10FEB12	08MAR12	21FEB12	19MAR12	7
1ARF3030	INSTALL NEW ROOFING SYSTEM	20	20	0	09MAR12	05APR12	20MAR12	16APR12	7
DEMOLITION									
1ADE2000	TEMP A/C CLIMATE CONTROL	5	5	0	24AUG11	30AUG11	21SEP11	27SEP11	19
1ADE2005	REMOVE CEILINGS	15	15	0	04OCT11	24OCT11	13OCT11	02NOV11	7
1ADE2010	REMOVE FLOORING	15	15	0	25OCT11	14NOV11	03NOV11	23NOV11	7
1ADE2020	SELECTIVE WALL DEMOLITION FOR	15	15	0	25OCT11	14NOV11	03NOV11	23NOV11	7
1ADE2030	SELECTIVE FLOOR DEMOLITION FOR	15	15	0	25OCT11	14NOV11	03NOV11	23NOV11	7
1ADE2040	REMOVE MECHANICAL TO BE	15	15	0	25OCT11	14NOV11	04NOV11	28NOV11	8
1ADE2050	REMOVE ELECTRICAL TO BE	15	15	0	25OCT11	14NOV11	04NOV11	28NOV11	8
1ADE2060	REMOVE PLUMBING TO BE	15	15	0	15NOV11	07DEC11	28NOV11	16DEC11	7
1ADE2070	REMOVE EXISTING F/P	15	15	0	25OCT11	14NOV11	04NOV11	28NOV11	8
1ADE2080	REMOVE OLD ACC TO RECEIVE NEW	15	15	0	25OCT11	14NOV11	03NOV11	23NOV11	7
1ADE2090	INSTALL SHORING CRAWEL SPACE	5	5	0	15NOV11	21NOV11	28NOV11	02DEC11	7
1ADE2100	INSTALL SHORING CAFETERIA	5	5	0	22NOV11	30NOV11	05DEC11	09DEC11	7
1ADE2110	INSTALL SHORING AUDITORIUM TO	5	5	0	01DEC11	07DEC11	12DEC11	16DEC11	7
1ADE2120	DEMOLISH THE N. WALL	7	7	0	10FEB12	20FEB12	24FEB12	05MAR12	10
1ADE2130	REMOVE SHORING FOR AUD WALL	5	5	0	21FEB12	27FEB12	06MAR12	12MAR12	10
INTERIOR 1ST FLOOR									
1AFF2030	FRAME WALLS	10	10	0	15NOV11	30NOV11	28NOV11	09DEC11	7
1AFF2040	TOP OUT FIRE SMOKE WALLS	5	5	0	01DEC11	07DEC11	12DEC11	16DEC11	7
1AFF2050	1 SIDE MECH AND ELE ROOMS	2	2	0	08DEC11	09DEC11	19DEC11	20DEC11	7
1AFF2060	IN WALL MECHANICAL	15	15	0	01DEC11	21DEC11	12DEC11	03JAN12	7
1AFF2070	IN WALL ELECTRICAL	15	15	0	01DEC11	21DEC11	12DEC11	03JAN12	7
1AFF2080	IN WALL LOW VOLTAGE, DATA, COM	15	15	0	01DEC11	21DEC11	12DEC11	03JAN12	7
1AFF2090	IN WALL FIRE ALARM	15	15	0	01DEC11	21DEC11	12DEC11	03JAN12	7
1AFF2100	IN WALL SECURITY	15	15	0	01DEC11	21DEC11	12DEC11	03JAN12	7

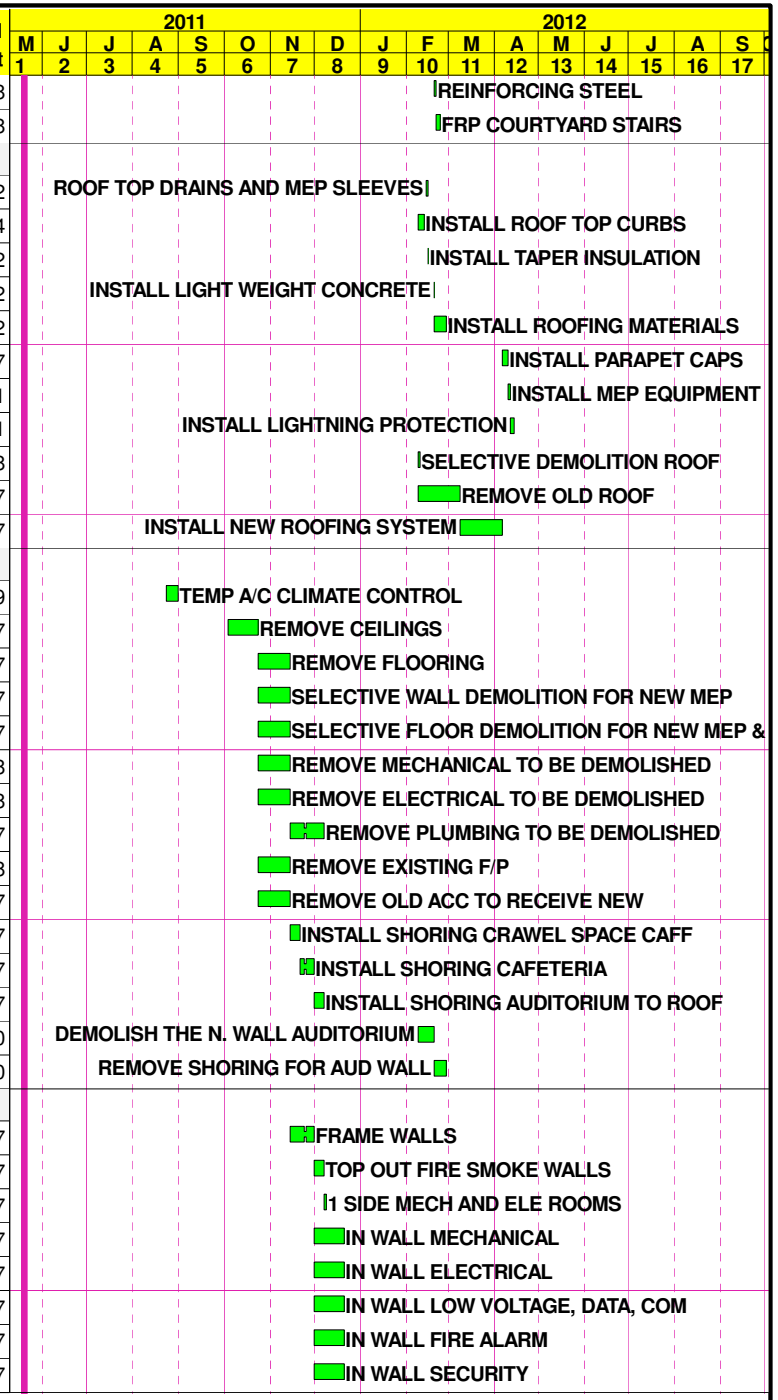

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
1AFF2110	IN WALL PLUMBING	15	15	0	01DEC11	21DEC11	12DEC11	03JAN12	7
1AFF2120	ROUGH DUCT	15	15	0	19DEC11	10JAN12	03JAN12	23JAN12	9
1AFF2140	ABOVE CEILING SANITARY	9	9	0	08DEC11	20DEC11	19DEC11	30DEC11	7
1AFF2150	ABOVE CEILING FIRE PROTECTION	10	10	0	15NOV11	30NOV11	29NOV11	12DEC11	8
1AFF2160	ABOVE CEILING MECHANICAL	15	15	0	22DEC11	13JAN12	05JAN12	25JAN12	8
1AFF2170	ABOVE CEILING PLUMBING	15	15	0	22DEC11	13JAN12	05JAN12	25JAN12	8
1AFF2180	ABOVE CEILING ELECTRICAL	15	15	0	16JAN12	03FEB12	26JAN12	15FEB12	8
1AFF2190	ABOVE CEILING LOW VOLTAGE,	15	15	0	22DEC11	13JAN12	05JAN12	25JAN12	8
1AFF2200	ABOVE CEILING FIRE ALARM	15	15	0	22DEC11	13JAN12	05JAN12	25JAN12	8
1AFF2210	ABOVE CEILING SECURITY	15	15	0	22DEC11	13JAN12	05JAN12	25JAN12	8
1AFF2220	SET MECH EQ	2	2	0	09JAN12	10JAN12	24JAN12	25JAN12	11
1AFF2230	TIE IN MECHANICAL	5	5	0	12JAN12	18JAN12	30JAN12	03FEB12	12
1AFF2240	SET PANELS ELE ROOM	2	2	0	02FEB12	03FEB12	14FEB12	15FEB12	8
1AFF2241	SET MDP AND STEP TRANS	2	2	0	07FEB12	08FEB12	05MAR12	06MAR12	19
1AFF2250	MEP HOUSE KEEPING PADS	2	2	0	12DEC11	13DEC11	21DEC11	22DEC11	7
1AFF2270	INSULATE WALLS	2	2	0	22DEC11	23DEC11	05JAN12	06JAN12	8
1AFF2280	INSTALL DRYWALL	5	5	0	19JAN12	25JAN12	31JAN12	06FEB12	8
1AFF2285	FRAME HARD CEILINGS	3	3	0	26JAN12	30JAN12	07FEB12	09FEB12	8
1AFF2290	FINISH DRYWALL	10	10	0	26JAN12	08FEB12	08FEB12	21FEB12	9
1AFF2300	INSTALL HARD CEILINGS	2	2	0	01FEB12	02FEB12	13FEB12	14FEB12	8
1AFF2310	FINISH HARD CEILINGS	5	5	0	03FEB12	09FEB12	15FEB12	21FEB12	8
1AFF2330	POINT UP MASONRY	3	3	0	04JAN12	06JAN12	13JAN12	17JAN12	7
1AFF2340	PRIME PAINT	5	5	0	10FEB12	16FEB12	22FEB12	28FEB12	8
1AFF2350	INSTALL CERAMIC TILE	5	5	0	17FEB12	23FEB12	29FEB12	06MAR12	8
1AFF2360	PAINT 1ST PASS COLOR	5	5	0	17FEB12	23FEB12	29FEB12	06MAR12	8
1AFF2370	BUMP OUT / TOUCH UP DRYWALL	3	3	0	24FEB12	28FEB12	07MAR12	09MAR12	8
1AFF2380	INSTALL MILL WORK	5	5	0	26APR12	02MAY12	11MAY12	17MAY12	11
1AFF2385	PATCH ABOVE CEILING PLASTER	15	15	0	06FEB12	24FEB12	20FEB12	09MAR12	10
1AFF2390	INSTALL CEILING GRID	5	5	0	29FEB12	06MAR12	12MAR12	16MAR12	8
1AFF2410	MECHANICAL IN GRID	5	5	0	07MAR12	13MAR12	19MAR12	23MAR12	8
1AFF2420	ELECTRICAL IN GRID	5	5	0	07MAR12	13MAR12	19MAR12	23MAR12	8
1AFF2430	LOW VOLTAGE, DATA, COM IN GRID	5	5	0	07MAR12	13MAR12	19MAR12	23MAR12	8
1AFF2440	FIRE ALARM IN GRID	5	5	0	07MAR12	13MAR12	20MAR12	26MAR12	9
1AFF2450	SECURITY IN GRID	5	5	0	07MAR12	13MAR12	20MAR12	26MAR12	9
1AFF2460	FIRE PROTECTION IN GRID	5	5	0	07MAR12	13MAR12	19MAR12	23MAR12	8
1AFF2465	INSTALL CEILING TILE	2	2	0	26APR12	27APR12	10MAY12	11MAY12	10
1AFF2470	FINAL PAINT	5	5	0	03MAY12	09MAY12	18MAY12	24MAY12	11
1AFF2480	INSTALL DIVISION 10 EQ	3	3	0	10MAY12	14MAY12	01JUN12	05JUN12	15
1AFF2500	INSTALL DOORS AND HARDWARE	3	3	0	10MAY12	14MAY12	04JUN12	06JUN12	16

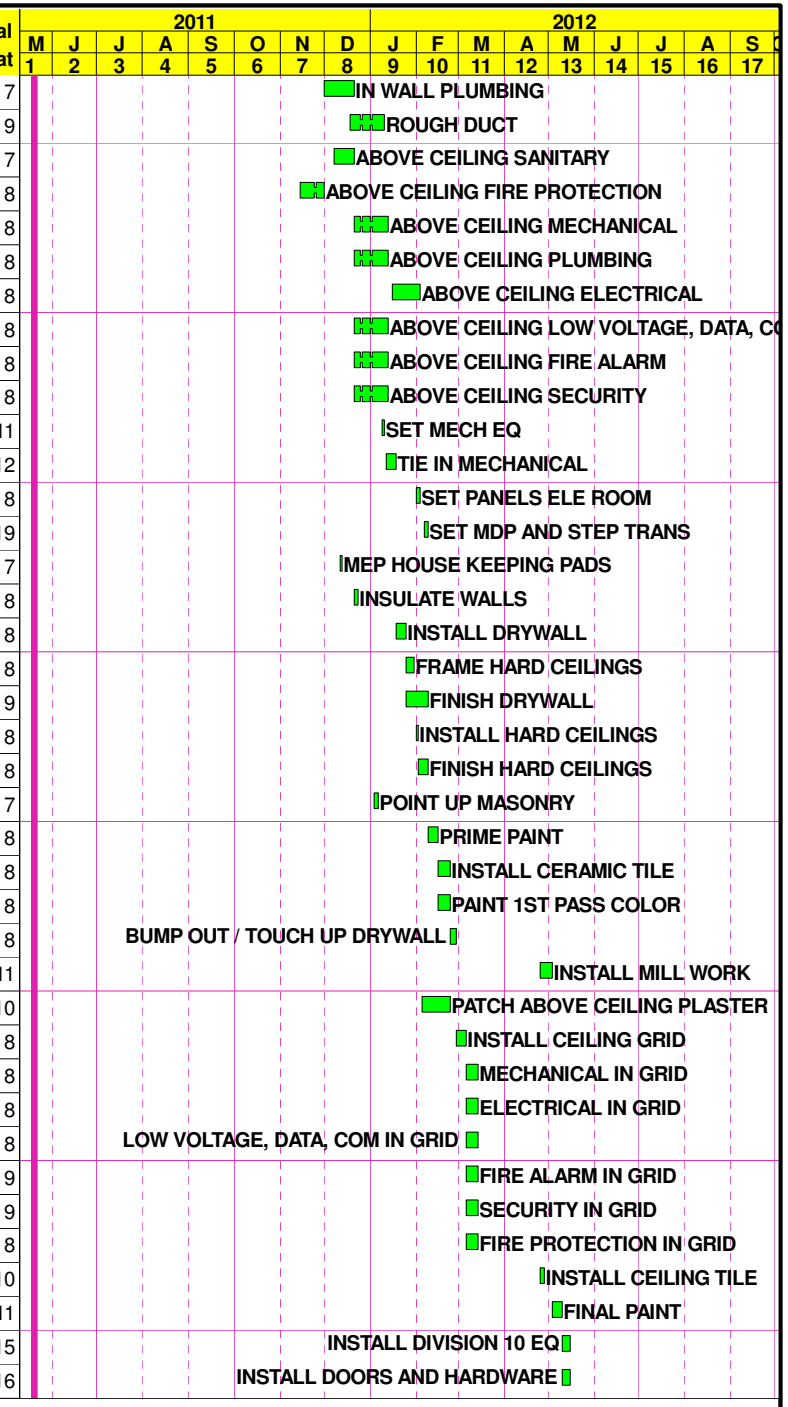

Start Date 20MAY11
Finish Date 30AUG12
Data Date 20MAY11
Run Date 12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0 Sheet 34 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
1AFF2510	INSTALL COMPOSITE FLOORING	5	5	0	03MAY12	09MAY12	18MAY12	24MAY12	11
1AFF2520	INSTALL CARPET	2	2	0	10MAY12	11MAY12	29MAY12	30MAY12	12
1AFF2530	TRIM OUT MECHANICAL	3	3	0	10MAY12	14MAY12	29MAY12	31MAY12	12
1AFF2540	TRIM OUT ELECTRICAL	3	3	0	15MAY12	17MAY12	01JUN12	05JUN12	12
1AFF2550	TRIM OUT PLUMBING SET FIXTURES	5	5	0	03MAY12	09MAY12	22MAY12	29MAY12	13
1AFF2560	FINAL PAINT DOOR FRAMES	2	2	0	15MAY12	16MAY12	08JUN12	11JUN12	17
1AFF2570	INSTALL BASE	2	2	0	14MAY12	15MAY12	31MAY12	01JUN12	12
1AFF2580	INSTALL SIGNAGE	1	1	0	10MAY12	10MAY12	25MAY12	25MAY12	11
INTERIOR 2ND FLOOR									
1ASF2030	FRAME WALLS	10	10	0	01DEC11	14DEC11	12DEC11	23DEC11	7
1ASF2040	TOP OUT FIRE SMOKE WALLS	4	4	0	15DEC11	20DEC11	27DEC11	30DEC11	7
1ASF2050	1 SIDE MECH AND ELE ROOMS	2	2	0	21DEC11	22DEC11	20JAN12	23JAN12	20
1ASF2060	IN WALL MECHANICAL	15	15	0	22DEC11	13JAN12	05JAN12	25JAN12	8
1ASF2070	IN WALL ELECTRICAL	15	15	0	22DEC11	13JAN12	05JAN12	25JAN12	8
1ASF2080	IN WALL LOW VOLTAGE, DATA, COM	15	15	0	22DEC11	13JAN12	05JAN12	25JAN12	8
1ASF2090	IN WALL FIRE ALARM	15	15	0	22DEC11	13JAN12	05JAN12	25JAN12	8
1ASF2100	IN WALL SECURITY	15	15	0	22DEC11	13JAN12	05JAN12	25JAN12	8
1ASF2110	IN WALL PLUMBING	15	15	0	22DEC11	13JAN12	05JAN12	25JAN12	8
1ASF2120	ROUGH DUCT	15	15	0	11JAN12	31JAN12	24JAN12	13FEB12	9
1ASF2130	ROUGH RAIN LEADERS	4	4	0	21DEC11	27DEC11	03JAN12	06JAN12	7
1ASF2150	ABOVE CEILING FIRE PROTECTION	10	10	0	21DEC11	05JAN12	04JAN12	17JAN12	8
1ASF2160	ABOVE CEILING MECHANICAL	10	10	0	16JAN12	27JAN12	01FEB12	14FEB12	12
1ASF2170	ABOVE CEILING PLUMBING	10	10	0	16JAN12	27JAN12	01FEB12	14FEB12	12
1ASF2180	ABOVE CEILING ELECTRICAL	10	10	0	06FEB12	17FEB12	16FEB12	29FEB12	8
1ASF2190	ABOVE CEILING LOW VOLTAGE,	10	10	0	16JAN12	27JAN12	09FEB12	22FEB12	18
1ASF2200	ABOVE CEILING FIRE ALARM	10	10	0	16JAN12	27JAN12	09FEB12	22FEB12	18
1ASF2210	ABOVE CEILING SECURITY	10	10	0	16JAN12	27JAN12	09FEB12	22FEB12	18
1ASF2220	EQ HOUSE KEEPING PADS	2	2	0	23DEC11	27DEC11	24JAN12	25JAN12	20
1ASF2221	SET MEP EQ	2	2	0	11JAN12	12JAN12	26JAN12	27JAN12	11
1ASF2230	TIE IN MECHANICAL	5	5	0	01FEB12	07FEB12	14FEB12	20FEB12	9
1ASF2240	SET PANELS ELE ROOM	2	2	0	06FEB12	07FEB12	27FEB12	28FEB12	15
1ASF2270	INSULATE WALLS	2	2	0	16JAN12	17JAN12	26JAN12	27JAN12	8
1ASF2280	INSTALL DRYWALL	5	5	0	26JAN12	01FEB12	13FEB12	17FEB12	12
1ASF2285	FRAME HARD CEILINGS	3	3	0	02FEB12	06FEB12	20FEB12	22FEB12	12
1ASF2290	FINISH DRYWALL	10	10	0	09FEB12	22FEB12	23FEB12	07MAR12	10
1ASF2300	INSTALL HARD CEILINGS	2	2	0	08FEB12	09FEB12	28FEB12	29FEB12	14
1ASF2310	FINISH HARD CEILINGS	5	5	0	10FEB12	16FEB12	01MAR12	07MAR12	14
1ASF2330	POINT UP MASONRY	3	3	0	09JAN12	11JAN12	06FEB12	08FEB12	20
1ASF2340	PRIME PAINT	5	5	0	23FEB12	29FEB12	08MAR12	14MAR12	10

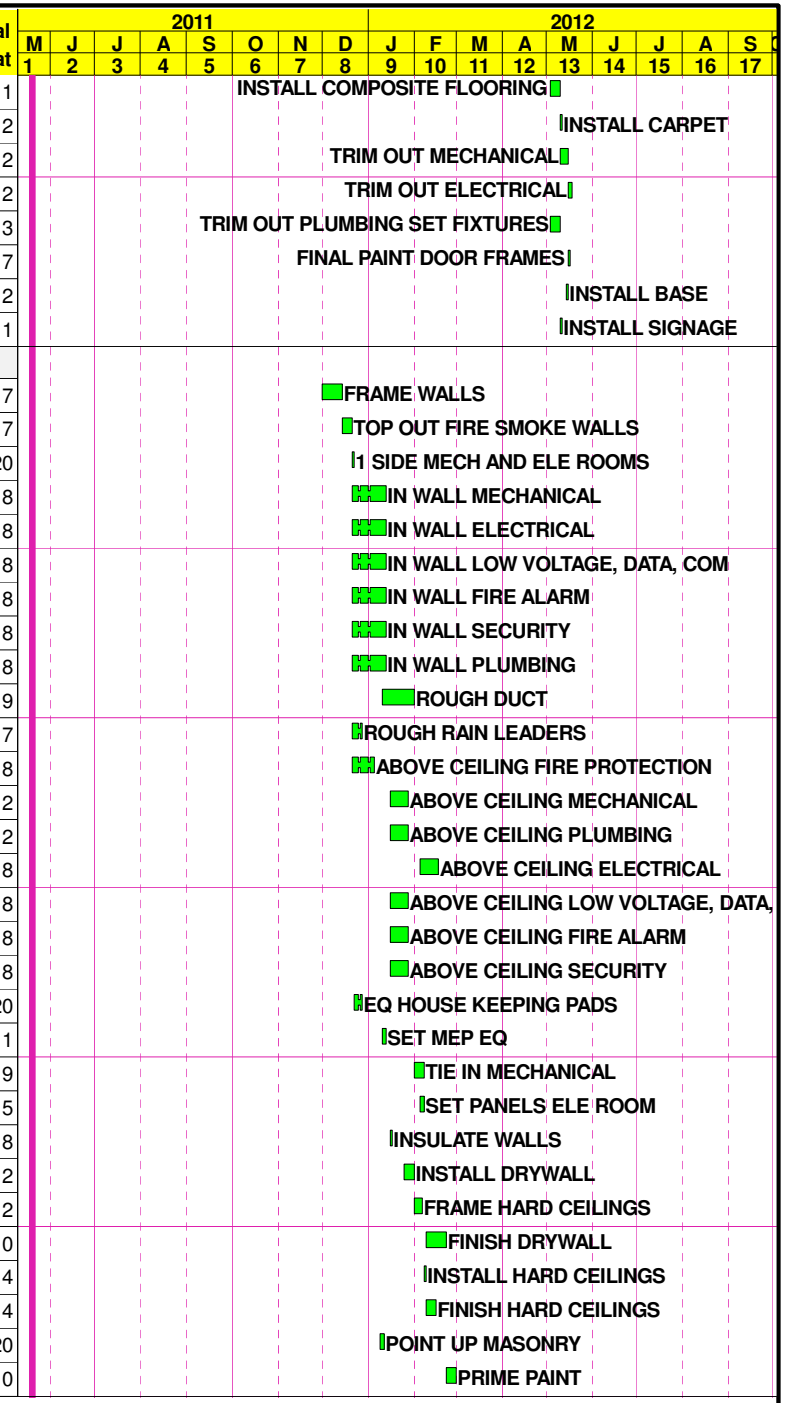

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
1ASF2350	INSTALL CERAMIC TILE	5	5	0	01MAR12	07MAR12	15MAR12	21MAR12	10
1ASF2360	PAINT 1ST PASS COLOR	5	5	0	01MAR12	07MAR12	15MAR12	21MAR12	10
1ASF2370	BUMP OUT / TOUCH UP DRYWALL	3	3	0	08MAR12	12MAR12	22MAR12	26MAR12	10
1ASF2380	INSTALL MILL WORK	5	5	0	03MAY12	09MAY12	18MAY12	24MAY12	11
1ASF2385	PATCH ABOVE CEILING PLASTER	15	15	0	20FEB12	09MAR12	01MAR12	21MAR12	8
1ASF2390	INSTALL CEILING GRID	5	5	0	12MAR12	16MAR12	22MAR12	28MAR12	8
1ASF2410	MECHANICAL IN GRID	5	5	0	19MAR12	23MAR12	29MAR12	04APR12	8
1ASF2420	ELECTRICAL IN GRID	5	5	0	19MAR12	23MAR12	29MAR12	04APR12	8
1ASF2430	LOW VOLTAGE, DATA, COM IN GRID	5	5	0	19MAR12	23MAR12	29MAR12	04APR12	8
1ASF2440	FIRE ALARM IN GRID	5	5	0	19MAR12	23MAR12	29MAR12	04APR12	8
1ASF2450	SECURITY IN GRID	5	5	0	19MAR12	23MAR12	29MAR12	04APR12	8
1ASF2460	FIRE PROTECTION IN GRID	5	5	0	19MAR12	23MAR12	29MAR12	04APR12	8
1ASF2465	INSTALL CEILING TILE	2	2	0	30APR12	01MAY12	14MAY12	15MAY12	10
1ASF2470	FINAL PAINT	5	5	0	10MAY12	16MAY12	25MAY12	01JUN12	11
1ASF2480	INSTALL DIVISION 10 EQ	3	3	0	17MAY12	21MAY12	06JUN12	08JUN12	13
1ASF2500	INSTALL DOORS AND HARDWARE	3	3	0	15MAY12	17MAY12	07JUN12	11JUN12	16
1ASF2510	INSTALL COMPOSITE FLOORING	5	5	0	10MAY12	16MAY12	25MAY12	01JUN12	11
1ASF2520	INSTALL CARPET	2	2	0	14MAY12	15MAY12	31MAY12	01JUN12	12
1ASF2530	TRIM OUT MECHANICAL	3	3	0	17MAY12	21MAY12	04JUN12	06JUN12	11
1ASF2540	TRIM OUT ELECTRICAL	3	3	0	18MAY12	22MAY12	07JUN12	11JUN12	13
1ASF2550	TRIM OUT PLUMBING SET FIXTURES	5	5	0	10MAY12	16MAY12	30MAY12	05JUN12	13
1ASF2560	FINAL PAINT DOOR FRAMES	2	2	0	18MAY12	21MAY12	12JUN12	13JUN12	16
1ASF2570	INSTALL BASE	2	2	0	17MAY12	18MAY12	04JUN12	05JUN12	11
1ASF2580	INSTALL SIGNAGE	1	1	0	21MAY12	21MAY12	06JUN12	06JUN12	11
AUDITORIUM									
1AUD2000	REMOVE AUDITORIUM SEATING AND	3	3	0	28FEB12	01MAR12	13MAR12	15MAR12	10
1AUD2010	SELECTIVE DEMOLITION FOR NEW	5	5	0	02MAR12	08MAR12	16MAR12	22MAR12	10
1AUD2020	CONSTRUCT NEW STAGE RAMP	15	15	0	09MAR12	29MAR12	23MAR12	12APR12	10
1AUD2030	SET SCAFFOLD SYSTEM FOR ABOVE	5	5	0	30MAR12	05APR12	13APR12	19APR12	10
1AUD2040	DEMO CEILING	5	5	0	06APR12	12APR12	20APR12	26APR12	10
1AUD2050	FRAME NEW SOFFITS	5	5	0	13APR12	19APR12	27APR12	03MAY12	10
1AUD2060	DUCT ROUGH	5	5	0	20APR12	26APR12	04MAY12	10MAY12	10
1AUD2070	INSULATE DUCT	3	3	0	27APR12	01MAY12	11MAY12	15MAY12	10
1AUD2080	ABOVE CEILING FIRE PROTECTION	3	3	0	07MAY12	09MAY12	16MAY12	18MAY12	7
1AUD2090	ABOVE CEILING MECHANICAL	3	3	0	17APR12	19APR12	04MAY12	08MAY12	13
1AUD2100	ABOVE CEILING ELECTRICAL	5	5	0	13APR12	19APR12	02MAY12	08MAY12	13
1AUD2110	ABOVE CEILING LOW VOLTAGE,	5	5	0	13APR12	19APR12	02MAY12	08MAY12	13
1AUD2120	ABOVE CEILING FIRE ALARM	5	5	0	13APR12	19APR12	02MAY12	08MAY12	13
1AUD2130	ABOVE CEILING SECURITY	5	5	0	13APR12	19APR12	02MAY12	08MAY12	13

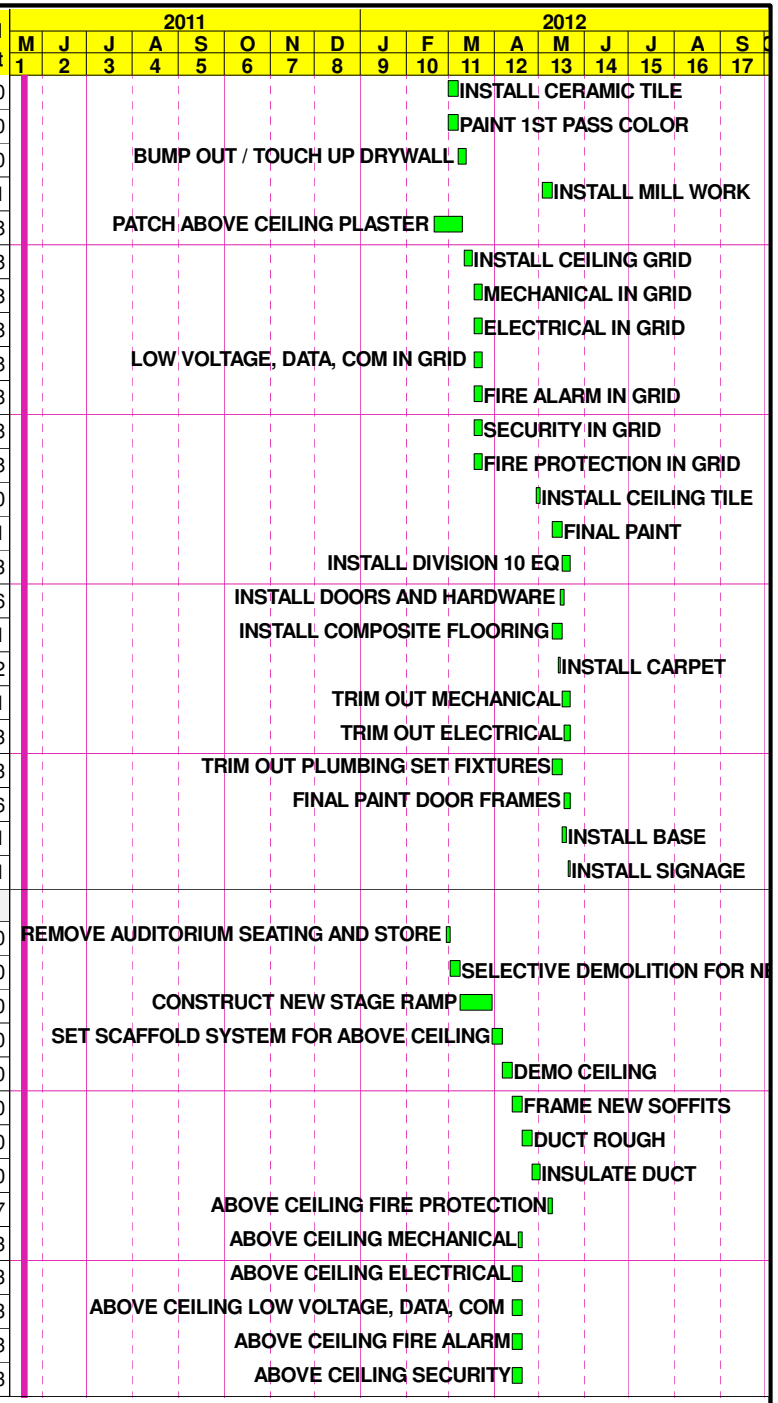

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
1AUD2140	INSTALL DRYWALL SOFFITS	2	2	0	20APR12	23APR12	09MAY12	10MAY12	13
1AUD2150	FINISH DRYWALL	3	3	0	24APR12	26APR12	11MAY12	15MAY12	13
1AUD2160	PRIME PAINT	2	2	0	27APR12	30APR12	16MAY12	17MAY12	13
1AUD2170	1ST PASS COLOR	2	2	0	01MAY12	02MAY12	18MAY12	21MAY12	13
1AUD2175	PATCH ABOVE CEILING PLASTER	11	11	0	10MAY12	24MAY12	21MAY12	05JUN12	7
1AUD2180	INSTALL CEILING GRID	2	2	0	25MAY12	29MAY12	06JUN12	07JUN12	7
1AUD2190	MECHANICAL IN GRID	3	3	0	30MAY12	01JUN12	08JUN12	12JUN12	7
1AUD2200	ELECTRICAL IN GRID	3	3	0	30MAY12	01JUN12	08JUN12	12JUN12	7
1AUD2210	LOW VOLTAGE, DATA, COM IN GRID	3	3	0	30MAY12	01JUN12	08JUN12	12JUN12	7
1AUD2220	FIRE ALARM IN GRID	3	3	0	30MAY12	01JUN12	08JUN12	12JUN12	7
1AUD2230	SECURITY IN GRID	3	3	0	30MAY12	01JUN12	08JUN12	12JUN12	7
1AUD2240	FIRE PROTECTION IN GRID	3	3	0	30MAY12	01JUN12	08JUN12	12JUN12	7
1AUD2245	INSTALL CEILING TILE	2	2	0	05JUN12	06JUN12	14JUN12	15JUN12	7
1AUD2250	TOUCH UP / BUMP OUT SOFFITS	3	3	0	03MAY12	07MAY12	22MAY12	24MAY12	13
1AUD2260	SPOT PRIME AND FINISH PAINT	2	2	0	08MAY12	09MAY12	25MAY12	29MAY12	13
1AUD2270	REMOVE SCAFFOLD SYSTEM	3	3	0	07JUN12	11JUN12	18JUN12	20JUN12	7
1AUD2280	COMPLETE REMAINING MEP ROUGH	5	5	0	12JUN12	18JUN12	21JUN12	27JUN12	7
1AUD2290	PATCH PAINT FINISH DRYWALL	5	5	0	19JUN12	25JUN12	28JUN12	05JUL12	7
1AUD2300	PRIME PAINT 1ST PASS COLOR	2	2	0	26JUN12	27JUN12	11JUL12	12JUL12	10
1AUD2310	FINISH PAINT	2	2	0	03JUL12	05JUL12	13JUL12	16JUL12	7
1AUD2320	REFINISH WOOD FLOORS	5	5	0	26JUN12	02JUL12	06JUL12	12JUL12	7
1AUD2330	REINSTALL SEATING	4	4	0	06JUL12	11JUL12	17JUL12	20JUL12	7
1AUD2340	INSTALL NEW STAGE EQ	7	7	0	06JUL12	16JUL12	23JUL12	31JUL12	11
EXTERIOR									
1AEX2000	REMOVE AND REPLACE OLD	15	15	0	07DEC11	28DEC11	04JAN12	24JAN12	18
1AEX2010	PREP EXTERIOR TO RECEIVE NEW	20	20	0	10APR12	07MAY12	19APR12	16MAY12	7
1AEX2020	PREP AND REMEDIATE EXIST EXT	20	20	0	08MAY12	05JUN12	17MAY12	14JUN12	7
TESTING & INSPECTIONS									
1ATN2000	PLUMBING / STACK	1	1	0	28DEC11	28DEC11	09JAN12	09JAN12	7
1ATN2010	UG ELECTRICAL	1	1	0	24JAN12	24JAN12	03FEB12	03FEB12	8
1ATN2020	UG MECH PIPING	1	1	0	22SEP11	22SEP11	13OCT11	13OCT11	15
1ATN2030	UG FIRE PROTECTION RISER ASS.	1	1	0	18JAN12	18JAN12	02FEB12	02FEB12	11
1ATN2040	LIGHTNING PROTECTION BOND FTG	1	1	0	20APR12	20APR12	01MAY12	01MAY12	7
1ATN2050	COLUMN FOOTING / BOLT PROJ	1	1	0	18OCT11	18OCT11	28OCT11	28OCT11	8
1ATN2060	FOUNDATION	1	1	0	22NOV11	22NOV11	06DEC11	06DEC11	8
1ATN2070	STEM WALL	1	1	0	02DEC11	02DEC11	23DEC11	23DEC11	15
1ATN2080	PEST CONTROL	1	1	0	12DEC11	12DEC11	21DEC11	21DEC11	7
1ATN2090	VAPOR BARRIER / REINFORCING	1	1	0	14DEC11	14DEC11	23DEC11	23DEC11	7
1ATN2100	CMU LIFT 1 (x2)	1	1	0	21DEC11	21DEC11	03JAN12	03JAN12	7

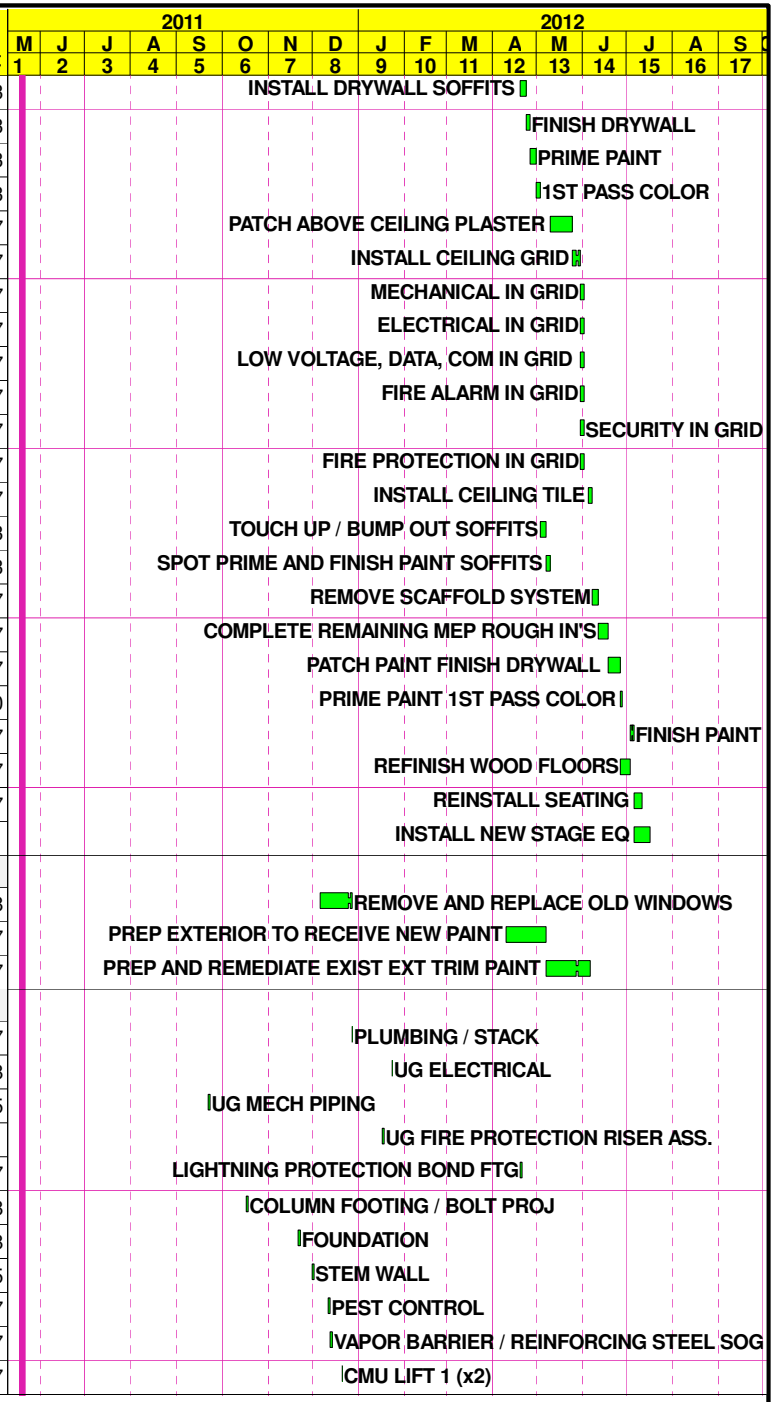

Start Date 20MAY11
Finish Date 30AUG12
Data Date 20MAY11
Run Date 12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0 Sheet 37 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
1ATN2110	CMU LIFT 2 (x2)	1	1	0	28DEC11	28DEC11	09JAN12	09JAN12	7
1ATN2120	BEAM / LINTEL (x2)	1	1	0	04JAN12	04JAN12	26JAN12	26JAN12	16
1ATN2130	STEEL COLUMN, BEAM, JOIST	1	1	0	09JAN12	09JAN12	18JAN12	18JAN12	7
1ATN2140	DECKING	1	1	0	12JAN12	12JAN12	26JAN12	26JAN12	10
1ATN2150	WELDING	1	1	0	16JAN12	16JAN12	09FEB12	09FEB12	18
1ATN2160	ROOF INSULATION	1	1	0	17FEB12	17FEB12	06MAR12	06MAR12	12
1ATN2170	ROOF MEMBRANE	1	1	0	28FEB12	28FEB12	15MAR12	15MAR12	12
1ATN2180	FINAL ROOF	1	1	0	06APR12	06APR12	18APR12	18APR12	8
1ATN2190	IN WALL MECHANICAL 1.0	1	1	0	22DEC11	22DEC11	04JAN12	04JAN12	7
1ATN2195	IN WALL MECHANICAL 20.	1	1	0	22DEC11	22DEC11	04JAN12	04JAN12	7
1ATN2200	IN WALL ELECTRICAL 1.0	1	1	0	22DEC11	22DEC11	04JAN12	04JAN12	7
1ATN2205	IN WALL ELECTRICAL 2.0	1	1	0	16JAN12	16JAN12	01FEB12	01FEB12	12
1ATN2210	IN WALL LOW VOLTAGE, DATA, COM	1	1	0	22DEC11	22DEC11	04JAN12	04JAN12	7
1ATN2215	IN WALL LOW VOLTAGE, DATA, COM	1	1	0	16JAN12	16JAN12	01FEB12	01FEB12	12
1ATN2220	IN WALL FIRE ALARM 1.0	1	1	0	22DEC11	22DEC11	04JAN12	04JAN12	7
1ATN2225	IN WALL FIRE ALARM 2.0	1	1	0	16JAN12	16JAN12	01FEB12	01FEB12	12
1ATN2230	IN WALL SECURITY 1.0	1	1	0	22DEC11	22DEC11	04JAN12	04JAN12	7
1ATN2235	IN WALL SECURITY 2.0	1	1	0	16JAN12	16JAN12	01FEB12	01FEB12	12
1ATN2240	IN WALL PLUMBING 1.0	1	1	0	22DEC11	22DEC11	04JAN12	04JAN12	7
1ATN2245	IN WALL PLUMBING 2.0	1	1	0	16JAN12	16JAN12	01FEB12	01FEB12	12
1ATN2246	FRAMING 1.0	1	1	0	18JAN12	18JAN12	30JAN12	30JAN12	8
1ATN2247	FRAMING 2.0	1	1	0	17JAN12	17JAN12	02FEB12	02FEB12	12
1ATN2250	ROUGH DUCT 1.0	1	1	0	08FEB12	08FEB12	21FEB12	21FEB12	9
1ATN2255	ROUGH DUCT 2.0	1	1	0	01FEB12	01FEB12	22FEB12	22FEB12	15
1ATN2260	DUCT INSULATION 1.0	1	1	0	09FEB12	09FEB12	22FEB12	22FEB12	9
1ATN2265	DUCT INSULATION 2.0	1	1	0	02FEB12	02FEB12	23FEB12	23FEB12	15
1ATN2270	WINDOW SET	1	1	0	29DEC11	29DEC11	25JAN12	25JAN12	18
1ATN2280	BELOW GROUND HYDRO	1	1	0	18JAN12	18JAN12	02FEB12	02FEB12	11
1ATN2290	ABOVE GROUND HYDRO 1.0	1	1	0	14MAR12	14MAR12	26MAR12	26MAR12	8
1ATN2295	ABOVE GROUND HYDRO 2.0	1	1	0	10MAY12	10MAY12	29MAY12	29MAY12	12
1ATN2300	ABOVE CEILING MECH / PIPING 1.0	1	1	0	14MAR12	14MAR12	26MAR12	26MAR12	8
1ATN2305	ABOVE CEILING MECH / PIPING 2.0	1	1	0	26MAR12	26MAR12	09APR12	09APR12	10
1ATN2310	ABOVE CEILING PLUMBING 1.0	1	1	0	16JAN12	16JAN12	09FEB12	09FEB12	18
1ATN2315	ABOVE CEILING PLUMBING 2.0	1	1	0	30JAN12	30JAN12	15FEB12	15FEB12	12
1ATN2320	ABOVE CEILING ELECTRICAL 1.0	1	1	0	14MAR12	14MAR12	26MAR12	26MAR12	8
1ATN2325	ABOVE CEILING ELECTRICAL 2.0	1	1	0	26MAR12	26MAR12	09APR12	09APR12	10
1ATN2330	ABOVE CEILING LOW VOLTAGE,	1	1	0	14MAR12	14MAR12	26MAR12	26MAR12	8
1ATN2335	ABOVE CEILING LOW VOLTAGE,	1	1	0	26MAR12	26MAR12	09APR12	09APR12	10
1ATN2340	ABOVE CEILING FIRE ALARM 1.0	1	1	0	15MAR12	15MAR12	27MAR12	27MAR12	8

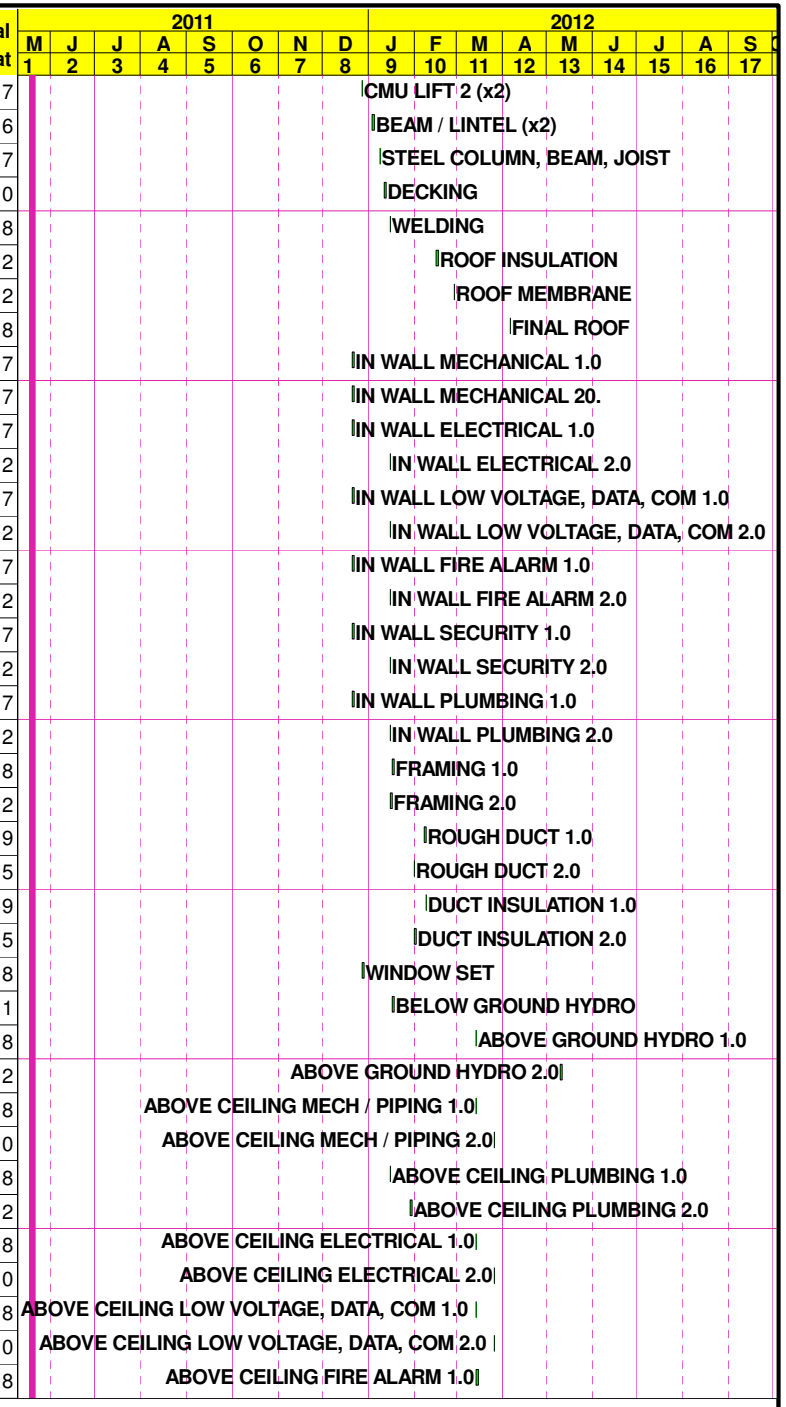

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

Sheet 38 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
1ATN2345	ABOVE CEILING FIRE ALARM 2.0	1	1	0	26MAR12	26MAR12	09APR12	09APR12	10
1ATN2350	ABOVE CEILING SECURITY 1.0	1	1	0	15MAR12	15MAR12	27MAR12	27MAR12	8
1ATN2355	ABOVE CEILING SECURITY 2.0	1	1	0	26MAR12	26MAR12	09APR12	09APR12	10
1ATN2360	MECH / PIPING INSULATION 1.0	1	1	0	16JAN12	16JAN12	09FEB12	09FEB12	18
1ATN2365	MECH / PIPING INSULATION 2.0	1	1	0	30JAN12	30JAN12	15FEB12	15FEB12	12
1ATN2370	PLUMBING INSULATION 1.0	1	1	0	16JAN12	16JAN12	09FEB12	09FEB12	18
1ATN2375	PLUMBING INSULATION 2.0	1	1	0	30JAN12	30JAN12	15FEB12	15FEB12	12
1ATN2380	HARD CEILING COVER UP 1.0	1	1	0	31JAN12	31JAN12	10FEB12	10FEB12	8
1ATN2385	HARD CEILING COVER UP 2.0	1	1	0	07FEB12	07FEB12	27FEB12	27FEB12	14
1ATN2387	ABOVE CEILING FINAL 1.0	1	1	0	16MAR12	16MAR12	28MAR12	28MAR12	8
1ATN2388	ABOVE CEILING FINAL 2.0	1	1	0	27MAR12	27MAR12	10APR12	10APR12	10
1ATN2389	ABOVE CEILING FINAL AUDITORIUM	1	1	0	04JUN12	04JUN12	13JUN12	13JUN12	7
1ATN2390	MECH EQ	1	1	0	08FEB12	08FEB12	21FEB12	21FEB12	9
1ATN2400	ELECTRICAL TRIM 1.0	1	1	0	18MAY12	18MAY12	12JUN12	12JUN12	16
1ATN2405	ELECTRICAL TRIM 2.0	1	1	0	23MAY12	23MAY12	12JUN12	12JUN12	13
1ATN2410	PLUMBING TRIM 1.0	1	1	0	10MAY12	10MAY12	30MAY12	30MAY12	13
1ATN2415	PLUMBING TRIM 2.0	1	1	0	21MAY12	21MAY12	06JUN12	06JUN12	11
1ATN2420	FINAL MECHANICAL	1	1	0	22MAY12	22MAY12	11JUN12	11JUN12	13
1ATN2430	FINAL ELECTRICAL	1	1	0	24MAY12	24MAY12	13JUN12	13JUN12	13
1ATN2440	FINAL PLUMBING	1	1	0	17MAY12	17MAY12	12JUN12	12JUN12	17
1ATN2450	FINAL FIRE ALARM	1	1	0	13JUL12	13JUL12	02AUG12	02AUG12	14
1ATN2460	FINAL SECURITY	1	1	0	25MAY12	25MAY12	14JUN12	14JUN12	13
1ATN2470	LIFE SAFETY WATER FOR FFE	1	1	0	12JUL12	12JUL12	23JUL12	23JUL12	7
1ATN2490	SIGNAGE	1	1	0	11MAY12	11MAY12	29MAY12	29MAY12	11
1ATN2500	LIGHTNING PROTECTION	1	1	0	16APR12	16APR12	01MAY12	01MAY12	11
REQUIRED DOCUMENTS									
1ARD2000	BUILDING FINAL W / ATTACHED	1	1	0	17JUL12	17JUL12	06AUG12	06AUG12	14
1ARD2010	FIRE SPRINKLER FINAL NFPA 13	1	1	0	13JUL12	13JUL12	03AUG12	03AUG12	15
1ARD2020	FIRE ALARM NFPA 72 FORM	1	1	0	16JUL12	16JUL12	03AUG12	03AUG12	14
1ARD2030	PLUMBING BACT TEST @ SAMPLE	10	10	0	18MAY12	01JUN12	13JUN12	26JUN12	17
1ARD2040	MECHANICAL T&B	5	5	0	23MAY12	30MAY12	12JUN12	18JUN12	13
1ARD2050	ELECTRICAL FINAL	1	1	0	25MAY12	25MAY12	14JUN12	14JUN12	13
1ARD2060	SECURITY SYSTEM FINAL SONITROL	1	1	0	29MAY12	29MAY12	15JUN12	15JUN12	13
1ARD2070	COMMUNICATION SYSTEM FINAL	1	1	0	25MAY12	25MAY12	14JUN12	14JUN12	13
1ARD2100	LIGHTNING PROTECTION UL	10	10	0	23APR12	04MAY12	02MAY12	15MAY12	7
1ARD2110	ROOFING FINAL	1	1	0	09APR12	09APR12	19APR12	19APR12	8
1ARD2120	SITE UG WATER PAPERS FLUSH	1	1	0	19JAN12	19JAN12	03FEB12	03FEB12	11
1ARD2130	ENERGY MANAGEMENT	1	1	0	29MAY12	29MAY12	15JUN12	15JUN12	13
1ARD2140	FIRE ALARM MONITORING	1	1	0	29MAY12	29MAY12	15JUN12	15JUN12	13

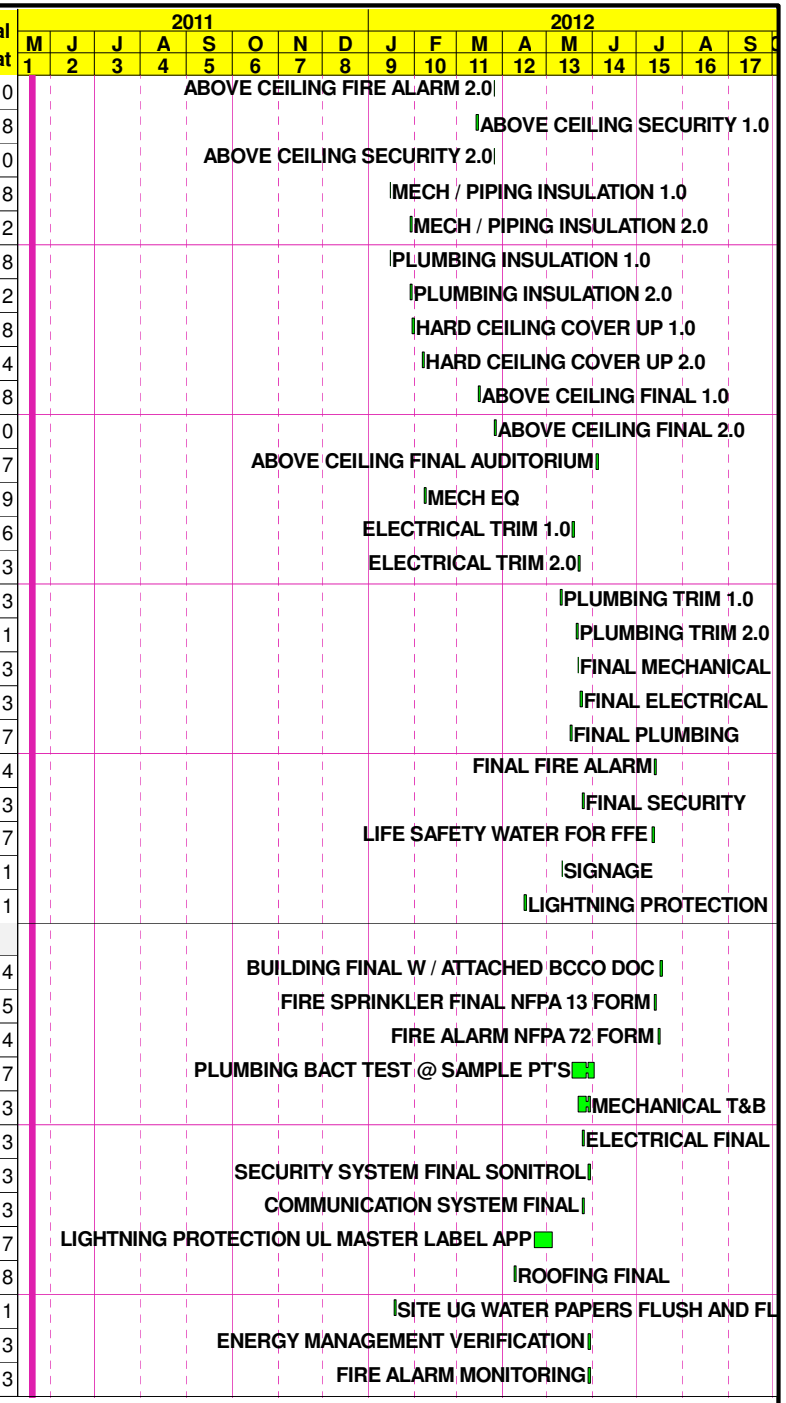

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
COMPLETION & PUNCH									
1APL2000	DOSTER PRE PUNCH LIST	5	5	0	12JUN12	18JUN12	15JUN12	21JUN12	3
1APL2010	COMPLETE DOSTER PRE PUNCH	10	10	0	19JUN12	02JUL12	22JUN12	06JUL12	3
1APL2020	COMPLETE OCPS QAQC LIST	5	5	0	03JUL12	10JUL12	09JUL12	13JUL12	3
1APL2030	OWNER ARCHITECT GENERATE	3	3	0	16JUL12	18JUL12	03AUG12	07AUG12	14
1APL2040	RECEIVE OWNER FINAL PUNCH LIST	1	1	0	24JUL12	24JUL12	08AUG12	08AUG12	11
1APL2050	COMPLETE OWNER ARCHITECT	15	15	0	25JUL12	14AUG12	09AUG12	29AUG12	11
BLDG 1B NEW KITCHEN									
MILESTONES									
1BMS2000	BUILDING SLAB IN PLACE	0	0	0		21MAR12		16APR12	18
1BMS2010	SHELL / DRYING	0	0	0		15MAY12		12JUN12	19
1BMS2020	ENERGIZE	1	1	0	24MAY12	24MAY12	12JUN12	12JUN12	12
1BMS2030	CONDITIONED AIR	1	1	0	25MAY12	25MAY12	13JUN12	13JUN12	12
1BMS2040	FFE	0	0	0		18JUN12		12JUL12	17
1BMS2050	SUBSTANTIAL COMPLETE	1	1	0	03JUL12	03JUL12	20JUL12	20JUL12	12
1BMS2060	SUB COMPLETION LIST COMPLETE	1	1	0	12JUL12	12JUL12	02AUG12	02AUG12	15
1BMS2070	OWNER ARCHITECT PUNCH	1	1	0	09AUG12	09AUG12	30AUG12	30AUG12	15
UNDERGROUND									
1BUG2000	LAY OUT BUILDING CORNERS	1	1	0	01FEB12	01FEB12	15FEB12	15FEB12	10
1BUG2020	DEEP FOUNDATION SLEEVES	1	1	0	07FEB12	07FEB12	02MAR12	02MAR12	18
1BUG2030	UG CHILLED WATER	2	2	0	02FEB12	03FEB12	16FEB12	17FEB12	10
1BUG2040	UG PLUMBING	5	5	0	02FEB12	08FEB12	22FEB12	28FEB12	14
1BUG2050	UG PRIMARIES ELECTRICAL	2	2	0	02FEB12	03FEB12	21FEB12	22FEB12	13
1BUG2060	UG SECONDARY'S ELECTRICAL	5	5	0	09FEB12	15FEB12	29FEB12	06MAR12	14
1BUG2070	UG FIRE PROTECTION	1	1	0	07MAR12	07MAR12	19MAR12	19MAR12	8
1BUG2080	UG LIGHTNING PROTECTION	1	1	0	17FEB12	17FEB12	08MAR12	08MAR12	14
1BUG2090	BACK FILL COMPACT	3	3	0	08MAR12	12MAR12	20MAR12	22MAR12	8
STRUCTURE									
1BST2000	EXCAVATE FOUNDATIONS	3	3	0	02FEB12	06FEB12	28FEB12	01MAR12	18
1BST2010	INSTALL REINFORCING STEEL	2	2	0	08FEB12	09FEB12	05MAR12	06MAR12	18
1BST2020	PLACE FOUNDATION	1	1	0	27FEB12	27FEB12	08MAR12	08MAR12	8
1BST2030	INSTALL STEM WALLS / FILL CELL	3	3	0	28FEB12	01MAR12	09MAR12	13MAR12	8
1BST2035	BACKFILL STEM WALLS	2	2	0	05MAR12	06MAR12	15MAR12	16MAR12	8
1BST2040	FINE GRADE	2	2	0	13MAR12	14MAR12	23MAR12	26MAR12	8
1BST2050	PEST CONTROL SPRAY	1	1	0	15MAR12	15MAR12	27MAR12	27MAR12	8
1BST2060	INSTALL VAPOR BARRIER &	1	1	0	19MAR12	19MAR12	29MAR12	29MAR12	8
1BST2070	PLACE SOG	1	1	0	21MAR12	21MAR12	02APR12	02APR12	8
1BST2072	FRP STAIRS AND RAMPS	5	5	0	28MAR12	03APR12	11APR12	17APR12	10
1BST2080	1ST LIFT MASONRY WALLS	4	4	0	22MAR12	27MAR12	17APR12	20APR12	18

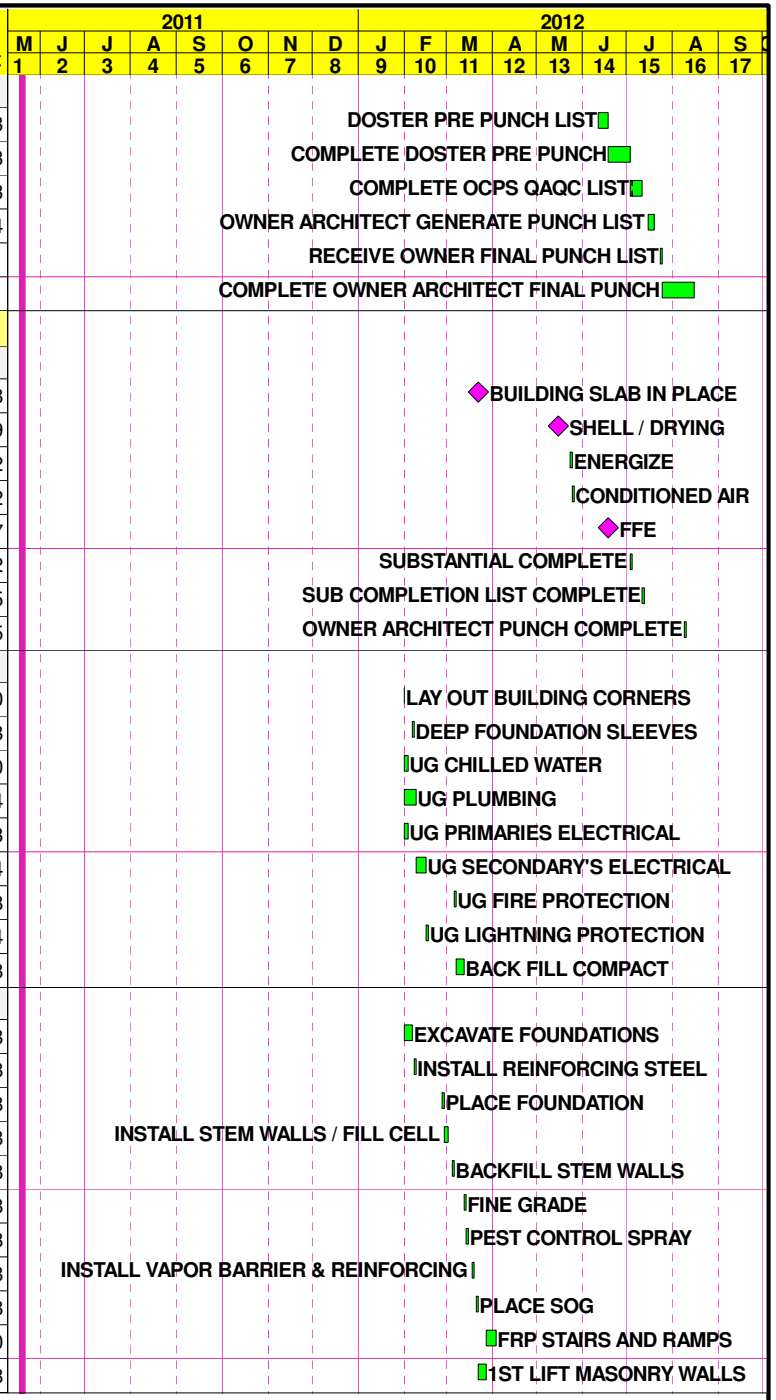

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
1BST2090	2ND LIFT MASONRY WALLS	4	4	0	29MAR12	03APR12	24APR12	27APR12	18
1BST2100	BEAMS AND LINTELS	4	4	0	05APR12	10APR12	01MAY12	04MAY12	18
1BST2110	INSTALL STEEL	4	4	0	12APR12	17APR12	08MAY12	11MAY12	18
1BST2120	INSTALL DECKING	3	3	0	19APR12	23APR12	15MAY12	17MAY12	18
ROOF									
1BRF2004	ROOF TOP DRAINS AND MEP	3	3	0	24APR12	26APR12	18MAY12	22MAY12	18
1BRF2006	INSTALL ROOF TOP CURBS	2	2	0	24APR12	25APR12	18MAY12	21MAY12	18
1BRF2008	INSTALL TAPER INSULATION	3	3	0	27APR12	01MAY12	23MAY12	25MAY12	18
1BRF2010	INSTALL LIGHT WEIGHT CONCRETE	3	3	0	02MAY12	04MAY12	29MAY12	31MAY12	18
1BRF2020	INSTALL ROOFING MATERIALS	7	7	0	07MAY12	15MAY12	01JUN12	11JUN12	18
1BRF2030	INSTALL PARAPET CAPS	4	4	0	17MAY12	22MAY12	13JUN12	18JUN12	18
1BRF2040	INSTALL MEP EQUIPMENT	4	4	0	23MAY12	29MAY12	20JUN12	25JUN12	19
1BRF2050	INSTALL LIGHTNING PROTECTION	2	2	0	30MAY12	31MAY12	26JUN12	27JUN12	19
INTERIOR 1ST FLOOR									
1BFF3000	1ST LIFT MASONRY	4	4	0	22MAR12	27MAR12	17APR12	20APR12	18
1BFF3010	2ND LIFT MASONRY	4	4	0	29MAR12	03APR12	24APR12	27APR12	18
1BFF3020	LINTEL / BEAM	2	2	0	05APR12	06APR12	03MAY12	04MAY12	20
1BFF3030	FRAME WALLS	4	4	0	22MAR12	27MAR12	03APR12	06APR12	8
1BFF3040	TOP OUT FIRE SMOKE WALLS	2	2	0	28MAR12	29MAR12	12APR12	13APR12	11
1BFF3050	1 SIDE MECH AND ELE ROOMS	2	2	0	28MAR12	29MAR12	13APR12	16APR12	12
1BFF3052	IN WALL MECHANICAL	5	5	0	28MAR12	03APR12	09APR12	13APR12	8
1BFF3060	IN WALL ELECTRICAL	5	5	0	28MAR12	03APR12	09APR12	13APR12	8
1BFF3070	IN WALL LOW VOLTAGE, DATA, COM	5	5	0	28MAR12	03APR12	09APR12	13APR12	8
1BFF3080	IN WALL FIRE ALARM	5	5	0	28MAR12	03APR12	09APR12	13APR12	8
1BFF3082	IN WALL SECURITY	5	5	0	28MAR12	03APR12	09APR12	13APR12	8
1BFF3090	IN WALL PLUMBING	5	5	0	28MAR12	03APR12	09APR12	13APR12	8
1BFF3100	ROUGH DUCT	7	7	0	30MAR12	09APR12	16APR12	24APR12	11
1BFF3105	INSULATE DUCT	5	5	0	13APR12	19APR12	26APR12	02MAY12	9
1BFF3110	ROUGH RAIN LEADERS	3	3	0	30MAR12	03APR12	17APR12	19APR12	12
1BFF3140	ABOVE CEILING FIRE PROTECTION	3	3	0	30MAR12	03APR12	17APR12	19APR12	12
1BFF3150	ABOVE CEILING MECHANICAL	5	5	0	30MAR12	05APR12	17APR12	23APR12	12
1BFF3160	ABOVE CEILING PLUMBING	5	5	0	04APR12	10APR12	20APR12	26APR12	12
1BFF3170	ABOVE CEILING ELECTRICAL	10	10	0	04APR12	17APR12	24APR12	07MAY12	14
1BFF3180	ABOVE CEILING LOW VOLTAGE,	5	5	0	04APR12	10APR12	30APR12	04MAY12	18
1BFF3190	ABOVE CEILING FIRE ALARM	5	5	0	04APR12	10APR12	30APR12	04MAY12	18
1BFF3200	ABOVE CEILING SECURITY	5	5	0	04APR12	10APR12	30APR12	04MAY12	18
1BFF3220	TIE IN MECHANICAL	2	2	0	10APR12	11APR12	23APR12	24APR12	9
1BFF3230	SET PANELS ELE ROOM	2	2	0	30MAR12	02APR12	17APR12	18APR12	12
1BFF3235	SET MDP AND STEP TRANS	3	3	0	07FEB12	09FEB12	05MAR12	07MAR12	19

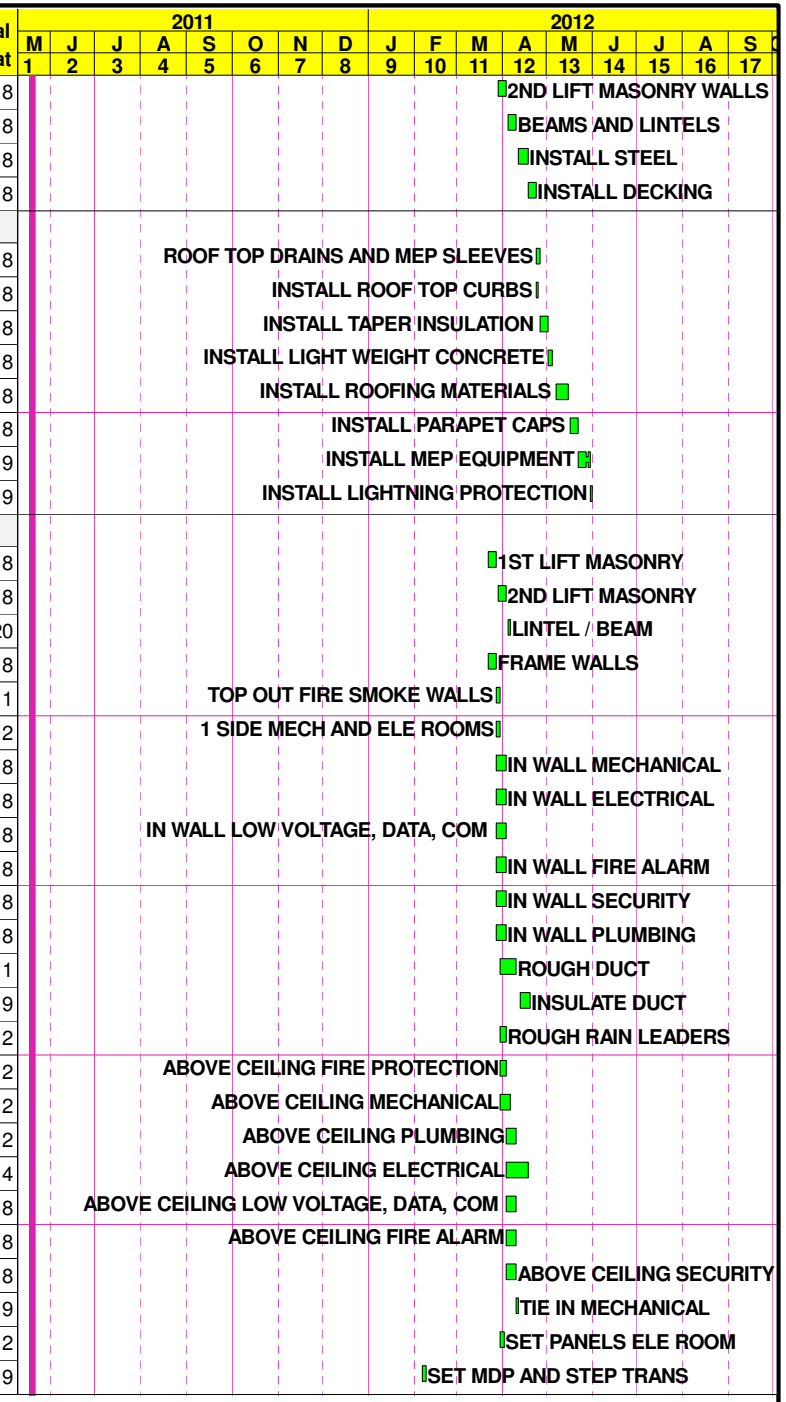

Start Date 20MAY11
Finish Date 30AUG12
Data Date 20MAY11
Run Date 12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
1BFF3240	MEP HOUSE KEEPING PADS	2	2	0	30MAR12	02APR12	17APR12	18APR12	12
1BFF3250	SET MEP EQ	2	2	0	06APR12	09APR12	19APR12	20APR12	9
1BFF3260	INSULATE WALLS	2	2	0	04APR12	05APR12	16APR12	17APR12	8
1BFF3270	INSTALL DRYWALL	3	3	0	10APR12	12APR12	20APR12	24APR12	8
1BFF3280	FINISH DRYWALL	4	4	0	13APR12	18APR12	25APR12	30APR12	8
1BFF3285	FRAME HARD CEILINGS	1	1	0	13APR12	13APR12	30APR12	30APR12	11
1BFF3290	INSTALL HARD CEILINGS	1	1	0	23APR12	23APR12	02MAY12	02MAY12	7
1BFF3300	FINISH HARD CEILINGS	5	5	0	26APR12	02MAY12	08MAY12	14MAY12	8
1BFF3310	SET COOLER, FREEZER, AND HOOD	5	5	0	19APR12	25APR12	01MAY12	07MAY12	8
1BFF3320	POINT UP MASONRY	2	2	0	16APR12	17APR12	11MAY12	14MAY12	19
1BFF3330	PRIME PAINT	2	2	0	03MAY12	04MAY12	15MAY12	16MAY12	8
1BFF3340	INSTALL CERAMIC TILE	10	10	0	07MAY12	18MAY12	17MAY12	31MAY12	8
1BFF3350	PAINT 1ST PASS COLOR	3	3	0	07MAY12	09MAY12	24MAY12	29MAY12	13
1BFF3360	BUMP OUT / TOUCH UP DRYWALL	2	2	0	10MAY12	11MAY12	30MAY12	31MAY12	13
1BFF3370	INSTALL MILL WORK	3	3	0	25MAY12	30MAY12	13JUN12	15JUN12	12
1BFF3380	INSTALL CEILING GRID	2	2	0	15MAY12	16MAY12	01JUN12	04JUN12	12
1BFF3385	DELIVER KITCHEN EQ	3	3	0	18MAY12	22MAY12	13JUN12	15JUN12	17
1BFF3390	MECHANICAL IN GRID	5	5	0	25MAY12	01JUN12	15JUN12	21JUN12	14
1BFF3400	ELECTRICAL IN GRID	4	4	0	17MAY12	22MAY12	05JUN12	08JUN12	12
1BFF3410	LOW VOLTAGE, DATA, COM IN GRID	5	5	0	17MAY12	23MAY12	07JUN12	13JUN12	14
1BFF3420	FIRE ALARM IN GRID	5	5	0	17MAY12	23MAY12	07JUN12	13JUN12	14
1BFF3430	SECURITY IN GRID	5	5	0	17MAY12	23MAY12	07JUN12	13JUN12	14
1BFF3440	FIRE PROTECTION IN GRID	3	3	0	17MAY12	21MAY12	15JUN12	19JUN12	20
1BFF3445	INSTALL CEILING TILE	2	2	0	07JUN12	08JUN12	27JUN12	28JUN12	14
1BFF3450	FINAL PAINT	4	4	0	31MAY12	05JUN12	18JUN12	21JUN12	12
1BFF3460	INSTALL DIVISION 10 EQ	2	2	0	06JUN12	07JUN12	29JUN12	02JUL12	17
1BFF3480	INSTALL DOORS AND HARDWARE	2	2	0	08JUN12	11JUN12	03JUL12	05JUL12	17
1BFF3490	INSTALL COMPOSITE FLOORING	10	10	0	31MAY12	13JUN12	18JUN12	29JUN12	12
1BFF3500	INSTALL CARPET	2	2	0	31MAY12	01JUN12	28JUN12	29JUN12	20
1BFF3510	TRIM OUT MECHANICAL	5	5	0	06JUN12	12JUN12	27JUN12	03JUL12	15
1BFF3520	TRIM OUT ELECTRICAL	4	4	0	06JUN12	11JUN12	26JUN12	29JUN12	14
1BFF3530	TRIM OUT PLUMBING SET FIXTURES	4	4	0	06JUN12	11JUN12	22JUN12	27JUN12	12
1BFF3540	FINAL PAINT DOOR FRAMES	3	3	0	12JUN12	14JUN12	06JUL12	10JUL12	17
1BFF3550	INSTALL BASE	2	2	0	14JUN12	15JUN12	02JUL12	03JUL12	12
1BFF3560	INSTALL SIGNAGE	1	1	0	06JUN12	06JUN12	02JUL12	02JUL12	18
EXTERIOR									
1BEX2000	INSTALL WINDOWS	2	2	0	11APR12	12APR12	07MAY12	08MAY12	18
1BEX2010	PREP / LATH / BEAD	5	5	0	16APR12	20APR12	11MAY12	17MAY12	19
1BEX2020	SCRATCH COAT	3	3	0	23APR12	25APR12	18MAY12	22MAY12	19

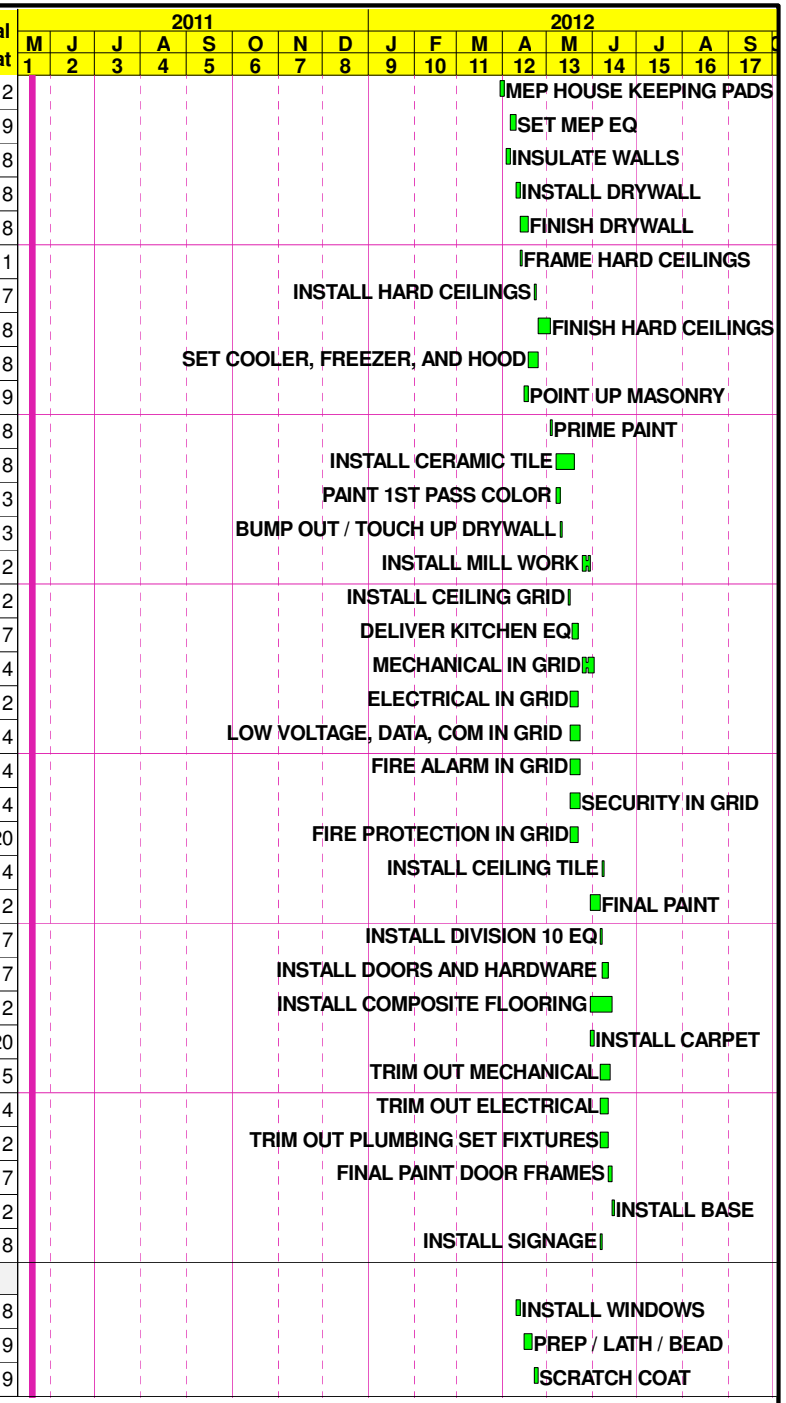

Start Date 20MAY11
Finish Date 30AUG12
Data Date 20MAY11
Run Date 12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
1BEX2030	BROWN COAT	3	3	0	01MAY12	03MAY12	25MAY12	30MAY12	18
1BEX2040	FINISH COAT	3	3	0	11MAY12	15MAY12	31MAY12	04JUN12	13
1BEX2050	PLASTER CURE	15	15	0	16MAY12	06JUN12	05JUN12	25JUN12	13
1BEX2060	PRIME PAINT	3	3	0	07JUN12	11JUN12	26JUN12	28JUN12	13
1BEX2070	1ST PASS COLOR	3	3	0	12JUN12	14JUN12	29JUN12	03JUL12	13
1BEX2080	FINISH PAINT	3	3	0	15JUN12	19JUN12	05JUL12	09JUL12	13
1BEX2090	INSTALL CANOPY FOUNDATIONS	5	5	0	13JUN12	19JUN12	02JUL12	09JUL12	13
1BEX2100	INSTALL CANOPY E & D	9	9	0	20JUN12	02JUL12	10JUL12	20JUL12	13
1BEX2110	FRP SIDE WALKS CANOPY E & D	10	10	0	05JUL12	18JUL12	31JUL12	13AUG12	18
TESTING & INSPECTIONS									
1BTN2000	UG PLUMBING / STACK	1	1	0	09FEB12	09FEB12	29FEB12	29FEB12	14
1BTN2010	UG ELECTRICAL	1	1	0	16FEB12	16FEB12	07MAR12	07MAR12	14
1BTN2020	UG MECH PIPING	1	1	0	06FEB12	06FEB12	20FEB12	20FEB12	10
1BTN2030	UG FIRE PROTECTION RISER ASS.	1	1	0	08MAR12	08MAR12	30MAR12	30MAR12	16
1BTN2040	LIGHTNING PROTECTION BOND FTG	1	1	0	28OCT11	28OCT11	28OCT11	28OCT11	0
1BTN2060	FOUNDATION	1	1	0	10FEB12	10FEB12	07MAR12	07MAR12	18
1BTN2070	STEM WALL	1	1	0	02MAR12	02MAR12	14MAR12	14MAR12	8
1BTN2080	PEST CONTROL	1	1	0	16MAR12	16MAR12	28MAR12	28MAR12	8
1BTN2090	VAPOR BARRIER / REINFORCING	1	1	0	20MAR12	20MAR12	30MAR12	30MAR12	8
1BTN2100	CMU LIFT 1	1	1	0	28MAR12	28MAR12	23APR12	23APR12	18
1BTN2110	CMU LIFT 2	1	1	0	04APR12	04APR12	30APR12	30APR12	18
1BTN2120	BEAM / LINTEL	1	1	0	11APR12	11APR12	07MAY12	07MAY12	18
1BTN2130	STEEL COLUMN, BEAM, JOIST	1	1	0	18APR12	18APR12	14MAY12	14MAY12	18
1BTN2140	DECKING	1	1	0	26APR12	26APR12	22MAY12	22MAY12	18
1BTN2150	WELDING	1	1	0	04MAY12	04MAY12	01JUN12	01JUN12	19
1BTN2160	ROOF INSULATION	2	2	0	07MAY12	08MAY12	01JUN12	04JUN12	18
1BTN2170	ROOF MEMBRANE	1	1	0	16MAY12	16MAY12	12JUN12	12JUN12	18
1BTN2180	FINAL ROOF	1	1	0	23MAY12	23MAY12	19JUN12	19JUN12	18
1BTN2190	IN WALL MECHANICAL	1	1	0	04APR12	04APR12	18APR12	18APR12	10
1BTN2200	IN WALL ELECTRICAL	1	1	0	04APR12	04APR12	18APR12	18APR12	10
1BTN2210	IN WALL LOW VOLTAGE, DATA, COM	1	1	0	04APR12	04APR12	18APR12	18APR12	10
1BTN2220	IN WALL FIRE ALARM	1	1	0	04APR12	04APR12	18APR12	18APR12	10
1BTN2230	IN WALL SECURITY	1	1	0	04APR12	04APR12	18APR12	18APR12	10
1BTN2240	IN WALL PLUMBING	1	1	0	04APR12	04APR12	18APR12	18APR12	10
1BTN2245	WALL INSULATION	1	1	0	06APR12	06APR12	18APR12	18APR12	8
1BTN2246	FRAMING	1	1	0	09APR12	09APR12	19APR12	19APR12	8
1BTN2250	ROUGH DUCT	1	1	0	12APR12	12APR12	25APR12	25APR12	9
1BTN2260	DUCT INSULATION	1	1	0	20APR12	20APR12	03MAY12	03MAY12	9
1BTN2270	WINDOW SET	1	1	0	13APR12	13APR12	10MAY12	10MAY12	19

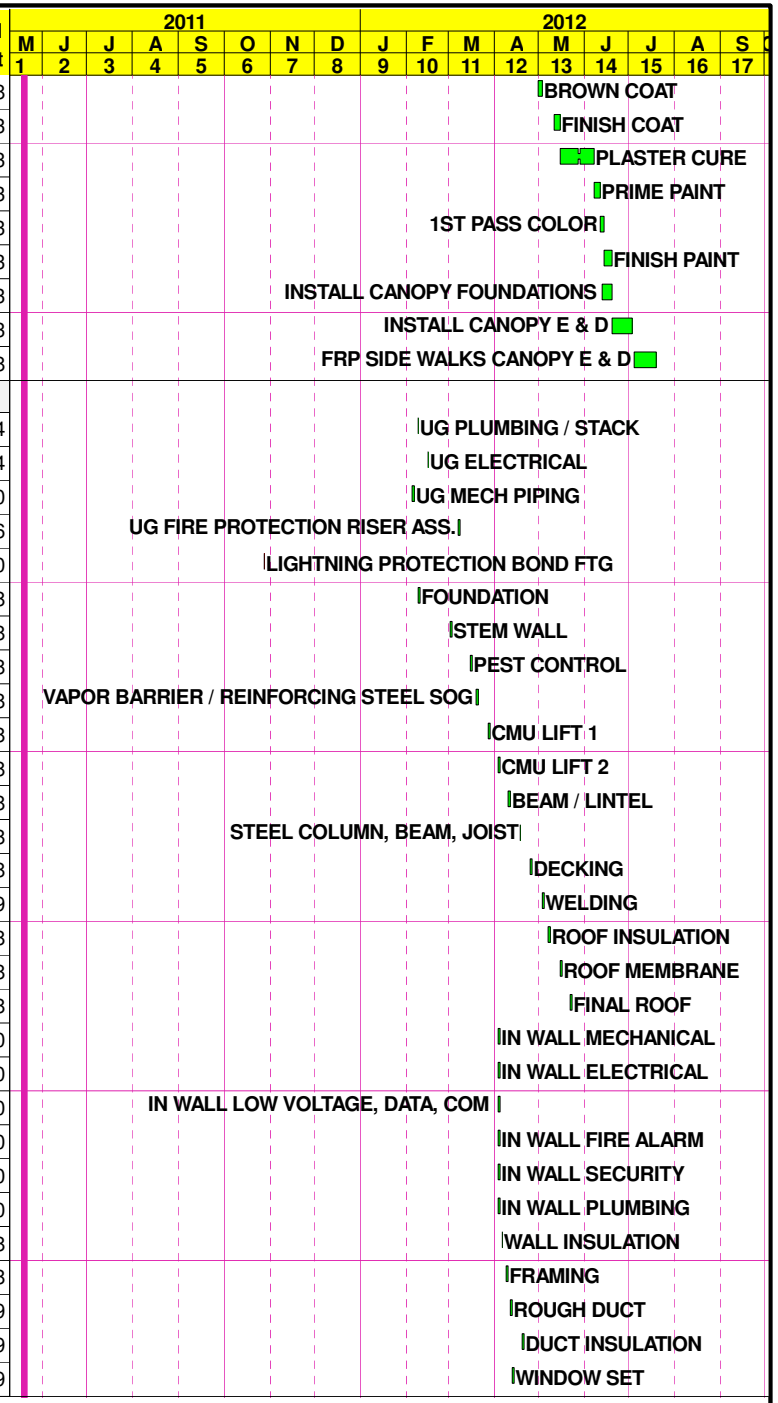

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
1BTN2280	BELOW GROUND HYDRO	1	1	0	15MAR12	15MAR12	27MAR12	27MAR12	8
1BTN2290	ABOVE GROUND HYDRO	1	1	0	25MAY12	25MAY12	20JUN12	20JUN12	17
1BTN2300	ABOVE CEILING MECH PIPING	1	1	0	04JUN12	04JUN12	22JUN12	22JUN12	14
1BTN2310	ABOVE CEILING PLUMBING	1	1	0	11APR12	11APR12	27APR12	27APR12	12
1BTN2320	ABOVE CEILING ELECTRICAL	1	1	0	23MAY12	23MAY12	11JUN12	11JUN12	12
1BTN2330	ABOVE CEILING LOW VOLTAGE,	1	1	0	24MAY12	24MAY12	14JUN12	14JUN12	14
1BTN2340	ABOVE CEILING FIRE ALARM	1	1	0	24MAY12	24MAY12	14JUN12	14JUN12	14
1BTN2350	ABOVE CEILING SECURITY	1	1	0	24MAY12	24MAY12	14JUN12	14JUN12	14
1BTN2360	MECH PIPING INSULATION	1	1	0	05JUN12	05JUN12	25JUN12	25JUN12	14
1BTN2370	PLUMBING INSULATION	1	1	0	12APR12	12APR12	30APR12	30APR12	12
1BTN2375	ABOVE CEILING FINAL	1	1	0	06JUN12	06JUN12	26JUN12	26JUN12	14
1BTN2380	HARD CEILING COVER UP	1	1	0	16APR12	16APR12	01MAY12	01MAY12	11
1BTN2410	ELECTRICAL TRIM	1	1	0	12JUN12	12JUN12	02JUL12	02JUL12	14
1BTN2420	PLUMBING TRIM	1	1	0	12JUN12	12JUN12	28JUN12	28JUN12	12
1BTN2430	FINAL MECHANICAL	1	1	0	13JUN12	13JUN12	09JUL12	09JUL12	17
1BTN2440	FINAL ELECTRICAL	1	1	0	13JUN12	13JUN12	03JUL12	03JUL12	14
1BTN2450	FINAL PLUMBING	1	1	0	13JUN12	13JUN12	29JUN12	29JUN12	12
1BTN2460	FINAL FIRE ALARM	1	1	0	14JUN12	14JUN12	09JUL12	09JUL12	16
1BTN2470	FINAL SECURITY	1	1	0	14JUN12	14JUN12	13JUL12	13JUL12	20
1BTN2480	LIFE SAFETY WATER FOR FFE	1	1	0	18JUN12	18JUN12	11JUL12	11JUL12	16
1BTN2500	SIGNAGE	1	1	0	07JUN12	07JUN12	03JUL12	03JUL12	18
1BTN2510	LIGHTNING PROTECTION	1	1	0	01JUN12	01JUN12	28JUN12	28JUN12	19
REQUIRED DOCUMENTS									
1BRD2000	BUILDING FINAL W / ATTACHED	3	3	0	28JUN12	02JUL12	17JUL12	19JUL12	12
1BRD2010	FIRE SPRINKLER FINAL NFPA 13	1	1	0	29MAY12	29MAY12	21JUN12	21JUN12	17
1BRD2020	FIRE ALARM NFPA 72 FORM	1	1	0	15JUN12	15JUN12	16JUL12	16JUL12	20
1BRD2030	PLUMBING BACT TEST @ SAMPLE	10	10	0	14JUN12	27JUN12	02JUL12	16JUL12	12
1BRD2040	MECHANICAL T&B	5	5	0	14JUN12	20JUN12	10JUL12	16JUL12	17
1BRD2050	ELECTRICAL FINAL	1	1	0	14JUN12	14JUN12	05JUL12	05JUL12	14
1BRD2060	SECURITY SYSTEM FINAL SONITROL	1	1	0	19JUN12	19JUN12	16JUL12	16JUL12	18
1BRD2070	COMMUNICATION SYSTEM FINAL	3	3	0	14JUN12	18JUN12	05JUL12	09JUL12	14
1BRD2080	KITCHEN HOOD SUPPRESSION	2	2	0	14JUN12	15JUN12	13JUL12	16JUL12	20
1BRD2100	LIGHTNING PROTECTION UL	10	10	0	04JUN12	15JUN12	29JUN12	13JUL12	19
1BRD2110	ROOFING FINAL	1	1	0	24MAY12	24MAY12	20JUN12	20JUN12	18
1BRD2120	SITE UG WATER PAPERS FLUSH	1	1	0	16MAR12	16MAR12	28MAR12	28MAR12	8
1BRD2130	ENERGY MANAGEMENT	1	1	0	26JUN12	26JUN12	16JUL12	16JUL12	13
1BRD2140	FIRE ALARM MONITORING	1	1	0	19JUN12	19JUN12	16JUL12	16JUL12	18
COMPLETION & PUNCH									
1BPL2000	DOSTER PRE PUNCH LIST	5	5	0	13JUN12	19JUN12	05JUL12	11JUL12	15

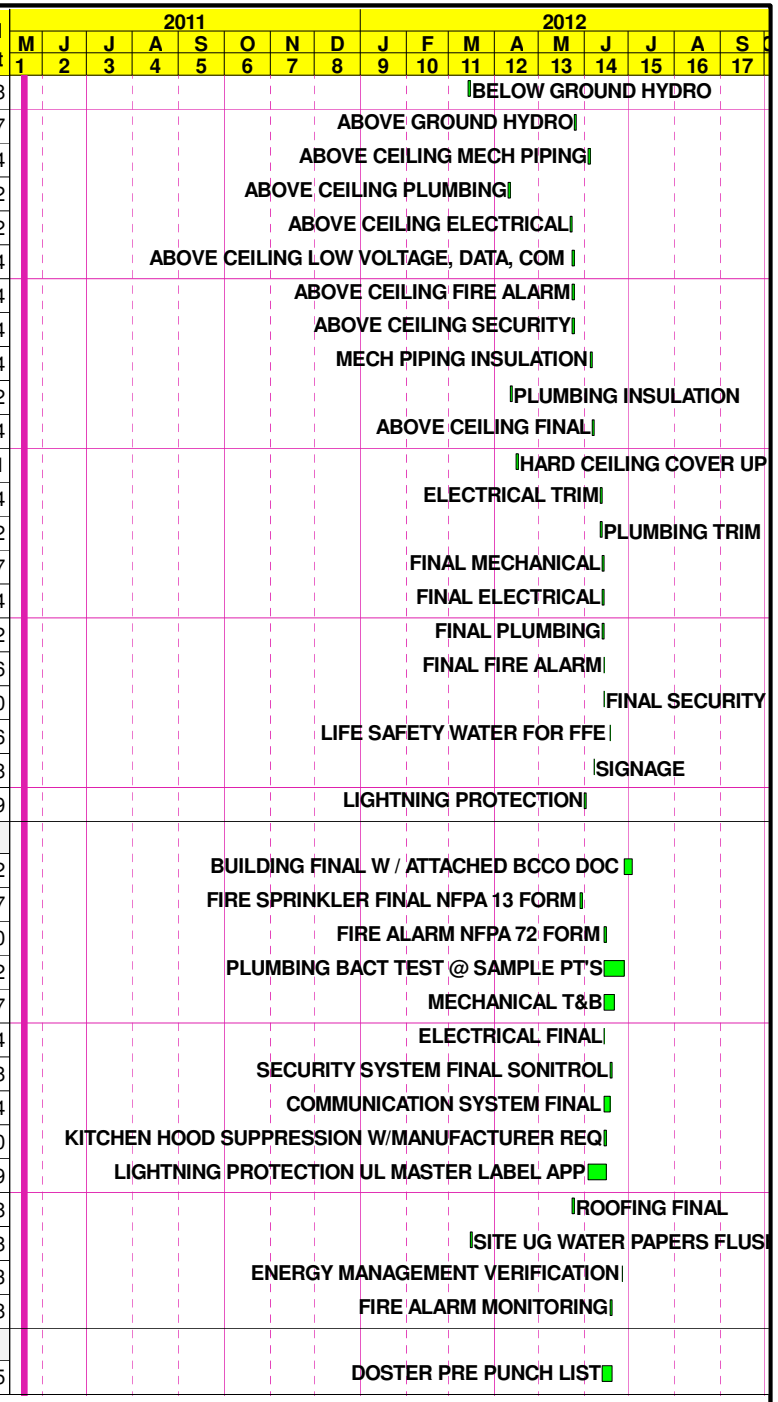

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0 Sheet 44 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
1BPL2010	COMPLETE DOSTER PRE PUNCH	10	10	0	20JUN12	03JUL12	12JUL12	25JUL12	15
1BPL2020	COMPLETE OCPS QAQC LIST	5	5	0	05JUL12	11JUL12	26JUL12	01AUG12	15
1BPL2030	OWNER ARCHITECT GENERATE	3	3	0	13JUL12	17JUL12	03AUG12	07AUG12	15
1BPL2040	RECEIVE OWNER FINAL PUNCH LIST	1	1	0	18JUL12	18JUL12	08AUG12	08AUG12	15
1BPL2050	COMPLETE OWNER ARCHITECT	15	15	0	19JUL12	08AUG12	09AUG12	29AUG12	15
BLDG 2 NEW ADDITION									
MILESTONES									
2BMS2000	BUILDING SLAB IN PLACE	0	0	0		23NOV11		23NOV11	0
2BMS2010	SHELL / DRYING	0	0	0		04APR12		12APR12	6
2BMS2020	ENERGIZE	0	0	0		14JUN12		14JUN12	0
2BMS2030	CONDITIONED AIR	1	1	0	15JUN12	15JUN12	15JUN12	15JUN12	0
2BMS2040	FFE	1	1	0	11JUL12	11JUL12	23JUL12	23JUL12	8
2BMS2050	SUBSTANTIAL COMPLETE	1	1	0	03AUG12	03AUG12	03AUG12	03AUG12	0
2BMS2060	SUB COMPLETION LIST COMPLETE	1	1	0	03AUG12	03AUG12	03AUG12	03AUG12	0
2BMS2070	OWNER ARCHITECT PUNCH	1	1	0	30AUG12	30AUG12	30AUG12	30AUG12	0
UNDERGROUND									
2BUG2020	DEEP FOUNDATION SLEEVES	1	1	0	10OCT11	10OCT11	10OCT11	10OCT11	0
2BUG2030	UG CHILLED WATER	2	2	0	11OCT11	12OCT11	14OCT11	17OCT11	3
2BUG2040	UG PLUMBING	5	5	0	11OCT11	17OCT11	11OCT11	17OCT11	0
2BUG2050	UG PRIMARIES ELECTRICAL	2	2	0	18OCT11	19OCT11	18OCT11	19OCT11	0
2BUG2060	UG SECONDARY'S ELECTRICAL	5	5	0	20OCT11	26OCT11	20OCT11	26OCT11	0
2BUG2070	UG FIRE PRITECTION	1	1	0	11OCT11	11OCT11	27OCT11	27OCT11	12
2BUG2080	UG LIGHTNING PROTECTION	1	1	0	27OCT11	27OCT11	27OCT11	27OCT11	0
2BUG2090	BACK FILL COMPACT	3	3	0	31OCT11	02NOV11	31OCT11	02NOV11	0
STRUCTURE									
2BST1000	FORM PANELS CAST BEDS EAST	1	1	0	07NOV11	07NOV11	18NOV11	18NOV11	9
2BST1010	FORM PANELS CAST BED WEST	1	1	0	07NOV11	07NOV11	18NOV11	18NOV11	9
2BST1020	REINFORCING STEEL & EMBEDS	1	1	0	08NOV11	08NOV11	21NOV11	21NOV11	9
2BST1030	CAST PANELS ON BEDS	3	3	0	09NOV11	11NOV11	22NOV11	28NOV11	9
2BST1040	PANEL CURE	7	7	0	14NOV11	22NOV11	02DEC11	12DEC11	12
2BST2000	LAY OUT BUILDING CORNERS	1	1	0	16SEP11	16SEP11	16SEP11	16SEP11	0
2BST2005	EXCAVATE COLUMN FOOTINGS	4	4	0	19SEP11	22SEP11	19SEP11	22SEP11	0
2BST2015	REINFORCING STEEL / BOLTS	4	4	0	23SEP11	28SEP11	23SEP11	28SEP11	0
2BST2025	PLACE COLUMN FOOTINGS	3	3	0	30SEP11	04OCT11	30SEP11	04OCT11	0
2BST2030	EXCAVATE FOUNDATIONS	3	3	0	05OCT11	07OCT11	05OCT11	07OCT11	0
2BST2040	INSTALL REINFORCING STEEL	1	1	0	11OCT11	11OCT11	26OCT11	26OCT11	11
2BST2050	PLACE FOUNDATION	1	1	0	13OCT11	13OCT11	28OCT11	28OCT11	11
2BST2060	FORM SLAB EDGES	5	5	0	03NOV11	09NOV11	03NOV11	09NOV11	0
2BST2070	FINE GRADE	3	3	0	10NOV11	14NOV11	10NOV11	14NOV11	0

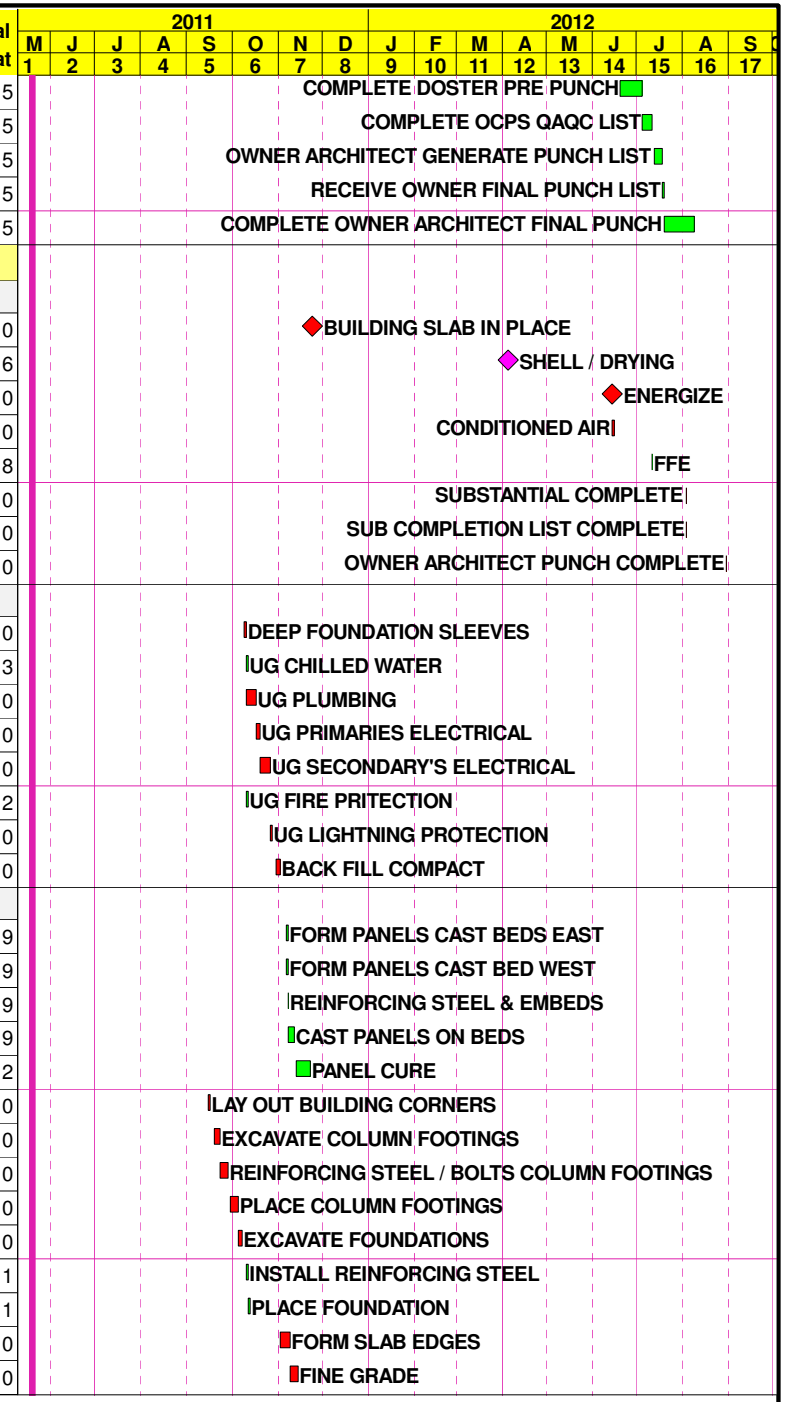

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
2BST2080	PEST CONTROL SPRAY	1	1	0	15NOV11	15NOV11	15NOV11	15NOV11	0
2BST2090	INSTALL VAPOR BARRIER,	2	2	0	17NOV11	18NOV11	17NOV11	18NOV11	0
2BST2100	PLACE SOG	2	2	0	22NOV11	23NOV11	22NOV11	23NOV11	0
2BST2110	FORM TILT WALL PANELS	5	5	0	28NOV11	02DEC11	28NOV11	02DEC11	0
2BST2120	REINFORCING STEEL & EMBEDS	5	5	0	05DEC11	09DEC11	05DEC11	09DEC11	0
2BST2130	CAST PANELS	4	4	0	13DEC11	16DEC11	13DEC11	16DEC11	0
2BST2140	PANEL CURE	7	7	0	19DEC11	28DEC11	19DEC11	28DEC11	0
2BST2150	ERECT PANELS	8	8	0	29DEC11	10JAN12	29DEC11	10JAN12	0
2BST2160	COLUMNS, BEAMS, JOISTS &	12	12	0	11JAN12	26JAN12	11JAN12	26JAN12	0
2BST2170	DECKING INTERMEDIATE SLAB	3	3	0	30JAN12	01FEB12	30JAN12	01FEB12	0
2BST2180	MEP HANGERS AND SLEEVES INT.	7	7	0	03FEB12	13FEB12	03FEB12	13FEB12	0
2BST2190	REINFORCING STEEL	3	3	0	14FEB12	16FEB12	14FEB12	16FEB12	0
2BST2200	PLACE INTERMEDIATE SLAB	2	2	0	20FEB12	21FEB12	20FEB12	21FEB12	0
2BST2210	FRAME ALL LARGE ROOF OPENINGS	5	5	0	22FEB12	28FEB12	22FEB12	28FEB12	0
2BST2220	DECK ROOF	3	3	0	29FEB12	02MAR12	29FEB12	02MAR12	0
2BST2230	FRP STAIRS AND RAMPS	10	10	0	22FEB12	06MAR12	29FEB12	13MAR12	5
ROOF									
2BRF2000	INSTALL ROOF DRAINS AND MEP	3	3	0	06MAR12	08MAR12	20MAR12	22MAR12	10
2BRF2010	INSTALL ROOF TOP CURBS	2	2	0	09MAR12	12MAR12	23MAR12	26MAR12	10
2BRF2020	INSTALL FINISH ROOF SYSTEM TILE	15	15	0	13MAR12	02APR12	27MAR12	16APR12	10
2BRF2030	INSTALL LIGHTNING PROTECTION	3	3	0	03APR12	05APR12	17APR12	19APR12	10
2BRF3000	INSTALL TAPER INSULATION	3	3	0	06MAR12	08MAR12	14MAR12	16MAR12	6
2BRF3010	INSTALL LIGHT WEIGHT CONCRETE	2	2	0	09MAR12	12MAR12	19MAR12	20MAR12	6
2BRF3020	INSTALL ROOFING MATERIALS	15	15	0	14MAR12	03APR12	22MAR12	11APR12	6
2BRF3030	INSTALL PARAPET CAPS	3	3	0	05APR12	09APR12	01MAY12	03MAY12	18
2BRF3040	INSTALL MEP EQUIPMENT	3	3	0	10APR12	12APR12	04MAY12	08MAY12	18
2BRF3050	INSTALL LIGHTNING PROTECTION	3	3	0	10APR12	12APR12	04MAY12	08MAY12	18
INTERIOR 1ST FLOOR									
2BFF2000	1ST LIFT MASONRY	3	3	0	22FEB12	24FEB12	09MAR12	13MAR12	12
2BFF2010	2ND LIFT MASONRY	3	3	0	13MAR12	15MAR12	23MAR12	27MAR12	8
2BFF2020	LINTEL / BEAM	2	2	0	19MAR12	20MAR12	29MAR12	30MAR12	8
2BFF2030	FRAME WALLS	10	10	0	22FEB12	06MAR12	02MAR12	15MAR12	7
2BFF2040	TOP OUT FIRE SMOKE WALLS	3	3	0	07MAR12	09MAR12	16MAR12	20MAR12	7
2BFF2050	1 SIDE MECH AND ELE ROOMS	1	1	0	12MAR12	12MAR12	26MAR12	26MAR12	10
2BFF2060	IN WALL MECHANICAL	15	15	0	07MAR12	27MAR12	19MAR12	06APR12	8
2BFF2070	IN WALL ELECTRICAL	15	15	0	07MAR12	27MAR12	19MAR12	06APR12	8
2BFF2080	IN WALL LOW VOLTAGE, DATA, COM	15	15	0	07FEB12	27FEB12	24FEB12	15MAR12	13
2BFF2090	IN WALL FIRE ALARM	15	15	0	07MAR12	27MAR12	19MAR12	06APR12	8
2BFF2100	IN WALL SECURITY	15	15	0	07MAR12	27MAR12	19MAR12	06APR12	8

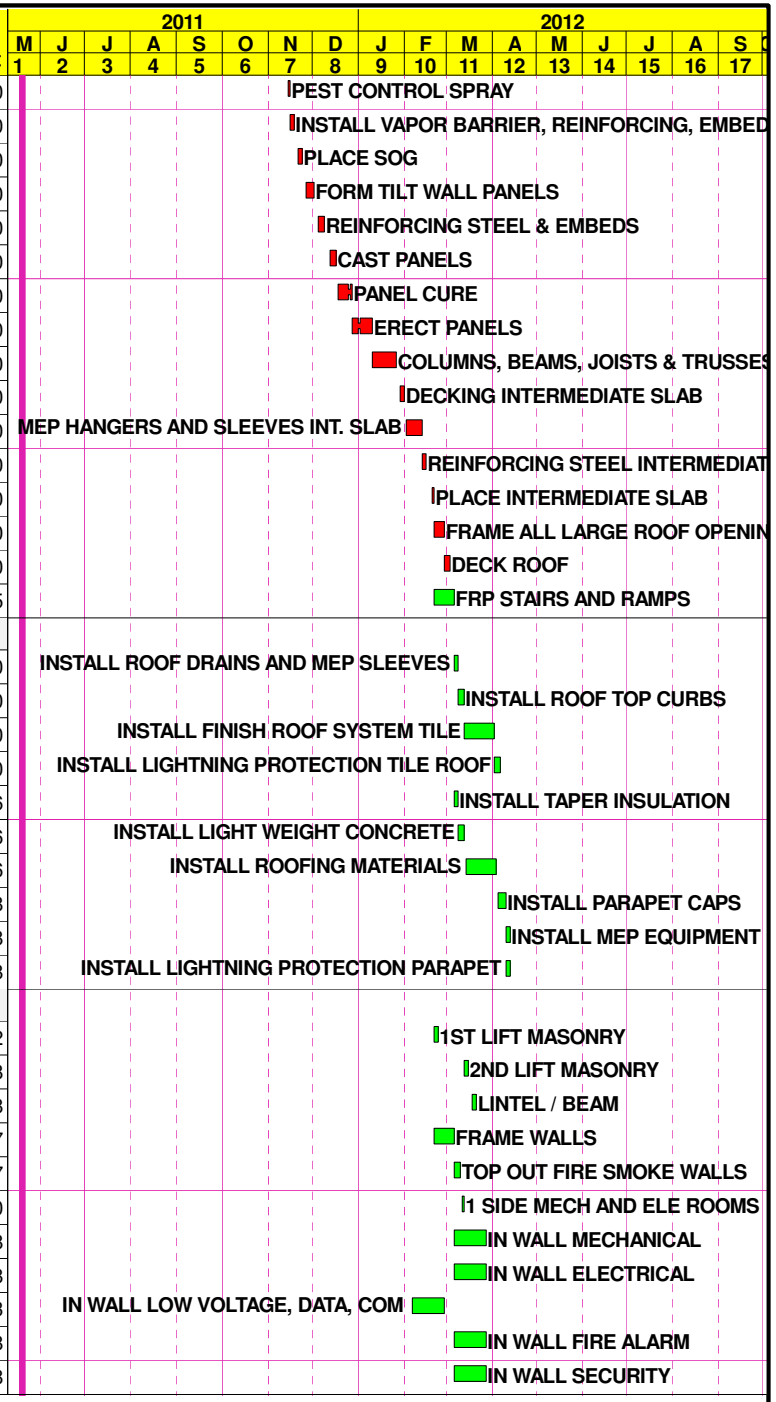

Start Date 20MAY11
Finish Date 30AUG12
Data Date 20MAY11
Run Date 12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0 Sheet 46 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
2BFF2110	IN WALL PLUMBING	15	15	0	07MAR12	27MAR12	19MAR12	06APR12	8
2BFF2120	ROUGH DUCT	15	15	0	12MAR12	30MAR12	21MAR12	10APR12	7
2BFF2125	DUCT INSULATION	10	10	0	06APR12	19APR12	17APR12	30APR12	7
2BFF2130	ROUGH RAIN LEADERS	5	5	0	12MAR12	16MAR12	22MAR12	28MAR12	8
2BFF2140	ABOVE CEILING SANITARY	5	5	0	12MAR12	16MAR12	22MAR12	28MAR12	8
2BFF2150	ABOVE CEILING FIRE PROTECTION	5	5	0	19MAR12	23MAR12	29MAR12	04APR12	8
2BFF2160	ABOVE CEILING MECHANICAL	15	15	0	26MAR12	13APR12	09APR12	27APR12	10
2BFF2170	ABOVE CEILING PLUMBING	15	15	0	26MAR12	13APR12	09APR12	27APR12	10
2BFF2180	ABOVE CEILING ELECTRICAL	15	15	0	19MAR12	06APR12	29MAR12	18APR12	8
2BFF2190	ABOVE CEILING LOW VOLTAGE,	15	15	0	26MAR12	13APR12	09APR12	27APR12	10
2BFF2200	ABOVE CEILING FIRE ALARM	15	15	0	26MAR12	13APR12	09APR12	27APR12	10
2BFF2210	ABOVE CEILING SECURITY	15	15	0	26MAR12	13APR12	09APR12	27APR12	10
2BFF2215	MEP HOUSE KEEPING PADS	2	2	0	13MAR12	14MAR12	05APR12	06APR12	17
2BFF2220	SET MECH EQ	2	2	0	15MAR12	16MAR12	09APR12	10APR12	17
2BFF2230	TIE IN MECHANICAL	3	3	0	02APR12	04APR12	11APR12	13APR12	7
2BFF2240	SET PANELS ELE ROOM	2	2	0	13MAR12	14MAR12	27MAR12	28MAR12	10
2BFF2245	SET MDP AND STEP TRANS	1	1	0	07FEB12	07FEB12	24FEB12	24FEB12	13
2BFF2270	INSULATE WALLS	2	2	0	30MAR12	02APR12	11APR12	12APR12	8
2BFF2280	INSTALL DRYWALL	5	5	0	03APR12	09APR12	13APR12	19APR12	8
2BFF2290	FINISH DRYWALL	10	10	0	13APR12	26APR12	25APR12	08MAY12	8
2BFF2300	INSTALL HARD CEILINGS	2	2	0	11APR12	12APR12	23APR12	24APR12	8
2BFF2330	POINT UP MASONRY	3	3	0	22MAR12	26MAR12	03APR12	05APR12	8
2BFF2340	PRIME PAINT	5	5	0	27APR12	03MAY12	09MAY12	15MAY12	8
2BFF2350	INSTALL CERAMIC TILE	10	10	0	04MAY12	17MAY12	16MAY12	30MAY12	8
2BFF2360	PAINT 1ST PASS COLOR	5	5	0	04MAY12	10MAY12	16MAY12	22MAY12	8
2BFF2370	BUMP OUT / TOUCH UP DRYWALL	2	2	0	11MAY12	14MAY12	29MAY12	30MAY12	11
2BFF2380	INSTALL MILL WORK	10	10	0	18JUN12	29JUN12	18JUN12	29JUN12	0
2BFF2390	INSTALL CEILING GRID	5	5	0	11MAY12	17MAY12	23MAY12	30MAY12	8
2BFF2410	MECHANICAL IN GRID	10	10	0	18MAY12	01JUN12	12JUN12	25JUN12	16
2BFF2420	ELECTRICAL IN GRID	10	10	0	18MAY12	01JUN12	31MAY12	13JUN12	8
2BFF2430	LOW VOLTAGE, DATA, COM IN GRID	10	10	0	18MAY12	01JUN12	13JUN12	26JUN12	17
2BFF2440	FIRE ALARM IN GRID	10	10	0	18MAY12	01JUN12	14JUN12	27JUN12	18
2BFF2450	SECURITY IN GRID	10	10	0	18MAY12	01JUN12	15JUN12	28JUN12	19
2BFF2460	FIRE PROTECTION IN GRID	5	5	0	18MAY12	24MAY12	05JUN12	11JUN12	11
2BFF2465	INSTALL CEILING TILE	2	2	0	18JUN12	19JUN12	11JUL12	12JUL12	16
2BFF2470	FINAL PAINT	5	5	0	25JUN12	29JUN12	25JUN12	29JUN12	0
2BFF2480	INSTALL DIVISION 10 EQ	5	5	0	02JUL12	09JUL12	13JUL12	19JUL12	8
2BFF2500	INSTALL DOORS AND HARDWARE	5	5	0	02JUL12	09JUL12	13JUL12	19JUL12	8
2BFF2510	INSTALL COMPOSITE FLOORING	15	15	0	18JUN12	09JUL12	03JUL12	24JUL12	11

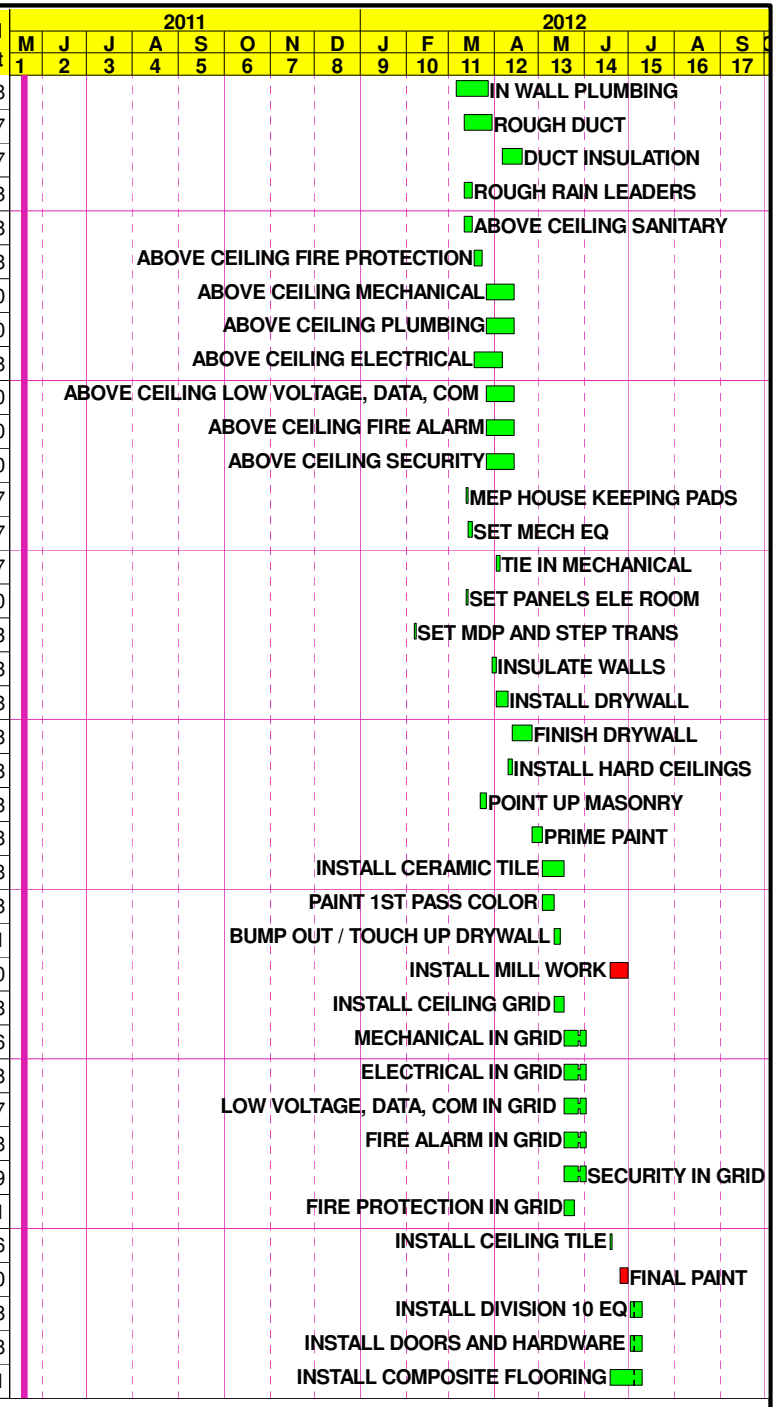

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
2BFF2520	INSTALL CARPET	5	5	0	02JUL12	09JUL12	13JUL12	19JUL12	8
2BFF2530	TRIM OUT MECHANICAL	5	5	0	02JUL12	09JUL12	02JUL12	09JUL12	0
2BFF2540	TRIM OUT ELECTRICAL	5	5	0	02JUL12	09JUL12	02JUL12	09JUL12	0
2BFF2550	TRIM OUT PLUMBING SET FIXTURES	10	10	0	02JUL12	16JUL12	02JUL12	16JUL12	0
2BFF2560	FINAL PAINT DOOR FRAMES	3	3	0	02JUL12	05JUL12	17JUL12	19JUL12	10
2BFF2570	INSTALL BASE	3	3	0	10JUL12	12JUL12	25JUL12	27JUL12	11
2BFF2580	INSTALL SIGNAGE	1	1	0	02JUL12	02JUL12	19JUL12	19JUL12	12
INTERIOR 2ND FLOOR									
2BSF2000	1ST LIFT MASONRY	3	3	0	07MAR12	09MAR12	14MAR12	16MAR12	5
2BSF2010	2ND LIFT MASONRY	3	3	0	13MAR12	15MAR12	23MAR12	27MAR12	8
2BSF2020	LINTEL / BEAM	2	2	0	19MAR12	20MAR12	29MAR12	30MAR12	8
2BSF2030	FRAME WALLS	10	10	0	05MAR12	16MAR12	05MAR12	16MAR12	0
2BSF2040	TOP OUT FIRE SMOKE WALLS	3	3	0	05MAR12	07MAR12	12MAR12	14MAR12	5
2BSF2050	1 SIDE MECH AND ELE ROOMS	1	1	0	07MAR12	07MAR12	14MAR12	14MAR12	5
2BSF2060	IN WALL MECHANICAL	15	15	0	19MAR12	06APR12	19MAR12	06APR12	0
2BSF2070	IN WALL ELECTRICAL	15	15	0	19MAR12	06APR12	19MAR12	06APR12	0
2BSF2080	IN WALL LOW VOLTAGE, DATA, COM	15	15	0	19MAR12	06APR12	19MAR12	06APR12	0
2BSF2090	IN WALL FIRE ALARM	15	15	0	19MAR12	06APR12	19MAR12	06APR12	0
2BSF2100	IN WALL SECURITY	15	15	0	19MAR12	06APR12	19MAR12	06APR12	0
2BSF2110	IN WALL PLUMBING	15	15	0	19MAR12	06APR12	19MAR12	06APR12	0
2BSF2120	ROUGH DUCT	15	15	0	08MAR12	28MAR12	22MAR12	11APR12	10
2BSF2125	MECHANICAL INSULATION	10	10	0	30MAR12	12APR12	13APR12	26APR12	10
2BSF2130	ROUGH RAIN LEADERS	5	5	0	08MAR12	14MAR12	20MAR12	26MAR12	8
2BSF2150	ABOVE CEILING FIRE PROTECTION	5	5	0	08MAR12	14MAR12	20MAR12	26MAR12	8
2BSF2160	ABOVE CEILING MECHANICAL	15	15	0	08MAR12	28MAR12	20MAR12	09APR12	8
2BSF2170	ABOVE CEILING PLUMBING	15	15	0	08MAR12	28MAR12	20MAR12	09APR12	8
2BSF2180	ABOVE CEILING ELECTRICAL	15	15	0	08MAR12	28MAR12	23MAR12	12APR12	11
2BSF2190	ABOVE CEILING LOW VOLTAGE,	15	15	0	08MAR12	28MAR12	23MAR12	12APR12	11
2BSF2200	ABOVE CEILING FIRE ALARM	15	15	0	08MAR12	28MAR12	23MAR12	12APR12	11
2BSF2210	ABOVE CEILING SECURITY	15	15	0	08MAR12	28MAR12	23MAR12	12APR12	11
2BSF2230	TIE IN MECHANICAL	3	3	0	29MAR12	02APR12	12APR12	16APR12	10
2BSF2240	SET PANELS ELE ROOM	2	2	0	08MAR12	09MAR12	15MAR12	16MAR12	5
2BSF2250	MEP HOUSE KEEPING PADS	3	3	0	08MAR12	12MAR12	23MAR12	27MAR12	11
2BSF2260	SET MEP EQ	2	2	0	13MAR12	14MAR12	28MAR12	29MAR12	11
2BSF2270	INSULATE WALLS	2	2	0	11APR12	12APR12	11APR12	12APR12	0
2BSF2280	INSTALL DRYWALL	5	5	0	13APR12	19APR12	13APR12	19APR12	0
2BSF2290	FINISH DRYWALL	10	10	0	20APR12	03MAY12	20APR12	03MAY12	0
2BSF2300	INSTALL HARD CEILINGS	2	2	0	20MAR12	21MAR12	30MAR12	02APR12	8
2BSF2310	FINISH HARD CEILINGS	3	3	0	04MAY12	08MAY12	04MAY12	08MAY12	0

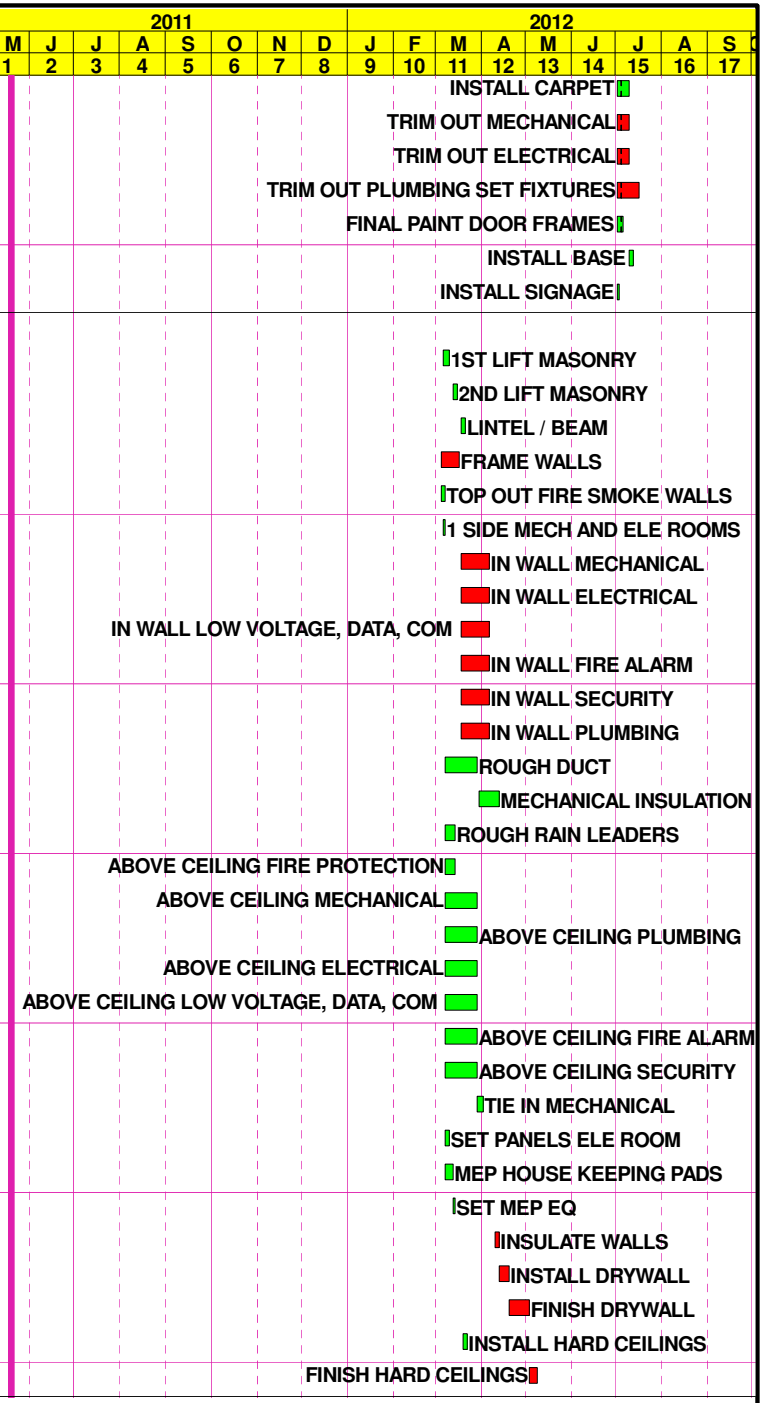

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
2BSF2330	POINT UP MASONRY	3	3	0	21MAR12	23MAR12	02APR12	04APR12	8
2BSF2340	PRIME PAINT	5	5	0	09MAY12	15MAY12	09MAY12	15MAY12	0
2BSF2350	INSTALL CERAMIC TILE	10	10	0	16MAY12	30MAY12	11JUN12	22JUN12	17
2BSF2360	PAINT 1ST PASS COLOR	5	5	0	16MAY12	22MAY12	16MAY12	22MAY12	0
2BSF2370	BUMP OUT / TOUCH UP DRYWALL	2	2	0	23MAY12	24MAY12	29MAY12	30MAY12	3
2BSF2380	INSTALL MILL WORK	10	10	0	23MAY12	06JUN12	18JUN12	29JUN12	17
2BSF2390	INSTALL CEILING GRID	5	5	0	23MAY12	30MAY12	23MAY12	30MAY12	0
2BSF2410	MECHANICAL IN GRID	10	10	0	31MAY12	13JUN12	27JUN12	11JUL12	19
2BSF2420	ELECTRICAL IN GRID	10	10	0	31MAY12	13JUN12	31MAY12	13JUN12	0
2BSF2430	LOW VOLTAGE, DATA, COM IN GRID	10	10	0	31MAY12	13JUN12	22JUN12	06JUL12	16
2BSF2440	FIRE ALARM IN GRID	10	10	0	31MAY12	13JUN12	22JUN12	06JUL12	16
2BSF2450	SECURITY IN GRID	10	10	0	31MAY12	13JUN12	22JUN12	06JUL12	16
2BSF2460	FIRE PROTECTION IN GRID	5	5	0	15JUN12	21JUN12	13JUL12	19JUL12	19
2BSF2465	INSTALL CEILING TILE	2	2	0	20JUN12	21JUN12	13JUL12	16JUL12	16
2BSF2470	FINAL PAINT	5	5	0	25MAY12	01JUN12	31MAY12	06JUN12	3
2BSF2480	INSTALL DIVISION 10 EQ	5	5	0	04JUN12	08JUN12	02JUL12	09JUL12	20
2BSF2500	INSTALL DOORS AND HARDWARE	5	5	0	18JUN12	22JUN12	16JUL12	20JUL12	19
2BSF2510	INSTALL COMPOSITE FLOORING	15	15	0	02JUL12	23JUL12	31JUL12	20AUG12	20
2BSF2520	INSTALL CARPET	5	5	0	24JUL12	30JUL12	21AUG12	27AUG12	20
2BSF2530	TRIM OUT MECHANICAL	5	5	0	04JUN12	08JUN12	02JUL12	09JUL12	20
2BSF2540	TRIM OUT ELECTRICAL	5	5	0	04JUN12	08JUN12	07JUN12	13JUN12	3
2BSF2550	TRIM OUT PLUMBING SET FIXTURES	10	10	0	12JUN12	25JUN12	02JUL12	16JUL12	14
2BSF2560	FINAL PAINT DOOR FRAMES	3	3	0	31JUL12	02AUG12	28AUG12	30AUG12	20
2BSF2570	INSTALL BASE	3	3	0	31JUL12	02AUG12	28AUG12	30AUG12	20
2BSF2580	INSTALL SIGNAGE	1	1	0	04JUN12	04JUN12	25JUN12	25JUN12	15
EXTERIOR									
2BEX2000	INSTALL WINDOWS & DOORS	5	5	0	04APR12	10APR12	20APR12	26APR12	12
2BEX2010	CAULK WINDOWS AND PANELS	3	3	0	12APR12	16APR12	30APR12	02MAY12	12
2BEX2020	TEX COAT	5	5	0	24APR12	30APR12	03MAY12	09MAY12	7
2BEX2030	MEP TRIM	5	5	0	01MAY12	07MAY12	10MAY12	16MAY12	7
2BEX2040	CANOPY A & B FOUNDATIONS	5	5	0	08MAY12	14MAY12	17MAY12	23MAY12	7
2BEX2050	ERECT CANOPIES A & B	5	5	0	21MAY12	25MAY12	01JUN12	07JUN12	8
2BEX2060	FRP SIDEWALKS CANOPY A & B	5	5	0	29MAY12	04JUN12	08JUN12	14JUN12	8
2BEX2070	INSTALL CANOPY G,H,J,&K	2	2	0	01MAY12	02MAY12	14MAY12	15MAY12	9
2BEX2080	INSTALL FOUNDATIONS CANOPY C	5	5	0	15MAY12	21MAY12	24MAY12	31MAY12	7
2BEX2090	ERECT CANOPY C	5	5	0	22MAY12	29MAY12	01JUN12	07JUN12	7
2BEX2100	FRP SIDEWALKS CANOPY C	5	5	0	30MAY12	05JUN12	08JUN12	14JUN12	7
2BEX2110	FRP BIKE RACK AND ART PATIO	5	5	0	01MAY12	07MAY12	25MAY12	01JUN12	18

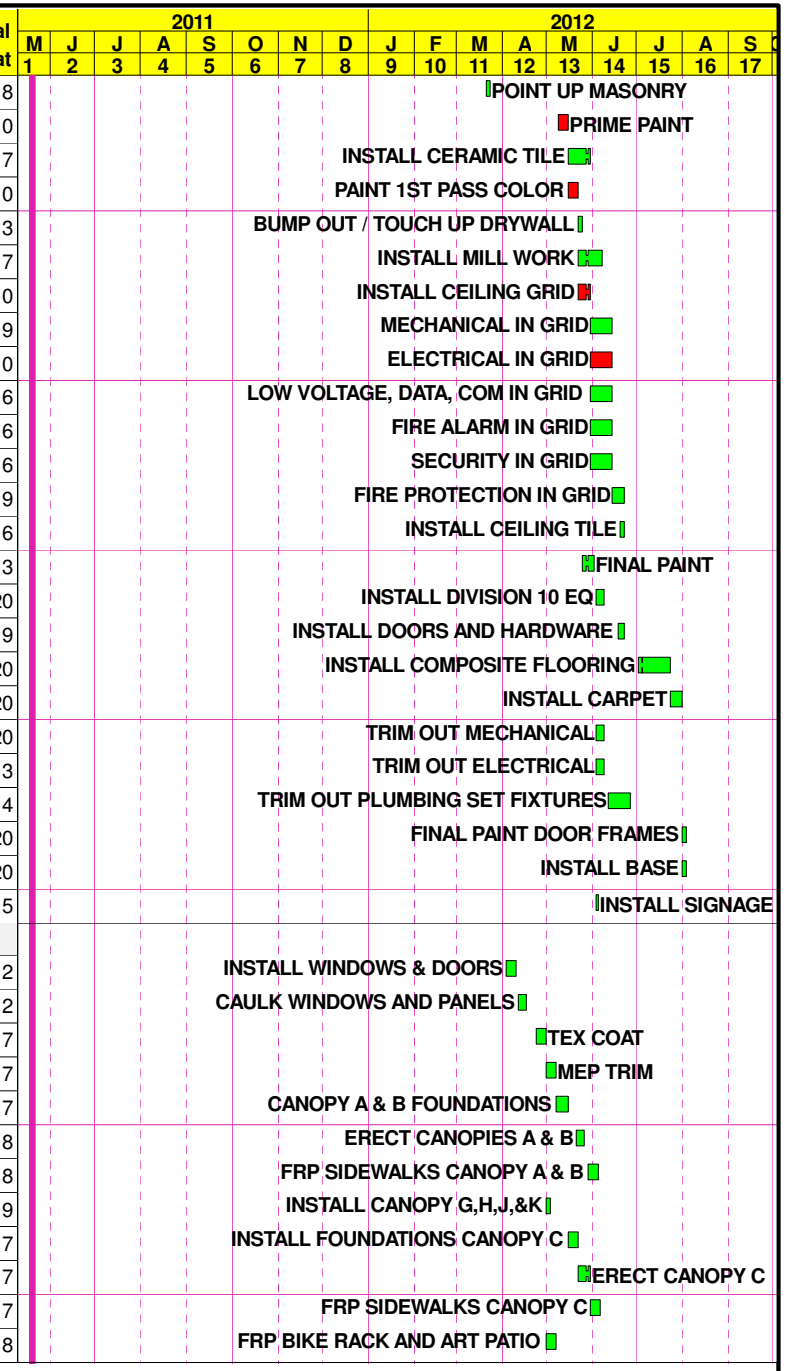

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
TESTING & INSPECTIONS									
2BTN2000	UG PLUMBING / STACK	1	1	0	18OCT11	18OCT11	28OCT11	28OCT11	8
2BTN2010	UG ELECTRICAL	1	1	0	27OCT11	27OCT11	28OCT11	28OCT11	1
2BTN2020	UG MECH PIPING	1	1	0	13OCT11	13OCT11	28OCT11	28OCT11	11
2BTN2030	UG FIRE PROTECTION RISER ASS.	1	1	0	12OCT11	12OCT11	28OCT11	28OCT11	12
2BTN2040	LIGHTNING PROTECTION BOND FTG	1	1	0	28OCT11	28OCT11	28OCT11	28OCT11	0
2BTN2050	COLUMN FOOTING / BOLT PROJ	1	1	0	29SEP11	29SEP11	29SEP11	29SEP11	0
2BTN2060	FOUNDATION	1	1	0	12OCT11	12OCT11	27OCT11	27OCT11	11
2BTN2080	PEST CONTROL	1	1	0	16NOV11	16NOV11	16NOV11	16NOV11	0
2BTN2090	VAPOR BARRIER / REINFORCING	1	1	0	21NOV11	21NOV11	21NOV11	21NOV11	0
2BTN2095	TILT WALL PANEL	1	1	0	12DEC11	12DEC11	12DEC11	12DEC11	0
2BTN2100	CMU LIFT 1	1	1	0	12MAR12	12MAR12	22MAR12	22MAR12	8
2BTN2110	CMU LIFT 2	1	1	0	16MAR12	16MAR12	28MAR12	28MAR12	8
2BTN2120	BEAM / LINTEL	1	1	0	21MAR12	21MAR12	02APR12	02APR12	8
2BTN2130	STEEL COLUMN, BEAM, JOIST	1	1	0	27JAN12	27JAN12	27JAN12	27JAN12	0
2BTN2140	DECKING INTERMEDIATE	1	1	0	02FEB12	02FEB12	02FEB12	02FEB12	0
2BTN2145	REINFORCING STEEL	1	1	0	17FEB12	17FEB12	17FEB12	17FEB12	0
2BTN2150	WELDING	1	1	0	05MAR12	05MAR12	13MAR12	13MAR12	6
2BTN2160	ROOF INSULATION	1	1	0	13MAR12	13MAR12	21MAR12	21MAR12	6
2BTN2170	ROOF MEMBRANE	1	1	0	04APR12	04APR12	12APR12	12APR12	6
2BTN2180	FINAL ROOF	1	1	0	13APR12	13APR12	09MAY12	09MAY12	18
2BTN2190	IN WALL MECHANICAL 1.0	1	1	0	28MAR12	28MAR12	09APR12	09APR12	8
2BTN2195	IN WALL MECHANICAL 2.0	1	1	0	09APR12	09APR12	09APR12	09APR12	0
2BTN2200	IN WALL ELECTRICAL 1.0	1	1	0	28MAR12	28MAR12	09APR12	09APR12	8
2BTN2205	IN WALL ELECTRICAL 2.0	1	1	0	09APR12	09APR12	09APR12	09APR12	0
2BTN2210	IN WALL LOW VOLTAGE, DATA, COM	1	1	0	28FEB12	28FEB12	16MAR12	16MAR12	13
2BTN2215	IN WALL LOW VOLTAGE, DATA, COM	1	1	0	09APR12	09APR12	09APR12	09APR12	0
2BTN2220	IN WALL FIRE ALARM 1.0	1	1	0	28MAR12	28MAR12	09APR12	09APR12	8
2BTN2225	IN WALL FIRE ALARM 2.0	1	1	0	09APR12	09APR12	09APR12	09APR12	0
2BTN2230	IN WALL SECURITY 1.0	1	1	0	28MAR12	28MAR12	09APR12	09APR12	8
2BTN2235	IN WALL SECURITY 2.0	1	1	0	09APR12	09APR12	09APR12	09APR12	0
2BTN2240	IN WALL PLUMBING 1.0	1	1	0	28MAR12	28MAR12	09APR12	09APR12	8
2BTN2245	IN WALL PLUMBING 2.0	1	1	0	09APR12	09APR12	09APR12	09APR12	0
2BTN2247	FRAMING 1.0	1	1	0	29MAR12	29MAR12	10APR12	10APR12	8
2BTN2249	FRAMING 2.0	1	1	0	10APR12	10APR12	10APR12	10APR12	0
2BTN2250	ROUGH DUCT 1.0	1	1	0	05APR12	05APR12	16APR12	16APR12	7
2BTN2255	ROUGH DUCT 2.0	1	1	0	29MAR12	29MAR12	12APR12	12APR12	10
2BTN2260	DUCT INSULATION 1.0	1	1	0	20APR12	20APR12	01MAY12	01MAY12	7
2BTN2265	DUCT INSULATION 2.0	1	1	0	13APR12	13APR12	10MAY12	10MAY12	19

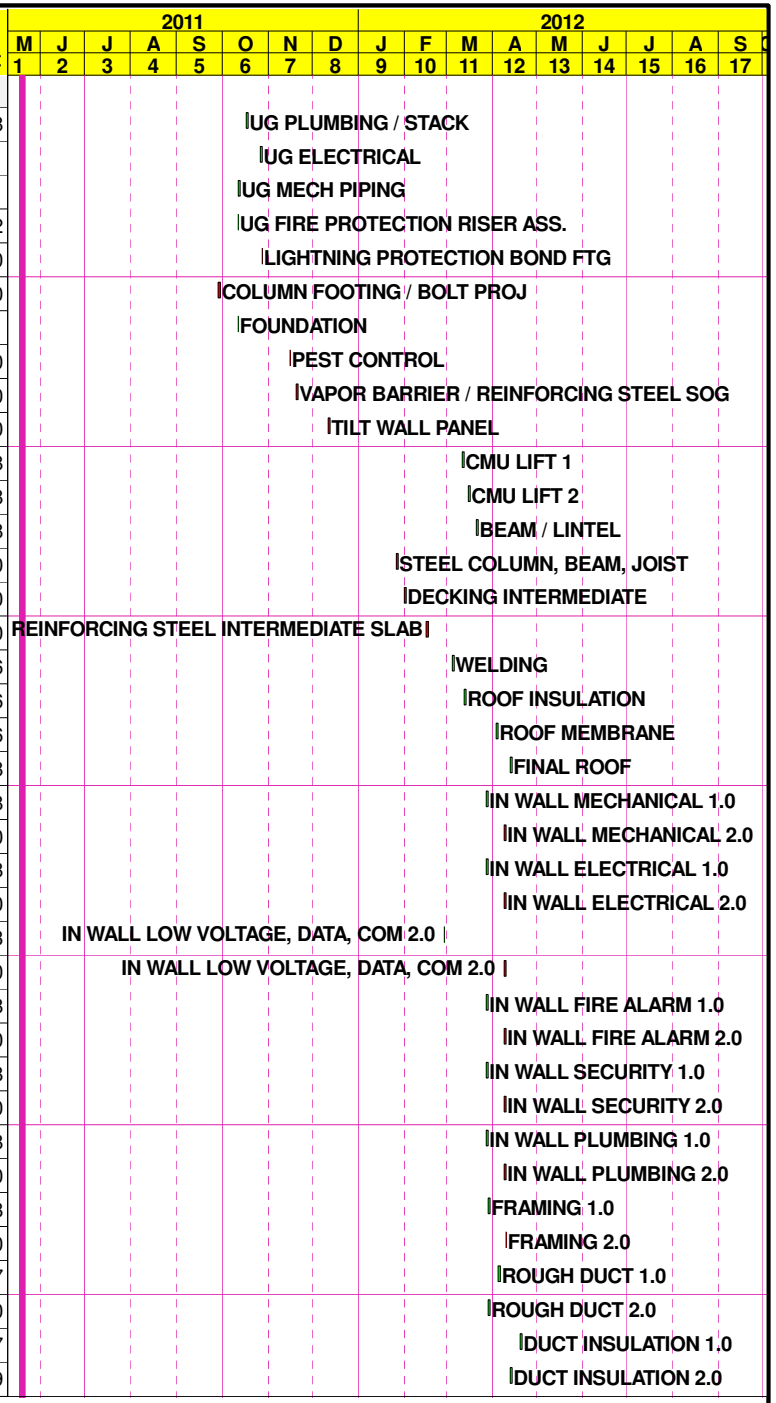

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

Sheet 50 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
2BTN2270	WINDOW SET 1.0	1	1	0	11APR12	11APR12	27APR12	27APR12	12
2BTN2275	WINDOW SET 2.0	1	1	0	11APR12	11APR12	02MAY12	02MAY12	15
2BTN2280	BELOW GROUND HYDRO	1	1	0	11APR12	11APR12	02MAY12	02MAY12	15
2BTN2290	ABOVE GROUND HYDRO	1	1	0	25MAY12	25MAY12	20JUN12	20JUN12	17
2BTN2300	ABOVE CEILING MECH PIPING 1.0	1	1	0	04JUN12	04JUN12	26JUN12	26JUN12	16
2BTN2305	ABOVE CEILING MECH PIPING 2.0	1	1	0	29MAR12	29MAR12	10APR12	10APR12	8
2BTN2310	ABOVE CEILING PLUMBING 1.0	1	1	0	16APR12	16APR12	10MAY12	10MAY12	18
2BTN2315	ABOVE CEILING PLUMBING 2.0	1	1	0	29MAR12	29MAR12	10APR12	10APR12	8
2BTN2320	ABOVE CEILING ELECTRICAL 1.0	1	1	0	04JUN12	04JUN12	14JUN12	14JUN12	8
2BTN2325	ABOVE CEILING ELECTRICAL 2.0	1	1	0	14JUN12	14JUN12	14JUN12	14JUN12	0
2BTN2330	ABOVE CEILING LOW VOLTAGE,	1	1	0	05JUN12	05JUN12	27JUN12	27JUN12	16
2BTN2335	ABOVE CEILING LOW VOLTAGE,	1	1	0	14JUN12	14JUN12	09JUL12	09JUL12	16
2BTN2340	ABOVE CEILING FIRE ALARM 1.0	1	1	0	08JUN12	08JUN12	28JUN12	28JUN12	14
2BTN2345	ABOVE CEILING FIRE ALARM 2.0	1	1	0	14JUN12	14JUN12	09JUL12	09JUL12	16
2BTN2350	ABOVE CEILING SECURITY 1.0	1	1	0	11JUN12	11JUN12	29JUN12	29JUN12	14
2BTN2355	ABOVE CEILING SECURITY 2.0	1	1	0	14JUN12	14JUN12	09JUL12	09JUL12	16
2BTN2360	MECH PIPING INSULATION 1.0	1	1	0	23APR12	23APR12	18MAY12	18MAY12	19
2BTN2365	MECH PIPING INSULATION 2.0	1	1	0	13APR12	13APR12	10MAY12	10MAY12	19
2BTN2366	ABOVE CEILING FINAL 1.0	1	1	0	15JUN12	15JUN12	10JUL12	10JUL12	16
2BTN2367	ABOVE CEILING FINAL2.0	1	1	0	14JUN12	14JUN12	12JUL12	12JUL12	19
2BTN2370	PLUMBING INSULATION 1.0	1	1	0	17APR12	17APR12	11MAY12	11MAY12	18
2BTN2375	PLUMBING INSULATION 2.0	1	1	0	16APR12	16APR12	14MAY12	14MAY12	20
2BTN2380	HARD CEILING COVER UP 1.O	1	1	0	10APR12	10APR12	20APR12	20APR12	8
2BTN2385	HARD CEILING COVER UP 2.0	1	1	0	19MAR12	19MAR12	29MAR12	29MAR12	8
2BTN2390	MECH EQ 1.0	1	1	0	05APR12	05APR12	17APR12	17APR12	8
2BTN2395	MECH EQ 2.0	1	1	0	03APR12	03APR12	17APR12	17APR12	10
2BTN2405	ELECTRICAL TRIM 1.0	1	1	0	10JUL12	10JUL12	30JUL12	30JUL12	14
2BTN2410	ELECTRICAL TRIM 2.0	1	1	0	11JUN12	11JUN12	14JUN12	14JUN12	3
2BTN2415	PLUMBING TRIM 1.0	1	1	0	17JUL12	17JUL12	17JUL12	17JUL12	0
2BTN2420	PLUMBING TRIM 2.0	1	1	0	26JUN12	26JUN12	17JUL12	17JUL12	14
2BTN2430	FINAL MECHANICAL	1	1	0	10JUL12	10JUL12	31JUL12	31JUL12	15
2BTN2440	FINAL ELECTRICAL	1	1	0	11JUL12	11JUL12	31JUL12	31JUL12	14
2BTN2450	FINAL PLUMBING	1	1	0	18JUL12	18JUL12	18JUL12	18JUL12	0
2BTN2460	FINAL FIRE ALARM	1	1	0	13JUL12	13JUL12	30JUL12	30JUL12	11
2BTN2470	FINAL SECURITY	1	1	0	10JUL12	10JUL12	31JUL12	31JUL12	15
2BTN2480	LIFE SAFETY WATER FOR FFE	1	1	0	10JUL12	10JUL12	20JUL12	20JUL12	8
2BTN2490	FIRE ALARM	1	1	0	10JUL12	10JUL12	31JUL12	31JUL12	15
2BTN2500	SIGNAGE	1	1	0	05JUN12	05JUN12	26JUN12	26JUN12	15
2BTN2510	LIGHTNING PROTECTION	1	1	0	13APR12	13APR12	10MAY12	10MAY12	19

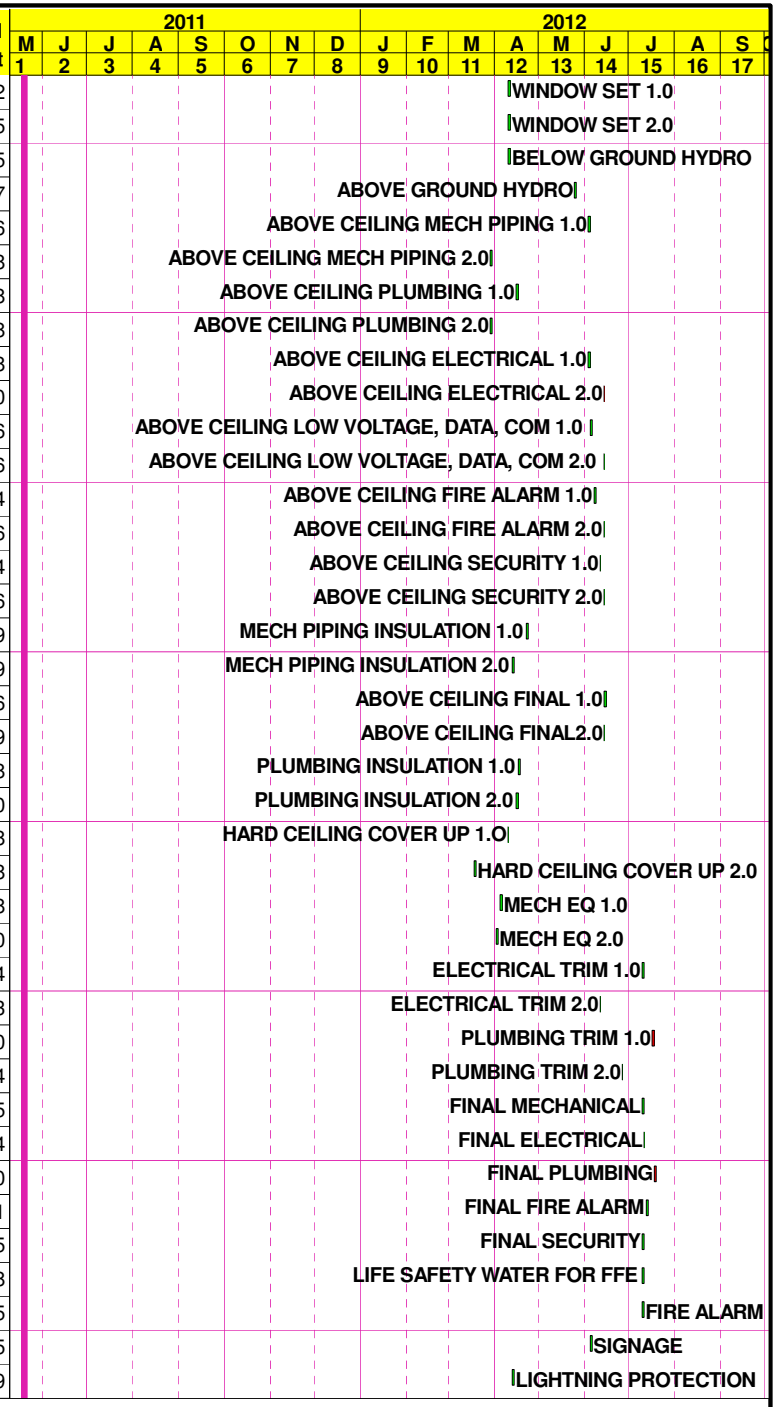

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
REQUIRED DOCUMENTS									
2BRD2000	BUILDING FINAL W / ATTACHED	1	1	0	02AUG12	02AUG12	02AUG12	02AUG12	0
2BRD2010	FIRE SPRINKLER FINAL NFPA 13	1	1	0	16JUL12	16JUL12	01AUG12	01AUG12	12
2BRD2020	FIRE ALARM NFPA 72 FORM	1	1	0	17JUL12	17JUL12	01AUG12	01AUG12	11
2BRD2030	PLUMBING BACT TEST @ SAMPLE	10	10	0	19JUL12	01AUG12	19JUL12	01AUG12	0
2BRD2040	MECHANICAL T&B	1	1	0	11JUL12	11JUL12	01AUG12	01AUG12	15
2BRD2050	ELECTRICAL FINAL	1	1	0	11JUL12	11JUL12	01AUG12	01AUG12	15
2BRD2060	SECURITY SYSTEM FINAL SONITROL	1	1	0	11JUL12	11JUL12	01AUG12	01AUG12	15
2BRD2070	COMMUNICATION SYSTEM FINAL	1	1	0	04JUN12	04JUN12	02JUL12	02JUL12	20
2BRD2100	LIGHTNING PROTECTION UL	10	10	0	16APR12	27APR12	11MAY12	24MAY12	19
2BRD2110	ROOFING FINAL	5	5	0	16APR12	20APR12	10MAY12	16MAY12	18
2BRD2120	SITE UG WATER PAPERS FLUSH	1	1	0	28NOV11	28NOV11	12DEC11	12DEC11	10
2BRD2130	ENERGY MANAGEMENT	1	1	0	12JUL12	12JUL12	01AUG12	01AUG12	14
2BRD2140	FIRE ALARM MONITORING	1	1	0	16JUL12	16JUL12	31JUL12	31JUL12	11
COMPLETION & PUNCH									
2BPL2000	DOSTER PRE PUNCH LIST	3	3	0	10JUL12	12JUL12	10JUL12	12JUL12	0
2BPL2010	COMPLETE DOSTER PRE PUNCH	10	10	0	13JUL12	26JUL12	13JUL12	26JUL12	0
2BPL2020	COMPLETE OCPS QAQC LIST	5	5	0	27JUL12	02AUG12	27JUL12	02AUG12	0
2BPL2030	OWNER ARCHITECT GENERATE	3	3	0	06AUG12	08AUG12	06AUG12	08AUG12	0
2BPL2040	RECEIVE OWNER FINAL PUNCH LIST	1	1	0	09AUG12	09AUG12	09AUG12	09AUG12	0
2BPL2050	COMPLETE OWNER ARCHITECT	14	14	0	10AUG12	29AUG12	10AUG12	29AUG12	0
BLDG 3 CHILLER, MEP, YARD									
MILESTONES									
3BMS2000	BUILDING SLAB IN PLACE	1	1	0	09FEB12	09FEB12	20FEB12	20FEB12	7
3BMS2010	SHELL / DRYING	1	1	0	13MAR12	13MAR12	23MAR12	23MAR12	8
3BMS2020	ENERGIZE	1	1	0	24APR12	24APR12	03MAY12	03MAY12	7
3BMS2030	CONDITIONED AIR	1	1	0	25APR12	25APR12	07MAY12	07MAY12	8
3BMS2040	FFE	1	1	0	19MAR12	19MAR12	29MAR12	29MAR12	8
3BMS2050	SUBSTANTIAL COMPLETE	1	1	0	04MAY12	04MAY12	16MAY12	16MAY12	8
3BMS2060	SUB COMPLETION LIST COMPLETE	1	1	0	22MAY12	22MAY12	07JUN12	07JUN12	11
3BMS2070	OWNER ARCHITECT PUNCH	1	1	0	15JUN12	15JUN12	12JUL12	12JUL12	18
UNDERGROUND									
3BUG2000	LAY OUT BUILDING CORNERS	1	1	0	10JAN12	10JAN12	24JAN12	24JAN12	10
3BUG2020	DEEP FOUNDATION SLEEVES	1	1	0	13JAN12	13JAN12	27JAN12	27JAN12	10
3BUG2030	UG CHILLED WATER	3	3	0	11JAN12	13JAN12	06FEB12	08FEB12	18
3BUG2040	UG PLUMBING	3	3	0	11JAN12	13JAN12	25JAN12	27JAN12	10
3BUG2050	UG PRIMARIES ELECTRICAL	3	3	0	24JAN12	26JAN12	02FEB12	06FEB12	7
3BUG2060	UG SECONDARY'S ELECTRICAL	2	2	0	27JAN12	30JAN12	07FEB12	08FEB12	7
3BUG2070	UG FIRE PROTECTION RISER ASS.	1	1	0	27JAN12	27JAN12	08FEB12	08FEB12	8

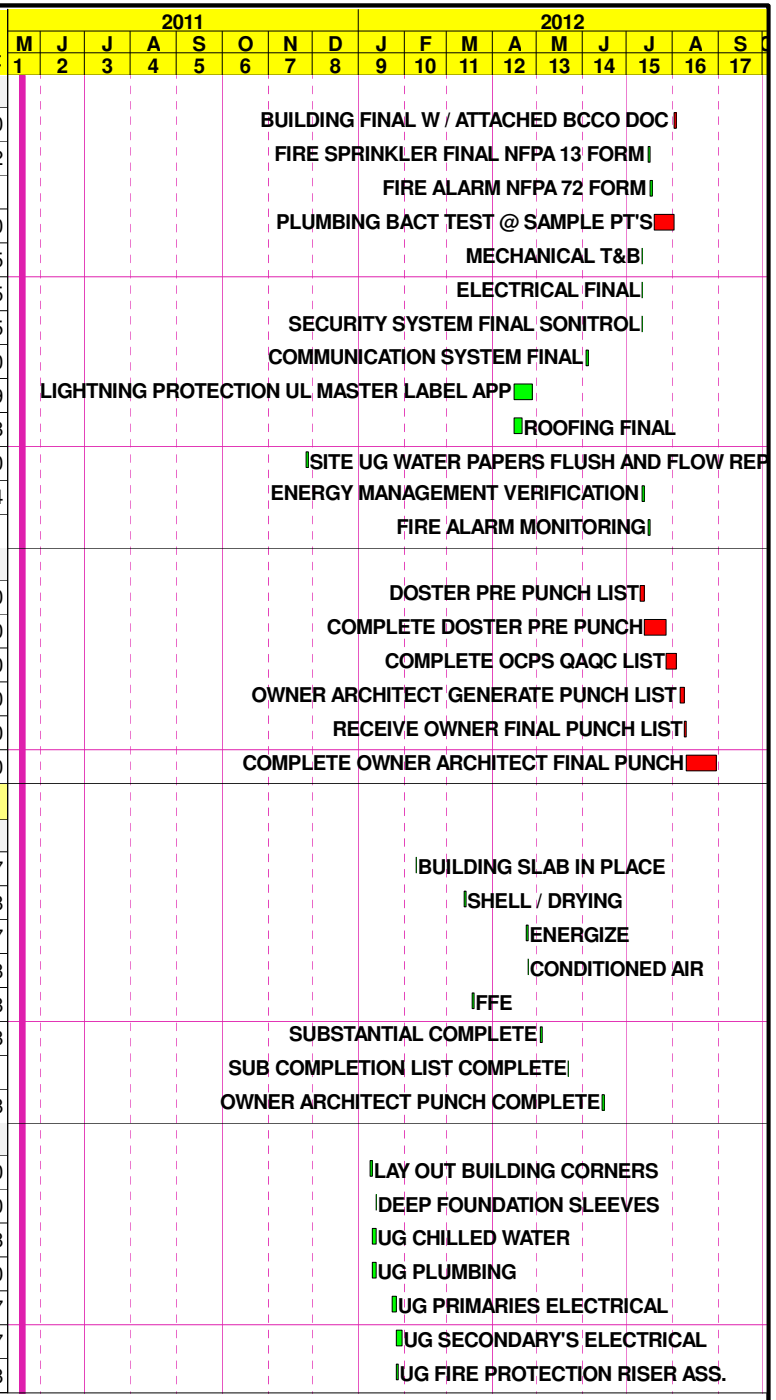

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
3BUG2080	UG LIGHTNING PROTECTION	1	1	0	27JAN12	27JAN12	08FEB12	08FEB12	8
3BUG2090	BACK FILL COMPACT	1	1	0	01FEB12	01FEB12	10FEB12	10FEB12	7
STRUCTURE									
3BST2000	EXCAVATE FOUNDATIONS	2	2	0	11JAN12	12JAN12	25JAN12	26JAN12	10
3BST2010	INSTALL REINFORCING STEEL	1	1	0	13JAN12	13JAN12	27JAN12	27JAN12	10
3BST2020	PLACE FOUNDATION	1	1	0	17JAN12	17JAN12	31JAN12	31JAN12	10
3BST2030	INSTALL STEM WALLS	2	2	0	18JAN12	19JAN12	01FEB12	02FEB12	10
3BST2032	FILL CELL STEM WALL	1	1	0	25JAN12	25JAN12	08FEB12	08FEB12	10
3BST2035	BACKFILL STEM WALLS	2	2	0	26JAN12	27JAN12	09FEB12	10FEB12	10
3BST2040	FINE GRADE	1	1	0	02FEB12	02FEB12	13FEB12	13FEB12	7
3BST2050	PEST CONTROL SPRAY	1	1	0	03FEB12	03FEB12	14FEB12	14FEB12	7
3BST2060	INSTALL VAPOR BARRIER &	1	1	0	06FEB12	06FEB12	15FEB12	15FEB12	7
3BST2070	PLACE SOG	1	1	0	08FEB12	08FEB12	17FEB12	17FEB12	7
3BST2080	1ST LIFT MASONRY WALLS	2	2	0	10FEB12	13FEB12	21FEB12	22FEB12	7
3BST2090	2ND LIFT MASONRY WALLS	2	2	0	15FEB12	16FEB12	24FEB12	27FEB12	7
3BST2100	BEAMS AND LINTELS	3	3	0	20FEB12	22FEB12	29FEB12	02MAR12	7
3BST2105	PLACE BEAM LINTEL FILL CELL	1	1	0	24FEB12	24FEB12	06MAR12	06MAR12	7
3BST2110	INSTALL ROOF FRAMING	2	2	0	27FEB12	28FEB12	08MAR12	09MAR12	8
3BST2120	INSTALL ROOF DECKING	2	2	0	01MAR12	02MAR12	13MAR12	14MAR12	8
ROOF									
3BRF2000	INSTALL TAPER INSULATION	1	1	0	06MAR12	06MAR12	16MAR12	16MAR12	8
3BRF2010	INSTALL LIGHT WEIGHT CONCRETE	1	1	0	07MAR12	07MAR12	19MAR12	19MAR12	8
3BRF2020	INSTALL ROOFING MATERIALS	2	2	0	09MAR12	12MAR12	21MAR12	22MAR12	8
3BRF2030	INSTALL PARAPET CAPS	2	2	0	14MAR12	15MAR12	26MAR12	27MAR12	8
3BRF2040	INSTALL MEP EQUIPMENT	1	1	0	16MAR12	16MAR12	28MAR12	28MAR12	8
3BRF2050	INSTALL LIGHTNING PROTECTION	1	1	0	16MAR12	16MAR12	28MAR12	28MAR12	8
INTERIOR 1ST FLOOR									
3BFF2000	IN WALL MECHANICAL	3	3	0	20JAN12	24JAN12	03FEB12	07FEB12	10
3BFF2010	IN WALL ELECTRICAL	3	3	0	20JAN12	24JAN12	03FEB12	07FEB12	10
3BFF2020	IN WALL PLUMBING	3	3	0	20JAN12	24JAN12	03FEB12	07FEB12	10
3BFF2030	IN WALL LOW VOLTAGE	3	3	0	20JAN12	24JAN12	03FEB12	07FEB12	10
3BFF2040	IN WALL FA	3	3	0	20JAN12	24JAN12	03FEB12	07FEB12	10
3BFF2050	POINT UP	2	2	0	27FEB12	28FEB12	07MAR12	08MAR12	7
3BFF2060	INSTALL DOORS & HWDR	1	1	0	29FEB12	29FEB12	09MAR12	09MAR12	7
3BFF2070	PRIME PAINT	1	1	0	01MAR12	01MAR12	12MAR12	12MAR12	7
3BFF2080	1ST PASS COLOR	1	1	0	02MAR12	02MAR12	13MAR12	13MAR12	7
3BFF2085	INSTALL DOORS AND HARDWARE	1	1	0	05MAR12	05MAR12	15MAR12	15MAR12	8
3BFF2090	MEP SURFACE MOUNT	3	3	0	05MAR12	07MAR12	14MAR12	16MAR12	7
3BFF2100	FINAL PASS COLOR	1	1	0	08MAR12	08MAR12	19MAR12	19MAR12	7

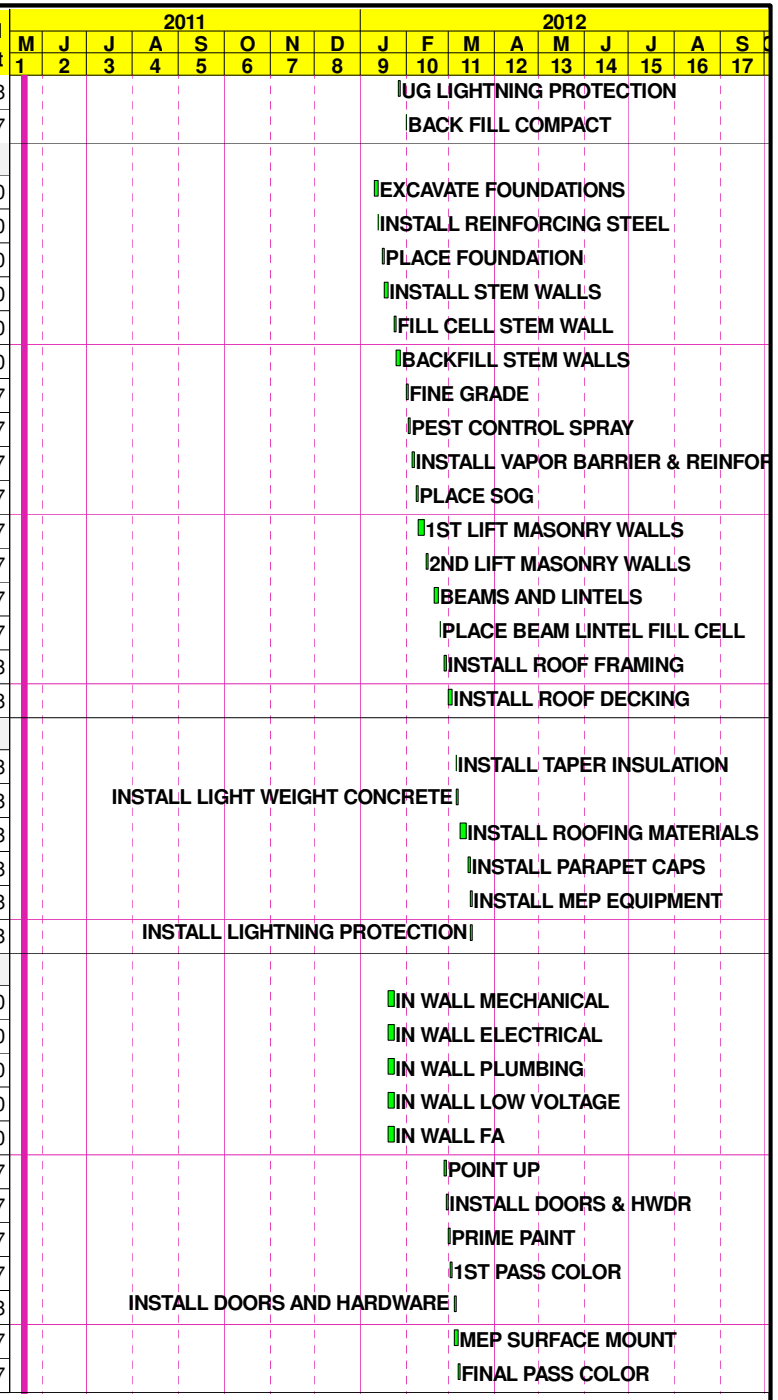

Start Date 20MAY11
Finish Date 30AUG12
Data Date 20MAY11
Run Date 12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

Sheet 53 of 61

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
3BFF2105	SET MDP AND STEP TRANS	3	3	0	07FEB12	09FEB12	24FEB12	28FEB12	13
3BFF2107	SET ELE PANELS	2	2	0	27FEB12	28FEB12	09MAR12	12MAR12	9
3BFF2110	SET MECH EQ	5	5	0	09MAR12	15MAR12	20MAR12	26MAR12	7
3BFF2120	PIPE MECHANICAL EQ	10	10	0	16MAR12	29MAR12	27MAR12	09APR12	7
3BFF2130	OVERHEAD PIPING MECHANICAL	5	5	0	30MAR12	05APR12	10APR12	16APR12	7
3BFF2140	OVERHEAD PIPING ELECTRICAL	5	5	0	06APR12	12APR12	17APR12	23APR12	7
3BFF2150	MEP TRIM	2	2	0	13APR12	16APR12	24APR12	25APR12	7
3BFF2155	EQ START UP	5	5	0	17APR12	23APR12	26APR12	02MAY12	7
3BFF2160	TOUCH UP PAINTING	1	1	0	17APR12	17APR12	01MAY12	01MAY12	10
3BFF2170	FINAL PAINT DOORS	1	1	0	18APR12	18APR12	02MAY12	02MAY12	10
EXTERIOR									
3BEX2010	PREP / LATH / BEAD	1	1	0	27FEB12	27FEB12	12MAR12	12MAR12	10
3BEX2020	SCRATCH COAT	1	1	0	28FEB12	28FEB12	13MAR12	13MAR12	10
3BEX2030	BROWN COAT	1	1	0	29FEB12	29FEB12	14MAR12	14MAR12	10
3BEX2040	FINISH COAT	1	1	0	01MAR12	01MAR12	15MAR12	15MAR12	10
3BEX2050	PLASTER CURE	15	15	0	02MAR12	22MAR12	16MAR12	05APR12	10
3BEX2060	PRIME PAINT	1	1	0	23MAR12	23MAR12	06APR12	06APR12	10
3BEX2070	1ST PASS COLOR	1	1	0	26MAR12	26MAR12	09APR12	09APR12	10
3BEX2080	FINISH PAINT	1	1	0	27MAR12	27MAR12	10APR12	10APR12	10
TESTING & INSPECTIONS									
3BTN2000	UG PLUMBING / STACK	1	1	0	16JAN12	16JAN12	09FEB12	09FEB12	18
3BTN2010	UG ELECTRICAL	1	1	0	31JAN12	31JAN12	09FEB12	09FEB12	7
3BTN2020	UG MECH PIPING	1	1	0	16JAN12	16JAN12	09FEB12	09FEB12	18
3BTN2030	UG FIRE PROTECTION RISER ASS.	1	1	0	30JAN12	30JAN12	09FEB12	09FEB12	8
3BTN2040	LIGHTNING PROTECTION BOND FTG	1	1	0	30JAN12	30JAN12	09FEB12	09FEB12	8
3BTN2060	FOUNDATION	1	1	0	16JAN12	16JAN12	30JAN12	30JAN12	10
3BTN2070	STEM WALL	1	1	0	24JAN12	24JAN12	07FEB12	07FEB12	10
3BTN2080	PEST CONTROL	1	1	0	06FEB12	06FEB12	16FEB12	16FEB12	8
3BTN2090	VAPOR BARRIER / REINFORCING	1	1	0	07FEB12	07FEB12	16FEB12	16FEB12	7
3BTN2110	CMU LIFT 1	1	1	0	14FEB12	14FEB12	23FEB12	23FEB12	7
3BTN2120	CMU LIFT 2	1	1	0	17FEB12	17FEB12	28FEB12	28FEB12	7
3BTN2130	BEAM / LINTEL	1	1	0	23FEB12	23FEB12	05MAR12	05MAR12	7
3BTN2140	STEEL COLUMN, BEAM, JOIST	1	1	0	29FEB12	29FEB12	12MAR12	12MAR12	8
3BTN2150	DECKING	1	1	0	05MAR12	05MAR12	15MAR12	15MAR12	8
3BTN2160	WELDING	1	1	0	05MAR12	05MAR12	15MAR12	15MAR12	8
3BTN2170	ROOF INSULATION	1	1	0	08MAR12	08MAR12	20MAR12	20MAR12	8
3BTN2180	ROOF MEMBRANE	1	1	0	13MAR12	13MAR12	28MAR12	28MAR12	11
3BTN2190	FINAL ROOF	1	1	0	19MAR12	19MAR12	29MAR12	29MAR12	8
3BTN2200	IN WALL MECHANICAL	1	1	0	25JAN12	25JAN12	13FEB12	13FEB12	13

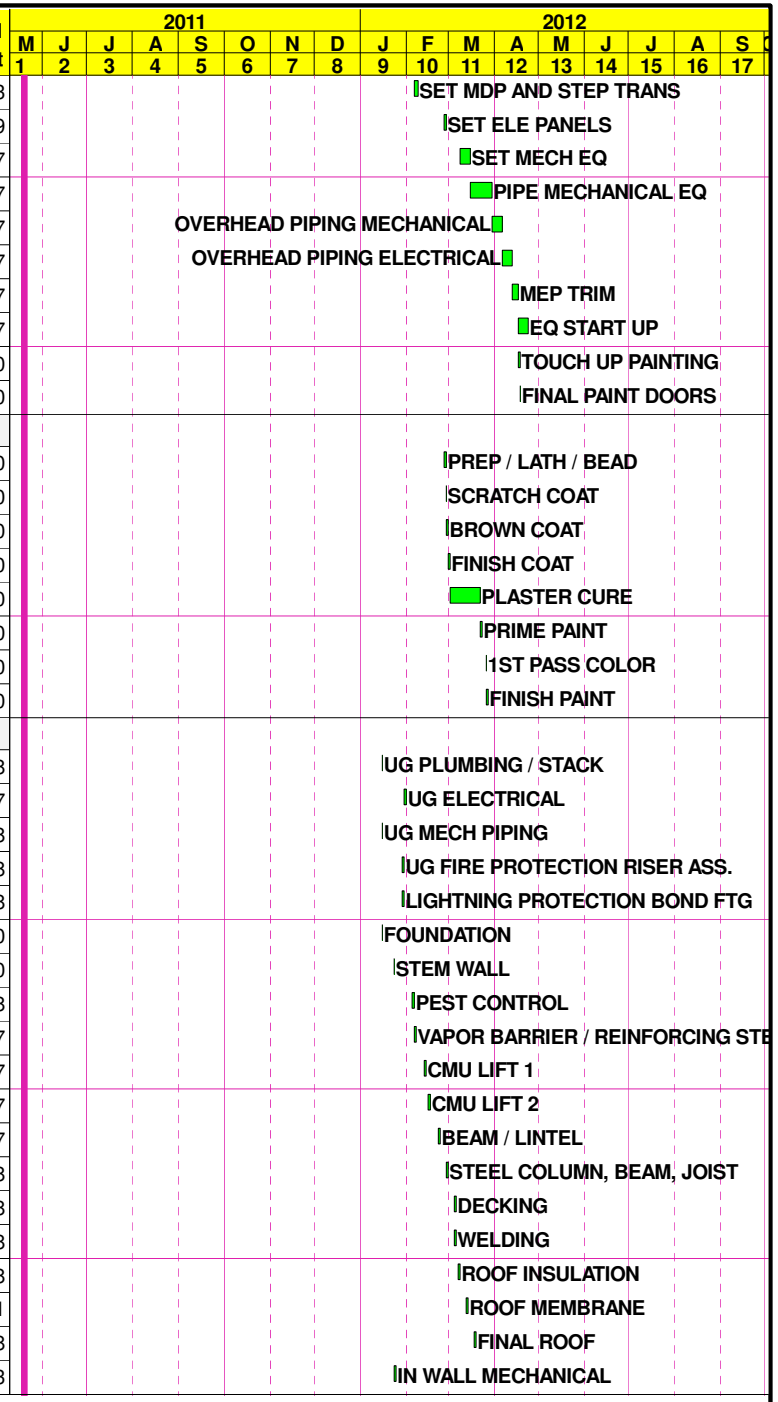

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
3BTN2210	IN WALL ELECTRICAL	1	1	0	25JAN12	25JAN12	13FEB12	13FEB12	13
3BTN2220	IN WALL LOW VOLTAGE, DATA, COM	1	1	0	25JAN12	25JAN12	13FEB12	13FEB12	13
3BTN2230	IN WALL FIRE ALARM	1	1	0	25JAN12	25JAN12	13FEB12	13FEB12	13
3BTN2240	IN WALL SECURITY	1	1	0	25JAN12	25JAN12	13FEB12	13FEB12	13
3BTN2250	IN WALL PLUMBING	1	1	0	25JAN12	25JAN12	13FEB12	13FEB12	13
3BTN2290	BELOW GROUND HYDRO	1	1	0	18JAN12	18JAN12	02FEB12	02FEB12	11
3BTN2300	ABOVE GROUND HYDRO	1	1	0	15MAR12	15MAR12	27MAR12	27MAR12	8
3BTN2310	ABOVE CEILING MECH PIPING	1	1	0	06APR12	06APR12	04MAY12	04MAY12	20
3BTN2320	ABOVE CEILING PLUMBING	1	1	0	06APR12	06APR12	04MAY12	04MAY12	20
3BTN2330	ABOVE CEILING ELECTRICAL	1	1	0	13APR12	13APR12	02MAY12	02MAY12	13
3BTN2340	ABOVE CEILING LOW VOLTAGE,	1	1	0	13APR12	13APR12	11MAY12	11MAY12	20
3BTN2350	ABOVE CEILING FIRE ALARM	1	1	0	13APR12	13APR12	11MAY12	11MAY12	20
3BTN2360	ABOVE CEILING SECURITY	1	1	0	13APR12	13APR12	11MAY12	11MAY12	20
3BTN2370	MECH PIPING INSULATION	1	1	0	06APR12	06APR12	04MAY12	04MAY12	20
3BTN2380	PLUMBING INSULATION	1	1	0	06APR12	06APR12	19APR12	19APR12	9
3BTN2390	HARD CEILING COVER UP	1	1	0	16APR12	16APR12	14MAY12	14MAY12	20
3BTN2410	ELECTRICAL TRIM	1	1	0	17APR12	17APR12	10MAY12	10MAY12	17
3BTN2420	PLUMBING TRIM	1	1	0	17APR12	17APR12	27APR12	27APR12	8
3BTN2430	FINAL MECHANICAL	1	1	0	17APR12	17APR12	07MAY12	07MAY12	14
3BTN2440	FINAL ELECTRICAL	1	1	0	18APR12	18APR12	11MAY12	11MAY12	17
3BTN2450	FINAL PLUMBING	1	1	0	18APR12	18APR12	30APR12	30APR12	8
3BTN2460	FINAL FIRE ALARM	1	1	0	19APR12	19APR12	03MAY12	03MAY12	10
3BTN2470	FINAL SECURITY	1	1	0	17APR12	17APR12	11MAY12	11MAY12	18
3BTN2480	LIFE SAFETY WATER	1	1	0	16MAR12	16MAR12	28MAR12	28MAR12	8
3BTN2490	FIRE ALARM	1	1	0	17APR12	17APR12	11MAY12	11MAY12	18
3BTN2500	SIGNAGE	1	1	0	18APR12	18APR12	14MAY12	14MAY12	18
3BTN2510	LIGHTNING PROTECTION	1	1	0	19MAR12	19MAR12	29MAR12	29MAR12	8
REQUIRED DOCUMENTS									
3BRD2000	BUILDING FINAL W / ATTACHED	1	1	0	03MAY12	03MAY12	15MAY12	15MAY12	8
3BRD2010	FIRE SPRINKLER FINAL NFPA 13	1	1	0	16MAR12	16MAR12	28MAR12	28MAR12	8
3BRD2020	FIRE ALARM NFPA 72 FORM	1	1	0	20APR12	20APR12	14MAY12	14MAY12	16
3BRD2030	PLUMBING BACT TEST @ SAMPLE	10	10	0	19APR12	02MAY12	01MAY12	14MAY12	8
3BRD2040	MECHANICAL T&B	5	5	0	26APR12	02MAY12	08MAY12	14MAY12	8
3BRD2050	ELECTRICAL FINAL	1	1	0	19APR12	19APR12	14MAY12	14MAY12	17
3BRD2060	SECURITY SYSTEM FINAL	1	1	0	18APR12	18APR12	14MAY12	14MAY12	18
3BRD2070	COMMUNICATION SYSTEM FINAL	1	1	0	19APR12	19APR12	14MAY12	14MAY12	17
3BRD2100	LIGHTNING PROTECTION UL	10	10	0	20MAR12	02APR12	30MAR12	12APR12	8
3BRD2110	ROOFING FINAL	1	1	0	20MAR12	20MAR12	30MAR12	30MAR12	8
3BRD2120	SITE UG WATER PAPERS FLUSH	1	1	0	19JAN12	19JAN12	03FEB12	03FEB12	11

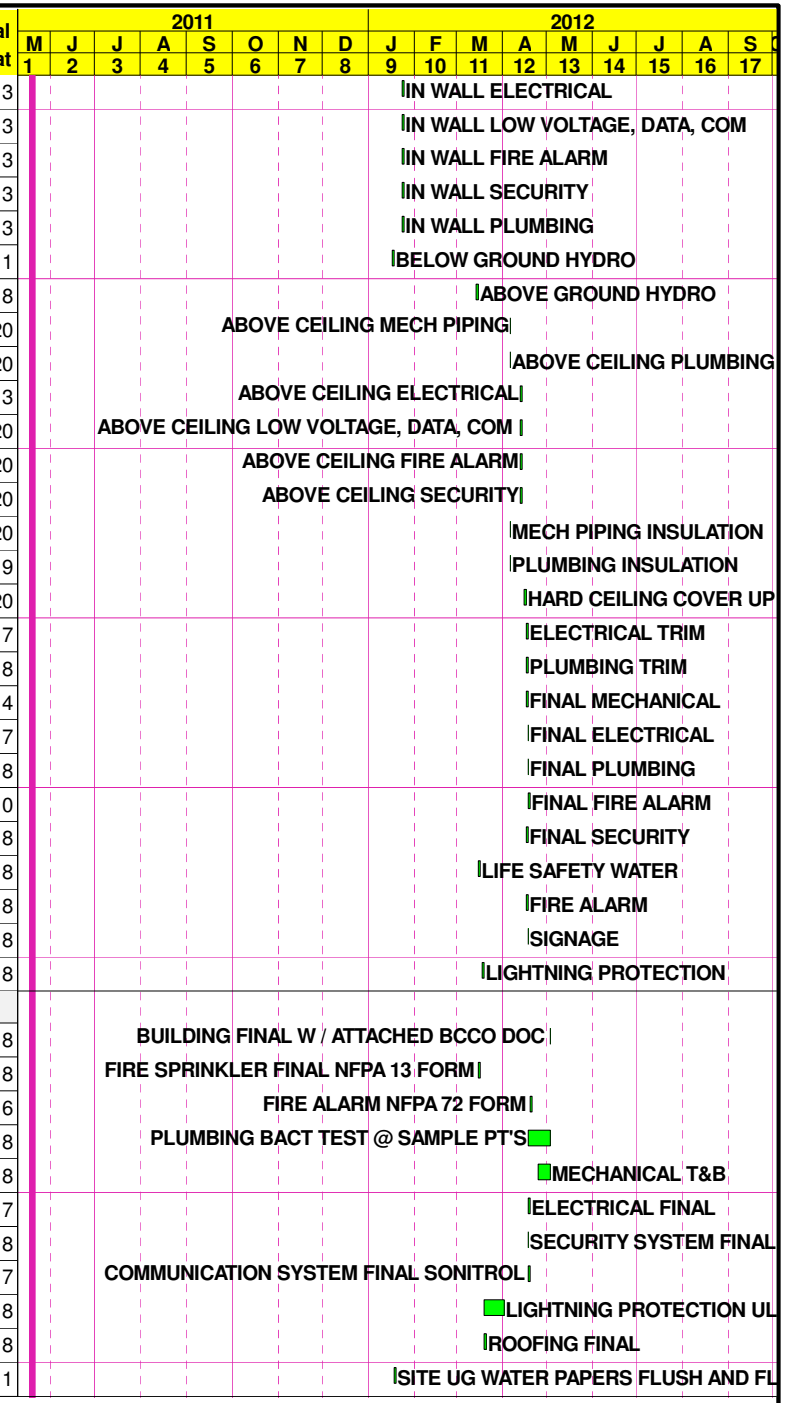

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
3BRD2130	ENERGY MANAGEMENT	1	1	0	19APR12	19APR12	14MAY12	14MAY12	17
3BRD2140	FIRE ALARM MONITORING	1	1	0	18APR12	18APR12	14MAY12	14MAY12	18
COMPLETION & PUNCH									
3BPL2000	DOSTER PRE PUNCH LIST	5	5	0	19APR12	25APR12	09MAY12	15MAY12	14
3BPL2010	COMPLETE DOSTER PRE PUNCH	10	10	0	26APR12	09MAY12	16MAY12	30MAY12	14
3BPL2020	COMPLETE OCPS QAQC LIST	5	5	0	10MAY12	16MAY12	31MAY12	06JUN12	14
3BPL2030	OWNER ARCHITECT GENERATE	3	3	0	25MAY12	30MAY12	12JUN12	14JUN12	11
3BPL2040	RECEIVE OWNER FINAL PUNCH LIST	1	1	0	31MAY12	31MAY12	26JUN12	26JUN12	18
3BPL2050	COMPLETE OWNER ARCHITECT	10	10	0	01JUN12	14JUN12	27JUN12	11JUL12	18
BLDG 4 COVERED PLAY AREA									
MILESTONES									
4BMS2000	BUILDING SLAB IN PLACE	1	1	0	02FEB12	02FEB12	15FEB12	15FEB12	9
4BMS2010	SHELL / DRYING	1	1	0	02MAR12	02MAR12	16MAR12	16MAR12	10
4BMS2020	ENERGIZE	1	1	0	14MAR12	14MAR12	28MAR12	28MAR12	10
4BMS2030	CONDITIONED AIR	1	1	0	25APR12	25APR12	04MAY12	04MAY12	7
4BMS2040	FFE	1	1	0	14MAR12	14MAR12	28MAR12	28MAR12	10
4BMS2050	SUBSTANTIAL COMPLETE	1	1	0	03MAY12	03MAY12	31MAY12	31MAY12	19
4BMS2060	SUB COMPLETION LIST COMPLETE	1	1	0	29MAY12	29MAY12	15JUN12	15JUN12	13
4BMS2070	OWNER ARCHITECT PUNCH	1	1	0	26JUN12	26JUN12	16JUL12	16JUL12	13
UNDERGROUND									
4BUG2000	LAY OUT BUILDING CORNERS	1	1	0	12JAN12	12JAN12	25JAN12	25JAN12	9
4BUG2020	DEEP FOUNDATIONS & SLEEVES	1	1	0	16JAN12	16JAN12	27JAN12	27JAN12	9
4BUG2040	UG PLUMBING	2	2	0	24JAN12	25JAN12	06FEB12	07FEB12	9
4BUG2060	UG ELECTRICAL	2	2	0	24JAN12	25JAN12	06FEB12	07FEB12	9
4BUG2080	UG LIGHTNING PROTECTION	1	1	0	24JAN12	24JAN12	07FEB12	07FEB12	10
4BUG2090	BACK FILL COMPACT	1	1	0	27JAN12	27JAN12	09FEB12	09FEB12	9
STRUCTURE									
4BST1000	EXCAVATE BUILDING FOUNDATION	1	1	0	13JAN12	13JAN12	26JAN12	26JAN12	9
4BST1010	REINFORCING STEEL BUILDING	1	1	0	16JAN12	16JAN12	27JAN12	27JAN12	9
4BST1020	PLACE FOUNDATION	1	1	0	18JAN12	18JAN12	31JAN12	31JAN12	9
4BST1030	STEM WALL FILL CELL	2	2	0	20JAN12	23JAN12	02FEB12	03FEB12	9
4BST1040	VAPOR BARRIER REINFORCING SOG	1	1	0	30JAN12	30JAN12	10FEB12	10FEB12	9
4BST1045	PLACE BUILDING SOG	1	1	0	01FEB12	01FEB12	14FEB12	14FEB12	9
4BST1050	1ST LIFT CMU	1	1	0	03FEB12	03FEB12	16FEB12	16FEB12	9
4BST1060	2ND LIFT CMU	1	1	0	07FEB12	07FEB12	21FEB12	21FEB12	10
4BST1070	LINTEL BEAM	2	2	0	10FEB12	13FEB12	23FEB12	24FEB12	9
4BST1080	EXCAVATE FOUNDATIONS CANOPY	1	1	0	13JAN12	13JAN12	30JAN12	30JAN12	11
4BST1090	INSTALL REINFORCING STEEL	1	1	0	16JAN12	16JAN12	31JAN12	31JAN12	11
4BST1100	PLACE FOUNDATION	1	1	0	18JAN12	18JAN12	02FEB12	02FEB12	11

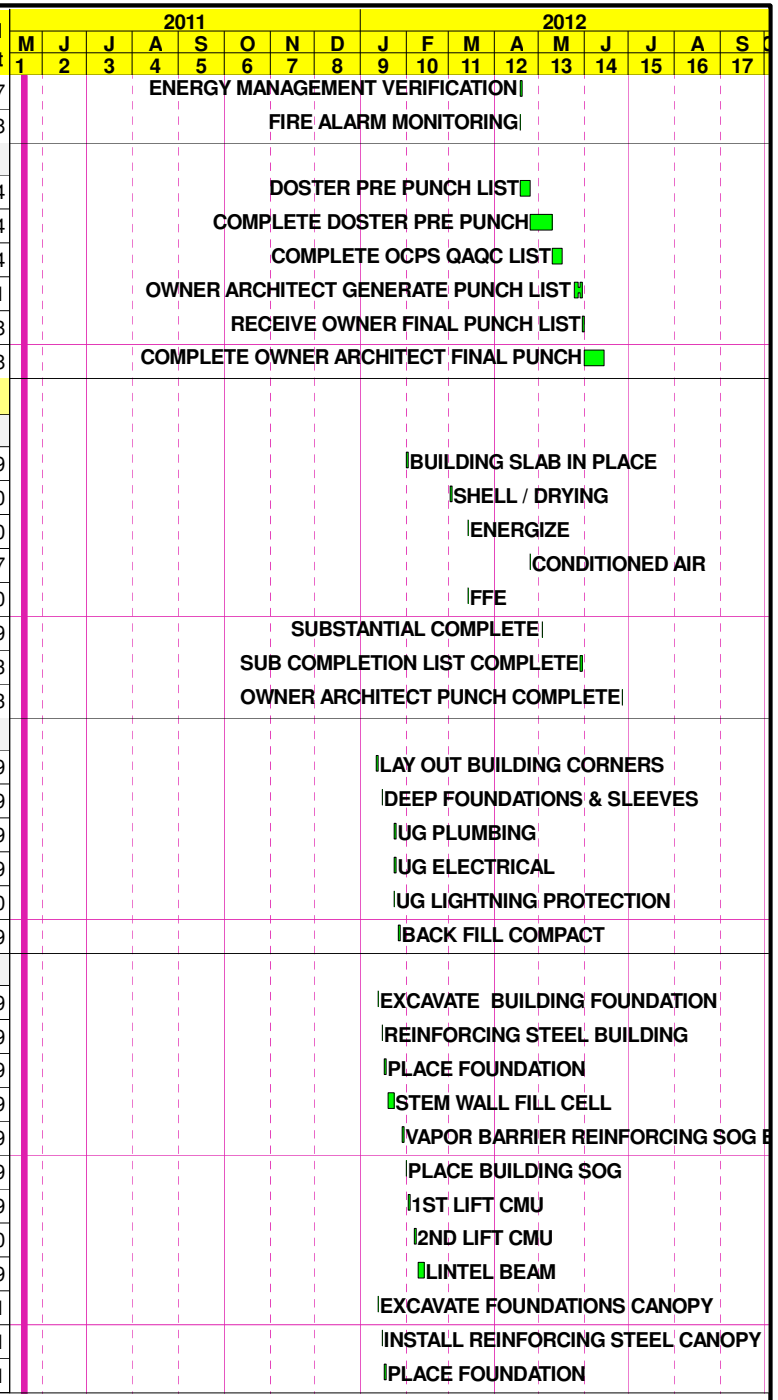

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
4BST1110	FORM SLAB EDGES	2	2	0	19JAN12	20JAN12	03FEB12	06FEB12	11
4BST1120	FINE GRADE	1	1	0	23JAN12	23JAN12	07FEB12	07FEB12	11
4BST1130	PEST CONTROL SPRAY	1	1	0	24JAN12	24JAN12	08FEB12	08FEB12	11
4BST1140	INSTALL VAPOR BARRIER,	1	1	0	26JAN12	26JAN12	10FEB12	10FEB12	11
4BST1150	PLACE SOG	1	1	0	01FEB12	01FEB12	22FEB12	22FEB12	15
4BST1160	COLUMNS BEAMS PLAY AREA	2	2	0	02FEB12	03FEB12	23FEB12	24FEB12	15
4BST1170	JOISTS BUILDING	1	1	0	15FEB12	15FEB12	28FEB12	28FEB12	9
4BST1180	DECKING	2	2	0	16FEB12	17FEB12	29FEB12	01MAR12	9
4BST1190	WELD	1	1	0	21FEB12	21FEB12	05MAR12	05MAR12	9
ROOF									
4RF2000	INSTALL TAPER INSULATION	2	2	0	23FEB12	24FEB12	07MAR12	08MAR12	9
4RF2010	INSTALL LIGHT WEIGHT CONCRETE	1	1	0	27FEB12	27FEB12	09MAR12	09MAR12	9
4RF2020	INSTALL ROOFING MATERIALS	2	2	0	29FEB12	01MAR12	13MAR12	14MAR12	9
4RF2030	INSTALL PARAPET CAPS	2	2	0	05MAR12	06MAR12	19MAR12	20MAR12	10
4RF2040	INSTALL MEP EQUIPMENT	1	1	0	07MAR12	07MAR12	21MAR12	21MAR12	10
4RF2050	INSTALL LIGHTNING PROTECTION	1	1	0	08MAR12	08MAR12	22MAR12	22MAR12	10
INTERIOR 1ST FLOOR									
4BFF2000	1ST LIFT CMU	1	1	0	02FEB12	02FEB12	16FEB12	16FEB12	10
4BFF2002	2ND LIFT CMU	1	1	0	08FEB12	08FEB12	21FEB12	21FEB12	9
4BFF2004	LINTEL BEAM	1	1	0	10FEB12	10FEB12	24FEB12	24FEB12	10
4BFF2010	IN WALL ELECTRICAL	3	3	0	03FEB12	07FEB12	17FEB12	21FEB12	10
4BFF2020	IN WALL PLUMBING	3	3	0	06FEB12	08FEB12	17FEB12	21FEB12	9
4BFF2030	IN WALL F/A	3	3	0	06FEB12	08FEB12	17FEB12	21FEB12	9
4BFF2040	IN WALL VOICE DATA	3	3	0	06FEB12	08FEB12	17FEB12	21FEB12	9
4BFF2080	ELECTRICAL ABOVE CEILING	2	2	0	02MAR12	05MAR12	22MAR12	23MAR12	14
4BFF2090	PLUMBING ABOVE CEILING	2	2	0	02MAR12	05MAR12	22MAR12	23MAR12	14
4BFF2110	PRIME PAINT	1	1	0	02MAR12	02MAR12	15MAR12	15MAR12	9
4BFF2120	POINT UP	1	1	0	05MAR12	05MAR12	16MAR12	16MAR12	9
4BFF2130	1ST PASS COLOR	1	1	0	06MAR12	06MAR12	19MAR12	19MAR12	9
4BFF2135	INSTALL DOORS AND HARDWARE	1	1	0	26APR12	26APR12	14MAY12	14MAY12	12
4BFF2140	FINAL PAINT	1	1	0	08MAR12	08MAR12	21MAR12	21MAR12	9
4BFF2150	INSTALL CEILING GRID	1	1	0	07MAR12	07MAR12	20MAR12	20MAR12	9
4BFF2160	MEP IN GRID	2	2	0	08MAR12	09MAR12	22MAR12	23MAR12	10
4BFF2170	INSTALL CEILING TILE	1	1	0	26APR12	26APR12	14MAY12	14MAY12	12
4BFF2180	INSTALL CERAMIC TILE	2	2	0	13FEB12	14FEB12	01MAR12	02MAR12	13
4BFF2190	MEP TRIM	2	2	0	09MAR12	12MAR12	23MAR12	26MAR12	10
4BFF2200	FINAL FLOORING & BASE	2	2	0	26APR12	27APR12	07MAY12	08MAY12	7
4BFF2210	SIGNAGE	1	1	0	09MAR12	09MAR12	22MAR12	22MAR12	9

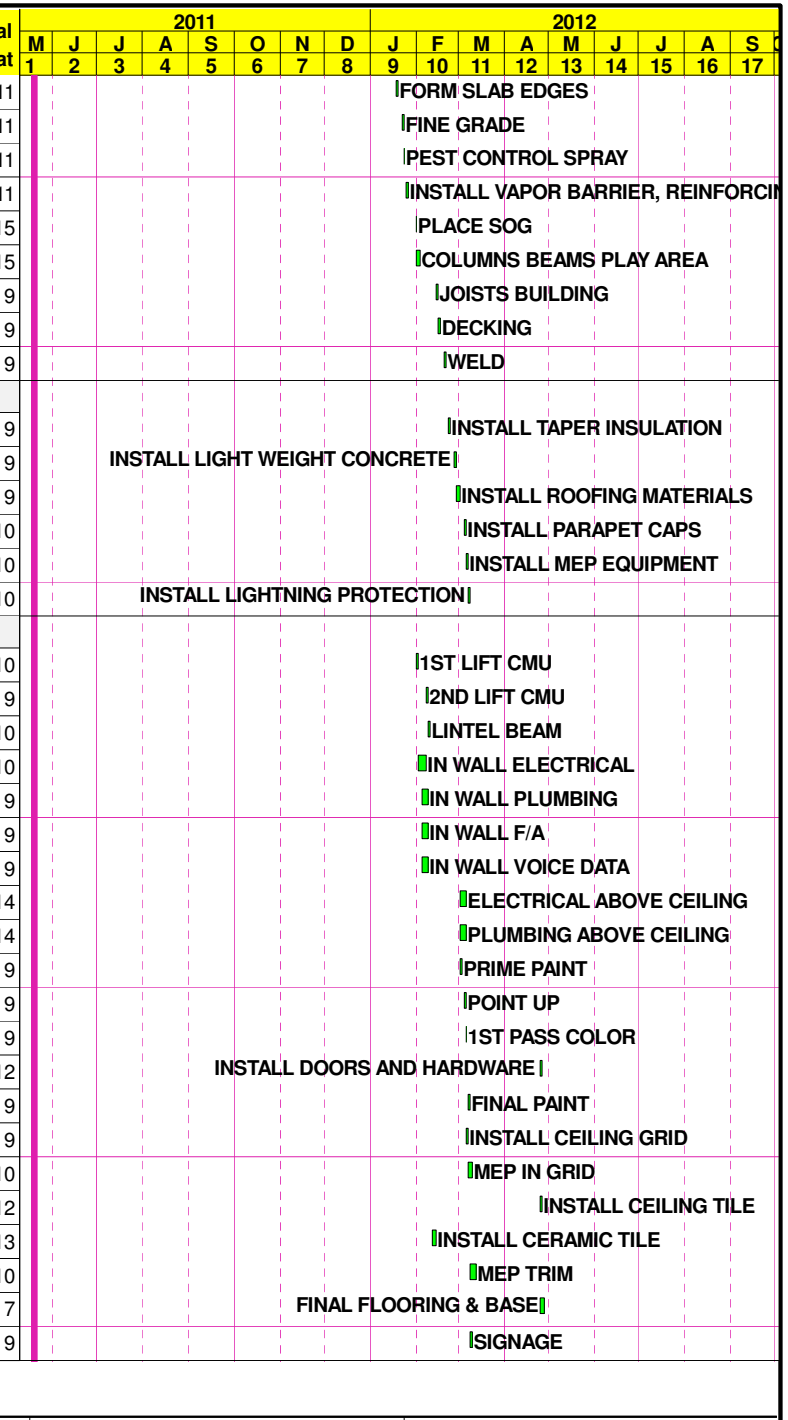

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
EXTERIOR									
4BEX2000	INSTALL WINDOWS	1	1	0	14FEB12	14FEB12	27FEB12	27FEB12	9
4BEX2010	PREP / LATH / BEAD	1	1	0	16FEB12	16FEB12	29FEB12	29FEB12	9
4BEX2020	SCRATCH COAT	1	1	0	17FEB12	17FEB12	01MAR12	01MAR12	9
4BEX2030	BROWN COAT	1	1	0	20FEB12	20FEB12	02MAR12	02MAR12	9
4BEX2040	FINISH COAT	1	1	0	21FEB12	21FEB12	05MAR12	05MAR12	9
4BEX2050	PLASTER CURE	15	15	0	22FEB12	13MAR12	06MAR12	26MAR12	9
4BEX2060	PRIME PAINT	1	1	0	14MAR12	14MAR12	27MAR12	27MAR12	9
4BEX2070	1ST PASS COLOR	1	1	0	15MAR12	15MAR12	28MAR12	28MAR12	9
4BEX2080	FINISH PAINT	1	1	0	16MAR12	16MAR12	29MAR12	29MAR12	9
TESTING & INSPECTIONS									
4BTN1000	UG PLUMBING / STACK	1	1	0	26JAN12	26JAN12	08FEB12	08FEB12	9
4BTN1010	UG ELECTRICAL	1	1	0	26JAN12	26JAN12	08FEB12	08FEB12	9
4BTN1020	FOUNDATION BUILDING	1	1	0	17JAN12	17JAN12	30JAN12	30JAN12	9
4BTN1030	STEM WALL BUILDING	1	1	0	19JAN12	19JAN12	01FEB12	01FEB12	9
4BTN1035	SOG BUILDING	1	1	0	31JAN12	31JAN12	13FEB12	13FEB12	9
4BTN1040	1ST LIFT CMU	1	1	0	06FEB12	06FEB12	20FEB12	20FEB12	10
4BTN1050	2ND LIFT CMU	1	1	0	09FEB12	09FEB12	22FEB12	22FEB12	9
4BTN1060	LINTEL BEAM	1	1	0	14FEB12	14FEB12	27FEB12	27FEB12	9
4BTN2040	LIGHTNING PROTECTION BOND FTG	1	1	0	25JAN12	25JAN12	08FEB12	08FEB12	10
4BTN2050	COLUMN FOOTING / BOLT PROJ	1	1	0	17JAN12	17JAN12	01FEB12	01FEB12	11
4BTN2080	PEST CONTROL	1	1	0	25JAN12	25JAN12	09FEB12	09FEB12	11
4BTN2090	VAPOR BARRIER / REINFORCING	1	1	0	27JAN12	27JAN12	13FEB12	13FEB12	11
4BTN2140	STEEL COLUMN, BEAM, JOIST	1	1	0	06FEB12	06FEB12	27FEB12	27FEB12	15
4BTN2150	DECKING	1	1	0	20FEB12	20FEB12	02MAR12	02MAR12	9
4BTN2160	WELDING	1	1	0	22FEB12	22FEB12	06MAR12	06MAR12	9
4BTN2170	ROOF INSULATION	1	1	0	28FEB12	28FEB12	12MAR12	12MAR12	9
4BTN2180	ROOF MEMBRANE	1	1	0	02MAR12	02MAR12	16MAR12	16MAR12	10
4BTN2190	FINAL ROOF	1	1	0	09MAR12	09MAR12	23MAR12	23MAR12	10
4BTN2210	IN WALL ELECTRICAL	1	1	0	08FEB12	08FEB12	22FEB12	22FEB12	10
4BTN2220	IN WALL LOW VOLTAGE, DATA, COM	1	1	0	09FEB12	09FEB12	22FEB12	22FEB12	9
4BTN2230	IN WALL FIRE ALARM	1	1	0	09FEB12	09FEB12	22FEB12	22FEB12	9
4BTN2250	IN WALL PLUMBING	1	1	0	09FEB12	09FEB12	22FEB12	22FEB12	9
4BTN2280	WINDOW SET	1	1	0	15FEB12	15FEB12	28FEB12	28FEB12	9
4BTN2320	ABOVE CEILING PLUMBING	1	1	0	06MAR12	06MAR12	26MAR12	26MAR12	14
4BTN2330	ABOVE CEILING ELECTRICAL	1	1	0	12MAR12	12MAR12	26MAR12	26MAR12	10
4BTN2340	ABOVE CEILING LOW VOLTAGE,	1	1	0	12MAR12	12MAR12	26MAR12	26MAR12	10
4BTN2350	ABOVE CEILING FIRE ALARM	1	1	0	12MAR12	12MAR12	26MAR12	26MAR12	10
4BTN2360	ABOVE CEILING SECURITY	1	1	0	12MAR12	12MAR12	26MAR12	26MAR12	10

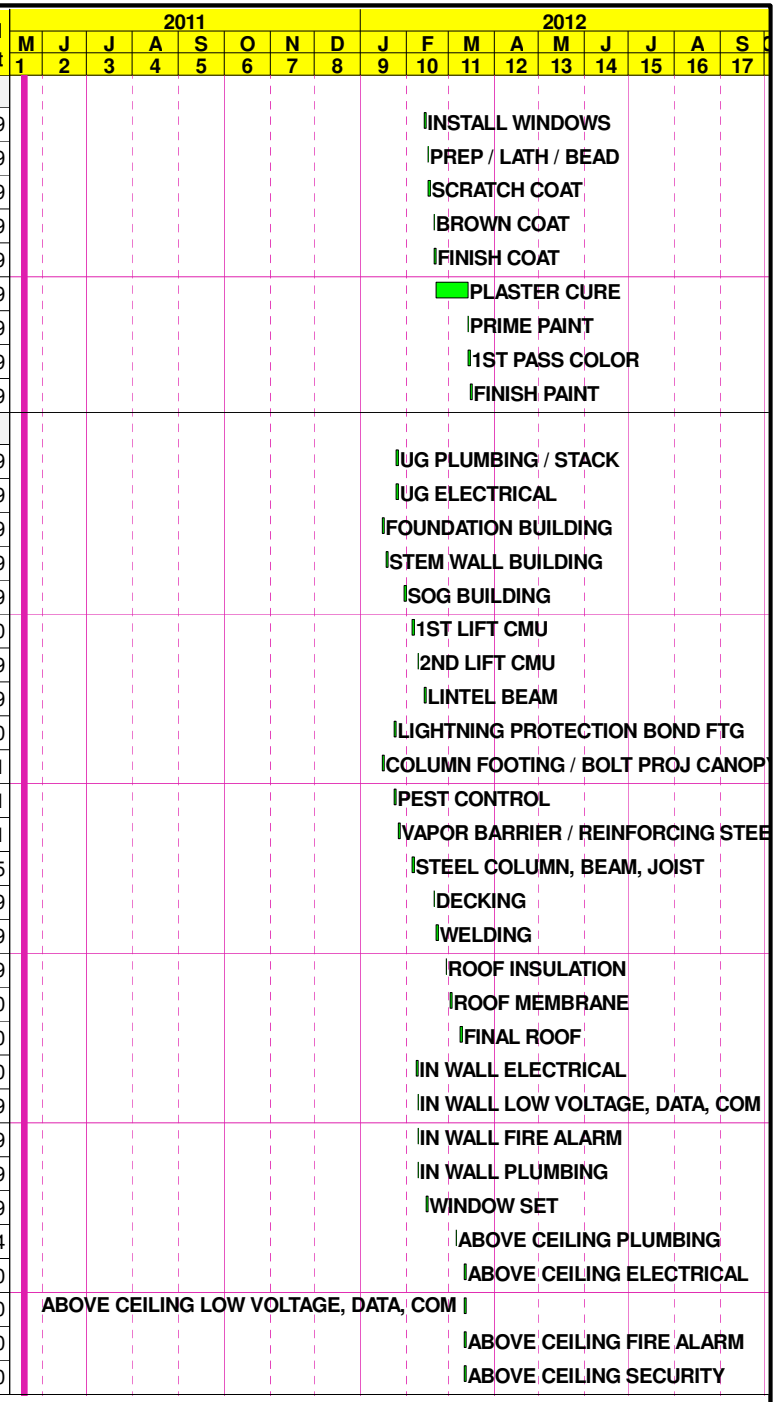

Start Date 20MAY11
Finish Date 30AUG12
Data Date 20MAY11
Run Date 12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
4BTN2365	ABOVE CEILING FINAL	1	1	0	13MAR12	13MAR12	27MAR12	27MAR12	10
4BTN2380	PLUMBING INSULATION	1	1	0	13MAR12	13MAR12	27MAR12	27MAR12	10
4BTN2410	ELECTRICAL TRIM	1	1	0	06MAR12	06MAR12	26MAR12	26MAR12	14
4BTN2420	PLUMBING TRIM	1	1	0	13MAR12	13MAR12	27MAR12	27MAR12	10
4BTN2430	FINAL MECHANICAL	1	1	0	13MAR12	13MAR12	27MAR12	27MAR12	10
4BTN2440	FINAL ELECTRICAL	1	1	0	13MAR12	13MAR12	27MAR12	27MAR12	10
4BTN2450	FINAL PLUMBING	1	1	0	14MAR12	14MAR12	28MAR12	28MAR12	10
4BTN2460	FINAL FIRE ALARM	1	1	0	30APR12	30APR12	15MAY12	15MAY12	11
4BTN2470	FINAL SECURITY	1	1	0	13MAR12	13MAR12	27MAR12	27MAR12	10
4BTN2500	SIGNAGE	1	1	0	12MAR12	12MAR12	23MAR12	23MAR12	9
4BTN2510	LIGHTNING PROTECTION	1	1	0	09MAR12	09MAR12	23MAR12	23MAR12	10
REQUIRED DOCUMENTS									
4BRD2000	BUILDING FINAL W / ATTACHED	1	1	0	02MAY12	02MAY12	17MAY12	17MAY12	11
4BRD2010	FIRE SPRINKLER FINAL NFPA 13	1	1	0	13MAR12	13MAR12	27MAR12	27MAR12	10
4BRD2020	FIRE ALARM NFPA 72 FORM	1	1	0	01MAY12	01MAY12	16MAY12	16MAY12	11
4BRD2030	PLUMBING BACT TEST @ SAMPLE	10	10	0	15MAR12	28MAR12	29MAR12	11APR12	10
4BRD2040	MECHANICAL T&B	5	5	0	14MAR12	20MAR12	28MAR12	03APR12	10
4BRD2050	ELECTRICAL FINAL	1	1	0	14MAR12	14MAR12	28MAR12	28MAR12	10
4BRD2060	SECURITY SYSTEM FINAL	1	1	0	14MAR12	14MAR12	28MAR12	28MAR12	10
4BRD2070	COMMUNICATION SYSTEM FINAL	1	1	0	14MAR12	14MAR12	28MAR12	28MAR12	10
4BRD2100	LIGHTNING PROTECTION UL	10	10	0	12MAR12	23MAR12	26MAR12	06APR12	10
4BRD2110	ROOFING FINAL	1	1	0	12MAR12	12MAR12	26MAR12	26MAR12	10
4BRD2140	FIRE ALARM MONITORING	1	1	0	15MAR12	15MAR12	29MAR12	29MAR12	10
COMPLETION & PUNCH									
4BPL2000	DOSTER PRE PUNCH LIST	5	5	0	30APR12	04MAY12	09MAY12	15MAY12	7
4BPL2010	COMPLETE DOSTER PRE PUNCH	10	10	0	07MAY12	18MAY12	16MAY12	30MAY12	7
4BPL2020	COMPLETE OCPS QAQC LIST	5	5	0	21MAY12	25MAY12	08JUN12	14JUN12	13
4BPL2030	OWNER ARCHITECT GENERATE	3	3	0	30MAY12	01JUN12	18JUN12	20JUN12	13
4BPL2040	RECEIVE OWNER FINAL PUNCH LIST	1	1	0	04JUN12	04JUN12	21JUN12	21JUN12	13
4BPL2050	COMPLETE OWNER ARCHITECT	15	15	0	05JUN12	25JUN12	22JUN12	13JUL12	13
CONNECTOR									
MILESTONES									
CONMS2000	BUILDINGS CONNECTED	1	1	0	12APR12	12APR12	30APR12	30APR12	12
CONMS2010	SUB COMPLETION LIST COMPLETE	1	1	0	29JUN12	29JUN12	17JUL12	17JUL12	11
CONMS2020	OWNER ARCHITECT PUNCH	1	1	0	23JUL12	23JUL12	07AUG12	07AUG12	11
UNDERGROUND									
CONUG2000	LAYOUT	1	1	0	05MAR12	05MAR12	15MAR12	15MAR12	8
CONUG2010	ALL MEP REQUIRES FOR	5	5	0	06MAR12	12MAR12	16MAR12	22MAR12	8

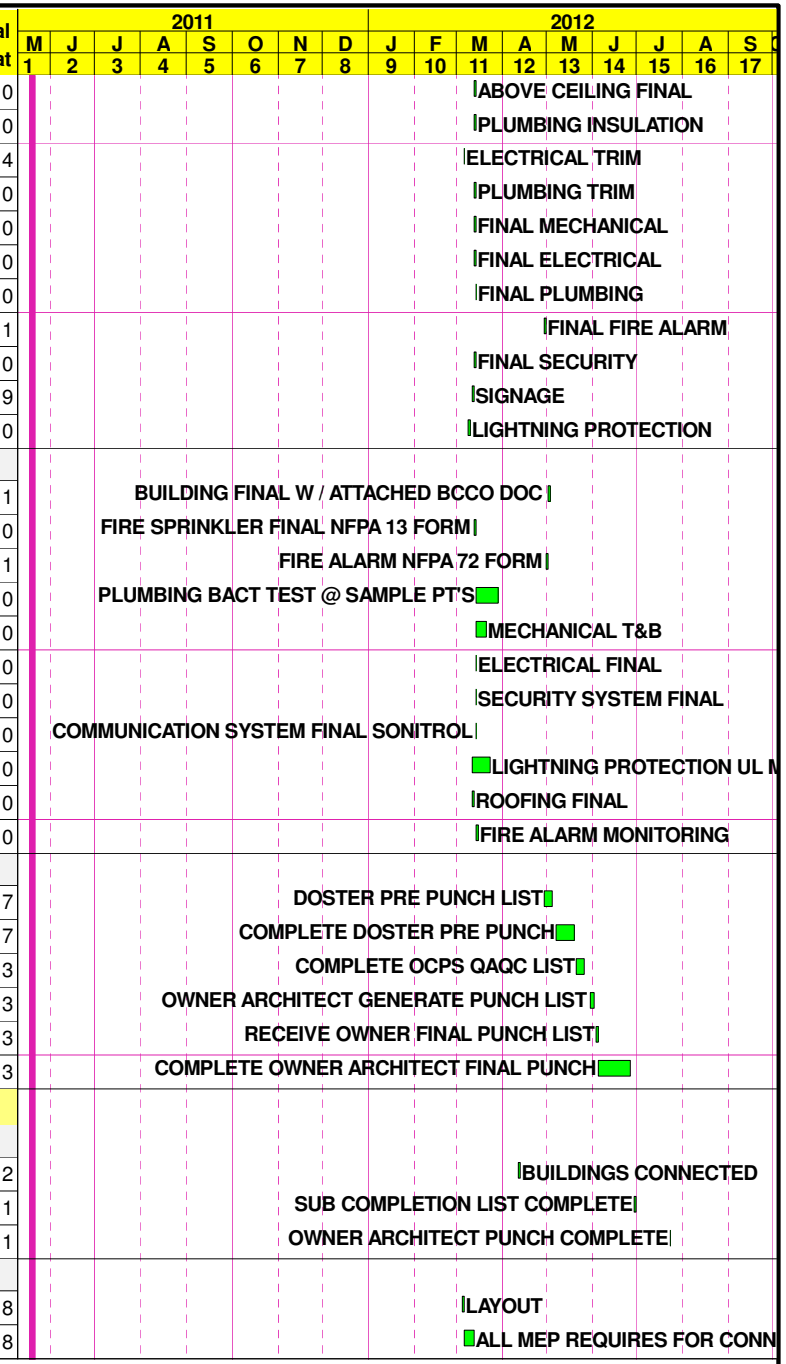

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
STRUCTURE									
CONST2000	EXCAVATE FOUNDATIONS	2	2	0	13MAR12	14MAR12	23MAR12	26MAR12	8
CONST2010	PLACE REINFORCING STEEL	2	2	0	15MAR12	16MAR12	27MAR12	28MAR12	8
CONST2020	PLACE FOUNDATIONS	2	2	0	20MAR12	21MAR12	30MAR12	02APR12	8
CONST2030	INSTALL COLUMN REINFORCING	2	2	0	22MAR12	23MAR12	03APR12	04APR12	8
CONST2040	FORM COLUMNS	2	2	0	26MAR12	27MAR12	05APR12	06APR12	8
CONST2050	PLACE COLUMNS	2	2	0	29MAR12	30MAR12	10APR12	11APR12	8
CONST2060	FORM 2ND LEVEL DECK	3	3	0	02APR12	04APR12	12APR12	16APR12	8
CONST2070	PLACE REINFORCING STEEL &	2	2	0	05APR12	06APR12	17APR12	18APR12	8
CONST2080	PLACE IN SLAB DRAINS AND PIPING	2	2	0	05APR12	06APR12	19APR12	20APR12	10
CONST2090	PLACE 2ND LEVEL DECK	2	2	0	09APR12	10APR12	19APR12	20APR12	8
CONST2100	REINFORCING STEEL & EMBEDS	2	2	0	11APR12	12APR12	23APR12	24APR12	8
CONST2110	FORM 2ND LEVEL COLUMNS	2	2	0	13APR12	16APR12	25APR12	26APR12	8
CONST2120	PLACE 2ND LEVEL COLUMNS	2	2	0	18APR12	19APR12	30APR12	01MAY12	8
CONST2130	FRAME ROOF STRUCTURE	3	3	0	20APR12	24APR12	02MAY12	04MAY12	8
CONST2150	INTERMEDIATE LANDING WALLS	3	3	0	22MAR12	26MAR12	05APR12	09APR12	10
CONST2160	BACKFILL INTERMEDIATE WALLS	2	2	0	28MAR12	29MAR12	11APR12	12APR12	10
CONST2170	FORM INTERMEDIATE SLAB	2	2	0	30MAR12	02APR12	13APR12	16APR12	10
CONST2180	PLACE REINFORCING STEEL	2	2	0	03APR12	04APR12	17APR12	18APR12	10
CONST2190	PLACE IN SLAB DRAINS AND PIPING	2	2	0	05APR12	06APR12	19APR12	20APR12	10
CONST2200	PLACE INTERMEDIATE SLAB	2	2	0	10APR12	11APR12	24APR12	25APR12	10
CONST2210	FORM STAIR RISERS	3	3	0	12APR12	16APR12	26APR12	30APR12	10
CONST2220	PLACE REINFORCING STEEL STAIRS	2	2	0	17APR12	18APR12	01MAY12	02MAY12	10
CONST2230	PLACE STAIRS	2	2	0	25APR12	26APR12	07MAY12	08MAY12	8
ROOF									
CONRF2000	INSTALL PRE-ENGINEERED ROOF	5	5	0	10MAY12	16MAY12	22MAY12	29MAY12	8
INTERIOR 1ST FLOOR									
CONF2000	INSTALL RAILS	2	2	0	21MAY12	22MAY12	06JUN12	07JUN12	11
CONF2010	INSTALL LIGHTING	2	2	0	23MAY12	24MAY12	08JUN12	11JUN12	11
INTERIOR 2ND FLOOR									
CONS2000	INSTALL RAILS	2	2	0	23MAY12	24MAY12	13JUN12	14JUN12	14
CONS2010	INSTALL LIGHTING	2	2	0	25MAY12	29MAY12	12JUN12	13JUN12	11
EXTERIOR									
CONEX2000	RUB EXPOSED SURFACES	3	3	0	27APR12	01MAY12	09MAY12	11MAY12	8
CONEX2010	PRIME PAINT	2	2	0	02MAY12	03MAY12	14MAY12	15MAY12	8
CONEX2020	POINT UP	2	2	0	04MAY12	07MAY12	16MAY12	17MAY12	8
CONEX2030	SPOT PRIME & 1ST PASS COLOR	2	2	0	08MAY12	09MAY12	18MAY12	21MAY12	8
CONEX2040	TRIM OUT MEP	2	2	0	25MAY12	29MAY12	12JUN12	13JUN12	11
CONEX2050	INSTALL PRECAST	2	2	0	10MAY12	11MAY12	25MAY12	29MAY12	11

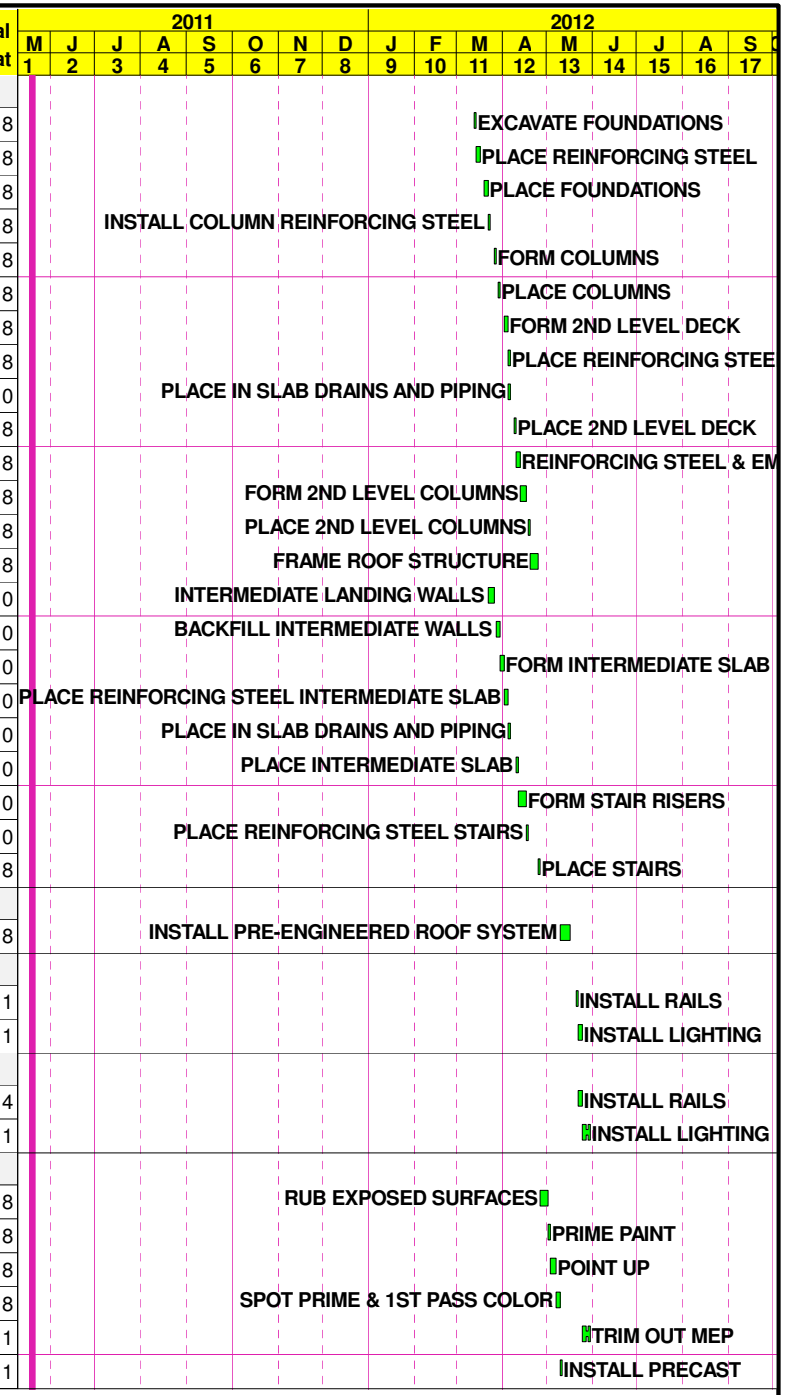

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
CONEX2060	FINAL PASS COLOR	2	2	0	30MAY12	31MAY12	14JUN12	15JUN12	11
TESTING & INSPECTIONS									
COSTN2000	FOUNDATIONS	1	1	0	19MAR12	19MAR12	29MAR12	29MAR12	8
COSTN2010	1ST LIFT COLUMNS	1	1	0	28MAR12	28MAR12	09APR12	09APR12	8
COSTN2020	1ST LIFT MASONRY	1	1	0	27MAR12	27MAR12	10APR12	10APR12	10
COSTN2030	2ND LIFT MASONRY	1	1	0	28MAR12	28MAR12	11APR12	11APR12	10
COSTN2040	INTERMEDIATE SLAB	1	1	0	09APR12	09APR12	23APR12	23APR12	10
COSTN2050	2ND LIFT COLUMNS	1	1	0	17APR12	17APR12	27APR12	27APR12	8
COSTN2060	ROOF / CANOPY	1	1	0	17MAY12	17MAY12	30MAY12	30MAY12	8
COSTN2070	1.0-INT STAIRS	1	1	0	19APR12	19APR12	03MAY12	03MAY12	10
COSTN2080	INT-2.0 STAIRS	1	1	0	24APR12	24APR12	04MAY12	04MAY12	8
COSTN2090	FINAL	1	1	0	18MAY12	18MAY12	31MAY12	31MAY12	8
REQUIRED DOCUMENTS									
CONRD2000	BUILDING FINAL W / ATTACHED	1	1	0	01JUN12	01JUN12	13JUN12	13JUN12	8
CONRD2020	FIRE ALARM NFPA 72 FORM	1	1	0	21MAY12	21MAY12	12JUN12	12JUN12	15
CONRD2050	ELECTRICAL FINAL	1	1	0	21MAY12	21MAY12	12JUN12	12JUN12	15
CONRD2060	SECURITY SYSTEM FINAL	1	1	0	21MAY12	21MAY12	12JUN12	12JUN12	15
CONRD2070	COMMUNICATION SYSTEM FINAL	1	1	0	21MAY12	21MAY12	12JUN12	12JUN12	15
CONRD2100	LIGHTNING PROTECTION UL	8	8	0	21MAY12	31MAY12	01JUN12	12JUN12	8
CONRD2110	ROOFING FINAL	1	1	0	21MAY12	21MAY12	12JUN12	12JUN12	15
CONRD2140	FIRE ALARM MONITORING	1	1	0	21MAY12	21MAY12	12JUN12	12JUN12	15
COMPLETION & PUNCH									
COPL2000	DOSTER PRE PUNCH LIST	5	5	0	01JUN12	07JUN12	18JUN12	22JUN12	11
COPL2010	COMPLETE DOSTER PRE PUNCH	10	10	0	08JUN12	21JUN12	25JUN12	09JUL12	11
COPL2020	COMPLETE OCPS QAQC LIST	5	5	0	22JUN12	28JUN12	10JUL12	16JUL12	11
COPL2030	OWNER ARCHITECT GENERATE	3	3	0	02JUL12	05JUL12	18JUL12	20JUL12	11
COPL2040	RECEIVE OWNER FINAL PUNCH LIST	1	1	0	06JUL12	06JUL12	23JUL12	23JUL12	11
COPL2050	COMPLETE OWNER ARCHITECT	10	10	0	09JUL12	20JUL12	24JUL12	06AUG12	11

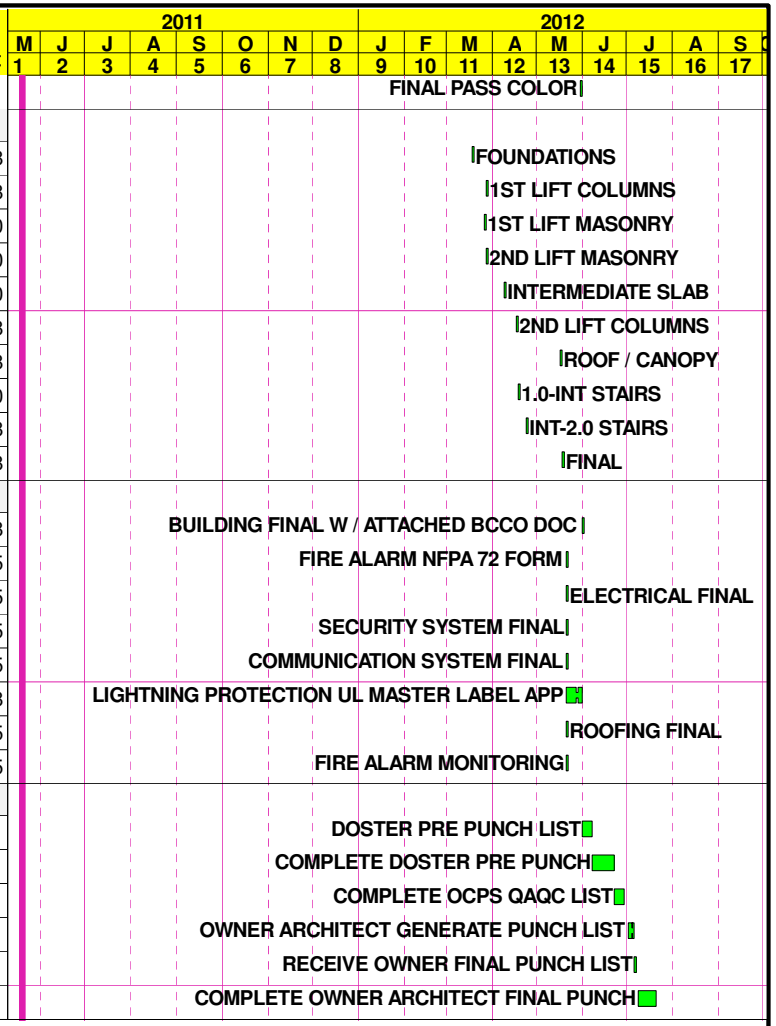

Start Date	20MAY11
Finish Date	30AUG12
Data Date	20MAY11
Run Date	12OCT11 11:51

Early Bar
Progress Bar
Critical Activity

OCP0

DOSTER CONSTRUCTION COMPANY

PRINCETON ELEMENTRY SCHOOL

Baseline Schedule

Date	Revision	Checked	Approved

© Primavera Systems, Inc.
