95RP	Activity ID	Activity Description	Orig Dur	Rem Dur	Actual Duration	%	Early Start	Early Finish	Target 1 Early Start	Target 1 Early Finish	Target 2 Early Start	Target 2 Early Finish	Total Float	Target Total Flo	Target Total Flo
HCC	C1060	Start Phase IV	0	0	0	0	16MAR15		16FEB15		02JUN14		-150	-45	0
	C1480	Mill and Resurface Broward SB and NB Lanes	171	171	0	0	16MAR15	22OCT15					-150	0	0
	C1360	Install Final FC/Painted Stripe Broward	36	36	0	0	26MAY15	08JUL15					-150	0	0
	C1490	Final Striping (thermoplastic) Broward	1	1	0	0	29JUL15	29JUL15					-150	0	0
	C1500	Install Delineators Broward	29	29	0	0	30JUL15	09SEP15					-150	0	0
	C1510	Remaining ITS Stand-Alone/Subsystem Testing Brow	10	10	0	0	10SEP15	23SEP15					-150	0	0
	C1400	FDOT/FTE Approves Subsystem Results	15	15	0	0	24SEP15	08OCT15	18MAY15	01JUN15			-188	-60	0
	C1390	Submit Subsystem Test Results to FDOT/FTE	1	1	0	0	24SEP15	24SEP15	18MAY15	18MAY15			-150	-56	0
	C1350	Notification to FDOT to beg, System Test	1	1	0	0	25SEP15	25SEP15	19MAY15	19MAY15			-150	-55	0
ITS	C1200	Conduct 30 calendar day System Test Period	30	30	0	0	26SEP15	25OCT15	20MAY15	18JUN15	04JUL14	02AUG14	-192	-64	1
	C1330	FDOT Written Approval of System Test	1	1	0	0	26OCT15	26OCT15	19JUN15	19JUN15			-192	-64	0
HCC	END	End of Construction	0	0	0	0		26OCT15		16JUL15		01OCT14	-192	-91	1
	FINALACC	Final Acceptance	0	0	0	0		26OCT15		16JUL15		01OCT14	-192	-91	1

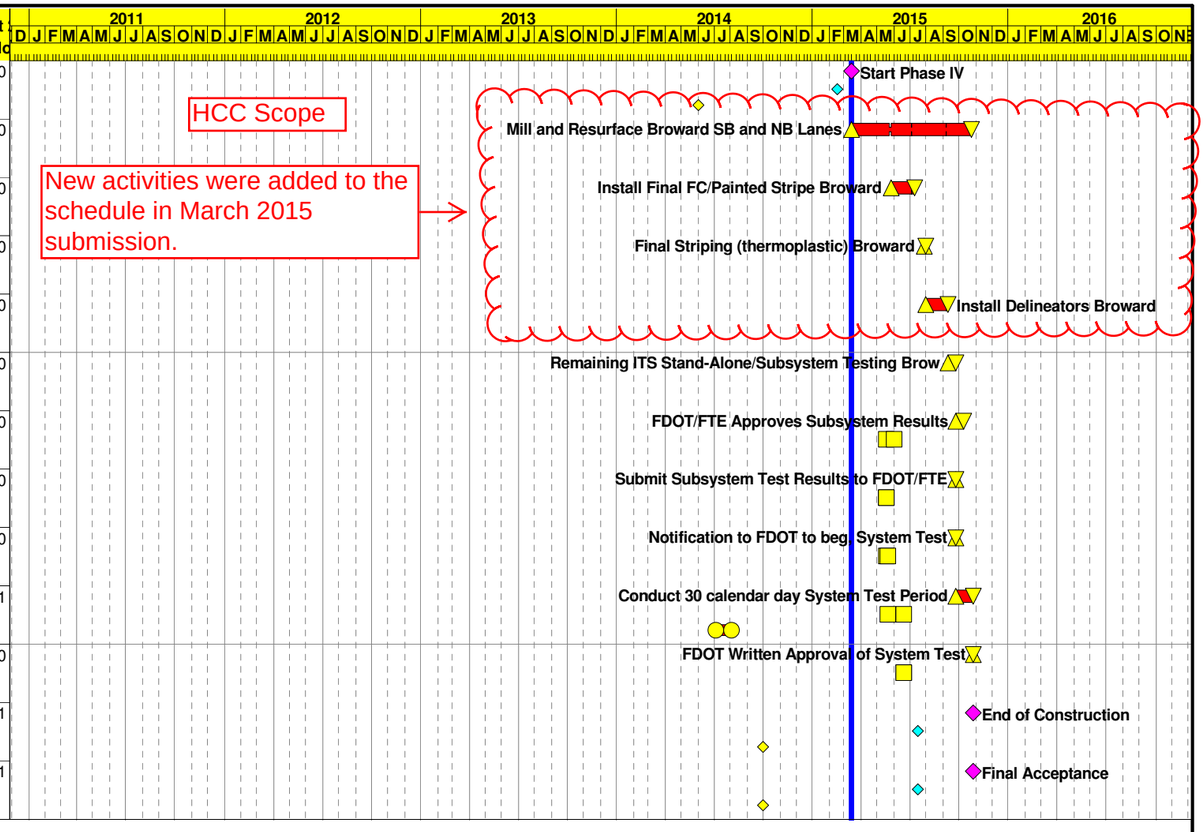

Start Date 28NOV10
Finish Date 26OCT15
Data Date 15MAR15
Must Finish Date 17APR15

Early Bar
Target 01
Target 02
Progress Bar
Critical Activity

© Primavera Systems, Inc.

0339

Sheet 1 of 1

Hubbard Construction

I-95 Express Lanes March Update

Longest Path (March 2015)

Target 01 = Previous Submission

Target 02 = Baseline Schedule

Date	Revision	Checked	Approved
