| 95RP | Activity ID | Activity Description | Orig Dur | Rem Dur | Actual Duration | % | Early Start | Early Finish | Target 1 Early Start | Target 1 Early Finish | Target 2 Early Start | Target 2 Early Finish | Total Float | Target Total Float | Target Total Float |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | 2BC390 | Demo median barrier wall as needed Phase 2B | 20 | 0 | 407 | 100 | 22APR13A | 15NOV14A | 22APR13A | 17OCT14 | 26FEB13 | 25MAR13 | | -30 | 3 |
| ITS | 2BC360 | Construct median sign & ITS foundations Phase 2B | 65 | 5 | 330 | 93 | 09AUG13A | 21NOV14 | 09AUG13A | 28OCT14 | 26MAR13 | 25JUN13 | -23 | -30 | 3 |
| TOLL | C1010 | Toll Gantry work | 40 | 8 | 66 | 80 | 25AUG14A | 03DEC14 | 25AUG14A | 07NOV14 | 09OCT13 | 05DEC13 | -23 | -30 | 3 |
| FTE | C1140 | Turn toll facilities over FTE/TEC install/test | 120 | 120 | 0 | 0 | 04DEC14 | 27APR15 | 19NOV14 | 12MAY15 | 03JUL14 | 02JUL14 | -23 | -30 | 4 |
| HCC | END | End of Construction | 0 | 0 | 0 | 0 | | 27APR15 | | 12MAY15 | | 01OCT14 | -27 | -42 | 1 |
| | FINALACC | Final Acceptance | 0 | 0 | 0 | 0 | | 27APR15 | | 12MAY15 | | 01OCT14 | -27 | -42 | 1 |

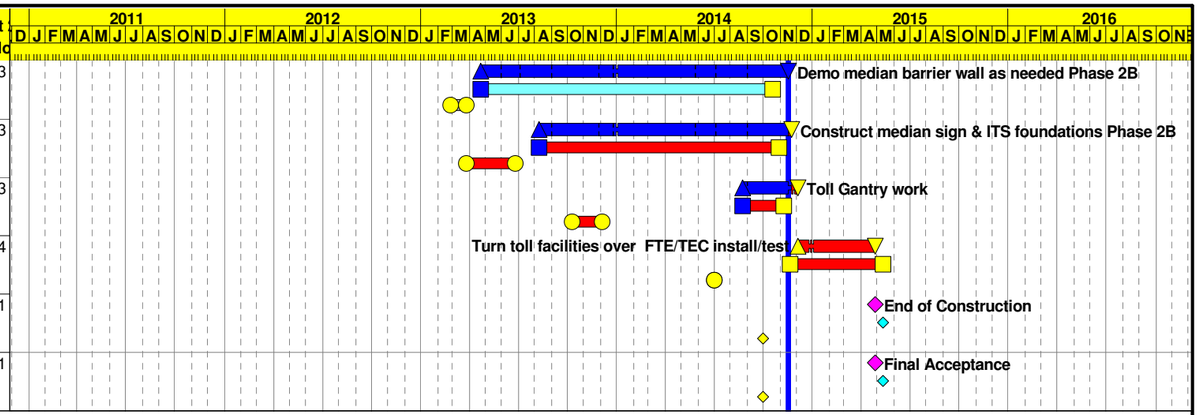


The current drop in the finish date occurred as a result of the modifications made to the assigned calendar (#01) by making Saturdays as working days. Accordingly, task C1140 "Turn toll facilities over FTE/TEC install/test" counted (145) cd's instead of the previously submitted (175) cd's.

| | |
|---|---|
| Start Date | 28NOV10 |
| Finish Date | 27APR15 |
| Data Date | 16NOV14 |
| Must Finish Date | 31MAR15 |

© Primavera Systems, Inc.

Early Bar
Target 01
Target 02
Progress Bar
Critical Activity

1139

Sheet 1 of 1

Hubbard Construction

I-95 Express Lanes November Update

Longest Path (November 2014)

Target 01 = Previous Submission

Target 02 = Baseline Schedule

| Date | Revision | Checked | Approved |
|---|---|---|---|
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |
