RESP	Activity ID	Activity Description	Orig Dur	Rem Dur	Actual Duration	%	Early Start	Early Finish	Target 1 Early Start	Target 1 Early Finish	Target 2 Early Start	Target 2 Early Finish	Total Float	Target Total Flo	Target Total Flo
ITS	2BC350	Construct ITS Phase 2B	40	4	364	90	16APR13A	25SEP14	16APR13A	21AUG14	09APR13	04JUN13	-28	-24	91
ITS	C860	Construct ITS (Cont'd)	80	16	364	80	16APR13A	13OCT14	16APR13A	15SEP14	18JUL13	07NOV13	-28	-24	75
ITS	C990	ITS Stand Alone Testing (All Components)	50	48	0	5	14OCT14	22DEC14	16SEP14	20NOV14	08NOV13	11DEC13	-28	-24	75
	C1370	Submit ITS Test Results to FDOT/FTE for Approval	14	14	0	0	23DEC14	14JAN15	21NOV14	12DEC14			-28	-24	0
ITS	C1030	ITS Integration	27	24	0	10	15JAN15	17FEB15	15DEC14	20JAN15	12DEC13	13FEB14	-28	-24	75
	C1380	Notify FDOT of Subsystem Testing	2	2	0	0	18FEB15	19FEB15	21JAN15	22JAN15			-28	-24	0
ITS	C1090	ITS Subsystem Testing	30	30	0	0	20FEB15	02APR15	23JAN15	05MAR15	02JUN14	03JUL14	-28	-24	0
	C1390	Submit Subsystem Test Results to FDOT/FTE	1	1	0	0	02APR15	02APR15	05MAR15	05MAR15			-28	-24	0
	C1400	FDOT/FTE Approves Subsystem Results	15	15	0	0	02APR15	22APR15	05MAR15	15APR15			-28	-24	0
	C1350	Notification to FDOT to beg, System Test	1	1	0	0	03APR15	03APR15	27MAR15	27MAR15			-28	-24	0
ITS	C1200	Conduct 30 calendar day System Test Period	30	30	0	0	04APR15	03MAY15	28MAR15	26APR15	04JUL14	02AUG14	-38	-32	1
	C1330	FDOT Written Approval of System Test	1	1	0	0	04MAY15	04MAY15	27APR15	27APR15			-38	-32	0
HCC	END	End of Construction	0	0	0	0		04MAY15		27APR15		01OCT14	-38	-32	1
	FINALACC	Final Acceptance	0	0	0	0		04MAY15		29APR15		01OCT14	-38	-34	1

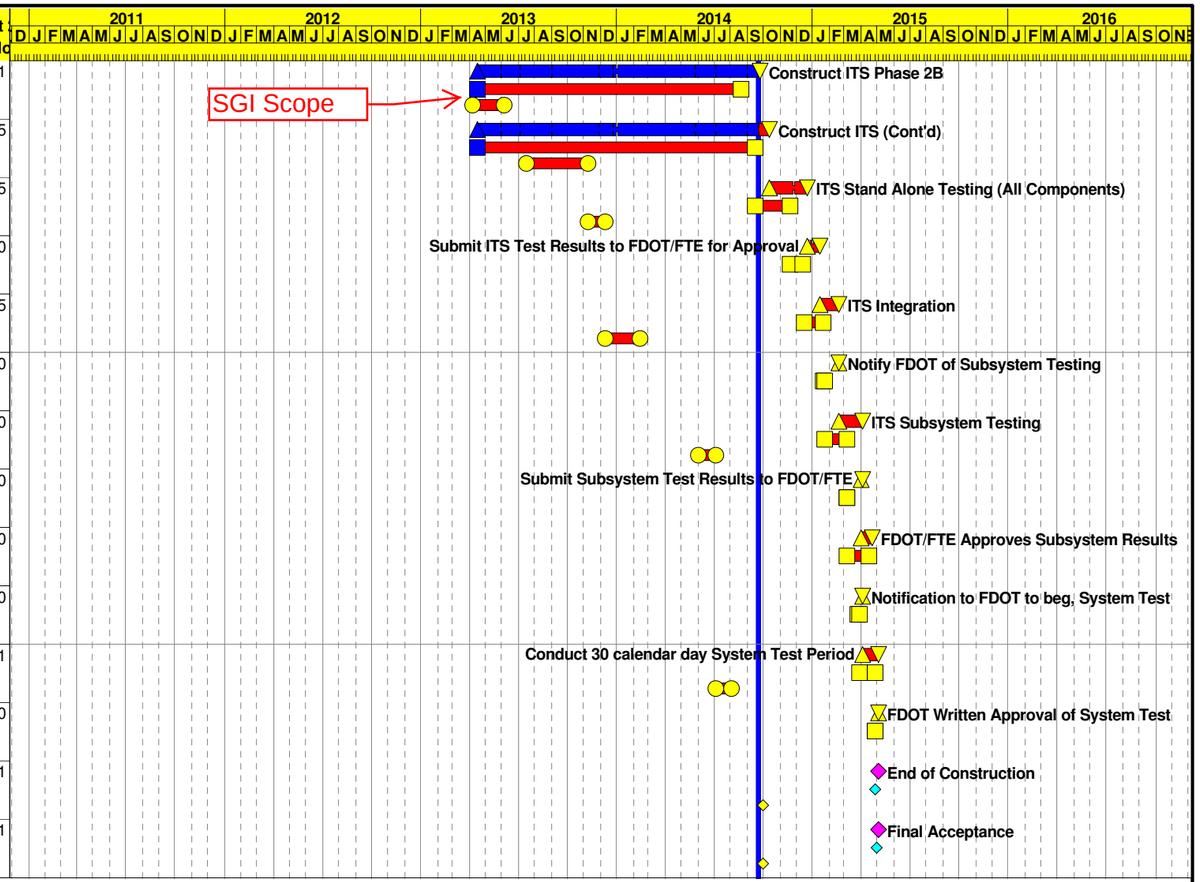

The duration of C1400 "FDOT/FTE Approves Subsystem Results" has been reduced by (15) working days.

Start Date 28NOV10
Finish Date 04MAY15
Data Date 21SEP14

© Primavera Systems, Inc.

Early Bar
Target 01
Target 02
Progress Bar
Critical Activity

0939

Sheet 1 of 1

Hubbard Construction

I-95 Express Lanes September Update

Longest Path (September 2014)

Target 01 = Previous Submission

Target 02 = Baseline Schedule

Date	Revision	Checked	Approved
