
Sample 230kV Underground Cable Project Schedule

HSE Contractors | Public Portfolio Example

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish
Sample 230kV Underground Cable Project Schedule		603	413	Nov-07-2025 A	Feb-29-2028	0	Nov-07-2025	
230kV Underground Cable Project		603	413	Nov-07-2025 A	Feb-29-2028	0	Nov-07-2025	
230kV Underground Cable Project		603	413	Nov-07-2025 A	Feb-29-2028	0	Nov-07-2025	
Milestones		547	411	Nov-07-2025 A	Feb-29-2028	0	Nov-07-2025	
Contract Milestones		765	575	Nov-07-2025 A	Feb-29-2028	0	Nov-07-2025	
MIL-OTHER-1000	Contract Award	0	0	Nov-07-2025 A			Nov-07-2025	
MIL-OTHER-1010	Date of PO Issuance	11	0	Jan-26-2026 A	Feb-05-2026 A		Jan-26-2026	Feb-05-2026
MIL-OTHER-1020	First Kick-off Meeting	0	0	Feb-06-2026 A	Feb-06-2026 A		Feb-06-2026	Feb-06-2026
MIL-OTHER-1030	Confirmation of Cut Length	0	0	May-07-2026 A	Jul-31-2026 A		May-07-2026	Jul-31-2026
MIL-OTHER-1060	Release of Cable Manufacturing	0	0	May-07-2026 A	May-07-2026 A		May-07-2026	May-07-2026
MAR-1000	Performance & Payment Bond	1	0	May-14-2026 A	May-14-2026 A		May-14-2026	May-14-2026
MIL-OTHER-1070	Release of Splice Manufacturing	0	0	Jul-07-2026 A	Jul-07-2026 A		Jul-07-2026	Jul-07-2026
MIL-OTHER-1080	Release of Outdoor Terminations Manufacturing	0	0	Jul-28-2026 A	Jul-28-2026 A		Jul-28-2026	Jul-28-2026
MIL-OTHER-1090	Release of Other Accessories Manufacturing	0	0	Aug-04-2026	Aug-04-2026	575		
MIL-OTHER-1040	Finalize Engineering Design	0	0	Aug-29-2026	Aug-29-2026	16		
MIL-OTHER-1100	Finalize Pre-Construction Deliverables	0	0	Oct-13-2026	Oct-13-2026	87		
MIL-OTHER-1050	Completion of Type Test & Seismic Test on Dry Type Termination	5	5	Dec-15-2026	Dec-19-2026	437		
M-162	100% Cable Splice on site	5	5	Dec-24-2026	Dec-28-2026	428		
M-163	100% Outer Termination on site	5	5	Mar-16-2027	Mar-20-2027	346		
M-160	100% Cable Onsite	0	0	May-01-2027	May-01-2027	305		
M-161	100% Cable Accessories Onsite	0	0	Jun-08-2027	Jun-08-2027	267		
M-155	100% Engineering & Testing	0	0	Oct-10-2027	Oct-10-2027	143		
M-195	Completion of Cable Installation	5	5	Oct-21-2027	Oct-25-2027	127		
M-210	Complete Cable Termination	0	0	Dec-05-2027	Dec-05-2027	87		
M-190	Complete Cable Racking & Grounding Installation	0	0	Dec-16-2027	Dec-16-2027	76		
M-200	Complete Cable Splicing	0	0	Jan-05-2028	Jan-05-2028	45		
M-220	Complete Testing and Commissioning	0	0	Feb-09-2028	Feb-09-2028	6		
MIL-OTHER-1110	Substantial Completion	0	0		Feb-09-2028*	21		
MIL-OTHER-1120	Final Completion	0	0		Feb-29-2028*	0		
Payment Milestones		457	392	May-14-2026 A	Feb-29-2028	0	May-14-2026	
Direct Payment Milestones		392	392	Aug-29-2026	Feb-29-2028	0		
PAY-ENG-SA-1030	Payment Milestone - Seismic Analysis of the Cable Racking System Owner's review and accep	1	1	Aug-29-2026	Aug-29-2026	549		
PAY-ET-ST-1040	Payment Milestone - Sesmic Testing on the Dry Type Termination	1	1	Sep-24-2026	Sep-24-2026	523		
PAY-EP-1050	Payment Milestone - Environmental Plan Acceptance	1	1	Oct-13-2026	Oct-13-2026	504		
PAY-ET-TT-1040	Payment Milestone - Cable System Type Testing	1	1	Nov-11-2026	Nov-11-2026	475		
PAY-MOB-1010	Payment Milestone - Mobilization & Site Set up	1	1	Dec-04-2026	Dec-04-2026	452		
PAY-MOB-1000	Payment Milestone - Establishment of Laydown yard (Project Laydown Yard)	1	1	Dec-04-2026	Dec-04-2026	452		
PAY-VI-1000	Payment Milestone - Racking & Grounding Materials Receiving Visual Inspection	1	1	Dec-17-2026	Dec-17-2026	439		
PAY-VI-1040	Payment Milestone - Cable Clamps (Spring Clamps, Racheting Devie, Joint Clamp, etc) Rece	1	1	Dec-17-2026	Dec-17-2026	439		
PAY-VI-1030	Payment Milestone - Bonding & Grounding Cables Receiving Visual Inspection	1	1	Dec-22-2026	Dec-22-2026	434		
PAY-CTR-1000	Payment Milestone - Cable Receiving Inspection & Testing - SITE-A/SITE-B - 1st Batch	1	1	Jan-02-2027	Jan-02-2027	423		
PAY-VI-1010	Payment Milestone - Splices Receiving Visual Inspection	1	1	Jan-07-2027	Jan-07-2027	418		
PAY-VI-1020	Payment Milestone - Outer terminations Receiving Visual Inspection -1st Batch	1	1	Jan-07-2027	Jan-07-2027	418		
PAY-VI-1050	Payment Milestone - Linkboxes+SVLs Receiving Visual Inspection	1	1	Jan-07-2027	Jan-07-2027	418		
FI-TS-1000-PAY	Payment Milestone - Post-test Install MH12-SC1 & SC2 to South Riser Pole Termination (6 D	1	1	Jan-19-2027	Jan-19-2027	406		
PAY-VI-1060	Payment Milestone - DAS Instrument Receiving Visual Inspection	1	1	Jan-19-2027	Jan-19-2027	406		
FI-TS-1010-PAY	Payment Milestone - Post-test Install MH2-SC1 & SC2 to North Riser Pole Termination (6 Dr	1	1	Feb-03-2027	Feb-03-2027	391		

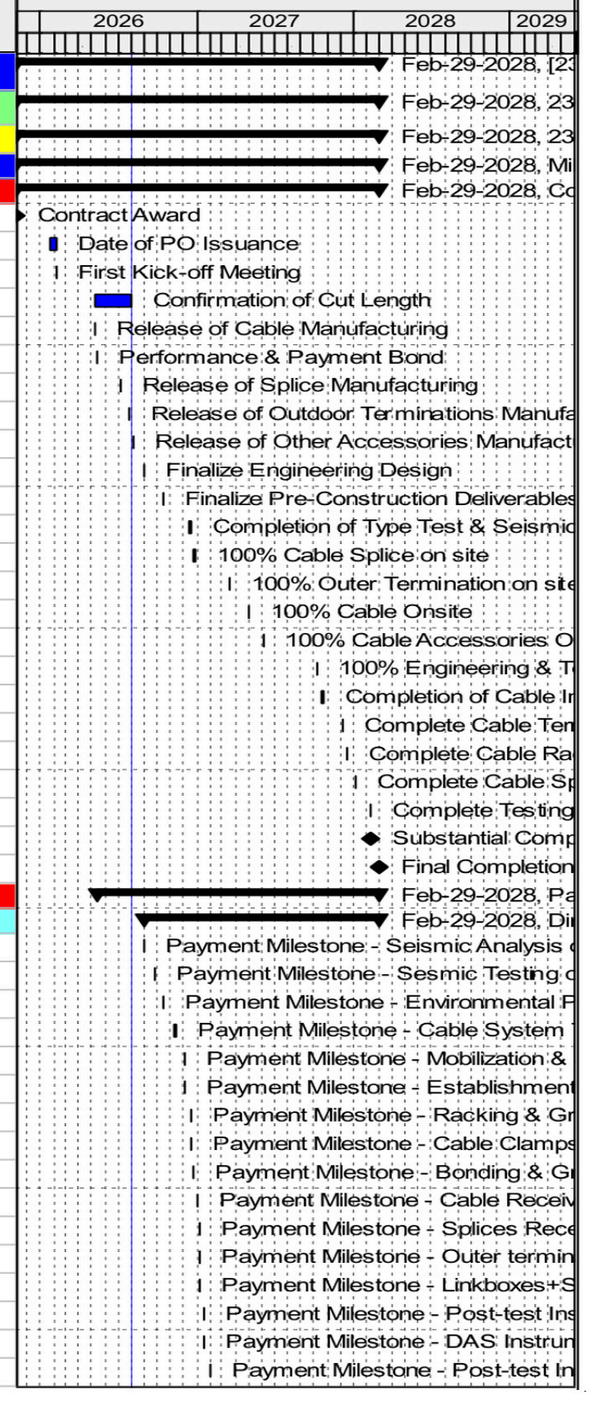


Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Sample 230kV Underground Cable Project Schedule

HSE Contractors | Public Portfolio Example


Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish
POST-TEST-1000-PAY	Payment Milestone - Post-test Install MH1-SC1 & SC2 to MH2-SC1 & SC2 (6 drums) - SITE-A	1	1	Feb-03-2027	Feb-03-2027	279		
PAY-TERM-INS-1010	Payment Milestone - Final Inspection for R&G&Termination - South Riser Poles (6 Terminatic	1	1	Feb-11-2027	Feb-11-2027	383		
FI-TS-2010-PAY	Payment Milestone - Post-test Install MH2-SC1 & SC2 to North Riser Pole Termination (6 Dr	1	1	Feb-17-2027	Feb-17-2027	377		
POST-TEST-1995-PAY	Payment Milestone - Post-test Install MH1-SC1 & SC2 to MH2-SC1 & SC2 (6 drums) - SITE-B	1	1	Feb-17-2027	Feb-17-2027	269		
PAY-TERM-INS-1000	Payment Milestone - Final Inspection for R&G&Termination - North Riser Poles (6 Terminatio	1	1	Feb-26-2027	Feb-26-2027	368		
FI-SPLICE-1000-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH1-SC1 & SC2	1	1	Feb-26-2027	Feb-26-2027	368		
FI-SPLICE-1995-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH1-SC1 & SC2	1	1	Feb-26-2027	Feb-26-2027	262		
POST-TEST-1010-PAY	Payment Milestone - Post-test Install MH2-SC1 & SC2 to MH3-SC1 & SC2 (6 drums) - SITE-A	1	1	Mar-04-2027	Mar-04-2027	362		
POST-TEST-1020-PAY	Payment Milestone - Post-test Install MH3-SC1 & SC2 to MH4-SC1 & SC2 (6 drums) - SITE-A	1	1	Mar-14-2027	Mar-14-2027	352		
PAY-VI-1070	Payment Milestone - Outer terminations Receiving Visual Inspection -2nd Batch	1	1	Mar-16-2027	Mar-16-2027	250		
PAY-TERM-INS-1030	Payment Milestone - Final Inspection for R&G&Termination - North Riser Poles (6 Terminatio	1	1	Mar-18-2027	Mar-18-2027	348		
PAY-CTR-1010	Payment Milestone - Cable Receiving Inspection & Testing - SITE-A/SITE-B - 2nd Batch	1	1	Mar-19-2027	Mar-19-2027	247		
FI-SPLICE-1020-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH3-SC1 & SC2	1	1	Mar-28-2027	Mar-28-2027	338		
POST-TEST-1030-PAY	Payment Milestone - Post-test Install MH4-SC1 & SC2 to MH5-SC1 & SC2 (6 drums) - SITE-A	1	1	Mar-31-2027	Mar-31-2027	335		
POST-TEST-1040-PAY	Payment Milestone - Post-test Install MH5-SC1 & SC2 to MH6-SC1 & SC2 (6 drums) - SITE-A	1	1	Apr-10-2027	Apr-10-2027	325		
FI-SPLICE-1030-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH4-SC1 & SC2	1	1	Apr-10-2027	Apr-10-2027	325		
POST-TEST-1050-PAY	Payment Milestone - Post-test Install MH6-SC1 & SC2 to MH7-SC1 & SC2 (6 drums) - SITE-A	1	1	Apr-21-2027	Apr-21-2027	314		
FI-SPLICE-1040-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH5-SC1 & SC2	1	1	Apr-21-2027	Apr-21-2027	314		
POST-TEST-1060-PAY	Payment Milestone - Post-test Install MH7-SC1 & SC2 to MH8-SC1 & SC2 (6 drums) - SITE-A	1	1	May-01-2027	May-01-2027	304		
FI-SPLICE-1050-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH6-SC1 & SC2	1	1	May-01-2027	May-01-2027	304		
PAY-CTR-1020	Payment Milestone - Cable Receiving Inspection & Testing - SITE-A/SITE-B - 3rd Batch	5	5	May-03-2027	May-07-2027	212		
POST-TEST-1070-PAY	Payment Milestone - Post-test Install MH8-SC1 & SC2 to MH9-SC1 & SC2 (6 drums) - SITE-A	1	1	May-12-2027	May-12-2027	293		
FI-SPLICE-1060-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH7-SC1 & SC2	1	1	May-12-2027	May-12-2027	293		
POST-TEST-1080-PAY	Payment Milestone - Post-test Install MH9-SC1 & SC2 to MH10-SC1 & SC2 (6 drums) - SITE-A	1	1	May-22-2027	May-22-2027	283		
FI-SPLICE-1070-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH8-SC1 & SC2	1	1	May-22-2027	May-22-2027	283		
POST-TEST-1090-PAY	Payment Milestone - Post-test Install MH10-SC1 & SC2 to MH11-SC1 & SC2 (6 drums) - SITE-A	1	1	Jun-02-2027	Jun-02-2027	272		
FI-SPLICE-1080-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH9-SC1 & SC2	1	1	Jun-02-2027	Jun-02-2027	272		
PAY-SA-130	Payment Milestone - Surge Arresters Receiving Visual Inspection	1	1	Jun-09-2027	Jun-09-2027	189		
POST-TEST-1100-PAY	Payment Milestone - Post-test Install MH11-SC1 & SC2 to MH12-SC1 & SC2 (6 drums) - SITE-A	1	1	Jun-12-2027	Jun-12-2027	262		
FI-SPLICE-1090-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH10-SC1 & SC2	1	1	Jun-12-2027	Jun-12-2027	262		
FI-SPLICE-1100-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH11-SC1 & SC2	1	1	Jun-23-2027	Jun-23-2027	251		
FI-SPLICE-1110-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH12-SC1 & SC2	1	1	Jul-03-2027	Jul-03-2027	241		
POST-TEST-2000-PAY	Payment Milestone - Post-test Install MH2-SC1 & SC2 to MH3-SC1 & SC2 (6 drums) - SITE-B	1	1	Jul-17-2027	Jul-17-2027	227		
POST-TEST-2010-PAY	Payment Milestone - Post-test Install MH3-SC1 & SC2 to MH4-SC1 & SC2 (6 drums) - SITE-B	1	1	Jul-28-2027	Jul-28-2027	216		
POST-TEST-2020-PAY	Payment Milestone - Post-test Install MH4-SC1 & SC2 to MH5-SC1 & SC2 (6 drums) - SITE-B	1	1	Aug-07-2027	Aug-07-2027	206		
FI-SPLICE-2010-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH3-SC1 & SC2	1	1	Aug-07-2027	Aug-07-2027	206		
POST-TEST-2030-PAY	Payment Milestone - Post-test Install MH5-SC1 & SC2 to MH6-SC1 & SC2 (6 drums) - SITE-B	1	1	Aug-18-2027	Aug-18-2027	195		
FI-SPLICE-2020-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH4-SC1 & SC2	1	1	Aug-18-2027	Aug-18-2027	195		
POST-TEST-2040-PAY	Payment Milestone - Post-test Install MH6-SC1 & SC2 to MH7-SC1 & SC2 (6 drums) - SITE-B	1	1	Aug-28-2027	Aug-28-2027	185		
FI-SPLICE-2030-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH5-SC1 & SC2	1	1	Aug-28-2027	Aug-28-2027	185		
POST-TEST-2050-PAY	Payment Milestone - Post-test Install MH7-SC1 & SC2 to MH8-SC1 & SC2 (6 drums) - SITE-B	1	1	Sep-09-2027	Sep-09-2027	173		
FI-SPLICE-2040-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH6-SC1 & SC2	1	1	Sep-09-2027	Sep-09-2027	173		
POST-TEST-2060-PAY	Payment Milestone - Post-test Install MH8-SC1 & SC2 to MH9-SC1 & SC2 (6 drums) - SITE-B	1	1	Sep-19-2027	Sep-19-2027	163		
FI-SPLICE-2050-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH7-SC1 & SC2	1	1	Sep-19-2027	Sep-19-2027	163		
POST-TEST-2070-PAY	Payment Milestone - Post-test Install MH9-SC1 & SC2 to MH10-SC1 & SC2 (6 drums) - SITE-B	1	1	Sep-30-2027	Sep-30-2027	152		
FI-SPLICE-2060-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH8-SC1 & SC2	1	1	Sep-30-2027	Sep-30-2027	152		
POST-TEST-2080-PAY	Payment Milestone - Post-test Install MH10-SC1 & SC2 to MH11-SC1 & SC2 (6 drums) - MI	1	1	Oct-10-2027	Oct-10-2027	142		

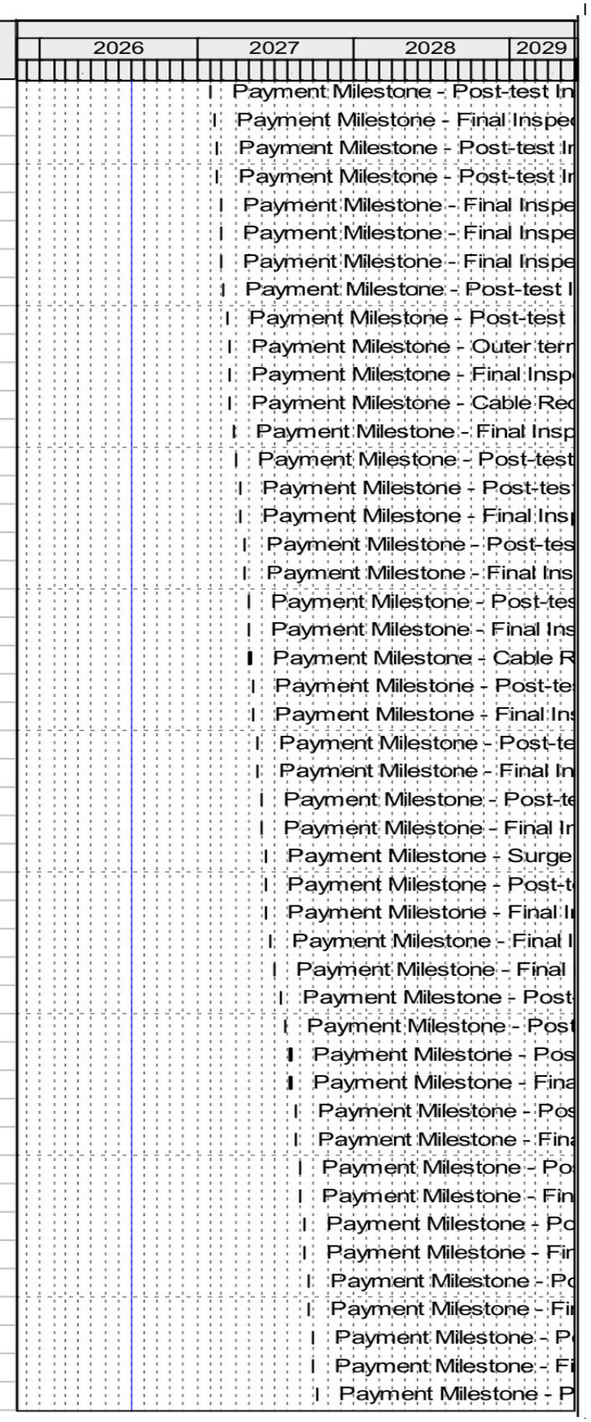

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Sample 230kV Underground Cable Project Schedule

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish
FI-SPLICE-2070-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH9-SC1 & SC2	1	1	Oct-10-2027	Oct-10-2027	142		
POST-TEST-2090-PAY	Payment Milestone - Post-test Install MH11-SC1 & SC2 to MH12-SC1 & SC2 (6 drums) - MI	1	1	Oct-21-2027	Oct-21-2027	131		
FI-SPLICE-2080-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH10-SC1 & SC2	1	1	Oct-21-2027	Oct-21-2027	131		
FI-SPLICE-2090-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH11-SC1 & SC2	1	1	Oct-31-2027	Oct-31-2027	121		
FI-TS-2000-PAY	Payment Milestone - Post-test Install MH12-SC1 & SC2 to South Riser Pole Termination (6 D	1	1	Nov-06-2027	Nov-06-2027	115		
FI-SPLICE-2100-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH12-SC1 & SC2	1	1	Nov-11-2027	Nov-11-2027	110		
PAY-TERM-INS-1020	Payment Milestone - Final Inspection for R&G&Termination - South Riser Poles (6 Terminatic	1	1	Dec-05-2027	Dec-05-2027	86		
FI-SPLICE-2000-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH2-SC1 & SC2	1	1	Dec-16-2027	Dec-16-2027	75		
FI-SPLICE-1010-PAY	Payment Milestone - Final Inspection for Racking & Grounding & Splicing - MH2-SC1 & SC2	1	1	Jan-05-2028	Jan-05-2028	55		
PAY-INT-T-1000	Payment Milestone - End to End Jacket Integrity Test (South Riser Pole to North Riser Pole)	1	1	Jan-11-2028	Jan-11-2028	49		
PAY-INT-T-1010	Payment Milestone - End to End Jacket Integrity Test (South Riser Pole to North Riser Pole)	1	1	Jan-16-2028	Jan-16-2028	44		
PAY-CON-1000	Payment Milestone - Configration Set up for PDM System	1	1	Jan-22-2028	Jan-22-2028	38		
PAY-CON-1010	Payment Milestone - Configration Set up for DTS & Fault locating System	1	1	Jan-22-2028	Jan-22-2028	38		
PAY-MOB-1020	Payment Milestone - Site Restoration (Project Laydown Yard)	5	5	Feb-15-2028	Feb-19-2028	10		
PAY-CD-100	Payment Milestone - Demobilization	1	1	Feb-19-2028	Feb-19-2028	10		
PAY-CD-120	Payment Milestone - O&M Manuals Review & Approval	1	1	Feb-29-2028	Feb-29-2028	0		
Monthly Indirect Cost Payment Milestones		638	425	May-14-2026 A	Feb-28-2028	1	May-14-2026	
March (2026)		1	0	May-14-2026 A	May-14-2026 A		May-14-2026	May-14-2026
MAR-26-1000	Performance & Payment Bod - Mar, 2026	1	0	May-14-2026 A	May-14-2026 A		May-14-2026	May-14-2026
December (2026)		1	1	Dec-31-2026	Dec-31-2026	425		
DEC-26-1000	Project Management Monthly - Dec,2026	1	1	Dec-31-2026	Dec-31-2026*	425		
DEC-26-1010	Environmental Management Monthly - Dec,2026	1	1	Dec-31-2026	Dec-31-2026*	425		
January (2027)		1	1	Jan-31-2027	Jan-31-2027	394		
JAN-27-1000	Project Management Monthly - Jan, 2027	1	1	Jan-31-2027	Jan-31-2027*	394		
JAN-27-1010	Environmental Management Monthly - Jan, 2027	1	1	Jan-31-2027	Jan-31-2027*	394		
February (2027)		1	1	Feb-28-2027	Feb-28-2027	366		
FEB-27-1000	Project Management Monthly - Feb, 2027	1	1	Feb-28-2027	Feb-28-2027*	366		
FEB-27-1010	Environmental Management Monthly - Feb, 2027	1	1	Feb-28-2027	Feb-28-2027*	366		
March (2027)		1	1	Mar-31-2027	Mar-31-2027	335		
MAR-27-1000	Project Management Monthly - March, 2027	1	1	Mar-31-2027	Mar-31-2027*	335		
MAR-27-1010	Environmental Management Monthly - March, 2027	1	1	Mar-31-2027	Mar-31-2027*	335		
April (2027)		1	1	Apr-30-2027	Apr-30-2027	305		
APR-27-1000	Project Management Monthly - April, 2027	1	1	Apr-30-2027	Apr-30-2027*	305		
APR-27-1010	Environmental Management Monthly - April, 2027	1	1	Apr-30-2027	Apr-30-2027*	305		
May (2027)		1	1	May-31-2027	May-31-2027	274		
MAY-27-1000	Project Management Monthly - May, 2027	1	1	May-31-2027	May-31-2027*	274		
MAY-27-1010	Environmental Management Monthly - May, 2027	1	1	May-31-2027	May-31-2027*	274		
June (2027)		1	1	Jun-30-2027	Jun-30-2027	244		
JUN-27-1000	Project Management Monthly - Jun, 2027	1	1	Jun-30-2027	Jun-30-2027*	244		
JUN-27-1010	Environmental Management Monthly - Jun, 2027	1	1	Jun-30-2027	Jun-30-2027*	244		
July (2027)		1	1	Jul-31-2027	Jul-31-2027	213		
JUL-27-1000	Project Management Monthly - Jul, 2027	1	1	Jul-31-2027	Jul-31-2027*	213		
JUL-27-1010	Environmental Management Monthly - Jul, 2027	1	1	Jul-31-2027	Jul-31-2027*	213		
August (2027)		1	1	Aug-31-2027	Aug-31-2027	182		
AUG-27-1000	Project Management Monthly - Aug, 2027	1	1	Aug-31-2027	Aug-31-2027*	182		
AUG-27-1010	Environmental Management Monthly - Aug, 2027	1	1	Aug-31-2027	Aug-31-2027*	182		
September (2027)		1	1	Sep-30-2027	Sep-30-2027	152		
SEP-27-1000	Project Management Monthly - Sep, 2027	1	1	Sep-30-2027	Sep-30-2027*	152		

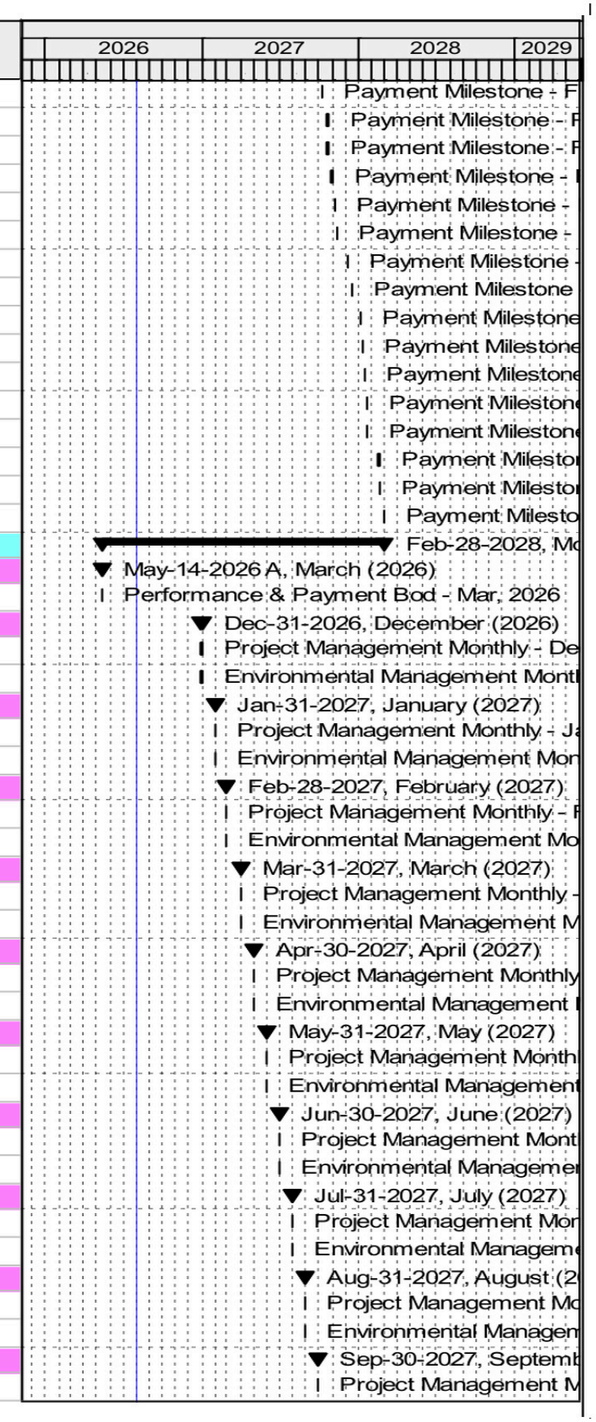


Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Sample 230kV Underground Cable Project Schedule

HSE Contractors | Public Portfolio Example

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish
SEP-27-1010	Environmental Management Monthly - Sep, 2027	1	1	Sep-30-2027	Sep-30-2027*	152		
November (2027)		1	1	Nov-30-2027	Nov-30-2027	91		
NOV-27-1000	Project Management Monthly - Nov, 2027	1	1	Nov-30-2027	Nov-30-2027*	91		
NOV-27-1010	Environmental Management Monthly - Nov, 2027	1	1	Nov-30-2027	Nov-30-2027*	91		
December (2027)		1	1	Dec-31-2027	Dec-31-2027	60		
DEC-27-1000	Project Management Monthly - Dec,2027	1	1	Dec-31-2027	Dec-31-2027*	60		
DEC-27-1010	Environmental Management Monthly - Dec,2027	1	1	Dec-31-2027	Dec-31-2027*	60		
January (2028)		1	1	Jan-31-2028	Jan-31-2028	29		
JAN-28-1000	Project Management Monthly - Jan, 2028	1	1	Jan-31-2028	Jan-31-2028*	29		
JAN-28-1010	Environmental Management Monthly - Jan, 2028	1	1	Jan-31-2028	Jan-31-2028*	29		
February (2028)		1	1	Feb-28-2028	Feb-28-2028	1		
FEB-28-1000	Project Management Monthly - Feb, 2028	1	1	Feb-28-2028	Feb-28-2028*	1		
FEB-28-1010	Environmental Management Monthly - Feb, 2028	1	1	Feb-28-2028	Feb-28-2028*	1		
Pre-Construction & Deliverables		286	96	Feb-06-2026 A	Dec-12-2026	317	Feb-06-2026	
Project Management Plan		155	31	Feb-06-2026 A	Sep-14-2026	71	Feb-06-2026	
PP-1000	Project Plan Preparation/Submittal	60	10	Feb-06-2026 A	Aug-13-2026	71	Feb-06-2026	
PP-1010	Project Plan Owner Review	10	10	Aug-14-2026	Aug-27-2026	71		
PP-1020	Project Plan Contractor Revised	10	10	Aug-28-2026	Sep-11-2026	71		
PP-1030	Project Plan Acceptance	1	1	Sep-14-2026	Sep-14-2026	71		
Risk Management Plan & Risk Register		138	10	Feb-06-2026 A	Aug-13-2026	105	Feb-06-2026	
RP-1000	Risk Plan Preparation/Submittal	15	0	Feb-06-2026 A	Feb-26-2026 A		Feb-06-2026	Feb-26-2026
RP-1010	Risk Plan Owner 1st Review	10	0	Feb-27-2026 A	Mar-13-2026 A		Feb-27-2026	Mar-13-2026
RP-1010.01	Risk Plan Contractor 1st Review	10	0	Mar-13-2026 A	Apr-14-2026 A		Mar-13-2026	Apr-14-2026
RP-1010.11	Risk Plan Owner 2nd Review	10	0	Apr-15-2026 A	Apr-21-2026 A		Apr-15-2026	Apr-21-2026
RP-1010.21	Risk Plan Contractor 2nd Review	10	0	Apr-22-2026 A	May-05-2026 A		Apr-22-2026	May-05-2026
RP-1030	Risk Plan Final review & Acceptance	10	10	May-06-2026 A	Aug-13-2026	92	May-06-2026	
Construction Management Plan		186	62	Feb-06-2026 A	Oct-27-2026	260	Feb-06-2026	
CP-1000	Construction Plan Preparation/Submittal	90	10	Feb-06-2026 A	Aug-13-2026	51	Feb-06-2026	
CP-1010	Construction Plan 1st Review	10	10	Aug-14-2026	Aug-27-2026	51		
CP-1020	Construction Plan 1st Revised	10	10	Aug-28-2026	Sep-11-2026	51		
CP-1030	Construction Plan 2nd Review	10	10	Sep-14-2026	Sep-25-2026	51		
CP-1040	Construction Plan 2nd Revised	10	10	Sep-28-2026	Oct-09-2026	51		
CP-1050	Construction Plan Acceptance	1	1	Oct-12-2026	Oct-12-2026	51		
Scaffolding Design		186	62	Feb-06-2026 A	Oct-27-2026	260	Feb-06-2026	
SCAFF-1000	Scaffolding Design Preparation & Submittal	90	32	Feb-06-2026 A	Sep-15-2026	260	Feb-06-2026	
SCAFF-1010	Scaffolding Design Owner Review	10	10	Sep-16-2026	Sep-29-2026	260		
SCAFF-1020	Scaffolding Design Design Contractor Revised	10	10	Sep-30-2026	Oct-13-2026	260		
SCAFF-1030	Scaffolding Design Owner Acceptance/Approval	10	10	Oct-14-2026	Oct-27-2026	260		
Material Management Plan Yard Plan		175	51	Feb-06-2026 A	Oct-12-2026	51	Feb-06-2026	
MP-1000	Develop/Submit Material Management Plan	90	10	Feb-06-2026 A	Aug-13-2026	51	Feb-06-2026	
MP-1010	Material Management Plan 1st Review	10	10	Aug-14-2026	Aug-27-2026	51		
MP-1020	Material Management Plan 1st Revised	10	10	Aug-28-2026	Sep-11-2026	51		
MP-1030	Material Management Plan 2nd Review	10	10	Sep-14-2026	Sep-25-2026	51		
MP-1040	Material Management Plan 2nd Revised	10	10	Sep-28-2026	Oct-09-2026	51		
MP-1050	Material Management Plan Acceptance	1	1	Oct-12-2026	Oct-12-2026	51		
Environmental Compliance Plan		175	51	Feb-06-2026 A	Oct-12-2026	21	Feb-06-2026	
EP-1000	Environmental Plan Preparation/Submittal	90	10	Feb-06-2026 A	Aug-13-2026	21	Feb-06-2026	
EP-1010	Environmental Plan 1st Review	10	10	Aug-14-2026	Aug-27-2026	21		

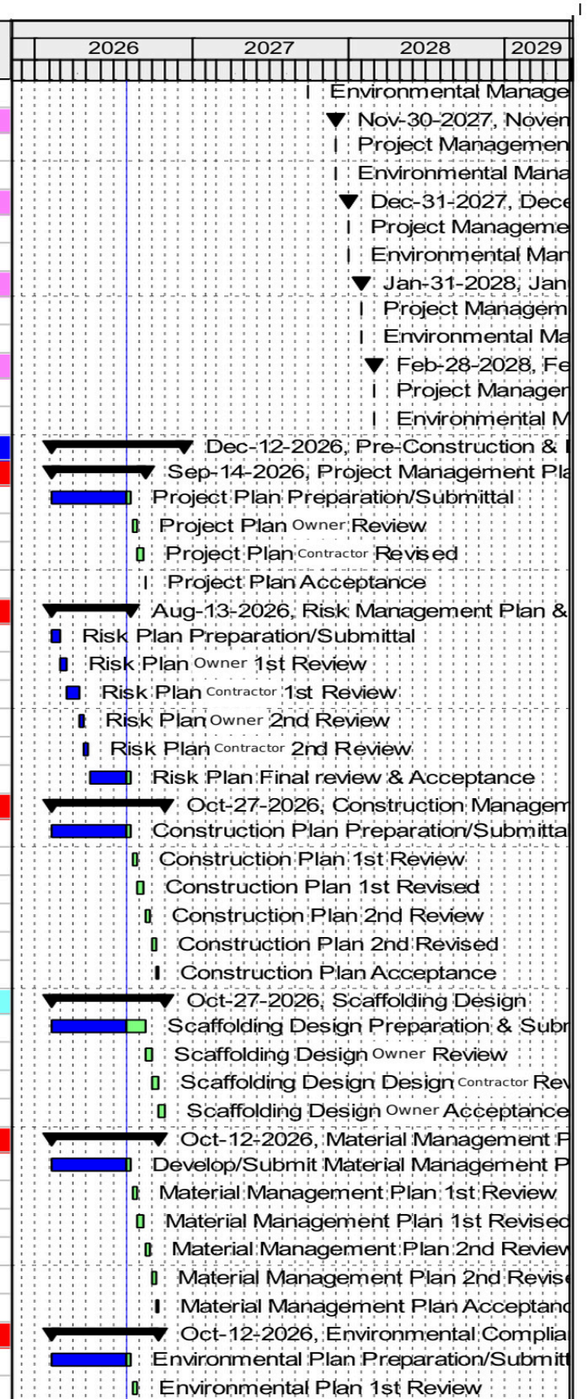


Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Sample 230kV Underground Cable Project Schedule

HSE Contractors | Public Portfolio Example

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish
EP-1020	Environmental Plan 1st Revised	10	10	Aug-28-2026	Sep-11-2026	21		
EP-1030	Environmental Plan 2nd Review	10	10	Sep-14-2026	Sep-25-2026	21		
EP-1040	Environmental Plan 2nd Revised	10	10	Sep-28-2026	Oct-09-2026	21		
EP-1050	Environmental Plan Acceptance	1	1	Oct-12-2026	Oct-12-2026	21		
Contractor Orientation & Safety Plan		65	0	Feb-06-2026 A	Jun-08-2026 A		Feb-06-2026	Jun-08-2026
SP-1000	Safety Plan Preparation/Submittal	30	0	Feb-06-2026 A	Mar-19-2026 A		Feb-06-2026	Mar-19-2026
SP-1010	Safety Plan Owner 1st Review	10	0	Mar-20-2026 A	Apr-02-2026 A		Mar-20-2026	Apr-02-2026
SP-1020	Safety Plan Contractor 1st Revised	10	0	Apr-03-2026 A	Apr-16-2026 A		Apr-03-2026	Apr-16-2026
SP-1020.01	Safety Plan Owner 2nd Review	5	0	Apr-17-2026 A	May-14-2026 A		Apr-17-2026	May-14-2026
SP-1020.11	Safety Plan Contractor 2nd Revised	5	0	May-15-2026 A	May-21-2026 A		May-15-2026	May-21-2026
SP-1030	Safety Plan Review and Acceptance	1	0	May-22-2026 A	Jun-08-2026 A		May-22-2026	Jun-08-2026
Confirm Cable Cut Length		126	0	Feb-06-2026 A	May-07-2026 A		Feb-06-2026	May-07-2026
Cutlength-1000	Owner provides cable cut length	15	0	Feb-06-2026 A	Apr-20-2026 A		Feb-06-2026	Apr-20-2026
Cutlength-1010	Contractor Review and Proposed Cut Length	5	0	Apr-21-2026 A	Apr-21-2026 A		Apr-21-2026	Apr-21-2026
Cutlength-1020	Owner 1st review	5	0	Apr-22-2026 A	Apr-23-2026 A		Apr-22-2026	Apr-23-2026
Cutlength-1030	Contractor 2nd Proposed Cut Length	5	0	Apr-24-2026 A	Apr-24-2026 A		Apr-24-2026	Apr-24-2026
Cutlength-1040	Owner Cable Cut Length Review and Acceptance	1	0	Apr-24-2026 A	May-07-2026 A		Apr-24-2026	May-07-2026
System Engineering Submittals		211	21	Feb-06-2026 A	Aug-28-2026	392	Feb-06-2026	
Electrical Design		80	0	Feb-06-2026 A	May-11-2026 A		Feb-06-2026	May-11-2026
ENG-ED-1000	Electrical Design Preparation/Submittal	3	0	Feb-06-2026 A	Feb-13-2026 A		Feb-06-2026	Feb-13-2026
ENG-ED-1010	Electrical Design Owner Review	10	0	Feb-16-2026 A	May-11-2026 A		Feb-16-2026	May-11-2026
ENG-ED-1020	Electrical Design Review and Acceptance by Owner	10	0	May-11-2026 A	May-11-2026 A		May-11-2026	May-11-2026
230kV Power Cable		85	0	Feb-06-2026 A	Apr-24-2026 A		Feb-06-2026	Apr-24-2026
ENG-PC-1000	Base Cable Design Preparation/Submittal	35	0	Feb-06-2026 A	Mar-03-2026 A		Feb-06-2026	Mar-03-2026
ENG-PC-1010	Base Cable Design Owner Review	30	0	Mar-04-2026 A	Apr-24-2026 A		Mar-04-2026	Apr-24-2026
ENG-PC-1020	Base Cable Design Review and Acceptance by Owner	20	0	Apr-24-2026 A	Apr-24-2026 A		Apr-24-2026	Apr-24-2026
230kV Cable Splice		150	0	Feb-06-2026 A	Jul-07-2026 A		Feb-06-2026	Jul-07-2026
ENG-CS-1000	Splice Design Preparation/Submittal	35	0	Feb-06-2026 A	Feb-13-2026 A		Feb-06-2026	Feb-13-2026
ENG-CS-1010	Splice Design Owner 1st Review	30	0	Feb-14-2026 A	Apr-07-2026 A		Feb-14-2026	Apr-07-2026
ENG-CS-1010.01	Splice Design Contractor 1st Review	5	0	Apr-08-2026 A	Apr-10-2026 A		Apr-08-2026	Apr-10-2026
ENG-CS-1010.11	Splice Design Owner 2nd Review	5	0	Apr-11-2026 A	Apr-13-2026 A		Apr-11-2026	Apr-13-2026
ENG-CS-1010.21	Splice Design Contractor 2nd Review	5	0	May-08-2026 A	May-26-2026 A		May-08-2026	May-26-2026
ENG-CS-1020	Splice Design Review and Acceptance by Owner	20	0	May-27-2026 A	Jul-07-2026 A		May-27-2026	Jul-07-2026
230kV Outdoor Termination Design		194	0	Feb-06-2026 A	Aug-07-2026 A		Feb-06-2026	Aug-07-2026
ENG-OT-1000	Outdoor Termination Design Preparation/Submittal	35	0	Feb-06-2026 A	Feb-13-2026 A		Feb-06-2026	Feb-13-2026
ENG-OT-1010	Outdoor Termination Design Owner 1st Review	30	0	Feb-16-2026 A	Apr-07-2026 A		Feb-16-2026	Apr-07-2026
ENG-OT-1010.01	Outdoor Termination Design Contractor 1st review	5	0	Apr-08-2026 A	Apr-10-2026 A		Apr-08-2026	Apr-10-2026
ENG-OT-1030	Outdoor Termination Design Owner 2nd Review	5	0	Apr-13-2026 A	May-11-2026 A		Apr-13-2026	May-11-2026
ENG-OT-1040	Outdoor Termination Design Contractor 2nd Revised	5	0	May-12-2026 A	May-22-2026 A		May-12-2026	May-22-2026
ENG-OT-1050	Outdoor Termination Design Owner 3rd Review and Acceptance	5	0	May-25-2026 A	Jun-01-2026 A		May-25-2026	Jun-01-2026
ENG-OT-1060	Outdoor Termination Design Contractor 3rd Revised	26	0	Jul-02-2026 A	Aug-07-2026 A		Jul-02-2026	Aug-07-2026
ENG-OT-1020	Outdoor Termination Design Final Review and Acceptance by Owner	1	0	Jul-08-2026 A	Jul-28-2026 A		Jul-08-2026	Jul-28-2026
Other Accessories Design		211	21	Feb-06-2026 A	Aug-28-2026	10	Feb-06-2026	
Racking & Grounding Design (for Splice Vault, Restraint Vaults, Riser Pole)		211	21	Feb-06-2026 A	Aug-28-2026	10	Feb-06-2026	
ENG-R&G-1000	Racking & Grounding Design Preparation / Sumittal	3	0	Feb-06-2026 A	Feb-13-2026 A		Feb-06-2026	Feb-13-2026
ENG-R&G-1010	Racking & Grounding Design 1st Owner Review	10	0	Feb-16-2026 A	Mar-05-2026 A		Feb-16-2026	Mar-05-2026
ENG-R&G-1010.01	Racking & Grounding Design 1st Contractor Review	5	0	Mar-06-2026 A	Mar-25-2026 A		Mar-06-2026	Mar-25-2026
ENG-R&G-1010.11	Racking & Grounding Design 2nd Owner Review	5	0	Mar-26-2026 A	Apr-07-2026 A		Mar-26-2026	Apr-07-2026

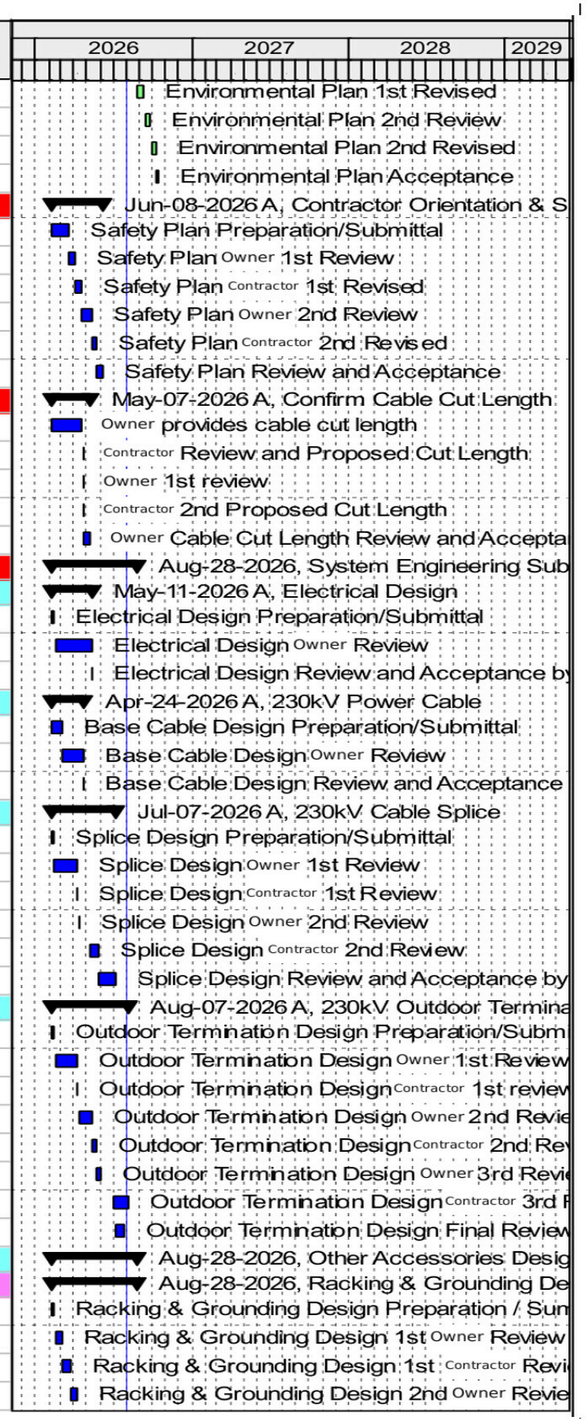


Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Milestone

Sample 230kV Underground Cable Project Schedule

HSE Contractors | Public Portfolio Example

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish
ENG-R&G-1010.21	Racking & Grounding Design 2nd Contractor Review	5	0	Apr-08-2026 A	Apr-09-2026 A		Apr-08-2026	Apr-09-2026
ENG-R&G-1010.31	Racking & Grounding Design 3rd Owner Review	5	0	Apr-10-2026 A	May-07-2026 A		Apr-10-2026	May-07-2026
ENG-R&G-1010.41	Racking & Grounding Design 3rd Contractor Review	5	0	May-08-2026 A	May-18-2026 A		May-08-2026	May-18-2026
ENG-R&G-1020	Racking & Grounding Design Review and Acceptance by Owner	5	0	May-19-2026 A	Jun-22-2026 A		May-19-2026	Jun-22-2026
ENG-R&G-1030	Racking & Grounding Design Contractor's 4th Revision	5	0	Jun-23-2026 A	Jul-13-2026 A		Jun-23-2026	Jul-13-2026
ENG-R&G-1040	Racking & Grounding Design Review and Acceptance by Owner	10	1	Jul-14-2026 A	Jul-31-2026	23	Jul-14-2026	
Seismic analysis of the cable racking system		142	21	Feb-11-2026 A	Aug-28-2026	9	Feb-11-2026	
ENG-SA-1000	Seismic Analysis of the Cable Racking System Preperation & Submittion	65	0	Feb-11-2026 A	Jul-23-2026 A		Feb-11-2026	Jul-23-2026
ENG-SA-1010	Seismic Analysis of the Cable Racking System Owner's 1st Review	10	10	Jul-24-2026 A	Aug-13-2026	9	Jul-24-2026	
ENG-SA-1020	Seismic Analysis of the Cable Racking System Contractor 1st Reivision	10	10	Aug-14-2026	Aug-27-2026	9		
ENG-SA-1030	Seismic Analysis of the Cable Racking System Owner's review and acceptance	1	1	Aug-28-2026	Aug-28-2026	9		
Spring Clamps Design		150	0	Feb-06-2026 A	Jul-28-2026 A		Feb-06-2026	Jul-28-2026
ENG-SC-1000	Spring Clamp Design Preparation/Submittal	30	0	Feb-06-2026 A	Feb-13-2026 A		Feb-06-2026	Feb-13-2026
ENG-SC-1010	Spring Clamp Design Owner 1st Review	35	0	Feb-16-2026 A	Apr-07-2026 A		Feb-16-2026	Apr-07-2026
ENG-SC-1010.01	Spring Clamp Design Contractor 1st Review	5	0	Apr-08-2026 A	May-20-2026 A		Apr-08-2026	May-20-2026
ENG-SC-1020	Spring Clamp Design Review and Acceptance by Owner	20	0	May-21-2026 A	Jul-28-2026 A		May-21-2026	Jul-28-2026
Joint Clamp Design		150	0	Feb-06-2026 A	Jul-28-2026 A		Feb-06-2026	Jul-28-2026
ENG-JC-1000	Splice Clamp Design Preparation/Submittal	30	0	Feb-06-2026 A	Feb-13-2026 A		Feb-06-2026	Feb-13-2026
ENG-JC-1010	Splice Clamp Design Owner 1st Review	35	0	Feb-16-2026 A	Apr-07-2026 A		Feb-16-2026	Apr-07-2026
ENG-JC-1010.01	Splice Clamp Design Contractor 1st Review	5	0	Apr-08-2026 A	May-20-2026 A		Apr-08-2026	May-20-2026
ENG-JC-1020	SpliceClamp Design Review and Acceptance by Owner	20	0	May-21-2026 A	Jul-28-2026 A		May-21-2026	Jul-28-2026
Link-Box Design		108	2	Feb-06-2026 A	Aug-03-2026	29	Feb-06-2026	
ENG-LB-1000	Link-Box Design Preparation/Submittal	30	0	Feb-06-2026 A	Feb-13-2026 A		Feb-06-2026	Feb-13-2026
ENG-LB-1010	Link-Box Design Owner Review	35	0	Feb-16-2026 A	May-18-2026 A		Feb-16-2026	May-18-2026
ENG-LB-1010.01	Link-Box Design Contractor Review	5	0	May-19-2026 A	May-21-2026 A		May-19-2026	May-21-2026
ENG-LB-1030	Link-Box Design Owner 2nd Review	5	0	May-22-2026 A	Jul-20-2026 A		May-22-2026	Jul-20-2026
ENG-LB-1040	Link-Box Design Contractor 2nd Revised	5	0	Jul-21-2026 A	Jul-22-2026 A		Jul-21-2026	Jul-22-2026
ENG-LB-1020	Link-Box Design Review and Acceptance by Owner	5	2	Jul-23-2026 A	Aug-03-2026	28	Jul-23-2026	
Lightning Arrester Design		116	0	Feb-06-2026 A	May-19-2026 A		Feb-06-2026	May-19-2026
ENG-LA-1000	Lightning Arrester Preparation/Submittal	30	0	Feb-06-2026 A	Mar-04-2026 A		Feb-06-2026	Mar-04-2026
ENG-LA-1010	Lightning Arrester 1st Owner Review	35	0	Mar-05-2026 A	Apr-10-2026 A		Mar-05-2026	Apr-10-2026
ENG-LA-1010.01	Lightning Arrester 1st Contractor Review	5	0	Apr-11-2026 A	Apr-20-2026 A		Apr-11-2026	Apr-20-2026
ENG-LA-1010.11	Lightning Arrester 2nd Owner Review	5	0	Apr-21-2026 A	May-18-2026 A		Apr-21-2026	May-18-2026
ENG-LA-1020	Lightning Arrester Review and Acceptance by Owner	20	0	May-19-2026 A	May-19-2026 A		May-19-2026	May-19-2026
Bonding & Ground Continuity Cables Design		116	0	Feb-06-2026 A	Jul-10-2026 A		Feb-06-2026	Jul-10-2026
ENG-B&GCC-1000	Bonding & Grounding Cable Preparation/Submittal	30	0	Feb-06-2026 A	Feb-13-2026 A		Feb-06-2026	Feb-13-2026
ENG-B&GCC-1010	Bonding & Grounding Cable 1st Owner Review	35	0	Feb-16-2026 A	May-18-2026 A		Feb-16-2026	May-18-2026
ENG-B&GCC-1010.01	Bonding & Grounding Cable 1st Contractor Review	5	0	May-19-2026 A	May-19-2026 A		May-19-2026	May-19-2026
ENG-B&GCC-1020	Bonding & Grounding Cable Owner Review and Acceptance by Owner	20	0	May-20-2026 A	Jul-10-2026 A		May-20-2026	Jul-10-2026
DAS Monitoring System Upgrade Design		200	1	Feb-06-2026 A	Jul-31-2026	30	Feb-06-2026	
ENG-DAS-1000	DAS Monitoring System Design Preparation/Submittal	30	0	Feb-06-2026 A	Mar-13-2026 A		Feb-06-2026	Mar-13-2026
ENG-DAS-1010	DAS Monitoring System Design Owner 1st Review	10	0	Mar-16-2026 A	Apr-01-2026 A		Mar-16-2026	Apr-01-2026
ENG-DAS-1010.01	DAS Monitoring System Design Contractor 1st Review	5	0	Apr-02-2026 A	Apr-15-2026 A		Apr-02-2026	Apr-15-2026
ENG-DAS-1010.11	DAS Monitoring System Design Owner 2nd Review	5	0	Apr-16-2026 A	Apr-20-2026 A		Apr-16-2026	Apr-20-2026
ENG-DAS-1010.21	DAS Monitoring System Design Contractor 2nd Review	5	0	Apr-21-2026 A	Apr-22-2026 A		Apr-21-2026	Apr-22-2026
ENG-DAS-1010.31	DAS Monitoring System Design Owner 3rd Review	5	0	Apr-23-2026 A	Apr-30-2026 A		Apr-23-2026	Apr-30-2026
ENG-DAS-1010.41	DAS Monitoring System Design Contractor 3rd Review	5	0	May-01-2026 A	May-01-2026 A		May-01-2026	May-01-2026
ENG-DAS-1010.51	DAS Monitoring System Design Owner 4th Review	5	0	May-04-2026 A	Jul-07-2026 A		May-04-2026	Jul-07-2026

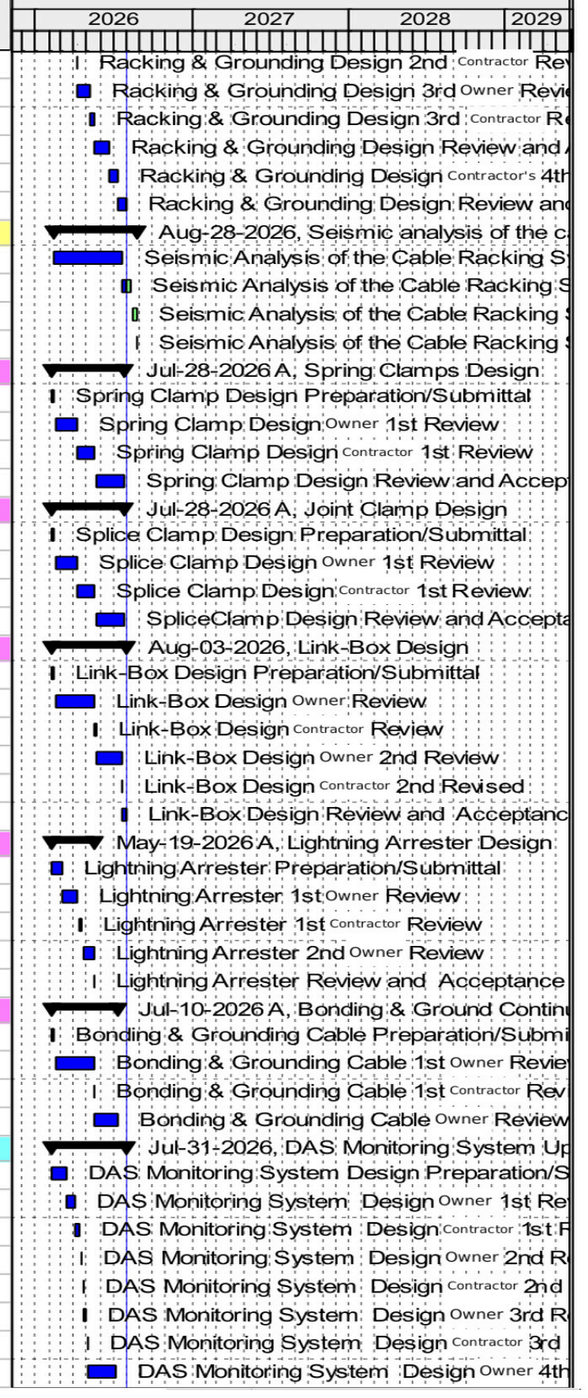


Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Sample 230kV Underground Cable Project Schedule

HSE Contractors | Public Portfolio Example

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish
ENG-DAS-1010.61	DAS Monitoring System Design Contractor 4th Revised	5	0	Jul-08-2026 A	Jul-29-2026 A		Jul-08-2026	Jul-29-2026
ENG-DAS-1020	DAS Monitoring System Design Review and Acceptance by Owner	5	1	Jul-30-2026 A	Jul-31-2026	29	Jul-30-2026	
QC Plan for Consturction		175	51	Feb-06-2026 A	Oct-12-2026	51	Feb-06-2026	
QC Plan for Shipping & Handling		175	51	Feb-06-2026 A	Oct-12-2026	37	Feb-06-2026	
QC-S&H-1000	QA/QC Plan for Field Work (Shipping & Handling) Preparation/Submittal	90	10	Feb-06-2026 A	Aug-13-2026	37	Feb-06-2026	
QC-S&H-1010	QA/QC Plan for Field Work (Shipping & Handling) 1st Owner Review	10	10	Aug-14-2026	Aug-27-2026	37		
QC-S&H-1020	QA/QC Plan for Field Work (Shipping & Handling) 1st Contractor Revised	10	10	Aug-28-2026	Sep-11-2026	37		
QC-S&H-1030	QA/QC Plan for Field Work (Shipping & Handling) 2nd Owner Review	10	10	Sep-14-2026	Sep-25-2026	37		
QC-S&H-1040	QA/QC Plan for Field Work (Shipping & Handling) 2nd Contractor Revised	10	10	Sep-28-2026	Oct-09-2026	37		
QC-S&H-1050	QA/QC Plan for Field Work (Shipping & Handling) Acceptance by Owner	1	1	Oct-12-2026	Oct-12-2026	37		
QC Plan for Racking & Grounding Installation		175	51	Feb-06-2026 A	Oct-12-2026	51	Feb-06-2026	
QC-R&G-1000	QA/QC Plan for Field Work (Racking & Grounding) Preparation/Submittal	90	10	Feb-06-2026 A	Aug-13-2026	51	Feb-06-2026	
QC-R&G-1010	QA/QC Plan for Field Work (Racking & Grounding) 1st Owner Review	10	10	Aug-14-2026	Aug-27-2026	51		
QC-R&G-1020	QA/QC Plan for Field Work (Racking & Grounding) 1st Contractor Revised	10	10	Aug-28-2026	Sep-11-2026	51		
QC-R&G-1030	QA/QC Plan for Field Work (Racking & Grounding) 2nd Owner Review	10	10	Sep-14-2026	Sep-25-2026	51		
QC-R&G-1040	QA/QC Plan for Field Work (Racking & Grounding) 2nd Contractor Revised	10	10	Sep-28-2026	Oct-09-2026	51		
QC-R&G-1050	QA/QC Plan for Field Work (Racking & Grounding) Acceptance by Owner	1	1	Oct-12-2026	Oct-12-2026	51		
QC Plan for Cable Installation		175	51	Feb-06-2026 A	Oct-12-2026	51	Feb-06-2026	
QC-CI-1000	QA/QC Plan for Field Work (Installation/Pulling) Preparation/Submittal	90	10	Feb-06-2026 A	Aug-13-2026	51	Feb-06-2026	
QC-CI-1010	QA/QC Plan for Field Work (Installation/Pulling) 1st Owner Review	10	10	Aug-14-2026	Aug-27-2026	51		
QC-CI-1020	QA/QC Plan for Field Work (Installation/Pulling) 1st Contractor Revised	10	10	Aug-28-2026	Sep-11-2026	51		
QC-CI-1030	QA/QC Plan for Field Work (Installation/Pulling) 2nd Owner Review	10	10	Sep-14-2026	Sep-25-2026	51		
QC-CI-1040	QA/QC Plan for Field Work (Installation/Pulling) 2nd Contractor Revised	10	10	Sep-28-2026	Oct-09-2026	51		
QC-CI-1050	QA/QC Plan for Field Work (Installation/Pulling) Acceptance by Owner	1	1	Oct-12-2026	Oct-12-2026	51		
QC Plan for Splicing & Termination		175	51	Feb-06-2026 A	Oct-12-2026	51	Feb-06-2026	
QC-S&T-1000	QA/QC Plan for Field Work (Splicing & Termination) Preparation/Submittal	90	10	Feb-06-2026 A	Aug-13-2026	51	Feb-06-2026	
QC-S&T-1010	QA/QC Plan for Field Work (Splicing & Termination) 1st Owner Review	10	10	Aug-14-2026	Aug-27-2026	51		
QC-S&T-1020	QA/QC Plan for Field Work (Splicing & Termination) 1st Contractor Revised	10	10	Aug-28-2026	Sep-11-2026	51		
QC-S&T-1030	QA/QC Plan for Field Work (Splicing & Termination) 2nd Owner Review	10	10	Sep-14-2026	Sep-25-2026	51		
QC-S&T-1040	QA/QC Plan for Field Work (Splicing & Termination) 2nd Contractor Revised	10	10	Sep-28-2026	Oct-09-2026	51		
QC-S&T-1050	QA/QC Plan for Field Work (Splicing & Termination) Acceptance by Owner	1	1	Oct-12-2026	Oct-12-2026	51		
QC Plan for DAS System Upgrade		175	51	Feb-06-2026 A	Oct-12-2026	51	Feb-06-2026	
QC-DAS-1000	QA/QC Plan for Field Work (DAS Upgrade) Preparation/Submittal	90	10	Feb-06-2026 A	Aug-13-2026	51	Feb-06-2026	
QC-DAS-1010	QA/QC Plan for Field Work (DAS Upgrade) 1st Owner Review	10	10	Aug-14-2026	Aug-27-2026	51		
QC-DAS-1020	QA/QC Plan for Field Work (DAS Upgrade) 1st Contractor Revised	10	10	Aug-28-2026	Sep-11-2026	51		
QC-DAS-1030	QA/QC Plan for Field Work (DAS Upgrade) 2nd Owner Review	10	10	Sep-14-2026	Sep-25-2026	51		
QC-DAS-1040	QA/QC Plan for Field Work (DAS Upgrade) 2nd Contractor Revised	10	10	Sep-28-2026	Oct-09-2026	51		
QC-DAS-1050	QA/QC Plan for Field Work (DAS Upgrade) Acceptance by Owner	1	1	Oct-12-2026	Oct-12-2026	51		
QC Plan for Commissioning Test		175	51	Feb-06-2026 A	Oct-12-2026	51	Feb-06-2026	
QC-C&T-1000	QA/QC Plan for Field Work (Commissioning Test) Preparation/Submittal	90	10	Feb-06-2026 A	Aug-13-2026	51	Feb-06-2026	
QC-C&T-1010	QA/QC Plan for Field Work (Commissioning Test) 1st Owner Review	10	10	Aug-14-2026	Aug-27-2026	51		
QC-C&T-1020	QA/QC Plan for Field Work (Commissioning Test) 1st Contractor Revised	10	10	Aug-28-2026	Sep-11-2026	51		
QC-C&T-1030	QA/QC Plan for Field Work (Commissioning Test) 2nd Owner Review	10	10	Sep-14-2026	Sep-25-2026	51		
QC-C&T-1040	QA/QC Plan for Field Work (Commissioning Test) 2nd Contractor Revised	10	10	Sep-28-2026	Oct-09-2026	51		
QC-C&T-1050	QA/QC Plan for Field Work (Commissioning Test) Acceptance by Owner	1	1	Oct-12-2026	Oct-12-2026	51		
Procurement Engineering		157	32	Feb-06-2026 A	Sep-14-2026	381	Feb-06-2026	
FAT Plan and Procedure for Factory Production		157	32	Feb-06-2026 A	Sep-14-2026	381	Feb-06-2026	
FAT Plan and Procedure for_230kV Power Cable		40	0	Feb-06-2026 A	Jun-23-2026 A		Feb-06-2026	Jun-23-2026

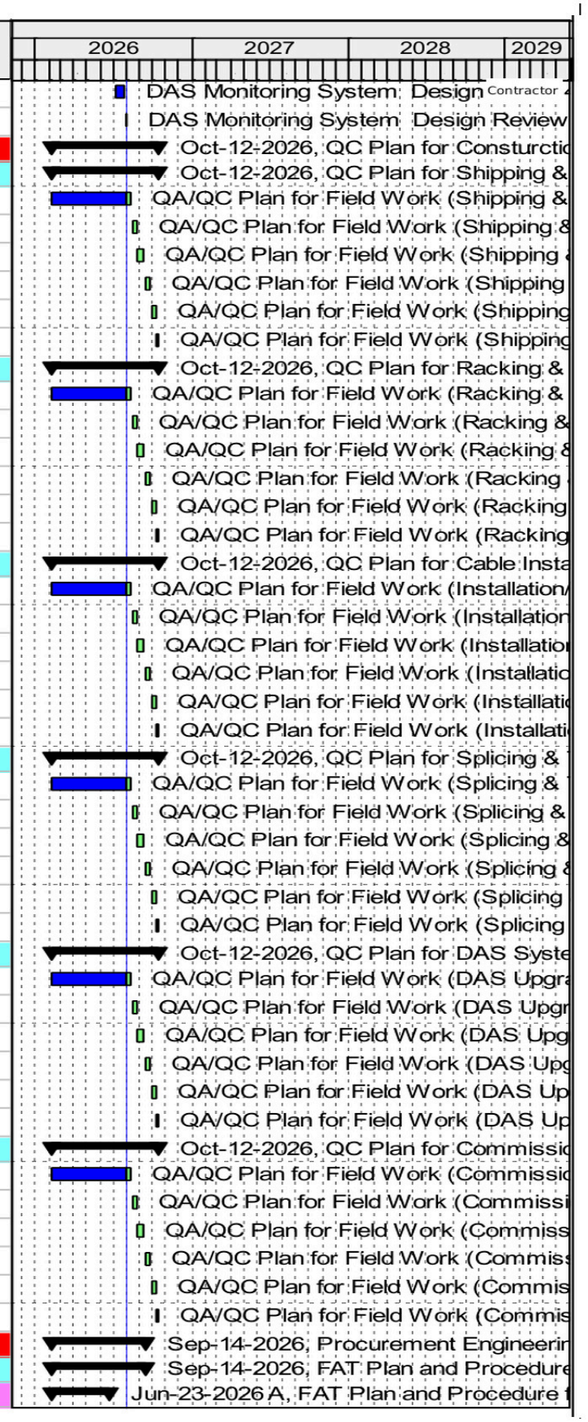


Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Sample 230kV Underground Cable Project Schedule

HSE Contractors | Public Portfolio Example


Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish
FAT-PC-1000	FAT Plan for Power Cable - Contractor Preperation / Submittion	30	0	Feb-06-2026 A	Mar-20-2026 A		Feb-06-2026	Mar-20-2026
FAT-PC-1010	FAT Plan for Power Cable - Owner Review / Approval	10	0	Mar-23-2026 A	Jun-23-2026 A		Mar-23-2026	Jun-23-2026
FAT Plan and Procedure for_Cable Splice		40	0	Feb-06-2026 A	Jul-28-2026 A		Feb-06-2026	Jul-28-2026
FAT-CS-1000	FAT Plan for Cable Splice - Contractor Preperation / Submittion	30	0	Feb-06-2026 A	Jun-11-2026 A		Feb-06-2026	Jun-11-2026
FAT-CS-1010	FAT Plan for Cable Splice - Owner Review / Approval	10	0	Jun-12-2026 A	Jul-28-2026 A		Jun-12-2026	Jul-28-2026
FAT Plan and Procedure for_Outdoor Termination		40	0	Feb-06-2026 A	Jul-28-2026 A		Feb-06-2026	Jul-28-2026
FAT-OT-1000	FAT Plan for Outdoor Termination - Contractor Preperation / Submittion	30	0	Feb-06-2026 A	Jun-11-2026 A		Feb-06-2026	Jun-11-2026
FAT-OT-1010	FAT Plan for Outdoor Termination - Owner Review / Approval	10	0	Jun-12-2026 A	Jul-28-2026 A		Jun-12-2026	Jul-28-2026
FAT Plan and Procedure for Cable Clamp		40	0	Feb-06-2026 A	Jul-28-2026 A		Feb-06-2026	Jul-28-2026
FAT-CC-1000	FAT Plan for Cable and Splice Clamps - Contractor Preperation / Submittion	30	0	Feb-06-2026 A	Mar-19-2026 A		Feb-06-2026	Mar-19-2026
FAT-CC-1010	FAT Plan for Cable and Splice Clamps - Owner Review / Approval	10	0	Mar-20-2026 A	Jul-28-2026 A		Mar-20-2026	Jul-28-2026
FAT Plan and Procedure for_Bonding & Grounding Continuity Cables		40	0	Feb-06-2026 A	Jul-28-2026 A		Feb-06-2026	Jul-28-2026
FAT-B&GCC-1000	FAT Plan for Bonding & Grounding Continuity - Contractor Preperation / Submittion	30	0	Feb-06-2026 A	Mar-19-2026 A		Feb-06-2026	Mar-19-2026
FAT-B&GCC-1010	FAT Plan for Bonding & Grounding Continuity - Owner Review / Approval	10	0	Mar-20-2026 A	Jul-28-2026 A		Mar-20-2026	Jul-28-2026
FAT Plan and Procedure for_Link-Box		40	0	Feb-06-2026 A	Jul-28-2026 A		Feb-06-2026	Jul-28-2026
FAT-LB-1000	FAT Plan for Link Box - Contractor Preperation / Submittion	30	0	Feb-06-2026 A	Mar-19-2026 A		Feb-06-2026	Mar-19-2026
FAT-LB-1010	FAT Plan for Link Box - Owner Review / Approval	10	0	Mar-20-2026 A	Jul-28-2026 A		Mar-20-2026	Jul-28-2026
FAT Plan and Procedure for_Surge Arrester		40	0	Feb-06-2026 A	May-18-2026 A		Feb-06-2026	May-18-2026
FAT-SA-1000	FAT Plan for Surge Arrestor - Contractor Preperation / Submittion	30	0	Feb-06-2026 A	Mar-12-2026 A		Feb-06-2026	Mar-12-2026
FAT-SA-1010	FAT Plan for Surge Arrestor - Owner Review / Approval	10	0	Mar-13-2026 A	May-18-2026 A		Mar-13-2026	May-18-2026
Procurement QAQC Plan for Racking & Grounding Materials		155	31	Feb-06-2026 A	Sep-14-2026	357	Feb-06-2026	
FAT-R&GM-1000	QA/QC Plan for Racking Materials Preparation/Submittal	90	10	Feb-06-2026 A	Aug-13-2026	357	Feb-06-2026	
FAT-R&GM-1010	QA/QC Plan for Racking Materials 1st Owner Review	10	10	Aug-14-2026	Aug-27-2026	357		
FAT-R&GM-1020	QA/QC Plan for Racking Materials 1st Contractor Revised	10	10	Aug-28-2026	Sep-11-2026	357		
FAT-R&GM-1030	QA/QC Plan for Racking Materials Acceptance by Owner	1	1	Sep-14-2026	Sep-14-2026	357		
Field Test QAQC Plan		203	54	Feb-06-2026 A	Oct-02-2026	68	Feb-06-2026	
QC-FT-1000	Field Test QA/QC Preparation/Submittal	90	13	Feb-06-2026 A	Aug-14-2026	68	Feb-06-2026	
QC-FT-1010	Field Test QA/QC 1st Owner Review	10	10	Aug-15-2026	Aug-26-2026	68		
QC-FT-1020	Field Test QA/QC 1st Contractor Revised	10	10	Aug-27-2026	Sep-08-2026	68		
QC-FT-1030	Field Test QA/QC 2nd Owner Review	10	10	Sep-09-2026	Sep-19-2026	68		
QC-FT-1040	Field Test QA/QC 2nd Contractor Revised	10	10	Sep-21-2026	Oct-01-2026	68		
QC-FT-1050	Field Test QA/QC Acceptance by Owner	1	1	Oct-02-2026	Oct-02-2026	68		
Permits		110	110	Jul-31-2026	Dec-12-2026	16		
Transportation Permits (Agency)		13	13	Nov-23-2026	Dec-12-2026	16		
PERMIT-T-1000	Transportation Permits Preparation	10	10	Nov-23-2026	Dec-09-2026	16		
PERMIT-T-1010	Transportation Permits Review and Approval	3	3	Dec-10-2026	Dec-12-2026	16		
Occupancy Permit		50	50	Jul-31-2026	Sep-28-2026	72		
PERMIT-OP-1000	Obtain Traffic Control Plan	30	30	Jul-31-2026	Sep-03-2026	72		
PERMIT-OP-1010	Occupancy Permits Preperation & Submittion	10	10	Sep-04-2026	Sep-16-2026	72		
PERMIT-OP-1020	Occupancy Permits Review and Approval	10	10	Sep-17-2026	Sep-28-2026	72		
Dust Permit		35	35	Oct-13-2026	Nov-21-2026	25		
PERMIT-DP-1000	Dust Permits Preparation	25	25	Oct-13-2026	Nov-10-2026	25		
PERMIT-DP-1010	Dust Permits Review and Approval	10	10	Nov-11-2026	Nov-21-2026	25		
Procurement		266	222	Feb-05-2026 A	Jun-07-2027	188	Feb-05-2026	
Material Manufacturing		211	200	Jun-01-2026 A	May-06-2027	146	Jun-01-2026	
Manufacturing of 230kV Power Cables		205	161	Jun-01-2026 A	Mar-12-2027	53	Jun-01-2026	
MM-PC-1000	Manufacturing of 1st Batch Power Cable	152	51	Jun-01-2026 A	Sep-19-2026	75	Jun-01-2026	
MM-PC-1010	Manufacturing of 2nd Batch Power Cable	79	79	Sep-01-2026	Dec-18-2026	27		
MM-PC-1020	Manufacturing of 3rd Batch Power Cable	80	80	Nov-23-2026	Mar-12-2027	53		

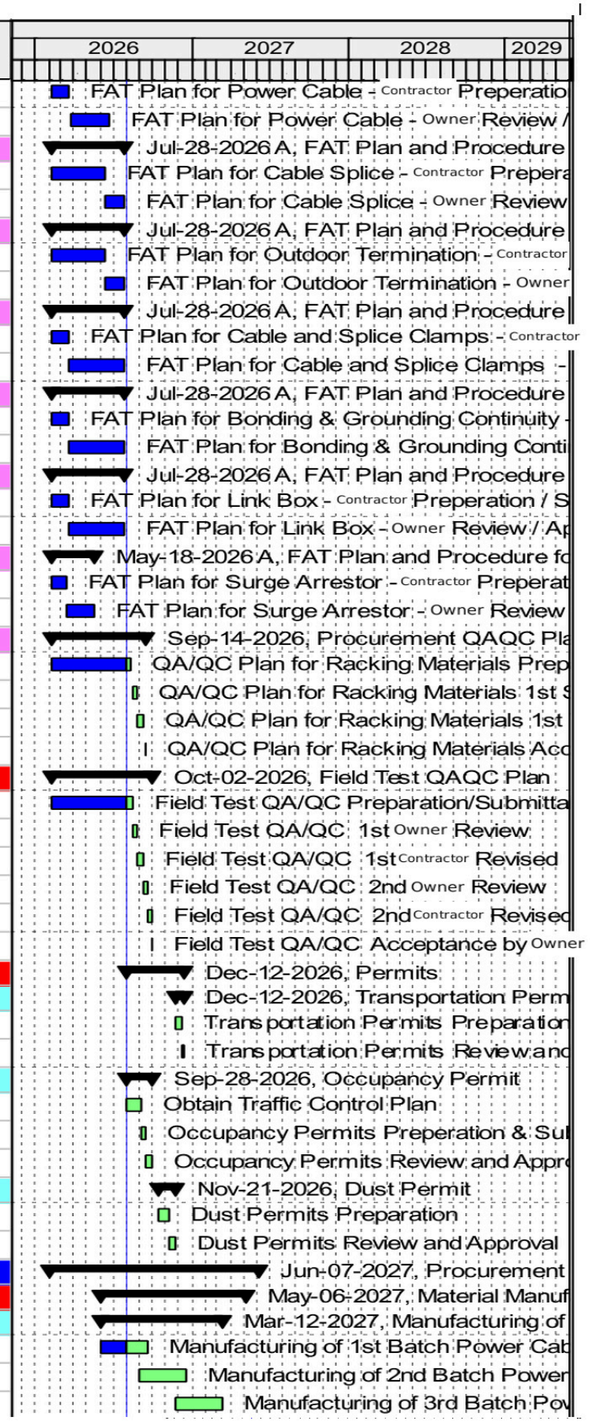

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Sample 230kV Underground Cable Project Schedule

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish
Manufacturing of 40ft Power cable and One outer Termination		66	11	Jun-01-2026 A	Aug-14-2026	294	Jun-01-2026	
MM-RM-1010	Manufacturing of 40 ft Power Cable for seismic test	49	0	Jun-01-2026 A	Jul-31-2026 A		Jun-01-2026	Jul-31-2026
MM-RM-1020	Manufacturing of one Outer Termination	22	11	Jul-06-2026 A	Aug-14-2026	294	Jul-06-2026	
Manufacturing of 230kV Cable Splices		91	91	Aug-08-2026	Nov-06-2026	83		
MM-CS-1000	Manufacturing of Cable Splices	91	91	Aug-08-2026	Nov-06-2026	83		
Manufacturing of 230kV Outdoor Terminations		162	162	Aug-07-2026	Jan-15-2027	263		
MM-OT-1000	Manufacturing of Outdoor Termination - 1st Batch	92	92	Aug-07-2026	Nov-06-2026	263		
MM-OT-1001	Manufacturing of Outdoor Termination - 2nd Batch	62	62	Nov-15-2026	Jan-15-2027	263		
Manufacturing of Other Accessories		280	280	Jun-16-2026 A	May-06-2027	199	Jun-16-2026	
MM-SA-2000	Manufacturing of Surge Arresters	280	280	Jun-16-2026 A	May-06-2027	199	Jun-16-2026	
MM-RM-1000	Manufacturing of Racking Materials	122	122	Aug-01-2026	Nov-30-2026	33		
MM-SC-1000	Manufacturing of Spring Clamps	88	88	Aug-10-2026*	Nov-05-2026	33		
MM-SC-2000	Manufacturing of Splice Clamps	89	89	Aug-10-2026*	Nov-06-2026	32		
MM-LB-2000	Manufacturing of Link-Box	89	89	Aug-10-2026*	Nov-06-2026	84		
MM-B&GC-2000	Manufacturing of Bonding & Grounding Cable	10	10	Sep-01-2026*	Sep-10-2026	84		
Manufacturing of DAS Monitoring System (FO Cables, Coaxial Cables, HFCT & LFCT Sensors)		121	121	Aug-01-2026	Nov-29-2026	362		
MM-DAS-2000	Preperation for Manufacturing	10	10	Aug-01-2026	Aug-10-2026	397		
MM-DAS-2010	Manufacturing DAS Monitoring System	76	76	Sep-15-2026	Nov-29-2026	362		
Factory Audit Test for Factory Production		122	122	Sep-29-2026	Mar-17-2027	147		
FAT_230kV Power Cables		122	122	Sep-29-2026	Mar-17-2027	52		
FAT-EXEC-PC-2000	Notification of FAT for Power Cable	0	0	Sep-29-2026*	Sep-29-2026	52		
FAT-EXEC-PC-2010	FAT for 1st Batch Power Cable (require Owner witness)	4	4	Nov-10-2026*	Nov-13-2026	16		
FAT-EXEC-PC-2020	FAT for 2nd Batch Power Cable (require Owner witness)	3	3	Jan-19-2027*	Jan-21-2027	6		
FAT-EXEC-PC-2030	FAT for 3rd Batch Power Cable (require Owner witness)	2	2	Mar-16-2027*	Mar-17-2027	52		
FAT_230kV Cable Splices		42	42	Sep-29-2026	Nov-16-2026	56		
FAT-EXEC-CS-2000	Notification of FAT for Cable Splices	1	1	Sep-29-2026*	Sep-29-2026	93		
FAT-EXEC-CS-2010	FAT for splices (require Owner witness)	4	4	Nov-12-2026*	Nov-16-2026	56		
FAT_230kV Outdoor Terminations		52	52	Nov-05-2026	Jan-21-2027	221		
FAT-EXEC-OT-2000	Notification of FAT for Outdoor Termination	1	1	Nov-05-2026	Nov-05-2026	265		
FAT-EXEC-OT-2010	FAT for Outdoor Terminations (require Owner witness) -1st Batch	4	4	Nov-10-2026*	Nov-13-2026	262		
FAT-EXEC-OT-2011	FAT for Outdoor Terminations (require Owner witness) - 2nd Batch	3	3	Jan-19-2027*	Jan-21-2027	221		
FAT_Other Accessories		4	4	Nov-10-2026	Nov-13-2026	52		
FAT-EXEC-LB-2000	FAT for Link-Box+SVLs	1	1	Nov-10-2026*	Nov-10-2026	55		
FAT-EXEC-SC-2000	FAT for Spring Clamp	4	4	Nov-10-2026*	Nov-13-2026	20		
FAT-EXEC-SC-3000	FAT for Splice Clamp	4	4	Nov-10-2026*	Nov-13-2026	20		
FAT-EXEC-B&GC-2000	FAT for Bonding & Grounding Cable	4	4	Nov-10-2026*	Nov-13-2026	16		
Engineering Testing		135	92	Feb-05-2026 A	Dec-14-2026	293	Feb-05-2026	
Type Test		103	62	Feb-05-2026 A	Dec-14-2026	293	Feb-05-2026	
ET-TT-1000	Cable System Type Testing Plan Preperation & Submittion	10	0	Feb-05-2026 A	Mar-20-2026 A		Feb-05-2026	Mar-20-2026
ET-TT-1010	Cable System Type Testing Plan Owner's Review	10	0	Mar-21-2026 A	Apr-29-2026 A		Mar-21-2026	Apr-29-2026
ET-TT-1020	Cable System Type Testing Plan Contractor Reivision	10	0	Apr-30-2026 A	May-08-2026 A		Apr-30-2026	May-08-2026
ET-TT-1030	Cable System Type Testing Plan Owner's Acceptance	10	0	May-09-2026 A	May-18-2026 A		May-09-2026	May-18-2026
ET-TT-1040	Cable System Type Testing	42	42	Sep-14-2026*	Nov-10-2026	0		
ET-TT-1050	Cable System Type Testing Final Report Submittion	10	10	Nov-11-2026	Nov-24-2026	293		
ET-TT-1060	Cable System Type Testing Final Report Owner's Review and Acceptance	10	10	Dec-01-2026	Dec-14-2026	293		
Seismic test on the dry type termination		101	58	Feb-05-2026 A	Oct-21-2026	272	Feb-05-2026	
ET-ST-1000	Sesmic Test on the Dry Type Termination Plan Preperation and Submission	35	0	Feb-05-2026 A	Jul-09-2026 A		Feb-05-2026	Jul-09-2026
ET-ST-1010	Sesmic Test on the Dry Type Termination Plan Owner's Review	10	2	Jul-10-2026 A	Aug-03-2026	278	Jul-10-2026	

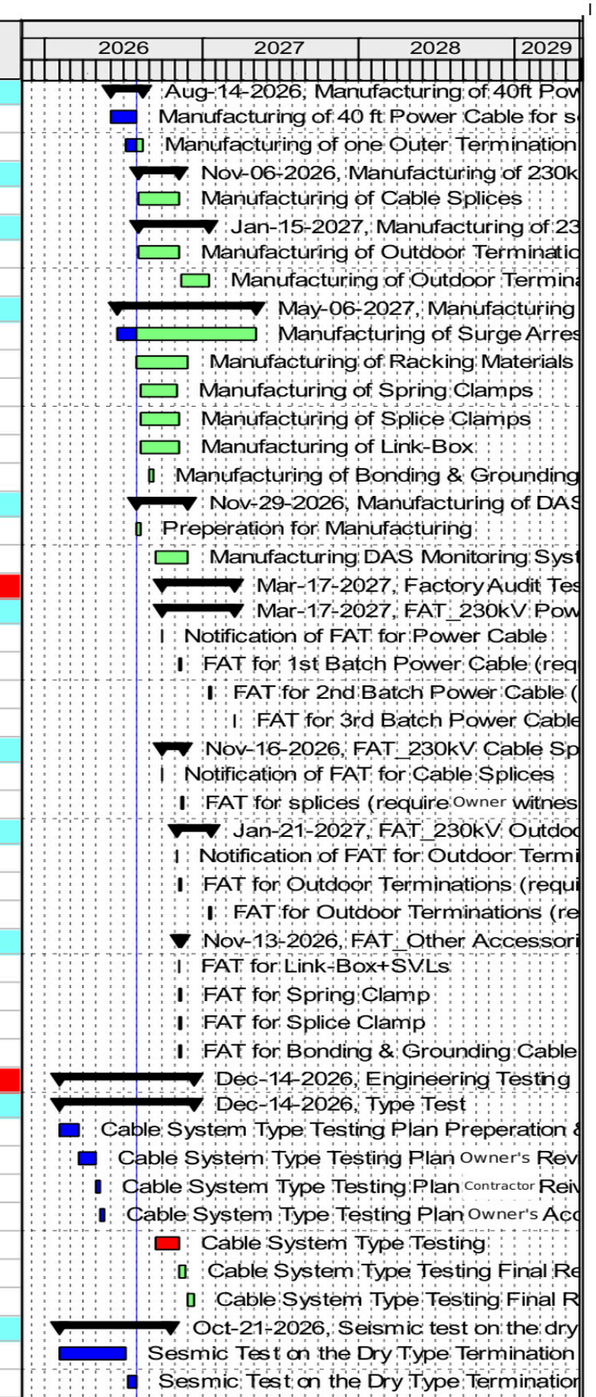


Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Sample 230kV Underground Cable Project Schedule

HSE Contractors | Public Portfolio Example


Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish
ET-ST-1020	Sesmic Test on the Dry Type Termination Plan Contractor Reivision	10	10	Aug-04-2026	Aug-17-2026	278		
ET-ST-1030	Sesmic Testing on the Dry Type Termination Plan Owner's Acceptance	10	10	Aug-18-2026	Aug-31-2026	278		
ET-ST-1040	Sesmic Testing on the Dry Type Termination	10	10	Sep-10-2026*	Sep-23-2026	272		
ET-ST-1050	Sesmic Test on the Dry Type Termination Final Report Preperation and Submission	10	10	Sep-24-2026	Oct-07-2026	272		
ET-ST-1060	Sesmic Test on the Dry Type Termination Final Report Owner's Review and Acceptance	10	10	Oct-08-2026	Oct-21-2026	272		
Shipping & Delivery of the Materials		211	211	Aug-17-2026	Jun-07-2027	159		
Shipping & Delivery of 40ft Power cable and One outer Termination		10	10	Aug-17-2026	Aug-28-2026	294		
S-PC-40-1000	Preperation for Shipping & Delivery from Overseas (40ft Power Cable and 1 One Outer Terminati	5	5	Aug-17-2026	Aug-21-2026	294		
S-PC-40-1020	Land Transport from Regional Port to Laydown Yard (40ft Power Cable and 1 One Outer	5	5	Aug-24-2026	Aug-28-2026	294		
Shipping & Delivery of 230kV Power Cables		113	113	Nov-14-2026	Apr-21-2027	55		
S-PC-1000	Preperation for Shipping & Delivery from Overseas (Power Cable) - 1st Batch	8	8	Nov-14-2026	Nov-21-2026	25		
S-PC-1010	Ocean Shipping of Power Cable to Regional Port (Power Cable) - 1st Batch	21	21	Nov-22-2026	Dec-12-2026	25		
S-PC-1020	Land Transport from Regional Port to Laydown Yard (Power Cable) - 1st Batch	3	3	Dec-14-2026	Dec-16-2026	14		
S-PC-2000	Preperation for Shipping & Delivery from Overseas (Power Cable) - 2nd Batch	11	11	Jan-22-2027	Feb-01-2027	10		
S-PC-2010	Ocean Shipping of Power Cable to Regional Port (Power Cable) - 2nd Batch	21	21	Feb-02-2027	Feb-22-2027	10		
S-PC-2020	Land Transport from Regional Port to Laydown Yard (Power Cable) - 2nd Batch	8	8	Feb-23-2027	Mar-04-2027	8		
S-PC-3000	Preperation for Shipping & Delivery from Overseas (Power Cable) - 3rd Batch	4	4	Mar-18-2027	Mar-21-2027	74		
S-PC-3010	Ocean Shipping of Power Cable to Regional Port (Power Cable) - 3rd Batch	21	21	Mar-22-2027	Apr-11-2027	74		
S-PC-3020	Land Transport from Regional Port to Laydown Yard (Power Cable) - 3rd Batch	8	8	Apr-12-2027	Apr-21-2027	54		
Shipping & Delivery of 230kV Cable Splices		27	27	Nov-17-2026	Dec-23-2026	59		
S-CS-1000	Preperation for Shipping & Delivery from Overseas (Splice)	9	9	Nov-17-2026	Nov-25-2026	83		
S-CS-1010	Ocean Shipping of Power Cable to Regional Port (Splice)	21	21	Nov-26-2026	Dec-16-2026	83		
S-CS-1020	Land Transport from Regional Port to Laydown Yard (Splice)	5	5	Dec-17-2026	Dec-23-2026	51		
Shipping & Delivery of 230kV Outdoor Terminations		78	78	Nov-14-2026	Mar-03-2027	185		
S-OT-1000	Preperation for Shipping & Delivery from Overseas (Termination) - 1st Batch	9	9	Nov-14-2026	Nov-22-2026	326		
S-OT-1010	Ocean Shipping of Power Cable to Regional Port (Termination) - 1st Batch	21	21	Nov-23-2026	Dec-13-2026	326		
S-OT-1020	Land Transport from Regional Port to Laydown Yard (Outdoor terminations) - 1st Batch	5	5	Dec-14-2026	Dec-18-2026	224		
S-OT-1030	Preperation for Shipping & Delivery from Overseas (Termination) - 2nd Batch	9	9	Jan-22-2027	Jan-30-2027	260		
S-OT-1040	Ocean Shipping of Power Cable to Regional Port (Termination) - 2nd Batch	21	21	Jan-31-2027	Feb-20-2027	260		
S-OT-1050	Land Transport from Regional Port to Laydown Yard (Outdoor terminations) - 2nd Batch	8	8	Feb-22-2027	Mar-03-2027	183		
Shipping & Delivery of 230kV Surge Arrestors		22	22	May-07-2027	Jun-07-2027	143		
S-SA-1000	Preperation for Shipping & Delivery from Overseas (Arrester)	5	5	May-07-2027	May-11-2027	199		
S-SA-1010	Ocean Shipping of Power Cable to Regional Port (Arrester)	20	20	May-12-2027	May-31-2027	199		
S-SA-1020	Land Transport from Regional Port to Laydown Yard (Arrester)	5	5	Jun-01-2027	Jun-07-2027	138		
Shipping & Delivery of Cable Clamps		22	22	Nov-14-2026	Dec-15-2026	22		
S-CC-1000	Preperation for Shipping & Delivery from Overseas (Clamp)	4	4	Nov-14-2026	Nov-17-2026	30		
S-CC-1010	Ocean Shipping of Power Cable to Regional Port (Clamp)	21	21	Nov-18-2026	Dec-08-2026	30		
S-CC-1020	Land Transport from Regional Port to Laydown Yard (Clamp)	5	5	Dec-09-2026	Dec-15-2026	14		
Shipping & Delivery of Racking & Grounding Materials		11	11	Dec-01-2026	Dec-15-2026	23		
S-R&GM-1000	Preperation for Shipping & Delivery (Racking & Grounding Materials)	8	8	Dec-01-2026	Dec-08-2026	33		
S-R&GM-1010	Delivery to Laydown Yard (Racking & Grounding Materials)	5	5	Dec-09-2026	Dec-15-2026	15		
Shipping & Delivery of Bonding & Grounding Continuity Cables		25	25	Nov-14-2026	Dec-18-2026	19		
S-B&GCC-1000	Preperation for Shipping & Delivery from Overseas (Bonding ang Grounding Cable)	9	9	Nov-14-2026	Nov-22-2026	25		
S-B&GCC-1010	Ocean Shipping of Power Cable to Regional Port (Bonding ang Grounding Cable)	21	21	Nov-23-2026	Dec-13-2026	25		
S-B&GCC-1020	Land Transport from Regional Port to Laydown Yard (Bonding ang Grounding Cable)	5	5	Dec-14-2026	Dec-18-2026	11		
Shipping & Delivery of Link-Box		23	23	Nov-11-2026	Dec-11-2026	59		
S-LB-1000	Preperation for Shipping & Delivery from Overseas (Link-Box)	14	14	Nov-11-2026	Nov-24-2026	82		
S-LB-1010	Ocean Shipping of Power Cable to Regional Port (Link-Box)	11	11	Nov-25-2026	Dec-05-2026	82		

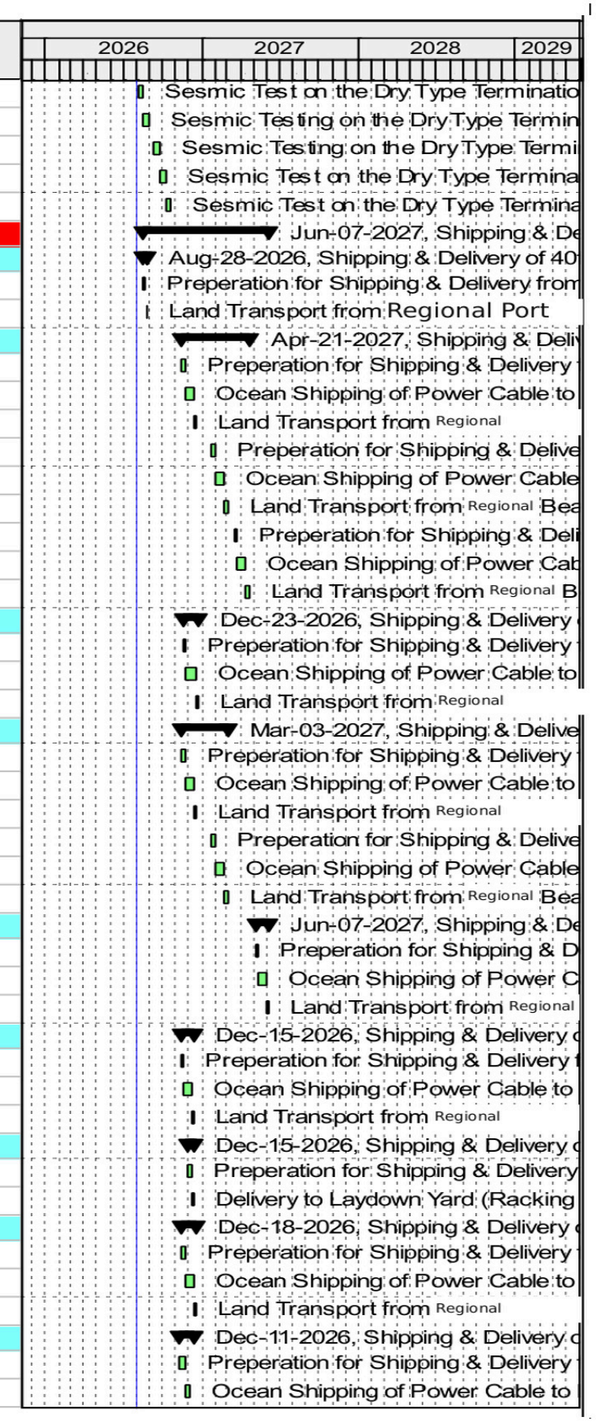

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Sample 230kV Underground Cable Project Schedule


Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish
S-LB-1020	Land Transport from Regional Port to Laydown Yard (Link-Box)	5	5	Dec-07-2026	Dec-11-2026	51		
Shipping & Delivery of DAS Monitoring System (FO Cables, Coaxial Cables, HFCT & LFCT Sensors)		36	36	Nov-30-2026	Jan-18-2027	259		
S-DAS-1000	Preperation for Shipping & Delivery (DAS Monitoring)	5	5	Nov-30-2026	Dec-04-2026	362		
S-DAS-1020	Ocean Shipping of Power Cable to Regional Port (DAS)	20	20	Dec-07-2026	Jan-13-2027	245		
S-DAS-1010	Delivery to Laydown Yard (DAS Monitoring)	5	5	Jan-14-2027	Jan-18-2027	361		
Construction		413	413	Jul-31-2026	Feb-29-2028	0		
Mobilization & Site Set-up		5	5	Nov-23-2026	Dec-03-2026	25		
MOB-1010	Mobilization & Site Set up	5	5	Nov-23-2026	Dec-03-2026	25		
MOB-1000	Establishment of Laydown yard (Project Laydown Yard)	5	5	Nov-23-2026	Dec-03-2026	25		
Cable Test Receiving		97	97	Dec-17-2026	Apr-30-2027	55		
CTR-1000	Cable Receiving Inspection & Testing - SITE-A/SITE-B - 1st batch	12	12	Dec-17-2026	Jan-01-2027	22		
CTR-1010	Cable Receiving Inspection & Testing - SITE-A/SITE-B - 2nd batch	10	10	Mar-05-2027	Mar-18-2027	8		
CTR-1020	Cable Receiving Inspection & Testing - SITE-A/SITE-B - 3rd batch	7	7	Apr-22-2027	Apr-30-2027	55		
Cable Accessories Visual Inspections		127	127	Dec-14-2026	Jun-08-2027	158		
VI-1050	Linkboxes+SVLs Receiving Visual Inspection	18	18	Dec-14-2026	Jan-06-2027	59		
VI-1000	Racking & Grounding Materials Receiving Visual Inspection	1	1	Dec-16-2026	Dec-16-2026	57		
VI-1040	Cable Clamps (Spring Clamps, Joint Clamp, etc) Receiving Visual	1	1	Dec-16-2026	Dec-16-2026	14		
VI-1020	Outer terminations Receiving Visual Inspection - 1st Batch	13	13	Dec-21-2026	Jan-06-2027	234		
VI-1030	Bonding & Grounding Cables Receiving Visual Inspection	1	1	Dec-21-2026	Dec-21-2026	11		
VI-1010	Splices Receiving Visual Inspection	10	10	Dec-24-2026	Jan-06-2027	59		
VI-1060	DAS Instrument Receiving Visual Inspection	0	0	Jan-19-2027	Jan-19-2027	259		
VI-1021	Outer terminations Receiving Visual Inspection -2nd Batch	8	8	Mar-04-2027	Mar-15-2027	185		
VI-1031	Surge Arresters Receiving Visual Inspection	1	1	Jun-08-2027	Jun-08-2027	150		
SITE-A Circuit		271	271	Dec-22-2026	Jan-04-2028	40		
Outdoor Termination Installation For SITE-A		50	50	Dec-22-2026	Mar-01-2027	221		
Pre-Racking & Grounding Installation		21	21	Dec-22-2026	Jan-19-2027	10		
PRE-R&G-INS-1000	MH12 - SC1-1 & SC1-2 & SC2-1 & SC2-2 (2 MHs) - Site Area - PRE-RACKING - SITE-A	2	2	Dec-22-2026	Dec-23-2026	13		
PRE-R&G-INS-1020	MH1 - SC1-1 & SC1-2 & SC2-1 & SC2-2 (2 MHs) - PRE-RACKING - SITE-A	2	2	Jan-14-2027	Jan-15-2027	13		
PRE-R&G-INS-1030	MH2 - SC1-1 & SC1-2 & SC2-1 & SC2-2 (2 MHs) - PRE-RACKING - SITE-A	2	2	Jan-18-2027	Jan-19-2027	10		
Cable Laying for 230kV cable, FO cable, LV cable including Conduit Proving		21	21	Jan-05-2027	Jan-28-2027	12		
CL-1000	MH12 - South Riser Poles (6 drums) - Site Area - CABLE-LAYING - SITE-A	8	8	Jan-05-2027	Jan-13-2027	13		
CL-1020	MH2 - North Riser Poles (6 drums) - outage - CABLE-LAYING - SITE-A	8	8	Jan-20-2027	Jan-28-2027	12		
Scaffolding Installation		47	47	Jan-14-2027	Mar-01-2027	309		
SCAFF-1040	Scaffolding Installation for South Riser Poles	15	15	Jan-14-2027	Jan-28-2027	306		
SCAFF-1050	Scaffolding Installation for North Riser Poles	15	15	Jan-29-2027	Feb-12-2027	303		
SCAFF-1060	Scaffolding Dismantle for South Riser Poles	5	5	Feb-10-2027	Feb-14-2027	324		
SCAFF-1070	Scaffolding Dismantle for North Riser Poles	5	5	Feb-25-2027	Mar-01-2027	309		
Termination Installation		23	23	Jan-29-2027	Feb-24-2027	253		
TERM-INS-1000	Termination at South Riser Pole (6 Termination) - 2 Crews - Site Area - SITE-A CIRCUIT	10	10	Jan-29-2027	Feb-09-2027	256		
TERM-INS-1020	Termination at North Riser Pole (6 Termination) - 2 Crews - outage -SITE-A CIRCUIT	10	10	Feb-13-2027	Feb-24-2027	253		
FO cable & LV cabe termination at Acqusition box		23	23	Jan-29-2027	Feb-24-2027	253		
FO-1000	South Riser Pole - SITE-A Circuits	10	10	Jan-29-2027	Feb-09-2027	256		
FO-1010	North Riser Pole - SITE-A Circuits	10	10	Feb-13-2027	Feb-24-2027	253		
Racking		18	18	Feb-18-2027	Mar-10-2027	71		
RACK-SITE-A-1010	MH3-SC1 & SC2 (2 MHs) - RACKING - SITE-A	2	2	Feb-18-2027	Feb-19-2027	15		
RACK-SITE-A-1020	MH4-SC1 & SC2 (2 MHs) - RACKING - SITE-A	2	2	Feb-20-2027	Feb-22-2027	22		
RACK-SITE-A-1030	MH5-SC1 & SC2 (2 MHs) - RACKING - SITE-A	2	2	Feb-23-2027	Feb-24-2027	29		
RACK-SITE-A-1040	MH6-SC1 & SC2 (2 MHs) - RACKING - SITE-A	2	2	Feb-25-2027	Feb-26-2027	36		

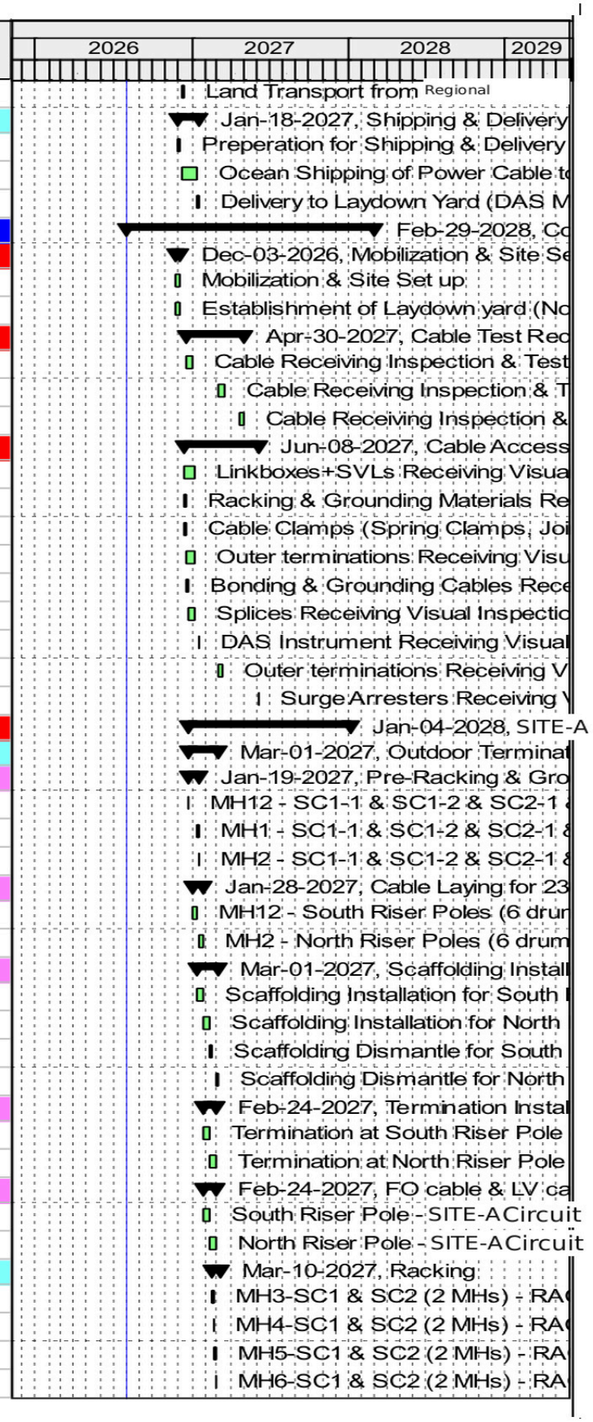

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Sample 230kV Underground Cable Project Schedule

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish
RACK-SITE-A-1050	MH7-SC1 & SC2 (2 MHs) - RACKING - SITE-A	2	2	Feb-27-2027	Mar-01-2027	43		
RACK-SITE-A-1060	MH8-SC1 & SC2 (2 MHs) - RACKING - SITE-A	2	2	Mar-02-2027	Mar-03-2027	50		
RACK-SITE-A-1070	MH9-SC1 & SC2 (2 MHs) - RACKING - SITE-A	2	2	Mar-04-2027	Mar-05-2027	57		
RACK-SITE-A-1080	MH10-SC1 & SC2 (2 MHs) - RACKING - SITE-A	2	2	Mar-06-2027	Mar-08-2027	64		
RACK-SITE-A-1090	MH11-SC1 & SC2 (2 MHs) - RACKING - SITE-A	2	2	Mar-09-2027	Mar-10-2027	71		
Cable Laying for 230kV cable, FO cable, LV cable including Conduit Proving		95	95	Feb-20-2027	Jun-10-2027	10		
CLAY-SITE-A-1010	MH2-SC1 & SC2 to MH3-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-A	9	9	Feb-20-2027	Mar-02-2027	15		
CLAY-SITE-A-1020	MH3-SC1 & SC2 to MH4-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-A	9	9	Mar-03-2027	Mar-12-2027	15		
CLAY-SITE-A-1030	MH4-SC1 & SC2 to MH5-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-A	9	9	Mar-19-2027	Mar-29-2027	10		
CLAY-SITE-A-1040	MH5-SC1 & SC2 to MH6-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-A	9	9	Mar-30-2027	Apr-08-2027	10		
CLAY-SITE-A-1050	MH6-SC1 & SC2 to MH7-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-A	9	9	Apr-09-2027	Apr-19-2027	10		
CLAY-SITE-A-1060	MH7-SC1 & SC2 to MH8-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-A	9	9	Apr-20-2027	Apr-29-2027	10		
CLAY-SITE-A-1070	MH8-SC1 & SC2 to MH9-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-A	9	9	Apr-30-2027	May-10-2027	10		
CLAY-SITE-A-1080	MH9-SC1 & SC2 to MH10-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-A	9	9	May-11-2027	May-20-2027	10		
CLAY-SITE-A-1090	MH10-SC1 & SC2 to MH11-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-A	9	9	May-21-2027	May-31-2027	10		
CLAY-SITE-A-1100	MH11-SC1 & SC2 to MH12-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-A	9	9	Jun-01-2027	Jun-10-2027	10		
Splicing & Termination work		204	204	Mar-17-2027	Dec-27-2027	5		
Splicing for 230kV cable		204	204	Mar-17-2027	Dec-27-2027	5		
SPLICE-SITE-A-1020	MH3-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-A	9	9	Mar-17-2027	Mar-26-2027	12		
SPLICE-SITE-A-1030	MH4-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-A	9	9	Mar-30-2027	Apr-08-2027	10		
SPLICE-SITE-A-1040	MH5-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-A	9	9	Apr-09-2027	Apr-19-2027	10		
SPLICE-SITE-A-1050	MH6-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-A	9	9	Apr-20-2027	Apr-29-2027	10		
SPLICE-SITE-A-1060	MH7-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-A	9	9	Apr-30-2027	May-10-2027	10		
SPLICE-SITE-A-1070	MH8-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-A	9	9	May-11-2027	May-20-2027	10		
SPLICE-SITE-A-1080	MH9-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-A	9	9	May-21-2027	May-31-2027	10		
SPLICE-SITE-A-1090	MH10-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-A	9	9	Jun-01-2027	Jun-10-2027	10		
SPLICE-SITE-A-1100	MH11-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-A	9	9	Jun-11-2027	Jun-21-2027	10		
SPLICE-SITE-A-1110	MH12-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-A	9	9	Jun-22-2027	Jul-01-2027	10		
SPLICE-SITE-A-1010	MH2-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-A	9	9	Dec-15-2027	Dec-27-2027	5		
FO cable & LV cabe termination at Acqusition box		5	5	Jun-11-2027	Jun-16-2027	168		
FO-SITE-A-1000	Circuit No. 2 MH#1, 2, 3, 4, 5, 6, 7, 8, 9, 10, 11, 12, 13 and both Riser pole - SITE-A	5	5	Jun-11-2027	Jun-16-2027	168		
Field Testing & Inspections		261	261	Jan-05-2027	Jan-04-2028	40		
Cable Test Before Cable Installation		106	106	Jan-05-2027	Jun-01-2027	195		
PRE-TEST-1110	Pretest Install MH12-SC1 & SC2 to South Riser Pole Termination (6 drums) - SITE-A	5	5	Jan-05-2027	Jan-11-2027	250		
PRE-TEST-1120	Pretest Install MH2-SC1 & SC2 to North Riser Pole Termination (6 drums) - SITE-A	5	5	Jan-20-2027	Jan-26-2027	239		
PRE-TEST-1010	Pretest Install MH2-SC1 & SC2 to MH3-SC1 & SC2 (6 drums) - SITE-A	1	1	Feb-20-2027	Feb-20-2027	296		
PRE-TEST-1020	Pretest Install MH3-SC1 & SC2 to MH4-SC1 & SC2 (6 drums) - SITE-A	1	1	Mar-03-2027	Mar-03-2027	288		
PRE-TEST-1030	Pretest Install MH4-SC1 & SC2 to MH5-SC1 & SC2 (6 drums) - SITE-A	1	1	Mar-19-2027	Mar-19-2027	275		
PRE-TEST-1040	Pretest Install MH5-SC1 & SC2 to MH6-SC1 & SC2 (6 drums) - SITE-A	1	1	Mar-30-2027	Mar-30-2027	267		
PRE-TEST-1050	Pretest Install MH6-SC1 & SC2 to MH7-SC1 & SC2 (6 drums) - SITE-A	1	1	Apr-09-2027	Apr-09-2027	259		
PRE-TEST-1060	Pretest Install MH7-SC1 & SC2 to MH8-SC1 & SC2 (6 drums) - SITE-A	1	1	Apr-20-2027	Apr-20-2027	251		
PRE-TEST-1070	Pretest Install MH8-SC1 & SC2 to MH9-SC1 & SC2 (6 drums) - SITE-A	1	1	Apr-30-2027	Apr-30-2027	243		
PRE-TEST-1080	Pretest Install MH9-SC1 & SC2 to MH10-SC1 & SC2 (6 drums) - SITE-A	1	1	May-11-2027	May-11-2027	235		
PRE-TEST-1090	Pretest Install MH10-SC1 & SC2 to MH11-SC1 & SC2 (6 drums) - SITE-A	1	1	May-21-2027	May-21-2027	227		
PRE-TEST-1100	Pretest Install MH11-SC1 & SC2 to MH12-SC1 & SC2 (6 drums) - SITE-A	1	1	Jun-01-2027	Jun-01-2027	219		
Cable Test After Cable Installation		109	109	Jan-12-2027	Jun-11-2027	147		
POST-TEST-1110	Post-test Install MH12-SC1 & SC2 to South Riser Pole Termination (6 Drums) - SITE-A	5	5	Jan-12-2027	Jan-18-2027	250		
POST-TEST-1120	Post-test Install MH2-SC1 & SC2 to North Riser Pole Termination (6 Drums) - SITE-A	5	5	Jan-27-2027	Feb-02-2027	239		

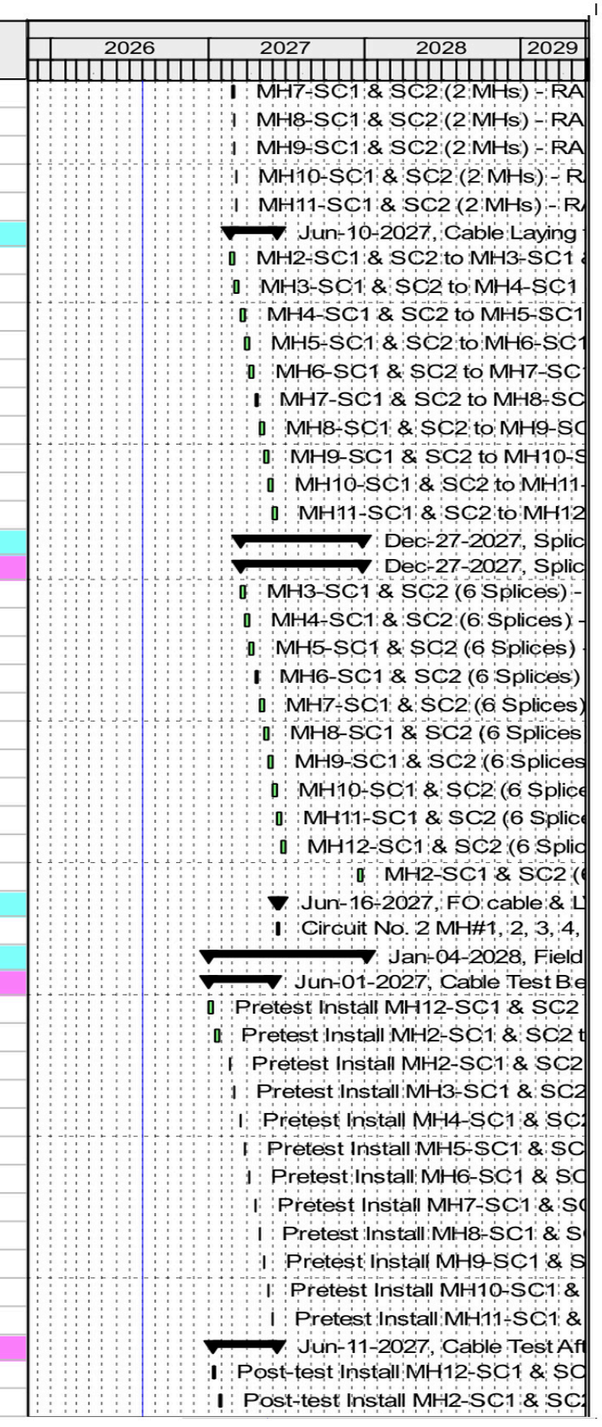


Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Sample 230kV Underground Cable Project Schedule

HSE Contractors | Public Portfolio Example


Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish
POST-TEST-1010	Post-test Install MH2-SC1 & SC2 to MH3-SC1 & SC2 (6 drums) - SITE-A	1	1	Mar-03-2027	Mar-03-2027	239		
POST-TEST-1020	Post-test Install MH3-SC1 & SC2 to MH4-SC1 & SC2 (6 drums) - SITE-A	1	1	Mar-13-2027	Mar-13-2027	231		
POST-TEST-1030	Post-test Install MH4-SC1 & SC2 to MH5-SC1 & SC2 (6 drums) - SITE-A	1	1	Mar-30-2027	Mar-30-2027	218		
POST-TEST-1040	Post-test Install MH5-SC1 & SC2 to MH6-SC1 & SC2 (6 drums) - SITE-A	1	1	Apr-09-2027	Apr-09-2027	210		
POST-TEST-1050	Post-test Install MH6-SC1 & SC2 to MH7-SC1 & SC2 (6 drums) - SITE-A	1	1	Apr-20-2027	Apr-20-2027	202		
POST-TEST-1060	Post-test Install MH7-SC1 & SC2 to MH8-SC1 & SC2 (6 drums) - SITE-A	1	1	Apr-30-2027	Apr-30-2027	194		
POST-TEST-1070	Post-test Install MH8-SC1 & SC2 to MH9-SC1 & SC2 (6 drums) - SITE-A	1	1	May-11-2027	May-11-2027	186		
POST-TEST-1080	Post-test Install MH9-SC1 & SC2 to MH10-SC1 & SC2 (6 drums) - SITE-A	1	1	May-21-2027	May-21-2027	178		
POST-TEST-1090	Post-test Install MH10-SC1 & SC2 to MH11-SC1 & SC2 (6 drums) - SITE-A	1	1	Jun-01-2027	Jun-01-2027	170		
POST-TEST-1100	Post-test Install MH11-SC1 & SC2 to MH12-SC1 & SC2 (6 drums) - SITE-A	1	1	Jun-11-2027	Jun-11-2027	162		
Final Racking & Grounding Inspections		267	267	Feb-10-2027	Jan-04-2028	0		
Splice Manhole		254	254	Feb-25-2027	Jan-04-2028	0		
FI-SPLICE-1000	Final Inspection for Racking & Grounding & Splicing - MH1-SC1 & SC2 (6 Splices) - SITE-A	1	1	Feb-25-2027	Feb-25-2027	253		
FI-SPLICE-1020	Final Inspection for Racking & Grounding & Splicing - MH3-SC1 & SC2 (6 Splices) - SITE-A	1	1	Mar-27-2027	Mar-27-2027	227		
FI-SPLICE-1030	Final Inspection for Racking & Grounding & Splicing - MH4-SC1 & SC2 (6 Splices) - SITE-A	1	1	Apr-09-2027	Apr-09-2027	216		
FI-SPLICE-1040	Final Inspection for Racking & Grounding & Splicing - MH5-SC1 & SC2 (6 Splices) - SITE-A	1	1	Apr-20-2027	Apr-20-2027	207		
FI-SPLICE-1050	Final Inspection for Racking & Grounding & Splicing - MH6-SC1 & SC2 (6 Splices) - SITE-A	1	1	Apr-30-2027	Apr-30-2027	198		
FI-SPLICE-1060	Final Inspection for Racking & Grounding & Splicing - MH7-SC1 & SC2 (6 Splices) - SITE-A	1	1	May-11-2027	May-11-2027	189		
FI-SPLICE-1070	Final Inspection for Racking & Grounding & Splicing - MH8-SC1 & SC2 (6 Splices) - SITE-A	1	1	May-21-2027	May-21-2027	180		
FI-SPLICE-1080	Final Inspection for Racking & Grounding & Splicing - MH9-SC1 & SC2 (6 Splices) - SITE-A	1	1	Jun-01-2027	Jun-01-2027	171		
FI-SPLICE-1090	Final Inspection for Racking & Grounding & Splicing - MH10-SC1 & SC2 (6 Splices) - SITE-A	1	1	Jun-11-2027	Jun-11-2027	162		
FI-SPLICE-1100	Final Inspection for Racking & Grounding & Splicing - MH11-SC1 & SC2 (6 Splices) - SITE-A	1	1	Jun-22-2027	Jun-22-2027	153		
FI-SPLICE-1110	Final Inspection for Racking & Grounding & Splicing - MH12-SC1 & SC2 (6 Splices) - SITE-A	1	1	Jul-02-2027	Jul-02-2027	144		
FI-SPLICE-1010	Final Inspection for Racking & Grounding & Splicing - MH2-SC1 & SC2 (6 Splices) - SITE-A	1	1	Jan-04-2028	Jan-04-2028	0		
Riser Poles		14	14	Feb-10-2027	Feb-25-2027	253		
FI-TS-1000	Final Inspection for Racking & Grounding - South Riser Poles (12 drums) - Site Area - SITE-A	1	1	Feb-10-2027	Feb-10-2027	266		
FI-TS-1010	Final Inspection for Racking & Grounding - North Riser Poles (12 drums) - outage - SITE-A	1	1	Feb-25-2027	Feb-25-2027	253		
SITE-B Circuit		359	359	Jul-31-2026	Dec-15-2027	54		
Outdoor Termination Installation For SITE-B		359	359	Jul-31-2026	Dec-15-2027	43		
Pre-Racking & Grounding Installation		191	191	Jan-29-2027	Oct-23-2027	9		
PRG-ML-1000	MH1 - SC1-1 & SC1-2 & SC2-1 & SC2-2 (2 MHs) - outage - PRE-RACKING - SITE-B	4	4	Jan-29-2027	Feb-02-2027	12		
PRG-ML-1010	MH2 - SC1-1 & SC1-2 & SC2-1 & SC2-2 (2 MHs) - outage - PRE-RACKING - SITE-B	4	4	Feb-03-2027	Feb-08-2027	10		
PRG-ML-1020	MH12 - SC1-1 & SC1-2 & SC2-1 & SC2-2 (2 MHs) - Site Area - PRE-RACKING - SITE-B	4	4	Oct-20-2027	Oct-23-2027	10		
Cable Laying for 230kV cable, FO cable, LV cable including Conduit Proving		227	227	Feb-09-2027	Nov-02-2027	10		
CL-ML-1000	MH2 - MH1 - North Riser Poles (6 drums) - outage - CABLE-LAYING - SITE-B	8	8	Feb-09-2027	Feb-17-2027	12		
CL-ML-1010	MH12 - South Riser Poles (6 drums) - Site Area - CABLE-LAYING - SITE-B	8	8	Oct-25-2027	Nov-02-2027	10		
Scaffolding Installation		294	294	Feb-18-2027	Dec-08-2027	68		
SCAF-ML-1000	Scaffolding Installation for North Riser Pole	15	15	Feb-18-2027	Mar-04-2027	14		
SCAF-ML-1010	Scaffolding Dismantle for North Riser Pole	5	5	Mar-17-2027	Mar-21-2027	330		
SCAF-ML-1020	Scaffolding Installation for South Riser Pole	15	15	Nov-03-2027	Nov-17-2027	12		
SCAF-ML-1030	Scaffolding Dismantle for South Riser Pole	5	5	Dec-04-2027	Dec-08-2027	68		
Outage Request		60	60	Jul-31-2026	Oct-23-2026	306		
OR-ML-1000	Outage Request Preparation & Submittal	30	30	Jul-31-2026	Sep-11-2026	306		
OR-ML-1010	Outage Request Owner Review	10	10	Sep-14-2026	Sep-25-2026	306		
OR-ML-1020	Outage Request Contractor Revised	10	10	Sep-28-2026	Oct-09-2026	306		
OR-ML-1030	Outage Request Owner Acceptance/Approval	10	10	Oct-12-2026	Oct-23-2026	306		
Termination Installation		229	229	Mar-05-2027	Dec-03-2027	6		
TI-ML-1000	Termination at North Riser Pole (6 Termination) - 2 Crews - outage - SITE-B CIRCUIT	10	10	Mar-05-2027	Mar-16-2027	12		

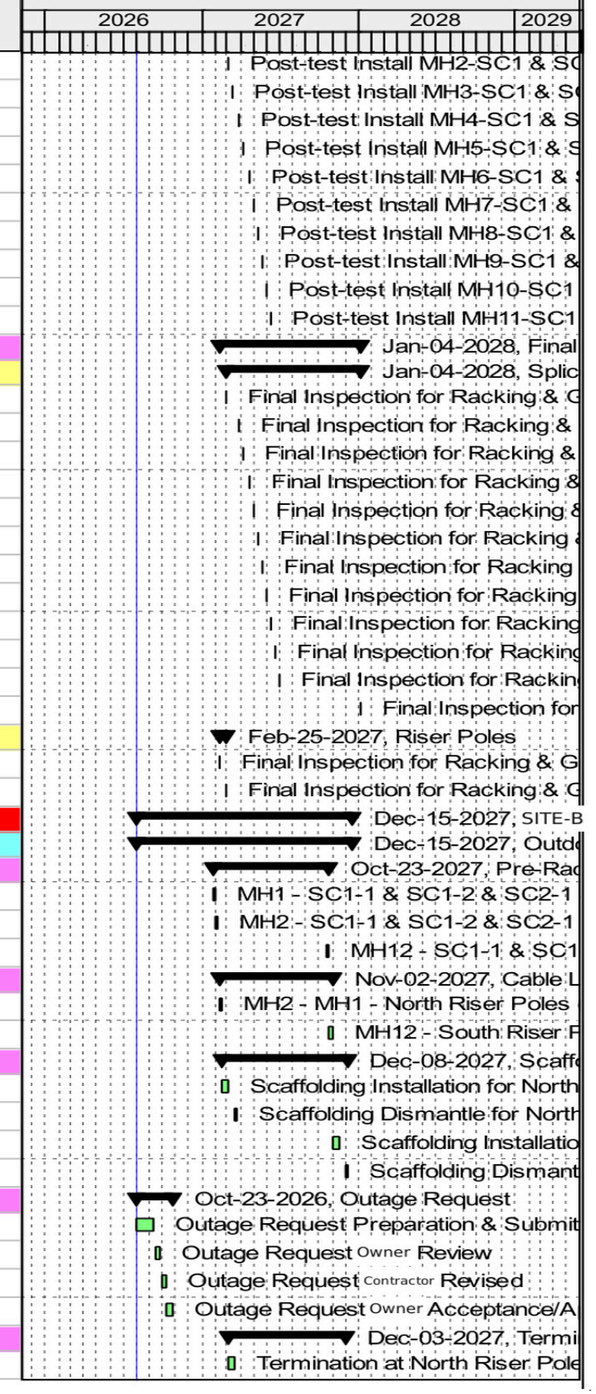

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Sample 230kV Underground Cable Project Schedule

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish
TI-ML-1010	Termination at South Riser Pole (6 Termination) - 2 Crews - Site Area - SITE-B-CIRCUIT	10	10	Nov-18-2027	Dec-03-2027	6		
Surge Arrester Installation		229	229	Mar-17-2027	Dec-15-2027	13		
SA-ML-1000	Termination at North Riser Pole (6 Termination) - 2 Crews - outage - SITE-B CIRCUIT	10	10	Mar-17-2027	Mar-27-2027	232		
SA-ML-1010	Termination at South Riser Pole (6 Termination) - 2 Crews - Site Area - SITE-B-CIRCUIT	10	10	Dec-04-2027	Dec-15-2027	13		
FO cable & LV cabe termination at Acqusition box		229	229	Mar-05-2027	Dec-03-2027	49		
FO-LV-ML-1000	North Riser Poles - SITE-B - Circuit Circuits	10	10	Mar-05-2027	Mar-16-2027	268		
FO-LV-ML-1010	South Riser Pole - SITE-B - Circuit Circuits	10	10	Nov-18-2027	Dec-03-2027	49		
Racking		18	18	Jul-02-2027	Jul-23-2027	66		
RACK-SITEB-1010	MH3-SC1 & SC2 (2 MHs) - RACKING - SITE-B	2	2	Jul-02-2027	Jul-03-2027	10		
RACK-SITEB-1020	MH4-SC1 & SC2 (2 MHs) - RACKING - SITE-B	2	2	Jul-06-2027	Jul-07-2027	17		
RACK-SITEB-1030	MH5-SC1 & SC2 (2 MHs) - RACKING - SITE-B	2	2	Jul-08-2027	Jul-09-2027	24		
RACK-SITEB-1040	MH6-SC1 & SC2 (2 MHs) - RACKING - SITE-B	2	2	Jul-10-2027	Jul-12-2027	31		
RACK-SITEB-1050	MH7-SC1 & SC2 (2 MHs) - RACKING - SITE-B	2	2	Jul-13-2027	Jul-14-2027	38		
RACK-SITEB-1060	MH8-SC1 & SC2 (2 MHs) - RACKING - SITE-B	2	2	Jul-15-2027	Jul-16-2027	45		
RACK-SITEB-1070	MH9-SC1 & SC2 (2 MHs) - RACKING - SITE-B	2	2	Jul-17-2027	Jul-19-2027	52		
RACK-SITEB-1080	MH10-SC1 & SC2 (2 MHs) - RACKING - SITE-B	2	2	Jul-20-2027	Jul-21-2027	59		
RACK-SITEB-1090	MH11-SC1 & SC2 (2 MHs) - RACKING - SITE-B	2	2	Jul-22-2027	Jul-23-2027	66		
Cable Laying for 230kV cable, FO cable, LV cable including Conduit Proving		90	90	Jul-06-2027	Oct-19-2027	10		
CLAY-SITEB-1010	MH2-SC1 & SC2 to MH3-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-B	9	9	Jul-06-2027	Jul-15-2027	10		
CLAY-SITEB-1020	MH3-SC1 & SC2 to MH4-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-B	9	9	Jul-16-2027	Jul-26-2027	10		
CLAY-SITEB-1030	MH4-SC1 & SC2 to MH5-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-B	9	9	Jul-27-2027	Aug-05-2027	10		
CLAY-SITEB-1040	MH5-SC1 & SC2 to MH6-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-B	9	9	Aug-06-2027	Aug-16-2027	10		
CLAY-SITEB-1050	MH6-SC1 & SC2 to MH7-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-B	9	9	Aug-17-2027	Aug-26-2027	10		
CLAY-SITEB-1060	MH7-SC1 & SC2 to MH8-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-B	9	9	Aug-27-2027	Sep-07-2027	10		
CLAY-SITEB-1070	MH8-SC1 & SC2 to MH9-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-B	9	9	Sep-08-2027	Sep-17-2027	10		
CLAY-SITEB-1080	MH9-SC1 & SC2 to MH10-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-B	9	9	Sep-18-2027	Sep-28-2027	10		
CLAY-SITEB-1090	MH10-SC1 & SC2 to MH11-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-B	9	9	Sep-29-2027	Oct-08-2027	10		
CLAY-SITEB-1100	MH11-SC1 & SC2 to MH12-SC1 & SC2 (6 drums) - CABLE-LAYING - SITE-B	9	9	Oct-09-2027	Oct-19-2027	10		
Splicing & Termination work		116	116	Jul-27-2027	Dec-14-2027	6		
Splicing for 230kV cable		116	116	Jul-27-2027	Dec-14-2027	6		
SPLICE-SITEB-1020	MH3-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-B	9	9	Jul-27-2027	Aug-05-2027	13		
SPLICE-SITEB-1030	MH4-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-B	9	9	Aug-06-2027	Aug-16-2027	13		
SPLICE-SITEB-1040	MH5-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-B	9	9	Aug-17-2027	Aug-26-2027	13		
SPLICE-SITEB-1050	MH6-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-B	9	9	Aug-27-2027	Sep-07-2027	13		
SPLICE-SITEB-1060	MH7-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-B	9	9	Sep-08-2027	Sep-17-2027	13		
SPLICE-SITEB-1070	MH8-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-B	9	9	Sep-18-2027	Sep-28-2027	13		
SPLICE-SITEB-1080	MH9-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-B	9	9	Sep-29-2027	Oct-08-2027	13		
SPLICE-SITEB-1090	MH10-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-B	9	9	Oct-09-2027	Oct-19-2027	13		
SPLICE-SITEB-1100	MH11-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-B	9	9	Oct-20-2027	Oct-29-2027	13		
SPLICE-SITEB-1110	MH12-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-B	9	9	Oct-30-2027	Nov-09-2027	13		
SPLICE-SITEB-1010	MH2-SC1 & SC2 (6 Splices) - 2 Crews - SPLICING - SITE-B	9	9	Dec-04-2027	Dec-14-2027	6		
FO cable & LV cabe termination at Acqusition box		5	5	Oct-20-2027	Oct-25-2027	58		
FO-SITEB-1000	Circuit No. 1 MH#1, 2, 3, 4, 5, 6, 7, 8, 9, 10, 11, 12 - SITE-B	5	5	Oct-20-2027	Oct-25-2027	58		
Field testing & Inspections		222	222	Feb-09-2027	Dec-15-2027	54		
Cable Test Before Cable Installation		189	189	Feb-09-2027	Oct-29-2027	87		
PRE-TEST-2110	Pretest Install MH2-SC1 & SC2 to North Riser Pole Termination (6 Drums) - SITE-B	1	1	Feb-09-2027	Feb-09-2027	233		
PRE-TEST-2000	Pretest Install MH2-SC1 & SC2 to MH3-SC1 & SC2 (6 drums) - SITE-B	1	1	Jul-06-2027	Jul-06-2027	181		
PRE-TEST-2010	Pretest Install MH3-SC1 & SC2 to MH4-SC1 & SC2 (6 drums) - SITE-B	1	1	Jul-16-2027	Jul-16-2027	173		

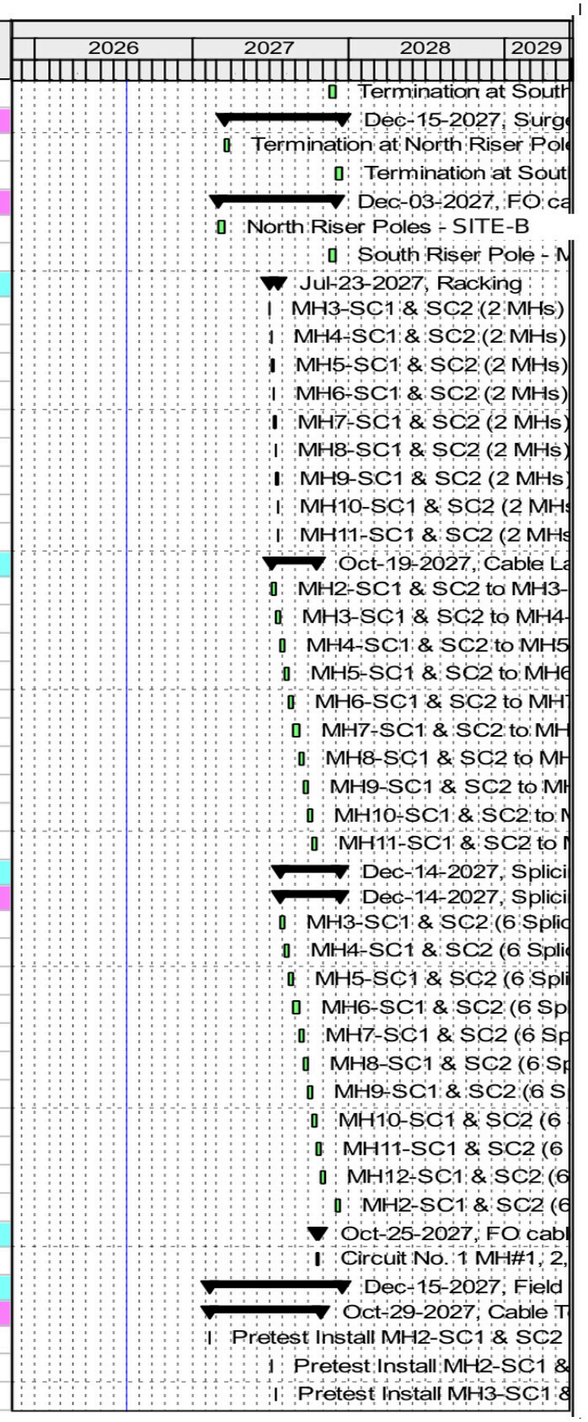


Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Sample 230kV Underground Cable Project Schedule

HSE Contractors | Public Portfolio Example

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish
PRE-TEST-2020	Pretest Install MH4-SC1 & SC2 to MH5-SC1 & SC2 (6 drums) - SITE-B	1	1	Jul-27-2027	Jul-27-2027	165		
PRE-TEST-2030	Pretest Install MH5-SC1 & SC2 to MH6-SC1 & SC2 (6 drums) - SITE-B	1	1	Aug-06-2027	Aug-06-2027	157		
PRE-TEST-2040	Pretest Install MH6-SC1 & SC2 to MH7-SC1 & SC2 (6 drums) - SITE-B	1	1	Aug-17-2027	Aug-17-2027	149		
PRE-TEST-2050	Pretest Install MH7-SC1 & SC2 to MH8-SC1 & SC2 (6 drums) - SITE-B	1	1	Aug-27-2027	Aug-27-2027	141		
PRE-TEST-2060	Pretest Install MH8-SC1 & SC2 to MH9-SC1 & SC2 (6 drums) - SITE-B	1	1	Sep-08-2027	Sep-08-2027	133		
PRE-TEST-2070	Pretest Install MH9-SC1 & SC2 to MH10-SC1 & SC2 (6 drums) - SITE-B	1	1	Sep-18-2027	Sep-18-2027	125		
PRE-TEST-2080	Pretest Install MH10-SC1 & SC2 to MH11-SC1 & SC2 (6 drums) - SITE-B	1	1	Sep-29-2027	Sep-29-2027	117		
PRE-TEST-2090	Pretest Install MH11-SC1 & SC2 to MH12-SC1 & SC2 (6 drums) - SITE-B	1	1	Oct-09-2027	Oct-09-2027	109		
PRE-TEST-2100	Pretest Install MH12-SC1 & SC2 to South Riser Pole Termination (6 Drums) - SITE-B	5	5	Oct-25-2027	Oct-29-2027	45		
Cable Test After Cable Installation		193	193	Feb-10-2027	Nov-05-2027	46		
POST-TEST-2110	Post-test Install MH2-SC1 & SC2 to North Riser Pole Termination (6 Drums) - SITE-B	5	5	Feb-10-2027	Feb-16-2027	233		
POST-TEST-2000	Post-test Install MH2-SC1 & SC2 to MH3-SC1 & SC2 (6 drums) - SITE-B	1	1	Jul-16-2027	Jul-16-2027	129		
POST-TEST-2010	Post-test Install MH3-SC1 & SC2 to MH4-SC1 & SC2 (6 drums) - SITE-B	1	1	Jul-27-2027	Jul-27-2027	121		
POST-TEST-2020	Post-test Install MH4-SC1 & SC2 to MH5-SC1 & SC2 (6 drums) - SITE-B	1	1	Aug-06-2027	Aug-06-2027	113		
POST-TEST-2030	Post-test Install MH5-SC1 & SC2 to MH6-SC1 & SC2 (6 drums) - SITE-B	1	1	Aug-17-2027	Aug-17-2027	105		
POST-TEST-2040	Post-test Install MH6-SC1 & SC2 to MH7-SC1 & SC2 (6 drums) - SITE-B	1	1	Aug-27-2027	Aug-27-2027	97		
POST-TEST-2050	Post-test Install MH7-SC1 & SC2 to MH8-SC1 & SC2 (6 drums) - SITE-B	1	1	Sep-08-2027	Sep-08-2027	89		
POST-TEST-2060	Post-test Install MH8-SC1 & SC2 to MH9-SC1 & SC2 (6 drums) - SITE-B	1	1	Sep-18-2027	Sep-18-2027	81		
POST-TEST-2070	Post-test Install MH9-SC1 & SC2 to MH10-SC1 & SC2 (6 drums) - SITE-B	1	1	Sep-29-2027	Sep-29-2027	73		
POST-TEST-2080	Post-test Install MH10-SC1 & SC2 to MH11-SC1 & SC2 (6 drums) - SITE-B	1	1	Oct-09-2027	Oct-09-2027	65		
POST-TEST-2090	Post-test Install MH11-SC1 & SC2 to MH12-SC1 & SC2 (6 drums) - SITE-B	1	1	Oct-20-2027	Oct-20-2027	57		
POST-TEST-2100	Post-test Install MH12-SC1 & SC2 to South Riser Pole Termination (6 Drums) - SITE-B	5	5	Nov-01-2027	Nov-05-2027	45		
Final Racking & Grounding Inspections		256	256	Feb-13-2027	Dec-15-2027	13		
Splice Manhole		256	256	Feb-13-2027	Dec-15-2027	13		
FI-SPLICE-1995	Final Inspection for Racking & Grounding & Splicing - MH1-SC1 & SC2 (6 Splices) - SITE-B	1	1	Feb-13-2027	Feb-13-2027	268		
FI-SPLICE-2010	Final Inspection for Racking & Grounding & Splicing - MH3-SC1 & SC2 (6 Splices) - SITE-B	1	1	Aug-06-2027	Aug-06-2027	120		
FI-SPLICE-2020	Final Inspection for Racking & Grounding & Splicing - MH4-SC1 & SC2 (6 Splices) - SITE-B	1	1	Aug-17-2027	Aug-17-2027	111		
FI-SPLICE-2030	Final Inspection for Racking & Grounding & Splicing - MH5-SC1 & SC2 (6 Splices) - SITE-B	1	1	Aug-27-2027	Aug-27-2027	102		
FI-SPLICE-2040	Final Inspection for Racking & Grounding & Splicing - MH6-SC1 & SC2 (6 Splices) - SITE-B	1	1	Sep-08-2027	Sep-08-2027	93		
FI-SPLICE-2050	Final Inspection for Racking & Grounding & Splicing - MH7-SC1 & SC2 (6 Splices) - SITE-B	1	1	Sep-18-2027	Sep-18-2027	84		
FI-SPLICE-2060	Final Inspection for Racking & Grounding & Splicing - MH8-SC1 & SC2 (6 Splices) - SITE-B	1	1	Sep-29-2027	Sep-29-2027	75		
FI-SPLICE-2070	Final Inspection for Racking & Grounding & Splicing - MH9-SC1 & SC2 (6 Splices) - SITE-B	1	1	Oct-09-2027	Oct-09-2027	66		
FI-SPLICE-2080	Final Inspection for Racking & Grounding & Splicing - MH10-SC1 & SC2 (6 Splices) - SITE-B	1	1	Oct-20-2027	Oct-20-2027	57		
FI-SPLICE-2090	Final Inspection for Racking & Grounding & Splicing - MH11-SC1 & SC2 (6 Splices) - SITE-B	1	1	Oct-30-2027	Oct-30-2027	48		
FI-SPLICE-2100	Final Inspection for Racking & Grounding & Splicing - MH12-SC1 & SC2 (6 Splices) - SITE-B	1	1	Nov-10-2027	Nov-10-2027	39		
FI-SPLICE-2000	Final Inspection for Racking & Grounding & Splicing - MH2-SC1 & SC2 (6 Splices) - SITE-B	1	1	Dec-15-2027	Dec-15-2027	13		
Riser Poles		220	220	Mar-17-2027	Dec-04-2027	22		
FI-TS-2010	Final Inspection for R&G&Termination - North Riser Poles (12 drums) - outage - SITE-B	1	1	Mar-17-2027	Mar-17-2027	241		
FI-TS-2000	Final Inspection for R&G&Termination - South Riser Poles (12 drums) - Site Area - SITE-B	1	1	Dec-04-2027	Dec-04-2027	22		
End to End JacketIntegrity test		10	10	Jan-05-2028	Jan-15-2028	0		
INT-T-1000	End to End Jacket Integrity Test (South Riser Pole to North Riser Pole) - SITE-A	5	5	Jan-05-2028	Jan-10-2028	0		
INT-T-1010	End to End Jacket Integrity Test (South Riser Pole to North Riser Pole) - SITE-B	5	5	Jan-11-2028	Jan-15-2028	0		
Setting of PD & DTS & Fault locating Monitoring for Both Circuits		5	5	Jan-17-2028	Jan-21-2028	0		
CON-1000	Configration Set up for PDM System	5	5	Jan-17-2028	Jan-21-2028	0		
CON-1010	Configration Set up for DTS & Fault locating System	5	5	Jan-17-2028	Jan-21-2028	0		
ACHV Test including PD Monitoring		20	20	Jan-22-2028	Feb-14-2028	0		
ACHV-1000	Preparation	5	5	Jan-22-2028	Jan-27-2028	0		
ACHV-1010	SITE-A Circuit for 6 cables	5	5	Jan-28-2028	Feb-02-2028	0		

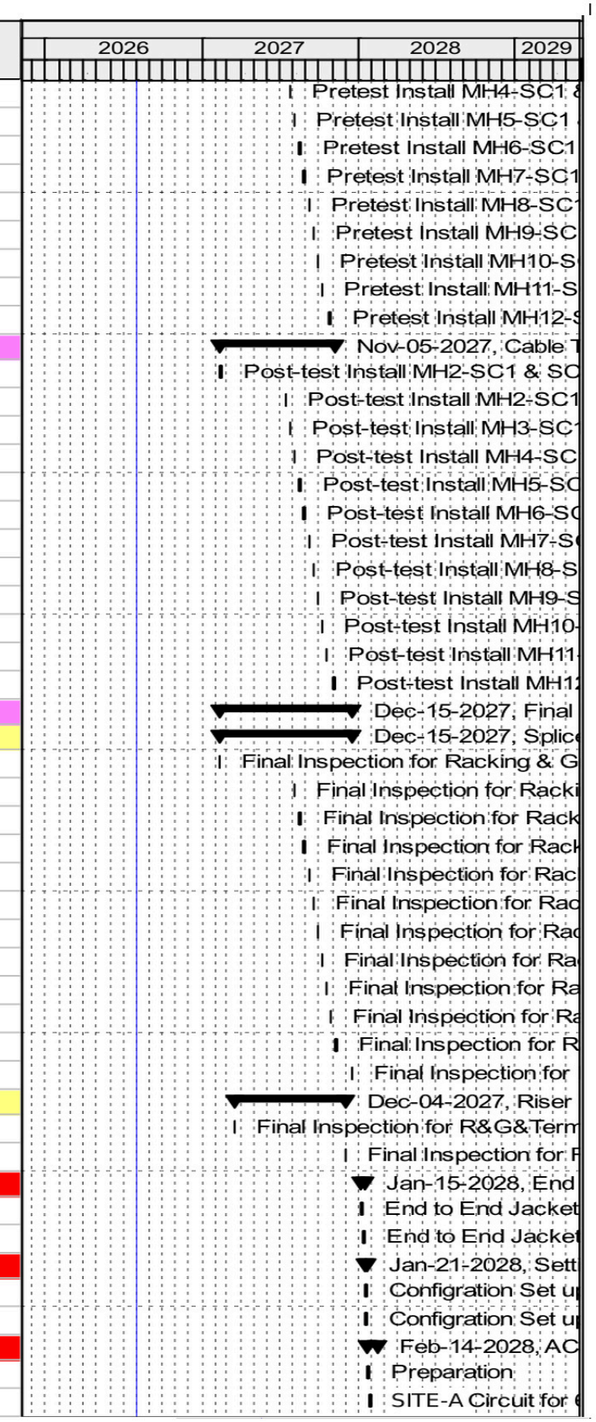


Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Sample 230kV Underground Cable Project Schedule

HSE Contractors | Public Portfolio Example

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish
ACHV-1020	SITE-B Circuit for 6 cables	5	5	Feb-03-2028	Feb-08-2028	0		
ACHV-1030	Site Restoration (Project Laydown Yard	5	5	Feb-09-2028	Feb-14-2028	0		
Closeout & Demobilization		13	13	Feb-15-2028	Feb-29-2028	0		
CD-100	Demobilization	4	4	Feb-15-2028	Feb-18-2028	0		
CD-110	O&M Manuals Submittal	4	4	Feb-19-2028	Feb-23-2028	0		
CD-105	Supply Cable Sample	9	9	Feb-19-2028	Feb-29-2028	0		
CD-120	O&M Manuals Review & Approval	4	4	Feb-24-2028	Feb-28-2028	0		

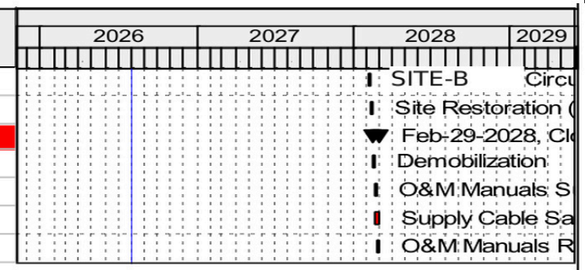

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
