
Sample 500kV Underground Cable Project Schedule

Engineering, Procurement and Construction - Monthly Progress Schedule


HSE SCHEDULING CONSULTANTS

Activity ID	Activity Name	Original Duration	Start	Finish
500kV Underground Monthly Progress Schedule		368d	Oct-31-25 A	Apr-20-27
500kV Underground Cable Project		368d	Oct-31-25 A	Apr-20-27
500kV Utility Project		368d	Oct-31-25 A	Apr-20-27
Milestones		297d	Oct-31-25 A	Apr-20-27
Contract Milestones		417d	Oct-31-25 A	Apr-20-27
PRJ-MIL-COAW-01	Contract Award	0d	Oct-31-25 A	
PRJ-MIL-DPI-01	Date of PO Issuance	0d	Nov-21-25 A	Nov-21-25 A
PRJ-MIL-FKOM-01	First Kick-off Meeting	0d	Dec-16-25 A	Dec-16-25 A
PRJ-MIL-RSM-01	Release of Splice Manufacturing	0d	Feb-28-26 A	Feb-28-26 A
PRJ-MIL-OTRM-01	Release of Outdoor Terminations Manufacturing	0d	Mar-19-26 A	Mar-19-26 A
PRJ-MIL-CCL-01	Confirmation of Cut Length	0d	Mar-27-26 A	Mar-27-26 A
PRJ-MIL-RCM-01	Release of Cable Manufacturing	0d	Mar-27-26 A	Mar-27-26 A
PRJ-MIL-ROAM-01	Release of Other Accessories Manufacturing	0d	Apr-20-26 A	Apr-20-26 A
PRJ-MIL-FED-01	Finalize Engineering Design	0d	Jul-10-26 A	Jul-10-26 A
PRJ-MIL-SPLC-01	100% Cable Splice On Site	0d	Aug-28-26 A	Aug-28-26 A
PRJ-MIL-OTRM-02	100% Outdoor Terminations On Site	0d	Aug-28-26 A	Aug-28-26 A
PRJ-MIL-10CAON-01	100% Cable Onsite	0d	Sep-30-26	Sep-30-26
PRJ-MIL-FPCD-01	Finalize Pre-Construction Deliverables	0d	Oct-16-26	Oct-16-26
PRJ-MIL-CINS-01	Completion of Cable Installation	5d	Oct-25-26	Oct-29-26
PRJ-MIL-CAO-01	100% Cable Accessories Onsite	0d	Nov-21-26	Nov-21-26
PRJ-MIL-SPTR-01	Complete Cable Splicing & Termination	0d	Dec-10-26	Dec-10-26
PRJ-MIL-RGRD-01	Complete Cable Racking & Grounding Installation	0d	Dec-11-26	Dec-11-26
PRJ-MIL-COMM-01	Complete Testing and Commissioning	0d	Dec-19-26	Dec-19-26
PRJ-MIL-SUCO-01	Substantial Completion	0d		Dec-19-26
PRJ-MIL-FIAC-01	Final Acceptance	0d		Apr-20-27
Payment Milestones		222d	Jun-15-26 A	Apr-20-27
Direct Payment Milestones		222d	Jun-15-26 A	Apr-20-27
PRJ-MIL-BOIN-01	Bond & Insurance	32d	Jun-15-26 A	Oct-31-26*
PRJ-MIL-MOB-02	Payment Milestone - Mobilization	1d	Jul-17-26 A	Jul-17-26 A
PRJ-MIL-RGRD-02	Payment Milestone - Racking & Grounding Materials Receiving Visual Inspection	1d	Jul-22-26 A	Aug-28-26 A
PRJ-MIL-ELY-01	Payment Milestone - Establishment of the Laydown Yard	1d	Jul-29-26 A	Jul-29-26 A
PRJ-MIL-RCVI-01	Payment Milestone - Cable Receiving Inspection & Testing - 1st Batch	1d	Aug-24-26 A	Aug-28-26 A
PRJ-MIL-SARVI-01	Payment Milestone - Surge Arresters Receiving Visual Inspection	1d	Aug-27-26 A	Aug-28-26 A
PRJ-MIL-BGCRVI-01	Payment Milestone - Bonding & Grounding Cables Receiving Visual Inspection	1d	Aug-27-26 A	Aug-28-26 A
PRJ-MIL-TPRA-01	Payment Milestone - Transportation Permits Review and Approval	1d	Aug-31-26 A	Aug-31-26 A
PRJ-MIL-POTEIN-02	Payment Milestone - Post-test Install Cable S/V#13 - S/V#14	1d	Aug-31-26 A	Aug-31-26 A
PRJ-MIL-POTEIN-03	Payment Milestone - Post-test Install Cable S/V#12 - S/V#13	1d	Sep-17-26 A	Sep-17-26 A
PRJ-MIL-POTEIN-04	Payment Milestone - Post-test Install Cable S/V#11 - S/V#12	1d	Sep-23-26 A	Sep-23-26 A
PRJ-MIL-SPLC-03	Payment Milestone - Splices Receiving Visual Inspection	1d	Sep-26-26 A	Sep-26-26 A
PRJ-MIL-OTRM-04	Payment Milestone - Outdoor Terminations Receiving Visual Inspection	1d	Sep-26-26 A	Sep-26-26 A
PRJ-MIL-LBOX-02	Payment Milestone - Link Boxes + SVLs Receiving Visual Inspection	1d	Sep-26-26 A	Sep-26-26 A
PRJ-MIL-CACLSP-01	Payment Milestone - Cable Clamps (Spring Clamps, Ratcheting Device, Joint Clamp, etc) Receiving Visual Inspectior	1d	Sep-26-26 A	Sep-26-26 A
PRJ-MIL-RCVI-02	Payment Milestone - Cable Receiving Inspection & Testing - 2nd Batch	1d	Sep-28-26 A	Sep-28-26 A
PRJ-MIL-POTEIN-08	Payment Milestone - Post-test Install Cable S/V#5 - R/V#5 - S/V#6 (fixed) - S/V#7	1d	Sep-29-26 A	Sep-29-26 A
PRJ-MIL-POTEIN-09	Payment Milestone - Post-test Install Cable S/V#4 - R/V#4 - S/V#5	1d	Sep-30-26	Sep-30-26
PRJ-MIL-RGRD-17	Payment Milestone - Final Inspection for Racking & Grounding - S/V#6 (Fixed)	1d	Oct-01-26	Oct-01-26
PRJ-MIL-RGRD-23	Payment Milestone - Final Inspection for Racking & Grounding - R/V#5	1d	Oct-01-26	Oct-01-26
PRJ-MIL-RGRD-22	Payment Milestone - Final Inspection for Racking & Grounding - R/V#4	1d	Oct-03-26	Oct-03-26
PRJ-MIL-POTEIN-05	Payment Milestone - Post-test Install Cable S/V#9 - S/V#10 (fixed) - S/V#11	1d	Oct-06-26	Oct-06-26

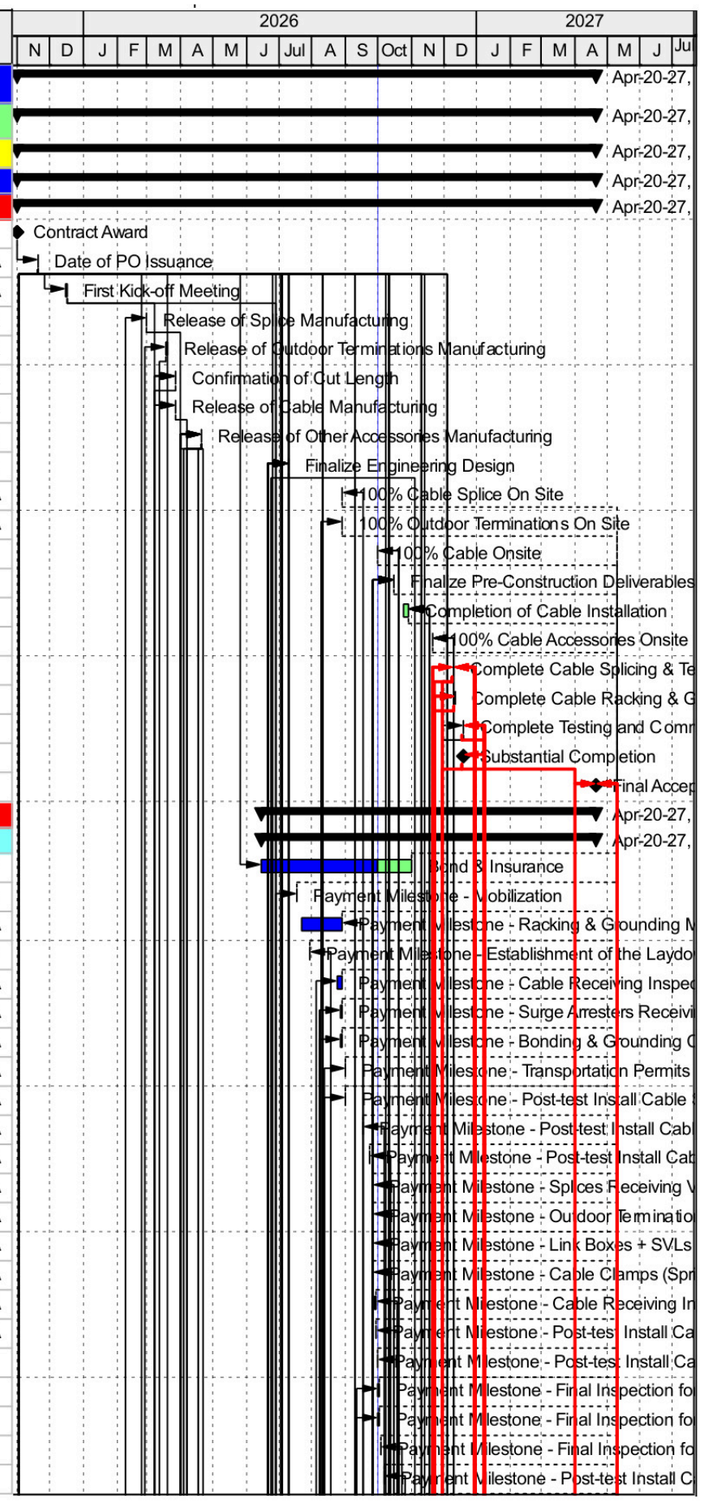


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish
PRJ-MIL-RGRD-16	Payment Milestone - Final Inspection for Racking & Grounding - S/V#10 (Fixed)	1d	Oct-07-26	Oct-07-26
PRJ-MIL-POTEIN-06	Payment Milestone - Post-test Install Cable S/V#8 - S/V#9	1d	Oct-09-26	Oct-09-26
PRJ-MIL-POTEIN-07	Payment Milestone - Post-test Install Cable S/V#7 - R/V#6 - S/V#8	1d	Oct-14-26	Oct-14-26
PRJ-MIL-RGRD-24	Payment Milestone - Final Inspection for Racking & Grounding - R/V#6	1d	Oct-16-26	Oct-16-26
PRJ-MIL-ICSSV-07	Payment Milestone - Install Cable Splicing - S/V#11	1d	Oct-18-26	Oct-18-26
PRJ-MIL-ICSSV-09	Payment Milestone - Install Cable Splicing - S/V#5	1d	Oct-18-26	Oct-18-26
PRJ-MIL-RGRD-13	Payment Milestone - Final Inspection for Racking & Grounding & Cable Splicing - S/V#5	1d	Oct-19-26	Oct-19-26
PRJ-MIL-POTEIN-12	Payment Milestone - Post-test Install Cable S/V#2 - R/V#2 - S/V#3 - R/V#3 - S/V#4 (fixed) |Site Constraint|	1d	Oct-20-26	Oct-20-26
PRJ-MIL-RGRD-11	Payment Milestone - Final Inspection for Racking & Grounding & Cable Splicing - S/V#11	1d	Oct-20-26	Oct-20-26
PRJ-MIL-RGRD-18	Payment Milestone - Final Inspection for Racking & Grounding - S/V#3 (Fixed)	1d	Oct-21-26	Oct-21-26
PRJ-MIL-RGRD-20	Payment Milestone - Final Inspection for Racking & Grounding - R/V#2	1d	Oct-21-26	Oct-21-26
PRJ-MIL-RGRD-21	Payment Milestone - Final Inspection for Racking & Grounding - R/V#3	1d	Oct-21-26	Oct-21-26
PRJ-MIL-POTEIN-11	Payment Milestone - Post-test Install Cable S/V#1 - R/V#1 - S/V#2 |Site Constraint|	1d	Oct-22-26	Oct-22-26
PRJ-MIL-ICSSV-06	Payment Milestone - Install Cable Splicing - S/V#13	1d	Oct-24-26	Oct-24-26
PRJ-MIL-RGRD-19	Payment Milestone - Final Inspection for Racking & Grounding - R/V#1	1d	Oct-24-26	Oct-24-26
PRJ-MIL-RGRD-10	Payment Milestone - Final Inspection for Racking & Grounding & Cable Splicing - S/V#13	1d	Oct-25-26	Oct-25-26
PRJ-MIL-POTEIN-10	Payment Milestone - Post-test Install Cable WTS to S/V#1	1d	Oct-26-26	Oct-26-26
PRJ-MIL-POTEIN-01	Payment Milestone - Post-test Install Cable S/V#14 - ETS	1d	Oct-29-26	Oct-29-26
PRJ-MIL-ICSSV-02	Payment Milestone - Install Cable Splicing - S/V#12	1d	Oct-30-26	Oct-30-26
PRJ-MIL-ICSSV-03	Payment Milestone - Install Cable Splicing - S/V#9	1d	Oct-30-26	Oct-30-26
PRJ-MIL-SCS-01	Payment Milestone - Supply Cable Sample	1d	Oct-30-26	Oct-30-26
PRJ-MIL-RGRD-04	Payment Milestone - Final Inspection for Racking & Grounding & Cable Splicing - S/V#12	1d	Oct-31-26	Oct-31-26
PRJ-MIL-RGRD-05	Payment Milestone - Final Inspection for Racking & Grounding & Cable Splicing - S/V#9	1d	Oct-31-26	Oct-31-26
PRJ-MIL-ICTSAE-01	Payment Milestone - Install Surge Arrester - ETS	1d	Nov-02-26	Nov-02-26
PRJ-MIL-ICSSV-08	Payment Milestone - Install Cable Splicing - S/V#8	1d	Nov-10-26	Nov-10-26
PRJ-MIL-ICSSV-05	Payment Milestone - Install Cable Splicing - S/V#4	1d	Nov-11-26	Nov-11-26
PRJ-MIL-RGRD-07	Payment Milestone - Final Inspection for Racking & Grounding & Cable Splicing - S/V#4	1d	Nov-11-26	Nov-11-26
PRJ-MIL-RGRD-12	Payment Milestone - Final Inspection for Racking & Grounding & Cable Splicing - S/V#8	1d	Nov-11-26	Nov-11-26
PRJ-MIL-ICTSAW-01	Payment Milestone - Install Surge Arrester - WTS	1d	Nov-14-26	Nov-14-26
PRJ-MIL-RGRD-08	Payment Milestone - Final Inspection for Racking & Grounding & Cable Termination - WTS	1d	Nov-17-26	Nov-17-26
PRJ-MIL-ICSSV-04	Payment Milestone - Install Cable Splicing - S/V#7	1d	Nov-21-26	Nov-21-26
PRJ-MIL-ICSSV-10	Payment Milestone - Install Cable Splicing - S/V#1	1d	Nov-21-26	Nov-21-26
PRJ-MIL-DAS-02	Payment Milestone - DAS Instrument Receiving Visual Inspection	1d	Nov-21-26	Nov-21-26
PRJ-MIL-RGRD-06	Payment Milestone - Final Inspection for Racking & Grounding & Cable Splicing - S/V#7	1d	Nov-23-26	Nov-23-26
PRJ-MIL-RGRD-15	Payment Milestone - Final Inspection for Racking & Grounding & Cable Splicing - S/V#1	1d	Nov-23-26	Nov-23-26
PRJ-MIL-ICSSV-01	Payment Milestone - Install Cable Splicing - S/V#14	1d	Dec-01-26	Dec-01-26
PRJ-MIL-RGRD-14	Payment Milestone - Final Inspection for Racking & Grounding & Cable Termination - ETS	1d	Dec-02-26	Dec-02-26
PRJ-MIL-DAS-01	Payment Milestone - DAS Commissioning	1d	Dec-08-26	Dec-08-26
PRJ-MIL-INCASP-01	Payment Milestone - Install Cable Splicing - S/V#2 (Site Constraint)	1d	Dec-09-26	Dec-09-26
PRJ-MIL-RGRD-03	Payment Milestone - Final Inspection for Racking & Grounding & Cable Splicing - S/V#14	1d	Dec-10-26	Dec-10-26
PRJ-MIL-RGRD-09	Payment Milestone - Final Inspection for Racking & Grounding & Cable Splicing - S/V#2 (Site Constraint)	1d	Dec-10-26	Dec-10-26
PRJ-MIL-ACWT-01	Payment Milestone - AC Withstand Test Phase A3	1d	Dec-16-26	Dec-16-26
PRJ-MIL-ACWT-02	Payment Milestone - AC Withstand Test Phase B3	1d	Dec-17-26	Dec-17-26
PRJ-MIL-ACWT-03	Payment Milestone - AC Withstand Test Phase C3	1d	Dec-18-26	Dec-18-26
PRJ-MIL-TRAINI-01	Payment Milestone - Training	1d	Dec-19-26	Dec-19-26
PRJ-MIL-MOB-01	Payment Milestone - Demobilization	1d	Dec-29-26	Dec-29-26
PRJ-MIL-SARVI-02	Payment Milestone - Spare Surge Arresters Receiving Visual Inspection	1d	Apr-20-27	Apr-20-27
Monthly Indirect Cost Payment Milestones		154d	Jul-24-26 A	Dec-24-26
February (2026)		1d	Jul-24-26 A	Jul-24-26 A

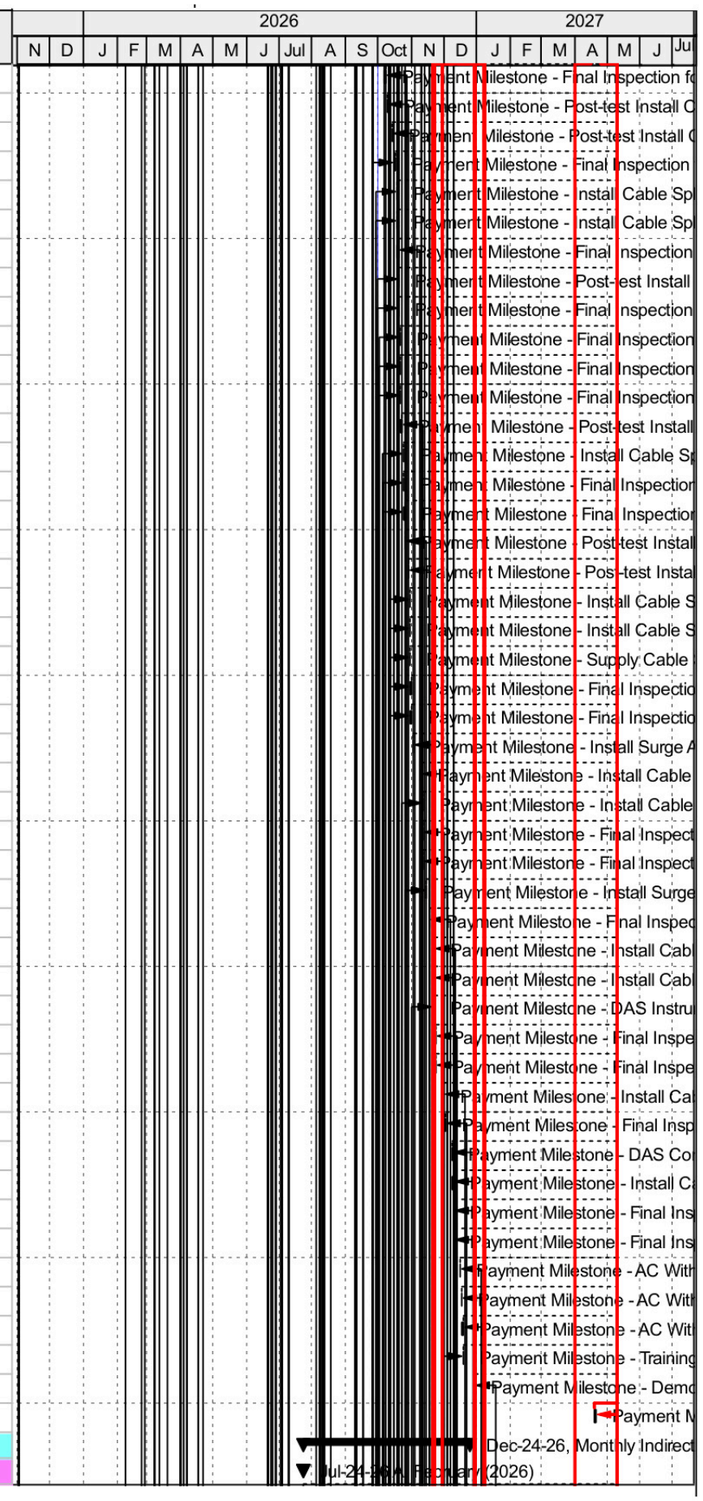


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish
PRJ-MIL-FEB26-01	Construction Management Staff 200HRS - February - 2026	1d	Jul-24-26 A	Jul-24-26 A
March (2026)		1d	Jul-24-26 A	Jul-24-26 A
PRJ-MIL-MAR26-01	Construction Management Staff 200HRS - March - 2026	1d	Jul-24-26 A	Jul-24-26 A
April (2026)		1d	Jul-24-26 A	Jul-24-26 A
PRJ-MIL-APR26-01	Construction Management Staff 200HRS - April - 2026	1d	Jul-24-26 A	Jul-24-26 A
May (2026)		1d	Jul-24-26 A	Jul-24-26 A
PRJ-MIL-MAY26-01	Construction Management Staff 200HRS - May - 2026	1d	Jul-24-26 A	Jul-24-26 A
June (2026)		1d	Jul-24-26 A	Jul-24-26 A
PRJ-MIL-JUN26-01	Construction Management Staff 200HRS - June - 2026	1d	Jul-24-26 A	Jul-24-26 A
July (2026)		1d	Jul-30-26 A	Jul-30-26 A
PRJ-MIL-JUL26-01	Construction Management Staff - July - 2026	1d	Jul-30-26 A	Jul-30-26 A
PRJ-MIL-JUL26-02	Environmental Compliance Personnel - July - 2026	1d	Jul-30-26 A	Jul-30-26 A
PRJ-MIL-JUL26-03	Safety - July - 2026	1d	Jul-30-26 A	Jul-30-26 A
August (2026)		1d	Aug-30-26 A	Aug-30-26 A
PRJ-MIL-AUG26-01	Construction Management Staff - August - 2026	1d	Aug-30-26 A	Aug-30-26 A
PRJ-MIL-AUG26-02	Environmental Compliance Personnel - August - 2026	1d	Aug-30-26 A	Aug-30-26 A
PRJ-MIL-AUG26-03	Safety - August - 2026	1d	Aug-30-26 A	Aug-30-26 A
September (2026)		1d	Sep-29-26 A	Sep-29-26 A
PRJ-MIL-SEP26-01	Construction Management Staff - September - 2026	1d	Sep-29-26 A	Sep-29-26 A
PRJ-MIL-SEP26-02	Environmental Compliance Personnel - September - 2026	1d	Sep-29-26 A	Sep-29-26 A
PRJ-MIL-SEP26-03	Safety - September - 2026	1d	Sep-29-26 A	Sep-29-26 A
October (2026)		1d	Oct-30-26	Oct-30-26
PRJ-MIL-OCT26-01	Construction Management Staff - October - 2026	1d	Oct-30-26	Oct-30-26*
PRJ-MIL-OCT26-02	Environmental Compliance Personnel - October - 2026	1d	Oct-30-26	Oct-30-26*
PRJ-MIL-OCT26-03	Safety - October - 2026	1d	Oct-30-26	Oct-30-26*
November (2026)		1d	Nov-29-26	Nov-29-26
PRJ-MIL-NOV26-01	Construction Management Staff - November - 2026	1d	Nov-29-26	Nov-29-26*
PRJ-MIL-NOV26-02	Environmental Compliance Personnel - November - 2026	1d	Nov-29-26	Nov-29-26*
PRJ-MIL-NOV26-03	Safety - November - 2026	1d	Nov-29-26	Nov-29-26*
December (2026)		1d	Dec-24-26	Dec-24-26
PRJ-MIL-DEC26-01	Construction Management Staff - December - 2026	1d	Dec-24-26	Dec-24-26*
PRJ-MIL-DEC26-02	Environmental Compliance Personnel - December - 2026	1d	Dec-24-26	Dec-24-26*
PRJ-MIL-DEC26-03	Safety - December - 2026	1d	Dec-24-26	Dec-24-26*
Pre-Construction & Deliverables		235d	Nov-21-25 A	Oct-15-26
Project Management Plan		99d	Nov-21-25 A	Oct-15-26
PRJ-PRE-PMAN-01	Project Plan Preparation/Submittal	30d	Nov-21-25 A	Jun-12-26 A
PRJ-PRE-PMAN-02	Project Plan Owner Review	10d	Jun-13-26 A	Sep-30-26
PRJ-PRE-PMAN-03	Project Plan Contractor Revised	10d	Oct-01-26	Oct-14-26
PRJ-PRE-PMAN-04	Project Plan Acceptance	1d	Oct-15-26	Oct-15-26
Risk Management Plan & Risk Register		135d	Nov-21-25 A	Sep-30-26
PRJ-PRE-RMRR-01	Risk Plan Preparation/Submittal	30d	Nov-21-25 A	Feb-18-26 A
PRJ-PRE-RMRR-02	Risk Plan Owner Review	10d	Feb-19-26 A	Apr-15-26 A
PRJ-PRE-RMRR-03	Risk Plan Contractor Revised	10d	Apr-16-26 A	May-05-26 A
PRJ-PRE-RMRR-04	Risk Plan Owner's Review and Acceptance	1d	May-06-26 A	Sep-30-26
Construction Management Plan		90d	Nov-21-25 A	Aug-11-26 A
PRJ-PRE-CMP-01	Construction Plan Preparation/Submittal	90d	Nov-21-25 A	Jun-12-26 A
PRJ-PRE-CMP-02	Construction Plan 1st Review	10d	Jun-13-26 A	Jul-23-26 A
PRJ-PRE-CMP-03	Construction Plan 1st Revised	10d	Jul-23-26 A	Jul-29-26 A
PRJ-PRE-CMP-04	Construction Plan 2nd Review	10d	Jul-30-26 A	Aug-04-26 A
PRJ-PRE-CMP-05	Construction Plan 2nd Revised	5d	Aug-05-26 A	Aug-08-26 A
PRJ-PRE-CMP-06	Construction Plan Acceptance	1d	Aug-10-26 A	Aug-11-26 A

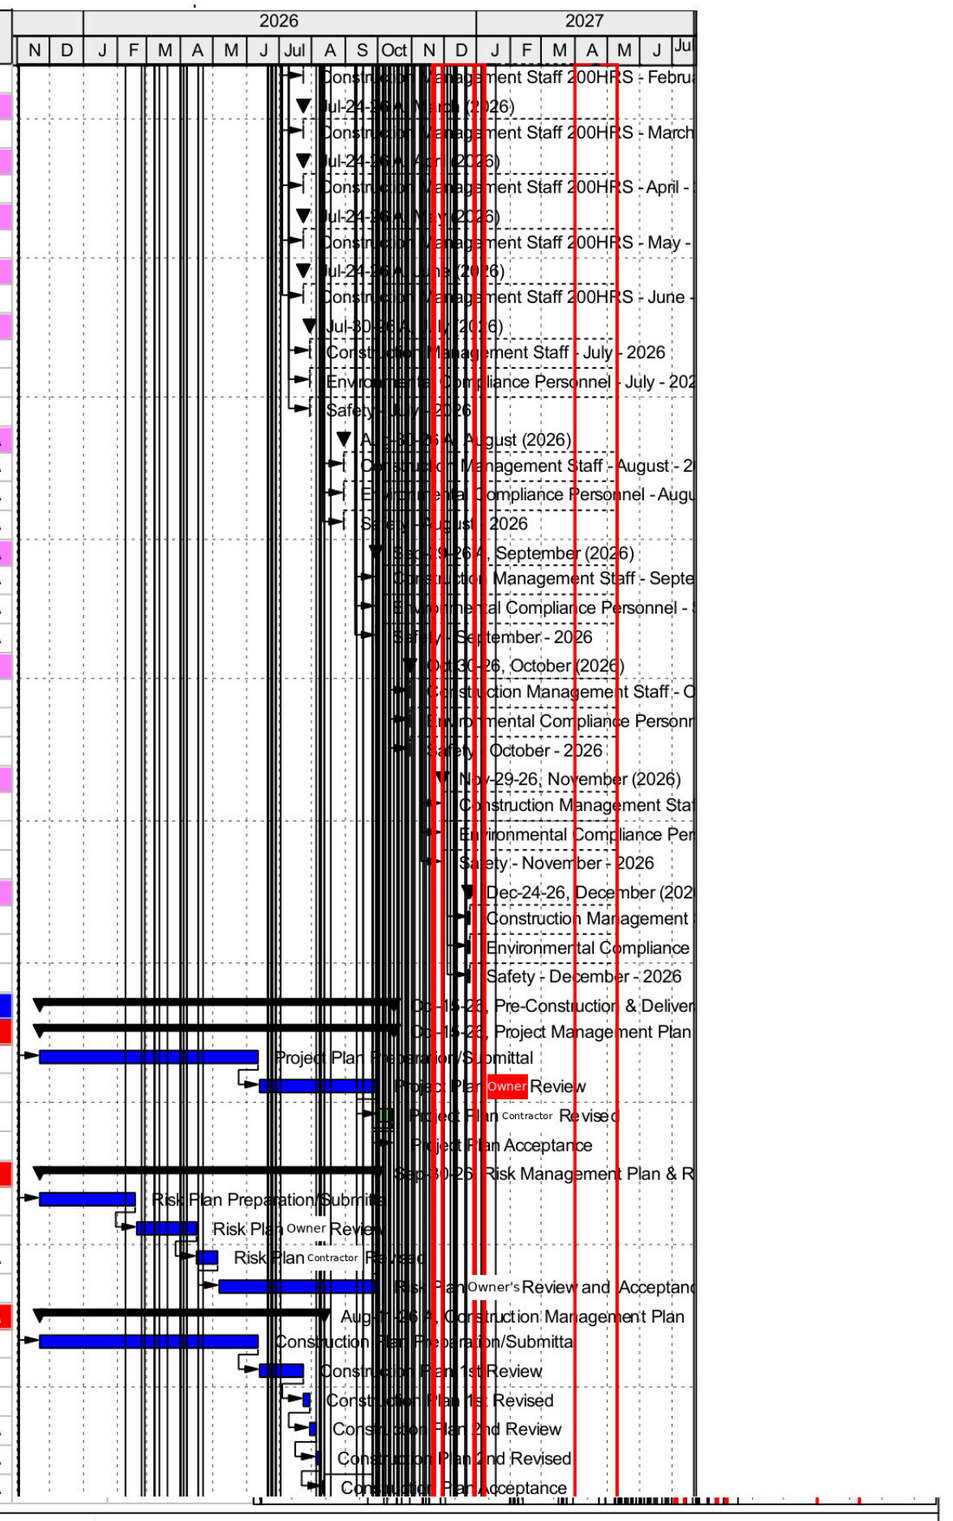

Remaining Level of Effort | Remaining Work | Summary
Actual Level of Effort | Critical Remaining Work
Actual Work | Milestone

Activity ID	Activity Name	Original Duration	Start	Finish
Material Management Plan Yard Plan		106d	Nov-21-25 A	Jul-06-26 A
PRJ-PRE-MMYP-01	Develop/Submit Yard Plan	90d	Nov-21-25 A	Apr-24-26 A
PRJ-PRE-MMYP-02	Yard Plan 1st Review	10d	Apr-25-26 A	Jun-02-26 A
PRJ-PRE-MMYP-03	Yard Plan 1st Revised	10d	Jun-03-26 A	Jun-04-26 A
PRJ-PRE-MMYP-04	Yard Plan 2nd Review	10d	Jun-05-26 A	Jun-22-26 A
PRJ-PRE-MMYP-05	Yard Plan 2nd Revised	10d	Jun-23-26 A	Jun-24-26 A
PRJ-PRE-MMYP-06	Yard Plan Acceptance	5d	Jun-25-26 A	Jul-06-26 A
Environmental Compliance Plan		90d	Nov-21-25 A	Sep-02-26 A
PRJ-PRE-ENV-01	Environmental Plan Preparation/Submittal	90d	Nov-21-25 A	Jul-17-26 A
PRJ-PRE-ENV-02	Environmental Plan 1st Review	5d	Jul-20-26 A	Aug-07-26 A
PRJ-PRE-ENV-06	Environmental Plan Acceptance	1d	Aug-10-26 A	Sep-02-26 A
Contractor Orientation & Safety Plan		61d	Nov-21-25 A	Mar-02-26 A
PRJ-PRE-COS-01	Safety Plan Preparation/Submittal	40d	Nov-21-25 A	Feb-12-26 A
PRJ-PRE-COS-02	Safety Plan Owner Review	10d	Jan-16-26 A	Feb-25-26 A
PRJ-PRE-COS-03	Safety Plan Contractor Revised	10d	Jan-30-26 A	Mar-02-26 A
PRJ-PRE-COS-04	Safety Plan Acceptance	1d	Mar-02-26 A	Mar-02-26 A
Confirm Cable Cut Length		71d	Nov-21-25 A	Mar-27-26 A
PRJ-PRE-CUT-02	Contractor Review and Proposed Cut Length	50d	Nov-21-25 A	Mar-20-26 A
PRJ-PRE-CUT-03	Owner cable cut length acceptance	10d	Feb-16-26 A	Mar-27-26 A
PRJ-PRE-CUT-01	Owner provides cable cut length	0d	Mar-16-26 A	Mar-16-26 A
System Engineering Submittals		176d	Nov-21-25 A	Jul-10-26 A
Electrical Design		68d	Nov-21-25 A	Jul-10-26 A
PRJ-PRE-ELDE-01	Electrical Design Preparation/Submittal	60d	Nov-21-25 A	Feb-10-26 A
PRJ-PRE-ELDE-02	Electrical Design Owner Review	10d	Feb-13-26 A	Jul-07-26 A
PRJ-PRE-ELDE-02.1	Electrical Design Contractor 1st Revision	5d	Jul-08-26 A	Jul-10-26 A
PRJ-PRE-ELDE-03	Electrical Design Acceptance by Owner	1d	Jul-10-26 A	Jul-10-26 A
500kV Power Cable		71d	Nov-21-25 A	Mar-19-26 A
PRJ-PRE-PCBL-01	Base Cable Design Preparation/Submittal	60d	Nov-21-25 A	Feb-10-26 A
PRJ-PRE-PCBL-02	Base Cable Design Owner Review	10d	Feb-13-26 A	Mar-13-26 A
PRJ-PRE-PCBL-03	Base Cable Design Acceptance by Owner	1d	Mar-19-26 A	Mar-19-26 A
500kV Cable Splice		71d	Nov-21-25 A	Feb-28-26 A
PRJ-PRE-SPLC-01	Splice Design Preparation/Submittal	60d	Nov-21-25 A	Feb-10-26 A
PRJ-PRE-SPLC-02	Splice Design Owner Review	10d	Feb-13-26 A	Feb-28-26 A
PRJ-PRE-SPLC-03	Splice Design Acceptance by Owner	1d	Feb-28-26 A	Feb-28-26 A
500kV Outdoor Termination Design		71d	Nov-21-25 A	Mar-19-26 A
PRJ-PRE-OTRM-01	Outdoor Termination Design Preparation/Submittal	60d	Nov-21-25 A	Feb-10-26 A
PRJ-PRE-OTRM-02	Outdoor Termination Design Owner Review	10d	Feb-13-26 A	Mar-13-26 A
PRJ-PRE-OTRM-03	Outdoor Termination Design Acceptance by Owner	1d	Mar-19-26 A	Mar-19-26 A
Other Accessories Design		137d	Nov-21-25 A	May-06-26 A
Racking & Grounding Design (for Splice Vault, Fixed Vaults, Restraint Vaults, Transition Stations)		71d	Nov-21-25 A	Feb-28-26 A
PRJ-PRE-RGRD-01	Racking & Grounding Design Preparation / Sumittal	60d	Nov-21-25 A	Feb-10-26 A
PRJ-PRE-RGRD-02	Racking & Grounding Design Owner Review	10d	Feb-13-26 A	Feb-28-26 A
PRJ-PRE-RGRD-03	Racking & Grounding Design Acceptance by Owner	1d	Feb-28-26 A	Feb-28-26 A
Spring Clamps Design		71d	Nov-21-25 A	Apr-20-26 A
PRJ-PRE-SCD-01	Spring Clamp Design Preparation/Submittal	60d	Nov-21-25 A	Feb-10-26 A
PRJ-PRE-SCD-02	Spring Clamp Design Owner Review	10d	Feb-13-26 A	Apr-15-26 A
PRJ-PRE-SCD-03	Spring Clamp Design Acceptance by Owner	1d	Apr-20-26 A	Apr-20-26 A
Joint Clamp Design		71d	Nov-21-25 A	Apr-20-26 A
PRJ-PRE-JCD-01	Splice Clamp Design Preparation/Submittal	60d	Nov-21-25 A	Feb-10-26 A
PRJ-PRE-JCD-02	Splice Clamp Design Owner Review	10d	Feb-13-26 A	Apr-15-26 A
PRJ-PRE-JCD-03	SpliceClamp Design Acceptance by Owner	1d	Apr-20-26 A	Apr-20-26 A

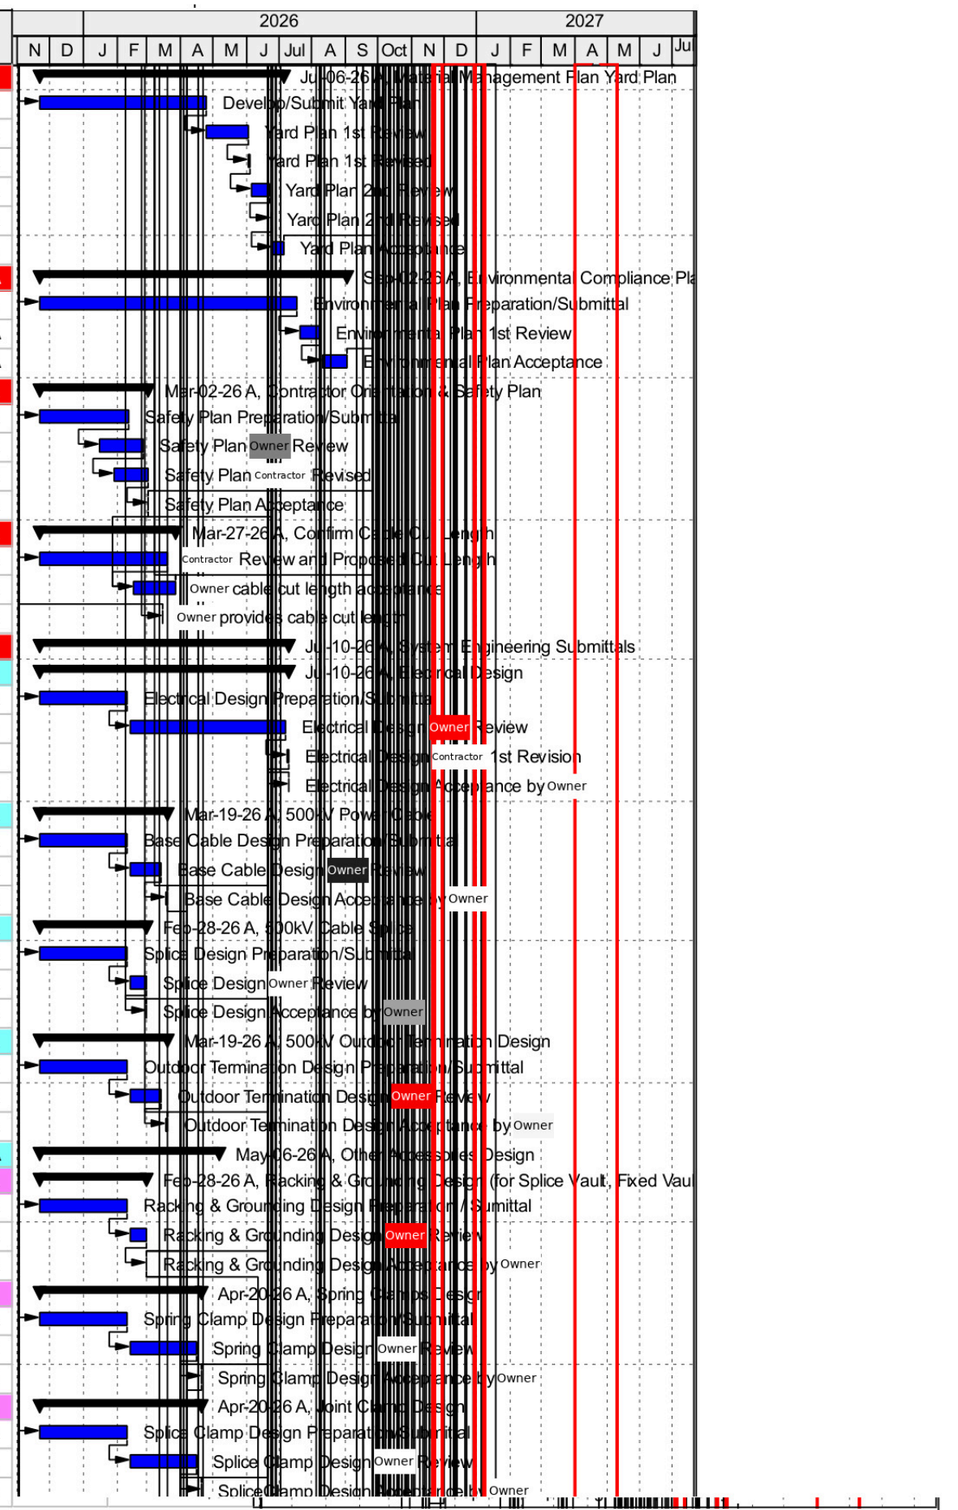


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample 500kV Underground Cable Project Schedule

Engineering, Procurement and Construction - Monthly Progress Schedule

HSE SCHEDULING CONSULTANTS

Activity ID	Activity Name	Original Duration	Start	Finish
Racheting Device Design		71d	Nov-21-25 A	Feb-28-26 A
PRJ-PRE-RDD-01	Ratchet Clamp Design Preparation/Submittal	60d	Nov-21-25 A	Feb-10-26 A
PRJ-PRE-RDD-02	Ratchet Clamp Design Owner Review	10d	Feb-13-26 A	Feb-28-26 A
PRJ-PRE-RDD-03	Ratchet Clamp Design Acceptance by Owner	1d	Feb-28-26 A	Feb-28-26 A
Link-Box Design		71d	Nov-21-25 A	Mar-21-26 A
PRJ-PRE-LBOX-01	Link-Box Design Preparation/Submittal	60d	Nov-21-25 A	Feb-10-26 A
PRJ-PRE-LBOX-02	Link-Box Design Owner Review	10d	Feb-13-26 A	Mar-14-26 A
PRJ-PRE-LBOX-03	Link-Box Design Acceptance by Owner	1d	Mar-21-26 A	Mar-21-26 A
Lightning Arrester Design		137d	Nov-21-25 A	May-06-26 A
PRJ-PRE-LAD-01	Lightning Arrester Preparation/Submittal	60d	Nov-21-25 A	Mar-04-26 A
PRJ-PRE-LAD-02.1	Lightning Arrester Revised and New Proposal	22d	Mar-05-26 A	Mar-27-26 A
PRJ-PRE-LAD-02	Lightning Arrester Owner Review	10d	Mar-28-26 A	May-06-26 A
PRJ-PRE-LAD-03	Lightning Arrester Acceptance by Owner	1d	May-06-26 A	May-06-26 A
Bonding & Ground Continuity Cables Design		109d	Nov-21-25 A	Apr-06-26 A
PRJ-PRE-BGCCD-01	Bonding & Grounding Cable Preparation/Submittal	60d	Nov-21-25 A	Feb-27-26 A
PRJ-PRE-BGCCD-02	Bonding & Grounding Cable Owner Review	10d	Feb-13-26 A	Apr-06-26 A
PRJ-PRE-BGCCD-03	Bonding & Grounding Cable Owner Acceptance by Owner	1d	Apr-06-26 A	Apr-06-26 A
DAS Monitoring System Upgrade Design		123d	Nov-21-25 A	May-12-26 A
PRJ-PRE-DAS-01	DAS Monitoring System Design Preparation/Submittal	60d	Nov-21-25 A	Feb-12-26 A
PRJ-PRE-DAS-02	DAS Monitoring System Design Owner Review	10d	Feb-13-26 A	May-11-26 A
PRJ-PRE-DAS-03	DAS Monitoring System Design Acceptance by Owner	3d	May-12-26 A	May-12-26 A
QA		91d	Nov-21-25 A	Aug-10-26 A
QC Plan for Consturction		91d	Nov-21-25 A	Aug-10-26 A
QC Plan for Shipping & Handling		90d	Nov-21-25 A	Aug-10-26 A
PRJ-PRE-SHIP-01	QA/QC Plan for Field Work (Shipping & Handling) Preparation/Submittal	90d	Nov-21-25 A	Jun-12-26 A
PRJ-PRE-SHIP-02	QA/QC Plan for Field Work (Shipping & Handling) 1st Owner Review	4d	Jun-13-26 A	Jul-22-26 A
PRJ-PRE-SHIP-06	QA/QC Plan for Field Work (Shipping & Handling) Acceptance by Owner	5d	Jul-23-26 A	Aug-10-26 A
QC Plan for Racking & Grounding Installation		91d	Nov-21-25 A	Aug-10-26 A
PRJ-PRE-RGRD-04	QA/QC Plan for Field Work (Racking & Grounding Installation) Preparation/Submittal	90d	Nov-21-25 A	Jun-12-26 A
PRJ-PRE-RGRD-05	QA/QC Plan for Field Work (Racking & Grounding Installation) 1st Owner Review & Approval	4d	Jun-13-26 A	Jul-22-26 A
PRJ-PRE-RGRD-09	QA/QC Plan for Field Work (Racking & Grounding Installation) Acceptance by Owner	5d	Jul-23-26 A	Aug-10-26 A
QC Plan for Cable Installation		90d	Nov-21-25 A	Aug-10-26 A
PRJ-PRE-CINS-01	QA/QC Plan for Field Work (Cable Installation) Preparation/Submittal	90d	Nov-21-25 A	Jun-12-26 A
PRJ-PRE-CINS-02	QA/QC Plan for Field Work (Cable Installation) 1st Owner Review	4d	Jun-13-26 A	Jul-22-26 A
PRJ-PRE-CINS-03	QA/QC Plan for Field Work (Cable Installation) 1st Contractor Revised	5d	Jul-23-26 A	Jul-24-26 A
PRJ-PRE-CINS-06	QA/QC Plan for Field Work (Cable Installation) 2nd Owner Review and Acceptance by Owner	5d	Jul-23-26 A	Aug-10-26 A
QC Plan for Splicing & Termination		90d	Nov-21-25 A	Aug-10-26 A
PRJ-PRE-SPTR-01	QA/QC Plan for Field Work (Splicing & Termination) Preparation/Submittal	90d	Nov-21-25 A	Jun-12-26 A
PRJ-PRE-SPTR-02	QA/QC Plan for Field Work (Splicing & Termination) 1st Owner Review	4d	Jun-13-26 A	Jul-22-26 A
PRJ-PRE-SPTR-06	QA/QC Plan for Field Work (Splicing & Termination) Acceptance by Owner	5d	Jul-23-26 A	Aug-10-26 A
QC Plan for DAS System Upgrade		90d	Nov-21-25 A	Aug-10-26 A
PRJ-PRE-DAS-04	QA/QC Plan for Field Work (DAS System Upgrade) Preparation/Submittal	90d	Nov-21-25 A	Jun-12-26 A
PRJ-PRE-DAS-05	QA/QC Plan for Field Work (DAS System Upgrade) 1st Owner Review	4d	Jun-13-26 A	Jul-22-26 A
PRJ-PRE-DAS-09	QA/QC Plan for Field Work (DAS System Upgrade) Acceptance by Owner	5d	Jul-23-26 A	Aug-10-26 A
QC Plan for Commissioning Test		90d	Nov-21-25 A	Aug-10-26 A
PRJ-PRE-COMM-01	QA/QC Plan for Field Work (Commissioning Test) Preparation/Submittal	90d	Nov-21-25 A	Jun-12-26 A
PRJ-PRE-COMM-02	QA/QC Plan for Field Work (Commissioning Test) 1st Owner Review	4d	Jun-13-26 A	Jul-22-26 A
PRJ-PRE-COMM-03	QA/QC Plan for Field Work (Commissioning Test) 1st Contractor Revised	5d	Jul-23-26 A	Jul-24-26 A
PRJ-PRE-COMM-06	QA/QC Plan for Field Work (Commissioning Test) 2nd Owner Review and Approval	5d	Jul-23-26 A	Aug-10-26 A
Permits		39d	Jul-17-26 A	Aug-31-26 A
Transportation Permits (Cal-Trans)		39d	Jul-17-26 A	Aug-31-26 A

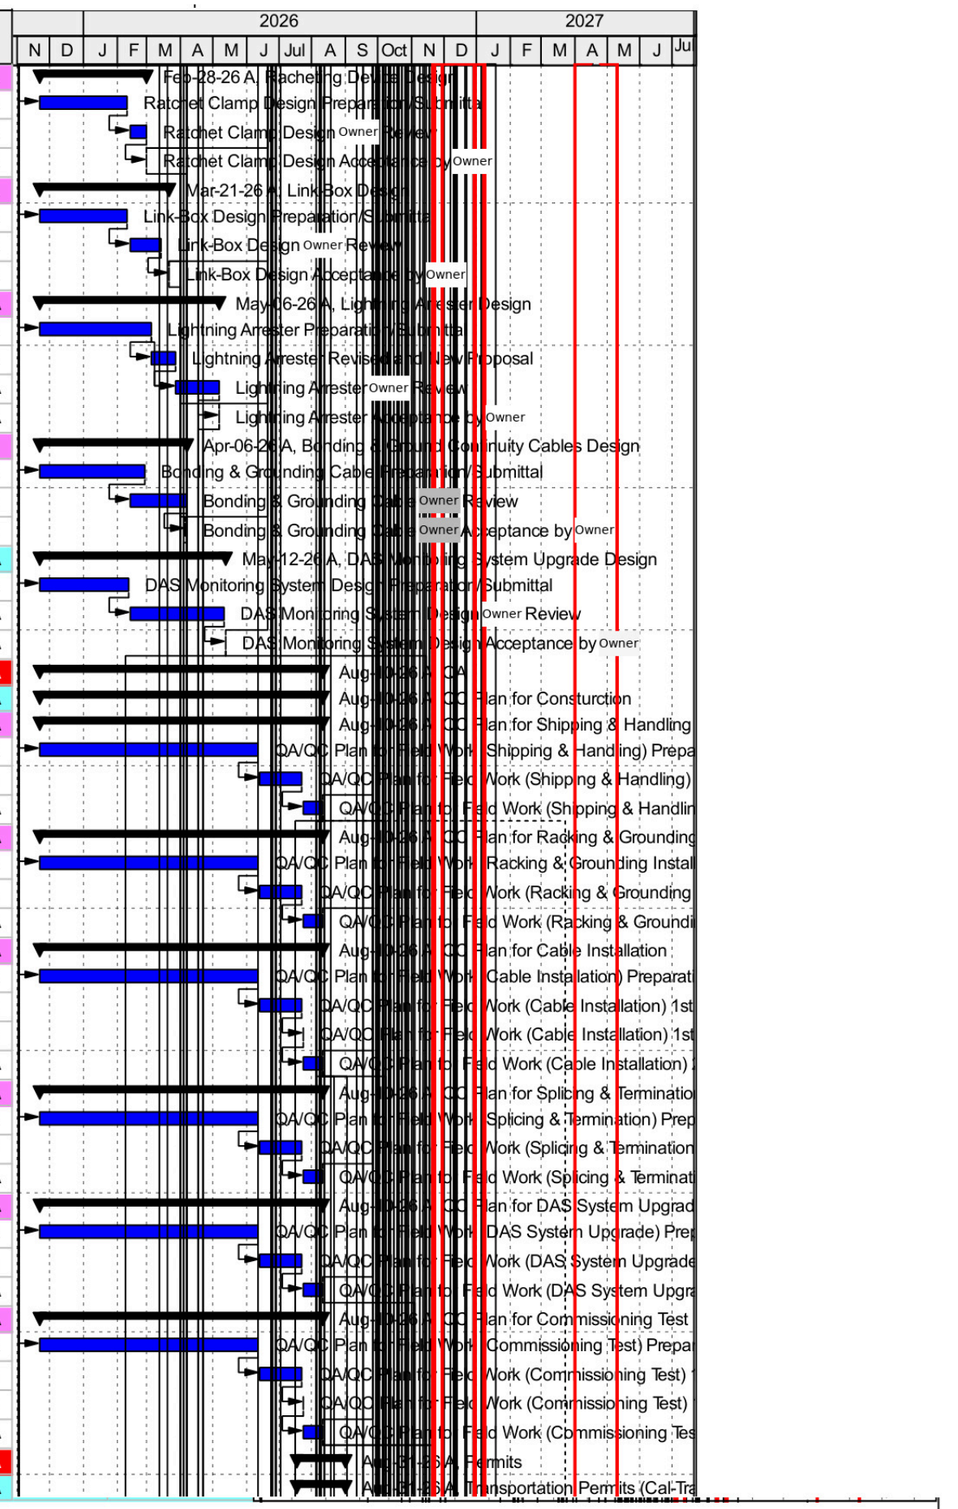

Remaining Level of Effort | Remaining Work | Summary

Actual Level of Effort | Critical Remaining Work


Actual Work | Milestone

Sample 500kV Underground Cable Project Schedule

Engineering, Procurement and Construction - Monthly Progress Schedule

HSE SCHEDULING CONSULTANTS


Activity ID	Activity Name	Original Duration	Start	Finish
PRJ-PRE-TPCT-01	Transportation Permits Preparation	5d	Jul-17-26 A	Aug-25-26 A
PRJ-PRE-TPCT-02	Transportation Permits Review and Approval	5d	Aug-26-26 A	Aug-31-26 A
Procurement Engineering		175d	Nov-21-25 A	Jul-07-26 A
FAT Plan and Procedure for Factory Production		175d	Nov-21-25 A	Jul-07-26 A
FAT Plan and Procedure for_500kV Power Cable		118d	Nov-21-25 A	Jun-09-26 A
PRJ-PRE-PCBL-04	FAT Plan for Power Cable - Contractor Preperation / Submittion	60d	Nov-21-25 A	Feb-10-26 A
PRJ-PRE-PCBL-05	FAT Plan for Power Cable - Owner Review / Approval	10d	Feb-11-26 A	Jun-09-26 A
FAT Plan and Procedure for_Cable Splice		156d	Nov-21-25 A	Jun-09-26 A
PRJ-PRE-SPLC-04	FAT Plan for Cable Splice - Contractor Preperation / Submittion	60d	Nov-21-25 A	Feb-10-26 A
PRJ-PRE-SPLC-05	FAT Plan for Cable Splice - Owner Review / Approval	10d	Feb-11-26 A	Jun-09-26 A
PRJ-PRE-SPLC-04.1	FAT Plan for Cable Splice - Owner review	5d	Feb-11-26 A	Jun-04-26 A
PRJ-PRE-SPLC-04.2	FAT Plan for Cable Splice - Contractor revised	5d	Jun-05-26 A	Jun-08-26 A
FAT Plan and Procedure for_Outdoor Termination		146d	Nov-21-25 A	Jun-09-26 A
PRJ-PRE-OTRM-04	FAT Plan for Outdoor Termination - Contractor Preperation / Submittion	60d	Nov-21-25 A	Feb-10-26 A
PRJ-PRE-OTRM-05	FAT Plan for Outdoor Termination - Owner Review / Approval	10d	Feb-11-26 A	Jun-09-26 A
PRJ-PRE-OTRM-04.1	FAT Plan for Outdoor Termination - Owner review	5d	Feb-11-26 A	Jun-04-26 A
PRJ-PRE-OTRM-04.2	FAT Plan for Outdoor Termination - Contractor Revised	5d	Jun-05-26 A	Jun-08-26 A
FAT Plan and Procedure for_Cable and Joint Rackings (Ratchet Device, Spings Clamps, Joint Clamps)		118d	Nov-21-25 A	Jun-30-26 A
PRJ-PRE-FAPRCA-01	FAT Plan for Cable and Splice Clamps - Contractor Preperation / Submittion	60d	Nov-21-25 A	Feb-10-26 A
PRJ-PRE-FAPRCA-02	FAT Plan for Cable and Splice Clamps - Owner Review / Approval	10d	Feb-11-26 A	Jun-30-26 A
FAT Plan and Procedure for_Bonding & Grounding Continuity Cables		118d	Nov-21-25 A	Jun-30-26 A
PRJ-PRE-FPBGCC-01	FAT Plan for Bonding & Grounding Continuity - Contractor Preperation / Submittion	60d	Nov-21-25 A	Feb-25-26 A
PRJ-PRE-FPBGCC-02	FAT Plan for Bonding & Grounding Continuity - Owner Review / Approval	10d	Feb-11-26 A	Jun-30-26 A
FAT Plan and Procedure for_Link-Box		175d	Nov-21-25 A	Jul-07-26 A
PRJ-PRE-LBOX-04	FAT Plan for Link Box - Contractor Preperation / Submittion	60d	Nov-21-25 A	Feb-10-26 A
PRJ-PRE-LBOX-05	FAT Plan for Link Box - 1st Owner Review	10d	Feb-11-26 A	Jun-30-26 A
PRJ-PRE-LBOX-6	FAT Plan for Link Box - 1st Contractor Reivision	5d	Jul-01-26 A	Jul-07-26 A
PRJ-PRE-LBOX-7	FAT Plan for Link Box - Owner Review and Approval	5d	Jul-07-26 A	Jul-07-26 A
Field Test QAQC Plan		90d	Nov-21-25 A	Aug-11-26 A
PRJ-PRE-FTQP-01	Field Test QA/QC Preparation/Submittal	90d	Nov-21-25 A	Jun-12-26 A
PRJ-PRE-FTQP-02	Field Test QA/QC 1st Owner Review	10d	Jun-13-26 A	Jul-22-26 A
PRJ-PRE-FTQP-03	Field Test QA/QC 1st Contractor Revised	10d	Jul-23-26 A	Jul-24-26 A
PRJ-PRE-FTQP-04	Field Test QA/QC 2nd Owner Review	5d	Jul-27-26 A	Aug-03-26 A
PRJ-PRE-FTQP-05	Field Test QA/QC 2nd Contractor Revised	5d	Aug-04-26 A	Aug-08-26 A
PRJ-PRE-FTQP-06	Field Test QA/QC 3rd Owner Review and Approval	2d	Aug-10-26 A	Aug-11-26 A
Procurement		258d	Feb-28-26 A	Apr-16-27
Material Manufacturing		233d	Feb-28-26 A	Mar-13-27
Manufacturing of 500kV Power Cables		110d	Apr-27-26 A	Jun-30-26 A
PRJ-PRC-PCBL-04	Manufacturing of Power Cable	110d	Apr-27-26 A	Jun-30-26 A
Manufacturing of 500kV Cable Splices		115d	Apr-20-26 A	Jun-05-26 A
PRJ-PRC-SPLC-04	Manufacturing of Cable Splices	115d	Apr-20-26 A	Jun-05-26 A
Manufacturing of 500kV Outdoor Terminations		115d	Apr-01-26 A	Jun-16-26 A
PRJ-PRC-OTRM-03	Manufacturing of Outdoor Termination	115d	Apr-01-26 A	Jun-16-26 A
Manufacturing of Other Accessories		233d	Apr-20-26 A	Mar-13-27
PRJ-PRC-MOA-05	Manufacturing of Link-Box	115d	Apr-20-26 A	Jun-20-26 A
PRJ-PRC-MOA-06	Manufacturing of Bonding & Grounding Cable	29d	Apr-24-26 A	Jun-01-26 A
PRJ-PRC-MOA-02	Manufacturing of Spring Clamps	115d	Apr-27-26 A	Jun-10-26 A
PRJ-PRC-MOA-03	Manufacturing of Splice Clamps	115d	Apr-27-26 A	Jul-10-26 A
PRJ-PRC-MOA-04	Manufacturing of Ratchet Devices	115d	Apr-27-26 A	Jul-10-26 A
PRJ-PRC-MOA-01	Manufacturing of Racking Materials	55d	May-07-26 A	Jun-30-26 A
PRJ-PRC-MOA-07.1	Manufacturing of Surge Arresters - Higher Rating (instock)	1d	May-07-26 A	May-07-26 A

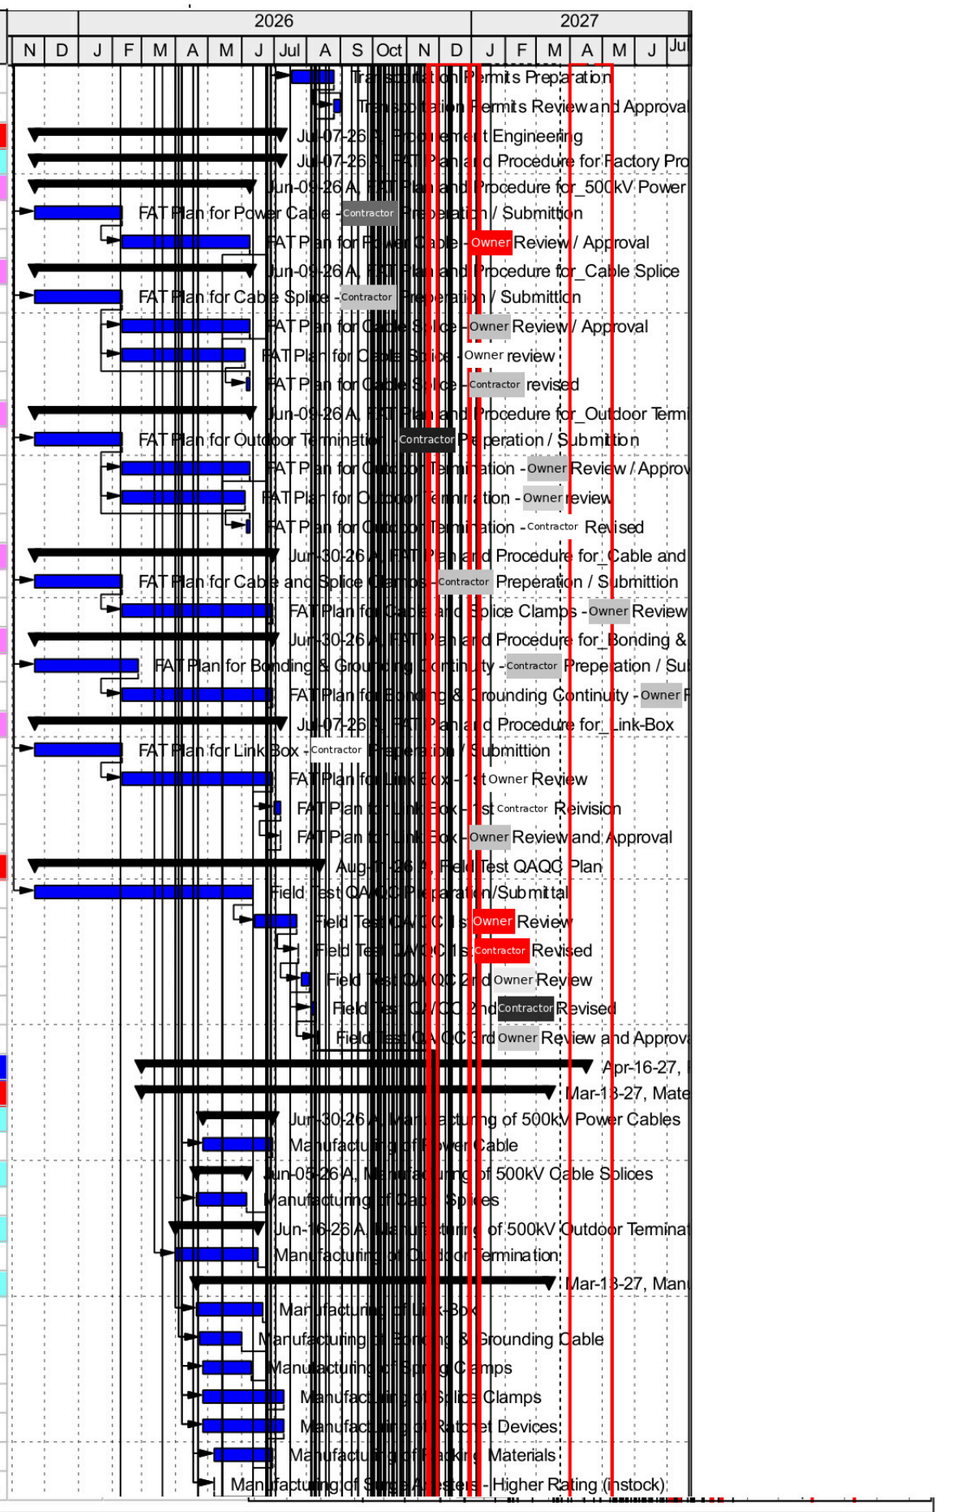

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Website Portfolio Sample

Activity ID	Activity Name	Original Duration	Start	Finish
PRJ-PRC-MOA-07	Manufacturing of Spare Surge Arresters - Higher Rating	308d	May-11-26 A	Mar-13-27
Manufacturing of DAS Monitoring System (FO Cables, Coaxial Cables, HFCT & LFCT Sensors)		35d	Feb-28-26 A	Oct-25-26
PRJ-PRC-DAS-01	Preperation for Manufacturing	6d	Feb-28-26 A	Mar-09-26 A
PRJ-PRC-DAS-02	Manufacturing DAS Monitoring System	35d	Mar-10-26 A	Oct-25-26
Factory Audit Test for Factory Production		71d	Jun-02-26 A	Oct-12-26
FAT_500 kV Power Cables		9d	Jun-02-26 A	Jul-16-26 A
PRJ-PRC-PCBL-05	Notification of FAT for Power Cable	1d	Jun-02-26 A	Jul-02-26 A
PRJ-PRC-PCBL-06	FAT for Power Cable (require Owner witness)	3d	Jul-14-26 A	Jul-16-26 A
FAT_500 kV Cable Splices		11d	Jun-02-26 A	Jul-16-26 A
PRJ-PRC-SPLC-05	Notification of FAT for Cable Splices	8d	Jun-02-26 A	Jun-02-26 A
PRJ-PRC-SPLC-06	FAT for Splices (require Owner witness)	3d	Jul-14-26 A	Jul-16-26 A
FAT_500 kV Outdoor Terminations		11d	Jun-02-26 A	Jul-16-26 A
PRJ-PRC-OTRM-04	Notification of FAT for Outdoor Termination	8d	Jun-02-26 A	Jun-02-26 A
PRJ-PRC-OTRM-05	FAT for Outdoor Terminations (require Owner witness)	3d	Jul-14-26 A	Jul-16-26 A
FAT_Other Accessories		8d	Jul-14-26 A	Jul-16-26 A
PRJ-PRC-FOA-01	FAT for Link-Box+SVLs	3d	Jul-14-26 A	Jul-16-26 A
PRJ-PRC-FOA-02	FAT for Spring Clamp	3d	Jul-14-26 A	Jul-16-26 A
PRJ-PRC-FOA-03	FAT for Ratchet Clamp	3d	Jul-14-26 A	Jul-16-26 A
PRJ-PRC-FOA-05	FAT for Splice Clamp	3d	Jul-14-26 A	Jul-16-26 A
PRJ-PRC-FOA-06	FAT for Bonding & Grounding Cable	3d	Jul-14-26 A	Jul-16-26 A
Type Test		40d	Jul-14-26 A	Oct-12-26
PRJ-PRC-TYTE-01	Cable System Type Test	40d	Jul-14-26 A	Oct-12-26
Shipping & Delivery of the Materials		196d	Jul-01-26 A	Apr-16-27
Shipping & Delivery of 500kV Power Cables		53d	Jul-17-26 A	Sep-30-26
PRJ-PRC-PCBL-01	Preperation for Shipping & Delivery from Overseas (Power Cable)	7d	Jul-17-26 A	Jul-25-26 A
PRJ-PRC-PCBL-02	Ocean Shipping of Power Cable to Regional Port (Power Cable) - 1st Batch (9 reels, 13,718 ft)	21d	Jul-26-26 A	Aug-21-26 A
PRJ-PRC-PCBL-02.1	Ocean Shipping of Power Cable to Regional Port (Power Cable) - 2nd Batch (Remainings)	13d	Aug-14-26 A	Aug-28-26 A
PRJ-PRC-PCBL-03	Land Transport from Regional Port to Laydown Yard (Power Cable) - 1st Batch (9 reels, 13,718 ft)	5d	Aug-27-26 A	Aug-28-26 A
PRJ-PRC-PCBL-03.1	Land Transport from Regional Port to Laydown Yard (Power Cable) - 2nd Batch (Remainigs)	23d	Aug-31-26 A	Sep-30-26
Shipping & Delivery of 500kV Cable Splices		31d	Jul-17-26 A	Aug-28-26 A
PRJ-PRC-SPLC-01	Preperation for Shipping & Delivery from Overseas (Splice)	5d	Jul-17-26 A	Jul-25-26 A
PRJ-PRC-SPLC-02	Ocean Shipping of Power Cable to Regional Port (Splice)	21d	Jul-26-26 A	Aug-21-26 A
PRJ-PRC-SPLC-03	Land Transport from Regional Port to Laydown Yard (Splice)	5d	Aug-24-26 A	Aug-28-26 A
Shipping & Delivery of 500kV Outdoor Terminations		31d	Jul-17-26 A	Aug-28-26 A
PRJ-PRC-OTRM-01	Preperation for Shipping & Delivery from Overseas (Termination)	5d	Jul-17-26 A	Jul-25-26 A
PRJ-PRC-OTRM-02	Ocean Shipping of Power Cable to Regional Port (Termination)	22d	Jul-26-26 A	Aug-21-26 A
PRJ-PRC-OTRM-06	Land Transport from Regional Port to Laydown Yard (Outdoor terminations)	5d	Aug-24-26 A	Aug-28-26 A
Shipping & Delivery of 500kV Surge Arrestors		25d	Jul-17-26 A	Aug-11-26 A
PRJ-PRC-SDSA-01	Preperation for Shipping & Delivery (Arrester)	10d	Jul-17-26 A	Aug-03-26 A
PRJ-PRC-SDSA-03	Land Transport from Regional Port to Laydown Yard (Arrester)	5d	Aug-04-26 A	Aug-11-26 A
Shipping & Delivery of 500kV Surge Arrestors (Spare)		25d	Mar-14-27	Apr-16-27
PRJ-PRC-SDSA-S-01	Preperation for Shipping & Delivery (Spare Arrester)	5d	Mar-14-27	Mar-18-27
PRJ-PRC-SDSA-S-02	Ocean Shipping of Power Cable to Regional Port (Spare Arrester)	22d	Mar-19-27	Apr-09-27
PRJ-PRC-SDSA-S-03	Land Transport from Regional Port to Owner Storage Facility (Spare Arrester)	5d	Apr-12-27	Apr-16-27
Shipping & Delivery of Cable Clamps (Spring Clamps, Racheting Devie, Joint Clamp, etc)		24d	Jul-17-26 A	Aug-26-26 A
PRJ-PRC-SHDECA-01	Preperation for Shipping & Delivery from Overseas (Clamp)	6d	Jul-17-26 A	Jul-25-26 A
PRJ-PRC-SHDECA-02	Ocean Shipping of Cable Clamp to Regional Port (Clamp)	22d	Jul-26-26 A	Aug-21-26 A
PRJ-PRC-SHDECA-03	Land Transport from Regional Port to Laydown Yard (Clamp)	5d	Aug-24-26 A	Aug-26-26 A
Shipping & Delivery of Racking & Grounding Materials		21d	Jul-01-26 A	Jul-20-26 A
PRJ-PRC-RGRD-01	Preperation for Shipping & Delivery (Racking & Grounding Materials)	10d	Jul-01-26 A	Jul-13-26 A
PRJ-PRC-RGRD-02	Delivery to Laydown Yard (Racking & Grounding Materials)	5d	Jul-14-26 A	Jul-20-26 A

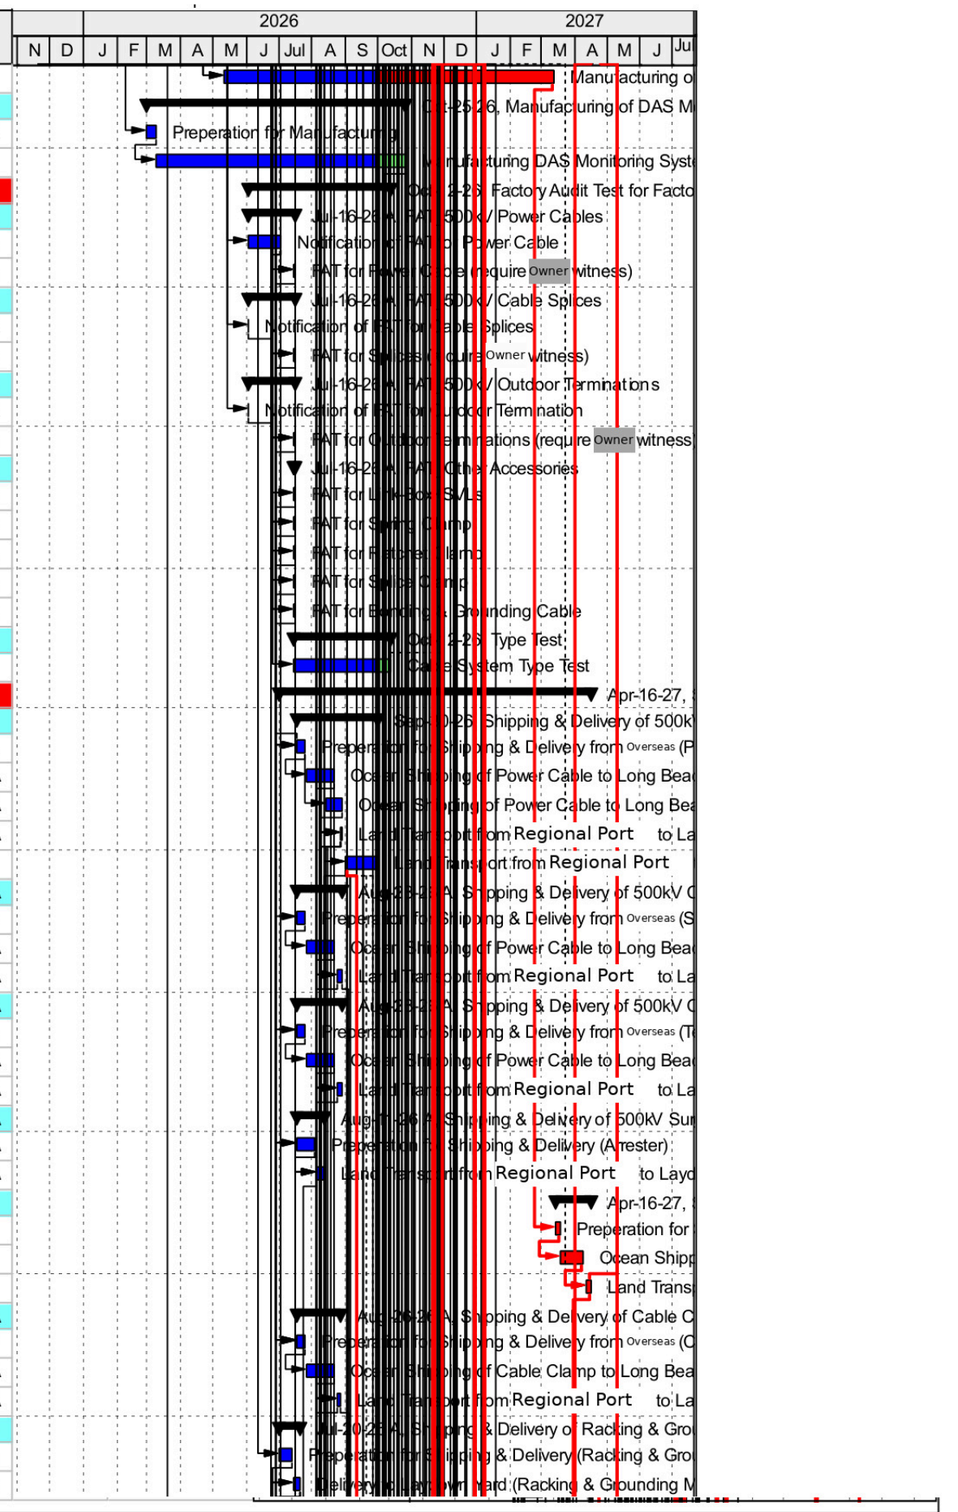


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample 500kV Underground Cable Project Schedule

Engineering, Procurement and Construction - Monthly Progress Schedule


HSE SCHEDULING CONSULTANTS

Activity ID	Activity Name	Original Duration	Start	Finish
Shipping & Delivery of Bonding & Grounding Continuity Cables		31d	Jul-17-26 A	Aug-24-26 A
PRJ-PRC-SDBGCC-01	Preperation for Shipping & Delivery from Overseas (Bonding ang Grounding Cable)	10d	Jul-17-26 A	Jul-25-26 A
PRJ-PRC-SDBGCC-02	Ocean Shipping of Power Cable to Regional Port (Bonding ang Grounding Cable)	22d	Jul-26-26 A	Aug-21-26 A
PRJ-PRC-SDBGCC-03	Land Transport from Regional Port to Laydown Yard (Bonding ang Grounding Cable)	5d	Aug-24-26 A	Aug-24-26 A
Shipping & Delivery of Link-Box		24d	Jul-17-26 A	Aug-28-26 A
PRJ-PRC-LBOX-01	Preperation for Shipping & Delivery from Overseas (Link-Box)	6d	Jul-17-26 A	Jul-25-26 A
PRJ-PRC-LBOX-02	Ocean Shipping of Power Cable to Regional Port (Link-Box)	22d	Jul-26-26 A	Aug-21-26 A
PRJ-PRC-LBOX-03	Land Transport from Regional Port to Laydown Yard (Link-Box)	5d	Aug-24-26 A	Aug-28-26 A
Shipping & Delivery of DAS Monitoring System (FO Cables, Coaxial Cables, HFCT & LFCT Sensors)		18d	Oct-26-26	Nov-18-26
PRJ-PRC-DAS-03	Preperation for Shipping & Delivery (DAS Monitoring)	2d	Oct-26-26	Oct-27-26
PRJ-PRC-DAS-05	Ocean Shipping of Power Cable to Regional Port (DAS)	20d	Oct-28-26	Nov-16-26
PRJ-PRC-DAS-04	Delivery to Laydown Yard (DAS Monitoring)	2d	Nov-17-26	Nov-18-26
Construction		241d	Apr-09-26 A	Apr-20-27
Outage Request		179d	Apr-09-26 A	Dec-30-26
PRJ-CON-OUTG-2	Outage Coordination Meeting	1d	Jul-22-26 A	Jul-22-26 A
PRJ-CON-OUTG-1	Outage Coordination / Planned Window for outage subcircuit 1 & 2	59d	Oct-13-26*	Dec-30-26
Induced Voltage Mitigation Plan / Additional Grounding Plan for Working Under Live Induction		130d	Apr-09-26 A	Sep-23-26 A
PRJ-CON-IND-1	Initial Notification for Requesting Owner's Review on Working under Live Induction	1d	Apr-09-26 A	May-19-26 A
PRJ-CON-IND-2	Owner Review and Requesting Contractor to Submit Detail Grounding Plan to reference IEEE1727	10d	May-20-26 A	Aug-18-26 A
PRJ-CON-IVMP-01	Induced Voltage Mitigation Plan - Preparation & Initial Submission	4d	Aug-19-26 A	Aug-22-26 A
PRJ-CON-IVMP-02	Induced Voltage Mitigation Plan - Owner Review / Comment Resolution	26d	Aug-24-26 A	Sep-22-26 A
PRJ-CON-IVMP-03	Induced Voltage Mitigation Plan - Final Approval	0d		Sep-23-26 A
Cable Installation - Induced Voltage Mitigation Plan		75d	Aug-19-26 A	Sep-09-26 A
PRJ-CON-CI-IND-01	Cable Installation Grounding & Induction Measurement & verification Plan - Contractor Initial Submition	10d	Aug-19-26 A	Aug-22-26 A
PRJ-CON-CI-IND-02	Cable Installation Grounding & Induction Measurement & verification Plan - Owner 1st Review	10d	Aug-24-26 A	Aug-24-26 A
PRJ-CON-CI-IND-03	Cable Installation Grounding & Induction Measurement & verification Plan - Contractor 2nd Submittal	10d	Aug-25-26 A	Aug-25-26 A
PRJ-CON-CI-IND-04	Cable Installation Grounding & Induction Measurement & verification Plan - Owner 2nd Review and Approved	10d	Aug-26-26 A	Aug-27-26 A
PRJ-CON-CI-IND-05	Cable Installation Grounding & Induction Measurement & verification Plan - Contractor 3rd Revision	10d	Aug-28-26 A	Aug-31-26 A
PRJ-CON-CI-IND-06	Cable Installation Grounding & Induction Measurement & verification Plan - Owner 3rd Review	1d	Sep-01-26 A	Sep-02-26 A
PRJ-CON-CI-IND-07	Cable Installation Grounding & Induction Measurement & verification Plan - Contractor 4th Revision	1d	Sep-03-26 A	Sep-04-26 A
PRJ-CON-CI-IND-08	Cable Installation Grounding & Induction Measurement & verification Plan - Owner 4th Review and Approval	1d	Sep-04-26 A	Sep-09-26 A
Cable Splicing - Induced Voltage Mitigation Plan		75d	Aug-19-26 A	Sep-23-26 A
PRJ-CON-CS-IND-01	Cable Splicing Grounding & Induction Measurement & verification Plan - Contractor Initial Submition	10d	Aug-19-26 A	Aug-22-26 A
PRJ-CON-CS-IND-02	Cable Splicing Grounding & Induction Measurement & verification Plan - Owner 1st Review	10d	Aug-24-26 A	Aug-24-26 A
PRJ-CON-CS-IND-03	Cable Splicing Grounding & Induction Measurement & verification Plan - Contractor 2nd Submittal	3d	Aug-28-26 A	Sep-17-26 A
PRJ-CON-CS-IND-04	Cable Splicing Grounding & Induction Measurement & verification Plan - Owner 2nd Review and Approval	3d	Sep-18-26 A	Sep-23-26 A
Mobilization & Material Receiving Inspection		11d	Jul-13-26 A	Jul-28-26 A
PRJ-CON-MOB-05	Mobilization	5d	Jul-13-26 A	Jul-17-26 A
PRJ-CON-MOB-06	Establishment of the Laydown Yard	10d	Jul-14-26 A	Jul-28-26 A
Pre- Racking & Grounding Installation (1 crew)		50d	Jul-20-26 A	Sep-18-26 A
PRJ-CON-RGRD-02	Cable Racking S/V#14	2d	Jul-20-26 A	Jul-22-26 A
PRJ-CON-RGRD-01	Cable Racking at ETS	5d	Jul-23-26 A	Jul-24-26 A
PRJ-CON-RGRD-03	Cable Racking S/V#13	2d	Jul-27-26 A	Jul-28-26 A
PRJ-CON-RGRD-04	Cable Racking S/V#12	2d	Jul-29-26 A	Jul-29-26 A
PRJ-CON-RGRD-05	Cable Racking S/V#11	2d	Jul-30-26 A	Jul-31-26 A
PRJ-CON-RGRD-06	Cable Racking S/V#10 (fixed)	1d	Aug-01-26 A	Aug-04-26 A
PRJ-CON-RGRD-07	Cable Racking S/V#9	2d	Aug-04-26 A	Aug-05-26 A
PRJ-CON-RGRD-08	Cable Racking S/V#8	2d	Aug-05-26 A	Aug-07-26 A
PRJ-CON-RGRD-09	Cable Racking R/V#6	1d	Aug-07-26 A	Aug-08-26 A
PRJ-CON-RGRD-10	Cable Racking S/V#7	2d	Aug-07-26 A	Aug-11-26 A

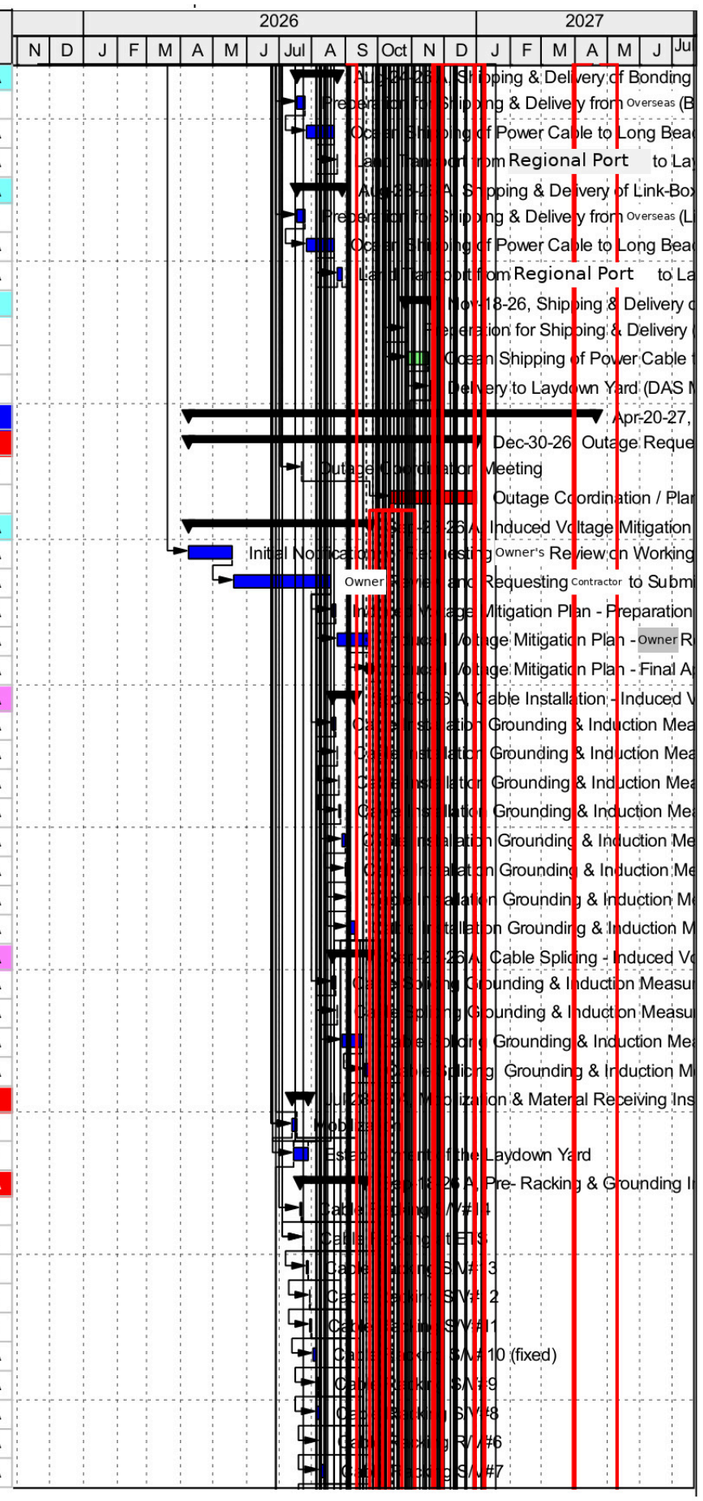

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish
PRJ-CON-RGRD-13	Cable Racking S/V#5	2d	Aug-07-26 A	Aug-08-26 A
PRJ-CON-RGRD-12	Cable Racking R/V#5	1d	Aug-10-26 A	Aug-11-26 A
PRJ-CON-RGRD-15	Cable Racking S/V#4	2d	Aug-11-26 A	Aug-13-26 A
PRJ-CON-RGRD-14	Cable Racking R/V#4	1d	Aug-12-26 A	Aug-13-26 A
PRJ-CON-RGRD-19	Cable Racking WTS	5d	Aug-13-26 A	Aug-14-26 A
PRJ-CON-RGRD-21	Cable Racking R/V#1	1d	Aug-18-26 A	Sep-18-26 A
PRJ-CON-RGRD-18	Cable Racking R/V#2	2d	Aug-19-26 A	Aug-19-26 A
PRJ-CON-RGRD-20	Cable Racking S/V#1	2d	Aug-19-26 A	Aug-20-26 A
PRJ-CON-RGRD-16	Cable Racking R/V#3	1d	Aug-20-26 A	Aug-20-26 A
PRJ-CON-RGRD-11	Cable Racking S/V#6 (fixed)	2d	Aug-21-26 A	Aug-25-26 A
PRJ-CON-RGRD-17	Cable Racking S/V#3 (Fixed)	2d	Aug-26-26 A	Aug-31-26 A
PRJ-CON-RGRD-22	Cable Racking S/V#2 (Site Constraint)	2d	Sep-15-26 A	Sep-17-26 A
Clean and Prove Ducts (1 crew)		50d	Aug-24-26 A	Oct-27-26
PRJ-CON-CPDC-02	Clean and Proof S/V#13 - S/V#14	1d	Aug-24-26 A	Aug-24-26 A
PRJ-CON-CPDC-03	Clean and Proof S/V#12 - S/V#13	1d	Sep-15-26 A	Sep-17-26 A
PRJ-CON-CPDC-04	Clean and Proof S/V#11 - S/V#12	1d	Sep-21-26 A	Sep-23-26 A
PRJ-CON-CPDC-08	Clean and Proof S/V#5 - R/V#5 - S/V#6 (fixed) - S/V#7	2d	Sep-25-26 A	Sep-28-26 A
PRJ-CON-CPDC-09	Clean and Proof S/V#4 - R/V#4 - S/V#5	1d	Sep-30-26 A	Sep-30-26
PRJ-CON-CPDC-05	Clean and Proof S/V#9 - S/V#10 (fixed) - S/V#11	2d	Oct-03-26	Oct-05-26
PRJ-CON-CPDC-06	Clean and Proof S/V#8 - S/V#9	1d	Oct-07-26	Oct-07-26
PRJ-CON-CPDC-07	Clean and Proof S/V#7 - R/V#6 - S/V#8	1d	Oct-10-26	Oct-10-26
PRJ-CON-CPDC-13	Clean and Prove S/V#2 - R/V#2 - S/V#3 - R/V#3 - S/V#4(fixed) |Site Constraint|	2d	Oct-15-26	Oct-16-26
PRJ-CON-CPDC-12	Clean and Prove S/V#1 - R/V#1 - S/V#2 |Site Constraint|	2d	Oct-20-26	Oct-21-26
PRJ-CON-CPDC-11	Clean and Proof WTS to S/V#1	1d	Oct-23-26	Oct-23-26
PRJ-CON-CPDC-01	Clean and Proof S/V#14 - ETS	1d	Oct-27-26	Oct-27-26
Cable Installation & 2nd Stage Racking(1 crew)		39d	Sep-10-26 A	Nov-02-26
PRJ-CON-CINS-02	Install Cable S/V#13 - S/V#14	3d	Sep-10-26 A	Sep-12-26 A
PRJ-CON-CINS-03	Install Cable S/V#12 - S/V#13	3d	Sep-15-26 A	Sep-17-26 A
PRJ-CON-CINS-04	Install Cable S/V#11 - S/V#12	3d	Sep-21-26 A	Sep-23-26 A
PRJ-CON-CINS-08	Install Cable S/V#5 - R/V#5 - S/V#6 (fixed) - S/V#7	3d	Sep-25-26 A	Sep-28-26 A
PRJ-CON-CINS-09	Install Cable S/V#4 - R/V#4 - S/V#5	3d	Sep-30-26 A	Oct-02-26
PRJ-CON-CINS-05	Install Cable S/V#9 - S/V#10 (fixed) - S/V#11	3d	Oct-03-26	Oct-06-26
PRJ-CON-CINS-06	Install Cable S/V#8 - S/V#9	3d	Oct-07-26	Oct-09-26
PRJ-CON-CINS-07	Install Cable S/V#7 - R/V#6 - S/V#8	3d	Oct-12-26	Oct-14-26
PRJ-CON-CINS-12	Install Cable S/V#2 |Site Constraint| - R/V#2 - S/V#3 (fixed) - R/V#3 - S/V#4	3d	Oct-16-26	Oct-19-26
PRJ-CON-CINS-11	Install Cable S/V#1 - R/V#1 - S/V#2 |Site Constraint|	3d	Oct-20-26	Oct-22-26
PRJ-CON-CINS-10	Install Cable WTS to S/V#1	3d	Oct-23-26	Oct-26-26
PRJ-CON-CINS-01	Install Cable S/V#14 - ETS	3d	Oct-27-26	Oct-29-26
PRJ-CON-SCN-065	Install Surge Arrester - WTS	2d	Oct-27-26	Oct-28-26
PRJ-CON-SCN-145	Install Surge Arrester - ETS	2d	Oct-30-26	Nov-02-26
Install Cable Splicing & Termination with Final Racking (3 crews -Work Plan		59d	Sep-23-26 A	Dec-09-26
Splicing Crew No.1		53d	Oct-03-26	Dec-09-26
PRJ-CON-SCN-11	Install Cable Splicing - S/V#5 (Preperation up to XLPE Smoothing)	5d	Oct-03-26	Oct-08-26
PRJ-CON-SCN-11.01	Install Cable Splicing - S/V#5 (Complete Splicing)	5d	Oct-13-26	Oct-17-26
PRJ-CON-SCN-03	Install Cable Splicing - S/V#9	10d	Oct-19-26	Oct-29-26
PRJ-CON-SCN-10	Install Cable Splicing - S/V#8	10d	Oct-30-26	Nov-10-26
PRJ-CON-SCN-04	Install Cable Splicing - S/V#7	10d	Nov-11-26	Nov-21-26
PRJ-CON-SCN-07	Install Cable Splicing - S/V#2 (Site Constraint)	10d	Nov-23-26	Dec-09-26
Splicing Crew No.2		65d	Sep-23-26 A	Dec-09-26
PRJ-CON-SCN-08	Install Cable Splicing - S/V#13 (Preperation up to XLPE Smoothing)	5d	Sep-23-26 A	Sep-29-26 A

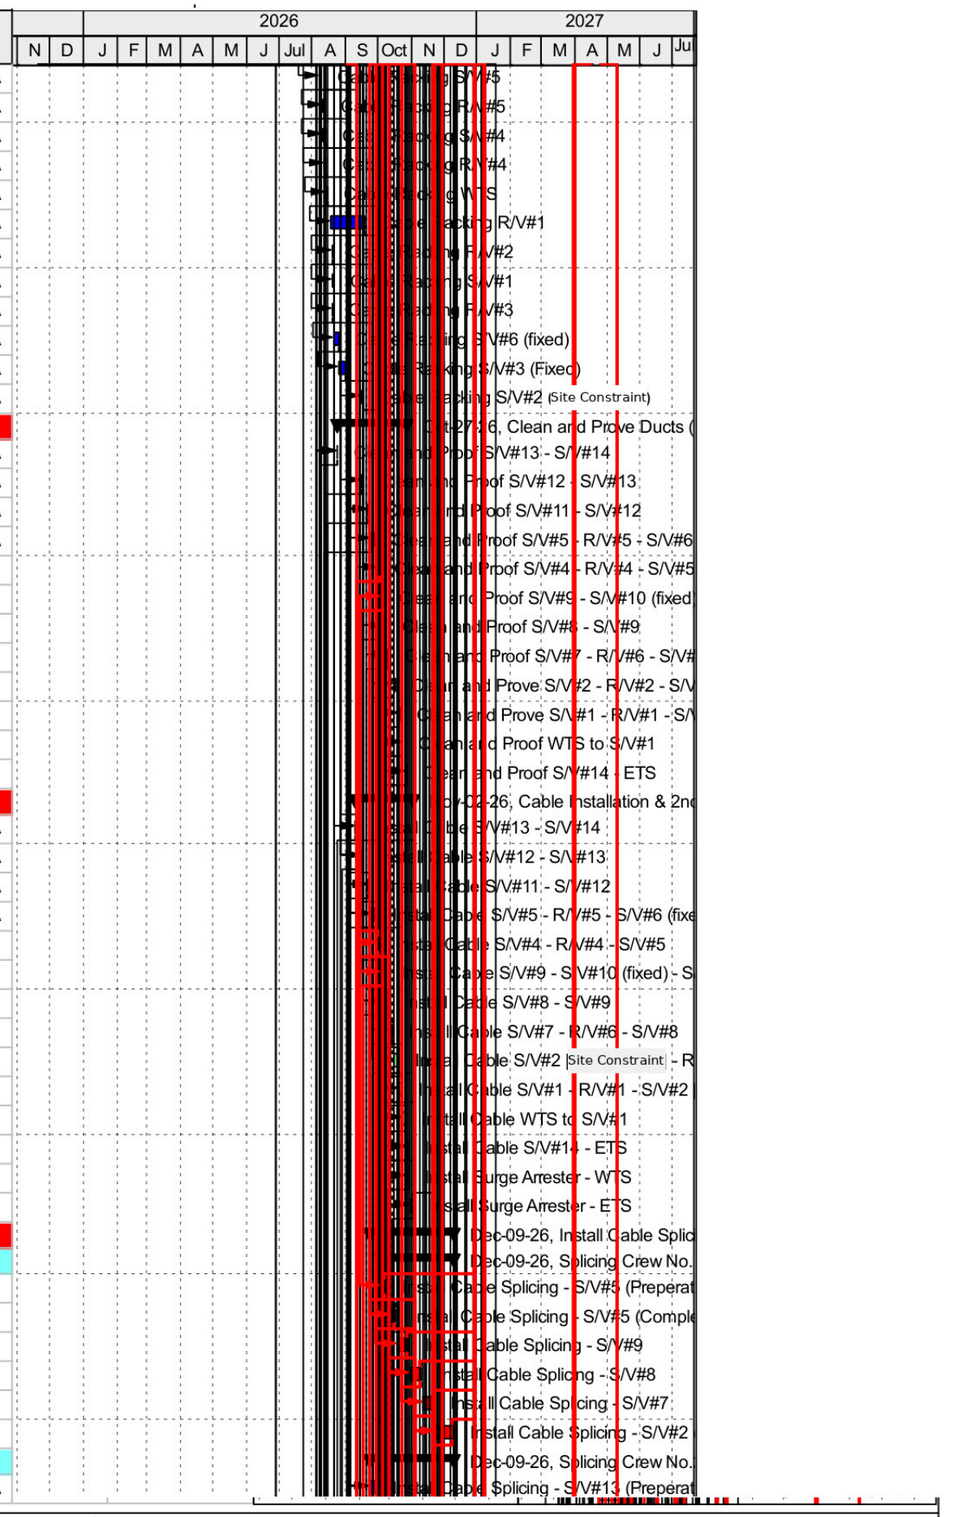


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample 500kV Underground Cable Project Schedule

Engineering, Procurement and Construction - Monthly Progress Schedule

HSE SCHEDULING CONSULTANTS

Activity ID	Activity Name	Original Duration	Start	Finish
PRJ-CON-SCN-02	Install Cable Splicing - S/V#12 (Preperation up to XLPE Smoothing)	5d	Sep-30-26 A	Oct-05-26
PRJ-CON-SCN-09	Install Cable Splicing - S/V#11 (Preperation up to XLPE Smoothing)	5d	Oct-07-26	Oct-12-26
PRJ-CON-SCN-09.01	Install Cable Splicing - S/V#11 (Complete Spicing)	5d	Oct-13-26	Oct-17-26
PRJ-CON-SCN-08.01	Install Cable Splicing - S/V#13 (Complete Splicing)	5d	Oct-19-26	Oct-23-26
PRJ-CON-SCN-02.01	Install Cable Splicing - S/V#12 (Complete Splicing)	5d	Oct-24-26	Oct-29-26
PRJ-CON-SCN-05	Install Cable Splicing - S/V#4	10d	Oct-30-26	Nov-10-26
PRJ-CON-SCN-13	Install Cable Splicing - S/V#1	10d	Nov-11-26	Nov-21-26
PRJ-CON-SCN-1	Install Cable Splicing - S/V#14	10d	Nov-23-26	Dec-09-26
Splicing Crew No.3 - Work Plan		26d	Oct-27-26	Dec-01-26
PRJ-CON-SCN-MOB3	Mobilize 3rd Splicing Crew - Site Induction, Tools & Workfront Readiness	3d	Oct-27-26	Oct-29-26
PRJ-CON-SCN-06	Install Cable Termination - WTS	10d	Nov-03-26	Nov-13-26
PRJ-CON-SCN-12	Install Cable Splicing - ETS	10d	Nov-14-26	Dec-01-26
List of Utility **Work**		34d	Sep-30-26	Nov-16-26
A1000	Install Unit-Strut & Grounding Tails at ETS	1d	Sep-30-26	Sep-30-26
A1010	Pre-Installation of Termination Structure at ETS	2d	Sep-30-26	Oct-01-26
A1040	Install Unit-Strut & Grounding Tails at WTS	1d	Sep-30-26	Sep-30-26
A1050	Pre-Installation of Termination Structure at WTS	2d	Sep-30-26	Oct-01-26
A1060	Final Installation of Termination Structure at WTS	3d	Oct-23-26	Oct-27-26
A1080	Remove Jumpers and Existing (6) Lighting arresters at WTS	2d	Oct-23-26	Oct-26-26
A1020	Final Installation of Termination Structure	3d	Oct-27-26	Oct-29-26
A1090	Remove Jumpers and Existing (6) Lighting arresters at ETS	2d	Oct-27-26	Oct-28-26
A1030	Expose Ground Grid near trench where Link-Box is located at ETS	1d	Nov-16-26	Nov-16-26
A1070	Expose Ground Grid near trench where Link-Box is located at WTS	1d	Nov-16-26	Nov-16-26
Scaffolding Installation		28d	Oct-28-26	Dec-04-26
Erection		7d	Oct-28-26	Nov-04-26
PRJ-CON-ERECTI-01	Scaffolding Installation for Termination Work at WTS	5d	Oct-28-26	Nov-02-26
PRJ-CON-ERECTI-02	Scaffolding Installation for Termination Work at ETS	5d	Oct-30-26	Nov-04-26
Dismantle		13d	Nov-14-26	Dec-04-26
PRJ-CON-DISMAN-01	Scaffolding Dismantle at WTS	3d	Nov-14-26	Nov-17-26
PRJ-CON-DISMAN-02	Scaffolding Dismantle at ETS	3d	Dec-02-26	Dec-04-26
DAS System Upgrade		5d	Nov-23-26	Dec-03-26
PRJ-CON-DAS-03	DAS Installation	5d	Nov-23-26*	Dec-03-26
Inspection & Testing		197d	Jul-18-26 A	Apr-20-27
Receiving Inspection		197d	Jul-18-26 A	Apr-20-27
PRJ-CON-RCVI-07	Racking & Grounding Materials Receiving Visual Inspection	4d	Jul-18-26 A	Aug-28-26 A
PRJ-CON-RCVI-04	Surge Arresters Receiving Visual Inspection	2d	Aug-12-26 A	Aug-28-26 A
PRJ-CON-RCVI-01	Splices Receiving Visual Inspection	2d	Aug-24-26 A	Sep-26-26 A
PRJ-CON-RCVI-02	Outdoor Terminations Receiving Visual Inspection	2d	Aug-24-26 A	Sep-26-26 A
PRJ-CON-RCVI-03	Link Boxes + SVLs Receiving Visual Inspection	2d	Aug-24-26 A	Sep-26-26 A
PRJ-CON-RCVI-05	Bonding & Grounding Cables Receiving Visual Inspection	2d	Aug-24-26 A	Aug-28-26 A
PRJ-CON-RCVI-06	Cable Clamps (Spring Clamps, Ratcheting Device, Joint Clamp, etc) Receiving Visual Inspection	2d	Aug-24-26 A	Sep-03-26 A
PRJ-CON-RCVI-08	DAS Instrument Receiving Visual Inspection	2d	Nov-19-26	Nov-20-26
PRJ-CON-RCVI-04.1	Spare Surge Arresters Receiving Visual Inspection	2d	Apr-19-27	Apr-20-27
24kV Jacket Integrity Test & OTDR		61d	Aug-24-26 A	Oct-29-26
Cable Test at Receiving		5d	Aug-24-26 A	Sep-25-26 A
PRJ-CON-CTRV-01	Cable Receiving Inspection & Testing - 1st Batch	2d	Aug-24-26 A	Aug-28-26 A
PRJ-CON-CTRV-11	Cable Receiving Inspection & Testing - 2nd Batch	5d	Aug-27-26 A	Sep-25-26 A
Cable Test before Cable Installation		69d	Aug-28-26 A	Oct-15-26
PRJ-CON-CINS-14	Pretest Install Cable S/V#13 - S/V#14	1d	Aug-28-26 A	Aug-28-26 A
PRJ-CON-CINS-13	Pretest Install Cable S/V#14 - ETS	1d	Aug-29-26 A	Aug-29-26 A

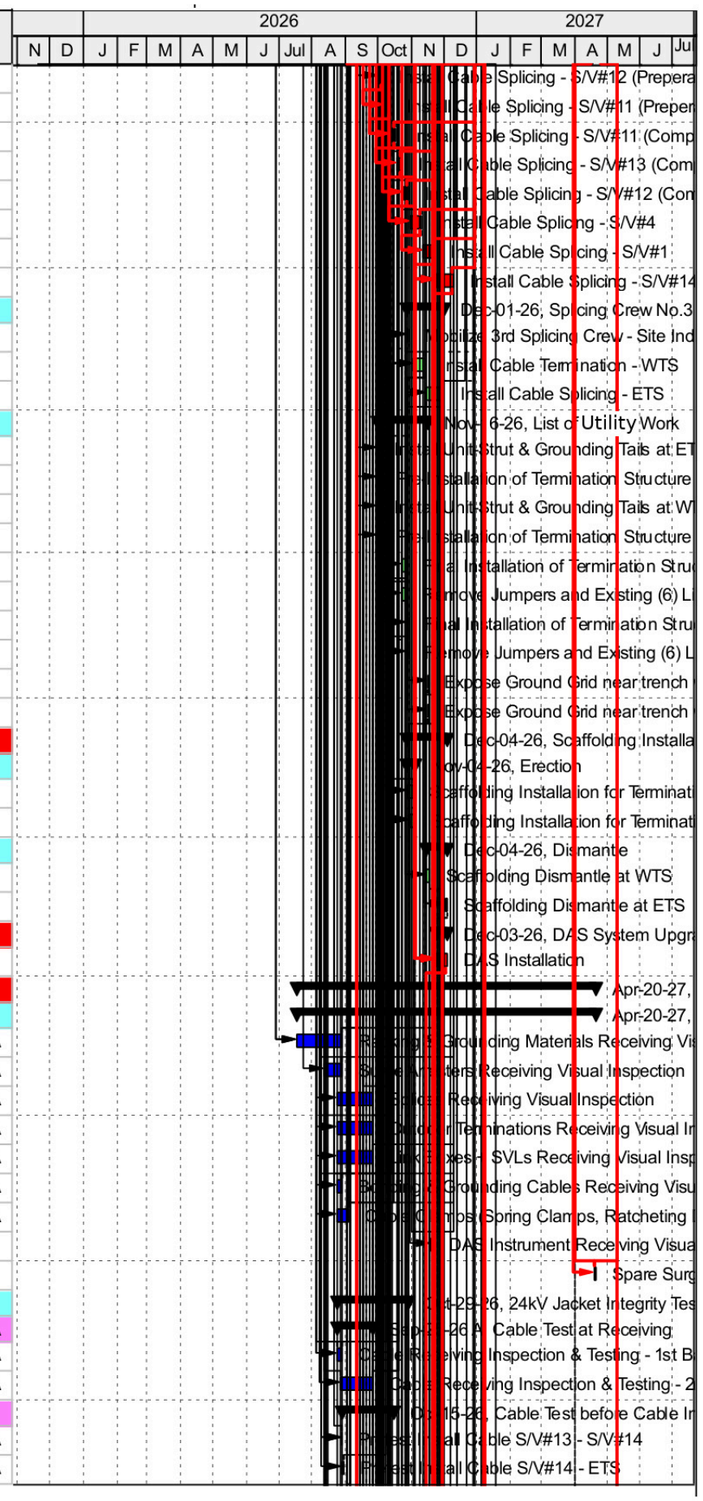


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample 500kV Underground Cable Project Schedule

Engineering, Procurement and Construction - Monthly Progress Schedule

HSE SCHEDULING CONSULTANTS

Activity ID	Activity Name	Original Duration	Start	Finish
PRJ-CON-CINS-20	Pretest Install Cable S/V#5 - R/V#5 - S/V#6 (fixed) - S/V#7	1d	Sep-01-26 A	Sep-02-26 A
PRJ-CON-CINS-15	Pretest Install Cable S/V#12 - S/V#13	1d	Sep-02-26 A	Sep-03-26 A
PRJ-CON-CINS-16	Pretest Install Cable S/V#11 - S/V#12	1d	Sep-04-26 A	Sep-07-26 A
PRJ-CON-CINS-17	Pretest Install Cable S/V#9 - S/V#10 (fixed) - S/V#11	1d	Sep-22-26 A	Sep-23-26 A
PRJ-CON-CINS-18	Pretest Install Cable S/V#8 - S/V#9	1d	Sep-22-26 A	Sep-23-26 A
PRJ-CON-CINS-22	Pretest Install Cable WTS to S/V#1	1d	Sep-25-26 A	Sep-26-26 A
PRJ-CON-CINS-23	Pretest Install Cable S/V#1 - R/V#1 - S/V#2 |Site Constraint|	1d	Sep-25-26 A	Sep-26-26 A
PRJ-CON-CINS-21	Pretest Install Cable S/V#4 - R/V#4 - S/V#5	1d	Sep-30-26 A	Sep-30-26
PRJ-CON-CINS-19	Pretest Install Cable S/V#7 - R/V#6 - S/V#8	1d	Oct-10-26	Oct-10-26
PRJ-CON-CINS-24	Pretest Install Cable S/V#2 - R/V#2 - S/V#3 - R/V#3 - S/V#4 (fixed) |Site Constraint|	1d	Oct-15-26	Oct-15-26
Cable Test after Cable Installation		35d	Sep-12-26 A	Oct-29-26
PRJ-CON-CINS-26	Post-test Install Cable S/V#13 - S/V#14	3d	Sep-12-26 A	Sep-12-26 A
PRJ-CON-CINS-27	Post-test Install Cable S/V#12 - S/V#13	3d	Sep-17-26 A	Sep-17-26 A
PRJ-CON-CINS-28	Post-test Install Cable S/V#11 - S/V#12	3d	Sep-21-26 A	Sep-23-26 A
PRJ-CON-CINS-32	Post-test Install Cable S/V#5 - R/V#5 - S/V#6 (fixed) - S/V#7	3d	Sep-24-26 A	Sep-28-26 A
PRJ-CON-CINS-33	Post-test Install Cable S/V#4 - R/V#4 - S/V#5	3d	Sep-30-26 A	Sep-30-26
PRJ-CON-CINS-29	Post-test Install Cable S/V#9 - S/V#10 (fixed) - S/V#11	3d	Oct-03-26	Oct-06-26
PRJ-CON-CINS-30	Post-test Install Cable S/V#8 - S/V#9	3d	Oct-07-26	Oct-09-26
PRJ-CON-CINS-31	Post-test Install Cable S/V#7 - R/V#6 - S/V#8	3d	Oct-12-26	Oct-14-26
PRJ-CON-CINS-36	Post-test Install Cable S/V#2 - R/V#2 - S/V#3 - R/V#3 - S/V#4 (fixed) |Site Constraint|	3d	Oct-16-26	Oct-19-26
PRJ-CON-CINS-35	Post-test Install Cable S/V#1 - R/V#1 - S/V#2 |Site Constraint|	3d	Oct-20-26	Oct-22-26
PRJ-CON-CINS-34	Post-test Install Cable WTS to S/V#1	3d	Oct-23-26	Oct-26-26
PRJ-CON-CINS-25	Post-test Install Cable S/V#14 - ETS	3d	Oct-27-26	Oct-29-26
Final Racking & Grounding Inspections		52d	Sep-30-26	Dec-10-26
Splice Manhole		41d	Oct-19-26	Dec-10-26
PRJ-CON-SPMA-08	Final Inspection for Racking & Grounding & Cable Splicing - S/V#11	1d	Oct-19-26	Oct-19-26
PRJ-CON-SPMA-10	Final Inspection for Racking & Grounding & Cable Splicing - S/V#5	1d	Oct-19-26	Oct-19-26
PRJ-CON-SPMA-07	Final Inspection for Racking & Grounding & Cable Splicing - S/V#13	1d	Oct-24-26	Oct-24-26
PRJ-CON-SPMA-02	Final Inspection for Racking & Grounding & Cable Splicing - S/V#12	1d	Oct-30-26	Oct-30-26
PRJ-CON-SPMA-03	Final Inspection for Racking & Grounding & Cable Splicing - S/V#9	1d	Oct-30-26	Oct-30-26
PRJ-CON-SPMA-05	Final Inspection for Racking & Grounding & Cable Splicing - S/V#4	1d	Nov-11-26	Nov-11-26
PRJ-CON-SPMA-09	Final Inspection for Racking & Grounding & Cable Splicing - S/V#8	1d	Nov-11-26	Nov-11-26
PRJ-CON-SPMA-04	Final Inspection for Racking & Grounding & Cable Splicing - S/V#7	1d	Nov-23-26	Nov-23-26
PRJ-CON-SPMA-11	Final Inspection for Racking & Grounding & Cable Splicing - S/V#1	1d	Nov-23-26	Nov-23-26
PRJ-CON-SPMA-01	Final Inspection for Racking & Grounding & Cable Splicing - S/V#14	1d	Dec-10-26	Dec-10-26
PRJ-CON-SPMA-06	Final Inspection for Racking & Grounding & Cable Splicing - S/V#2 (Site Constraint)	1d	Dec-10-26	Dec-10-26
Restraint Manhole		21d	Sep-30-26	Oct-23-26
PRJ-CON-REMA-02	Final Inspection for Racking & Grounding - S/V#6 (Fixed)	1d	Sep-30-26	Sep-30-26
PRJ-CON-REMA-08	Final Inspection for Racking & Grounding - R/V#5	1d	Sep-30-26	Sep-30-26
PRJ-CON-REMA-07	Final Inspection for Racking & Grounding - R/V#4	1d	Oct-03-26	Oct-03-26
PRJ-CON-REMA-01	Final Inspection for Racking & Grounding - S/V#10 (Fixed)	1d	Oct-07-26	Oct-07-26
PRJ-CON-REMA-09	Final Inspection for Racking & Grounding - R/V#6	1d	Oct-15-26	Oct-15-26
PRJ-CON-REMA-03	Final Inspection for Racking & Grounding - S/V#3 (Fixed)	1d	Oct-20-26	Oct-20-26
PRJ-CON-REMA-05	Final Inspection for Racking & Grounding - R/V#2	1d	Oct-20-26	Oct-20-26
PRJ-CON-REMA-06	Final Inspection for Racking & Grounding - R/V#3	1d	Oct-20-26	Oct-20-26
PRJ-CON-REMA-04	Final Inspection for Racking & Grounding - R/V#1	1d	Oct-23-26	Oct-23-26
Transition Station		25d	Oct-29-26	Dec-02-26
PRJ-CON-TRST-015	Final Inspection for Surge Arrester Installation - WTS	1d	Oct-29-26	Oct-29-26
PRJ-CON-TRST-025	Final Inspection for Surge Arrester Installation - ETS	1d	Nov-03-26	Nov-03-26
PRJ-CON-TRST-01	Final Inspection for Racking & Grounding & Cable Termination - WTS	1d	Nov-17-26	Nov-17-26

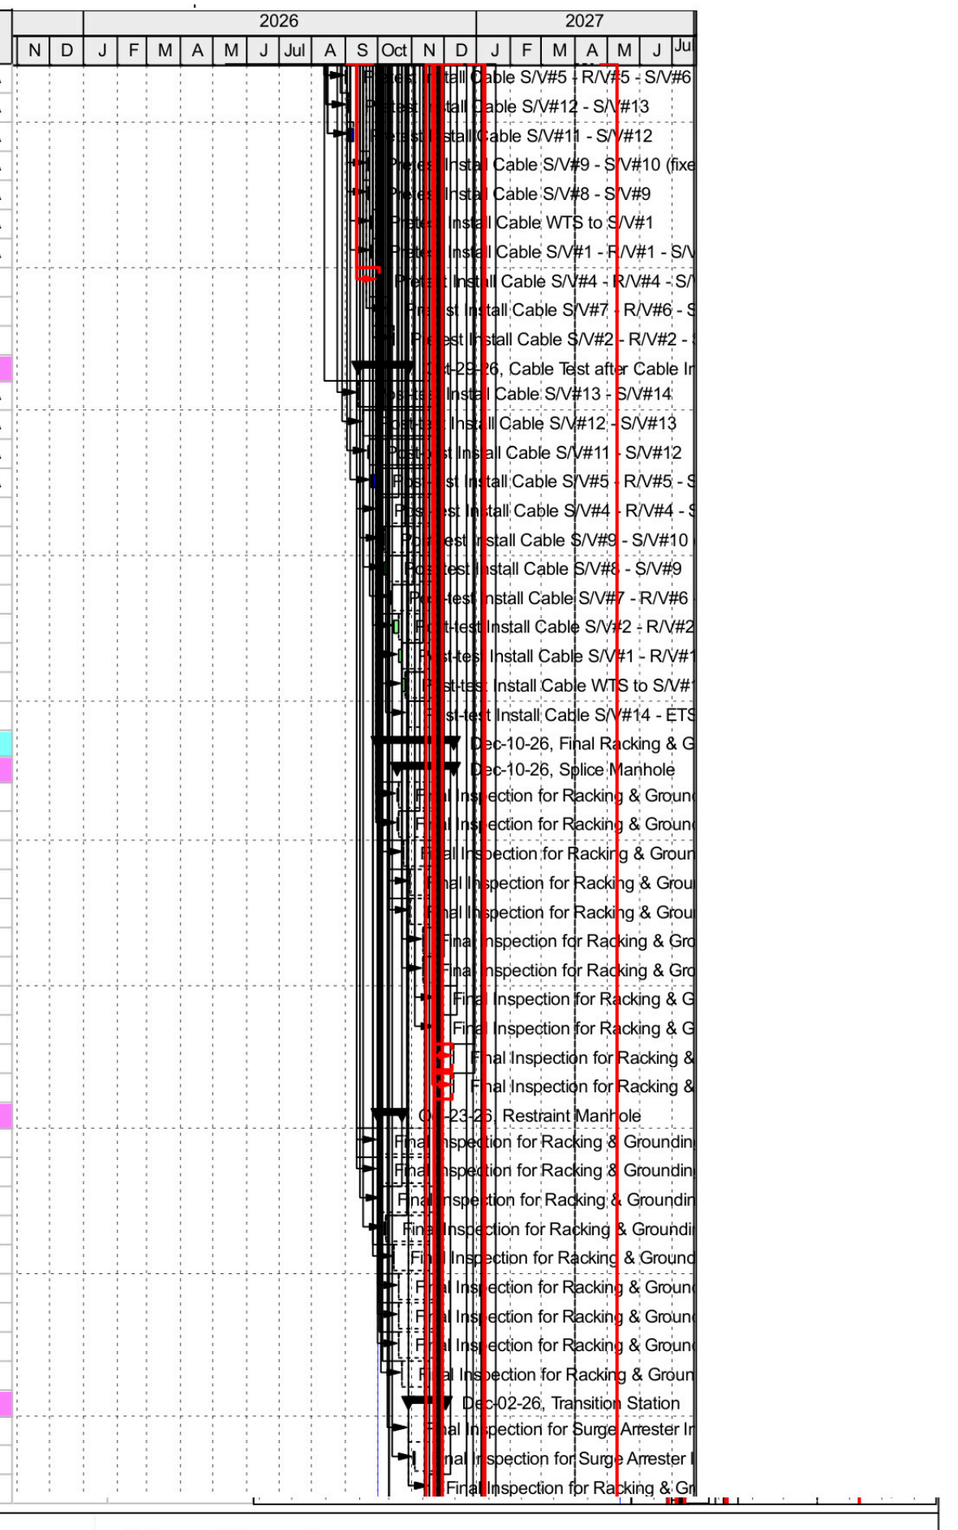

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary


Website Portfolio Sample

Sample 500kV Underground Cable Project Schedule

Engineering, Procurement and Construction - Monthly Progress Schedule

HSE SCHEDULING CONSULTANTS

Activity ID	Activity Name	Original Duration	Start	Finish
PRJ-CON-TRST-02	Final Inspection for Racking & Grounding & Cable Termination - ETS	1d	Dec-02-26	Dec-02-26
Commissioning Test		13d	Dec-04-26	Dec-18-26
Cable Sheath Test (End to End)		2d	Dec-11-26	Dec-12-26
PRJ-CON-CSHT-01	Cable Sheath Test after Jointing and Terminating	2d	Dec-11-26	Dec-12-26
Impedance Test, Capacitance Test, Insulation Resistance Test		2d	Dec-14-26	Dec-15-26
PRJ-CON-ICIR-01	Impedance, Capacitance, Insulation Tests Preparation	1d	Dec-14-26	Dec-14-26
PRJ-CON-ICIR-02	Impedance, Capacitance, Insulation Tests A3 & B3 & C3	1d	Dec-15-26	Dec-15-26
AC Withstand Test with PD Measurement		5d	Dec-14-26	Dec-18-26
PRJ-CON-ACWT-01	AC Withstand Test Preparation	2d	Dec-14-26	Dec-15-26
PRJ-CON-ACWT-02	AC Withstand Test Phase A3	1d	Dec-16-26	Dec-16-26
PRJ-CON-ACWT-03	AC Withstand Test Phase B3	1d	Dec-17-26	Dec-17-26
PRJ-CON-ACWT-04	AC Withstand Test Phase C3	1d	Dec-18-26	Dec-18-26
DAS Commissoning		4d	Dec-04-26	Dec-08-26
PRJ-CON-DAS-01	PDM & DAS Calibration	2d	Dec-04-26	Dec-05-26
PRJ-CON-DAS-02	DAS Commissioning	2d	Dec-07-26	Dec-08-26
Closeout & Demobilization		49d	Oct-30-26	Jan-05-27
PRJ-CON-MOB-07	Supply Cable Sample	5d	Oct-30-26	Nov-04-26
PRJ-COM-PLC-01	Punchlist Corrections	3d	Dec-02-26	Dec-04-26
PRJ-CON-MOB-01	Demobilization & Restoration	5d	Dec-19-26	Dec-29-26
PRJ-CON-MOB-02	O&M Manuals Submittal	1d	Dec-19-26	Dec-19-26
PRJ-CON-MOB-04	Training	5d	Dec-19-26	Dec-29-26
PRJ-CON-MOB-03	O&M Manuals Review & Approval	10d	Dec-21-26	Jan-05-27

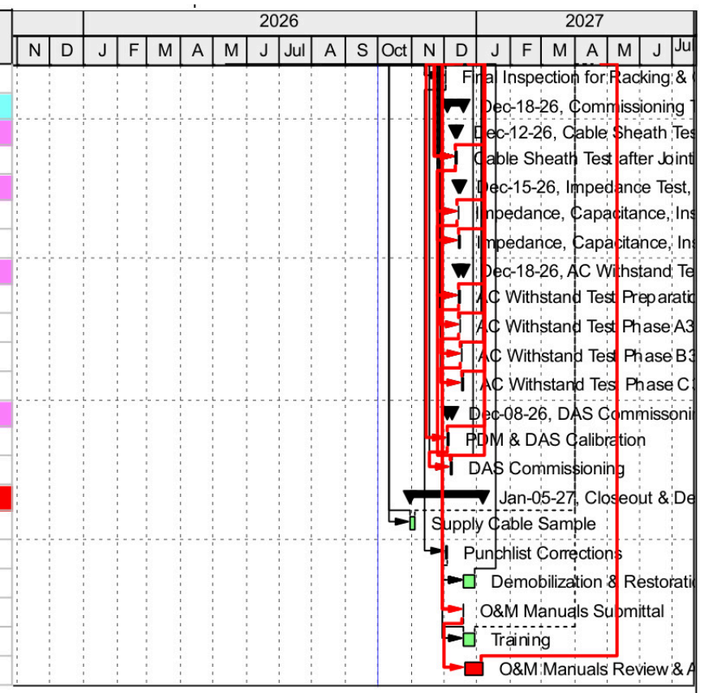

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Website Portfolio Sample
