
HSE | CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Sample Data Center Baseline Schedule		421	30-Jan-26 A	13-Sep-27		
/ Owner Performed Milestones		153	26-Feb-26 A	29-Sep-26		
Owner Performed Milestones		153	26-Feb-26 A	29-Sep-26		
DC.OWN.OPM.150	Wet Lines Complete (by others)	67	26-Feb-26 A	22-Jun-26		
DC.OWN.OPM.110	Building Pad & Roadways Complete (by others)	25	26-Feb-26 A	30-Apr-26		
DC.OWN.OPM.120	Electrical Undergrounds Complete (by others)	67	26-Feb-26 A	22-Jun-26		
DC.OWN.OPM.130	Fiber Undergrounds Complete (by others)	67	26-Feb-26 A	22-Jun-26		
DC.OWN.OPM.140	Temporary Construction Power Complete (by others)	0	02-Jul-26			
DC.OWN.OPM.100	Permenant Power Available (by others)	0		29-Sep-26		
Milestones		344	19-May-26	13-Sep-27		
Construction Milestones		176	19-May-26	20-Jan-27		
DC.OWN.CON.MS.100	Start Foundation	0	19-May-26			
DC.OWN.CON.MS.110	Start Superstructure	0	31-Jul-26			
DC.OWN.CON.MS.120	Start Roofing	0	31-Jul-26			
DC.OWN.CON.MS.130	Perm Power Ready from Utility	0		16-Oct-26		
DC.OWN.CON.MS.140	Complete U/G Utilities	0		19-Nov-26		
DC.OWN.CON.MS.150	Complete of Utility / MV UG Electrical	0		19-Nov-26		
DC.OWN.CON.MS.160	Complete Slab On Grade	0		30-Nov-26		
DC.OWN.CON.MS.170	Complete Weather Tight	0		30-Nov-26		
DC.OWN.CON.MS.180	Cx Start	0	06-Jan-27			
DC.OWN.CON.MS.190	Complete MEP Rough-In	0		20-Jan-27		
Site Milestones		0	07-Jun-27	07-Jun-27		
Site		0	07-Jun-27	07-Jun-27		
OWN.87.MS.SITE.100	Site - Substantial Completion (SC)	0		07-Jun-27		
Shell Milestones		275	19-May-26	07-Jun-27		
Shell		275	19-May-26	07-Jun-27		
OWN.87.MS.SHELL.110	Shell - SWD	0	19-May-26			
OWN.87.MS.SHELL.100	Shell - Substantial Completion (SC)	0		07-Jun-27		
Contract Milestones		344	19-May-26	13-Sep-27		
OWN.NTP.120	Foundation Start	0	19-May-26			
Control Milestones		63	02-Sep-26	30-Nov-26		
OWN.NTP.300	Foundations Complete	0		02-Sep-26		
OWN.NTP.330	Weather Tight Complete	0		29-Oct-26		
OWN.NTP.320	Underground Utilities Complete	0		23-Nov-26		
OWN.NTP.310	Slab on Grade Complete	0		30-Nov-26		
Phase 1 (ROMP 1 & 2 + Office & Catcher)		181	12-Oct-26	22-Jun-27		
ROMP 1		181	12-Oct-26	22-Jun-27		
OWN.87.PH1.MS.100	SWD (RCS) - PH1 ROMP1	0	12-Oct-26			
OWN.87.PH1.MS.120	Fiber Early Access (FEA) - PH1 ROMP1	0	08-Feb-27			
OWN.87.PH1.MS.140	Network Early Access (NEA) - PH1 ROMP1	0	06-Mar-27			
OWN.87.PH1.MS.160	Handoff to Commissioning (H2C) - PH1 ROMP1	0		09-Apr-27		
OWN.87.PH1.MS.180	Substantial Completion (SC) - PH1 ROMP1	0		07-Jun-27		
OWN.87.PH1.MS.210	Final Completion (PCO) - PH1 ROMP1	0		22-Jun-27		
ROMP 2		181	12-Oct-26	22-Jun-27		
OWN.87.PH1.MS.110	SWD (RCS) - PH1 ROMP 2	0	12-Oct-26			

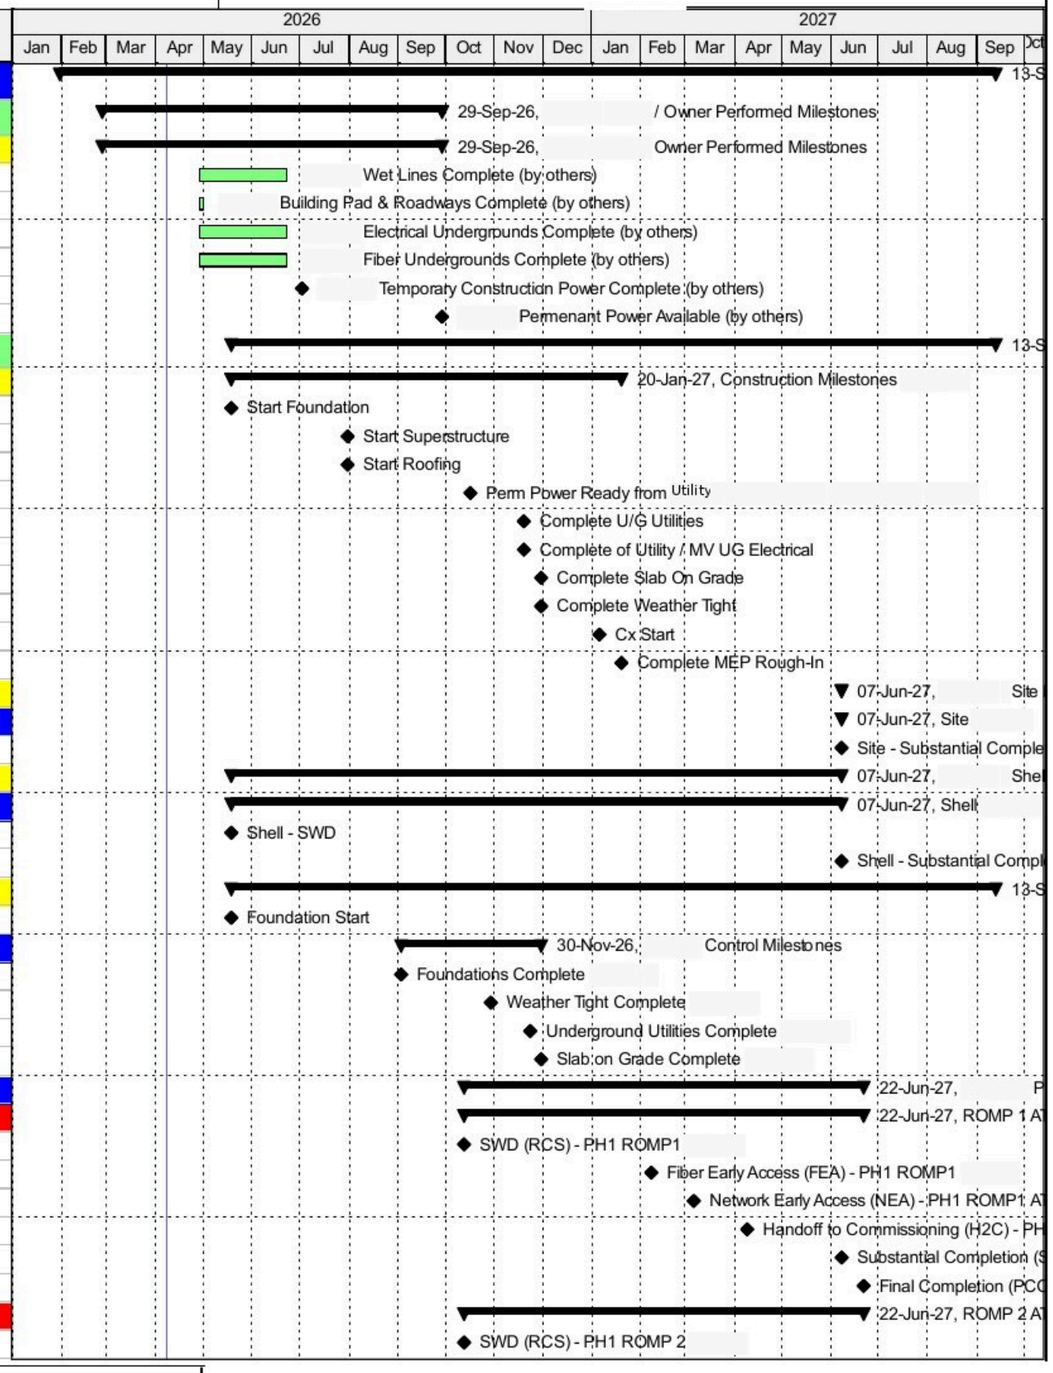


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
OWN.87.PH1.MS.130	Fiber Early Access (FEA) - PH1 ROMP 2	0	08-Feb-27			
OWN.87.PH1.MS.150	Network Early Access (NEA) - PH1 ROMP2	0	06-Mar-27			
OWN.87.PH1.MS.170	Handoff to Commissioning (H2C) - PH1 ROMP2	0		09-Apr-27		
OWN.87.PH1.MS.190	Substantial Completion (SC) - PH1 ROMP2	0		07-Jun-27		
OWN.87.PH1.MS.200	Final Completion (PCO) - PH1 ROMP2	0		22-Jun-27		
Phase 2 (ROMP 3 & 4)		170	07-Dec-26	02-Aug-27		
ROMP 3		170	07-Dec-26	02-Aug-27		
OWN.87.PH2.MS.100	SWD (RCS) - PH2 ROMP3	0	07-Dec-26			
OWN.87.PH2.MS.120	Network Early Access (NEA) - PH2 ROMP3	0	04-May-27			
OWN.87.PH2.MS.140	Handoff to Commissioning (H2C) - PH2 ROMP3	0		07-Jun-27		
OWN.87.PH2.MS.160	Substantial Completion (SC) - PH2 ROMP3	0		20-Jul-27		
OWN.87.PH2.MS.190	Final Completion (PCO) - PH2 ROMP3	0		02-Aug-27		
ROMP 4		170	07-Dec-26	02-Aug-27		
OWN.87.PH2.MS.110	SWD (RCS) - PH2 ROMP4	0	07-Dec-26			
OWN.87.PH2.MS.130	Network Early Access (NEA) - PH2 ROMP4	0	04-May-27			
OWN.87.PH2.MS.150	Handoff to Commissioning (H2C) - PH2 ROMP4	0		07-Jun-27		
OWN.87.PH2.MS.170	Substantial Completion (SC) - PH2 ROMP4	0		20-Jul-27		
OWN.87.PH2.MS.180	Final Completion (PCO) - PH2 ROMP4	0		02-Aug-27		
Phase 3 (ROMP 5 & 6)		170	18-Jan-27	13-Sep-27		
ROMP 5		170	18-Jan-27	13-Sep-27		
OWN.87.PH3.MS.100	SWD (RCS) - PH3 ROMP5	0	18-Jan-27			
OWN.87.PH3.MS.120	Network Early Access (NEA) - PH3 ROMP5	0	15-Jun-27			
OWN.87.PH3.MS.140	Handoff to Commissioning (H2C) - PH3 ROMP5	0		17-Jul-27		
OWN.87.PH3.MS.160	Substantial Completion (SC) - PH3 ROMP5	0		31-Aug-27		
OWN.87.PH3.MS.190	Final Completion (PCO) - PH3 ROMP5	0		13-Sep-27		
ROMP 6		170	18-Jan-27	13-Sep-27		
OWN.87.PH3.MS.110	SWD (RCS) - PH3 ROMP6	0	18-Jan-27			
OWN.87.PH3.MS.130	Network Early Access (NEA) - PH3 ROMP6	0	15-Jun-27			
OWN.87.PH3.MS.150	Handoff to Commissioning (H2C) - PH3 ROMP6	0		17-Jul-27		
OWN.87.PH3.MS.170	Substantial Completion (SC) - PH3 ROMP6	0		31-Aug-27		
OWN.87.PH3.MS.180	Final Completion (PCO) - PH3 ROMP6	0		13-Sep-27		
		413	30-Jan-26 A	31-Aug-27		
Buyout / Shops / Procurement		267	26-Feb-26 A	08-Mar-27		
CFCI		247	26-Feb-26 A	05-Feb-27		
Buy Out & Procurement		247	26-Feb-26 A	05-Feb-27		
Foundation / Structure		142	26-Feb-26 A	11-Sep-26		
Cast in Place Concrete		65	26-Feb-26 A	27-May-26		
DC.SHELL.PROC.100	Buyout (concrete)	25	26-Feb-26 A	01-May-26		
DC.SHELL.PROC.110	Submittal Development (concrete)	10	19-Mar-26 A	05-May-26		
DC.SHELL.PROC.120	GC Submittal Review (concrete)	1	06-May-26	06-May-26		
DC.SHELL.PROC.130	Designer Submittal Approval (concrete)	10	07-May-26	20-May-26		
DC.SHELL.PROC.140	Fabrication & Delivery (concrete)	5	21-May-26	27-May-26		
Concrete Reinforcement		58	26-Feb-26 A	18-May-26		
DC.SHELL.PROC.150	Buyout (Concrete Reinforcement)	25	26-Feb-26 A	01-May-26		
DC.SHELL.PROC.160	Submittal Development (Concrete Reinforcement)	10	19-Mar-26 A	04-May-26		

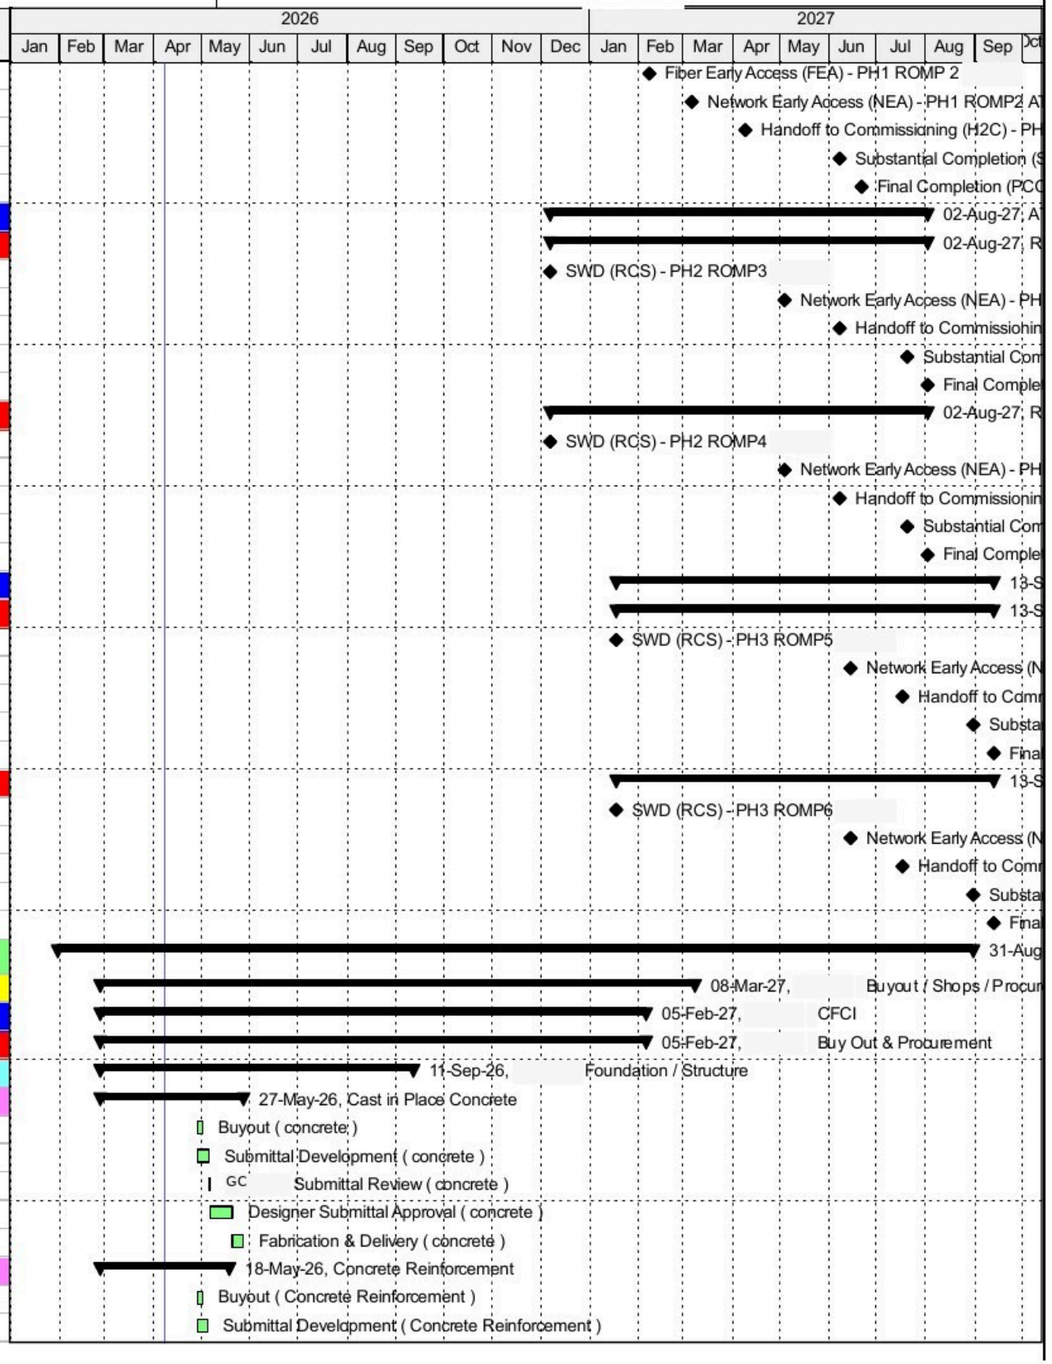


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
DC.SHELL.PROC.170	GC Submittal Review (Concrete Reinforcement)	1	04-May-26	04-May-26		
DC.SHELL.PROC.180	Designer Submittal Approval (Concrete Reinforcement)	10	05-May-26	18-May-26		
DC.SHELL.PROC.190	Fabrication & Delivery (Concrete Reinforcement)	5	12-May-26	18-May-26		
Dampproofing and Waterproofing		70	26-Feb-26 A	03-Jun-26		
DC.SHELL.PROC.200	Buyout (Dampproofing and Waterproofing)	25	26-Feb-26 A	01-May-26		
DC.SHELL.PROC.210	Submittal Development (Dampproofing and Waterproofing)	5	30-Apr-26	06-May-26		
DC.SHELL.PROC.220	GC Submittal Review (Dampproofing and Waterproofing)	1	06-May-26	06-May-26		
DC.SHELL.PROC.230	Designer Submittal Approval (Dampproofing and Waterproofing)	10	07-May-26	20-May-26		
DC.SHELL.PROC.240	Fabrication & Delivery (Dampproofing and Waterproofing)	10	21-May-26	03-Jun-26		
Precast Structural Concrete		122	26-Feb-26 A	14-Aug-26		
DC.SHELL.PROC.250	Buyout (structural precast)	28	26-Feb-26 A	01-May-26		
DC.SHELL.PROC.260	Submittal Development (structural precast)	15	30-Apr-26	20-May-26		
DC.SHELL.PROC.270	GC Submittal Review (structural precast)	1	20-May-26	20-May-26		
DC.SHELL.PROC.280	Designer Submittal Approval (structural precast)	10	21-May-26	03-Jun-26		
DC.SHELL.PROC.290	Fabrication & Delivery (structural precast)	50	04-Jun-26	14-Aug-26		
CMU		73	26-Feb-26 A	08-Jun-26		
DC.SHELL.PROC.300	Buyout (CMU)	30	26-Feb-26 A	01-May-26		
DC.SHELL.PROC.310	Submittal Development (CMU)	10	04-May-26	15-May-26		
DC.SHELL.PROC.320	GC Submittal Review (CMU)	2	15-May-26	18-May-26		
DC.SHELL.PROC.330	Designer Submittal Approval (CMU)	10	19-May-26	01-Jun-26		
DC.SHELL.PROC.340	Fabrication & Delivery (CMU)	5	02-Jun-26	08-Jun-26		
Metal Panels		137	26-Feb-26 A	04-Sep-26		
DC.SHELL.PROC.350	Buyout (Metal Panels)	45	26-Feb-26 A	20-May-26		
DC.SHELL.PROC.360	Submittal Development (Metal Panels)	10	21-May-26	03-Jun-26		
DC.SHELL.PROC.370	GC Submittal Review (Metal Panels)	5	04-Jun-26	10-Jun-26		
DC.SHELL.PROC.380	Designer Submittal Approval (Metal Panels)	10	11-Jun-26	25-Jun-26		
DC.SHELL.PROC.390	Fabrication & Delivery (Metal Panels / Screen Wall)	50	26-Jun-26	04-Sep-26		
DC.SHELL.PROC.400	Fabrication & Delivery (Metal Panels / IMP)	30	26-Jun-26	07-Aug-26		
Hollow Metal Door Frames in Concrete or Masonry		101	26-Feb-26 A	16-Jul-26		
DC.SHELL.PROC.410	Buyout (hollow metal frames in masonry)	35	26-Feb-26 A	06-May-26		
DC.SHELL.PROC.420	Submittal Development (hollow metal frames in masonry)	10	07-May-26	20-May-26		
DC.SHELL.PROC.430	GC Submittal Review (hollow metal frames in masonry)	5	14-May-26	20-May-26		
DC.SHELL.PROC.440	Designer Submittal Approval (hollow metal frames in masonry)	10	21-May-26	03-Jun-26		
DC.SHELL.PROC.450	Fabrication & Delivery (hollow metal frames in masonry)	30	04-Jun-26	16-Jul-26		
Metal Canopy		142	26-Feb-26 A	11-Sep-26		
DC.SHELL.PROC.460	Buyout (Metal Canopy)	60	26-Feb-26 A	10-Jun-26		
DC.SHELL.PROC.470	Submittal Development (Metal Canopy)	20	11-Jun-26	09-Jul-26		
DC.SHELL.PROC.480	GC Submittal Review (Metal Canopy)	5	10-Jul-26	16-Jul-26		
DC.SHELL.PROC.490	Designer Submittal Approval (Metal Canopy)	10	17-Jul-26	31-Jul-26		
DC.SHELL.PROC.500	Fabrication & Delivery (Metal Canopy)	30	03-Aug-26	11-Sep-26		
Metal Railings (Bollards & Guardrails)		142	26-Feb-26 A	11-Sep-26		
DC.SHELL.PROC.510	Buyout (Metal Railings Bollards & Guardrails)	45	26-Feb-26 A	20-May-26		
DC.SHELL.PROC.520	Submittal Development (Metal Railings Bollards & Guardrails)	25	21-May-26	25-Jun-26		
DC.SHELL.PROC.530	GC Submittal Review (Metal Railings Bollards & Guardrails)	5	26-Jun-26	02-Jul-26		
DC.SHELL.PROC.540	Designer Submittal Approval (Metal Railings Bollards & Guardrails)	10	03-Jul-26	16-Jul-26		

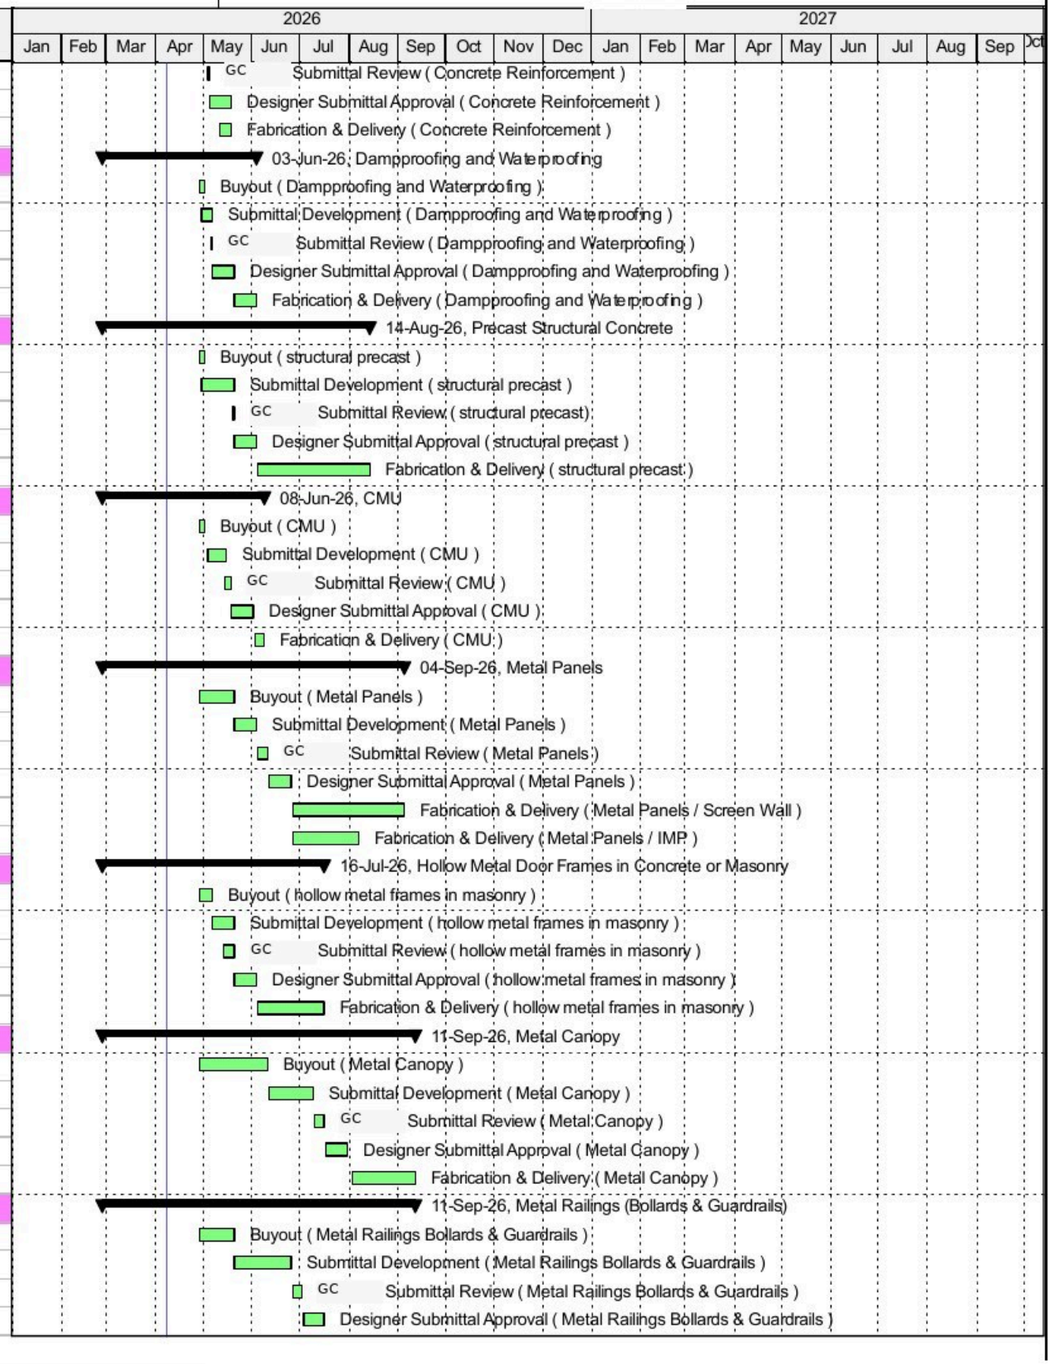


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
DC.SHELL.PROC.550	Fabrication & Delivery (Metal Railings Bollards & Guardrails)	40	17-Jul-26	11-Sep-26		
Metal Decking		112	26-Feb-26 A	31-Jul-26		
DC.SHELL.PROC.560	Buyout (decking)	23	26-Feb-26 A	01-May-26		
DC.SHELL.PROC.570	Submittal Development (decking)	10	30-Apr-26	13-May-26		
DC.SHELL.PROC.580	GC Submittal Review (decking)	5	14-May-26	20-May-26		
DC.SHELL.PROC.590	Designer Submittal Approval (decking)	10	21-May-26	03-Jun-26		
DC.SHELL.PROC.600	Fabrication & Delivery (decking)	40	04-Jun-26	31-Jul-26		
Steel Stairs		119	26-Feb-26 A	11-Aug-26		
DC.SHELL.PROC.610	Buyout (steel stairs)	23	26-Feb-26 A	01-May-26		
DC.SHELL.PROC.620	Submittal Development (steel stairs)	25	04-May-26	05-Jun-26		
DC.SHELL.PROC.630	GC Submittal Review (steel stairs)	5	01-Jun-26	05-Jun-26		
DC.SHELL.PROC.640	Designer Submittal Approval (steel stairs)	10	08-Jun-26	22-Jun-26		
DC.SHELL.PROC.650	Fabrication & Delivery (steel stairs)	35	23-Jun-26	11-Aug-26		
Exterior Enclosure		205	26-Feb-26 A	09-Dec-26		
Window Treatments		205	26-Feb-26 A	09-Dec-26		
DC.SHELL.PROC.660	Buyout (Window Treatments)	70	26-Feb-26 A	25-Jun-26		
DC.SHELL.PROC.670	Submittal Development (Window Treatments)	10	26-Jun-26	09-Jul-26		
DC.SHELL.PROC.680	GC Submittal Review (Window Treatments)	5	03-Jul-26	09-Jul-26		
DC.SHELL.PROC.690	Designer Submittal Approval (Window Treatments)	10	10-Jul-26	23-Jul-26		
DC.SHELL.PROC.700	Field Measure After Drywall (Window Treatments)	5	05-Nov-26	11-Nov-26		
DC.SHELL.PROC.710	Fabrication and Delivery (Window Treatments)	20	12-Nov-26	09-Dec-26		
Glass/Glazing		137	26-Feb-26 A	04-Sep-26		
DC.SHELL.PROC.720	Buyout (Glass/Glazing)	50	26-Feb-26 A	27-May-26		
DC.SHELL.PROC.730	Submittal Development (Glass/Glazing)	10	28-May-26	10-Jun-26		
DC.SHELL.PROC.740	GC Submittal Review (Glass/Glazing)	1	10-Jun-26	10-Jun-26		
DC.SHELL.PROC.750	Designer Submittal Approval (Glass/Glazing)	10	11-Jun-26	25-Jun-26		
DC.SHELL.PROC.760	Fabrication & Delivery (Glass/Glazing)	50	26-Jun-26	04-Sep-26		
Exterior Doors and Frames		137	26-Feb-26 A	04-Sep-26		
DC.SHELL.PROC.770	Buyout (Exterior Doors and Frames)	55	26-Feb-26 A	03-Jun-26		
DC.SHELL.PROC.780	Submittal Development (Exterior Doors and Frames)	20	04-Jun-26	02-Jul-26		
DC.SHELL.PROC.790	GC Submittal Review (Exterior Doors and Frames)	5	03-Jul-26	09-Jul-26		
DC.SHELL.PROC.800	Designer Submittal Approval (Exterior Doors and Frames)	10	10-Jul-26	23-Jul-26		
DC.SHELL.PROC.810	Fabrication & Delivery (Exterior Doors and Frames)	30	27-Jul-26	04-Sep-26		
Expansion Control (Expansion Joints)		142	26-Feb-26 A	11-Sep-26		
DC.SHELL.PROC.820	Buyout (Expansion Joints)	45	26-Feb-26 A	20-May-26		
DC.SHELL.PROC.830	Submittal Development (Expansion Joints)	10	21-May-26	03-Jun-26		
DC.SHELL.PROC.840	GC Submittal Review (Expansion Joints)	5	28-May-26	03-Jun-26		
DC.SHELL.PROC.850	Designer Submittal Approval (Expansion Joints)	10	04-Jun-26	18-Jun-26		
DC.SHELL.PROC.860	Fabrication & Delivery (Expansion Joints)	60	19-Jun-26	11-Sep-26		
DC.SHELL.PROC.870	Field Measurement Needed	5	21-Aug-26	27-Aug-26		
Membrane Roofing (TPO, Bituminous, EPDM, etc.)		117	26-Feb-26 A	07-Aug-26		
DC.SHELL.PROC.880	Buyout (membrane roofing)	50	26-Feb-26 A	27-May-26		
DC.SHELL.PROC.890	Submittal Development (membrane roofing)	15	28-May-26	18-Jun-26		
DC.SHELL.PROC.900	GC Submittal Review (membrane roofing)	5	19-Jun-26	25-Jun-26		
DC.SHELL.PROC.910	Designer Submittal Approval (membrane roofing)	10	26-Jun-26	09-Jul-26		

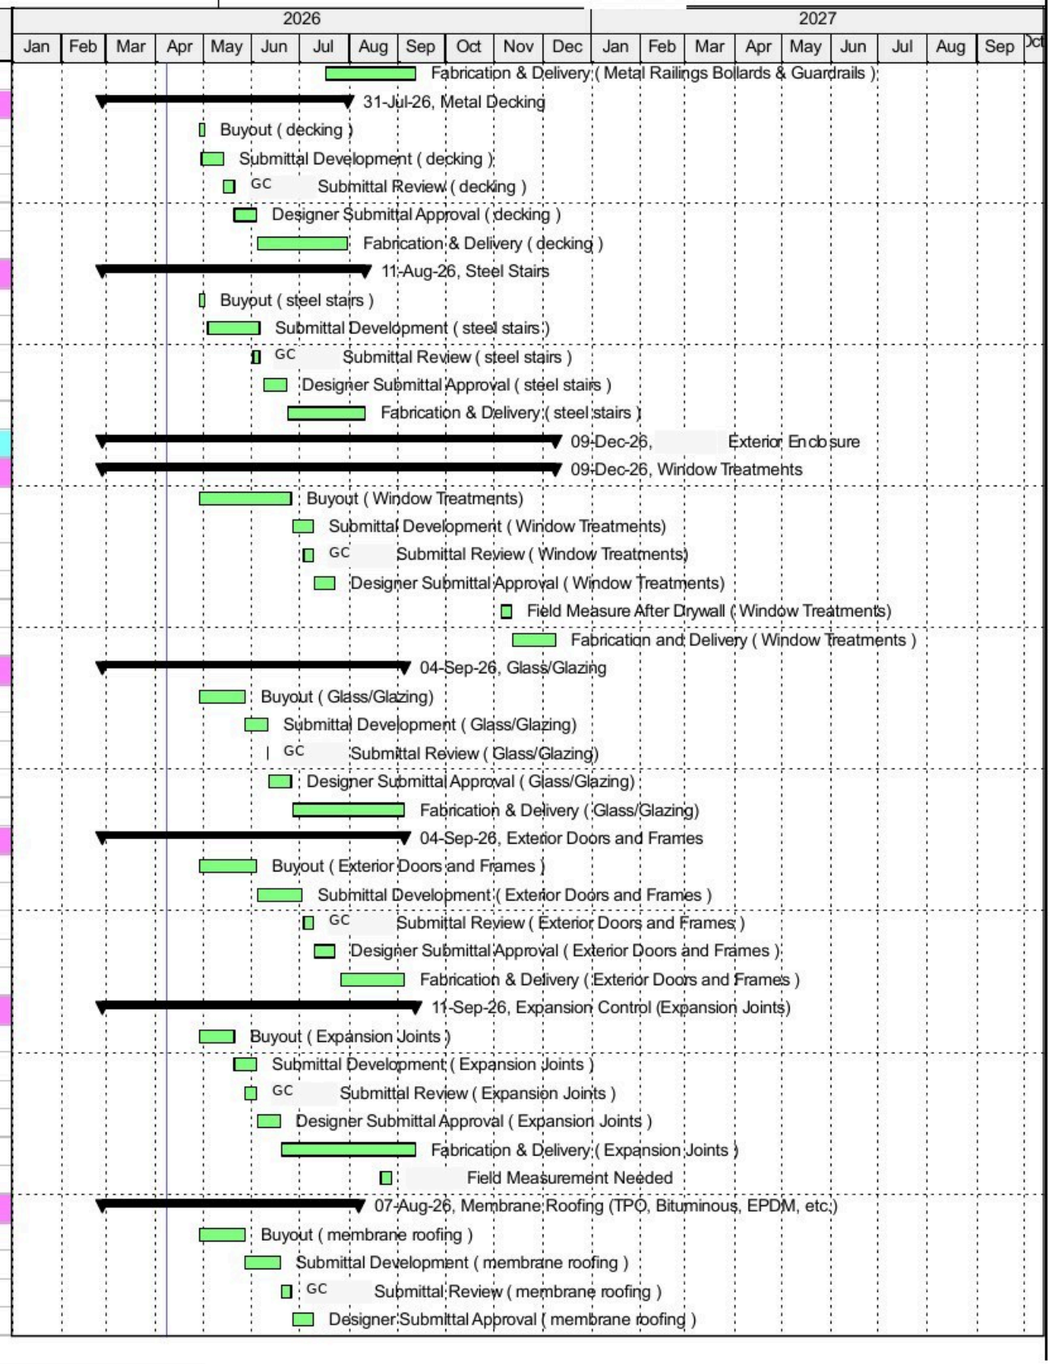


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
DC.SHELL.PROC.920	Fabrication & Delivery (membrane roofing)	20	10-Jul-26	07-Aug-26		
Bird Screen (New)		142	26-Feb-26 A	11-Sep-26		
DC.SHELL.PROC.930	Buyout (Bird Screen)	40	26-Feb-26 A	13-May-26		
DC.SHELL.PROC.940	Submittal Development (Bird Screen)	15	14-May-26	03-Jun-26		
DC.SHELL.PROC.950	GC Submittal Review (Bird Screen)	5	04-Jun-26	10-Jun-26		
DC.SHELL.PROC.960	Designer Submittal Approval (Bird Screen)	10	11-Jun-26	25-Jun-26		
DC.SHELL.PROC.970	Fabrication and Delivery (Bird Screen)	55	26-Jun-26	11-Sep-26		
Exterior Architectural Louvers		158	26-Feb-26 A	05-Oct-26		
DC.SHELL.PROC.980	Buyout (Exterior Architectural Louvers)	60	26-Feb-26 A	10-Jun-26		
DC.SHELL.PROC.990	Submittal Development (Exterior Architectural Louvers)	20	11-Jun-26	09-Jul-26		
DC.SHELL.PROC.1000	GC Submittal Review (Exterior Architectural Louvers)	5	03-Jul-26	09-Jul-26		
DC.SHELL.PROC.1010	Designer Submittal Approval (Exterior Architectural Louvers)	10	10-Jul-26	23-Jul-26		
DC.SHELL.PROC.1020	Fabrication & Delivery (Exterior Architectural Louvers)	50	27-Jul-26	05-Oct-26		
Interior Buildout		183	26-Feb-26 A	09-Nov-26		
Elevator		183	26-Feb-26 A	09-Nov-26		
DC.IB.PROC.100	Buyout (Elevator)	45	26-Feb-26 A	20-May-26		
DC.IB.PROC.110	Submittal Development (Elevator)	20	21-May-26	18-Jun-26		
DC.IB.PROC.120	GC Submittal Review (Elevator)	5	11-Jun-26	18-Jun-26		
DC.IB.PROC.130	Designer Submittal Approval (Elevator)	10	19-Jun-26	02-Jul-26		
DC.IB.PROC.140	Fabrication & Delivery (Elevator)	90	03-Jul-26	09-Nov-26		
Metal Studs		132	26-Feb-26 A	28-Aug-26		
DC.IB.PROC.150	Buyout (Metal Framing)	60	26-Feb-26 A	10-Jun-26		
DC.IB.PROC.160	Submittal Development (Metal Framing)	10	11-Jun-26	25-Jun-26		
DC.IB.PROC.170	GC Submittal Review (Metal Framing)	5	26-Jun-26	02-Jul-26		
DC.IB.PROC.180	Designer Submittal Approval (Metal Framing)	10	03-Jul-26	16-Jul-26		
DC.IB.PROC.190	Fabrication & Delivery (Metal Framing)	30	17-Jul-26	28-Aug-26		
Plaster and Gypsum Board (Drywall)		112	26-Feb-26 A	31-Jul-26		
DC.IB.PROC.200	Buyout (drywall)	60	26-Feb-26 A	10-Jun-26		
DC.IB.PROC.210	Submittal Development (drywall)	10	11-Jun-26	25-Jun-26		
DC.IB.PROC.220	GC Submittal Review (drywall)	5	26-Jun-26	02-Jul-26		
DC.IB.PROC.230	Designer Submittal Approval (drywall)	10	03-Jul-26	16-Jul-26		
DC.IB.PROC.240	Fabrication & Delivery (drywall)	10	17-Jul-26	31-Jul-26		
Doors and Frames		137	26-Feb-26 A	04-Sep-26		
DC.IB.PROC.250	Buyout (doors and frames)	55	26-Feb-26 A	03-Jun-26		
DC.IB.PROC.260	Submittal Development (doors and frames)	20	04-Jun-26	02-Jul-26		
DC.IB.PROC.270	GC Submittal Review (doors and frames)	5	03-Jul-26	09-Jul-26		
DC.IB.PROC.280	Designer Submittal Approval (doors and frames)	10	10-Jul-26	23-Jul-26		
DC.IB.PROC.290	Fabrication & Delivery (doors and frames)	30	27-Jul-26	04-Sep-26		
Door Hardware		175	26-Feb-26 A	28-Oct-26		
DC.IB.PROC.300	Buyout (door hardware)	55	26-Feb-26 A	03-Jun-26		
DC.IB.PROC.310	Submittal Development (door hardware)	20	04-Jun-26	02-Jul-26		
DC.IB.PROC.320	GC Submittal Review (door hardware)	2	03-Jul-26	06-Jul-26		
DC.IB.PROC.330	Designer Submittal Approval (door hardware)	10	07-Jul-26	20-Jul-26		
DC.IB.PROC.340	Fabrication & Delivery (door hardware)	70	21-Jul-26	28-Oct-26		
OH Coiling Doors		142	26-Feb-26 A	11-Sep-26		

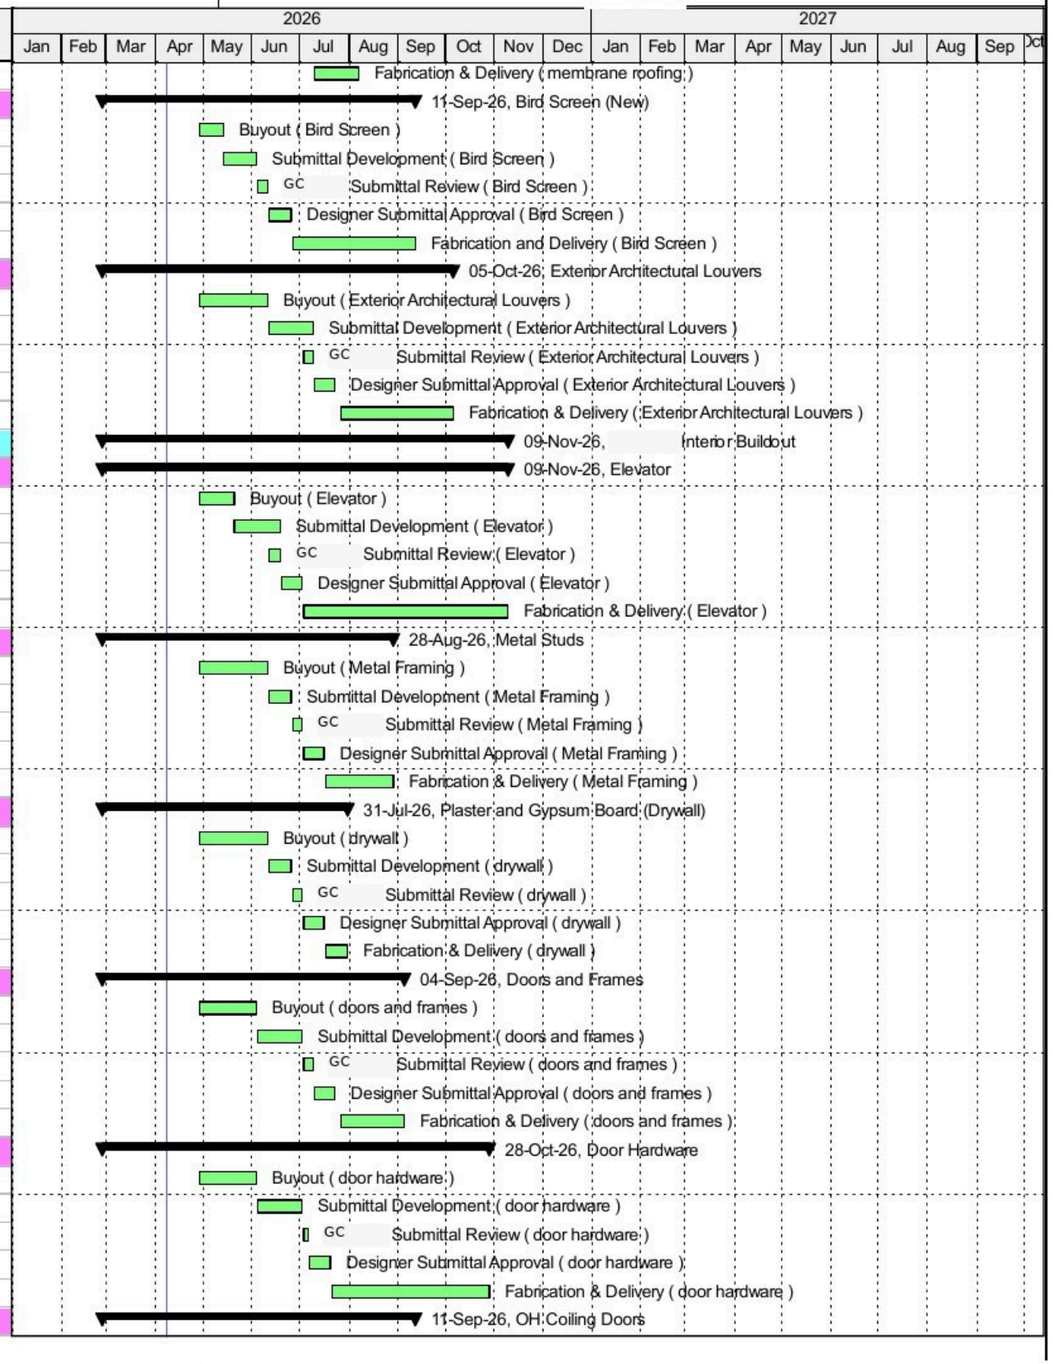


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
DC.IB.PROC.350	Buyout (OH Coiling Doors)	60	26-Feb-26 A	10-Jun-26		
DC.IB.PROC.360	Submittal Development (OH Coiling Doors)	10	11-Jun-26	25-Jun-26		
DC.IB.PROC.370	GC Submittal Review (OH Coiling Doors)	5	26-Jun-26	02-Jul-26		
DC.IB.PROC.380	Designer Submittal Approval (OH Coiling Doors)	10	03-Jul-26	16-Jul-26		
DC.IB.PROC.390	Fabrication & Delivery (OH Coiling Doors)	40	17-Jul-26	11-Sep-26		
Paint		117	26-Feb-26 A	07-Aug-26		
DC.IB.PROC.400	Buyout (paint)	70	26-Feb-26 A	25-Jun-26		
DC.IB.PROC.410	Submittal Development (paint)	10	26-Jun-26	09-Jul-26		
DC.IB.PROC.420	GC Submittal Review (paint)	5	03-Jul-26	09-Jul-26		
DC.IB.PROC.430	Designer Submittal Approval (paint)	10	10-Jul-26	23-Jul-26		
DC.IB.PROC.440	Fabrication & Delivery (paint)	10	27-Jul-26	07-Aug-26		
Acoustical Ceilings		122	26-Feb-26 A	14-Aug-26		
DC.IB.PROC.450	Buyout (acoustical ceilings)	60	26-Feb-26 A	10-Jun-26		
DC.IB.PROC.460	Submittal Development (acoustical ceilings)	10	11-Jun-26	25-Jun-26		
DC.IB.PROC.470	GC Submittal Review (acoustical ceilings)	5	26-Jun-26	02-Jul-26		
DC.IB.PROC.480	Designer Submittal Approval (acoustical ceilings)	10	03-Jul-26	16-Jul-26		
DC.IB.PROC.490	Fabrication & Delivery (acoustical ceilings)	20	17-Jul-26	14-Aug-26		
Tile		163	26-Feb-26 A	12-Oct-26		
DC.IB.PROC.500	Buyout (tile)	60	26-Feb-26 A	10-Jun-26		
DC.IB.PROC.510	Submittal Development (tile)	10	11-Jun-26	25-Jun-26		
DC.IB.PROC.520	GC Submittal Review (tile)	5	26-Jun-26	02-Jul-26		
DC.IB.PROC.530	Designer Submittal Approval (tile)	10	03-Jul-26	16-Jul-26		
DC.IB.PROC.540	Fabrication & Delivery (tile)	60	17-Jul-26	12-Oct-26		
Wood Trim / Millwork		168	26-Feb-26 A	19-Oct-26		
DC.IB.PROC.550	Buyout (Wood Trim / Millwork)	75	26-Feb-26 A	02-Jul-26		
DC.IB.PROC.560	Submittal Development (Wood Trim / Millwork)	20	03-Jul-26	31-Jul-26		
DC.IB.PROC.570	GC Submittal Review (Wood Trim / Millwork)	5	03-Aug-26	07-Aug-26		
DC.IB.PROC.580	Designer Submittal Approval (Wood Trim / Millwork)	10	10-Aug-26	21-Aug-26		
DC.IB.PROC.590	Fabrication & Delivery (Wood Trim / Millwork)	40	24-Aug-26	19-Oct-26		
Bathroom Vanity Tops		168	26-Feb-26 A	19-Oct-26		
DC.IB.PROC.600	Buyout (Bathroom Vanity Tops)	75	26-Feb-26 A	02-Jul-26		
DC.IB.PROC.610	Submittal Development (Bathroom Vanity Tops)	20	03-Jul-26	31-Jul-26		
DC.IB.PROC.620	GC Submittal Review (Bathroom Vanity Tops)	5	03-Aug-26	07-Aug-26		
DC.IB.PROC.630	Designer Submittal Approval (Bathroom Vanity Tops)	10	10-Aug-26	21-Aug-26		
DC.IB.PROC.640	Fabrication & Delivery (Bathroom Vanity Tops)	40	24-Aug-26	19-Oct-26		
Unit Bathroom Mirrors		137	26-Feb-26 A	04-Sep-26		
DC.IB.PROC.650	Buyout (Unit Bathroom Mirrors)	75	26-Feb-26 A	02-Jul-26		
DC.IB.PROC.660	Submittal Development (Unit Bathroom Mirrors)	10	03-Jul-26	16-Jul-26		
DC.IB.PROC.670	GC Submittal Review (Unit Bathroom Mirrors)	5	17-Jul-26	23-Jul-26		
DC.IB.PROC.680	Designer Submittal Approval (Unit Bathroom Mirrors)	10	27-Jul-26	07-Aug-26		
DC.IB.PROC.690	Fabrication & Delivery (Unit Bathroom Mirrors)	20	10-Aug-26	04-Sep-26		
Flooring		158	26-Feb-26 A	05-Oct-26		
DC.IB.PROC.700	Buyout (flooring)	75	26-Feb-26 A	02-Jul-26		
DC.IB.PROC.710	Submittal Development (flooring)	10	03-Jul-26	16-Jul-26		
DC.IB.PROC.720	GC Submittal Review (flooring)	5	17-Jul-26	23-Jul-26		

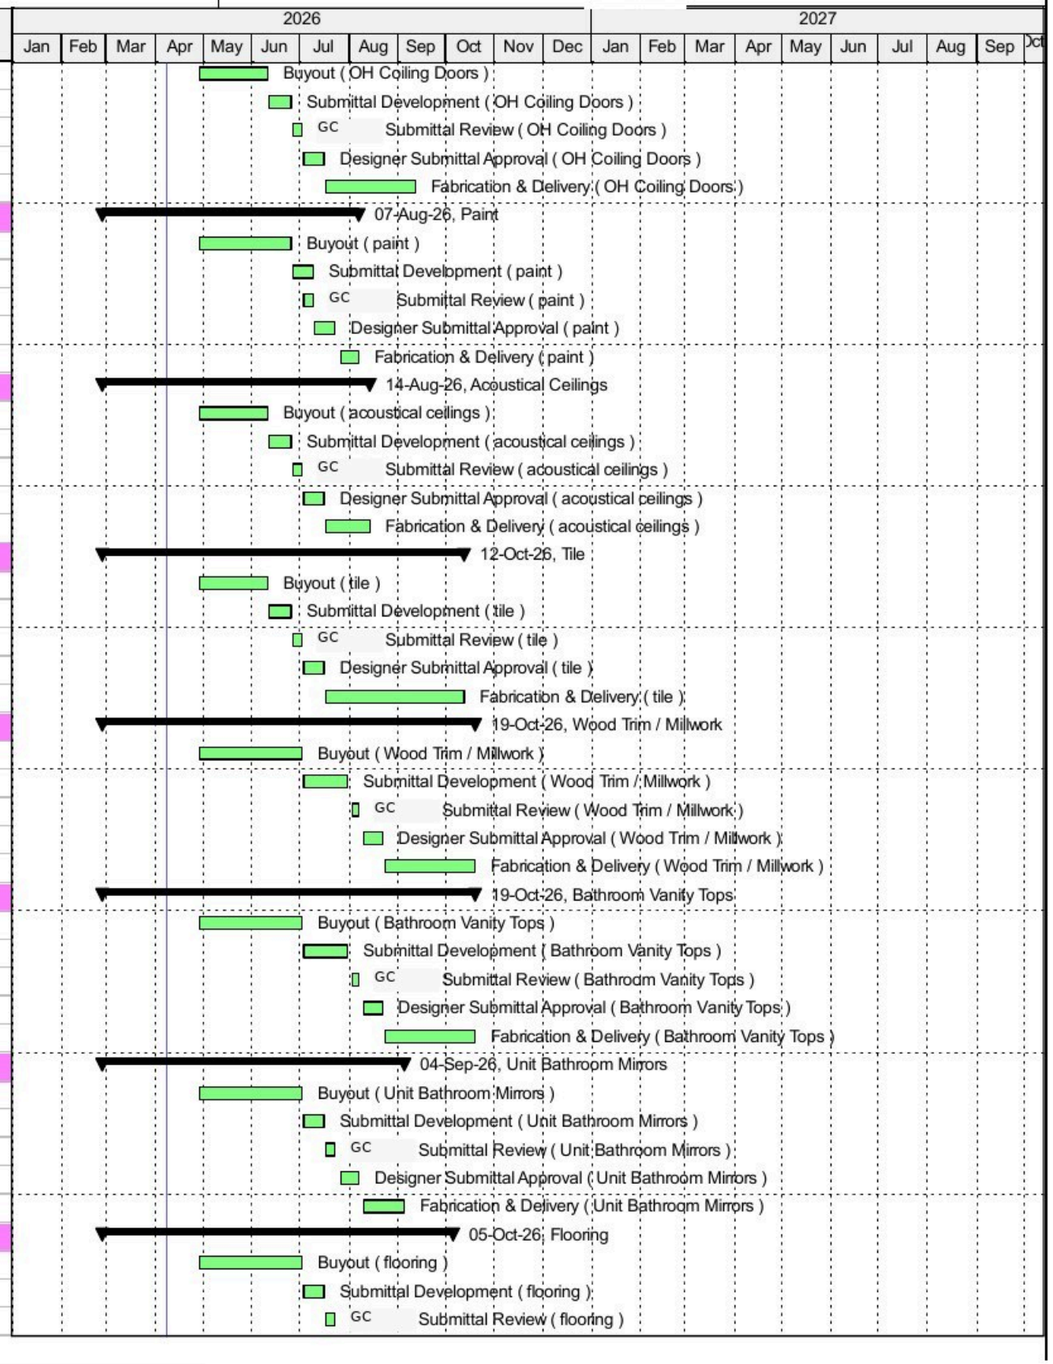


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
DC.IB.PROC.730	Designer Submittal Approval (flooring)	10	27-Jul-26	07-Aug-26		
DC.IB.PROC.740	Fabrication & Delivery (flooring)	40	10-Aug-26	05-Oct-26		
Specialties		224	26-Feb-26 A	05-Jan-27		
Toilet Partitions / Specialties		183	26-Feb-26 A	09-Nov-26		
DC.IB.PROC.750	Buyout (toilet partitions / specialties)	70	26-Feb-26 A	25-Jun-26		
DC.IB.PROC.760	Submittal Development (toilet partitions / specialties)	30	26-Jun-26	07-Aug-26		
DC.IB.PROC.770	GC Submittal Review (toilet partitions / specialties)	5	10-Aug-26	14-Aug-26		
DC.IB.PROC.780	Designer Submittal Approval (toilet partitions / specialties)	10	17-Aug-26	28-Aug-26		
DC.IB.PROC.790	Fabrication & Delivery (toilet partitions / specialties)	50	31-Aug-26	09-Nov-26		
Fire Ext. Cabinets		208	26-Feb-26 A	14-Dec-26		
DC.IB.PROC.800	Buyout (Fire Ext. Cabinets)	70	26-Feb-26 A	25-Jun-26		
DC.IB.PROC.810	Submittal Development (Fire Ext. Cabinets)	10	26-Jun-26	09-Jul-26		
DC.IB.PROC.820	GC Submittal Review (Fire Ext. Cabinets)	5	10-Jul-26	16-Jul-26		
DC.IB.PROC.830	Designer Submittal Approval (Fire Ext. Cabinets)	10	17-Jul-26	31-Jul-26		
DC.IB.PROC.840	Fabrication & Delivery (Fire Ext. Cabinets)	95	03-Aug-26	14-Dec-26		
Interior Signage		137	26-Feb-26 A	04-Sep-26		
DC.IB.PROC.850	Buyout (Interior Signage)	75	26-Feb-26 A	02-Jul-26		
DC.IB.PROC.860	Submittal Development (Interior Signage)	20	03-Jul-26	31-Jul-26		
DC.IB.PROC.870	GC Submittal Review (Interior Signage)	5	03-Aug-26	07-Aug-26		
DC.IB.PROC.880	Designer Submittal Approval (Interior Signage)	10	10-Aug-26	21-Aug-26		
DC.IB.PROC.890	Fabrication & Delivery (Interior Signage)	10	24-Aug-26	04-Sep-26		
Furniture		168	26-Feb-26 A	19-Oct-26		
DC.IB.PROC.900	Buyout (Furniture)	80	26-Feb-26 A	09-Jul-26		
DC.IB.PROC.910	Submittal Development (Furniture)	10	10-Jul-26	23-Jul-26		
DC.IB.PROC.920	GC Submittal Review (Furniture)	5	27-Jul-26	31-Jul-26		
DC.IB.PROC.930	Designer Submittal Approval (Furniture)	10	03-Aug-26	14-Aug-26		
DC.IB.PROC.940	Fabrication & Delivery (Furniture)	45	17-Aug-26	19-Oct-26		
Dock Equipment		118	26-Feb-26 A	10-Aug-26		
DC.IB.PROC.950	Buyout (Dock Equipment)	60	26-Feb-26 A	10-Jun-26		
DC.IB.PROC.960	Submittal Development (Dock Equipment)	10	11-Jun-26	25-Jun-26		
DC.IB.PROC.970	GC Submittal Review (Dock Equipment)	1	26-Jun-26	26-Jun-26		
DC.IB.PROC.980	Designer Submittal Approval (Dock Equipment)	10	29-Jun-26	10-Jul-26		
DC.IB.PROC.990	Fabrication & Delivery (Dock Equipment)	20	13-Jul-26	10-Aug-26		
Lockers		224	26-Feb-26 A	05-Jan-27		
DC.IB.PROC.1000	Buyout (Lockers)	75	26-Feb-26 A	02-Jul-26		
DC.IB.PROC.1010	Submittal Development (Lockers)	10	03-Jul-26	16-Jul-26		
DC.IB.PROC.1020	GC Submittal Review (Lockers)	5	17-Jul-26	23-Jul-26		
DC.IB.PROC.1030	Designer Submittal Approval (Lockers)	10	27-Jul-26	07-Aug-26		
DC.IB.PROC.1040	Fabrication & Delivery (Lockers)	105	10-Aug-26	05-Jan-27		
Hot Aisle Containment (HAC)		193	26-Feb-26 A	23-Nov-26		
DC.IB.PROC.1050	Buyout (HACs)	60	26-Feb-26 A	10-Jun-26		
DC.IB.PROC.1060	Submittal Development (HACs)	20	11-Jun-26	09-Jul-26		
DC.IB.PROC.1070	GC Submittal Review (HACs)	5	10-Jul-26	16-Jul-26		
DC.IB.PROC.1080	Designer Submittal Review (HACs)	10	17-Jul-26	31-Jul-26		
DC.IB.PROC.1090	Frabrication & Delivery (HACs)	80	03-Aug-26	23-Nov-26		

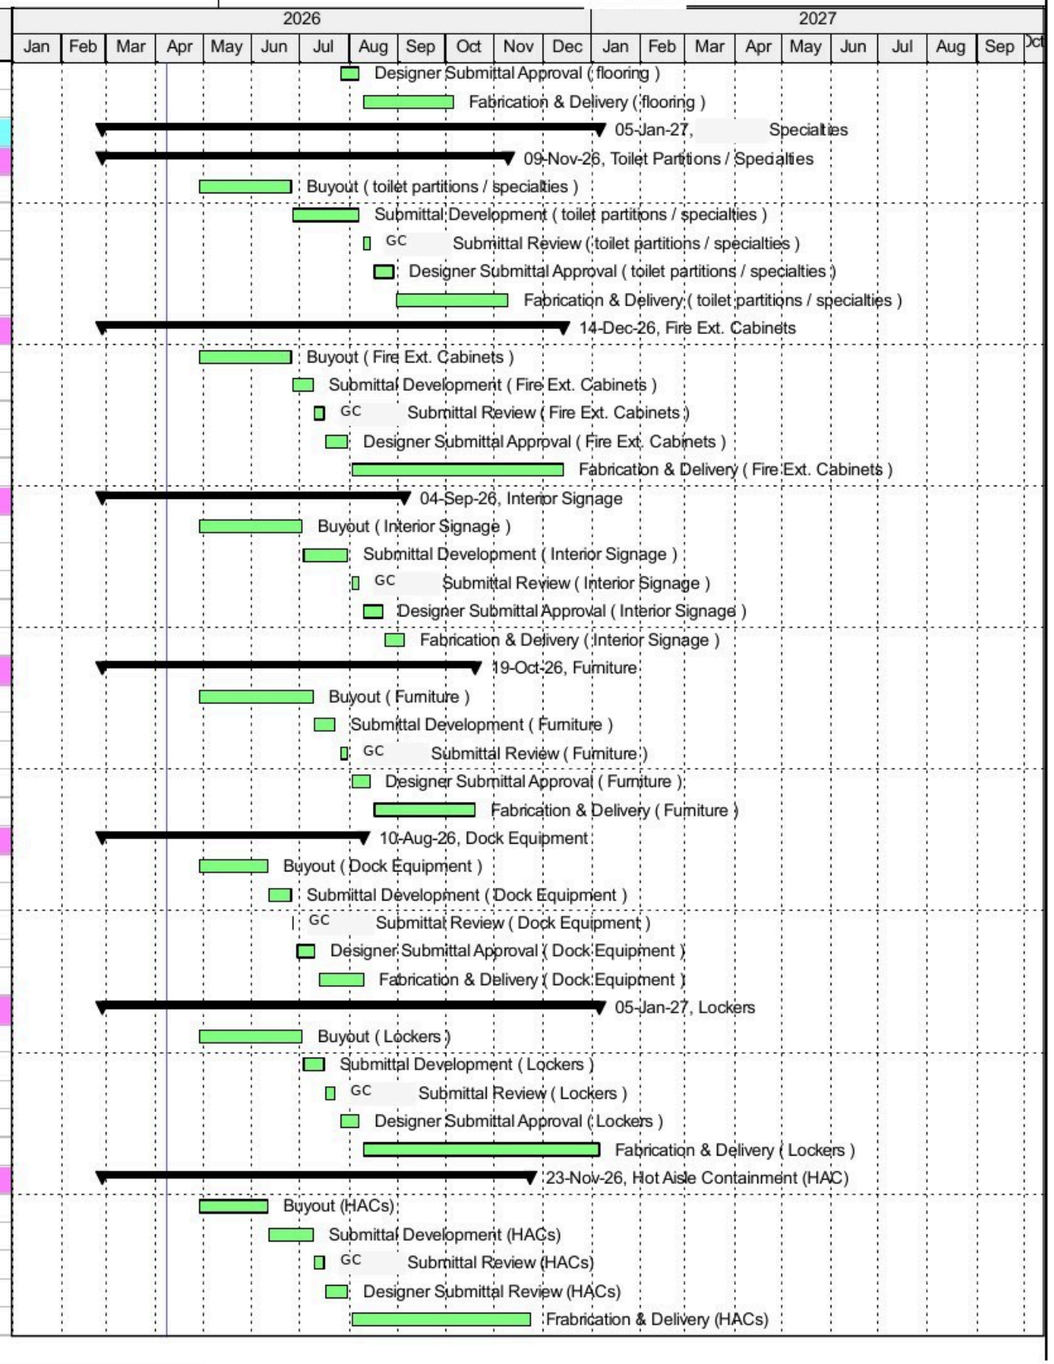


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Fire Protection		127	26-Feb-26 A	21-Aug-26		
Fire Sprinkler		127	26-Feb-26 A	21-Aug-26		
DC.MEPF.PROC.100	Buyout (fire sprinkler)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.110	Submittal Development (fire sprinkler)	20	14-May-26	10-Jun-26		
DC.MEPF.PROC.120	GC Submittal Review (fire sprinkler)	5	11-Jun-26	18-Jun-26		
DC.MEPF.PROC.130	Designer Submittal Approval (fire sprinkler)	10	19-Jun-26	02-Jul-26		
DC.MEPF.PROC.140	Fabrication & Delivery (fire sprinkler)	35	03-Jul-26	21-Aug-26		
Plumbing		247	26-Feb-26 A	05-Feb-27		
Plumbing Piping / Accessories		96	26-Feb-26 A	09-Jul-26		
DC.MEPF.PROC.190	Buyout (plumbing piping / acc)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.200	Submittal Development (plumbing piping / acc)	20	14-May-26	10-Jun-26		
DC.MEPF.PROC.210	GC Submittal Review (plumbing piping / acc)	5	04-Jun-26	10-Jun-26		
DC.MEPF.PROC.220	Designer Submittal Approval (plumbing piping / acc)	10	11-Jun-26	25-Jun-26		
DC.MEPF.PROC.230	Fabrication & Delivery (plumbing piping / acc)	10	26-Jun-26	09-Jul-26		
IW Pumps/Tanks and OX Skid		214	26-Feb-26 A	22-Dec-26		
DC.MEPF.PROC.240	Buyout (IW Pumps/Tanks and OX Skid)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.250	Submittal Development (IW Pumps/Tanks and OX Skid)	20	14-May-26	10-Jun-26		
DC.MEPF.PROC.260	GC Submittal Review (IW Pumps/Tanks and OX Skid)	5	11-Jun-26	18-Jun-26		
DC.MEPF.PROC.270	Designer Submittal Approval (Water Tanks)	10	19-Jun-26	02-Jul-26		
DC.MEPF.PROC.280	Designer Submittal Approval (OX Skid)	10	19-Jun-26	02-Jul-26		
DC.MEPF.PROC.290	Designer Submittal Approval (IW Pumps)	10	19-Jun-26	02-Jul-26		
DC.MEPF.PROC.300	Fabrication & Delivery (IW Pumps Skid)	120	03-Jul-26	22-Dec-26		
DC.MEPF.PROC.310	Fabrication & Delivery (OX Skid)	120	03-Jul-26	22-Dec-26		
DC.MEPF.PROC.320	Fabrication & Delivery (Water Tanks)	70	03-Jul-26	12-Oct-26		
Plumbing Fixtures		122	26-Feb-26 A	14-Aug-26		
DC.MEPF.PROC.330	Buyout (plumbing fixtures)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.340	Submittal Development (plumbing fixtures)	20	14-May-26	10-Jun-26		
DC.MEPF.PROC.350	GC Submittal Review (plumbing fixtures)	5	04-Jun-26	10-Jun-26		
DC.MEPF.PROC.360	Designer Submittal Approval (plumbing fixtures)	10	11-Jun-26	25-Jun-26		
DC.MEPF.PROC.370	Fabrication & Delivery (plumbing fixtures)	35	26-Jun-26	14-Aug-26		
CFN Piping		247	26-Feb-26 A	05-Feb-27		
DC.MEPF.PROC.380	Buyout (CFN Piping / Passivation / Expansion Tanks)	40	26-Feb-26 A	13-May-26	Trade	CFN/SFN Pipir
DC.MEPF.PROC.390	Product Data Development (CFN Piping & Expansion Tanks)	20	14-May-26	10-Jun-26	Trade	CFN/SFN Pipir
DC.MEPF.PROC.420	Shop Drawing Development (CFN Piping)	25	26-Jun-26	31-Jul-26	Trade	CFN/SFN Pipir
DC.MEPF.PROC.430	Fabrication and Delivery (Expansion Tanks)	55	03-Jul-26	18-Sep-26	Trade	CFN/SFN Pipir
DC.MEPF.PROC.460	Fabrication and Delivery of Piping Materials (CFN Piping)	70	24-Aug-26	30-Nov-26	Trade	CFN/SFN Pipir
DC.MEPF.PROC.470	Fabrication of Phase 1 Piping Assembly	15	17-Nov-26	07-Dec-26	Trade	CFN/SFN Pipir
DC.MEPF.PROC.480	Passivating of Phase 1 Piping	10	08-Dec-26	22-Dec-26	Trade	CFN/SFN Pipir
DC.MEPF.PROC.490	Fabrication of Phase 2 Piping Assembly	15	08-Dec-26	29-Dec-26	Trade	CFN/SFN Pipir
DC.MEPF.PROC.500	Passivating of Phase 2 Piping	10	30-Dec-26	12-Jan-27	Trade	CFN/SFN Pipir
DC.MEPF.PROC.510	Fabrication of Phase 3 Piping Assembly	15	30-Dec-26	21-Jan-27	Trade	CFN/SFN Pipir
DC.MEPF.PROC.520	Passivating of Phase 3 Piping	10	25-Jan-27	05-Feb-27	Trade	CFN/SFN Pipir
DC.MEPF.PROC.400	GC Product Data Review (CFN Piping & Expansion Tanks)	5	11-Jun-26	18-Jun-26		
DC.MEPF.PROC.410	Designer Product Data Approval (CFN Piping & Expansion Tanks)	10	19-Jun-26	02-Jul-26		
DC.MEPF.PROC.440	GC Shop Drawing Review (CFN Piping)	5	03-Aug-26	07-Aug-26		

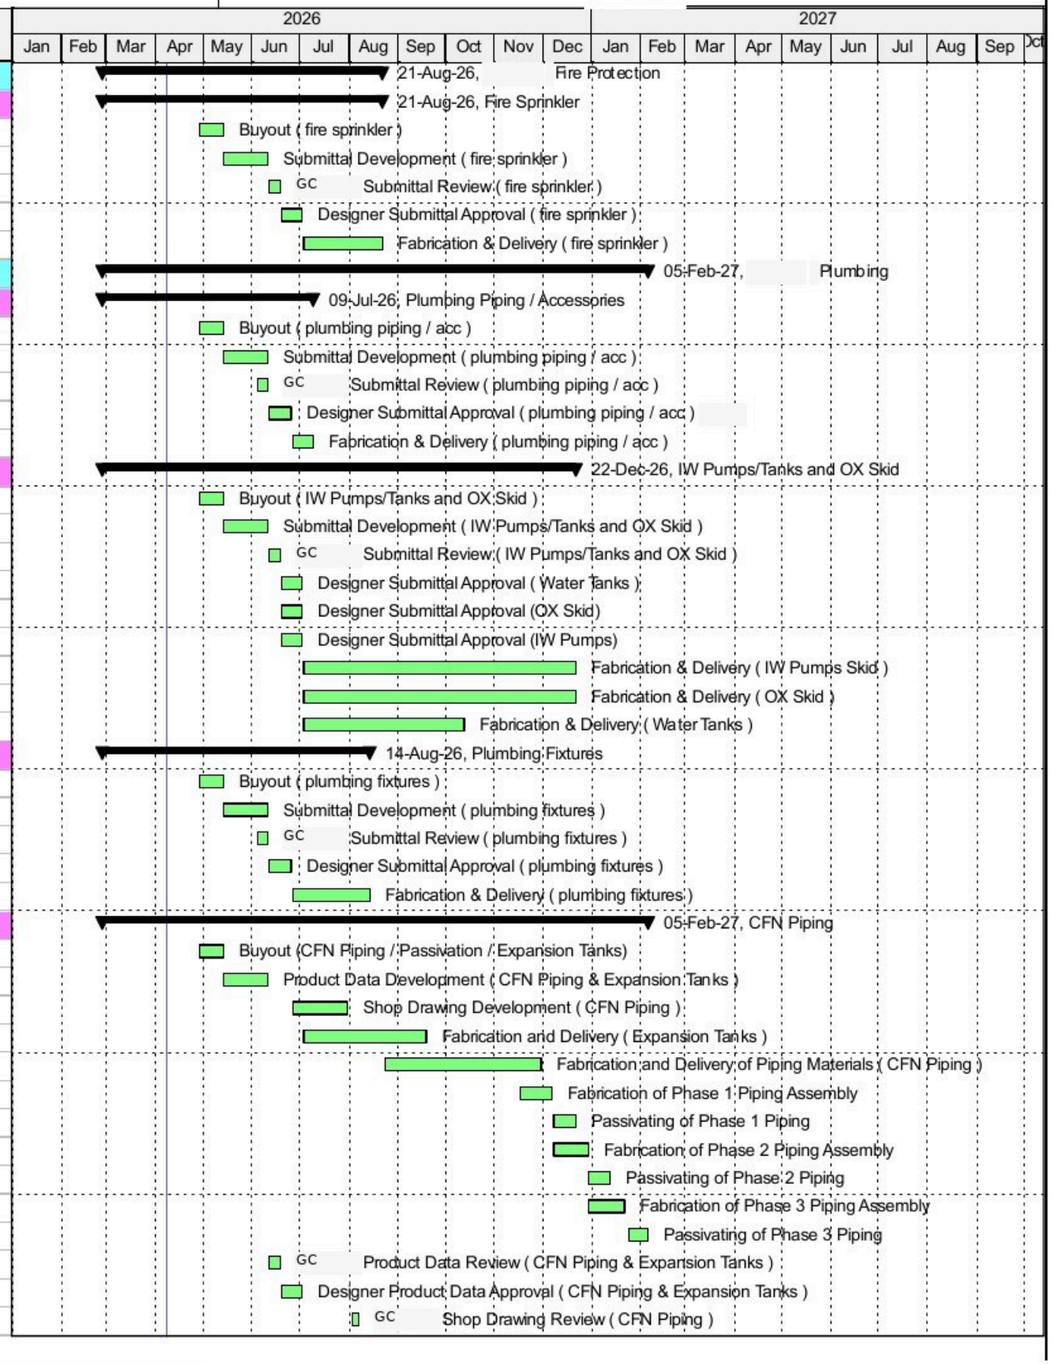


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
DC.MEPF.PROC.450	Designer Shop Drawing Approval (CFN Piping)	10	10-Aug-26	21-Aug-26		
Mechanical		188	26-Feb-26 A	16-Nov-26		
Fuel Oil Equipment		173	26-Feb-26 A	26-Oct-26		
DC.MEPF.PROC.530	Buyout (Fuel Oil Equipment)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.540	Submittal Development (Fuel Oil Equipment)	30	14-May-26	25-Jun-26		
DC.MEPF.PROC.550	GC Submittal Review (Fuel Oil Equipment)	5	19-Jun-26	25-Jun-26		
DC.MEPF.PROC.560	Designer Submittal Approval (Fuel Oil Equipment)	10	26-Jun-26	09-Jul-26		
DC.MEPF.PROC.570	Fabrication & Delivery (Fuel Oil Equipment)	75	10-Jul-26	26-Oct-26		
Industrial Water Piping		101	26-Feb-26 A	16-Jul-26		
DC.MEPF.PROC.580	Buyout (Industrial Water Piping)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.590	Submittal Development (Industrial Water Piping)	20	14-May-26	10-Jun-26		
DC.MEPF.PROC.600	GC Submittal Review (Industrial Water Piping)	5	04-Jun-26	10-Jun-26		
DC.MEPF.PROC.610	Designer Submittal Approval (Industrial Water Piping)	10	11-Jun-26	25-Jun-26		
DC.MEPF.PROC.620	Fabrication & Delivery (Industrial Water Pip in g)	15	26-Jun-26	16-Jul-26		
Office BAS Controls		127	26-Feb-26 A	21-Aug-26		
DC.MEPF.PROC.630	Buyout (Office BAS Controls)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.640	Submittal Development (Office BAS Controls)	40	14-May-26	09-Jul-26		
DC.MEPF.PROC.650	GC Submittal Review (Office BAS Controls)	5	03-Jul-26	09-Jul-26		
DC.MEPF.PROC.660	Designer Submittal Approval (Office BAS Controls)	10	10-Jul-26	23-Jul-26		
DC.MEPF.PROC.670	Fabrication & Delivery (Office BAS Controls)	20	27-Jul-26	21-Aug-26		
Exterior Mechanical Louvers		142	26-Feb-26 A	11-Sep-26		
DC.MEPF.PROC.680	Buyout (Exterior Mechanical Louvers)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.690	Submittal Development (Exterior Mechanical Louvers)	15	14-May-26	03-Jun-26		
DC.MEPF.PROC.700	GC Submittal Review (Exterior Mechanical Louvers)	5	28-May-26	03-Jun-26		
DC.MEPF.PROC.710	Designer Submittal Approval (Exterior Mechanical Louvers)	10	04-Jun-26	18-Jun-26		
DC.MEPF.PROC.720	Fabrication & Delivery (Exterior Mechanical Louvers)	60	19-Jun-26	11-Sep-26		
Sound Attenuators		147	26-Feb-26 A	18-Sep-26		
DC.MEPF.PROC.730	Buyout (Sound Attenuators)	40	26-Feb-26 A	13-May-26	Trade	HVAC
DC.MEPF.PROC.740	Submittal Development (Sound Attenuators)	15	14-May-26	03-Jun-26	Trade	HVAC
DC.MEPF.PROC.770	Fabrication & Delivery (Sound Attenuators)	60	26-Jun-26	18-Sep-26	Trade	HVAC
DC.MEPF.PROC.750	GC Submittal Review (Sound Attenuators)	5	04-Jun-26	10-Jun-26		
DC.MEPF.PROC.760	Designer Submittal Approval (Sound Attenuators)	10	11-Jun-26	25-Jun-26		
Ductwork		112	26-Feb-26 A	31-Jul-26		
DC.MEPF.PROC.780	Buyout (ductwork)	40	26-Feb-26 A	13-May-26	Trade	HVAC
DC.MEPF.PROC.790	Submittal Development (ductwork)	20	14-May-26	10-Jun-26	Trade	HVAC
DC.MEPF.PROC.820	Fabrication & Delivery (ductwork)	25	26-Jun-26	31-Jul-26	Trade	HVAC
DC.MEPF.PROC.800	GC Submittal Review (ductwork)	5	04-Jun-26	10-Jun-26		
DC.MEPF.PROC.810	Designer Submittal Approval (ductwork)	10	11-Jun-26	25-Jun-26		
Duct Insulation		112	26-Feb-26 A	31-Jul-26		
DC.MEPF.PROC.830	Buyout (duct insulation)	40	26-Feb-26 A	13-May-26	Trade	HVAC
DC.MEPF.PROC.840	Submittal Development (duct insulation)	20	14-May-26	10-Jun-26	Trade	HVAC
DC.MEPF.PROC.870	Fabrication & Delivery (duct insulation)	25	26-Jun-26	31-Jul-26	Trade	HVAC
DC.MEPF.PROC.850	GC Submittal Review (duct insulation)	5	04-Jun-26	10-Jun-26		
DC.MEPF.PROC.860	Designer Submittal Approval (duct insulation)	10	11-Jun-26	25-Jun-26		
Grilles / Diffusers		106	26-Feb-26 A	23-Jul-26		

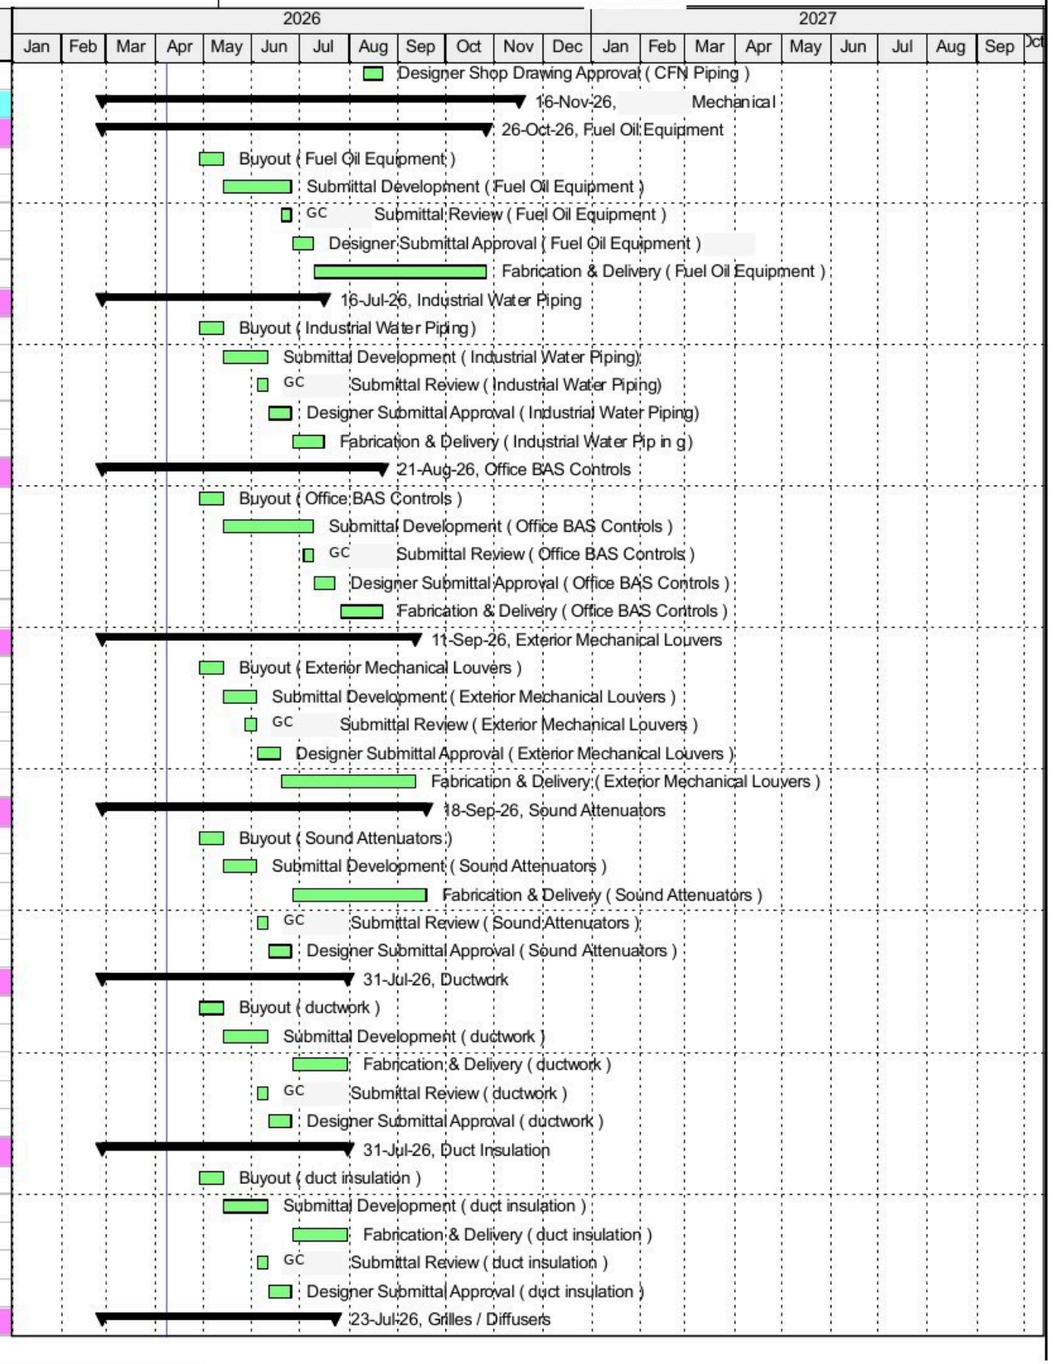


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
DC.MEPF.PROC.880	Buyout (grilles / diffusers)	40	26-Feb-26 A	13-May-26	Trade	HVAC
DC.MEPF.PROC.890	Submittal Development (grilles / diffusers)	20	14-May-26	10-Jun-26	Trade	HVAC
DC.MEPF.PROC.920	Fabrication & Delivery (grilles / diffusers)	20	26-Jun-26	23-Jul-26	Trade	HVAC
DC.MEPF.PROC.900	GC Submittal Review (grilles / diffusers)	5	04-Jun-26	10-Jun-26		
DC.MEPF.PROC.910	Designer Submittal Approval (grilles / diffusers)	10	11-Jun-26	25-Jun-26		
ERV's		132	26-Feb-26 A	28-Aug-26		
DC.MEPF.PROC.930	Buyout (ERV's)	40	26-Feb-26 A	13-May-26	Trade	HVAC
DC.MEPF.PROC.940	Submittal Development (ERV's)	20	14-May-26	10-Jun-26	Trade	HVAC
DC.MEPF.PROC.970	Fabrication & Delivery (ERV's)	45	26-Jun-26	28-Aug-26	Trade	HVAC
DC.MEPF.PROC.950	GC Submittal Review (ERV's)	5	04-Jun-26	10-Jun-26		
DC.MEPF.PROC.960	Designer Submittal Approval (ERV's)	10	11-Jun-26	25-Jun-26		
EF VFD's		178	26-Feb-26 A	02-Nov-26		
DC.MEPF.PROC.980	Buyout (EF VFD's)	40	26-Feb-26 A	13-May-26	Trade	HVAC
DC.MEPF.PROC.990	Submittal Development (EF VFD's)	20	14-May-26	10-Jun-26	Trade	HVAC
DC.MEPF.PROC.1020	Fabrication & Delivery (EF VFD's)	90	26-Jun-26	02-Nov-26	Trade	HVAC
DC.MEPF.PROC.1000	GC Submittal Review (EF VFD's)	5	04-Jun-26	10-Jun-26		
DC.MEPF.PROC.1010	Designer Submittal Approval (EF VFD's)	10	11-Jun-26	25-Jun-26		
Roof Top Unit		188	26-Feb-26 A	16-Nov-26		
DC.MEPF.PROC.1030	Buyout (RTU)	40	26-Feb-26 A	13-May-26	Trade	HVAC
DC.MEPF.PROC.1040	Submittal Development (RTU)	20	14-May-26	10-Jun-26	Trade	HVAC
DC.MEPF.PROC.1070	Fabrication & Delivery (RTU)	100	26-Jun-26	16-Nov-26	Trade	HVAC
DC.MEPF.PROC.1050	GC Submittal Review (RTU)	5	04-Jun-26	10-Jun-26		
DC.MEPF.PROC.1060	Designer Submittal Approval (RTU)	10	11-Jun-26	25-Jun-26		
CRAC Units		178	26-Feb-26 A	02-Nov-26		
DC.MEPF.PROC.1080	Buyout (CRAC Units)	40	26-Feb-26 A	13-May-26	Trade	HVAC
DC.MEPF.PROC.1090	Submittal Development (CRAC Units)	20	14-May-26	10-Jun-26	Trade	HVAC
DC.MEPF.PROC.1120	Fabrication & Delivery (CRAC Units)	90	26-Jun-26	02-Nov-26	Trade	HVAC
DC.MEPF.PROC.1100	GC Submittal Review (CRAC Units)	5	04-Jun-26	10-Jun-26		
DC.MEPF.PROC.1110	Designer Submittal Approval (CRAC Units)	10	11-Jun-26	25-Jun-26		
VAVs		122	26-Feb-26 A	14-Aug-26		
DC.MEPF.PROC.1130	Buyout (VAVs)	40	26-Feb-26 A	13-May-26	Trade	HVAC
DC.MEPF.PROC.1140	Submittal Development (VAVs)	30	14-May-26	25-Jun-26	Trade	HVAC
DC.MEPF.PROC.1170	Fabrication & Delivery (VAVs)	20	17-Jul-26	14-Aug-26	Trade	HVAC
DC.MEPF.PROC.1150	GC Submittal Review (VAVs)	5	26-Jun-26	02-Jul-26		
DC.MEPF.PROC.1160	Designer Submittal Approval (VAVs)	10	03-Jul-26	16-Jul-26		
Exhaust Fans		152	26-Feb-26 A	25-Sep-26		
DC.MEPF.PROC.1180	Buyout (EFs)	40	26-Feb-26 A	13-May-26	Trade	HVAC
DC.MEPF.PROC.1190	Submittal Development (EFs)	20	14-May-26	10-Jun-26	Trade	HVAC
DC.MEPF.PROC.1220	Fabrication & Delivery (EFs)	60	03-Jul-26	25-Sep-26	Trade	HVAC
DC.MEPF.PROC.1200	GC Submittal Review (EFs)	5	11-Jun-26	18-Jun-26		
DC.MEPF.PROC.1210	Designer Submittal Approval (EFs)	10	19-Jun-26	02-Jul-26		
Split Systems (ICUs/ISUs/OSUs)		122	26-Feb-26 A	14-Aug-26		
DC.MEPF.PROC.1230	Buyout (ICUs / ISUs / OSUs)	40	26-Feb-26 A	13-May-26	Trade	HVAC
DC.MEPF.PROC.1240	Submittal Development (ICUs / ISUs / OSUs)	30	14-May-26	25-Jun-26	Trade	HVAC
DC.MEPF.PROC.1270	Fabrication & Delivery (ICUs / ISUs / OSUs)	20	17-Jul-26	14-Aug-26	Trade	HVAC

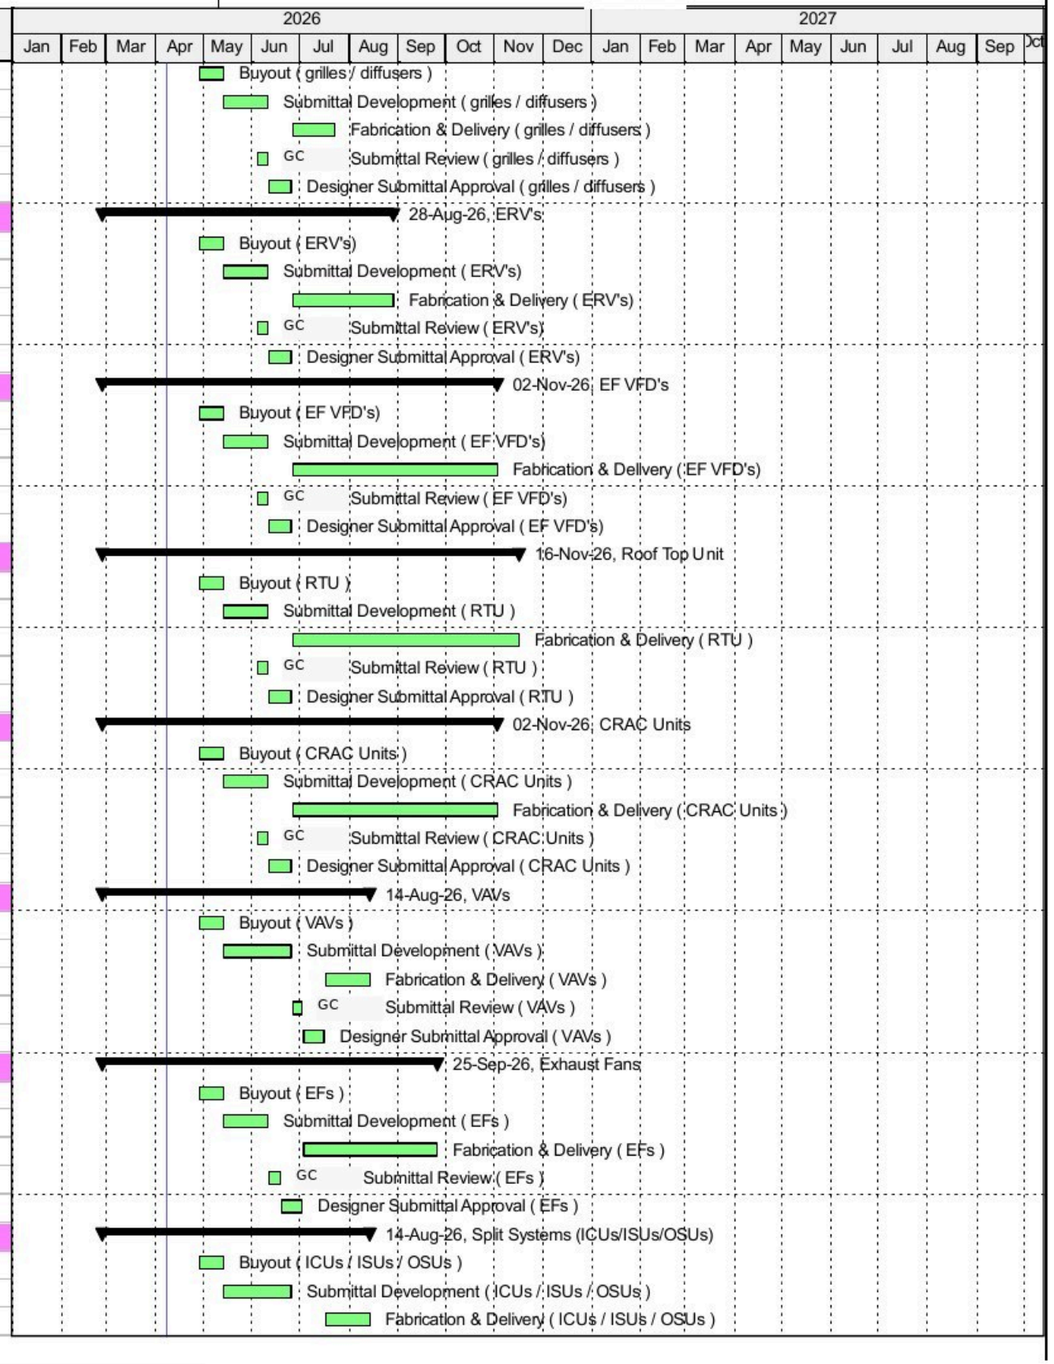


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
DC.MEPF.PROC.1250	GC Submittal Review (ICUs / ISUs / OSUs)	5	26-Jun-26	02-Jul-26		
DC.MEPF.PROC.1260	Designer Submittal Approval (ICUs / ISUs / OSUs)	10	03-Jul-26	16-Jul-26		
Electrical		193	26-Feb-26 A	23-Nov-26		
MV Cable		112	26-Feb-26 A	31-Jul-26		
DC.MEPF.PROC.1280	Buyout (MV Cable)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.1290	Submittal Development (MV Cable)	15	14-May-26	03-Jun-26		
DC.MEPF.PROC.1300	GC Submittal Review (MV Cable)	5	28-May-26	03-Jun-26		
DC.MEPF.PROC.1310	Designer Submittal Approval (MV Cable)	10	04-Jun-26	18-Jun-26		
DC.MEPF.PROC.1320	Fabrication & Delivery (MV Cable)	30	19-Jun-26	31-Jul-26		
Cable Bus		177	26-Feb-26 A	30-Oct-26		
DC.MEPF.PROC.1330	Buyout (Cable Bus)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.1340	Submittal Development (Cable Bus)	15	14-May-26	03-Jun-26		
DC.MEPF.PROC.1350	GC Submittal Review (Cable Bus)	5	04-Jun-26	10-Jun-26		
DC.MEPF.PROC.1360	Designer Submittal Approval (Cable Bus)	10	11-Jun-26	25-Jun-26		
DC.MEPF.PROC.1370	Fabrication & Delivery (Cable Bus)	90	25-Jun-26	30-Oct-26		
Conduit / Wiring		106	26-Feb-26 A	23-Jul-26		
DC.MEPF.PROC.1380	Buyout (conduit / wiring)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.1390	Submittal Development (Raceway)	20	14-May-26	10-Jun-26		
DC.MEPF.PROC.1400	GC Submittal Review (Raceway)	5	04-Jun-26	10-Jun-26		
DC.MEPF.PROC.1410	Designer Submittal Approval (Raceway)	10	11-Jun-26	25-Jun-26		
DC.MEPF.PROC.1420	Fabrication & Delivery (Raceway)	20	26-Jun-26	23-Jul-26		
Lightning Protection		122	26-Feb-26 A	14-Aug-26		
DC.MEPF.PROC.1430	Buyout (Lightning Protection)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.1440	Submittal Development (Lightning Protection)	40	14-May-26	09-Jul-26		
DC.MEPF.PROC.1450	GC Submittal Review (Lightning Protection)	5	10-Jul-26	16-Jul-26		
DC.MEPF.PROC.1460	Designer Submittal Approval (Lightning Protection)	10	17-Jul-26	31-Jul-26		
DC.MEPF.PROC.1470	Fabrication & Delivery (Lightning Protection)	10	03-Aug-26	14-Aug-26		
Light Fixtures (standard / Non decorative)		122	26-Feb-26 A	14-Aug-26		
DC.MEPF.PROC.1480	Buyout (standard light fixtures)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.1490	Submittal Development (standard light fixtures)	40	14-May-26	09-Jul-26		
DC.MEPF.PROC.1500	GC Submittal Review (standard light fixtures)	5	10-Jul-26	16-Jul-26		
DC.MEPF.PROC.1510	Designer Submittal Approval (standard light fixtures)	10	17-Jul-26	31-Jul-26		
DC.MEPF.PROC.1520	Fabrication & Delivery (standard light fixtures)	10	03-Aug-26	14-Aug-26		
Cable Tray		142	26-Feb-26 A	11-Sep-26		
DC.MEPF.PROC.1530	Buyout (comm/data/low volt)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.1540	Submittal Development (comm/data/low volt)	25	14-May-26	18-Jun-26		
DC.MEPF.PROC.1550	Designer Submittal Approval (comm/data/low volt)	10	04-Jun-26	18-Jun-26		
DC.MEPF.PROC.1560	GC Submittal Review (comm/data/low volt)	5	11-Jun-26	18-Jun-26		
DC.MEPF.PROC.1570	Fabrication & Delivery (comm/data/low volt)	60	19-Jun-26	11-Sep-26		
Vesda		163	26-Feb-26 A	12-Oct-26		
DC.MEPF.PROC.1580	Buyout (Vesda)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.1590	Submittal Development (Vesda)	40	14-May-26	09-Jul-26		
DC.MEPF.PROC.1600	GC Submittal Review (Vesda)	5	10-Jul-26	16-Jul-26		
DC.MEPF.PROC.1610	Designer Submittal Approval (Vesda)	10	17-Jul-26	31-Jul-26		
DC.MEPF.PROC.1620	Fabrication & Delivery (Vesda)	50	03-Aug-26	12-Oct-26		

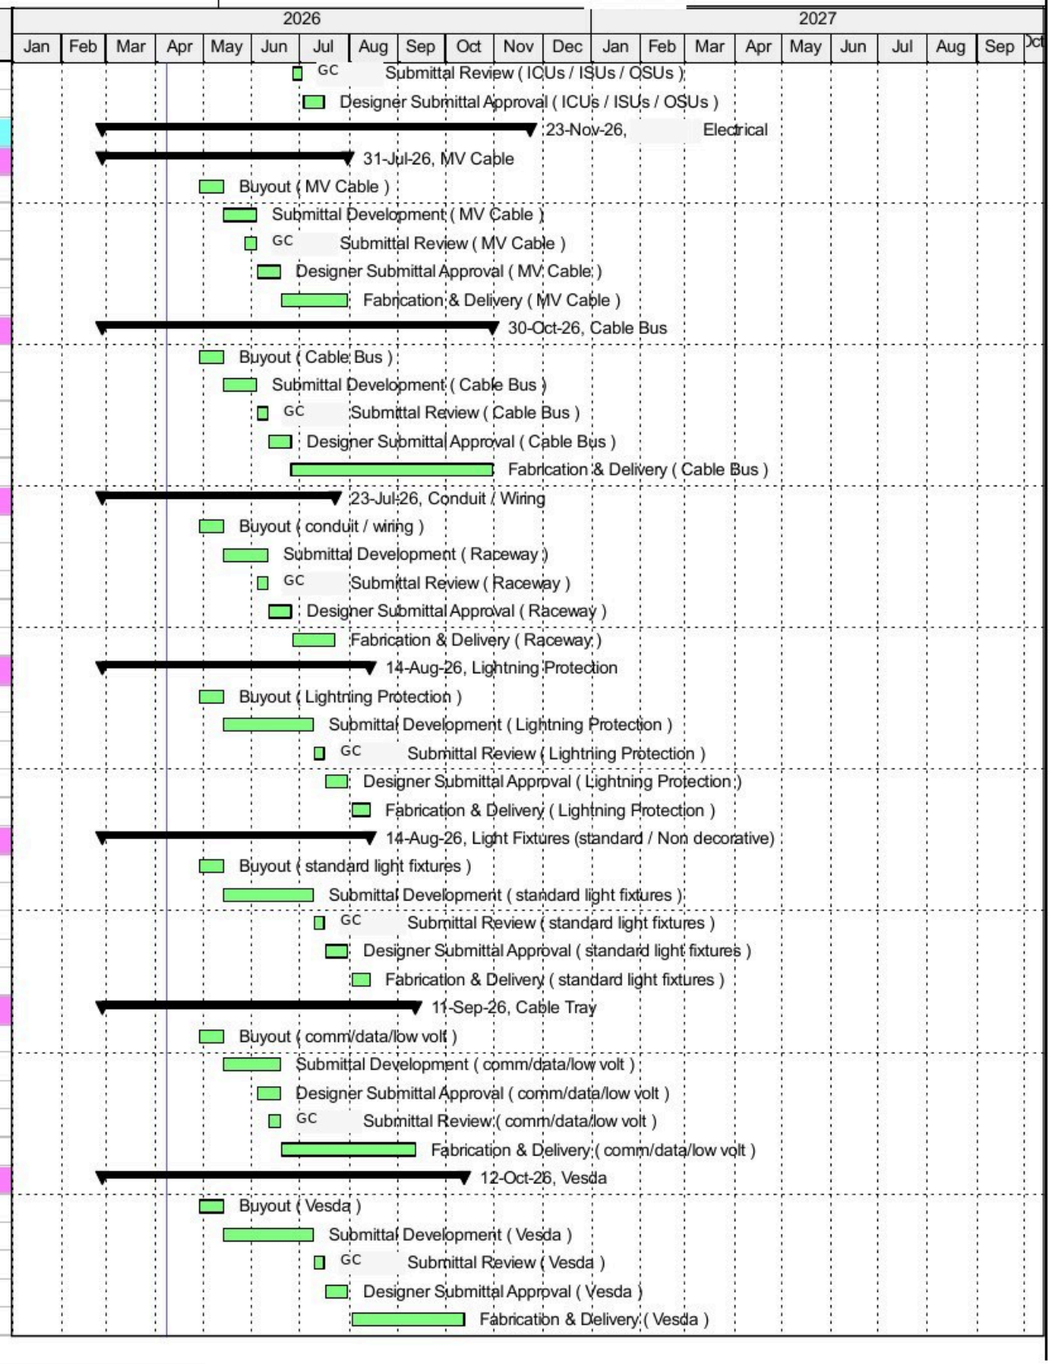


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Fire Alarm		132	26-Feb-26 A	28-Aug-26		
DC.MEPF.PROC.1630	Buyout (fire alarm)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.1640	Submittal Development (fire alarm)	40	14-May-26	09-Jul-26		
DC.MEPF.PROC.1650	GC Submittal Review (fire alarm)	5	10-Jul-26	16-Jul-26		
DC.MEPF.PROC.1660	Designer Submittal Approval (fire alarm)	10	17-Jul-26	31-Jul-26		
DC.MEPF.PROC.1670	Fabrication & Delivery (fire alarm)	20	03-Aug-26	28-Aug-26		
600V MC Feeder Cable (4C/500)		193	26-Feb-26 A	23-Nov-26		
DC.MEPF.PROC.1680	Buyout (MC Feeder)	40	26-Feb-26 A	13-May-26		
DC.MEPF.PROC.1690	Submittal Development (MC Feeder)	15	14-May-26	03-Jun-26		
DC.MEPF.PROC.1700	GC Submittal Review (MC Feeder)	5	28-May-26	03-Jun-26		
DC.MEPF.PROC.1710	Designer Submittal Approval (MC Feeder)	10	04-Jun-26	18-Jun-26		
DC.MEPF.PROC.1720	Fabrication & Delivery (MC Feeder)	110	19-Jun-26	23-Nov-26		
Procurement - Sub Provided		89	28-May-26	29-Sep-26		
Steel		89	28-May-26	29-Sep-26		
OWN.STEEL.PROC.100	Steel Fabrication Seq#17 thru 147 Main Steel	40	28-May-26	23-Jul-26		
OWN.STEEL.PROC.110	Steel Fabrication Seq#207 thru 237 Gallery Wall Framing and Louve	40	12-Jun-26	10-Aug-26		
OWN.STEEL.PROC.120	Steel Fabrication Seq#307 thru 337 F-Line Framing Near or at Top o	40	06-Jul-26	31-Aug-26		
OWN.STEEL.PROC.140	Steel Fabrication Seq#507 Thru 527 Gen Yard Flue Support and Pla	40	04-Aug-26	29-Sep-26		
OWN.STEEL.PROC.130	Steel Fabrication Seq#407 thru 427 Screen Wall & Cable Tray Suppo	40	20-Jul-26	14-Sep-26		
OFCI		116	25-Sep-26	08-Mar-27		
OFCI Equipment Deliveries		101	16-Oct-26	08-Mar-27		
ROMP1 & ROMP2 - OFCI Equipment		56	16-Oct-26	04-Jan-27		
DC.OFCI.PH1.140	PH1 - Data Hall Air Handling Units (TAHU) (ROJ: 09/25/26)	0	16-Oct-26			
DC.OFCI.PH1.200	PH1 - MV Switchgear (SWGR-MV) (ROJ: 9/28/26)	0	19-Oct-26			
DC.OFCI.PH1.230	PH1 - PDC Whips & Racking (ROJ: 10/5/26)	0	26-Oct-26			
DC.OFCI.PH1.210	PH1 - MV Transformers (USB-XFMR)(ROJ: 10/05/26)	0	26-Oct-26			
DC.OFCI.PH1.120	PH1 - Busduct (ROJ: 10/5/26)	0	26-Oct-26			
DC.OFCI.PH1.150	PH1 - Generators (GEN, GEN-CAM) (ROJ:10/12/26)	0	02-Nov-26			
DC.OFCI.PH1.100	PH1 - Owner Change Over Panel (AMCOP) (ROJ: 10/15/26)	0	05-Nov-26			
DC.OFCI.PH1.190	PH1 - MSDB (ROJ: 10/15/26)	0	05-Nov-26			
DC.OFCI.PH1.160	PH1 - HUPS & HUPS-MBP (ROJ: 10/15/26)	0	05-Nov-26			
DC.OFCI.PH1.180	PH1 - LV Panelboards and Transformers (ROJ: 10/15/26)	0	05-Nov-26			
DC.OFCI.PH1.130	PH1 - Busduct Skid (ROJ: 10/15/26)	0	05-Nov-26			
DC.OFCI.PH1.110	PH1 - ATS (ROJ: 10/15/26)	0	05-Nov-26			
DC.OFCI.PH1.220	PH1 - PDC (ROJ: 11/23/26)	0	14-Dec-26			
DC.OFCI.PH1.240	PH1 - SFN V 1.0, 1.2, & Piping (ROJ: 12/14/26)	0	04-Jan-27			
DC.OFCI.PH1.170	PH1 - IRHX (ROJ: 12/14/26)	0	04-Jan-27			
ROMP3 & ROMP4 - OFCI Equipment		52	05-Nov-26	18-Jan-27		
DC.OFCI.PH2.100	PH2 - Owner Change Over Panel (AMCOP) (ROJ: 10/15/26)	0	05-Nov-26			
DC.OFCI.PH2.200	PH2 - MSDB (ROJ: 10/15/26)	0	05-Nov-26			
DC.OFCI.PH2.190	PH2 - LV Switchgear (ROJ: 10/15/26)	0	05-Nov-26			
DC.OFCI.PH2.180	PH2 - LV Panelboards and Transformers (ROJ: 10/15/26)	0	05-Nov-26			
DC.OFCI.PH2.130	PH2 - Busduct Skid (OSA: 7/30/25 / ROJ: 10/15/26)	0	05-Nov-26			
DC.OFCI.PH2.110	PH2 - ATS / LV Switchgear (ROJ: 10/15/26)	0	05-Nov-26			
DC.OFCI.PH2.120	PH2 - Busduct (ROJ: 10/15/26)	0	05-Nov-26			

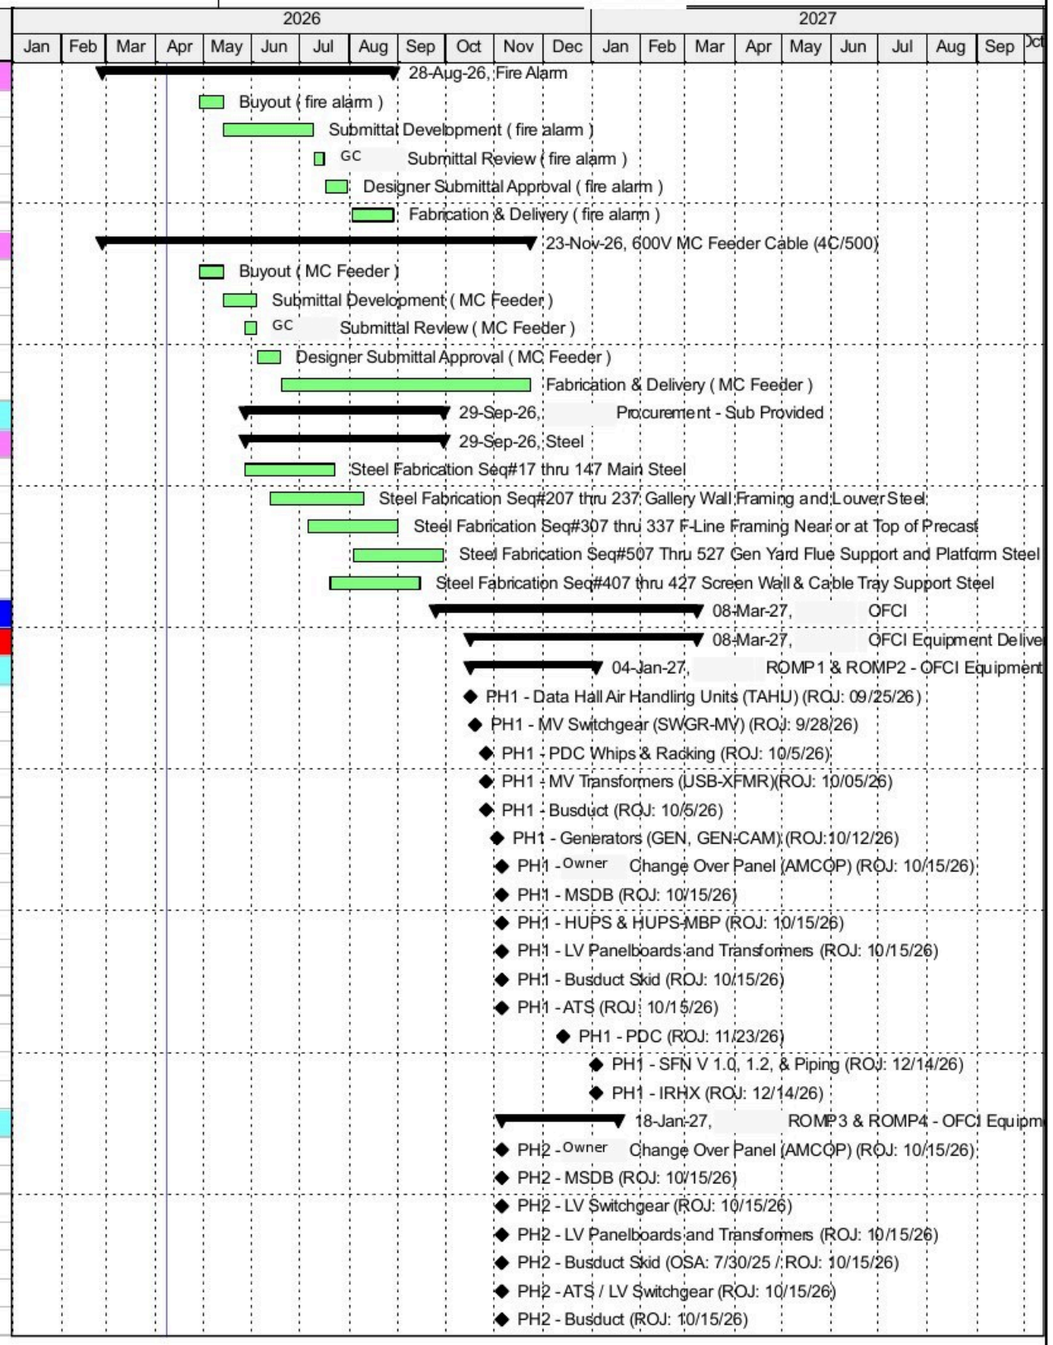


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
DC.OFCI.PH2.160	PH2 - HLP/HPP/HPP-XFMR-HUPP (ROJ: 10/15/26)	0	05-Nov-26			
DC.OFCI.PH2.210	PH2 - PDC (ROJ: 10/21/26)	0	11-Nov-26			
DC.OFCI.PH2.140	PH2 - Data Hall Air Handling Units (TAHU) (ROJ: 10/29/26)	0	19-Nov-26			
DC.OFCI.PH2.220	PH2 - PDC Whips & Racking (ROJ: 11/10/26)	0	01-Dec-26			
DC.OFCI.PH2.150	PH2 - Generators (GEN, GEN-CAM) (ROJ: 11/17/26)	0	08-Dec-26			
DC.OFCI.PH2.170	PH2 - IRHX (ROJ: 12/28/26)	0	18-Jan-27			
DC.OFCI.PH2.230	PH2 - SFN V 1.0, 1.2, & Piping (ROJ: 12/28/26)	0	18-Jan-27			
ROMP5 & ROMP6 - OFCI Equipment		90	02-Nov-26	08-Mar-27		
DC.OFCI.PH3.210	PH3 - MV Transformers (USB-XFMR) (ROJ:10/12/26)	0	02-Nov-26			
DC.OFCI.PH3.100	PH3 - Owner Change Over Panel (AMCOP) (ROJ: 11/18/26)	0	09-Dec-26			
DC.OFCI.PH3.200	PH3 - MSDB (ROJ: 11/18/26)	0	09-Dec-26			
DC.OFCI.PH3.190	PH3 - LV Switchgear (ROJ: 11/18/26)	0	09-Dec-26			
DC.OFCI.PH3.180	PH3 - LV Panelboards and Transformers (ROJ: 11/18/26)	0	09-Dec-26			
DC.OFCI.PH3.130	PH3 - Busduct Skid (OSA: 9/2/25 / ROJ: 11/18/26)	0	09-Dec-26			
DC.OFCI.PH3.110	PH3 - ATS / LV Switchgear (ROJ: 11/18/26)	0	09-Dec-26			
DC.OFCI.PH3.120	PH3 - Busduct (ROJ: 11/18/26)	0	09-Dec-26			
DC.OFCI.PH3.160	PH3 - HLP/HPP/HPP-XFMR-HUPP (ROJ: 11/18/26)	0	09-Dec-26			
DC.OFCI.PH3.150	PH3 - Generators (GEN, GEN-CAM) (ROJ: 11/30/26)	0	21-Dec-26			
DC.OFCI.PH3.140	PH3 - Data Hall Air Handling Units (TAHU) (ROJ: 12/7/26)	0	28-Dec-26			
DC.OFCI.PH3.230	PH3 - PDC Whips & Racking (ROJ:1/18/27)	0	08-Feb-27			
DC.OFCI.PH3.220	PH3 - PDC (ROJ: 1/20/26)	0	10-Feb-27			
DC.OFCI.PH3.170	PH3 - IRHX Unit (ROJ: 2/15/27)	0	08-Mar-27			
DC.OFCI.PH3.240	PH3 - SFN V 1.0, 1.2, & Piping (ROJ: 2/15/27)	0	08-Mar-27			
OFCI Equipment Setting		116	25-Sep-26	08-Mar-27		
ROMP1 & ROMP2 - Setting OFCI Equipment		71	25-Sep-26	04-Jan-27		
DC.OFCI.PH1.SET.200	PH1 - MV Switchgear (SWGR-MV)	0	25-Sep-26			
DC.OFCI.PH1.SET.120	PH1 - Busduct	0	25-Sep-26			
DC.OFCI.PH1.SET.230	PH1 - PDC Whips & Racking	0	12-Oct-26			
DC.OFCI.PH1.SET.160	PH1 - HUPS & HUPS-MBP	0	12-Oct-26			
DC.OFCI.PH1.SET.180	PH1 - LV Panelboards and Transformers	0	12-Oct-26			
DC.OFCI.PH1.SET.130	PH1 - Busduct Skid	0	12-Oct-26			
DC.OFCI.PH1.SET.140	PH1 - Data Hall Air Handling Units (TAHU)	0	16-Oct-26			
DC.OFCI.PH1.SET.150	PH1 - Generators (GEN, GEN-CAM)	0	21-Oct-26			
DC.OFCI.PH1.SET.220	PH1 - PDC	0	26-Oct-26			
DC.OFCI.PH1.SET.100	PH1 - Owner Change Over Panel (AMCOP)	0	28-Oct-26			
DC.OFCI.PH1.SET.190	PH1 - MSDB	0	28-Oct-26			
DC.OFCI.PH1.SET.110	PH1 - ATS	0	28-Oct-26			
DC.OFCI.PH1.SET.210	PH1 - MV Transformers (USB-XFMR)	0	03-Nov-26			
DC.OFCI.PH1.SET.170	PH1 - IRHX	0	08-Dec-26			
DC.OFCI.PH1.SET.240	PH1 - SFN V 1.0, 1.2, & Piping	0	04-Jan-27			
ROMP3 & ROMP4 - Setting OFCI Equipment		78	01-Oct-26	19-Jan-27		
DC.OFCI.PH2.SET.120	PH2 - Busduct	0	01-Oct-26			
DC.OFCI.PH2.SET.130	PH2 - Busduct Skid	0	12-Oct-26			
DC.OFCI.PH2.SET.200	PH2 - MSDB	0	28-Oct-26			
DC.OFCI.PH2.SET.180	PH2 - LV Panelboards and Transformers	0	28-Oct-26			

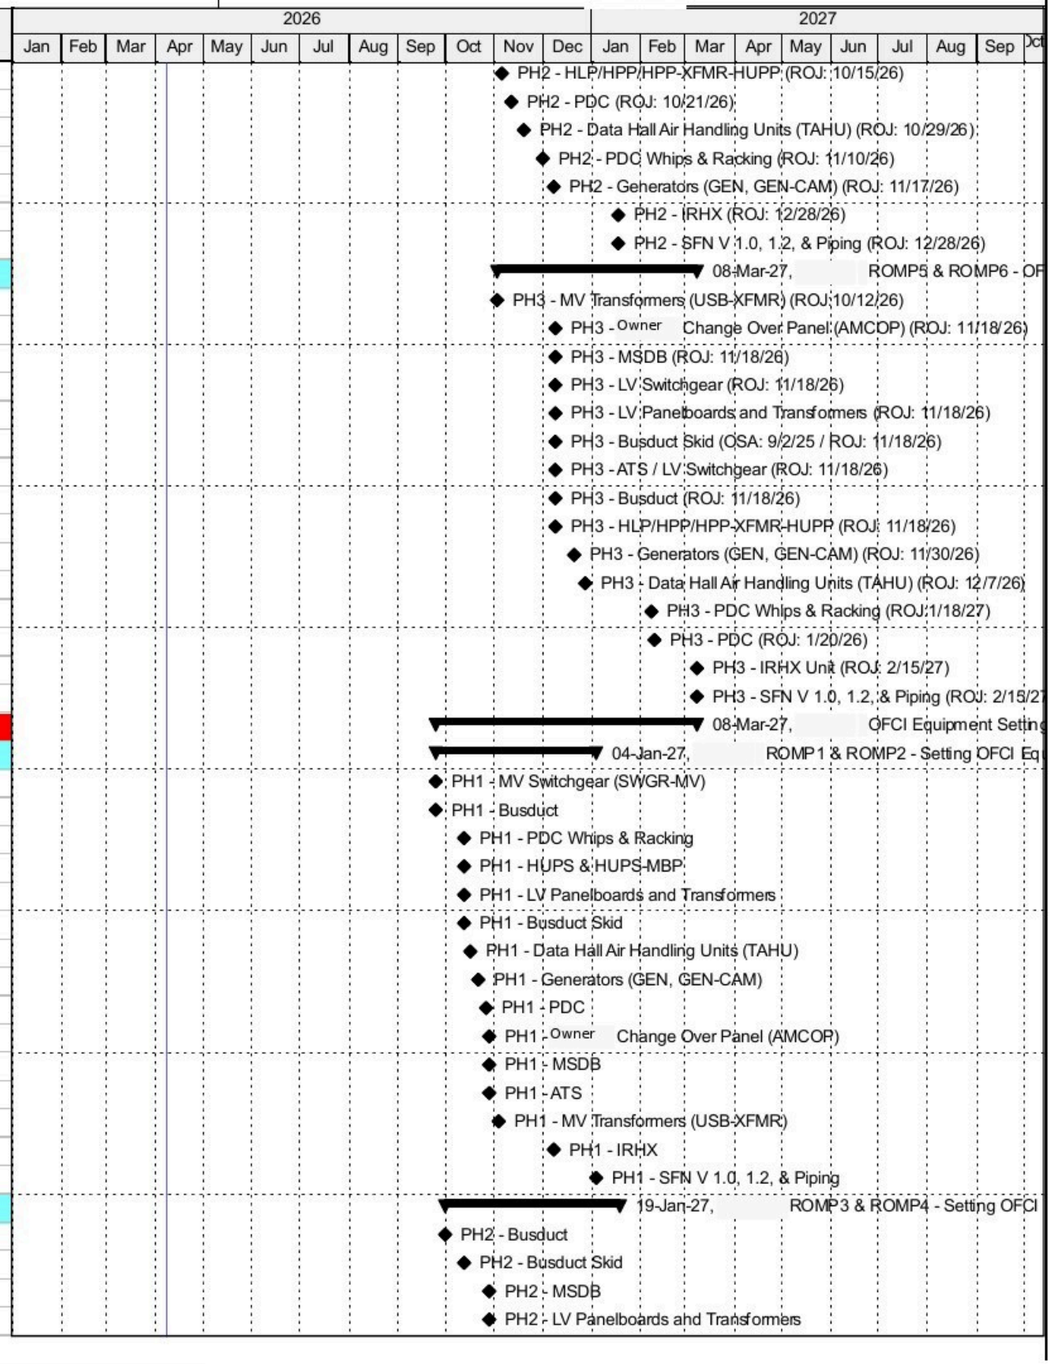


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
DC.OFCI.PH2.SET.110	PH2 - ATS / LV Switchgear	0	28-Oct-26			
DC.OFCI.PH2.SET.160	PH2 - HLP/HPP/HPP-XFMR-HUPP	0	28-Oct-26			
DC.OFCI.PH2.SET.100	PH2 - Owner Change Over Panel (AMCOP)	0	02-Nov-26			
DC.OFCI.PH2.SET.190	PH2 - LV Switchgear	0	02-Nov-26			
DC.OFCI.PH2.SET.210	PH2 - PDC	0	02-Nov-26			
DC.OFCI.PH2.SET.150	PH2 - Generators (GEN, GEN-CAM)	0	06-Nov-26			
DC.OFCI.PH2.SET.220	PH2 - PDC Whips & Racking	0	12-Nov-26			
DC.OFCI.PH2.SET.140	PH2 - Data Hall Air Handling Units (TAHU)	0	19-Nov-26			
DC.OFCI.PH2.SET.170	PH2 - IRHX	0	06-Jan-27			
DC.OFCI.PH2.SET.230	PH2 - SFN V 1.0, 1.2, & Piping	0	19-Jan-27			
ROMP5 & ROMP6 - Setting OFCI Equipment		116	25-Sep-26	08-Mar-27		
DC.OFCI.PH3.SET.160	PH3 - HLP/HPP/HPP-XFMR-HUPP	0	25-Sep-26			
DC.OFCI.PH3.SET.130	PH3 - Busduct Skid	0	08-Oct-26			
DC.OFCI.PH3.SET.120	PH3 - Busduct	0	08-Oct-26			
DC.OFCI.PH3.SET.100	PH3 - Owner Change Over Panel (AMCOP)	0	02-Nov-26			
DC.OFCI.PH3.SET.200	PH3 - MSDB	0	02-Nov-26			
DC.OFCI.PH3.SET.190	PH3 - LV Switchgear	0	02-Nov-26			
DC.OFCI.PH3.SET.180	PH3 - LV Panelboards and Transformers	0	02-Nov-26			
DC.OFCI.PH3.SET.110	PH3 - ATS / LV Switchgear	0	02-Nov-26			
DC.OFCI.PH3.SET.220	PH3 - PDC	0	09-Nov-26			
DC.OFCI.PH3.SET.210	PH3 - MV Transformers (USB-XFMR)	0	10-Nov-26			
DC.OFCI.PH3.SET.150	PH3 - Generators (GEN, GEN-CAM)	0	12-Nov-26			
DC.OFCI.PH3.SET.230	PH3 - PDC Whips & Racking	0	19-Nov-26			
DC.OFCI.PH3.SET.140	PH3 - Data Hall Air Handling Units (TAHU)	0	22-Dec-26			
DC.OFCI.PH3.SET.170	PH3 - IRHX Unit	0	01-Mar-27			
DC.OFCI.PH3.SET.240	PH3 - SFN V 1.0, 1.2, & Piping	0	08-Mar-27			
Precon		132	30-Jan-26 A	03-Aug-26		
BIM Coordination		84	02-Mar-26 A	25-Jun-26		
	Underground - BIM Coordination	11	02-Mar-26 A	30-Apr-26		
	Shell - BIM Coordination	21	17-Mar-26 A	05-May-26		
	Generator Yard - BIM Coordination	27	23-Mar-26 A	19-May-26		
	Underground - BIM Signoff	1	30-Apr-26	30-Apr-26		
	Shell - BIM Signoff	1	06-May-26	06-May-26		
	Phase 1/ Office - BIM Coordination	25	06-May-26	09-Jun-26		
	Phase 2 & 3 - BIM Coordination	30	13-May-26	24-Jun-26		
	Generator Yard - BIM Signoff	1	20-May-26	20-May-26		
	Phase 1 / Office - BIM Signoff	1	10-Jun-26	10-Jun-26		
	Phase 2 & 3 - BIM signoff	1	25-Jun-26	25-Jun-26		
Delegated Design		20	14-May-26	10-Jun-26		
Delegated Design - Fire Alarm		20	14-May-26	10-Jun-26		
OWN.DD.100	Delegated Design - Fire Alarm	20	14-May-26	10-Jun-26		
Shop Drawings - Early Work Subs		132	30-Jan-26 A	03-Aug-26		
Steel		132	30-Jan-26 A	03-Aug-26		
Steel Seq #17 Thru 147 Main Steel		84	30-Jan-26 A	27-May-26		
OWN.SHOPS.STEEL.100	Steel Shop Drawings / Engineering - Seq #17 Thru 147	52	30-Jan-26 A	01-May-26		

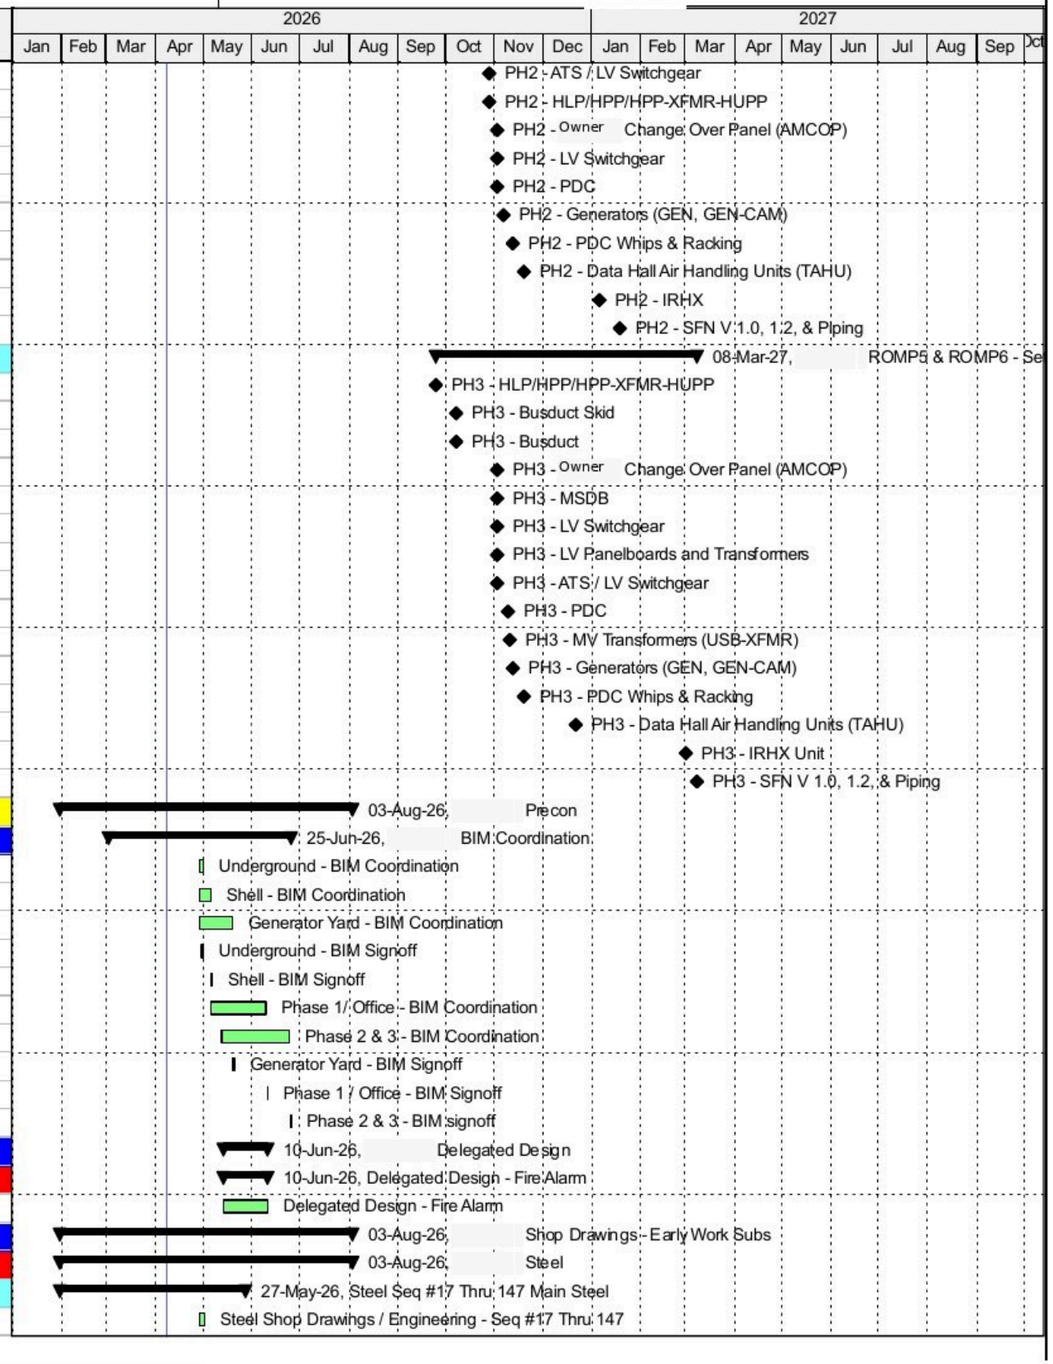


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE | CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
OWN.SHOPS.STEEL.110	Steel Shop Drawings / Finalization - Seq #17 Thru 147	5	04-May-26	08-May-26		
OWN.SHOPS.STEEL.120	Steel Shop Drawings / GC Review & Submission to EOR - Seq	3	11-May-26	13-May-26		
OWN.SHOPS.STEEL.130	Steel Shop Drawings / EOR Review and Approval - Seq #17 Thru 14	10	14-May-26	27-May-26		
Steel Seq #207 Thru 237 Gallery Wall & Louver Steel		95	30-Jan-26 A	11-Jun-26		
OWN.SHOPS.STEEL.200	Steel Shop Drawings / Engineering - Seq #207 Thru 237	60	30-Jan-26 A	14-May-26		
OWN.SHOPS.STEEL.210	Steel Shop Drawings / Finalization - Seq #207 Thru 237	5	15-May-26	21-May-26		
OWN.SHOPS.STEEL.220	Steel Shop Drawings / GC Review & Submission to EOR - Seq	5	22-May-26	28-May-26		
OWN.SHOPS.STEEL.230	Steel Shop Drawings / EOR Review and Approval - Seq #207 Thru 2	10	29-May-26	11-Jun-26		
Steel Seq #307 Thru 337 F-Line Framing Near or atTop of Precast		111	30-Jan-26 A	03-Jul-26		
OWN.SHOPS.STEEL.300	Steel Shop Drawings / Engineering - Seq #307 Thru 337	75	30-Jan-26 A	04-Jun-26		
OWN.SHOPS.STEEL.310	Steel Shop Drawings / Finalization - Seq #307 Thru 337	5	05-Jun-26	11-Jun-26		
OWN.SHOPS.STEEL.320	Steel Shop Drawings / GC Review & Submission to EOR - Seq	5	12-Jun-26	19-Jun-26		
OWN.SHOPS.STEEL.330	Steel Shop Drawings / EOR Review and Approval - Seq #307 Thru 3	10	22-Jun-26	03-Jul-26		
Steel Seq #407 Thru 427 Screen Wall & Cable Tray Support Steel		121	30-Jan-26 A	17-Jul-26		
OWN.SHOPS.STEEL.400	Steel Shop Drawings / Engineering - Seq #407 Thru 427	85	30-Jan-26 A	19-Jun-26		
OWN.SHOPS.STEEL.410	Steel Shop Drawings / Finalization - Seq #407 Thru 427	5	22-Jun-26	26-Jun-26		
OWN.SHOPS.STEEL.420	Steel Shop Drawings / GC Review & Submission to EOR - Seq	5	29-Jun-26	03-Jul-26		
OWN.SHOPS.STEEL.430	Steel Shop Drawings / EOR Review and Approval - Seq #407 Thru 4	10	06-Jul-26	17-Jul-26		
Steel Seq #507 Thru 527 Gen Yard FLue Support & Platform Steel		132	30-Jan-26 A	03-Aug-26		
OWN.SHOPS.STEEL.500	Steel Shop Drawings / Engineering - Seq #507 Thru 527	95	30-Jan-26 A	03-Jul-26		
OWN.SHOPS.STEEL.510	Steel Shop Drawings / Finalization - Seq #507 Thru 527	5	06-Jul-26	10-Jul-26		
OWN.SHOPS.STEEL.520	Steel Shop Drawings / GC Review & Submission to EOR - Seq	5	13-Jul-26	17-Jul-26		
OWN.SHOPS.STEEL.530	Steel Shop Drawings / EOR Review and Approval - Seq #507 Thru 5	10	20-Jul-26	03-Aug-26		
Shell		172	06-May-26	31-Dec-26		
Foundations		18	19-May-26	11-Jun-26		
OWN.P3.FOND.100	PH3 - R5 & 6 - CL A-D / 1-20 - Foundations	5	19-May-26	25-May-26		
OWN.P3.FOND.110	PH3 - R5 & 6 - CL D-F / 1-20 - Foundations	5	19-May-26	25-May-26		
OWN.Off.FOND.100	PH1 - Office - CL A21 - A25 - Foundations	5	21-May-26	27-May-26		
OWN.P2.FOND.100	PH2 - R3 & 4 - CL A-D / 1-20 - Foundations	5	26-May-26	01-Jun-26		
OWN.P2.FOND.110	PH2 - R3 & 4 - CL D-F / 1-20 - Foundations	5	26-May-26	01-Jun-26		
OWN.Off.FOND.115	PH1 - Office - Foundations at Best Refuge	3	28-May-26	01-Jun-26		
OWN.P1.FOND.100	PH1 - R1 & 2 - CL A-D / 1-20 - Foundations	5	02-Jun-26	08-Jun-26		
OWN.P1.FOND.110	PH1 - R1 & 2 - CL D-F / 1-20 - Foundations	5	02-Jun-26	08-Jun-26		
OWN.Off.FOND.125	PH1 - Office - Foundations at Elevator Pit	3	02-Jun-26	04-Jun-26		
OWN.Off.FOND.110	PH1 - Office - CL B-G / 21-25 - Foundations	5	05-Jun-26	11-Jun-26		
MEPF Undergrounds		33	06-May-26	19-Jun-26		
OWN.UGMEPF.S.100	Pad Release for Building Underground	1	06-May-26	06-May-26		
OWN.P3.UGMEPF.100	PH3 - R5 & 6 - CL A-D / 1-7 - MEPF Undergrounds (Deep Plumbing	2	07-May-26	08-May-26		
OWN.P3.UGMEPF.110	PH3 - R5 & 6 - CL D-F / 1-7 - MEPF Undergrounds (Deep Electrical)	3	07-May-26	11-May-26		
OWN.Off.UGMEPF.110	PH1 - Office - CL A-D / 20-25 - MEPF Undergrounds (Deep Telecom	5	07-May-26	13-May-26		
OWN.P1.UGMEPF.120	PH1 - R1 & 2 - CL A-D / 19-21 - MEPF Undergrounds (Deep Telecor	5	07-May-26	13-May-26		
OWN.P2.UGMEPF.100	PH2 - R3 & 4 - CL A-D / 7-13 - MEPF Undergrounds (Deep Plumbin	2	11-May-26	12-May-26		
OWN.P2.UGMEPF.110	PH2 - R3 & 4 - CL D-F / 7-13- MEPF Undergrounds (Deep Electrical	3	12-May-26	14-May-26		
OWN.P1.UGMEPF.100	PH1 - R1 & 2 - CL A-D /13-20 - MEPF Undergrounds (Deep Plumbir	2	13-May-26	14-May-26		
OWN.UGMEPF.100	PH3 & 2 - R3-6 - CL A-D / 1-14 - Cap, Test, & Backfill plumbingg	2	13-May-26	14-May-26		

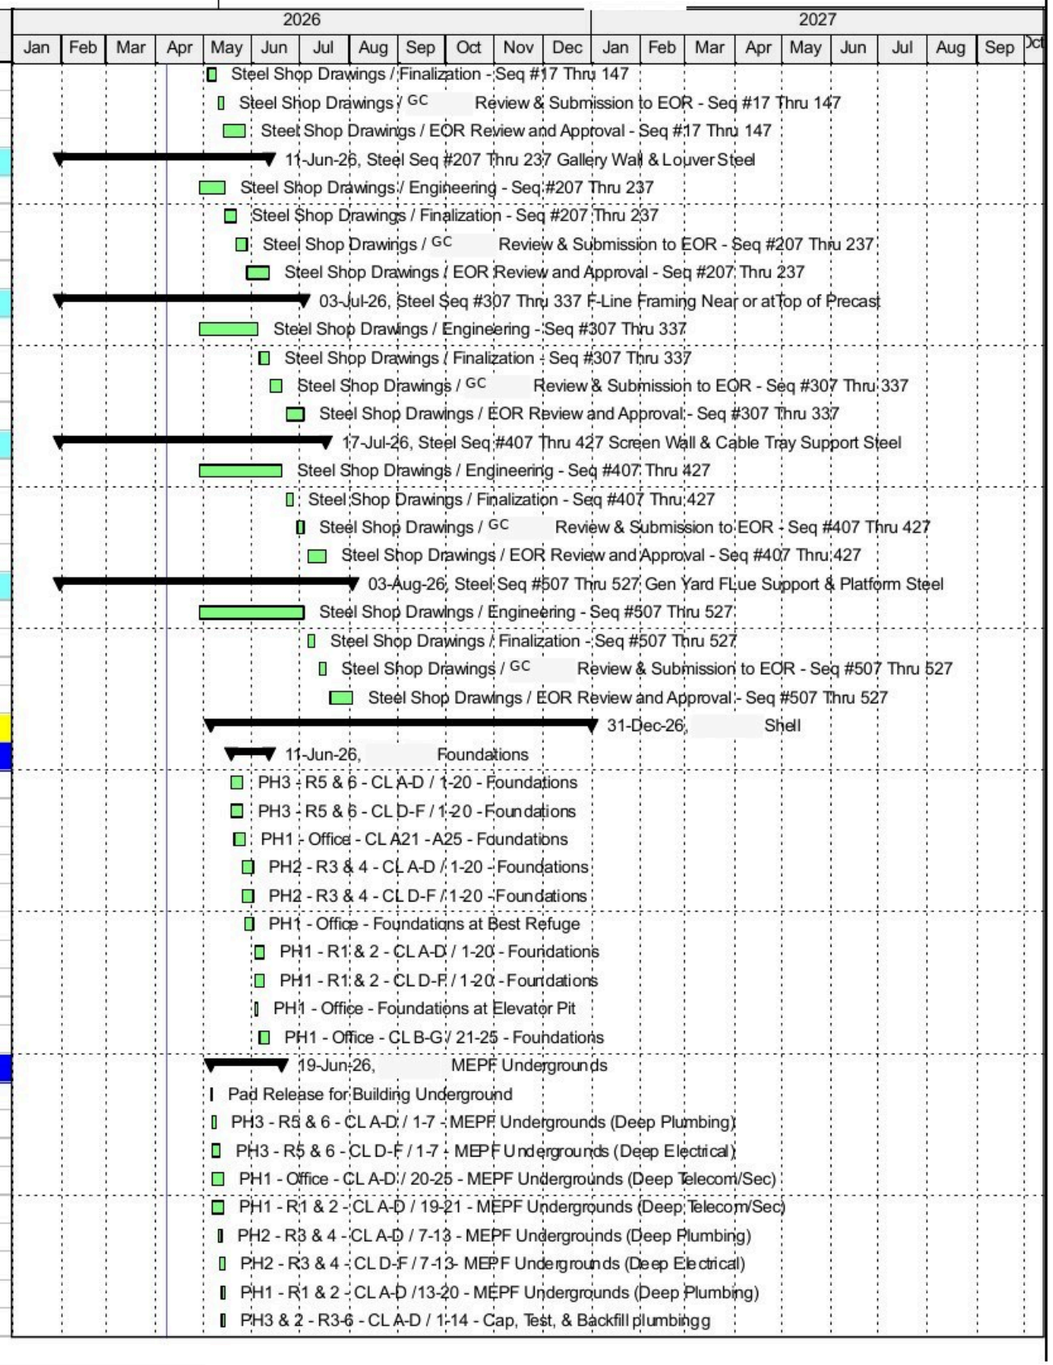


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
OWN.P1.UGMEPF.130	PH1 - R1 & 2 - CL D-F / 18-21 - MEPF Undergrounds (Deep Telecon	5	14-May-26	20-May-26		
OWN.Off.UGMEPF.120	PH1 - Office - CL D-G / 20-25 - MEPF Undergrounds (Deep Telecom	5	14-May-26	20-May-26		
OWN.P1.UGMEPF.110	PH1 - R1 & 2 - CL D-F / 13-20 - MEPF Undergrounds (Deep Electric	3	15-May-26	19-May-26		
OWN.Off.UGMEPF.140	PH1 - Office - MEPF Undergrounds (Deep Plumbing)	2	15-May-26	18-May-26		
OWN.UGMEPF.110	PH1 - R1, 2 & Office - CL A-D / 14-20 - Cap, Test, & Backfill plumbing	2	19-May-26	20-May-26		
OWN.Off.UGMEPF.130	PH1 - Office - MEPF Undergrounds (Deep Electrical)	5	21-May-26	27-May-26		
OWN.Off.UGMEPF.100	PH1 - Office - MEPF Undergrounds (Fire Lines)	5	28-May-26	03-Jun-26		
OWN.Off.UGMEPF.150	PH1 - Office - MEPF Undergrounds (Shallow ElectricalTelecom/Sec)	5	12-Jun-26	19-Jun-26		
OWN.Off.UGMEPF.160	PH1 - Office - MEPF Undergrounds (Shallow Plumbing)	5	12-Jun-26	19-Jun-26		
Office Slab Ancilliary Work		33	09-Jun-26	23-Jul-26		
OWN.Off.AW-BR.100	PH1 - Office - CMU at Foundation 1st 4 courses	2	09-Jun-26	10-Jun-26		
OWN.Off.AW-BR.105	PH1 - Office - Shallow MEP at Best Refuge	2	11-Jun-26	12-Jun-26		
OWN.Off.AW-BR.110	PH1 - Office - CMU Walls at Best Refuge	5	10-Jul-26	16-Jul-26		
OWN.Off.AW-BR.120	PH1 - Office - Decking at Best Refuge	2	17-Jul-26	20-Jul-26		
OWN.Off.AW-BR.130	PH1 - Office - F/R/P SOMD at Best Refuge	3	21-Jul-26	23-Jul-26		
SOG		79	04-Jun-26	22-Sep-26		
Phase 1 - Office SOG		16	22-Jun-26	13-Jul-26		
OWN.Off.SOG.120	PH1 - Office - Waterproofing	3	22-Jun-26	24-Jun-26		
OWN.Off.SOG.100	PH1 - Office - F/R/P Slab on Grade	5	01-Jul-26	07-Jul-26		
OWN.Off.SOG.110	PH1 - Office - SOG Cure-Time	6	08-Jul-26	13-Jul-26		
Phase 1 - ROMP 1 & 2 + Catcher SOG		73	12-Jun-26	22-Sep-26		
OWN.PH1.SOG.120	PH1 - R1 & 2 - CL A-C / 14-21 - Waterproofing	3	12-Jun-26	17-Jun-26		
OWN.PH1.SOG.180	PH1 - R1 & 2 - CL D-F / 14-21 - Waterproofing	3	12-Jun-26	17-Jun-26		
OWN.PH1.SOG.100	PH1 - R1 & 2 - CL A-C / 14-21 - F/R/P Slab on Grade	5	18-Jun-26	24-Jun-26		
OWN.PH1.SOG.110	PH1 - R1 & 2 - CL A-C / 14-21 - SOG Cure-Time	6	25-Jun-26	30-Jun-26		
OWN.PH1.SOG.160	PH1 - R1 & 2 - CL D-F / 14-21 - F/R/P Slab on Grade	5	25-Jun-26	01-Jul-26		
OWN.PH1.SOG.170	PH1 - R1 & 2 - CL D-F / 14-21 - SOG Cure-Time	6	02-Jul-26	07-Jul-26		
OWN.PH1.SOG.150	PH1 - R1 & 2 - CL C-D / 14-21 - Waterproofing	3	21-Aug-26	25-Aug-26		
OWN.PH1.SOG.130	PH1 - R1 & 2 - CL C-D / 14-21 - F/R/P Slab on Grade In-fill	5	10-Sep-26	16-Sep-26		
OWN.PH1.SOG.140	PH1 - R1 & 2 - CL C-D / 14-21 - SOG In-fil Cure Time	6	17-Sep-26	22-Sep-26		
Phase 2 - ROMP 3 & 4 SOG		76	09-Jun-26	22-Sep-26		
OWN.PH2.SOG.120	PH2 - R3 & 4 - CL A-C / 7-14 - Waterproofing	3	09-Jun-26	11-Jun-26		
OWN.PH2.SOG.180	PH2 - R3 & 4 - CL D-F / 7-14 - Waterproofing	3	09-Jun-26	11-Jun-26		
OWN.PH2.SOG.100	PH2 - R3 & 4 - CL A-C / 7-14 - F/R/P Slab on Grade	5	18-Jun-26	24-Jun-26		
OWN.PH2.SOG.110	PH2 - R3 & 4 - CL A-C / 7-14 - SOG Cure-Time	6	25-Jun-26	30-Jun-26		
OWN.PH2.SOG.160	PH2 - R3 & 4 - CL D-F / 7-14 - F/R/P Slab on Grade	5	25-Jun-26	01-Jul-26		
OWN.PH2.SOG.170	PH2 - R3 & 4 - CL D-F / 7-14 - SOG Cure-Time	6	02-Jul-26	07-Jul-26		
OWN.PH2.SOG.150	PH2 - R3 & 4 - CL C-D / 7-14 - Waterproofing	3	28-Aug-26	01-Sep-26		
OWN.PH2.SOG.130	PH2 - R3 & 4 - CL C-D / 7-14 - F/R/P Slab on Grade In-fill	5	10-Sep-26	16-Sep-26		
OWN.PH2.SOG.140	PH2 - R3 & 4 - CL C-D / 7-14 - SOG In-fil Cure Time	6	17-Sep-26	22-Sep-26		
Phase 3 - ROMP 5 & 6 SOG		79	04-Jun-26	22-Sep-26		
OWN.PH3.SOG.120	PH3 - R5 & 6 - CL A-C / 1-7 - Waterproofing	3	04-Jun-26	08-Jun-26		
OWN.PH3.SOG.180	PH3 - R5 & 6 - CL D-F / 1-7 - Waterproofing	3	04-Jun-26	08-Jun-26		
OWN.PH3.SOG.100	PH3 - R5 & 6 - CL A-C / 1-7 - F/R/P Slab on Grade	5	18-Jun-26	24-Jun-26		
OWN.PH3.SOG.110	PH3 - R5 & 6 - CL A-C / 1-7 - SOG Cure-Time	6	25-Jun-26	30-Jun-26		

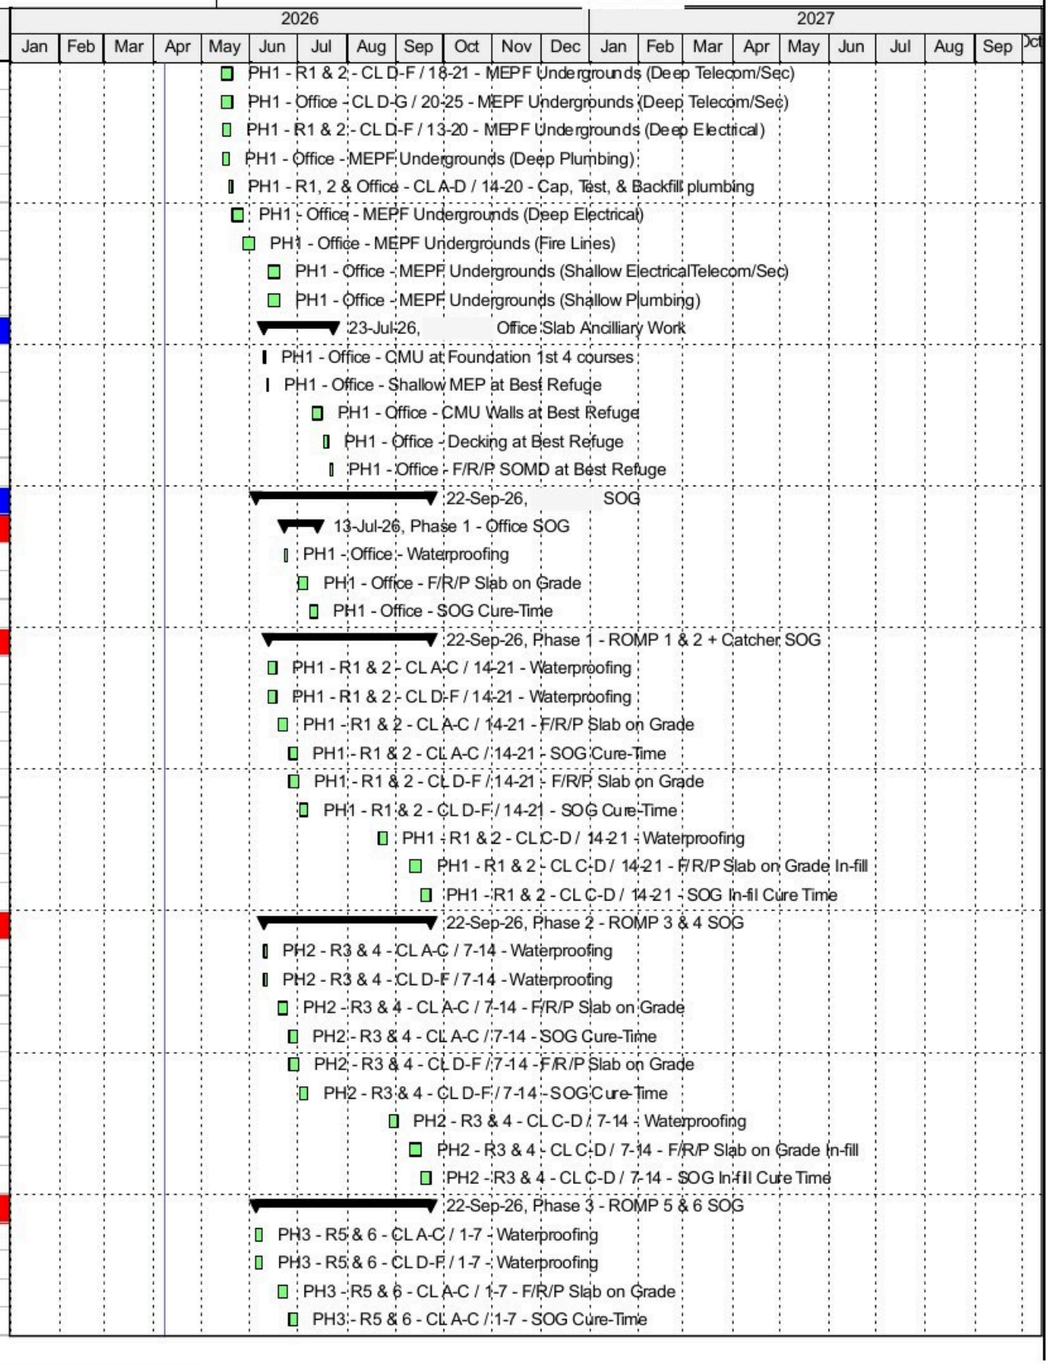


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
OWN.PH3.SOG.160	PH3 - R5 & 6 - CL D-F / 1-7 - F/R/P Slab on Grade	5	25-Jun-26	01-Jul-26		
OWN.PH3.SOG.170	PH3 - R5 & 6 - CL D-F / 1-7 - SOG Cure-Time	6	02-Jul-26	07-Jul-26		
OWN.PH3.SOG.150	PH3 - R5 & 6 - CL C-D / 1-7 - Waterproofing	3	07-Sep-26	09-Sep-26		
OWN.PH3.SOG.130	PH3 - R5 & 6 - CL C-D / 1-7 - F/R/P Slab on Grade In-fill	5	10-Sep-26	16-Sep-26		
OWN.PH3.SOG.140	PH3 - R5 & 6 - CL C-D / 1-7 - SOG In-fill Cure Time	6	17-Sep-26	22-Sep-26		
Superstructure		120	17-Jul-26	31-Dec-26		
Shakeout/Delivery		23	17-Jul-26	18-Aug-26		
OWN.87.STEEL.100	Steel Start Mobilization	0	17-Jul-26			
OWN.87.STEEL.110	Crane Setup	6	17-Jul-26	27-Jul-26		
OWN.87.STEEL.120	Deliveries & Shakeout	20	27-Jul-26	18-Aug-26		
Main Structure		31	27-Jul-26	07-Sep-26		
Erection/Detailing/Decking - Phase 1		20	27-Jul-26	21-Aug-26		
OWN.87.STEEL.130	PH1 - Office - Seq 017 Erection	3	27-Jul-26	30-Jul-26		
OWN.87.STEEL.140	PH1 - Office - Seq 017 Detailing	5	28-Jul-26	03-Aug-26		
OWN.87.STEEL.150	PH1 - Office - Seq 027 Erection	3	01-Aug-26	04-Aug-26		
OWN.87.STEEL.160	PH1 - Office - Seq 027 Detailing	5	01-Aug-26	07-Aug-26		
OWN.87.STEEL.170	PH1 - R1 & R2 - Seq 037 Erection	3	03-Aug-26	06-Aug-26		
OWN.87.STEEL.180	PH1 - R1 & R2 - Seq 047 Erection	2	06-Aug-26	08-Aug-26		
OWN.87.STEEL.190	PH1 - Office - Sector 7/8 Decking	6	07-Aug-26	14-Aug-26		
OWN.87.STEEL.200	PH1 - R1 & R2 - Seq 037 Detailing	3	07-Aug-26	11-Aug-26		
OWN.87.STEEL.210	PH1 - R1 & R2 - Seq 057 Erection	1	08-Aug-26	10-Aug-26		
OWN.87.STEEL.220	PH1 - R1 & R2 - Seq 067 Erection	2	10-Aug-26	12-Aug-26		
OWN.87.STEEL.230	PH1 - R1 & R2 - Seq 047 Detailing	3	10-Aug-26	13-Aug-26		
OWN.87.STEEL.240	PH1 - R1 & R2 - Seq 057 Detailing	2	13-Aug-26	15-Aug-26		
OWN.87.STEEL.250	PH1 - R1 & R2 - Sector 5/6 Decking	6	14-Aug-26	21-Aug-26		
OWN.87.STEEL.260	PH1 - R1 & R2 - Seq 067 Detailing	2	14-Aug-26	17-Aug-26		
Erection/Detailing/Decking - Phase 2		13	12-Aug-26	28-Aug-26		
OWN.87.STEEL.270	PH2 - R3 & R4 - Seq 077 Erection	2	12-Aug-26	14-Aug-26		
OWN.87.STEEL.280	PH2 - R3 & R4 - Seq 087 Erection	2	14-Aug-26	17-Aug-26		
OWN.87.STEEL.290	PH2 - R3 & R4 - Seq 097 Erection	1	17-Aug-26	18-Aug-26		
OWN.87.STEEL.300	PH2 - R3 & R4 - Seq 077 Detailing	2	17-Aug-26	19-Aug-26		
OWN.87.STEEL.310	PH2 - R3 & R4 - Seq 107 Erection	2	18-Aug-26	20-Aug-26		
OWN.87.STEEL.320	PH2 - R3 & R4 - Seq 087 Detailing	2	19-Aug-26	21-Aug-26		
OWN.87.STEEL.330	PH2 - R3 & R4 - Sector 3/4 Decking	6	21-Aug-26	28-Aug-26		
OWN.87.STEEL.340	PH2 - R3 & R4 - Seq 097 Detailing	2	21-Aug-26	24-Aug-26		
OWN.87.STEEL.350	PH2 - R3 & R4 - Seq 107 Detailing	2	24-Aug-26	26-Aug-26		
Erection/Detailing/Decking - Phase 3		13	20-Aug-26	07-Sep-26		
OWN.87.STEEL.360	PH3 - R5 & R6 - Seq 117 Erection	2	20-Aug-26	22-Aug-26		
OWN.87.STEEL.370	PH3 - R5 & R6 - Seq 127 Erection	2	22-Aug-26	25-Aug-26		
OWN.87.STEEL.380	PH3 - R5 & R6 - Seq 137 Erection	1	25-Aug-26	26-Aug-26		
OWN.87.STEEL.390	PH3 - R5 & R6 - Seq 147 Erection	2	26-Aug-26	28-Aug-26		
OWN.87.STEEL.400	PH3 - R5 & R6 - Seq 117 Detailing	2	26-Aug-26	28-Aug-26		
OWN.87.STEEL.410	PH3 - R5 & R6 - Seq 127 Detailing	2	28-Aug-26	31-Aug-26		
OWN.87.STEEL.420	PH3 - R5 & R6 - Sector 1/2 Decking	6	31-Aug-26	07-Sep-26		
OWN.87.STEEL.430	PH3 - R5 & R6 - Seq 137 Detailing	2	31-Aug-26	02-Sep-26		

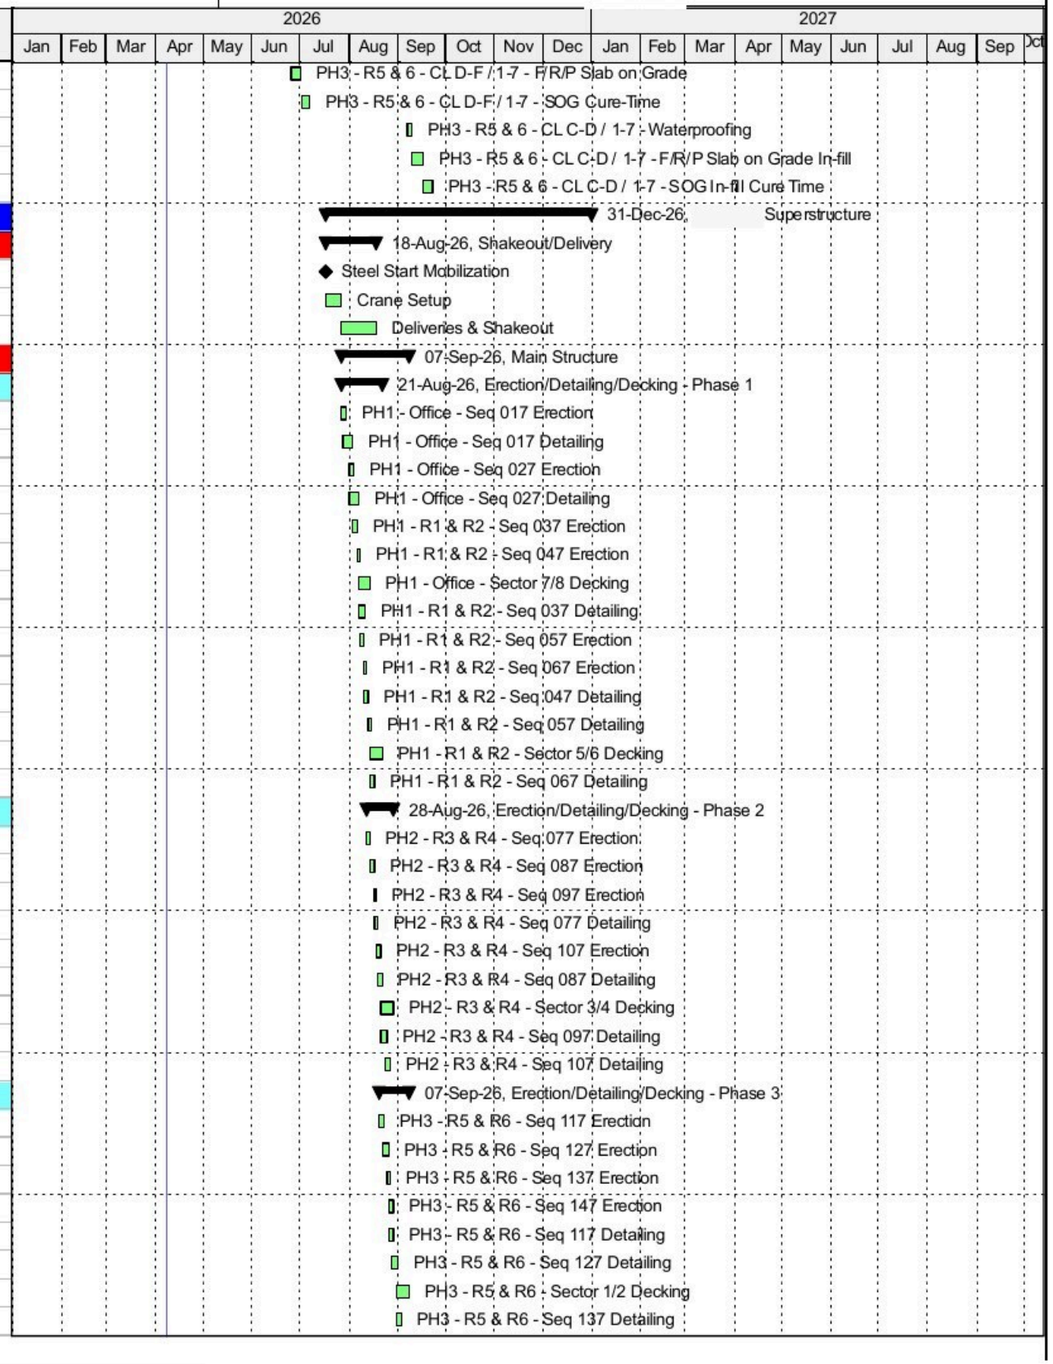


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE | CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
OWN.87.STEEL.440	PH3 - R5 & R6 - Seq 147 Detailing	2	02-Sep-26	04-Sep-26		
Gallery Wall		16	04-Sep-26	25-Sep-26		
OWN.87.STEEL.450	PH1 - R1 & R2 - Seq 207 Gallery Wall Framing	3	04-Sep-26	08-Sep-26		
OWN.87.STEEL.460	PH1 - R1 & R2 - Seq 237A - A-Line Louver Framing	3	08-Sep-26	11-Sep-26		
OWN.87.STEEL.470	PH2 - R3 & R4 - Seq 217 Gallery Wall Framing	3	11-Sep-26	15-Sep-26		
OWN.87.STEEL.480	PH2 - R3 & R4 - Seq 237B - A-Line Louver Framing	3	15-Sep-26	18-Sep-26		
OWN.87.STEEL.490	PH3 - R5 & R6 - Seq 227 Gallery Wall Framing	3	18-Sep-26	22-Sep-26		
OWN.87.STEEL.500	PH3 - R5 & R6 - Seq 237C - A-Line Louver Framing	3	22-Sep-26	25-Sep-26		
F-Line Framing		15	14-Sep-26	03-Oct-26		
F-Line Framing Erection		13	14-Sep-26	30-Sep-26		
OWN.87.STEEL.510	PH1 - R1 & R2 - Seq 337 - F-Line Framing - Erection	4	14-Sep-26	18-Sep-26		
OWN.87.STEEL.520	PH2 - R3 & R4 - Seq 327 - F-Line Framing - Erection	2	18-Sep-26	21-Sep-26		
OWN.87.STEEL.530	PH3 - R5 & R6 - Seq 317 - F-Line Framing - Erection	2	29-Sep-26	30-Sep-26		
F-Line Framing Detailing		14	15-Sep-26	03-Oct-26		
OWN.87.STEEL.540	PH1 - R1 & R2 - Seq 337 - F-Line Framing - Detailing	6	15-Sep-26	22-Sep-26		
OWN.87.STEEL.550	PH2 - R3 & R4 - Seq 327 - F-Line Framing - Detailing	4	22-Sep-26	26-Sep-26		
OWN.87.STEEL.560	PH3 - R5 & R6 - Seq 307 - F-Line Framing - Detailing	4	30-Sep-26	03-Oct-26		
Gen Yard Steel		65	02-Oct-26	31-Dec-26		
Gen Yard - Screen Wall and Cable Tray Support Erection		21	02-Oct-26	31-Oct-26		
OWN.87.STEEL.570	PH1 - R1 & R2 - Seq 427 - Screen Wall and Cable Tray Support Ste	6	02-Oct-26	08-Oct-26		
OWN.87.STEEL.580	PH2 - R3 & R4 - Seq 417 - Screen Wall and Cable Tray Support Ste	6	19-Oct-26	24-Oct-26		
OWN.87.STEEL.590	PH3 - R5 & R6 - Seq 407 - Screen Wall and Cable Tray Support Ste	6	26-Oct-26	31-Oct-26		
Gen Yard - Screen Wall and Cable Tray Support Detailing		21	05-Oct-26	02-Nov-26		
OWN.87.STEEL.600	PH1 - R1 & R2 - Seq 427 - Screen Wall and Cable Tray Support Ste	6	05-Oct-26	10-Oct-26		
OWN.87.STEEL.610	PH2 - R3 & R4 - Seq 417 - Screen Wall and Cable Tray Support Ste	6	20-Oct-26	26-Oct-26		
OWN.87.STEEL.620	PH3 - R5 & R6 - Seq 407 - Screen Wall and Cable Tray Support Ste	6	27-Oct-26	02-Nov-26		
Gen Yard - Flue Support Steel Erection		19	14-Oct-26	09-Nov-26		
OWN.87.STEEL.630	PH1 - R1 & R2 - Seq 527A - Flue Support Steel Erection	4	14-Oct-26	17-Oct-26		
OWN.87.STEEL.640	PH2 - R3 & R4 - Seq 517A - Flue Support Steel Erection	2	02-Nov-26	03-Nov-26		
OWN.87.STEEL.650	PH3 - R5 & R6 - Seq 507A - Flue Support Steel Erection	2	07-Nov-26	09-Nov-26		
Gen Yard - Flue Support Steel Detailing		20	15-Oct-26	11-Nov-26		
OWN.87.STEEL.660	PH1 - R1 & R2 - Seq 527A - Flue Support Steel Detailing	5	15-Oct-26	20-Oct-26		
OWN.87.STEEL.670	PH2 - R3 & R4 - Seq 517A - Flue Support Steel Detailing	3	03-Nov-26	05-Nov-26		
OWN.87.STEEL.680	PH3 - R5 & R6 - Seq 507A - Flue Support Steel Detailing	3	09-Nov-26	11-Nov-26		
Gen Yard - Platform Steel Erection		35	10-Nov-26	28-Dec-26		
OWN.87.STEEL.690	PH1 - R1 & R2 - Seq 527B - Platform Steel Erection	4	10-Nov-26	13-Nov-26		
OWN.87.STEEL.700	PH2 - R3 & R4 - Seq 517B - Platform Steel Erection	2	15-Dec-26	16-Dec-26		
OWN.87.STEEL.710	PH3 - R5 & R6 - Seq 507B - Platform Steel Erection	2	26-Dec-26	28-Dec-26		
Gen Yard - Platform Steel Detailing		36	12-Nov-26	31-Dec-26		
OWN.87.STEEL.720	PH1 - R1 & R2 - Seq 527B - Platform Steel Detailing	5	12-Nov-26	17-Nov-26		
OWN.87.STEEL.730	PH2 - R3 & R4 - Seq 517B - Platform Steel Detailing	4	16-Dec-26	21-Dec-26		
OWN.87.STEEL.740	PH3 - R5 & R6 - Seq 507B - Platform Steel Detailing	4	28-Dec-26	31-Dec-26		
Slab on Metal Deck		25	14-Aug-26	17-Sep-26		
OWN.Off.SOMD.100	PH1 - Office Mezz - F/R/P Slab on Metal Deck	5	14-Aug-26	20-Aug-26		
OWN.Off.SOMD.110	PH1 - Office Mezz - SOMD Cure Time	7	21-Aug-26	27-Aug-26		

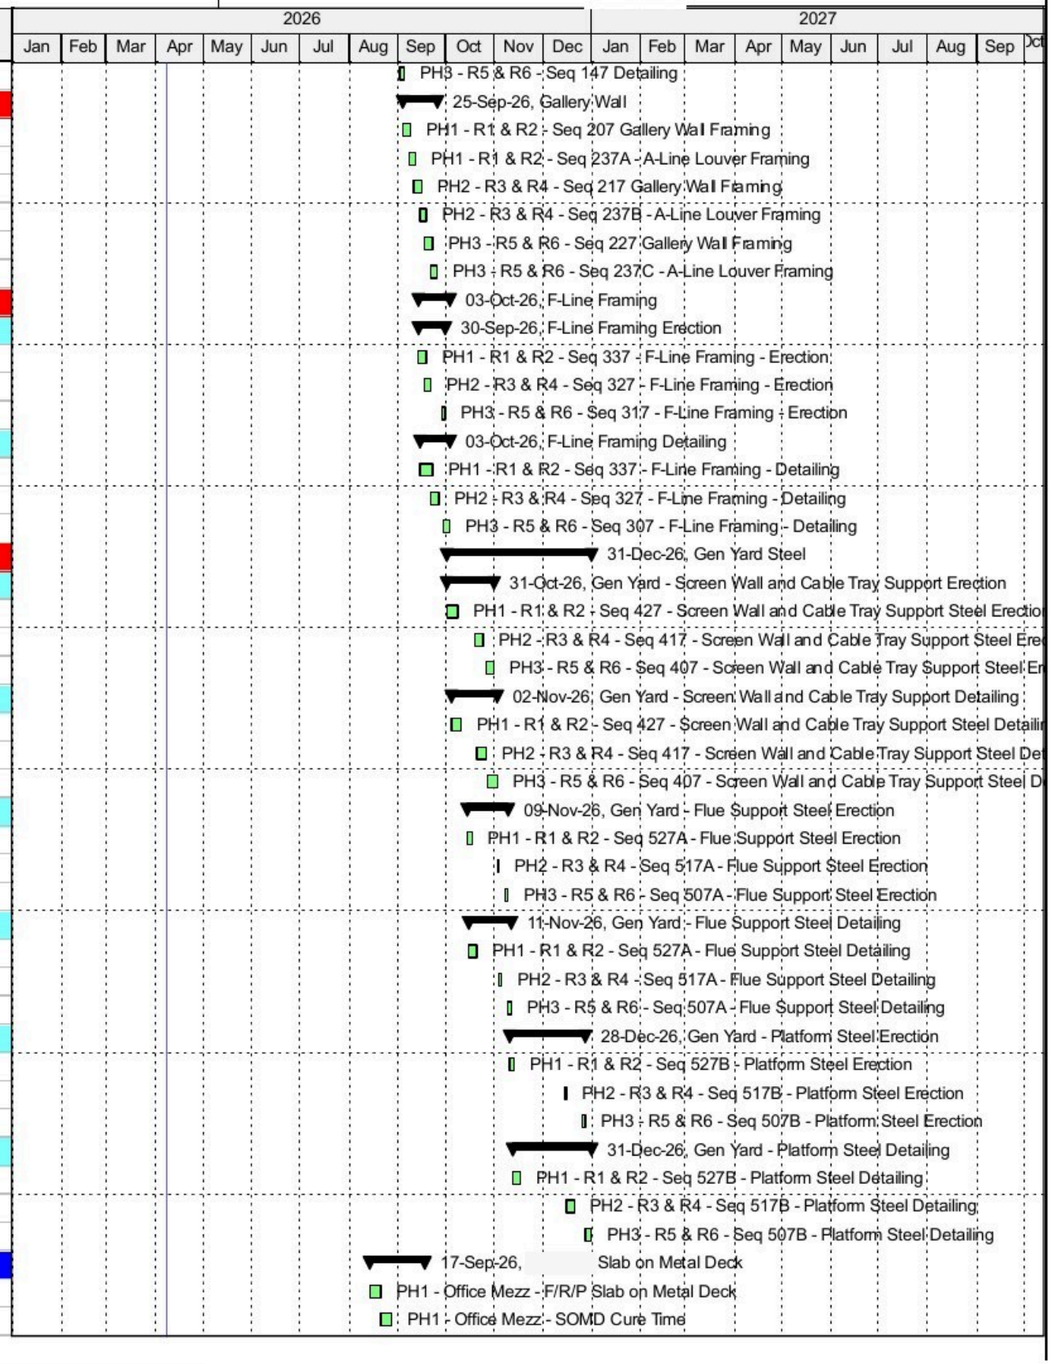


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
OWN.P1.SOMD.100	PH1 - ROMP 1 & 2 Mezz - F/R/P Slab on Metal Deck	4	21-Aug-26	26-Aug-26		
OWN.P1.SOMD.110	PH1 - ROMP 1 & 2 Mezz - SOMD Cure Time	7	27-Aug-26	02-Sep-26		
OWN.P2.SOMD.100	PH2 - ROMP 3 & 4 Mezz - F/R/P Slab on Metal Deck	4	28-Aug-26	02-Sep-26		
OWN.P2.SOMD.110	PH2 - ROMP 3 & 4 Mezz - SOMD Cure Time	7	03-Sep-26	09-Sep-26		
OWN.P3.SOMD.100	PH3 - ROMP 5 & 6 Mezz - F/R/P Slab on Metal Deck	4	07-Sep-26	10-Sep-26		
OWN.P3.SOMD.110	PH3 - ROMP 5 & 6 Mezz - SOMD Cure Time	7	11-Sep-26	17-Sep-26		
Exterior Precast		20	28-Aug-26	24-Sep-26		
OWN.P2.PRECAST.100	PH2 - ROMP 3 & 4 - A-Line Precast	2	28-Aug-26	31-Aug-26		
OWN.P1.PRECAST.100	PH1 - ROMP 1 & 2 - A-Line Precast	2	31-Aug-26	02-Sep-26		
OWN.Off.PRECAST.100	PH1 - Office - A-Line Precast	2	02-Sep-26	04-Sep-26		
OWN.Off.PRECAST.110	PH1 - Office - North Precast	2	04-Sep-26	07-Sep-26		
OWN.Off.PRECAST.120	PH1 - Office - G-Line Precast	2	07-Sep-26	09-Sep-26		
OWN.P1.PRECAST.110	PH1 - ROMP 1 & 2 - F-Line Precast	2	09-Sep-26	11-Sep-26		
OWN.P2.PRECAST.110	PH2 - ROMP 3 & 4 - F-Line Precast	2	11-Sep-26	14-Sep-26		
OWN.P3.PRECAST.120	PH3 - ROMP 5 & 6 - F-Line Precast	2	18-Sep-26	19-Sep-26		
OWN.P3.PRECAST.110	PH3 - ROMP 5 & 6 - South Precast	2	21-Sep-26	22-Sep-26		
OWN.P3.PRECAST.100	PH3 - ROMP 5 & 6 - A-Line Precast	2	23-Sep-26	24-Sep-26		
Exterior IMP		19	04-Sep-26	30-Sep-26		
OWN.Off.IMP.100	PH1 - Office - A-Line IMP	5	04-Sep-26	10-Sep-26		
OWN.Off.IMP.110	PH1 - Office - North IMP	5	11-Sep-26	17-Sep-26		
OWN.Off.IMP.120	PH1 - Office - G-Line IMP	5	18-Sep-26	24-Sep-26		
OWN.Off.IMP.130	PH1 - Office - Penthouse IMP	3	25-Sep-26	30-Sep-26		
Precast Pain		20	31-Aug-26	26-Sep-26		
OWN.P2.PAINT.100	PH2 - ROMP 3 & 4 - A-Line Precast Paint	2	31-Aug-26	02-Sep-26		
OWN.P1.PAINT.100	PH1 - ROMP 1 & 2 - A-Line Precast Paint	2	02-Sep-26	04-Sep-26		
OWN.Off.PAINT.100	PH1 - Office - A-Line Precast Paint	2	04-Sep-26	07-Sep-26		
OWN.Off.PAINT.110	PH1 - Office - North Precast Paint	2	07-Sep-26	09-Sep-26		
OWN.Off.PAINT.120	PH1 - Office - G-Line Precast Paint	2	09-Sep-26	11-Sep-26		
OWN.P1.PAINT.110	PH1 - ROMP 1 & 2 - F-Line Precast Paint	2	11-Sep-26	14-Sep-26		
OWN.P2.PAINT.110	PH2 - ROMP 3 & 4 - F-Line Precast Paint	2	14-Sep-26	16-Sep-26		
OWN.P3.PAINT.120	PH3 - ROMP 5 & 6 - A-Line Precast Paint	2	21-Sep-26	22-Sep-26		
OWN.P3.PAINT.110	PH3 - ROMP 5 & 6 - South Precast Paint	2	23-Sep-26	24-Sep-26		
OWN.P3.PAINT.100	PH3 - ROMP 5 & 6 - F-Line Precast Paint	2	25-Sep-26	26-Sep-26		
Roofing		32	21-Aug-26	05-Oct-26		
OWN.P1.ROOF.100	PH1 - ROMP 1 & 2 - CL B-E Roofing	5	21-Aug-26	27-Aug-26		
OWN.Off.ROOF.100	PH1 - Office - CL B-F / 20-24 Roofing	5	26-Aug-26	01-Sep-26		
OWN.P2.ROOF.100	PH2 - ROMP 3 & 4 - CL B-E Roofing	5	28-Aug-26	03-Sep-26		
OWN.P1.ROOF.110	PH1 - ROMP 1 & 2 - CL A-B Roofing	3	02-Sep-26	04-Sep-26		
OWN.P2.ROOF.110	PH2 - ROMP 3 & 4 - CL A-B Roofing	3	04-Sep-26	08-Sep-26		
OWN.P3.ROOF.100	PH3 - ROMP 5 & 6 - CL B-E Roofing	5	07-Sep-26	11-Sep-26		
OWN.Off.ROOF.110	PH1 - Office - CL A-B / 20-24 Roofing	3	11-Sep-26	15-Sep-26		
OWN.P1.ROOF.120	PH1 - ROMP 1 & 2 - CL E-F Roofing	3	11-Sep-26	15-Sep-26		
OWN.P2.ROOF.120	PH2 - ROMP 3 & 4 - CL E-F Roofing	3	14-Sep-26	16-Sep-26		
OWN.Off.ROOF.130	PH1 - Office - CL A-G / 24-25 Roofing	3	18-Sep-26	22-Sep-26		
OWN.P3.ROOF.120	PH3 - ROMP 5 & 6 - CL E-F Roofing	3	21-Sep-26	23-Sep-26		

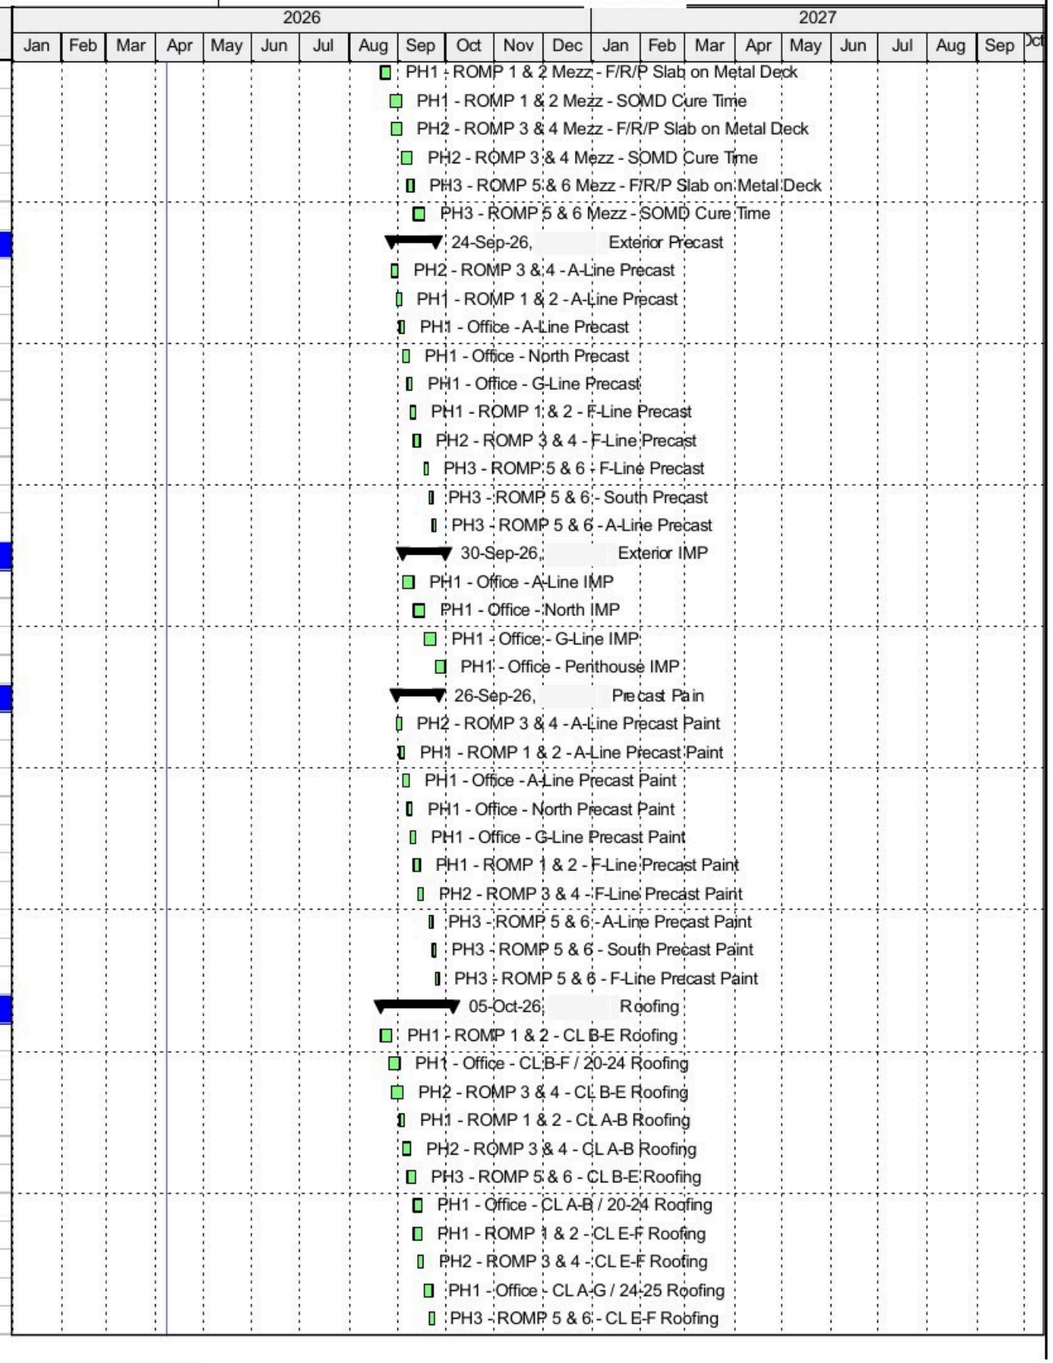


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
OWN.Off.ROOF.120	PH1 - Office - CL F-G / 20-24 Roofing	3	25-Sep-26	30-Sep-26		
OWN.P3.ROOF.110	PH3 - ROMP 5 & 6 - CL A-B Roofing	3	25-Sep-26	30-Sep-26		
OWN.Off.ROOF.140	PH1 - Office - Penthouse Roofing	3	01-Oct-26	05-Oct-26		
Louvers/Damper/Attenuators		38	08-Sep-26	29-Oct-26		
A-Line Louvers/Bracing/Attenuators (New)		38	08-Sep-26	29-Oct-26		
OWN.P1.LOUV.110	PH1 - ROMP 1 & 2 - Attenuator Bracing	3	08-Sep-26	10-Sep-26	Trade	HVAC
OWN.P2.LOUV.110	PH2 - ROMP 3 & 4 - Attenuator Bracing	3	15-Sep-26	17-Sep-26	Trade	HVAC
OWN.P3.LOUV.110	PH3 - ROMP 5 & 6 - Attenuator Bracing	3	25-Sep-26	30-Sep-26	Trade	HVAC
OWN.P1.LOUV.130	PH1 - ROMP 1 & 2 - A-Line Sound Attenuators	3	13-Oct-26	15-Oct-26	Trade	HVAC
OWN.P2.LOUV.130	PH2 - ROMP 3 & 4 - A-Line Sound Attenuators	3	20-Oct-26	22-Oct-26	Trade	HVAC
OWN.P3.LOUV.130	PH3 - ROMP 5 & 6 - A-Line Sound Attenuators	3	27-Oct-26	29-Oct-26	Trade	HVAC
OWN.P1.LOUV.100	PH1 - ROMP 1 & 2 - A-Line Louvers	5	06-Oct-26	12-Oct-26		
OWN.P2.LOUV.100	PH2 - ROMP 3 & 4 - A-Line Louvers	5	13-Oct-26	19-Oct-26		
OWN.P3.LOUV.100	PH3 - ROMP 5 & 6 - A-Line Louvers	5	20-Oct-26	26-Oct-26		
F-Line Dampers/Bird Screen (New)		16	22-Sep-26	13-Oct-26		
OWN.P1.LOUV.200	PH1 - ROMP 1 & 2 - F-Line Dampers	4	22-Sep-26	25-Sep-26	Trade	HVAC
OWN.P2.LOUV.200	PH2 - ROMP 3 & 4 - F-Line Dampers	4	29-Sep-26	02-Oct-26	Trade	HVAC
OWN.P3.LOUV.200	PH3 - ROMP 5 & 6 - F-Line Dampers	4	05-Oct-26	08-Oct-26	Trade	HVAC
OWN.P1.LOUV.210	PH1 - ROMP 1 & 2 - Bird Screen	3	29-Sep-26	01-Oct-26		
OWN.P2.LOUV.210	PH2 - ROMP 3 & 4 - Bird Screen	3	05-Oct-26	07-Oct-26		
OWN.P3.LOUV.210	PH3 - ROMP 5 & 6 - Bird Screen	3	09-Oct-26	13-Oct-26		
Stairs		36	12-Aug-26	30-Sep-26		
OWN.Off.Stairs.100	PH1 - Office - Install Stair 03	10	12-Aug-26	25-Aug-26		
OWN.Off.Stairs.110	PH1 - Office - Install Stair 01	5	26-Aug-26	01-Sep-26		
OWN.Off.Stairs.120	PH1 - Office - Install Stair 02	5	02-Sep-26	08-Sep-26		
OWN.P1.Stairs.100	PH1 - ROMP 1 & 2 - Install Stairs	5	09-Sep-26	15-Sep-26		
OWN.P2.Stairs.100	PH2 - ROMP 3 & 4 - Install Stairs	5	16-Sep-26	22-Sep-26		
OWN.P3.Stairs.100	PH3 - ROMP 5 & 6 - Install Stairs	5	23-Sep-26	30-Sep-26		
Fireproofing		26	02-Sep-26	07-Oct-26		
OWN.Off.FP.100	PH1 - Office - L1 - Fireproofing	5	02-Sep-26	08-Sep-26		
OWN.P1.FP.100	PH1 - ROMP 1 & 2 - Fireproofing	5	16-Sep-26	22-Sep-26		
OWN.P2.FP.100	PH2 - ROMP 3 & 4 - Fireproofing	5	23-Sep-26	30-Sep-26		
OWN.Off.FP.110	PH1 - Office - M1 - Fireproofing	5	23-Sep-26	30-Sep-26		
OWN.P3.FP.100	PH3 - ROMP 5 & 6 - Fireproofing	5	01-Oct-26	07-Oct-26		
Exterior Buildout / Genyard / Tankfarm / Site		227	07-May-26	19-Mar-27		
PH1 - Office - Tank Farm		100	19-Aug-26	05-Jan-27		
Office.TF.MEPUG.100	PH1 - Office - MEPF Shallow U/G's	5	19-Aug-26	25-Aug-26		
Office.TF.FOND.100	PH1 - Office - F/R/P Equipment Pads	5	07-Sep-26	11-Sep-26		
Office.TF.FOND.120	PH1 - Office - Equipment Pads Cure	7	12-Sep-26	18-Sep-26		
Office.TF.FOND.110	PH1 - Office - F/R/P Slab at Water Tanks	10	14-Sep-26	25-Sep-26		
Office.TF.FOND.130	PH1 - Office - Water Tank Slab Cure	7	26-Sep-26	02-Oct-26		
PH1 - Office - Tank Farm Equipment		30	13-Oct-26	23-Nov-26		
Office.TF.100	PH1 - Office - Install Water Tanks (OFCI)	15	13-Oct-26	02-Nov-26		
Office.TF.110	PH1 - Office - MEPF Connections	15	03-Nov-26	23-Nov-26		
PH1 - Office - Tank Farm Commissioning		31	24-Nov-26	05-Jan-27		

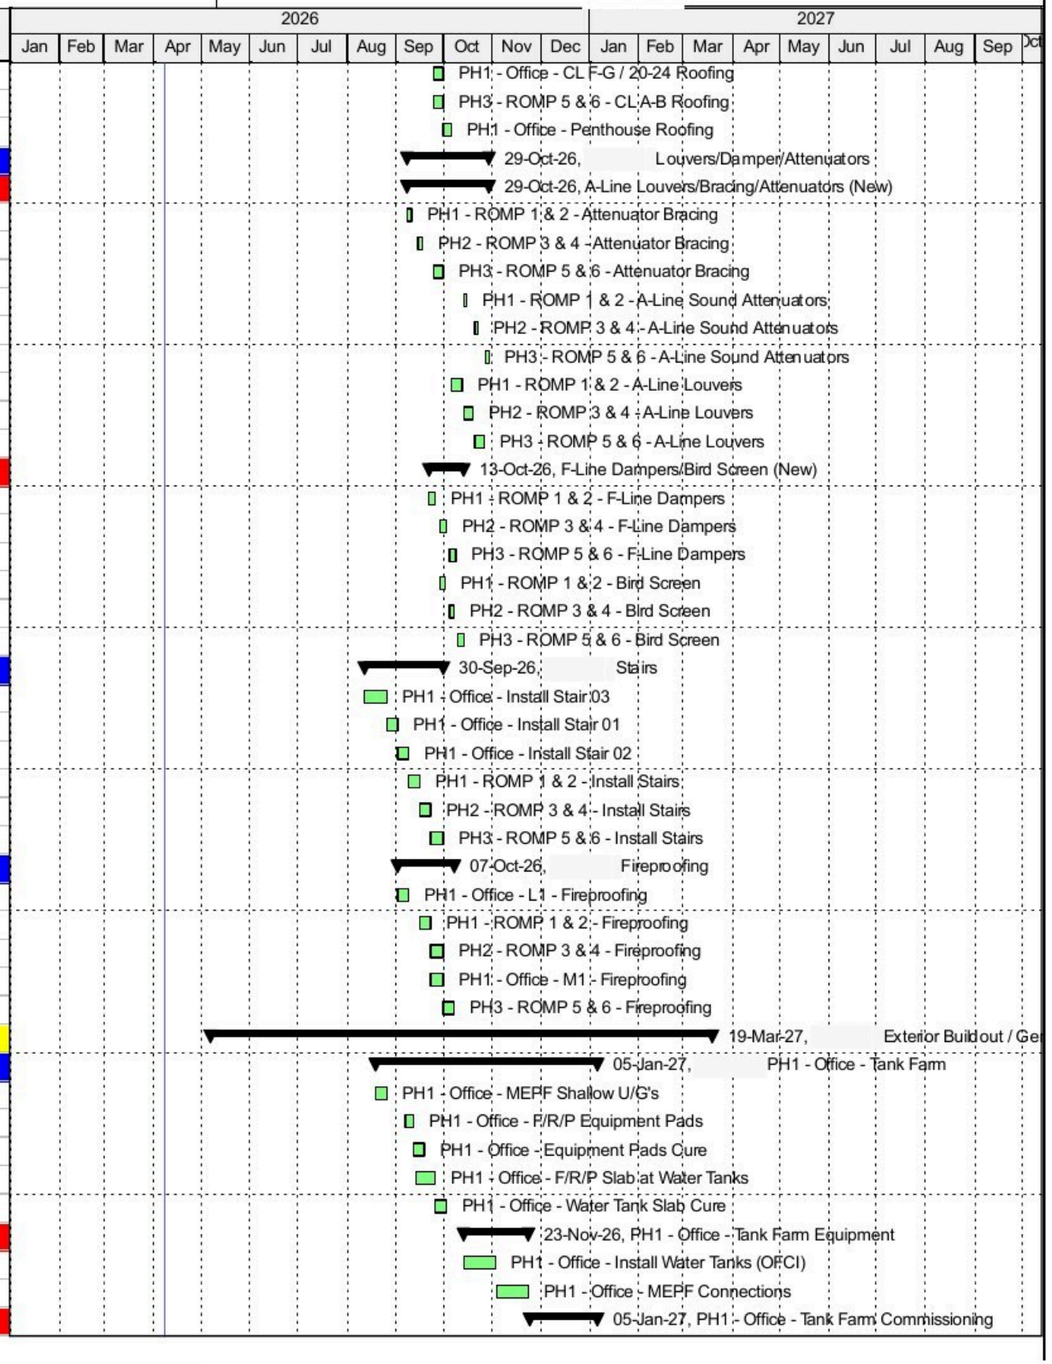


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE | CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.Office.TF.100	L2 Commissioning - Office Tank Farm	10	24-Nov-26	07-Dec-26		
Cx.Office.TF.110	Energize Equipment - Office Tank Farm	5	08-Dec-26	14-Dec-26		
Cx.Office.TF.120	L3 Commissioning - Office Tank Farm	15	15-Dec-26	05-Jan-27		
PH1 - Office - Gen Yard		111	05-Aug-26	06-Jan-27		
Office.GY.MEPUG.100	PH1 - Office - Deep MEP U/G	5	05-Aug-26	11-Aug-26		
Office.GY.MEPUG.110	PH1 - Office - Shallow MEP U/G	5	12-Aug-26	18-Aug-26		
Office.GY.FOND.100	PH1 - Office - F/R/P Equipment Pads and Foundations	5	27-Aug-26	02-Sep-26		
Office.GY.FOND.110	PH1 - Office - Equipment Pads and Foundations Cure	5	25-Sep-26	30-Sep-26		
Office.GY.FOND.120	PH1 - Office - Excavate for Loading Dock	5	27-Oct-26	02-Nov-26		
Office.GY.FOND.130	PH1 - Office - F/R/P Stem Wall at Loading Dock Ramp	10	03-Nov-26	16-Nov-26		
Office.GY.FOND.140	PH1 - Office - F/R/P Stem Wall at Trash Enclosure	5	17-Nov-26	23-Nov-26		
Office.GY.110	PH1 - Office - Pull & Terminate Wires	15	24-Nov-26	14-Dec-26		
Office.GY.FOND.150	PH1 - Office - F/R/P Slab at Exterior Loading Dock CL 18-29	5	24-Nov-26	30-Nov-26		
Office.GY.140	PH1 - Office - CMU at Trash Enclosure	5	01-Dec-26	07-Dec-26		
PH1 - Office Gen Yard Equipment		5	19-Oct-26	23-Oct-26		
Office.GY.100	PH1 - Office - Install MVA & MVB (OFCI)	5	19-Oct-26	23-Oct-26		
PH1 - Office Gen Yard Commissioning		17	15-Dec-26	06-Jan-27		
PH1 - Office Gen Yard - MVA & MVB		17	15-Dec-26	06-Jan-27		
Cx.Office.GY.MVA.MVB.100	Office Gen Yard - MVA & MVB - Pre Startup Installer	5	15-Dec-26	22-Dec-26		
Cx.Office.GY.MVA.MVB.110	Office Gen Yard - MVA & MVB - Pre Startup Vendor	3	15-Dec-26	18-Dec-26		
Cx.Office.GY.MVA.MVB.120	Office Gen Yard - MVA & MVB - L2 QC	1	23-Dec-26	23-Dec-26		
Cx.Office.GY.MVA.MVB.130	Office Gen Yard - MVA & MVB - Installation Verification Checklist	1	24-Dec-26	24-Dec-26		
Cx.Office.GY.MVA.MVB.140	Office Gen Yard - MVA & MVB - Yellow Tag	1	25-Dec-26	25-Dec-26		
Cx.Office.GY.MVA.MVB.150	Office Gen Yard - MVA & MVB - Energize Equipment	1	28-Dec-26	28-Dec-26		
Cx.Office.GY.MVA.MVB.160	Office Gen Yard - MVA & MVB - L3 Startup	4	29-Dec-26	01-Jan-27		
Cx.Office.GY.MVA.MVB.170	Office Gen Yard - MVA & MVB - EPMS SAT	1	04-Jan-27	04-Jan-27		
Cx.Office.GY.MVA.MVB.180	Office Gen Yard - MVA & MVB - Thermographic Checks	1	05-Jan-27	05-Jan-27		
Cx.Office.GY.MVA.MVB.190	Office Gen Yard - MVA & MVB - Green Tag	1	06-Jan-27	06-Jan-27		
Phase 1 Gen Yard (ROMP 1 & 2)		199	21-May-26	23-Feb-27		
PH1.GY.FOND.100	PH1 - ROMP 1 & 2 - Micropile Drilling	5	21-May-26	27-May-26		
PH1.GY.FOND.110	PH1 - ROMP 1 & 2 - Micropile Grouting	3	28-May-26	01-Jun-26		
PH1.GY.FOND.120	PH1 - ROMP 1 & 2 - Micropile Cure	7	02-Jun-26	08-Jun-26		
PH1.GY.FOND.130	PH1 - ROMP 1 & 2 - Micropile Asbuilts	3	02-Jun-26	04-Jun-26		
PH1.GY.FOND.140	PH1 - ROMP 1 & 2 - Micropile Testing	3	09-Jun-26	11-Jun-26		
PH1.GY.FOND.150	PH1 - ROMP 1 & 2 - Micropile Excavation	3	12-Jun-26	17-Jun-26		
PH1.GY.FOND.160	PH1 - ROMP 1 & 2 - F/R/P Micropile Caps	5	18-Jun-26	24-Jun-26		
PH1.GY.FOND.170	PH1 - ROMP 1 & 2 - Micropile Cap Cure	7	25-Jun-26	01-Jul-26		
PH1.GY.MEPUG.100	PH1 - ROMP 1 & 2 - F-Line U/G Deep Storm Install	5	02-Jul-26	08-Jul-26		
PH1.GY.MEPUG.110	PH1 - ROMP 1 & 2 - U/G Deep Storm Test and Backfill	3	09-Jul-26	13-Jul-26		
PH1.GY.MEPUG.120	PH1 - ROMP 1 & 2 - F-Line MEP U/G (Ductbanks)	5	29-Jul-26	04-Aug-26		
PH1.GY.MEPUG.130	PH1 - ROMP 1 & 2 - Shallow MEPF U/G	5	05-Aug-26	11-Aug-26		
PH1.GY.MEPUG.150	PH1 - ROMP 1 & 2 - Shallow Storm Drain Connection	3	05-Aug-26	07-Aug-26		
PH1.GY.FOND.180	PH1 - ROMP 1 & 2 - F/R/P Equipment Pads and Foundations	7	18-Aug-26	26-Aug-26		
PH1.GY.FOND.190	PH1 - ROMP 1 & 2 - Equipment Pads and Foundations Cure	7	27-Aug-26	02-Sep-26		
PH1.GY.180	PH1 - ROMP 1 & 2 - Install Screen Wall Panels	5	12-Oct-26	16-Oct-26		

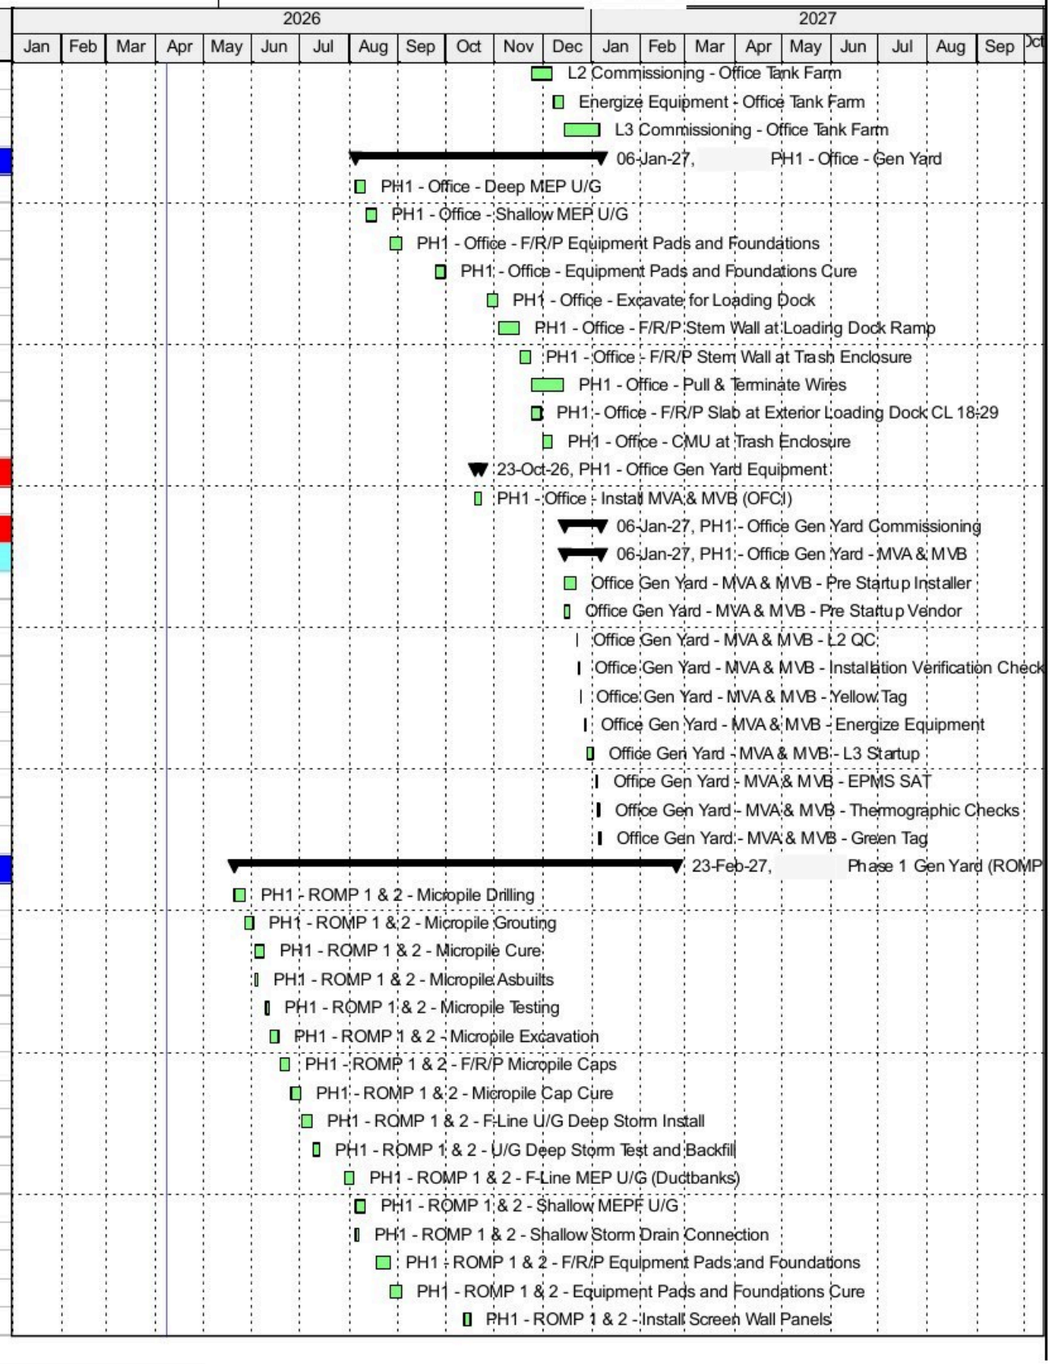


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH1.GY.MEPUG.140	PH1 - ROMP 1 & 2 - Shallow Security Loop U/G	5	19-Oct-26	23-Oct-26		
PH1.GY.150	PH1 - ROMP 1 & 2 - Install Cable Bus	15	02-Nov-26	23-Nov-26		
PH1.GY.160	PH1 - ROMP 1 & 2 - Pull & Terminate Wires	15	15-Dec-26	05-Jan-27		
Phase 1 Gen Yard Equipment (ROMP 1 & 2)		42	02-Nov-26	29-Dec-26		
PH1.GY.220	PH1 - ROMP 1 & 2 - Install Exhaust Flues	5	09-Nov-26	13-Nov-26	Trade	Mechanical
PH1.GY.140	PH1 - ROMP 1 & 2 - Install Generators (OFCI)	5	02-Nov-26	06-Nov-26		
PH1.GY.170	PH1 - ROMP 1 & 2 - Install XFMR-USB's (OFCI)	5	03-Nov-26	09-Nov-26		
PH1.GY.130	PH1 - ROMP 1 & 2 - Install HPP Panels (OFCI)	5	05-Nov-26	11-Nov-26		
PH1.GY.190	PH1 - ROMP 1 & 2 - Install Fuel Top Up System	5	09-Nov-26	13-Nov-26		
PH1.GY.200	PH1 - ROMP 1 & 2 - Generator to ATS/MV-XFMR - Cable Pulls	10	24-Nov-26	07-Dec-26		
PH1.GY.210	PH1 - ROMP 1 & 2 - Generator to ATS/MV-XFMR - Cable Test & Ter	15	08-Dec-26	29-Dec-26		
Phase 1 Gen Yard Commissioning (ROMP 1 & 2)		35	06-Jan-27	23-Feb-27		
PH1 - ROMP 1 & 2 Gen Yard - XFMR-USB-1.1M, 1.1C, 1.1A, 1.1B,1.2A, & 1.2B Cx		19	06-Jan-27	01-Feb-27		
Cx.PH1.GY.XFMR.100	PH1 Gen Yard - XFMR's - Pre Startup Installer	5	06-Jan-27	12-Jan-27		
Cx.PH1.GY.XFMR.110	PH1 Gen Yard - XFMR's - Pre Startup Vendor	3	06-Jan-27	08-Jan-27		
Cx.PH1.GY.XFMR.120	PH1 Gen Yard - XFMR's - L2 QC	1	13-Jan-27	13-Jan-27		
Cx.PH1.GY.XFMR.130	PH1 Gen Yard - XFMR's - Installation Verification Checklist	1	18-Jan-27	18-Jan-27		
Cx.PH1.GY.XFMR.140	PH1 Gen Yard - XFMR's - Yellow Tag	1	19-Jan-27	19-Jan-27		
Cx.PH1.GY.XFMR.150	PH1 Gen Yard - XFMR's - Energize Equipment	1	20-Jan-27	20-Jan-27		
Cx.PH1.GY.XFMR.160	PH1 Gen Yard - XFMR's - L3 Startup	4	21-Jan-27	27-Jan-27		
Cx.PH1.GY.XFMR.170	PH1 Gen Yard - XFMR's - EPMS SAT	1	28-Jan-27	28-Jan-27		
Cx.PH1.GY.XFMR.180	PH1 Gen Yard - XFMR's - Thermographic Checks	1	29-Jan-27	29-Jan-27		
Cx.PH1.GY.XFMR.190	PH1 Gen Yard - XFMR's - Green Tag	1	01-Feb-27	01-Feb-27		
PH1 - ROMP 1 & 2 Gen Yard - GEN-1.1M, GEN-1.1C, GEN1.1A, GEN1.1B, GEN-1.2A, & GEN-1.2B Cx		19	06-Jan-27	01-Feb-27		
Cx.PH1.GY.GEN.100	PH1 Gen Yard - Gen's - Pre Startup Installer	5	06-Jan-27	12-Jan-27		
Cx.PH1.GY.GEN.110	PH1 Gen Yard - Gen's - Pre Startup Vendor	3	06-Jan-27	08-Jan-27		
Cx.PH1.GY.GEN.120	PH1 Gen Yard - Gen's - L2 QC	1	13-Jan-27	13-Jan-27		
Cx.PH1.GY.GEN.130	PH1 Gen Yard - Gen's - Installation Verification Checklist	1	18-Jan-27	18-Jan-27		
Cx.PH1.GY.GEN.140	PH1 Gen Yard - Gen's - Yellow Tag	1	19-Jan-27	19-Jan-27		
Cx.PH1.GY.GEN.150	PH1 Gen Yard - Gen's - Energize Equipment	1	20-Jan-27	20-Jan-27		
Cx.PH1.GY.GEN.160	PH1 Gen Yard - Gen's - L3 Startup	4	21-Jan-27	27-Jan-27		
Cx.PH1.GY.GEN.170	PH1 Gen Yard - Gen's - EPMS SAT	1	28-Jan-27	28-Jan-27		
Cx.PH1.GY.GEN.180	PH1 Gen Yard - Gen's - Thermographic Checks	1	29-Jan-27	29-Jan-27		
Cx.PH1.GY.GEN.190	PH1 Gen Yard - Gen's - Green Tag	1	01-Feb-27	01-Feb-27		
PH1 - ROMP 1 & 2 Gen Yard - HPP-FC1 Cx		35	06-Jan-27	23-Feb-27		
Cx.PH1.GY.HPP.100	PH1 Gen Yard - HPP - Pre Startup Installer	5	06-Jan-27	12-Jan-27		
Cx.PH1.GY.HPP.110	PH1 Gen Yard - HPP - Pre Startup Vendor	3	06-Jan-27	08-Jan-27		
Cx.PH1.GY.HPP.120	PH1 Gen Yard - HPP - L2 QC	1	13-Jan-27	13-Jan-27		
Cx.PH1.GY.HPP.130	PH1 Gen Yard - HPP - Installation Verification Checklist	2	18-Jan-27	19-Jan-27		
Cx.PH1.GY.HPP.140	PH1 Gen Yard - HPP - Yellow Tag	1	20-Jan-27	20-Jan-27		
Cx.PH1.GY.HPP.150	PH1 Gen Yard - HPP - Energize Equipment	1	17-Feb-27	17-Feb-27		
Cx.PH1.GY.HPP.160	PH1 Gen Yard - HPP - L3 Startup	1	18-Feb-27	18-Feb-27		
Cx.PH1.GY.HPP.170	PH1 Gen Yard - HPP - EPMS SAT	1	19-Feb-27	19-Feb-27		
Cx.PH1.GY.HPP.180	PH1 Gen Yard - HPP - Thermographic Checks	1	22-Feb-27	22-Feb-27		
Cx.PH1.GY.HPP.190	PH1 Gen Yard - HPP - Green Tag	1	23-Feb-27	23-Feb-27		

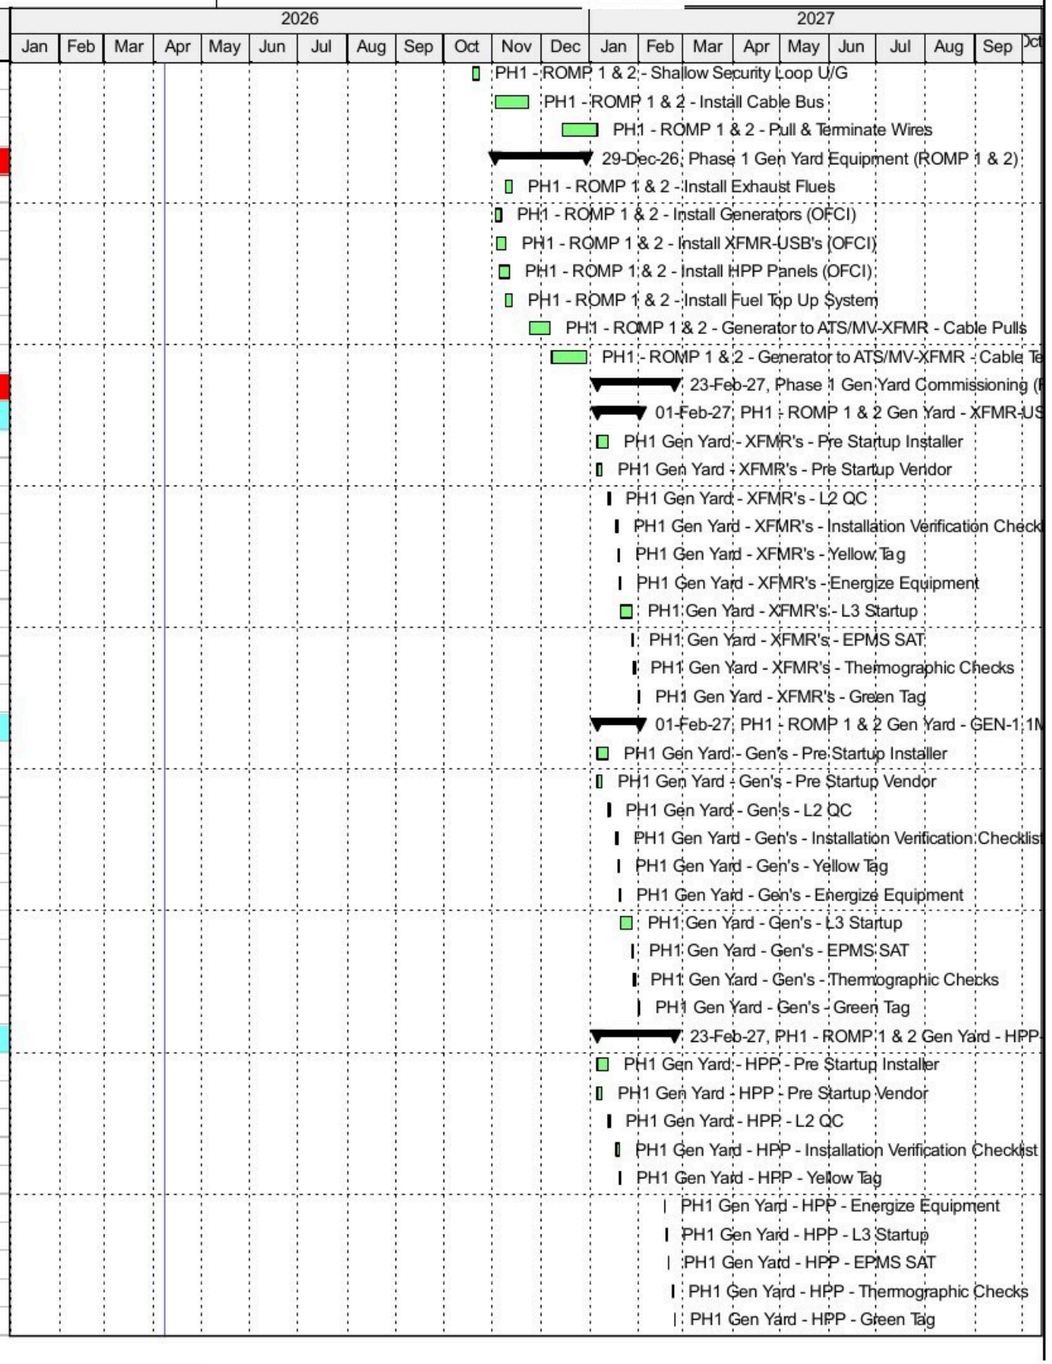


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Phase 2 Gen Yard (ROMP 3 & 4)		206	14-May-26	25-Feb-27		
PH2.GY.FOND.100	PH2 - ROMP 3 & 4 - Micropile Drilling	5	14-May-26	20-May-26		
PH2.GY.FOND.110	PH2 - ROMP 3 & 4 - Micropile Grouting	3	21-May-26	25-May-26		
PH2.GY.FOND.120	PH2 - ROMP 3 & 4 - Micropile Cure	7	26-May-26	01-Jun-26		
PH2.GY.FOND.130	PH2 - ROMP 3 & 4 - Micropile Asbuilts	3	26-May-26	28-May-26		
PH2.GY.FOND.140	PH2 - ROMP 3 & 4 - Micropile Testing	3	02-Jun-26	04-Jun-26		
PH2.GY.FOND.150	PH2 - ROMP 3 & 4 - Micropile Excavation	3	05-Jun-26	09-Jun-26		
PH2.GY.FOND.160	PH2 - ROMP 3 & 4 - F/R/P Micropile Caps	5	10-Jun-26	17-Jun-26		
PH2.GY.FOND.170	PH2 - ROMP 3 & 4 - Micropile Cap Cure	7	18-Jun-26	24-Jun-26		
PH2.GY.MEPUG.100	PH2 - ROMP 3 & 4 - F-Line U/G Deep Storm Install	5	25-Jun-26	01-Jul-26		
PH2.GY.MEPUG.110	PH2 - ROMP 3 & 4 - U/G Deep Storm Test and Backfill	3	09-Jul-26	13-Jul-26		
PH2.GY.MEPUG.120	PH2 - ROMP 3 & 4 - F-Line MEP U/G (Ductbanks)	5	21-Jul-26	28-Jul-26		
PH2.GY.MEPUG.130	PH2 - ROMP 3 & 4 - Shallow MEPF U/G	5	29-Jul-26	04-Aug-26		
PH2.GY.MEPUG.150	PH2 - ROMP 3 & 4 - Shallow Storm Drain Connection	3	29-Jul-26	31-Jul-26		
PH2.GY.FOND.180	PH2 - ROMP 3 & 4 - F/R/P Equipment Pads and Foundations	7	07-Aug-26	17-Aug-26		
PH2.GY.FOND.190	PH2 - ROMP 3 & 4 - Equipment Pads and Foundations Cure	7	18-Aug-26	24-Aug-26		
PH2.GY.280	PH2 - ROMP 3 & 4 - Install Screen Wall Panels	5	27-Oct-26	02-Nov-26		
PH2.GY.MEPUG.140	PH2 - ROMP 3 & 4 - Shallow Security Loop U/G	5	06-Nov-26	12-Nov-26		
PH2.GY.250	PH2 - ROMP 3 & 4 - Install Cable Bus	15	04-Dec-26	25-Dec-26		
PH2.GY.260	PH2 - ROMP 3 & 4 - Pull & Terminate Wires	15	06-Jan-27	29-Jan-27		
Phase 2 Gen Yard Equipment (ROMP 3 & 4)		65	05-Nov-26	03-Feb-27		
PH2.GY.300	PH2 - ROMP 3 & 4 - Install Exhaust Flues	10	15-Dec-26	29-Dec-26	Trade	Mechanical
PH2.GY.230	PH2 - ROMP 3 & 4 - Install HPP Panels (OFCI)	5	05-Nov-26	11-Nov-26		
PH2.GY.240	PH2 - ROMP 3 & 4 - Install Generators (OFCI)	5	08-Dec-26	14-Dec-26		
PH2.GY.290	PH2 - ROMP 3 & 4 - Install Fuel Top Up System	5	15-Dec-26	22-Dec-26		
PH2.GY.320	PH2 - ROMP 3 & 4 - Generator to ATS/MV-XFMR - Cable Pulls	10	28-Dec-26	08-Jan-27		
PH2.GY.330	PH2 - ROMP 3 & 4 - Generator to ATS/MV-XFMR - Cable Test & Ter	15	11-Jan-27	03-Feb-27		
Phase 2 Gen Yard Commissioning (ROMP 3 & 4)		16	04-Feb-27	25-Feb-27		
PH2 - ROMP 3 & 4 Gen Yard - XFMR-USB-1.3M, 1.3C, 1.3A, 1.3B,1.4A, & 1.4B Cx		16	04-Feb-27	25-Feb-27		
Cx.PH2.GY.XFMR.100	PH2 Gen Yard - XFMR's - Pre Startup Installer	5	04-Feb-27	10-Feb-27		
Cx.PH2.GY.XFMR.110	PH2 Gen Yard - XFMR's - Pre Startup Vendor	3	04-Feb-27	08-Feb-27		
Cx.PH2.GY.XFMR.120	PH2 Gen Yard - XFMR's - L2 QC	1	11-Feb-27	11-Feb-27		
Cx.PH2.GY.XFMR.130	PH2 Gen Yard - XFMR's - Installation Verification Checklist	1	12-Feb-27	12-Feb-27		
Cx.PH2.GY.XFMR.140	PH2 Gen Yard - XFMR's - Yellow Tag	1	15-Feb-27	15-Feb-27		
Cx.PH2.GY.XFMR.150	PH2 Gen Yard - XFMR's - Energize Equipment	1	16-Feb-27	16-Feb-27		
Cx.PH2.GY.XFMR.160	PH2 Gen Yard - XFMR's - L3 Startup	4	17-Feb-27	22-Feb-27		
Cx.PH2.GY.XFMR.170	PH2 Gen Yard - XFMR's - EPMS SAT	1	23-Feb-27	23-Feb-27		
Cx.PH2.GY.XFMR.180	PH2 Gen Yard - XFMR's - Thermographic Checks	1	24-Feb-27	24-Feb-27		
Cx.PH2.GY.XFMR.190	PH2 Gen Yard - XFMR's - Green Tag	1	25-Feb-27	25-Feb-27		
PH2 - ROMP 3 & 4 Gen Yard - GEN-1.3M, GEN-1.3C, GEN1.3A, GEN1.3B, GEN-1.4A, & GEN-1.4B Cx		16	04-Feb-27	25-Feb-27		
Cx.PH2.GY.GEN.100	PH2 Gen Yard - Gen's - Pre Startup Installer	5	04-Feb-27	10-Feb-27		
Cx.PH2.GY.GEN.110	PH2 Gen Yard - Gen's - Pre Startup Vendor	3	04-Feb-27	08-Feb-27		
Cx.PH2.GY.GEN.120	PH2 Gen Yard - Gen's - L2 QC	1	11-Feb-27	11-Feb-27		
Cx.PH2.GY.GEN.130	PH2 Gen Yard - Gen's - Installation Verification Checklist	1	12-Feb-27	12-Feb-27		
Cx.PH2.GY.GEN.140	PH2 Gen Yard - Gen's - Yellow Tag	1	15-Feb-27	15-Feb-27		

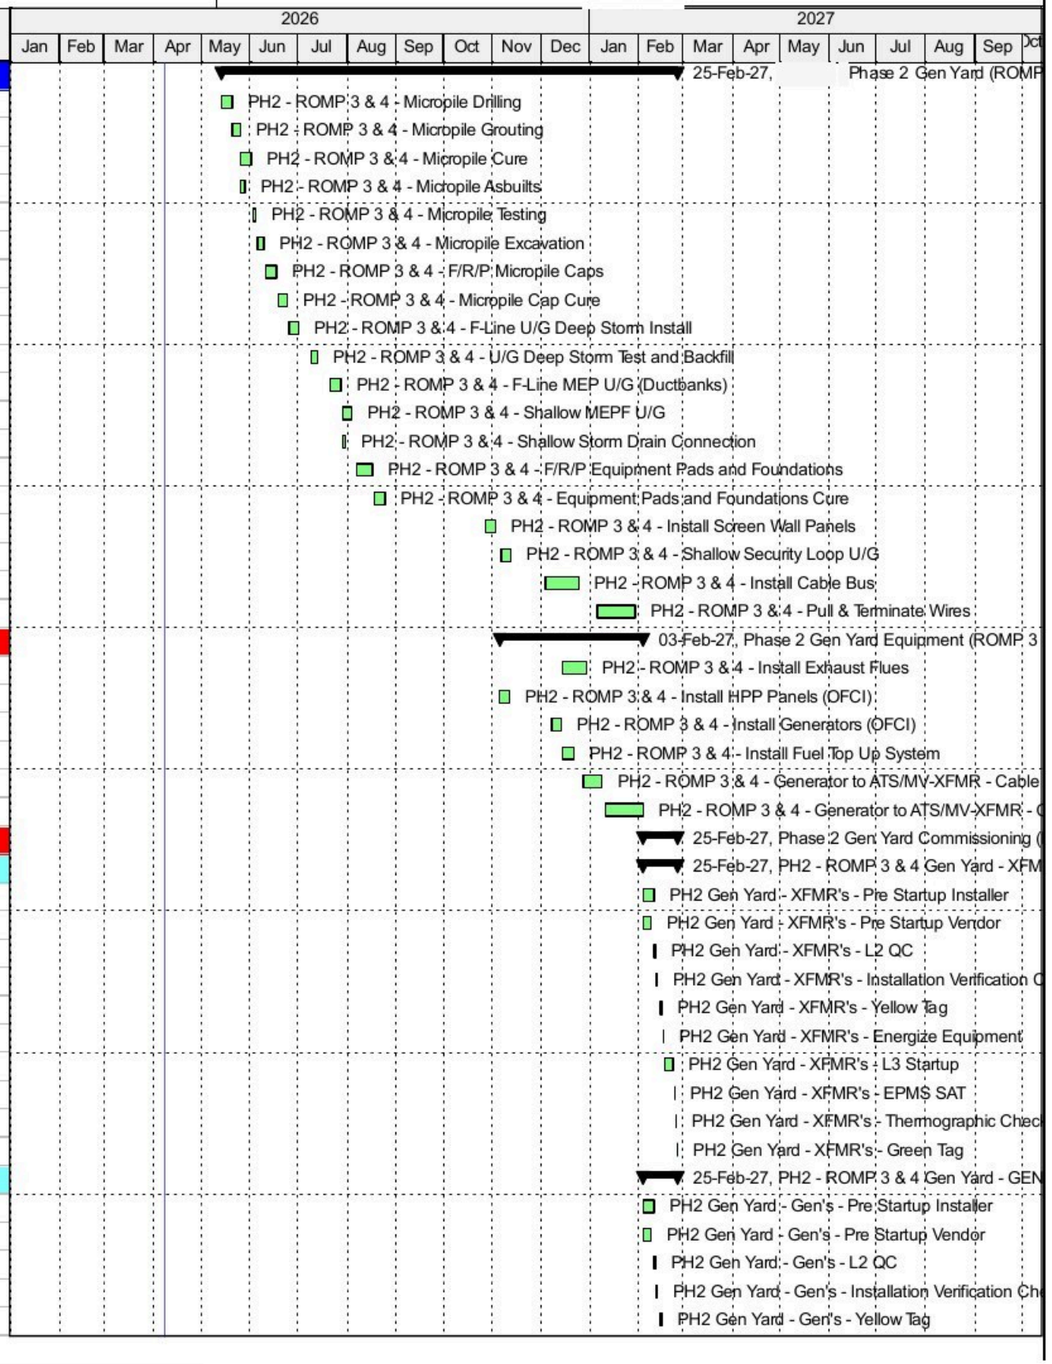


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH2.GY.GEN.150	PH2 Gen Yard - Gen's - Energize Equipment	1	16-Feb-27	16-Feb-27		
Cx.PH2.GY.GEN.160	PH2 Gen Yard - Gen's - L3 Startup	4	17-Feb-27	22-Feb-27		
Cx.PH2.GY.GEN.170	PH2 Gen Yard - Gen's - EPMS SAT	1	23-Feb-27	23-Feb-27		
Cx.PH2.GY.GEN.180	PH2 Gen Yard - Gen's - Thermographic Checks	1	24-Feb-27	24-Feb-27		
Cx.PH2.GY.GEN.190	PH2 Gen Yard - Gen's - Green Tag	1	25-Feb-27	25-Feb-27		
Phase 3 Gen Yard (ROMP 5 & 6)		223	07-May-26	15-Mar-27		
PH3.GY.FOND.100	PH3 - ROMP 5 & 6 - Micropile Drilling	5	07-May-26	13-May-26		
PH3.GY.FOND.110	PH3 - ROMP 5 & 6 - Micropile Grouting	3	14-May-26	18-May-26		
PH3.GY.FOND.120	PH3 - ROMP 5 & 6 - Micropile Cure	7	19-May-26	25-May-26		
PH3.GY.FOND.130	PH3 - ROMP 5 & 6 - Micropile Asbuilts	3	19-May-26	21-May-26		
PH3.GY.FOND.140	PH3 - ROMP 5 & 6 - Micropile Testing	3	26-May-26	28-May-26		
PH3.GY.FOND.150	PH3 - ROMP 5 & 6 - Micropile Excavation	3	29-May-26	02-Jun-26		
PH3.GY.FOND.160	PH3 - ROMP 5 & 6 - F/R/P Micropile Caps	5	03-Jun-26	09-Jun-26		
PH3.GY.FOND.170	PH3 - ROMP 5 & 6 - Micropile Cap Cure	7	10-Jun-26	16-Jun-26		
PH3.GY.MEPUG.100	PH3 - ROMP 5 & 6 - F-Line U/G Deep Storm Install	5	17-Jun-26	23-Jun-26		
PH3.GY.MEPUG.110	PH3 - ROMP 5 & 6 - U/G Deep Storm Test and Backfill	3	09-Jul-26	13-Jul-26		
PH3.GY.MEPUG.120	PH3 - ROMP 5 & 6 - F-Line MEP U/G (Ductbanks)	5	14-Jul-26	20-Jul-26		
PH3.GY.MEPUG.130	PH3 - ROMP 5 & 6 - Shallow MEPF U/G	5	21-Jul-26	28-Jul-26		
PH3.GY.MEPUG.150	PH3 - ROMP 5 & 6 - Shallow Storm Drain Connection	3	21-Jul-26	23-Jul-26		
PH3.GY.FOND.180	PH3 - ROMP 5 & 6 - F/R/P Equipment Pads and Foundations	7	29-Jul-26	06-Aug-26		
PH3.GY.FOND.190	PH3 - ROMP 5 & 6 - Equipment Pads and Foundations Cure	7	07-Aug-26	13-Aug-26		
PH3.GY.380	PH3 - ROMP 5 & 6 - Install Screen Wall Panels	5	03-Nov-26	09-Nov-26		
PH3.GY.MEPUG.140	PH3 - ROMP 5 & 6 - Shallow Security Loop U/G	5	13-Nov-26	19-Nov-26		
PH3.GY.350	PH3 - ROMP 5 & 6 - Install Cable Bus	15	16-Dec-26	06-Jan-27		
PH3.GY.360	PH3 - ROMP 5 & 6 - Pull & Terminate Wires	15	01-Feb-27	19-Feb-27		
Phase 3 Gen Yard Equipment (ROMP 5 & 6)		70	10-Nov-26	15-Feb-27		
PH3.GY.400	PH3 - ROMP 5 & 6 - Install Exhaust Flues	10	28-Dec-26	08-Jan-27	Trade	Mechanical
PH3.GY.370	PH3 - ROMP 5 & 6 - Install XFMR-USB's (OFCI)	5	10-Nov-26	16-Nov-26		
PH3.GY.330	PH3 - ROMP 5 & 6 - Install HPP Panels (OFCI)	5	09-Dec-26	15-Dec-26		
PH3.GY.340	PH3 - ROMP 5 & 6 - Install Generators (OFCI)	5	21-Dec-26	25-Dec-26		
PH3.GY.390	PH3 - ROMP 5 & 6 - Install Fuel Top Up System	5	28-Dec-26	01-Jan-27		
PH3.GY.420	PH3 - ROMP 5 & 6 - Generator to ATS/MV-XFMR - Cable Pulls	10	07-Jan-27	25-Jan-27		
PH3.GY.430	PH3 - ROMP 5 & 6 - Generator to ATS/MV-XFMR - Cable Test & Ter	15	26-Jan-27	15-Feb-27		
Phase 3 Gen Yard Commissioning (ROMP 5 & 6)		16	22-Feb-27	15-Mar-27		
PH3 - ROMP 5 & 6 Gen Yard - XFMR-USB-1.5A, XFMR-USB-1.5B, XFMR-USB-1.6A, & XFMR-USB-1.6B Cx		16	22-Feb-27	15-Mar-27		
Cx.PH3.GY.XFMR.100	PH3 Gen Yard - XFMR's - Pre Startup Installer	5	22-Feb-27	26-Feb-27		
Cx.PH3.GY.XFMR.110	PH3 Gen Yard - XFMR's - Pre Startup Vendor	3	22-Feb-27	24-Feb-27		
Cx.PH3.GY.XFMR.120	PH3 Gen Yard - XFMR's - L2 QC	1	01-Mar-27	01-Mar-27		
Cx.PH3.GY.XFMR.130	PH3 Gen Yard - XFMR's - Installation Verification Checklist	1	02-Mar-27	02-Mar-27		
Cx.PH3.GY.XFMR.140	PH3 Gen Yard - XFMR's - Yellow Tag	1	03-Mar-27	03-Mar-27		
Cx.PH3.GY.XFMR.150	PH3 Gen Yard - XFMR's - Energize Equipment	1	04-Mar-27	04-Mar-27		
Cx.PH3.GY.XFMR.160	PH3 Gen Yard - XFMR's - L3 Startup	4	05-Mar-27	10-Mar-27		
Cx.PH3.GY.XFMR.170	PH3 Gen Yard - XFMR's - EPMS SAT	1	11-Mar-27	11-Mar-27		
Cx.PH3.GY.XFMR.180	PH3 Gen Yard - XFMR's - Thermographic Checks	1	12-Mar-27	12-Mar-27		
Cx.PH3.GY.XFMR.190	PH3 Gen Yard - XFMR's - Green Tag	1	15-Mar-27	15-Mar-27		

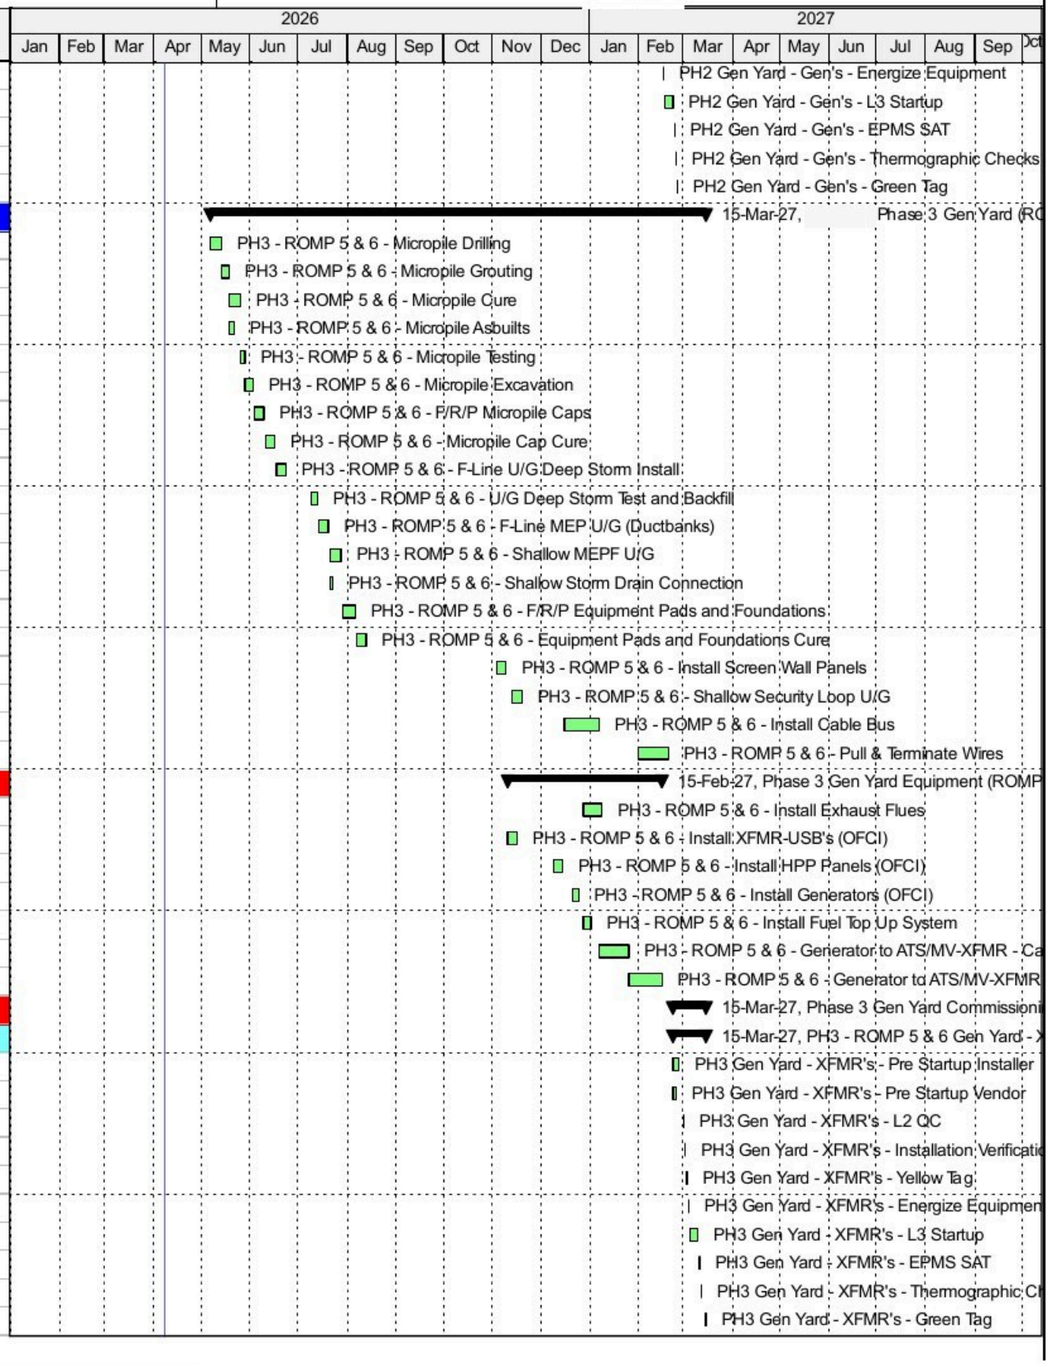


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH3 - ROMP 5 & 6 Gen Yard - GEN-1.5A, GEN-1.5B, GEN1.6A, & GEN1.6B Cx		16	22-Feb-27	15-Mar-27		
Cx.PH3.GY.GEN.100	PH3 Gen Yard - Gen's - Pre Startup Installer	5	22-Feb-27	26-Feb-27		
Cx.PH3.GY.GEN.110	PH3 Gen Yard - Gen's - Pre Startup Vendor	3	22-Feb-27	24-Feb-27		
Cx.PH3.GY.GEN.120	PH3 Gen Yard - Gen's - L2 QC	1	01-Mar-27	01-Mar-27		
Cx.PH3.GY.GEN.130	PH3 Gen Yard - Gen's - Installation Verification Checklist	1	02-Mar-27	02-Mar-27		
Cx.PH3.GY.GEN.140	PH3 Gen Yard - Gen's - Yellow Tag	1	03-Mar-27	03-Mar-27		
Cx.PH3.GY.GEN.150	PH3 Gen Yard - Gen's - Energize Equipment	1	04-Mar-27	04-Mar-27		
Cx.PH3.GY.GEN.160	PH3 Gen Yard - Gen's - L3 Startup	4	05-Mar-27	10-Mar-27		
Cx.PH3.GY.GEN.170	PH3 Gen Yard - Gen's - EPMS SAT	1	11-Mar-27	11-Mar-27		
Cx.PH3.GY.GEN.180	PH3 Gen Yard - Gen's - Thermographic Checks	1	12-Mar-27	12-Mar-27		
Cx.PH3.GY.GEN.190	PH3 Gen Yard - Gen's - Green Tag	1	15-Mar-27	15-Mar-27		
Site Work		106	23-Oct-26	19-Mar-27		
Sidewalks		51	23-Oct-26	01-Jan-27		
PH2.SITE.110	PH2 - ROMP 3 & 4 - F/R/P Sidewalk CL A / 7-14	5	23-Oct-26	29-Oct-26		
PH1.SITE.110	PH1 - ROMP 1 & 2 - F/R/P Sidewalk CL A / 14-21	5	30-Oct-26	05-Nov-26		
Office.SITE.110	PH1 - Office - F/R/P Sidewalk CL A / 21-25	5	06-Nov-26	12-Nov-26		
Office.SITE.120	PH1 - Office - F/R/P North Sidewalk CL A-G / 25	5	13-Nov-26	19-Nov-26		
Office.SITE.100	PH1 - Office - F/R/P Sidewalk CL G / 21-25	5	20-Nov-26	26-Nov-26		
PH1.SITE.100	PH1 - ROMP 1 & 2 - F/R/P Sidewalk CL G / 14-21	5	27-Nov-26	03-Dec-26		
PH2.SITE.100	PH2 - ROMP 3 & 4 - F/R/P Sidewalk CL G / 7-14	5	04-Dec-26	10-Dec-26		
PH3.SITE.100	PH3 - ROMP 5 & 6 - F/R/P Sidewalk CL G / 1-7	5	11-Dec-26	18-Dec-26		
PH3.SITE.120	PH3 - ROMP 5 & 6 - F/R/P South Sidewalk CL A-G / 1	5	21-Dec-26	25-Dec-26		
PH3.SITE.110	PH3 - ROMP 5 & 6 - F/R/P Sidewalk CL A / 1-7	5	28-Dec-26	01-Jan-27		
Fencing		69	15-Dec-26	19-Mar-27		
Office.SITE.210	PH1 - Office - North - Install Fencing	10	15-Dec-26	29-Dec-26		
Office.SITE.200	PH1 - Office - West - Install Fencing	10	30-Dec-26	12-Jan-27		
Office.SITE.220	PH1 - Office - East - Install Fencing	10	30-Dec-26	12-Jan-27		
PH1.SITE.200	PH1 - ROMP 1 & 2 - West - Install Fencing	10	13-Jan-27	29-Jan-27		
PH1.SITE.210	PH1 - ROMP 1 & 2 - East - Install Fencing	10	13-Jan-27	29-Jan-27		
PH2.SITE.200	PH2 - ROMP 3 & 4 - West - Install Fencing	10	04-Feb-27	17-Feb-27		
PH2.SITE.210	PH2 - ROMP 3 & 4 - East - Install Fencing	10	04-Feb-27	17-Feb-27		
PH3.SITE.200	PH3 - ROMP 5 & 6 - West - Install Fencing	10	22-Feb-27	05-Mar-27		
PH3.SITE.220	PH3 - ROMP 5 & 6 - East - Install Fencing	10	22-Feb-27	05-Mar-27		
PH3.SITE.210	PH3 - ROMP 5 & 6 - South - Install Fencing	10	08-Mar-27	19-Mar-27		
Rooftop Installations		92	01-Oct-26	05-Feb-27		
PH1 - Office - Rooftop Installations		66	01-Oct-26	31-Dec-26		
Office.Roof.220	PH1 Roof - Office - Set Exhaust Fans	5	01-Oct-26	07-Oct-26	Trade	HVAC
Office.Roof.230	PH1 Roof - Office - Set Split Units	5	01-Oct-26	07-Oct-26	Trade	HVAC
Office.Roof.210	PH1 Roof - Office - Set RTU	5	17-Nov-26	23-Nov-26	Trade	HVAC
Office.Roof.100	PH1 Roof - Office - Install Scuppers & Downspouts	5	01-Oct-26	07-Oct-26		
Office.Roof.320	PH1 Roof - Office - Security Rough-In Pathways	15	01-Oct-26	21-Oct-26		
Office.Roof.110	PH1 Roof - Office - Install Cross-over stairs	5	01-Oct-26	07-Oct-26		
Office.Roof.310	PH1 Roof - Office - Fixtures & Devices	15	05-Nov-26	25-Nov-26		
Office.Roof.330	PH1 Roof - Office - Electrical Rough-In Pathways	15	05-Nov-26	25-Nov-26		
Office.Roof.340	PH1 Roof - Office - Controls Rough-In Pathways	15	05-Nov-26	25-Nov-26		

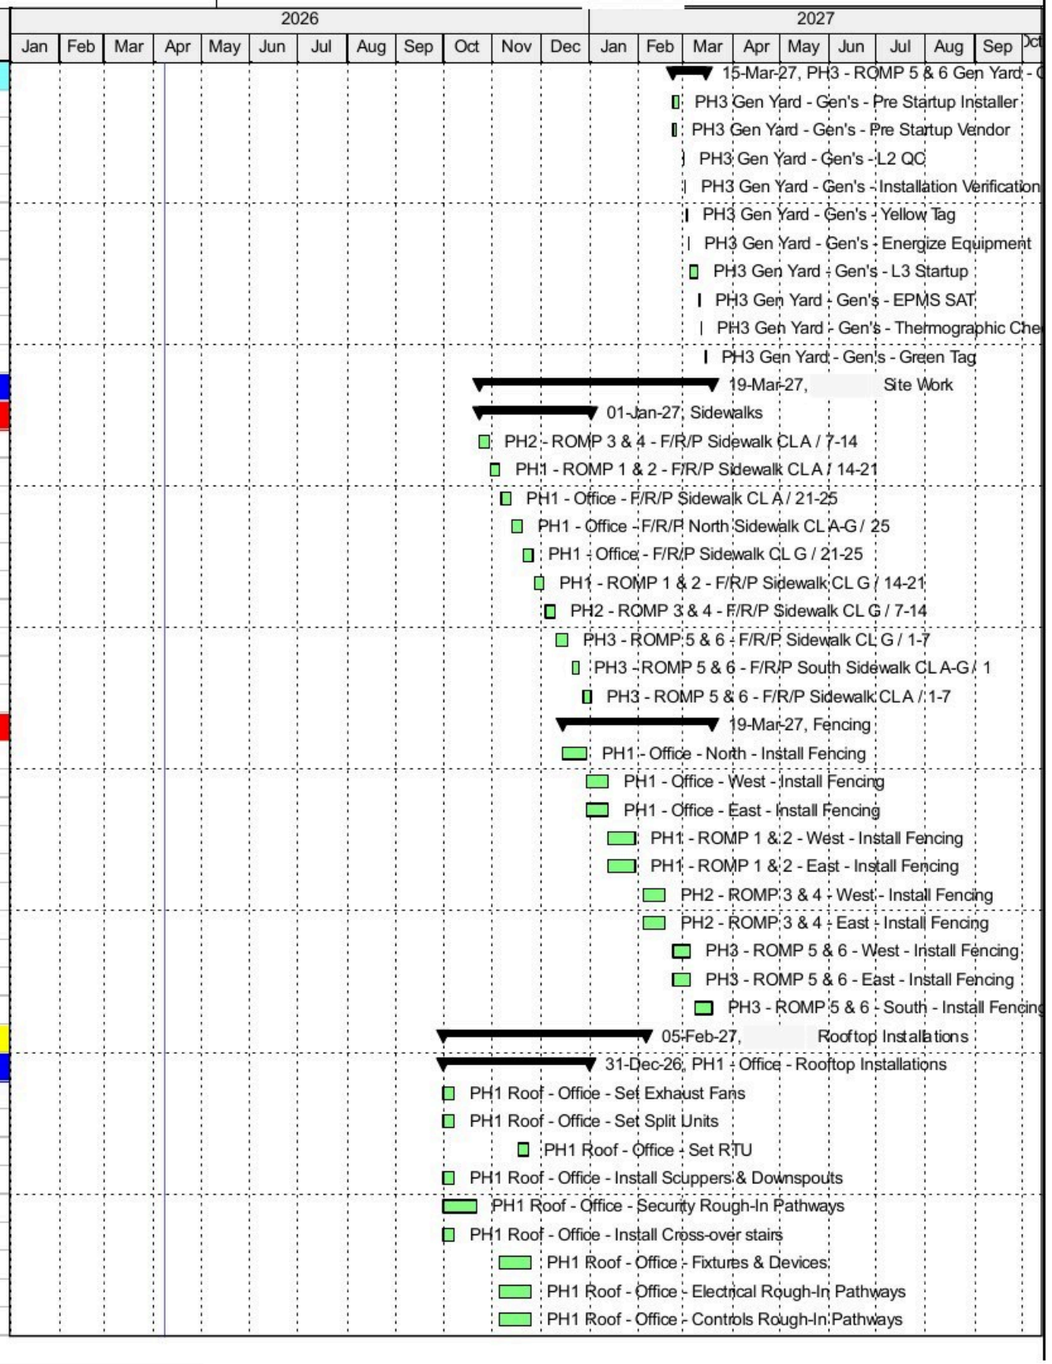


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule


Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Office.Roof.300	PH1 Roof - Office - Roof Piping	10	12-Nov-26	25-Nov-26		
Office.Roof.400	PH1 Roof - Office - Cable Pulls	10	26-Nov-26	09-Dec-26		
Office.Roof.410	PH1 Roof - Office - Test & Terminate Cables	15	10-Dec-26	31-Dec-26		
PH1 - Romp 1 & 2 - Rooftop Installations		54	08-Oct-26	22-Dec-26		
PH1.Roof.220	PH1 Roof - R1&2 - Set Exhaust Fans	5	08-Oct-26	14-Oct-26	Trade	HVAC
PH1.Roof.240	PH1 Roof - R1&2 - Set ACCUs/Condensers/Outdoor CRACs	5	03-Nov-26	09-Nov-26	Trade	HVAC
PH1.Roof.250	PH1 Roof - R1&2 - Set Heat Pump/OSUs	5	03-Nov-26	09-Nov-26	Trade	HVAC
PH1.Roof.100	PH1 Roof - R1&2 - Install Scuppers & Downspouts	5	08-Oct-26	14-Oct-26		
PH1.Roof.230	PH1 Roof - R1&2 - Set Split Units	5	08-Oct-26	14-Oct-26		
PH1.Roof.110	PH1 Roof - R1&2 - Install Cross-over stairs	5	08-Oct-26	14-Oct-26		
PH1.Roof.320	PH1 Roof - R1&2 - Security Rough-In Pathways	15	22-Oct-26	11-Nov-26		
PH1.Roof.330	PH1 Roof - R1&2 - Electrical Rough-In Pathways	15	22-Oct-26	11-Nov-26		
PH1.Roof.310	PH1 Roof - R1&2 - Fixtures & Devices	15	27-Oct-26	16-Nov-26		
PH1.Roof.340	PH1 Roof - R1&2 - Controls Rough-In Pathways	15	27-Oct-26	16-Nov-26		
PH1.Roof.300	PH1 Roof - R1&2 - Roof Piping	10	29-Oct-26	11-Nov-26		
PH1.Roof.400	PH1 Roof - R1&2 - Cable Pulls	10	17-Nov-26	30-Nov-26		
PH1.Roof.410	PH1 Roof - R1&2 - Test & Terminate Cables	15	01-Dec-26	22-Dec-26		
PH2 - Romp 3 & 4 - Rooftop Installations		64	15-Oct-26	12-Jan-27		
PH2.Roof.220	PH2 Roof - R3&4 - Set Exhaust Fans	5	15-Oct-26	21-Oct-26	Trade	HVAC
PH2.Roof.240	PH2 Roof - R3&4 - Set ACCUs/Condensers/Outdoor CRACs	5	10-Nov-26	16-Nov-26	Trade	HVAC
PH2.Roof.250	PH2 Roof - R3&4 - Set Heat Pump/OSUs	5	10-Nov-26	16-Nov-26	Trade	HVAC
PH2.Roof.100	PH2 Roof - R3&4 - Install Scuppers & Downspouts	5	15-Oct-26	21-Oct-26		
PH2.Roof.110	PH2 Roof - R3&4 - Install Cross-over stairs	5	15-Oct-26	21-Oct-26		
PH2.Roof.320	PH2 Roof - R3&4 - Security Rough-In Pathways	15	12-Nov-26	02-Dec-26		
PH2.Roof.330	PH2 Roof - R3&4 - Electrical Rough-In Pathways	15	12-Nov-26	02-Dec-26		
PH2.Roof.300	PH2 Roof - R3&4 - Roof Piping	10	17-Nov-26	30-Nov-26		
PH2.Roof.310	PH2 Roof - R3&4 - Fixtures & Devices	15	17-Nov-26	07-Dec-26		
PH2.Roof.340	PH2 Roof - R3&4 - Controls Rough-In Pathways	15	17-Nov-26	07-Dec-26		
PH2.Roof.400	PH2 Roof - R3&4 - Cable Pulls	10	08-Dec-26	22-Dec-26		
PH2.Roof.410	PH2 Roof - R3&4 - Test & Terminate Cables	15	23-Dec-26	12-Jan-27		
PH3 - Romp 5 & 6 - Rooftop Installations		77	22-Oct-26	05-Feb-27		
PH3.Roof.240	PH3 Roof - R5&6 - Set ACCUs/Condensers/Outdoor CRACs	5	17-Nov-26	23-Nov-26	Trade	HVAC
PH3.Roof.100	PH3 Roof - R5&6 - Install Scuppers & Downspouts	5	22-Oct-26	28-Oct-26		
PH3.Roof.110	PH3 Roof - R5&6 - Install Cross-over stairs	5	22-Oct-26	28-Oct-26		
PH3.Roof.300	PH3 Roof - R5&6 - Roof Piping	5	24-Nov-26	30-Nov-26		
PH3.Roof.310	PH3 Roof - R5&6 - Fixtures & Devices	15	24-Nov-26	14-Dec-26		
PH3.Roof.320	PH3 Roof - R5&6 - Security Rough-In Pathways	15	03-Dec-26	24-Dec-26		
PH3.Roof.330	PH3 Roof - R5&6 - Electrical Rough-In Pathways	15	03-Dec-26	24-Dec-26		
PH3.Roof.340	PH3 Roof - R5&6 - Controls Rough-In Pathways	15	08-Dec-26	29-Dec-26		
PH3.Roof.400	PH3 Roof - R5&6 - Cable Pulls	10	30-Dec-26	12-Jan-27		
PH3.Roof.410	PH3 Roof - R5&6 - Test & Terminate Cables	15	13-Jan-27	05-Feb-27		
Interior Buildout		188	02-Sep-26	21-May-27		
PH1 - Office		129	02-Sep-26	01-Mar-27		
PH1 - Office - Level 01		129	02-Sep-26	01-Mar-27		
PH1 - Office - L1 - Elevator and Stair 03 Tower		114	09-Sep-26	15-Feb-27		

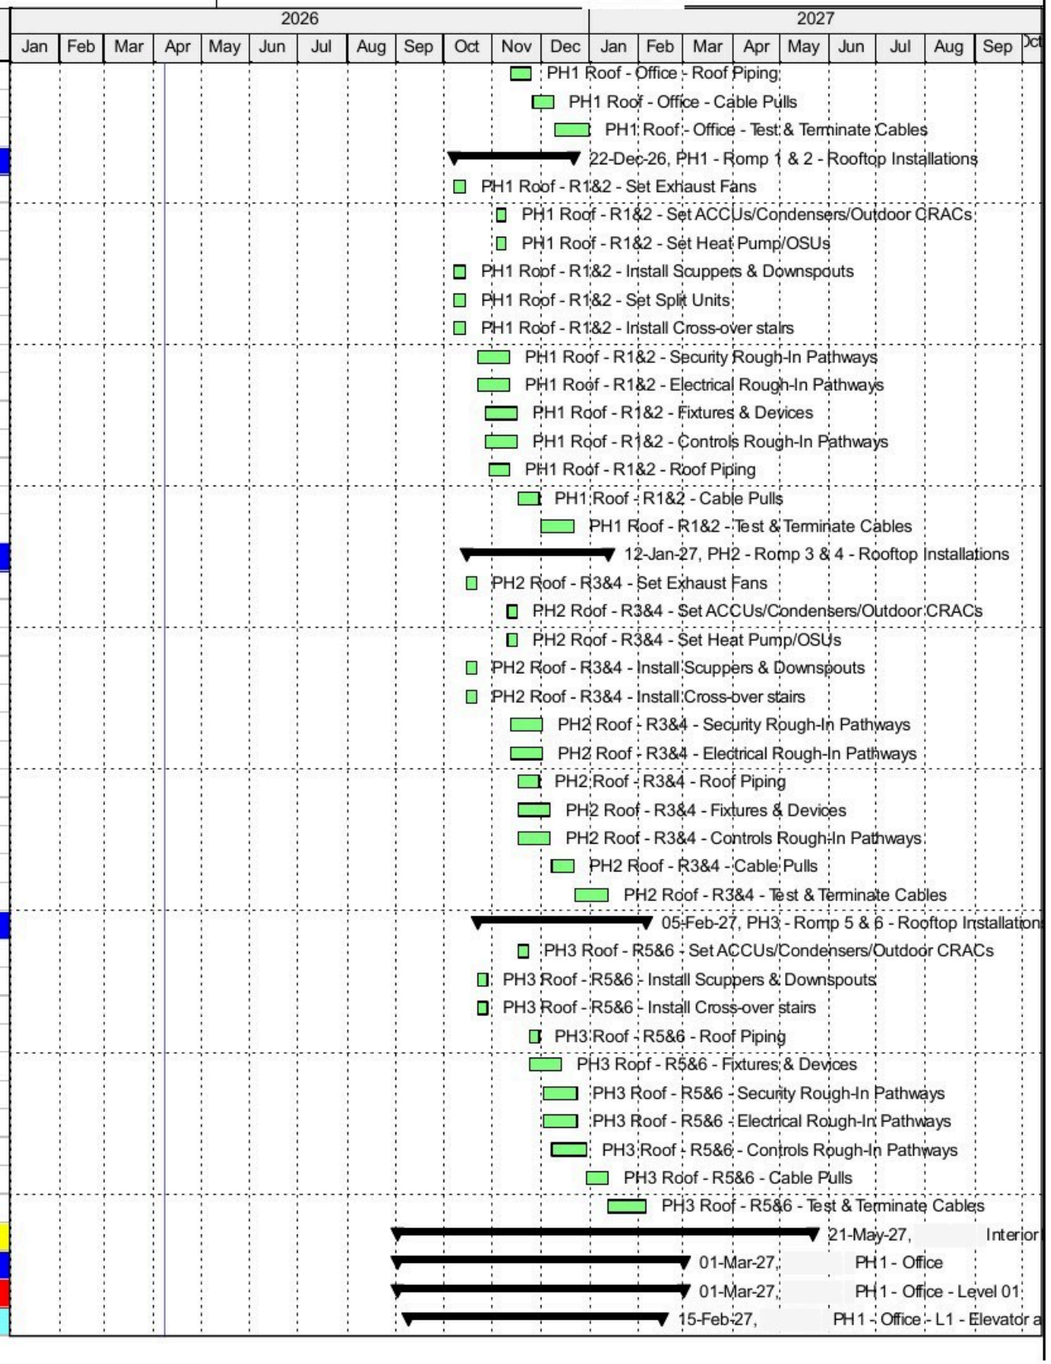


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Office.L1.ELVST.330	Office - L1 - ELV & ST03 Tower - Mechanical OH Rough-Ins	1	08-Oct-26	08-Oct-26	Trade	Mechanical
Office.L1.ELVST.530	Office - L1 - ELV & ST03 Tower - Mechanical Trim-out	2	29-Oct-26	30-Oct-26	Trade	Mechanical
Office.L1.ELVST.100	Office - L1 - ELV & ST03 Tower - Layout Walls	1	09-Sep-26	09-Sep-26		
Office.L1.ELVST.110	Office - L1 - ELV & ST03 Tower - Frame Walls	2	10-Sep-26	11-Sep-26		
Office.L1.ELVST.200	Office - L1 - ELV & ST03 Tower - Electrical/Fire Alarm In-Wall Rough-I	3	14-Sep-26	16-Sep-26		
Office.L1.ELVST.210	Office - L1 - ELV & ST03 Tower - Sec/Telecom In-Wall Rough-Ins	3	14-Sep-26	16-Sep-26		
Office.L1.ELVST.300	Office - L1 - ELV & ST03 Tower - Fire Sprinkler OH Rough-Ins	2	06-Oct-26	07-Oct-26		
Office.L1.ELVST.310	Office - L1 - ELV & ST03 Tower - Electrical/Fire Alarm OH Rough-Ins	3	08-Oct-26	12-Oct-26		
Office.L1.ELVST.320	Office - L1 - ELV & ST03 Tower - Sec/Telecom OH Rough-Ins	3	08-Oct-26	12-Oct-26		
Office.L1.ELVST.120	Office - L1 - ELV & ST03 Tower - One Side Drywall	2	12-Oct-26	13-Oct-26		
Office.L1.ELVST.390	Office - L1 - ELV & ST03 Tower - OH Inspections	1	13-Oct-26	13-Oct-26		
Office.L1.ELVST.130	Office - L1 - ELV & ST03 Tower - Hang Door Frames	1	14-Oct-26	14-Oct-26		
Office.L1.ELVST.290	Office - L1 - ELV & ST03 Tower - In-Wall Inspections	1	14-Oct-26	14-Oct-26		
Office.L1.ELVST.140	Office - L1 - ELV & ST03 Tower - Hang, Tape, & Finish Drywall	3	15-Oct-26	19-Oct-26		
Office.L1.ELVST.160	Office - L1 - ELV & ST03 Tower - Prime Paint	2	20-Oct-26	21-Oct-26		
Office.L1.ELVST.500	Office - L1 - ELV & ST03 Tower - Fire Sprinkler Trim-out	2	22-Oct-26	23-Oct-26		
Office.L1.ELVST.490	Office - L1 - ELV & ST03 Tower - Install Security Devices (By Others)	5	22-Oct-26	28-Oct-26		
Office.L1.ELVST.410	Office - L1 - ELV & ST03 Tower - Pull & Terminate Wires	5	22-Oct-26	28-Oct-26		
Office.L1.ELVST.580	Office - L1 - ELV & ST03 Tower - Install Lighting	2	22-Oct-26	23-Oct-26		
Office.L1.ELVST.400	Office - L1 - ELV & ST03 Tower - Install Doors & Hardware	1	29-Oct-26	29-Oct-26		
Office.L1.ELVST.510	Office - L1 - ELV & ST03 Tower - Electrical Trim-out	2	29-Oct-26	30-Oct-26		
Office.L1.ELVST.520	Office - L1 - ELV & ST03 Tower - Fire Alarm Trim-out	2	29-Oct-26	30-Oct-26		
Office.L1.ELVST.590	Office - L1 - ELV & ST03 Tower - Security Trim-out (By Others)	5	29-Oct-26	04-Nov-26		
Office.L1.ELVST.600	Office - L1 - ELV & ST03 Tower - Final Paint	5	05-Nov-26	11-Nov-26		
Office.L1.ELVST.610	Office - L1 - ELV & ST03 Tower - Install Signage	2	12-Nov-26	13-Nov-26		
Office.L1.ELVST.680	Office - L1 - ELV & ST03 Tower - Punchlist	5	16-Nov-26	20-Nov-26		
Office.L1.ELVST.690	Office - L1 - ELV & ST03 Tower - Final Clean	5	23-Nov-26	27-Nov-26		
PH1 - Office - L1 - Elevator Equipment and Commissioning		46	10-Nov-26	12-Jan-27		
Office.ELV.100	Office - Elevator - Pre-Installation Readiness Inspection	1	10-Nov-26	10-Nov-26		
Office.ELV.110	Office - Elevator - Elevator Pit Sump	2	10-Nov-26	11-Nov-26		
Office.ELV.120	Office - Elevator - Elevator Pit Electrical/Sec Rough-In	4	12-Nov-26	17-Nov-26		
Office.ELV.130	Office - Elevator - Elevator Pit Misc Install	3	12-Nov-26	16-Nov-26		
Office.ELV.140	Office - Elevator - Guide Rail and Shaft Installation	5	18-Nov-26	24-Nov-26		
Office.ELV.150	Office - Elevator - Entrance Installation	5	20-Nov-26	26-Nov-26		
Office.ELV.160	Office - Elevator - Hydraulic System Install	9	25-Nov-26	07-Dec-26		
Office.ELV.170	Office - Elevator - Car Frame & Platform Install	5	08-Dec-26	14-Dec-26		
Office.ELV.180	Office - Elevator - Elevator Room Equip Install (M1)	15	08-Dec-26	29-Dec-26		
Office.ELV.190	Office - Elevator - Car enclosure & Interior Fit-Out	5	15-Dec-26	22-Dec-26		
Office.ELV.200	Office - Elevator - Electrical & Control System Install	10	23-Dec-26	05-Jan-27		
Office.ELV.220	Office - Elevator - Trim out	10	30-Dec-26	12-Jan-27		
Office.ELV.210	Office - Elevator - Security & Comms System Install	5	06-Jan-27	12-Jan-27		
PH1 - Office - L1 - Elevator Equipment		15	26-Jan-27	15-Feb-27		
Cx.Office.ELV.100	Office - Elevator Commissioning	15	26-Jan-27	15-Feb-27		
PH1 - Office - L1 - Stairs 01 & 02		54	09-Sep-26	23-Nov-26		
Office.L1.STR.330	Office - L1 - ST01&02 - Mechanical OH Rough-Ins	1	11-Sep-26	11-Sep-26	Trade	Mechanical

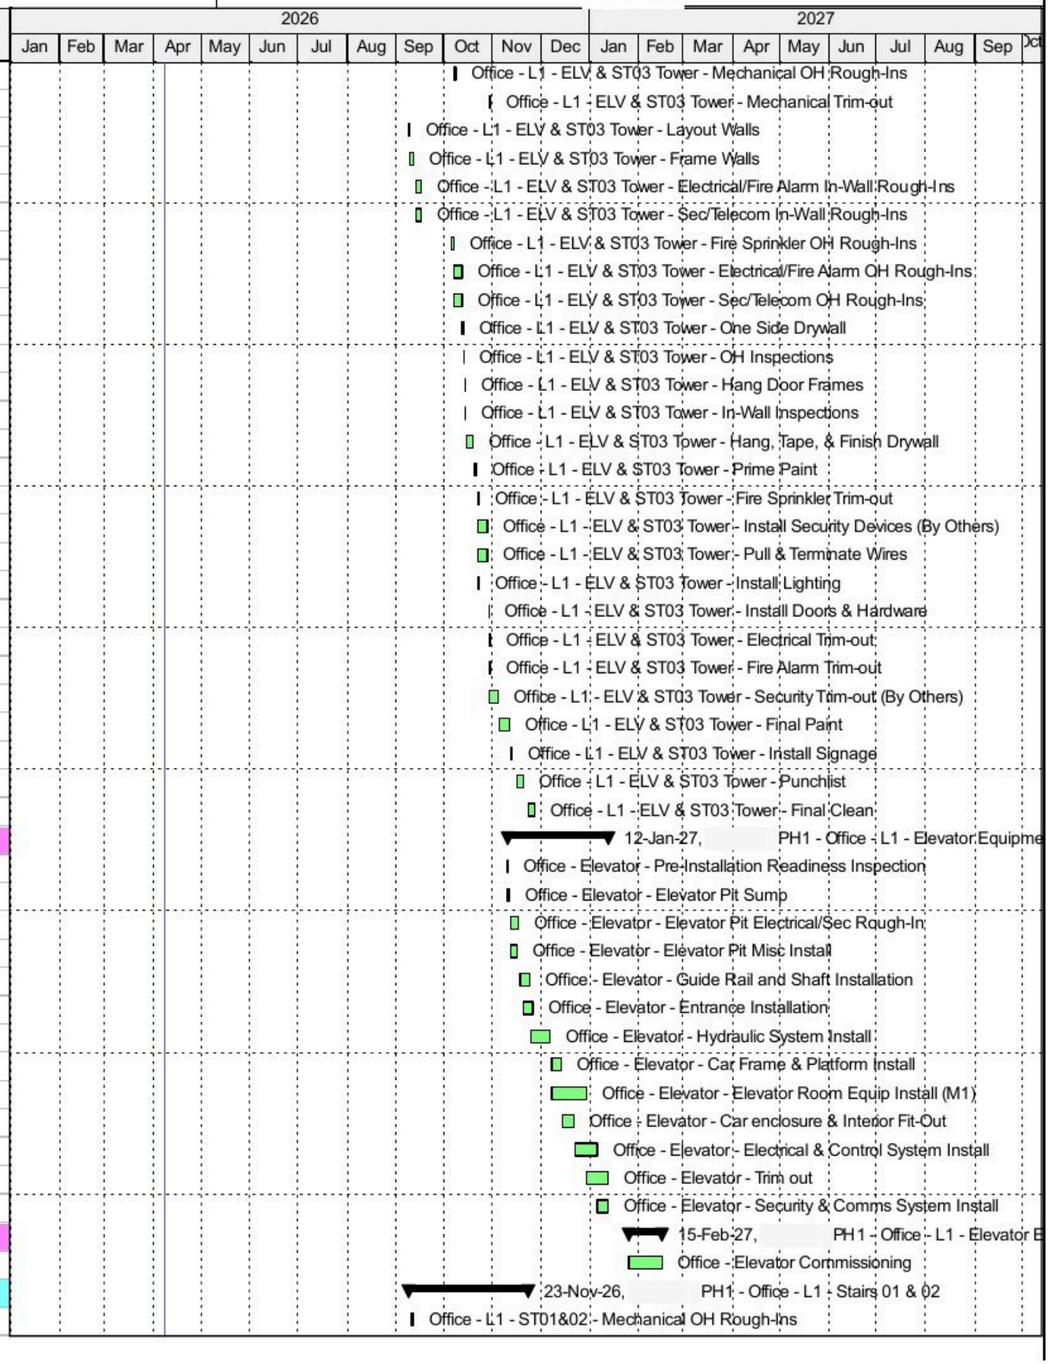

Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Office.L1.STR.530	Office - L1 - ST01&02 - Mechanical Trim-out	2	20-Oct-26	21-Oct-26	Trade	Mechanical
Office.L1.STR.300	Office - L1 - ST01&02 - Fire Sprinkler OH Rough-Ins	2	09-Sep-26	10-Sep-26		
Office.L1.STR.100	Office - L1 - ST01&02 - Layout Walls	1	09-Sep-26	09-Sep-26		
Office.L1.STR.110	Office - L1 - ST01&02 - Frame Walls	2	10-Sep-26	11-Sep-26		
Office.L1.STR.310	Office - L1 - ST01&02 - Electrical/Fire Alarm OH Rough-Ins	3	11-Sep-26	15-Sep-26		
Office.L1.STR.320	Office - L1 - ST01&02 - Sec/Telecom OH Rough-Ins	3	11-Sep-26	15-Sep-26		
Office.L1.STR.200	Office - L1 - ST01&02 - Electrical/Fire Alarm In-Wall Rough-Ins	3	14-Sep-26	16-Sep-26		
Office.L1.STR.210	Office - L1 - ST01&02 - Sec/Telecom In-Wall Rough-Ins	3	14-Sep-26	16-Sep-26		
Office.L1.STR.390	Office - L1 - ST01&02 - OH Inspections	1	16-Sep-26	16-Sep-26		
Office.L1.STR.120	Office - L1 - ST01&02 - One Side Drywall	2	01-Oct-26	02-Oct-26		
Office.L1.STR.130	Office - L1 - ST01&02 - Hang Door Frames	1	05-Oct-26	05-Oct-26		
Office.L1.STR.290	Office - L1 - ST01&02 - In-Wall Inspections	1	05-Oct-26	05-Oct-26		
Office.L1.STR.140	Office - L1 - ST01&02 - Hang, Tape, & Finish Drywall	3	06-Oct-26	08-Oct-26		
Office.L1.STR.160	Office - L1 - ST01&02 - Prime Paint	2	09-Oct-26	12-Oct-26		
Office.L1.STR.500	Office - L1 - ST01&02 - Fire Sprinkler Trim-out	2	13-Oct-26	14-Oct-26		
Office.L1.STR.490	Office - L1 - ST01&02 - Install Security Devices (By Others)	5	13-Oct-26	19-Oct-26		
Office.L1.STR.410	Office - L1 - ST01&02 - Pull & Terminate Wires	5	13-Oct-26	19-Oct-26		
Office.L1.STR.580	Office - L1 - ST01&02 - Install Lighting	2	13-Oct-26	14-Oct-26		
Office.L1.STR.510	Office - L1 - ST01&02 - Electrical Trim-out	2	20-Oct-26	21-Oct-26		
Office.L1.STR.520	Office - L1 - ST01&02 - Fire Alarm Trim-out	2	20-Oct-26	21-Oct-26		
Office.L1.STR.590	Office - L1 - ST01&02 - Security Trim-out (By Others)	5	20-Oct-26	26-Oct-26		
Office.L1.STR.400	Office - L1 - ST01&02 - Install Doors & Hardware	1	29-Oct-26	29-Oct-26		
Office.L1.STR.600	Office - L1 - ST01&02 - Final Paint	5	30-Oct-26	05-Nov-26		
Office.L1.STR.610	Office - L1 - ST01&02 - Install Signage	2	06-Nov-26	09-Nov-26		
Office.L1.STR.680	Office - L1 - ST01&02 - Punchlist	5	10-Nov-26	16-Nov-26		
Office.L1.STR.690	Office - L1 - ST01&02 - Final Clean	5	17-Nov-26	23-Nov-26		
PH1 - Office - L1 - Mechanical Room		113	16-Sep-26	19-Feb-27		
Office.L1.Mech.400	Office - MR - Mechanical OH Rough-ins	10	23-Sep-26	07-Oct-26	Trade	Mechanical
Office.L1.Mech.410	Office - MR - Mechanical Trim-out	5	23-Oct-26	29-Oct-26	Trade	Mechanical
Office.L1.Mech.100	Office - MR - Layout and Frame Walls	5	16-Sep-26	22-Sep-26		
Office.L1.Mech.110	Office - MR - Fire Sprinkler OH Rough-ins	5	16-Sep-26	22-Sep-26		
Office.L1.Mech.210	Office - MR - One Side Drywall	5	23-Sep-26	30-Sep-26		
Office.L1.Mech.360	Office - MR - Plumbing In-Wall Rough-ins	2	23-Sep-26	24-Sep-26		
Office.L1.Mech.370	Office - MR - Electrical In-Wall Rough-ins	4	23-Sep-26	29-Sep-26		
Office.L1.Mech.380	Office - MR - Mechanical In-Wall Rough-ins	2	23-Sep-26	24-Sep-26		
Office.L1.Mech.440	Office - MR - Hang Door Frames	5	23-Sep-26	30-Sep-26		
Office.L1.Mech.190	Office - MR - In-Wall Inspections	1	30-Sep-26	30-Sep-26		
Office.L1.Mech.130	Office - MR - Hang, Tape, & Finish Drywall	5	08-Oct-26	14-Oct-26		
Office.L1.Mech.390	Office - MR - Electrical OH Rough-ins	5	08-Oct-26	14-Oct-26		
Office.L1.Mech.140	Office - MR - Prime Paint	5	12-Oct-26	16-Oct-26		
Office.L1.Mech.200	Office - MR - OH Inspections	1	15-Oct-26	15-Oct-26		
Office.L1.Mech.160	Office - MR - Install Ceiling Grid & Tiles	5	16-Oct-26	22-Oct-26		
Office.L1.Mech.220	Office - MR - Install Security Devices (By Others)	5	23-Oct-26	29-Oct-26		
Office.L1.Mech.180	Office - MR - Electrical Trim-out	5	23-Oct-26	29-Oct-26		
Office.L1.Mech.170	Office - MR - Install Doors & Hardware	5	29-Oct-26	04-Nov-26		

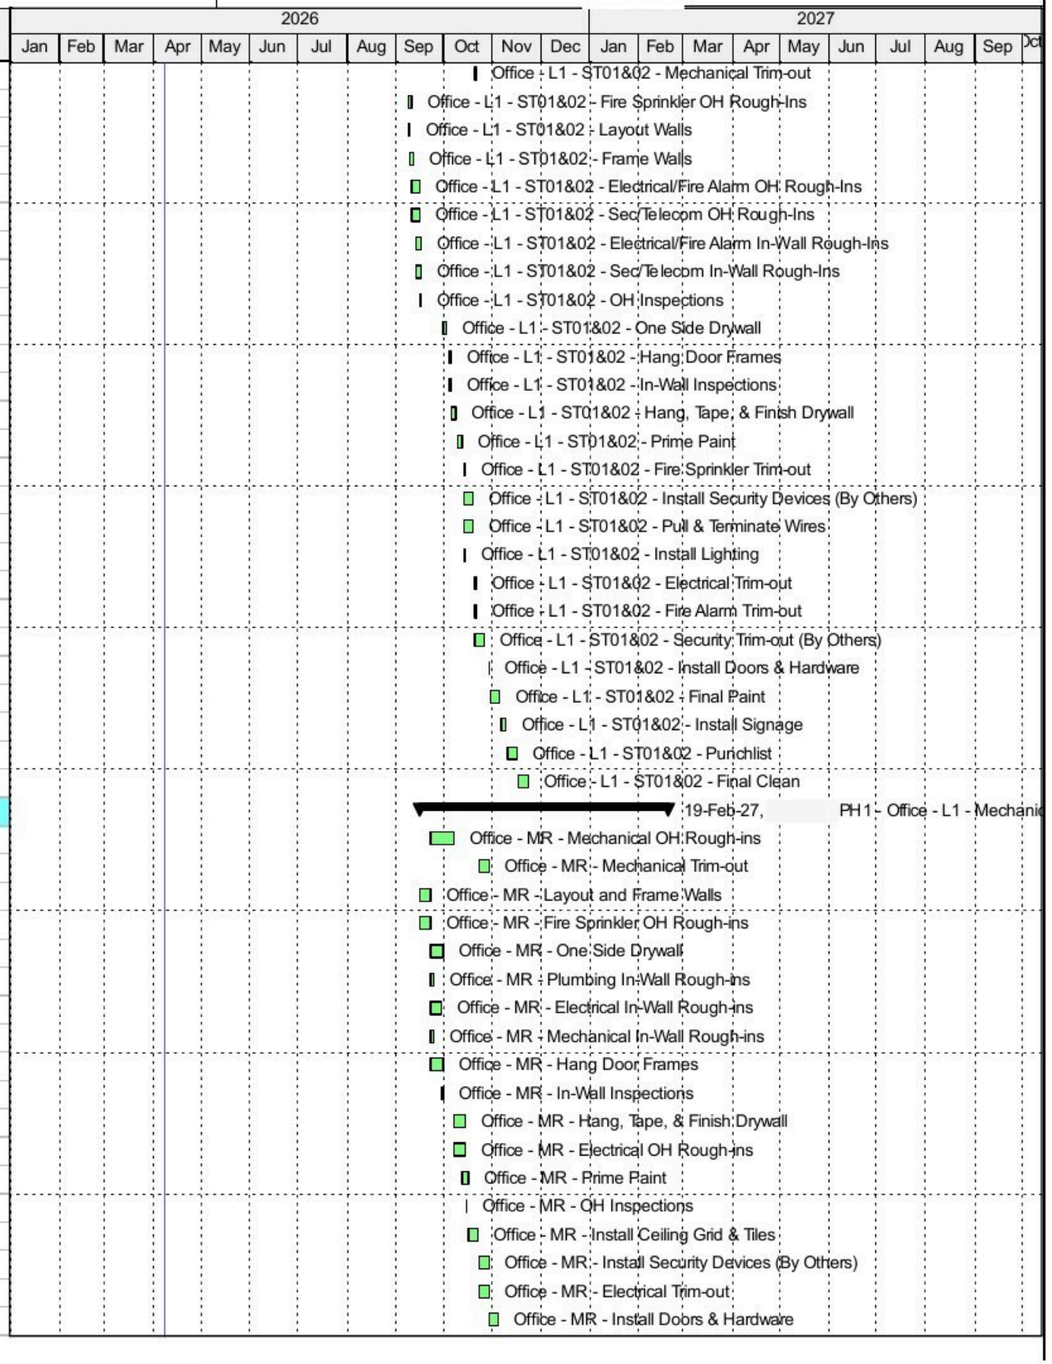

Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule


Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Office.L1.Mech.420	Office - MR - Punch	5	05-Nov-26	11-Nov-26		
Office.L1.Mech.430	Office - MR - Final Clean	5	12-Nov-26	18-Nov-26		
PH1 - Office - L1 - Mech Room Equipment		57	19-Oct-26	05-Jan-27		
Office.L1.MechRM.100	Office - MR - Install Expansion Tank (IW-XT)	10	19-Oct-26	30-Oct-26		
Office.L1.MechRM.110	Office - MR - Install Industrial Water Panels (IWP's)	5	19-Oct-26	23-Oct-26		
Office.L1.MechRM.120	Office - MR - Install OX Skid	10	23-Dec-26	05-Jan-27		
Office.L1.MechRM.130	Office - MR - Install IW Pump Skid	5	23-Dec-26	29-Dec-26		
PH1 - Office - L1 - Mech Room Commissioning		33	06-Jan-27	19-Feb-27		
Cx.Office.Mech.100	L2 Commissioning - Office Mech RM	10	06-Jan-27	21-Jan-27		
Cx.Office.Mech.110	Energize Equipment - Office Mech RM	5	25-Jan-27	29-Jan-27		
Cx.Office.Mech.120	L3 Commissioning - Office Mech RM	15	01-Feb-27	19-Feb-27		
PH1 - Office - L1 - Sprinkler Room		69	23-Sep-26	28-Dec-26		
Office.L1.SR.400	Office - SR - Mechanical OH Rough-ins	5	08-Oct-26	14-Oct-26	Trade	Mechanical
Office.L1.SR.410	Office - SR - Mechanical Trim-out	5	23-Nov-26	27-Nov-26	Trade	Mechanical
Office.L1.SR.100	Office - SR - Frame Walls	5	23-Sep-26	30-Sep-26		
Office.L1.SR.110	Office - SR - Fire Sprinkler OH Rough-ins	10	23-Sep-26	07-Oct-26		
Office.L1.SR.210	Office - SR - One-Side Drywall	5	01-Oct-26	07-Oct-26		
Office.L1.SR.360	Office - SR - Plumbing In-wall Rough-ins	4	01-Oct-26	06-Oct-26		
Office.L1.SR.370	Office - SR - Electrical In-wall Rough-ins	4	01-Oct-26	06-Oct-26		
Office.L1.SR.380	Office - SR - Mechanical In-wall Rough-ins	2	01-Oct-26	02-Oct-26		
Office.L1.SR.440	Office - SR - Hang Door Frames	5	01-Oct-26	07-Oct-26		
Office.L1.SR.190	Office - SR - In-wall Inspections	1	07-Oct-26	07-Oct-26		
Office.L1.SR.130	Office - SR - Hang, Tape, & Finish Drywall	5	15-Oct-26	21-Oct-26		
Office.L1.SR.390	Office - SR - Electrical OH Rough-ins	5	15-Oct-26	21-Oct-26		
Office.L1.SR.140	Office - SR - Prime Paint	5	19-Oct-26	23-Oct-26		
Office.L1.SR.200	Office - SR - OH Inspections	1	22-Oct-26	22-Oct-26		
Office.L1.SR.150	Office - SR - MEPF Connections	5	09-Nov-26	13-Nov-26		
Office.L1.SR.160	Office - SR - Install Ceiling Grid & Tiles	5	16-Nov-26	20-Nov-26		
Office.L1.SR.180	Office - SR - Install Doors & Hardware	5	23-Nov-26	27-Nov-26		
Office.L1.SR.220	Office - SR - Install Security Devices (By Others)	5	23-Nov-26	27-Nov-26		
Office.L1.SR.120	Office - SR - Electrical Trim-out	5	23-Nov-26	27-Nov-26		
Office.L1.SR.420	Office - SR - Punch	5	30-Nov-26	04-Dec-26		
Office.L1.SR.430	Office - SR - Final Clean	5	07-Dec-26	11-Dec-26		
PH1 - Office - L1 - Sprinkler Room Equipment		10	26-Oct-26	06-Nov-26		
Office.L1.Sprinkler.100	Office - SR - Install FACP	5	26-Oct-26	30-Oct-26		
Office.L1.Sprinkler.110	Office - SR - Install Sprinkler System	10	26-Oct-26	06-Nov-26		
PH1 - Office - L1 - Sprinkler Room Commissioning		31	16-Nov-26	28-Dec-26		
Cx.Office.SR.100	L2 Commissioning - Office Sprinkler Room	10	16-Nov-26	27-Nov-26		
Cx.Office.SR.110	Energize Equipment - Office Sprinkler Room	5	30-Nov-26	04-Dec-26		
Cx.Office.SR.120	L3 Commissioning - Office Sprinkler Room	15	07-Dec-26	28-Dec-26		
PH1 - Office - L1 - Electrical Closet		128	02-Sep-26	26-Feb-27		
Office.L1.EC.510	Office - EC - Mechanical OH Rough-ins	5	02-Sep-26	08-Sep-26	Trade	Mechanical
Office.L1.EC.520	Office - EC - Mechanical Trim-out	5	03-Dec-26	09-Dec-26	Trade	Mechanical
Office.L1.EC.150	Office - EC - Layout & Frame Walls	5	02-Sep-26	08-Sep-26		
Office.L1.EC.160	Office - EC - Fire Sprinkler OH Rough-ins	4	02-Sep-26	07-Sep-26		




Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Office.L1.EC.270	Office - EC - One Side Drywall	5	09-Sep-26	15-Sep-26		
Office.L1.EC.470	Office - EC - Plumbing In-wall Rough-ins	2	09-Sep-26	10-Sep-26		
Office.L1.EC.480	Office - EC - Electrical In-wall Rough-ins	4	09-Sep-26	14-Sep-26		
Office.L1.EC.490	Office - EC - Mechanical In-wall Rough-ins	2	09-Sep-26	10-Sep-26		
Office.L1.EC.550	Office - EC - Hang Door Frames	5	09-Sep-26	15-Sep-26		
Office.L1.EC.500	Office - EC - Electrical OH Rough-ins	10	14-Sep-26	25-Sep-26		
Office.L1.EC.250	Office - EC - In-Wall Inspection	1	15-Sep-26	15-Sep-26		
Office.L1.EC.180	Office - EC - Hang, Tape, & Finish Drywall	5	16-Sep-26	22-Sep-26		
Office.L1.EC.190	Office - EC - Prime Paint	5	18-Sep-26	24-Sep-26		
Office.L1.EC.260	Office - EC - OH Inspection	1	29-Sep-26	29-Sep-26		
Office.L1.EC.220	Office - EC - Install Ceiling Grid & Tiles	5	12-Nov-26	18-Nov-26		
Office.L1.EC.200	Office - EC - Install Cable Tray	5	19-Nov-26	25-Nov-26		
Office.L1.EC.210	Office - EC - Pull & Terminate Wires	5	26-Nov-26	02-Dec-26		
Office.L1.EC.240	Office - EC - Install Doors & Hardware	5	03-Dec-26	09-Dec-26		
Office.L1.EC.280	Office - EC - Install Security Devices (By Others)	5	03-Dec-26	09-Dec-26		
Office.L1.EC.170	Office - EC - Electrical Trim-out	5	03-Dec-26	09-Dec-26		
Office.L1.EC.530	Office - EC - Punch	5	10-Dec-26	16-Dec-26		
Office.L1.EC.540	Office - EC - Final Clean	5	18-Dec-26	24-Dec-26		
PH1 - Office - L1 - Electrical Closet Equipment		34	25-Sep-26	11-Nov-26		
Office.L1.EC.130	Office - EC - Install HGP Panels	5	25-Sep-26	02-Oct-26		
Office.L1.EC.100	Office - EC - Install OPP-XFMR's (OFCI)	5	05-Nov-26	11-Nov-26		
Office.L1.EC.110	Office - EC - Install OUPP, OLP, & OMP Panels (OFCI)	5	05-Nov-26	11-Nov-26		
Office.L1.EC.120	Office - EC - Install SLP Panel (OFCI)	5	05-Nov-26	11-Nov-26		
PH1 - Office - L1 - Electrical Closet Commissioning		62	03-Dec-26	26-Feb-27		
PH1 - Office - Electrical Closet OPP-01, 02, 03, 04, 06, 07 Cx		36	18-Dec-26	05-Feb-27		
Cx.Off.EC-OPP.100	Office Electrical Closet - OPP's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.Off.EC-OPP.110	Office Electrical Closet - OPP's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.Off.EC-OPP.120	Office Electrical Closet - OPP's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.Off.EC-OPP.130	Office Electrical Closet - OPP's - Installation Verification Checklist	1	28-Dec-26	28-Dec-26		
Cx.Off.EC-OPP.140	Office Electrical Closet - OPP's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.Off.EC-OPP.150	Office Electrical Closet - OPP's - Energize Equipment	1	27-Jan-27	27-Jan-27		
Cx.Off.EC-OPP.160	Office Electrical Closet - OPP's - L3 Startup	4	28-Jan-27	02-Feb-27		
Cx.Off.EC-OPP.170	Office Electrical Closet - OPP's - EPMS SAT	1	03-Feb-27	03-Feb-27		
Cx.Off.EC-OPP.180	Office Electrical Closet - OPP's - Thermographic Checks	1	04-Feb-27	04-Feb-27		
Cx.Off.EC-OPP.190	Office Electrical Closet - OPP's - Green Tag	1	05-Feb-27	05-Feb-27		
PH1 - Office - Electrical Closet OPP-XFMR-01 & OPP-XFMR-06 Cx		35	18-Dec-26	04-Feb-27		
Cx.Off.EC-OPP-XFMR.100	Office Electrical Closet - OPP-XFMR's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.Off.EC-OPP-XFMR.110	Office Electrical Closet - OPP-XFMR's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.Off.EC-OPP-XFMR.120	Office Electrical Closet - OPP-XFMR's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.Off.EC-OPP-XFMR.130	Office Electrical Closet - OPP-XFMR's - Installation Verification Check	1	28-Dec-26	28-Dec-26		
Cx.Off.EC-OPP-XFMR.140	Office Electrical Closet - OPP-XFMR's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.Off.EC-OPP-XFMR.150	Office Electrical Closet - OPP-XFMR's - Energize Equipment	1	26-Jan-27	26-Jan-27		
Cx.Off.EC-OPP-XFMR.160	Office Electrical Closet - OPP-XFMR's - L3 Startup	4	27-Jan-27	01-Feb-27		
Cx.Off.EC-OPP-XFMR.170	Office Electrical Closet - OPP-XFMR's - EPMS SAT	1	02-Feb-27	02-Feb-27		
Cx.Off.EC-OPP-XFMR.180	Office Electrical Closet - OPP-XFMR's - Thermographic Checks	1	03-Feb-27	03-Feb-27		

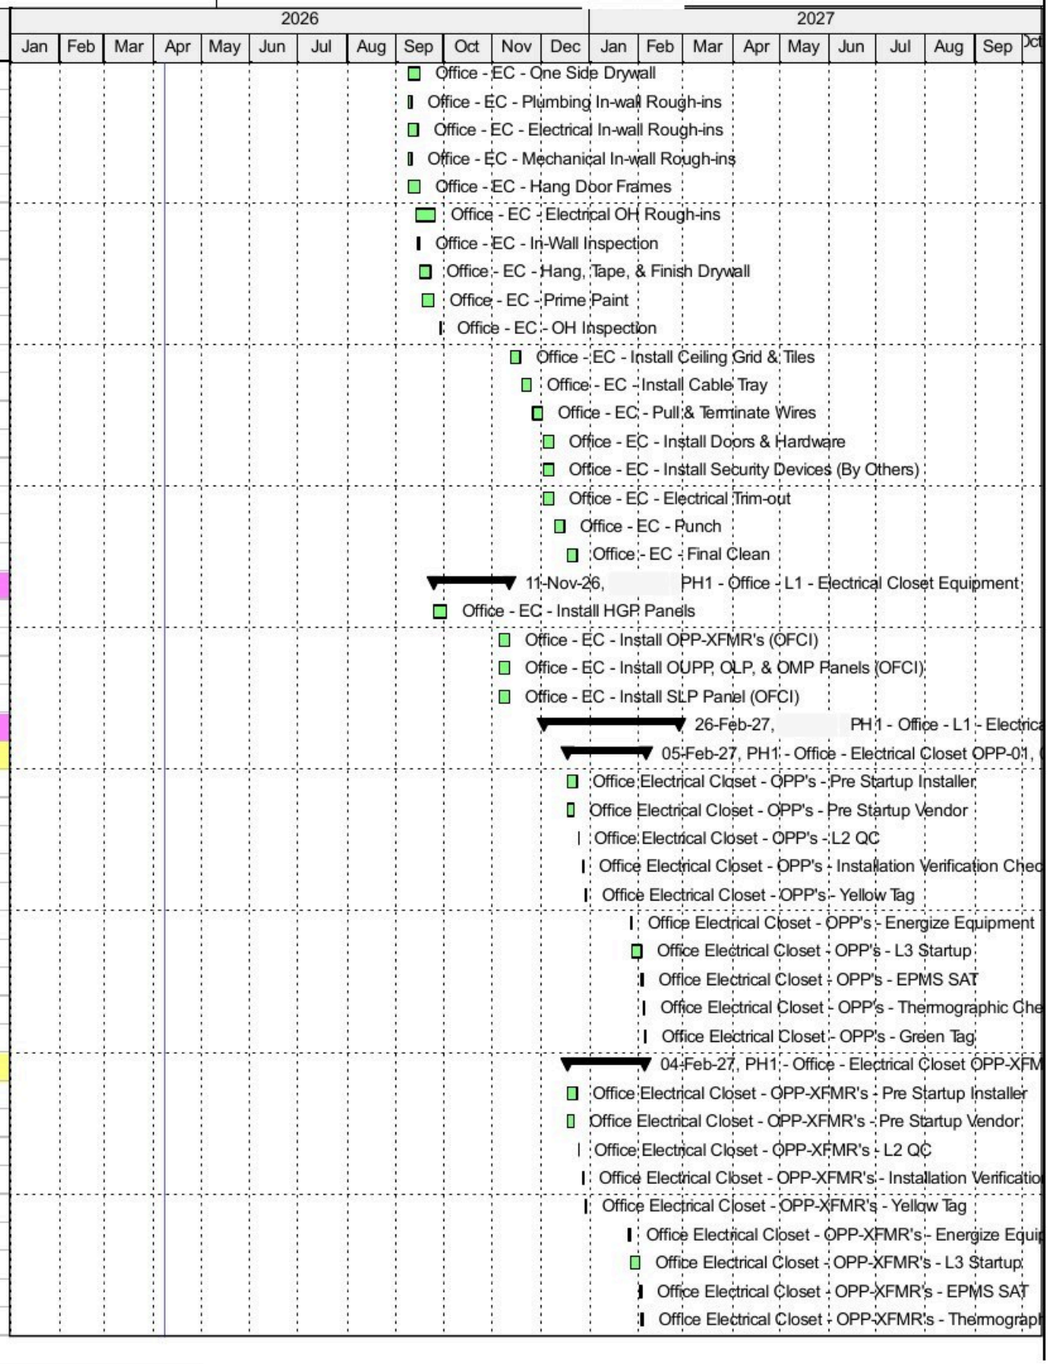

Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.Off.EC-OPP-XFMR.190	Office Electrical Closet - OPP-XFMR's - Green Tag	1	04-Feb-27	04-Feb-27		
PH1 - Office - Electrical Closet OLP-01 & OLP-02 Cx		51	18-Dec-26	26-Feb-27		
Cx.Off.EC-OLP.100	Office Electrical Closet - OLP's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.Off.EC-OLP.110	Office Electrical Closet - OLP's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.Off.EC-OLP.120	Office Electrical Closet - OLP's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.Off.EC-OLP.130	Office Electrical Closet - OLP's - Installation Verification Checklist	1	28-Dec-26	28-Dec-26		
Cx.Off.EC-OLP.140	Office Electrical Closet - OLP's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.Off.EC-OLP.150	Office Electrical Closet - OLP's - Energize Equipment	1	17-Feb-27	17-Feb-27		
Cx.Off.EC-OLP.160	Office Electrical Closet - OLP's - L3 Startup	4	18-Feb-27	23-Feb-27		
Cx.Off.EC-OLP.170	Office Electrical Closet - OLP's - EPMS SAT	1	24-Feb-27	24-Feb-27		
Cx.Off.EC-OLP.180	Office Electrical Closet - OLP's - Thermographic Checks	1	25-Feb-27	25-Feb-27		
Cx.Off.EC-OLP.190	Office Electrical Closet - OLP's - Green Tag	1	26-Feb-27	26-Feb-27		
PH1 - Office - Electrical Closet SLP Cx		59	03-Dec-26	23-Feb-27		
Cx.Off.EC-SLP.100	Office Electrical Closet - SLP - Pre Startup Installer	5	03-Dec-26	09-Dec-26		
Cx.Off.EC-SLP.110	Office Electrical Closet - SLP - Pre Startup Vendor	3	03-Dec-26	07-Dec-26		
Cx.Off.EC-SLP.120	Office Electrical Closet - SLP - L2 QC	1	10-Dec-26	10-Dec-26		
Cx.Off.EC-SLP.130	Office Electrical Closet - SLP - Installation Verification Checklist	1	11-Dec-26	11-Dec-26		
Cx.Off.EC-SLP.140	Office Electrical Closet - SLP - Yellow Tag	1	14-Dec-26	14-Dec-26		
Cx.Off.EC-SLP.150	Office Electrical Closet - SLP - Energize Equipment	1	17-Feb-27	17-Feb-27		
Cx.Off.EC-SLP.160	Office Electrical Closet - SLP - L3 Startup	1	18-Feb-27	18-Feb-27		
Cx.Off.EC-SLP.170	Office Electrical Closet - SLP - EPMS SAT	1	19-Feb-27	19-Feb-27		
Cx.Off.EC-SLP.180	Office Electrical Closet - SLP - Thermographic Checks	1	22-Feb-27	22-Feb-27		
Cx.Off.EC-SLP.190	Office Electrical Closet - SLP - Green Tag	1	23-Feb-27	23-Feb-27		
PH1 - Office - Electrical Closet OMP-01 & OMP-02 Cx		62	03-Dec-26	26-Feb-27		
Cx.Off.EC-OMP.100	Office Electrical Closet - OMP's - Pre Startup Installer	5	03-Dec-26	09-Dec-26		
Cx.Off.EC-OMP.110	Office Electrical Closet - OMP's - Pre Startup Vendor	3	03-Dec-26	07-Dec-26		
Cx.Off.EC-OMP.120	Office Electrical Closet - OMP's - L2 QC	1	10-Dec-26	10-Dec-26		
Cx.Off.EC-OMP.130	Office Electrical Closet - OMP's - Installation Verification Checklist	1	11-Dec-26	11-Dec-26		
Cx.Off.EC-OMP.140	Office Electrical Closet - OMP's - Yellow Tag	1	14-Dec-26	14-Dec-26		
Cx.Off.EC-OMP.150	Office Electrical Closet - OMP's - Energize Equipment	1	17-Feb-27	17-Feb-27		
Cx.Off.EC-OMP.160	Office Electrical Closet - OMP's - L3 Startup	4	18-Feb-27	23-Feb-27		
Cx.Off.EC-OMP.170	Office Electrical Closet - OMP's - EPMS SAT	1	24-Feb-27	24-Feb-27		
Cx.Off.EC-OMP.180	Office Electrical Closet - OMP's - Thermographic Checks	1	25-Feb-27	25-Feb-27		
Cx.Off.EC-OMP.190	Office Electrical Closet - OMP's - Green Tag	1	26-Feb-27	26-Feb-27		
PH1 - Office - Electrical Closet OUPP-01 & OUPP-02 Cx		59	03-Dec-26	23-Feb-27		
Cx.Off.EC-OUPP.100	Office Electrical Closet - OUPP's - Pre Startup Installer	5	03-Dec-26	09-Dec-26		
Cx.Off.EC-OUPP.110	Office Electrical Closet - OUPP's - Pre Startup Vendor	5	03-Dec-26	09-Dec-26		
Cx.Off.EC-OUPP.120	Office Electrical Closet - OUPP's - L2 QC	5	10-Dec-26	16-Dec-26		
Cx.Off.EC-OUPP.130	Office Electrical Closet - OUPP's - Installation Verification Checklist	5	18-Dec-26	24-Dec-26		
Cx.Off.EC-OUPP.140	Office Electrical Closet - OUPP's - Yellow Tag	5	25-Dec-26	31-Dec-26		
Cx.Off.EC-OUPP.150	Office Electrical Closet - OUPP's - Energize Equipment	1	17-Feb-27	17-Feb-27		
Cx.Off.EC-OUPP.160	Office Electrical Closet - OUPP's - L3 Startup	1	18-Feb-27	18-Feb-27		
Cx.Off.EC-OUPP.170	Office Electrical Closet - OUPP's - EPMS SAT	1	19-Feb-27	19-Feb-27		
Cx.Off.EC-OUPP.180	Office Electrical Closet - OUPP's - Thermographic Checks	1	22-Feb-27	22-Feb-27		
Cx.Off.EC-OUPP.190	Office Electrical Closet - OUPP's - Green Tag	1	23-Feb-27	23-Feb-27		

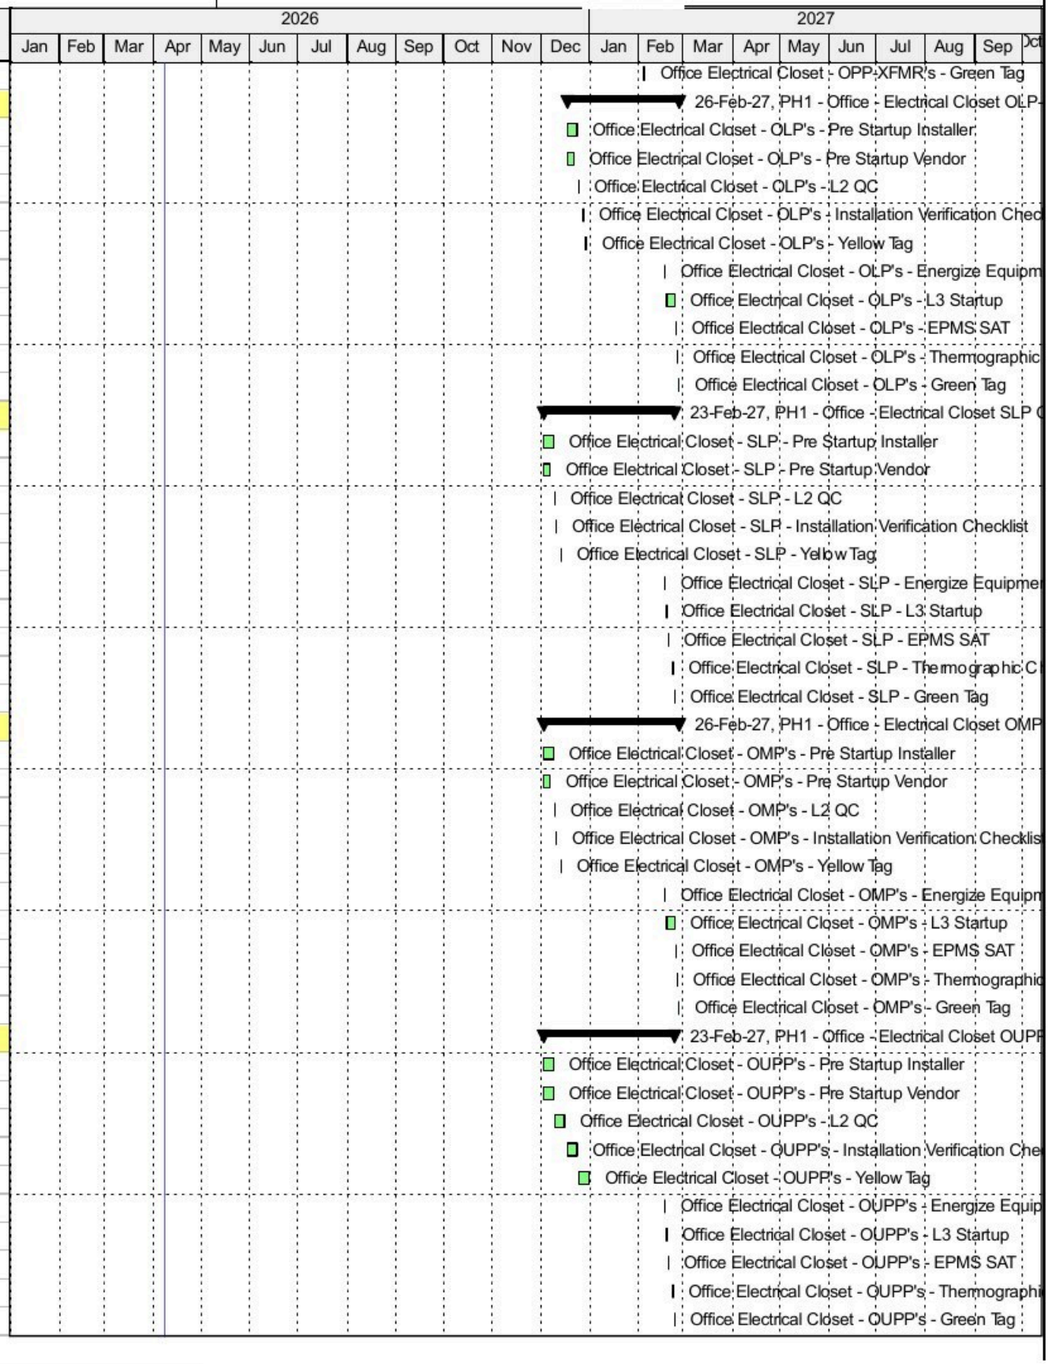


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH1 - Office - L1 - FER Rooms		94	23-Sep-26	01-Feb-27		
Office.L1.FER.460	Office - FER - Mechanical OH Rough-ins	5	30-Sep-26	06-Oct-26	Trade	Mechanical
Office.L1.FER.470	Office - FER - Mechanical Trim-out	5	24-Dec-26	30-Dec-26	Trade	Mechanical
Office.L1.FER.100	Office - FER - Layout & Frame Walls	5	23-Sep-26	30-Sep-26		
Office.L1.FER.110	Office - FER - Fire Sprinkler OH Rough-ins	4	23-Sep-26	29-Sep-26		
Office.L1.FER.240	Office - FER - One Side Drywall	5	01-Oct-26	07-Oct-26		
Office.L1.FER.420	Office - FER - Plumbing In-Wall Rough-ins	2	01-Oct-26	02-Oct-26		
Office.L1.FER.430	Office - FER - Electrical In-Wall Rough-ins	5	01-Oct-26	07-Oct-26		
Office.L1.FER.440	Office - FER - Mechancial In-Wall Rough-ins	2	01-Oct-26	02-Oct-26		
Office.L1.FER.480	Office - FER - Hang Door Frames	5	01-Oct-26	07-Oct-26		
Office.L1.FER.450	Office - FER - Electrical OH Rough-ins	5	07-Oct-26	13-Oct-26		
Office.L1.FER.220	Office - FER - In-Wall Inspection	1	08-Oct-26	08-Oct-26		
Office.L1.FER.130	Office - FER - Hang, Tape, & Finish Drywall	10	09-Oct-26	22-Oct-26		
Office.L1.FER.230	Office - FER - OH Inspection	1	14-Oct-26	14-Oct-26		
Office.L1.FER.200	Office - FER - Install Plywood	3	23-Oct-26	27-Oct-26		
Office.L1.FER.140	Office - FER - Prime Paint	5	28-Oct-26	03-Nov-26		
Office.L1.FER.180	Office - FER - Install Ceiling System	5	04-Nov-26	10-Nov-26		
Office.L1.FER.150	Office - FER - Install Cable Tray	10	11-Nov-26	24-Nov-26		
Office.L1.FER.160	Office - FER - Pull & Terminate Wires	15	25-Nov-26	15-Dec-26		
Office.L1.FER.170	Office - FER - Install Doors & Hardware	5	16-Dec-26	23-Dec-26		
Office.L1.FER.250	Office - FER - Install Security Devices (By Others)	5	24-Dec-26	30-Dec-26		
Office.L1.FER.120	Office - FER - Electrical Trim-out	5	24-Dec-26	30-Dec-26		
Office.L1.FER.210	Office - FER - Electrical Build-out	20	31-Dec-26	01-Feb-27		
PH1 - Office - L1 - Catcher 1 Rooms (ER-C1.1 / ER-H1.1 / ER-M1.1)		90	01-Oct-26	03-Feb-27		
Office.L1.Catcher1-500	PH1 - Catcher1 - Mechanical OH Rough-ins	5	08-Oct-26	14-Oct-26	Trade	Mechanical
Office.L1.Catcher1-530	PH1 - Catcher1 - Mechanical Trim-out	2	05-Jan-27	06-Jan-27	Trade	Mechanical
Office.L1.Catcher1-100	PH1 - Catcher1 - Layout & Frame Walls	5	01-Oct-26	07-Oct-26		
Office.L1.Catcher1-490	PH1 - Catcher1 - Fire Sprinkler OH Rough-ins	5	01-Oct-26	07-Oct-26		
Office.L1.Catcher1-190	PH1 - Catcher1 - Vesda	5	08-Oct-26	14-Oct-26		
Office.L1.Catcher1-230	PH1 - Catcher1 - One-side Drywall	5	08-Oct-26	14-Oct-26		
Office.L1.Catcher1-440	PH1 - Catcher1 - Electrical In-Wall Rough-ins	4	08-Oct-26	13-Oct-26		
Office.L1.Catcher1-450	PH1 - Catcher1 - Plumbing In-Wall Rough-ins	2	08-Oct-26	09-Oct-26		
Office.L1.Catcher1-460	PH1 - Catcher1 - Security In-Wall Rough-ins	2	08-Oct-26	09-Oct-26		
Office.L1.Catcher1-470	PH1 - Catcher1 - Fire Alarm In-Wall Rough-ins	2	08-Oct-26	09-Oct-26		
Office.L1.Catcher1-510	PH1 - Catcher1 - Plumbing OH Rough-ins	5	08-Oct-26	14-Oct-26		
Office.L1.Catcher1-560	PH1 - Catcher1 - Hang Door Frames	5	08-Oct-26	14-Oct-26		
Office.L1.Catcher1-480	PH1 - Catcher1 - Electrical/Fire Alarm OH Rough-ins	15	12-Oct-26	30-Oct-26		
Office.L1.Catcher1-210	PH1 - Catcher1 - In-wall Inspections	1	14-Oct-26	14-Oct-26		
Office.L1.Catcher1-170	PH1 - Catcher1 - Hang, Tape, & Finish Drywall	10	15-Oct-26	28-Oct-26		
Office.L1.Catcher1-180	PH1 - Catcher1 - Prime Paint	5	26-Oct-26	30-Oct-26		
Office.L1.Catcher1-220	PH1 - Catcher1 - OH Inspections	1	02-Nov-26	02-Nov-26		
Office.L1.Catcher1-200	PH1 - Catcher1 - Install Ceiling Systems	5	12-Nov-26	18-Nov-26		
Office.L1.Catcher1-130	PH1 - Catcher1 - Install Cable Tray	10	19-Nov-26	02-Dec-26		
Office.L1.Catcher1-140	PH1 - Catcher1 - Pull & Terminate Wires	15	03-Dec-26	24-Dec-26		
Office.L1.Catcher1-150	PH1 - Catcher1 - Install Doors & Hardware	5	25-Dec-26	31-Dec-26		

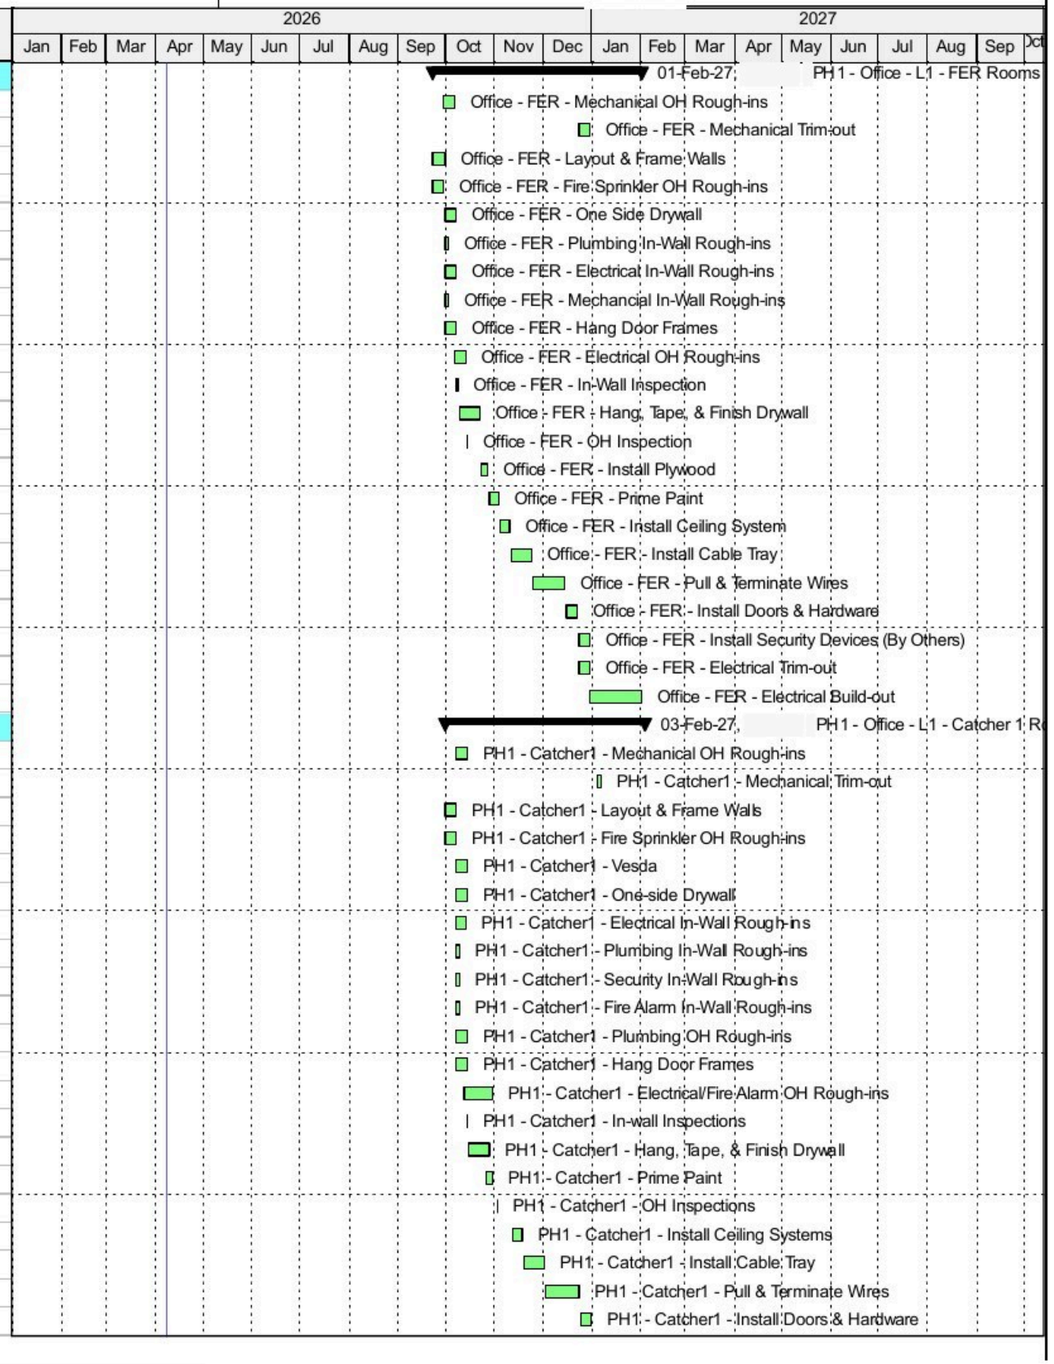


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule


Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Office.L1.Catcher1-240	PH1 - Catcher1 - Install Security Devices (By Others)	5	25-Dec-26	31-Dec-26		
Office.L1.Catcher1-520	PH1 - Catcher1 - Electrical Trim-out	2	01-Jan-27	04-Jan-27		
Office.L1.Catcher1-550	PH1 - Catcher1 - Fire Alarm Trim-out	2	07-Jan-27	08-Jan-27		
Office.L1.Catcher1-400	PH1 - Catcher1 - Punchlist	5	11-Jan-27	19-Jan-27		
Office.L1.Catcher1-410	PH1 - Catcher1 - Final Clean	5	20-Jan-27	27-Jan-27		
PH1 - Office - L1 - Electrical Room C1.1		67	02-Nov-26	02-Feb-27		
Office.L1.ER.C1.1-110	PH1 - C1.1 - Set ISU-1.1C's	5	02-Nov-26	06-Nov-26	Trade	HVAC
Office.L1.ER.C1.1-120	PH1 - C1.1 - Set ERV-1.1C-01	5	02-Nov-26	06-Nov-26	Trade	HVAC
Office.L1.ER.C1.1-150	PH1 - C1.1 - Set GENAN-1.1C	5	02-Nov-26	06-Nov-26		
Office.L1.ER.C1.1-100	PH1 - C1.1 - Set USB-1.1C (OFCI)	5	05-Nov-26	11-Nov-26		
Office.L1.ER.C1.1-130	PH1 - C1.1 - Set AMCOP-1.1C (OFCI)	5	05-Nov-26	11-Nov-26		
Office.L1.ER.C1.1-140	PH1 - C1.1 - Set DLB-1.1C (OFCI)	5	05-Nov-26	11-Nov-26		
Cx.PH1.Off.ER.C1.1-USB.100	ER C1.1 - USB's - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.C1.1-USB.110	ER C1.1 - USB's - Pre Startup Vendor	3	25-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.C1.1-USB.120	ER C1.1 - USB's - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.C1.1-USB.130	ER C1.1 - USB's - Installation Verfication Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.C1.1-USB.140	ER C1.1 - USB's - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.C1.1-USB.150	ER C1.1 - USB's - Energize Equipment	1	21-Jan-27	21-Jan-27		
Cx.PH1.Off.ER.C1.1-USB.160	ER C1.1 - USB's - L3 Startup	4	25-Jan-27	28-Jan-27		
Cx.PH1.Off.ER.C1.1-USB.170	ER C1.1 - USB's - EPMS SAT	1	29-Jan-27	29-Jan-27		
Cx.PH1.Off.ER.C1.1-USB.180	ER C1.1 - USB's - Thermographic Checks	1	01-Feb-27	01-Feb-27		
Cx.PH1.Off.ER.C1.1-USB.190	ER C1.1 - USB's - Green Tag	1	02-Feb-27	02-Feb-27		
Cx.PH1.Off.ER.C1.1-ISU.100	ER C1.1 - ISU's - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.C1.1-ISU.110	ER C1.1 - ISU's - Pre Startup Vendor	3	29-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.C1.1-ISU.120	ER C1.1 - ISU's - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.C1.1-ISU.130	ER C1.1 - ISU's - Installation Verfication Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.C1.1-ISU.140	ER C1.1 - ISU's - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.C1.1-ISU.150	ER C1.1 - ISU's - Energize Equipment	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.C1.1-ISU.160	ER C1.1 - ISU's - L3 Startup	4	07-Jan-27	12-Jan-27		
Cx.PH1.Off.ER.C1.1-ISU.170	ER C1.1 - ISU's - EPMS SAT	1	13-Jan-27	13-Jan-27		
Cx.PH1.Off.ER.C1.1-ISU.180	ER C1.1 - ISU's - Thermographic Checks	1	18-Jan-27	18-Jan-27		
Cx.PH1.Off.ER.C1.1-ISU.190	ER C1.1 - ISU's - Green Tag	1	19-Jan-27	19-Jan-27		
Cx.PH1.Off.ER.C1.1-GENAN.100	ER C1.1 - GENAN - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.C1.1-GENAN.110	ER C1.1 - GENAN - Pre Startup Vendor	3	25-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.C1.1-GENAN.120	ER C1.1 - GENAN - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.C1.1-GENAN.130	ER C1.1 - GENAN - Installation Verification Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.C1.1-GENAN.140	ER C1.1 - GENAN - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.C1.1-GENAN.150	ER C1.1 - GENAN - Energize Equipment	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.C1.1-GENAN.160	ER C1.1 - GENAN - L3 Startup	2	07-Jan-27	08-Jan-27		
Cx.PH1.Off.ER.C1.1-GENAN.170	ER C1.1 - GENAN - EPMS SAT	1	11-Jan-27	11-Jan-27		
Cx.PH1.Off.ER.C1.1-GENAN.180	ER C1.1 - GENAN - Thermographic Checks	1	12-Jan-27	12-Jan-27		
Cx.PH1.Off.ER.C1.1-GENAN.190	ER C1.1 - GENAN - Green Tag	1	13-Jan-27	13-Jan-27		
Cx.PH1.Off.ER.C1.1-AMCOP.100	ER C1.1 - AMCOP - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.C1.1-AMCOP.110	ER C1.1 - AMCOP - Pre Startup Vendor	3	25-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.C1.1-AMCOP.120	ER C1.1 - AMCOP - L2 QC	1	01-Jan-27	01-Jan-27		

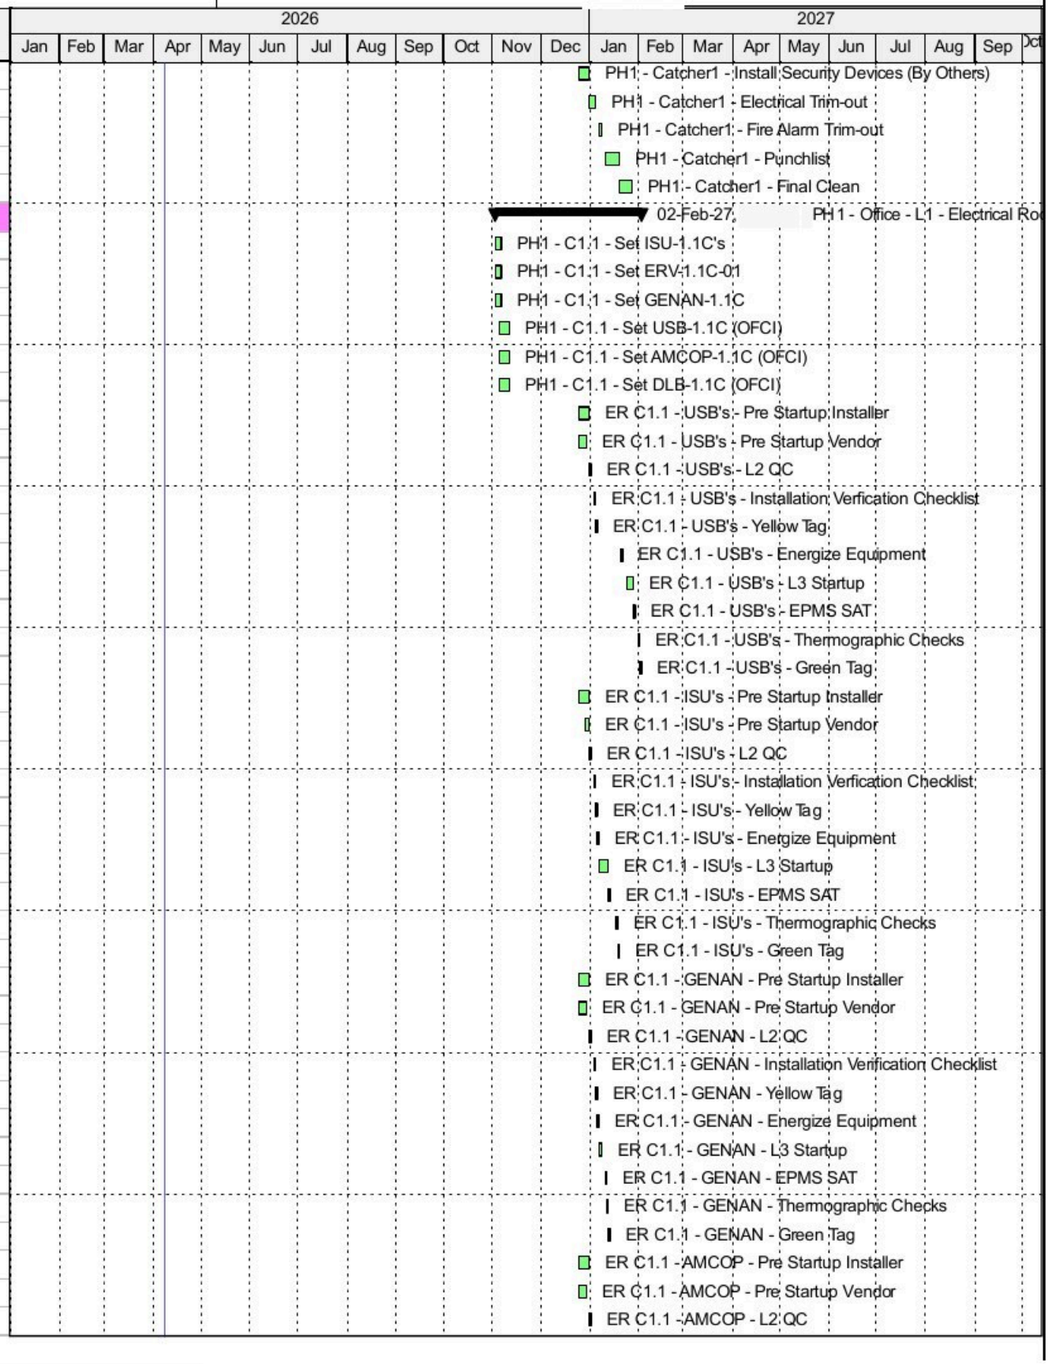


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH1.Off.ER.C1.1-AMCOP.130	ER C1.1 - AMCOP - Installation Verification Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.C1.1-AMCOP.140	ER C1.1 - AMCOP - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.C1.1-AMCOP.150	ER C1.1 - AMCOP - Energize Equipment	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.C1.1-AMCOP.160	ER C1.1 - AMCOP - L3 Startup	2	07-Jan-27	08-Jan-27		
Cx.PH1.Off.ER.C1.1-AMCOP.170	ER C1.1 - AMCOP - EPMS SAT	1	11-Jan-27	11-Jan-27		
Cx.PH1.Off.ER.C1.1-AMCOP.180	ER C1.1 - AMCOP - Thermographic Checks	1	12-Jan-27	12-Jan-27		
Cx.PH1.Off.ER.C1.1-AMCOP.190	ER C1.1 - AMCOP - Green Tag	1	13-Jan-27	13-Jan-27		
Cx.PH1.Off.ER.C1.1-ERV.100	ER C1.1 - ERV - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.C1.1-ERV.110	ER C1.1 - ERV - Pre Startup Vendor	3	25-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.C1.1-ERV.120	ER C1.1 - ERV - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.C1.1-ERV.130	ER C1.1 - ERV - Installation Verification Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.C1.1-ERV.140	ER C1.1 - ERV - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.C1.1-ERV.150	ER C1.1 - ERV - Energize Equipment	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.C1.1-ERV.160	ER C1.1 - ERV - L3 Startup	2	07-Jan-27	08-Jan-27		
Cx.PH1.Off.ER.C1.1-ERV.170	ER C1.1 - ERV - EPMS SAT	1	11-Jan-27	11-Jan-27		
Cx.PH1.Off.ER.C1.1-ERV.180	ER C1.1 - ERV - Thermographic Checks	1	12-Jan-27	12-Jan-27		
Cx.PH1.Off.ER.C1.1-ERV.190	ER C1.1 - ERV - Green Tag	1	13-Jan-27	13-Jan-27		
Cx.PH1.Off.ER.C1.1-DLB.100	ER C1.1 - DLB - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.C1.1-DLB.110	ER C1.1 - DLB - Pre Startup Vendor	3	25-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.C1.1-DLB.120	ER C1.1 - DLB - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.C1.1-DLB.130	ER C1.1 - DLB - Installation Verification Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.C1.1-DLB.140	ER C1.1 - DLB - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.C1.1-DLB.150	ER C1.1 - DLB - Energize Equipment	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.C1.1-DLB.160	ER C1.1 - DLB - L3 Startup	2	07-Jan-27	08-Jan-27		
Cx.PH1.Off.ER.C1.1-DLB.170	ER C1.1 - DLB - EPMS SAT	1	11-Jan-27	11-Jan-27		
Cx.PH1.Off.ER.C1.1-DLB.180	ER C1.1 - DLB - Thermographic Checks	1	12-Jan-27	12-Jan-27		
Cx.PH1.Off.ER.C1.1-DLB.190	ER C1.1 - DLB - Green Tag	1	13-Jan-27	13-Jan-27		
PH1 - Office - L1 - Electrical Room M1.1		67	02-Nov-26	02-Feb-27		
PH1.Off.ER.M1.1-110	PH1 - M1.1 - Set ISU-1.1M's	5	02-Nov-26	06-Nov-26	Trade	HVAC
PH1.Off.ER.M1.1-150	PH1 - M1.1 - Set ERV-1.1M-01	5	02-Nov-26	06-Nov-26	Trade	HVAC
PH1.Off.ER.M1.1-120	PH1 - M1.1 - Set RCP-01	5	02-Nov-26	06-Nov-26		
PH1.Off.ER.M1.1-140	PH1 - M1.1 - Set GENAN-M1.1	5	02-Nov-26	06-Nov-26		
PH1.Off.ER.M1.1-100	PH1 - M1.1 - Set USB-1.1M (OFCI)	5	05-Nov-26	11-Nov-26		
PH1.Off.ER.M1.1-130	PH1 - M1.1 - Set AMCOP-1.1M (OFCI)	5	05-Nov-26	11-Nov-26		
Cx.PH1.Off.ER.M1.1-USB.100	ER M1.1 - USB - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.M1.1-USB.110	ER M1.1 - USB - Pre Startup Vendor	3	25-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.M1.1-USB.120	ER M1.1 - USB - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.M1.1-USB.130	ER M1.1 - USB - Installation Verficiation Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.M1.1-USB.140	ER M1.1 - USB - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.M1.1-USB.150	ER M1.1 - USB - Energize Equipment	1	21-Jan-27	21-Jan-27		
Cx.PH1.Off.ER.M1.1-USB.160	ER M1.1 - USB - L3 Startup	4	25-Jan-27	28-Jan-27		
Cx.PH1.Off.ER.M1.1-USB.170	ER M1.1 - USB - EPMS SAT	1	29-Jan-27	29-Jan-27		
Cx.PH1.Off.ER.M1.1-USB.180	ER M1.1 - USB - Thermographic Checks	1	01-Feb-27	01-Feb-27		
Cx.PH1.Off.ER.M1.1-USB.190	ER M1.1 - USB - Green Tag	1	02-Feb-27	02-Feb-27		
Cx.PH1.Off.ER.M1.1-ISU.100	ER M1.1 - ISU - Pre Startup Installer	5	25-Dec-26	31-Dec-26		

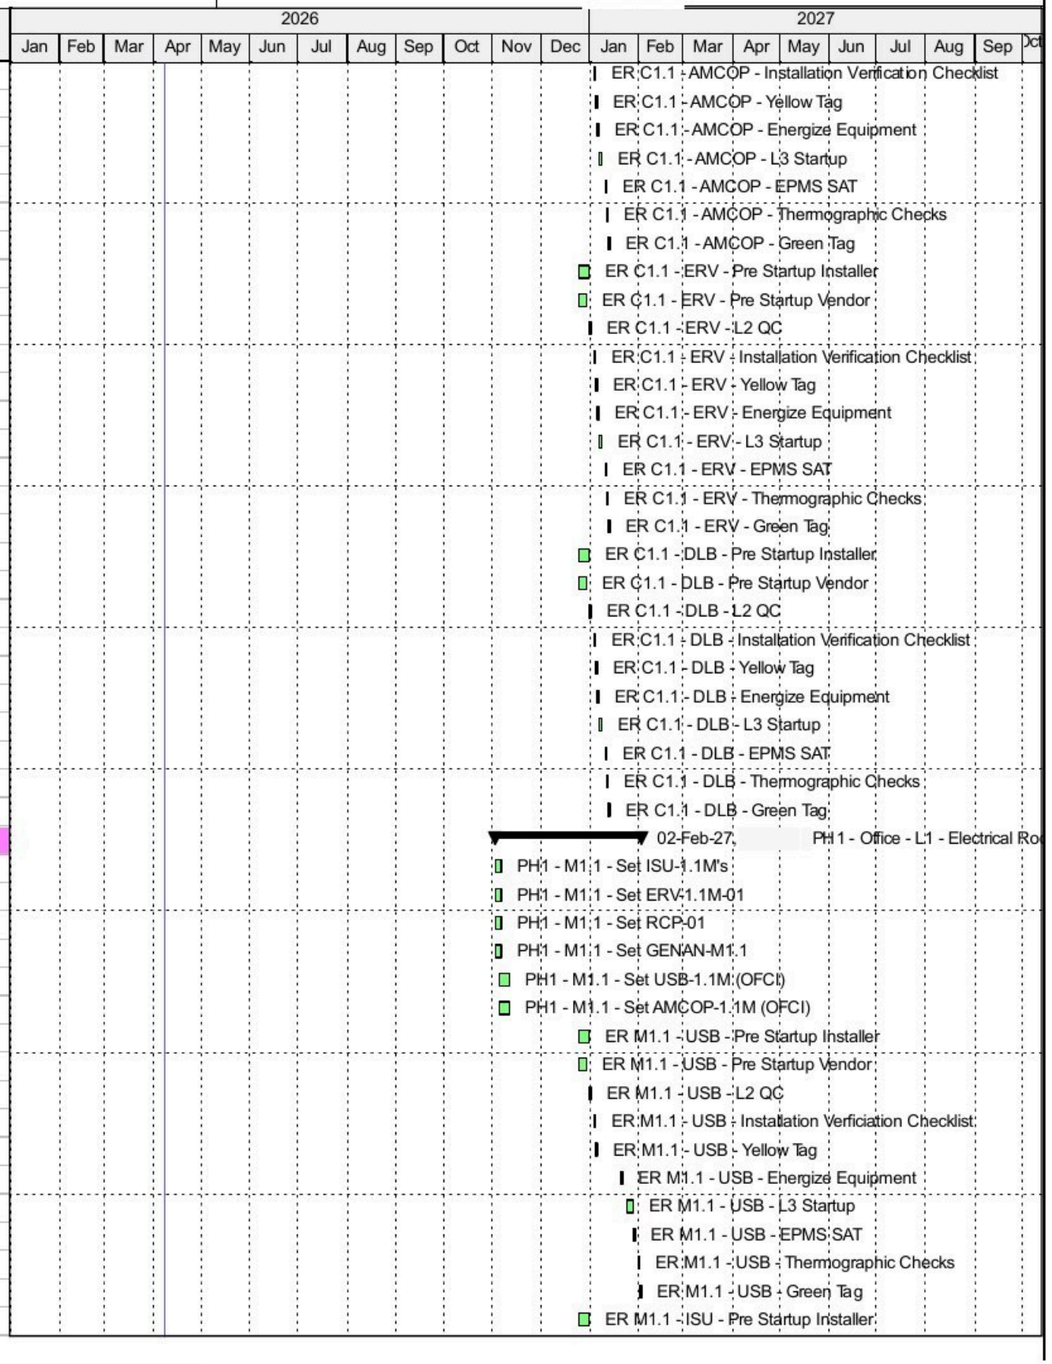

Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH1.Off.ER.M1.1-ISU.110	ER M1.1 - ISU - Pre Startup Vendor	3	29-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.M1.1-ISU.120	ER M1.1 - ISU - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.M1.1-ISU.130	ER M1.1 - ISU - Installation Verification Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.M1.1-ISU.140	ER M1.1 - ISU - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.M1.1-ISU.150	ER M1.1 - ISU - Energize Equipment	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.M1.1-ISU.160	ER M1.1 - ISU - L3 Startup	4	07-Jan-27	12-Jan-27		
Cx.PH1.Off.ER.M1.1-ISU.170	ER M1.1 - ISU - EPMS SAT	1	13-Jan-27	13-Jan-27		
Cx.PH1.Off.ER.M1.1-ISU.180	ER M1.1 - ISU - Thermographic Checks	1	18-Jan-27	18-Jan-27		
Cx.PH1.Off.ER.M1.1-ISU.190	ER M1.1 - ISU - Green Tag	1	19-Jan-27	19-Jan-27		
Cx.PH1.Off.ER.M1.1-ERV.100	ER M1.1 - ERV - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.M1.1-ERV.110	ER M1.1 - ERV - Pre Startup Vendor	3	25-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.M1.1-ERV.120	ER M1.1 - ERV - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.M1.1-ERV.130	ER M1.1 - ERV - Installation Verification Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.M1.1-ERV.140	ER M1.1 - ERV - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.M1.1-ERV.150	ER M1.1 - ERV - Energize Equipment	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.M1.1-ERV.160	ER M1.1 - ERV - L3 Startup	2	07-Jan-27	08-Jan-27		
Cx.PH1.Off.ER.M1.1-ERV.170	ER M1.1 - ERV - EPMS SAT	1	11-Jan-27	11-Jan-27		
Cx.PH1.Off.ER.M1.1-ERV.180	ER M1.1 - ERV - Thermographic Checks	1	12-Jan-27	12-Jan-27		
Cx.PH1.Off.ER.M1.1-ERV.190	ER M1.1 - ERV - Green Tag	1	13-Jan-27	13-Jan-27		
Cx.PH1.Off.ER.M1.1-GENAN.100	ER M1.1 - GENAN - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.M1.1-GENAN.110	ER M1.1 - GENAN - Pre Startup Vendor	3	25-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.M1.1-GENAN.120	ER M1.1 - GENAN - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.M1.1-GENAN.130	ER M1.1 - GENAN - Installation Verification Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.M1.1-GENAN.140	ER M1.1 - GENAN - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.M1.1-GENAN.150	ER M1.1 - GENAN - Energize Equipment	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.M1.1-GENAN.160	ER M1.1 - GENAN - L3 Startup	2	07-Jan-27	08-Jan-27		
Cx.PH1.Off.ER.M1.1-GENAN.170	ER M1.1 - GENAN - EPMS SAT	1	11-Jan-27	11-Jan-27		
Cx.PH1.Off.ER.M1.1-GENAN.180	ER M1.1 - GENAN - Thermographic Checks	1	12-Jan-27	12-Jan-27		
Cx.PH1.Off.ER.M1.1-GENAN.190	ER M1.1 - GENAN - Green Tag	1	13-Jan-27	13-Jan-27		
Cx.PH1.Off.ER.M1.1-AMCOP.100	ER M1.1 - AMCOP - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.M1.1-AMCOP.110	ER M1.1 - AMCOP - Pre Startup Vendor	3	25-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.M1.1-AMCOP.120	ER M1.1 - AMCOP - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.M1.1-AMCOP.130	ER M1.1 - AMCOP - Installation Verification Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.M1.1-AMCOP.140	ER M1.1 - AMCOP - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.M1.1-AMCOP.150	ER M1.1 - AMCOP - Energize Equipment	1	25-Jan-27	25-Jan-27		
Cx.PH1.Off.ER.M1.1-AMCOP.160	ER M1.1 - AMCOP - L3 Startup	2	26-Jan-27	27-Jan-27		
Cx.PH1.Off.ER.M1.1-AMCOP.170	ER M1.1 - AMCOP - EPMS SAT	1	28-Jan-27	28-Jan-27		
Cx.PH1.Off.ER.M1.1-AMCOP.180	ER M1.1 - AMCOP - Thermographic Checks	1	29-Jan-27	29-Jan-27		
Cx.PH1.Off.ER.M1.1-AMCOP.190	ER M1.1 - AMCOP - Green Tag	1	01-Feb-27	01-Feb-27		
PH1 - Office - L1 - Electrical Room H1.1		68	02-Nov-26	03-Feb-27		
PH1.Off.ER.H1.1-130	PH1 - H1.1 - Set ERV-1.1H-01	5	02-Nov-26	06-Nov-26	Trade	HVAC
PH1.Off.ER.H1.1-140	PH1 - H1.1 - Set ISU-1.1H's	5	02-Nov-26	06-Nov-26	Trade	HVAC
PH1.Off.ER.H1.1-150	PH1 - H1.1 - Set MV-CP-01	5	02-Nov-26	06-Nov-26		
PH1.Off.ER.H1.1-100	PH1 - H1.1 - Set TPB-MSDB's (OFCI)	5	05-Nov-26	11-Nov-26		
PH1.Off.ER.H1.1-110	PH1 - H1.1 - Set HSDB & HUPS-MBP (OFCI)	5	05-Nov-26	11-Nov-26		

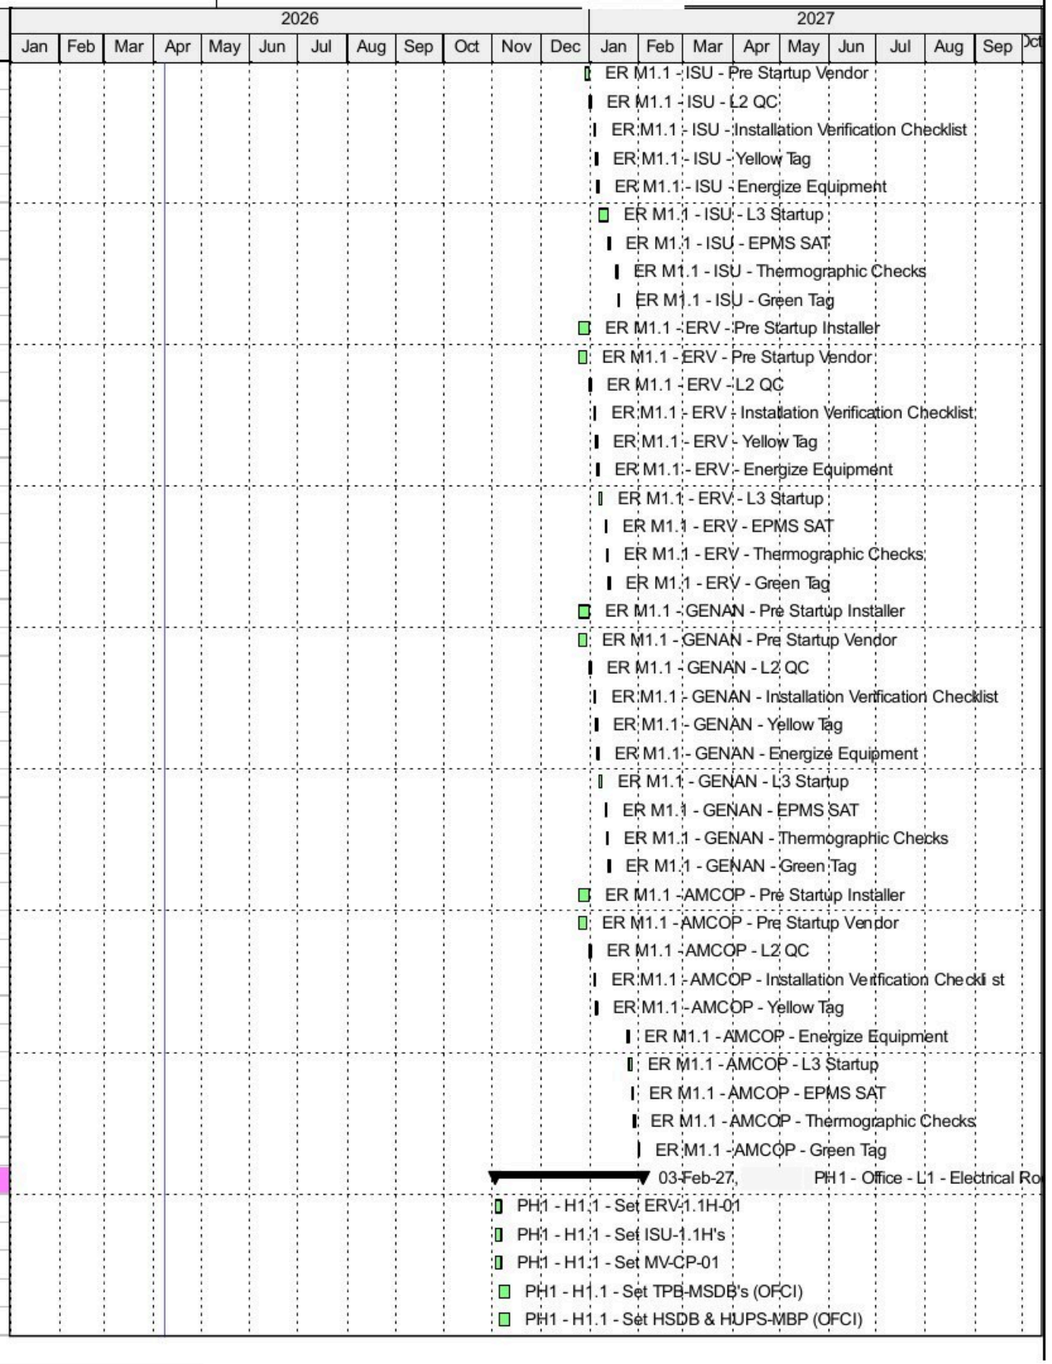


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule


Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH1.Off.ER.H1.1-120	PH1 - H1.1 - Set HUPS-01 (OFCI)	5	05-Nov-26	11-Nov-26		
Cx.PH1.Off.ER.H1.1-MV-CP.100	ER H1.1 - MV-CP - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.H1.1-MV-CP.110ER	H1.1 - MV-CP - Pre Startup Vendor	3	25-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.H1.1-MV-CP.120	ER H1.1 - MV-CP - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.H1.1-MV-CP.130	ER H1.1 - MV-CP - Installation Verification Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.H1.1-MV-CP.140	ER H1.1 - MV-CP - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.H1.1-MV-CP.150	ER H1.1 - MV-CP - Energize Equipment	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.H1.1-MV-CP.160	ER H1.1 - MV-CP - L3 Startup	4	07-Jan-27	12-Jan-27		
Cx.PH1.Off.ER.H1.1-MV-CP.170	ER H1.1 - MV-CP - EPMS SAT	1	13-Jan-27	13-Jan-27		
Cx.PH1.Off.ER.H1.1-MV-CP.180	ER H1.1 - MV-CP - Thermographic Checks	1	18-Jan-27	18-Jan-27		
Cx.PH1.Off.ER.H1.1-MV-CP.190	ER H1.1 - MV-CP - Green Tag	1	19-Jan-27	19-Jan-27		
Cx.PH1.Off.ER.H1.1-TPB-MSDB.100	ER H1.1 - TPB-MSDB - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.H1.1-TPB-MSDB.110	ER H1.1 - TPB-MSDB - Pre Startup Vendor	3	25-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.H1.1-TPB-MSDB.120	ER H1.1 - TPB-MSDB - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.H1.1-TPB-MSDB.130	ER H1.1 - TPB-MSDB - Installation Verification Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.H1.1-TPB-MSDB.140	ER H1.1 - TPB-MSDB - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.H1.1-TPB-MSDB.150	ER H1.1 - TPB-MSDB - Energize Equipment	1	25-Jan-27	25-Jan-27		
Cx.PH1.Off.ER.H1.1-TPB-MSDB.160	ER H1.1 - TPB-MSDB - L3 Startup	4	26-Jan-27	29-Jan-27		
Cx.PH1.Off.ER.H1.1-TPB-MSDB.170	ER H1.1 - TPB-MSDB - EPMS SAT	1	01-Feb-27	01-Feb-27		
Cx.PH1.Off.ER.H1.1-TPB-MSDB.180	ER H1.1 - TPB-MSDB - Thermographic Checks	1	02-Feb-27	02-Feb-27		
Cx.PH1.Off.ER.H1.1-TPB-MSDB.190	ER H1.1 - TPB-MSDB - Green Tag	1	03-Feb-27	03-Feb-27		
Cx.PH1.Off.ER.H1.1-HUPS.100ER	H1.1 - HUP's - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.H1.1-HUPS.110ER	H1.1 - HUP's - Pre Startup Vendor	3	25-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.H1.1-HUPS.120ER	H1.1 - HUP's - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.H1.1-HUPS.130ER	H1.1 - HUP's - Installation Verification Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.H1.1-HUPS.140ER	H1.1 - HUP's - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.H1.1-HUPS.150ER	H1.1 - HUP's - Energize Equipment	1	25-Jan-27	25-Jan-27		
Cx.PH1.Off.ER.H1.1-HUPS.160ER	H1.1 - HUP's - L3 Startup	4	26-Jan-27	29-Jan-27		
Cx.PH1.Off.ER.H1.1-HUPS.170ER	H1.1 - HUP's - EPMS SAT	1	01-Feb-27	01-Feb-27		
Cx.PH1.Off.ER.H1.1-HUPS.180ER	H1.1 - HUP's - Thermographic Checks	1	02-Feb-27	02-Feb-27		
Cx.PH1.Off.ER.H1.1-HUPS.190ER	H1.1 - HUP's - Green Tag	1	03-Feb-27	03-Feb-27		
Cx.PH1.Off.ER.H1.1-HSDB.100ER	H1.1 - HSDB - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.H1.1-HSDB.110ER	H1.1 - HSDB - Pre Startup Vendor	3	25-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.H1.1-HSDB.120ER	H1.1 - HSDB - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.H1.1-HSDB.130ER	H1.1 - HSDB - Installation Verification Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.H1.1-HSDB.140ER	H1.1 - HSDB - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.H1.1-HSDB.150ER	H1.1 - HSDB - Energize Equipment	1	25-Jan-27	25-Jan-27		
Cx.PH1.Off.ER.H1.1-HSDB.160ER	H1.1 - HSDB - L3 Startup	4	26-Jan-27	29-Jan-27		
Cx.PH1.Off.ER.H1.1-HSDB.170ER	H1.1 - HSDB - EPMS SAT	1	01-Feb-27	01-Feb-27		
Cx.PH1.Off.ER.H1.1-HSDB.180ER	H1.1 - HSDB - Thermographic Checks	1	02-Feb-27	02-Feb-27		
Cx.PH1.Off.ER.H1.1-HSDB.190ER	H1.1 - HSDB - Green Tag	1	03-Feb-27	03-Feb-27		
Cx.PH1.Off.ER.H1.1-ISU.100	ER H1.1 - ISU's - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.H1.1-ISU.110	ER H1.1 - ISU's - Pre Startup Vendor	3	29-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.H1.1-ISU.120	ER H1.1 - ISU's - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.H1.1-ISU.130	ER H1.1 - ISU's - Installation Verification Checklist	1	04-Jan-27	04-Jan-27		

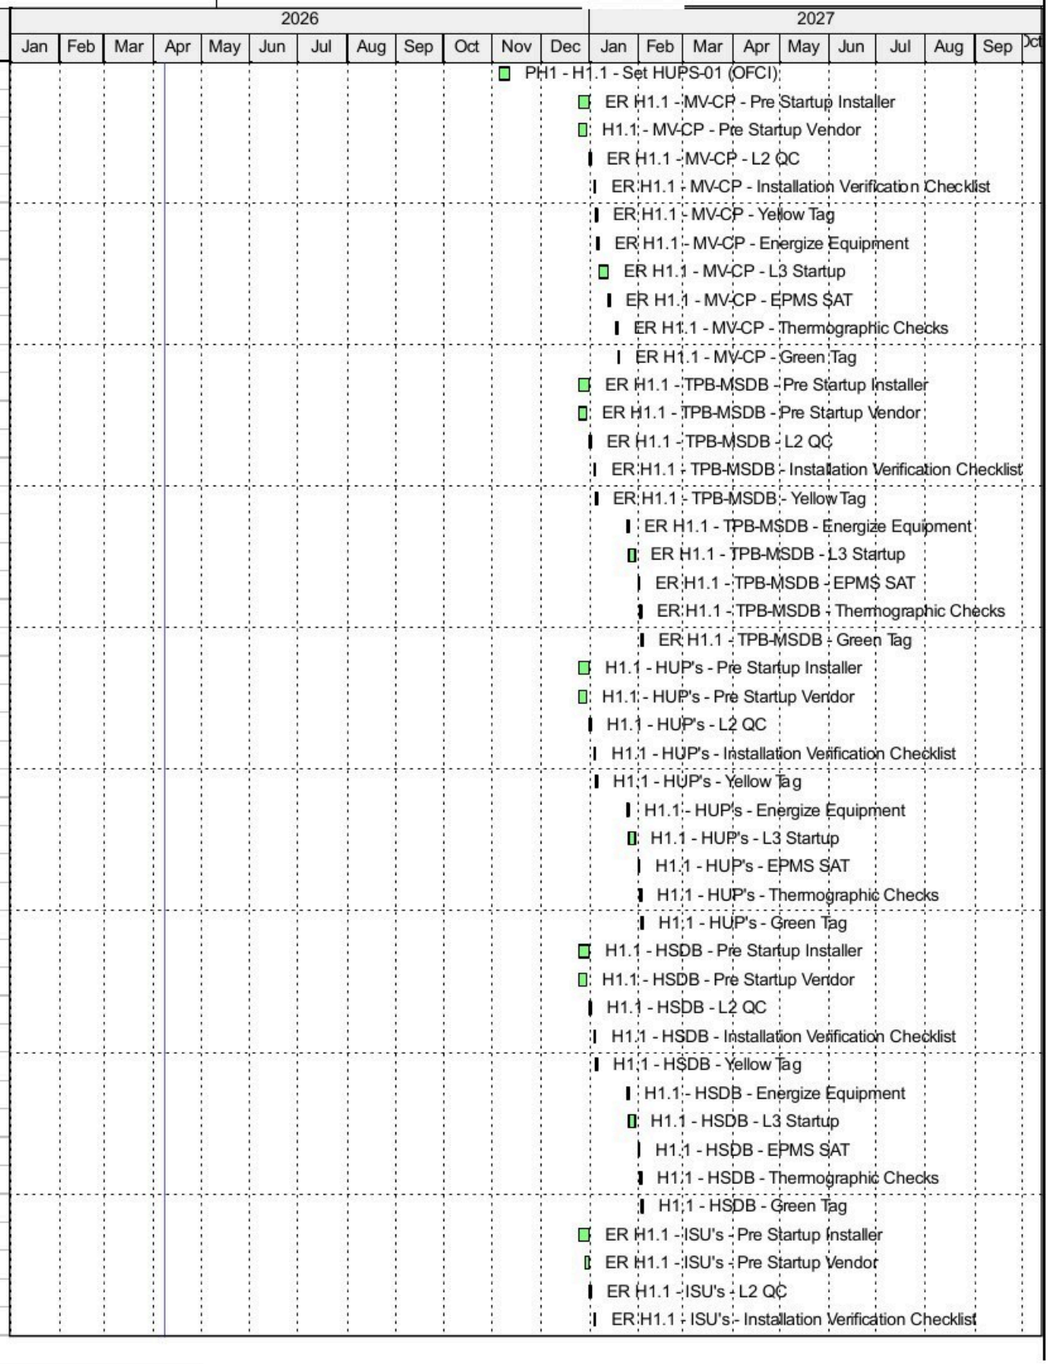

Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH1.Off.ER.H1.1-ISU.140	ER H1.1 - ISU's - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.H1.1-ISU.150	ER H1.1 - ISU's - Energize Equipment	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.H1.1-ISU.160	ER H1.1 - ISU's - L3 Startup	4	07-Jan-27	12-Jan-27		
Cx.PH1.Off.ER.H1.1-ISU.170	ER H1.1 - ISU's - EPMS SAT	1	13-Jan-27	13-Jan-27		
Cx.PH1.Off.ER.H1.1-ISU.180	ER H1.1 - ISU's - Thermographic Checks	1	18-Jan-27	18-Jan-27		
Cx.PH1.Off.ER.H1.1-ISU.190	ER H1.1 - ISU's - Green Tag	1	19-Jan-27	19-Jan-27		
Cx.PH1.Off.ER.H1.1-ERV.100	ER H1.1 - ERV - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.H1.1-ERV.110	ER H1.1 - ERV - Pre Startup Vendor	3	25-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.H1.1-ERV.120	ER H1.1 - ERV - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.H1.1-ERV.130	ER H1.1 - ERV - Installation Verification Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.H1.1-ERV.140	ER H1.1 - ERV - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.H1.1-ERV.150	ER H1.1 - ERV - Energize Equipment	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.H1.1-ERV.160	ER H1.1 - ERV - L3 Startup	4	07-Jan-27	12-Jan-27		
Cx.PH1.Off.ER.H1.1-ERV.170	ER H1.1 - ERV - EPMS SAT	1	13-Jan-27	13-Jan-27		
Cx.PH1.Off.ER.H1.1-ERV.180	ER H1.1 - ERV - Thermographic Checks	1	18-Jan-27	18-Jan-27		
Cx.PH1.Off.ER.H1.1-ERV.190	ER H1.1 - ERV - Green Tag	1	19-Jan-27	19-Jan-27		
PH1 - Office - L1 - Catcher 2 Rooms (ER-C2.1 / ER-H2.1 / ER-M2.1)		108	01-Oct-26	01-Mar-27		
Office.L1.Catcher2-650	PH1 - Catcher2 - Mechanical OH Rough-ins	5	08-Oct-26	14-Oct-26	Trade	Mechanical
Office.L1.Catcher2-680	PH1 - Catcher2 - Mechanical Trim-out	2	29-Dec-26	30-Dec-26	Trade	Mechanical
Office.L1.Catcher2-250	PH1 - Catcher2 - Layout & Frame Walls	5	01-Oct-26	07-Oct-26		
Office.L1.Catcher2-660	PH1 - Catcher2 - Fire Sprinkler OH Rough-ins	5	01-Oct-26	07-Oct-26		
Office.L1.Catcher2-340	PH1 - Catcher2 - Vesda	5	08-Oct-26	14-Oct-26		
Office.L1.Catcher2-380	PH1 - Catcher2 - One-side Drywall	5	08-Oct-26	14-Oct-26		
Office.L1.Catcher2-590	PH1 - Catcher2 - Plumbing In-Wall Rough-ins	2	08-Oct-26	09-Oct-26		
Office.L1.Catcher2-600	PH1 - Catcher2 - Electrical In-Wall Rough-Ins	4	08-Oct-26	13-Oct-26		
Office.L1.Catcher2-610	PH1 - Catcher2 - Fire Alarm In-Wall Rough-Ins	2	08-Oct-26	09-Oct-26		
Office.L1.Catcher2-620	PH1 - Catcher2 - Security In-Wall Rough-ins	2	08-Oct-26	09-Oct-26		
Office.L1.Catcher2-640	PH1 - Catcher2 - Electrical/Fire Alarm OH Rough-ins	15	08-Oct-26	28-Oct-26		
Office.L1.Catcher2-710	PH1 - Catcher2 - Hang Door Frames	5	08-Oct-26	14-Oct-26		
Office.L1.Catcher2-630	PH1 - Catcher2 - Plumbing OH Rough-ins	5	09-Oct-26	15-Oct-26		
Office.L1.Catcher2-360	PH1 - Catcher2 - In-wall Inspections	1	14-Oct-26	14-Oct-26		
Office.L1.Catcher2-320	PH1 - Catcher2 - Hang, Tape, & Finish Drywall	10	15-Oct-26	28-Oct-26		
Office.L1.Catcher2-330	PH1 - Catcher2 - Prime Paint	5	26-Oct-26	30-Oct-26		
Office.L1.Catcher2-370	PH1 - Catcher2 - OH Inspections	1	29-Oct-26	29-Oct-26		
Office.L1.Catcher2-350	PH1 - Catcher2 - Install Ceiling Systems	5	12-Nov-26	18-Nov-26		
Office.L1.Catcher2-280	PH1 - Catcher2 - Install Cable Tray	10	19-Nov-26	02-Dec-26		
Office.L1.Catcher2-290	PH1 - Catcher2 - Pull & Terminate Wires	10	03-Dec-26	16-Dec-26		
Office.L1.Catcher2-300	PH1 - Catcher2 - Install Doors & Hardware	5	18-Dec-26	24-Dec-26		
Office.L1.Catcher2-390	PH1 - Catcher2 - Install Security Devices (By Others)	5	18-Dec-26	24-Dec-26		
Office.L1.Catcher2-670	PH1 - Catcher2 - Electrical Trim-out	2	25-Dec-26	28-Dec-26		
Office.L1.Catcher2-690	PH1 - Catcher2 - Fire Alarm Trim-out	2	31-Dec-26	01-Jan-27		
Office.L1.Catcher2-700	PH1 - Catcher2 - Security Trim-out (By Others)	2	04-Jan-27	05-Jan-27		
Office.L1.Catcher2-550	PH1 - Catcher2 - Punchlist	5	06-Jan-27	12-Jan-27		
Office.L1.Catcher2-560	PH1 - Catcher2 - Final Clean	5	13-Jan-27	21-Jan-27		
PH1 - Office - L1 - Electrical Room C2.1		85	02-Nov-26	26-Feb-27		

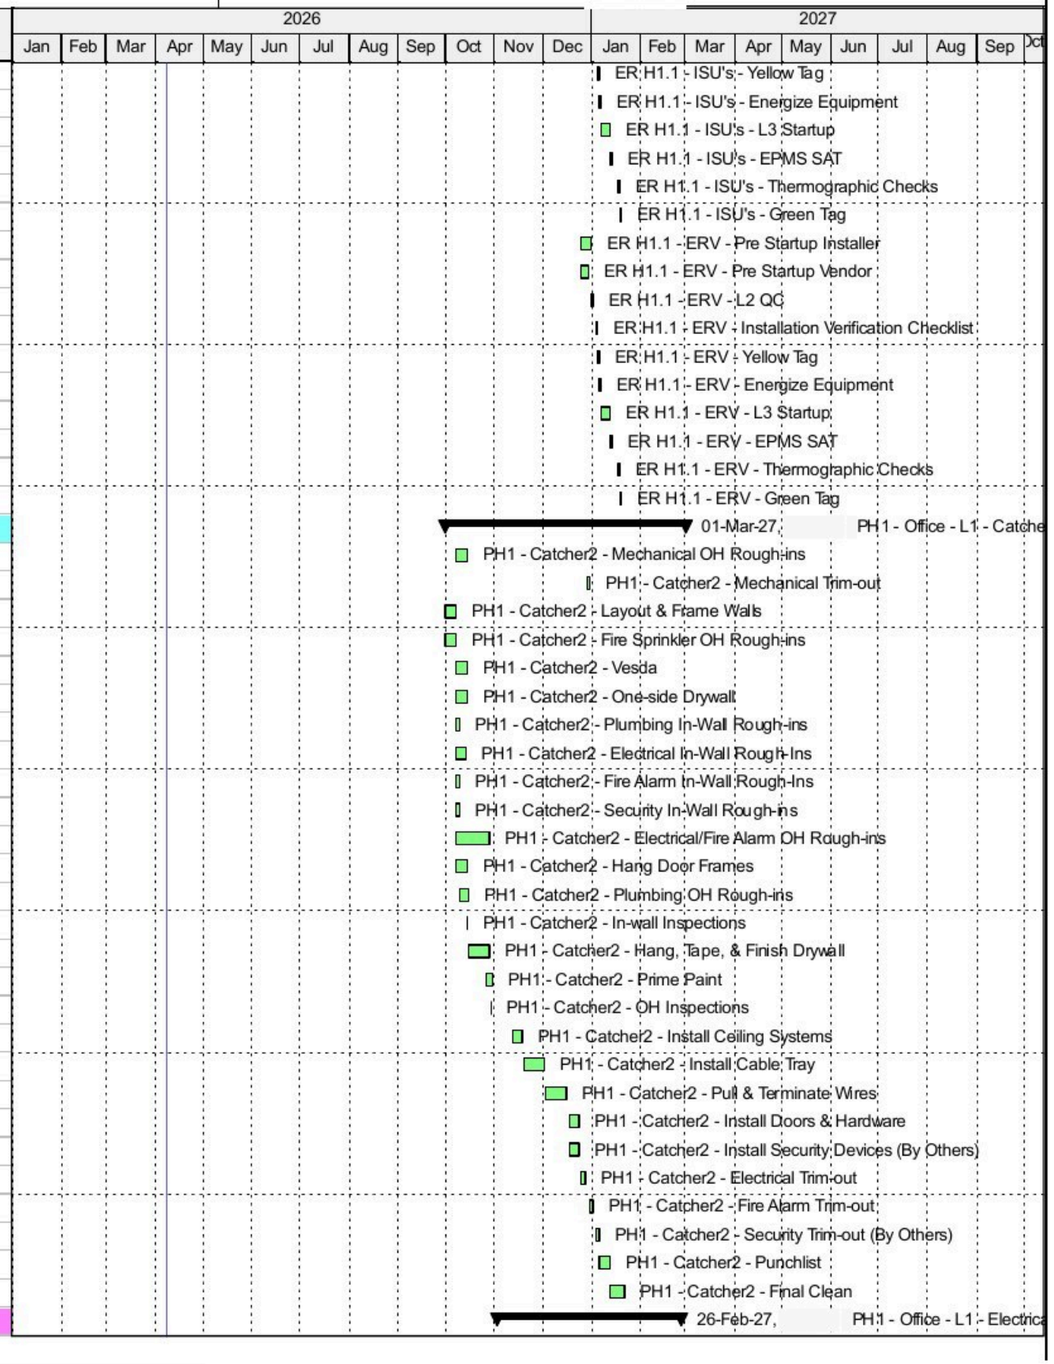


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH1.Off.ER.C2.1-170	PH1 - C2.1 - Set ISU-1.1C's	5	02-Nov-26	06-Nov-26	Trade	HVAC
PH1.Off.ER.C2.1-180	PH1 - C2.1 - Set ERV-1.1C-01	5	02-Nov-26	06-Nov-26	Trade	HVAC
PH1.Off.ER.C2.1-210	PH1 - C2.1 - Set GENAN-1.1C	5	02-Nov-26	06-Nov-26		
PH1.Off.ER.C2.1-160	PH1 - C2.1 - Set USB-1.1C (OFCI)	5	05-Nov-26	11-Nov-26		
PH1.Off.ER.C2.1-190	PH1 - C2.1 - Set AMCOP-1.1C (OFCI)	5	05-Nov-26	11-Nov-26		
PH1.Off.ER.C2.1-200	PH1 - C2.1 - Set DLB-1.1C (OFCI)	5	05-Nov-26	11-Nov-26		
Cx.PH1.Off.ER.C2.1-USB.100	ER C2.1 - USB's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH1.Off.ER.C2.1-USB.110	ER C2.1 - USB's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH1.Off.ER.C2.1-USB.120	ER C2.1 - USB's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH1.Off.ER.C2.1-USB.130	ER C2.1 - USB's - Installation Verfication Checklist	1	28-Dec-26	28-Dec-26		
Cx.PH1.Off.ER.C2.1-USB.140	ER C2.1 - USB's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.C2.1-USB.150	ER C2.1 - USB's - Energize Equipment	1	17-Feb-27	17-Feb-27		
Cx.PH1.Off.ER.C2.1-USB.160	ER C2.1 - USB's - L3 Startup	4	18-Feb-27	23-Feb-27		
Cx.PH1.Off.ER.C2.1-USB.170	ER C2.1 - USB's - EPMS SAT	1	24-Feb-27	24-Feb-27		
Cx.PH1.Off.ER.C2.1-USB.180	ER C2.1 - USB's - Thermographic Checks	1	25-Feb-27	25-Feb-27		
Cx.PH1.Off.ER.C2.1-USB.190	ER C2.1 - USB's - Green Tag	1	26-Feb-27	26-Feb-27		
Cx.PH1.Off.ER.C2.1-ISU.100	ER C2.1 - ISU's - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.C2.1-ISU.110	ER C2.1 - ISU's - Pre Startup Vendor	3	29-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.C2.1-ISU.120	ER C2.1 - ISU's - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.C2.1-ISU.130	ER C2.1 - ISU's - Installation Verfication Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.C2.1-ISU.140	ER C2.1 - ISU's - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.C2.1-ISU.150	ER C2.1 - ISU's - Energize Equipment	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.C2.1-ISU.160	ER C2.1 - ISU's - L3 Startup	4	07-Jan-27	12-Jan-27		
Cx.PH1.Off.ER.C2.1-ISU.170	ER C2.1 - ISU's - EPMS SAT	1	13-Jan-27	13-Jan-27		
Cx.PH1.Off.ER.C2.1-ISU.180	ER C2.1 - ISU's - Thermographic Checks	1	18-Jan-27	18-Jan-27		
Cx.PH1.Off.ER.C2.1-ISU.190	ER C2.1 - ISU's - Green Tag	1	19-Jan-27	19-Jan-27		
Cx.PH1.Off.ER.C2.1-GENAN.100	ER C2.1 - GENAN - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH1.Off.ER.C2.1-GENAN.110	ER C2.1 - GENAN - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH1.Off.ER.C2.1-GENAN.120	ER C2.1 - GENAN - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH1.Off.ER.C2.1-GENAN.130	ER C2.1 - GENAN - Installation Verification Checklist	1	28-Dec-26	28-Dec-26		
Cx.PH1.Off.ER.C2.1-GENAN.140	ER C2.1 - GENAN - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.C2.1-GENAN.150	ER C2.1 - GENAN - Energize Equipment	1	30-Dec-26	30-Dec-26		
Cx.PH1.Off.ER.C2.1-GENAN.160	ER C2.1 - GENAN - L3 Startup	2	31-Dec-26	01-Jan-27		
Cx.PH1.Off.ER.C2.1-GENAN.170	ER C2.1 - GENAN - EPMS SAT	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.C2.1-GENAN.180	ER C2.1 - GENAN - Thermographic Checks	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.C2.1-GENAN.190	ER C2.1 - GENAN - Green Tag	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.C2.1-AMCOP.100	ER C2.1 - AMCOP - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH1.Off.ER.C2.1-AMCOP.110	ER C2.1 - AMCOP - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH1.Off.ER.C2.1-AMCOP.120	ER C2.1 - AMCOP - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH1.Off.ER.C2.1-AMCOP.130	ER C2.1 - AMCOP - Installation Verification Checklist	1	28-Dec-26	28-Dec-26		
Cx.PH1.Off.ER.C2.1-AMCOP.140	ER C2.1 - AMCOP - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.C2.1-AMCOP.150	ER C2.1 - AMCOP - Energize Equipment	1	30-Dec-26	30-Dec-26		
Cx.PH1.Off.ER.C2.1-AMCOP.160	ER C2.1 - AMCOP - L3 Startup	2	31-Dec-26	01-Jan-27		
Cx.PH1.Off.ER.C2.1-AMCOP.170	ER C2.1 - AMCOP - EPMS SAT	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.C2.1-AMCOP.180	ER C2.1 - AMCOP - Thermographic Checks	1	05-Jan-27	05-Jan-27		

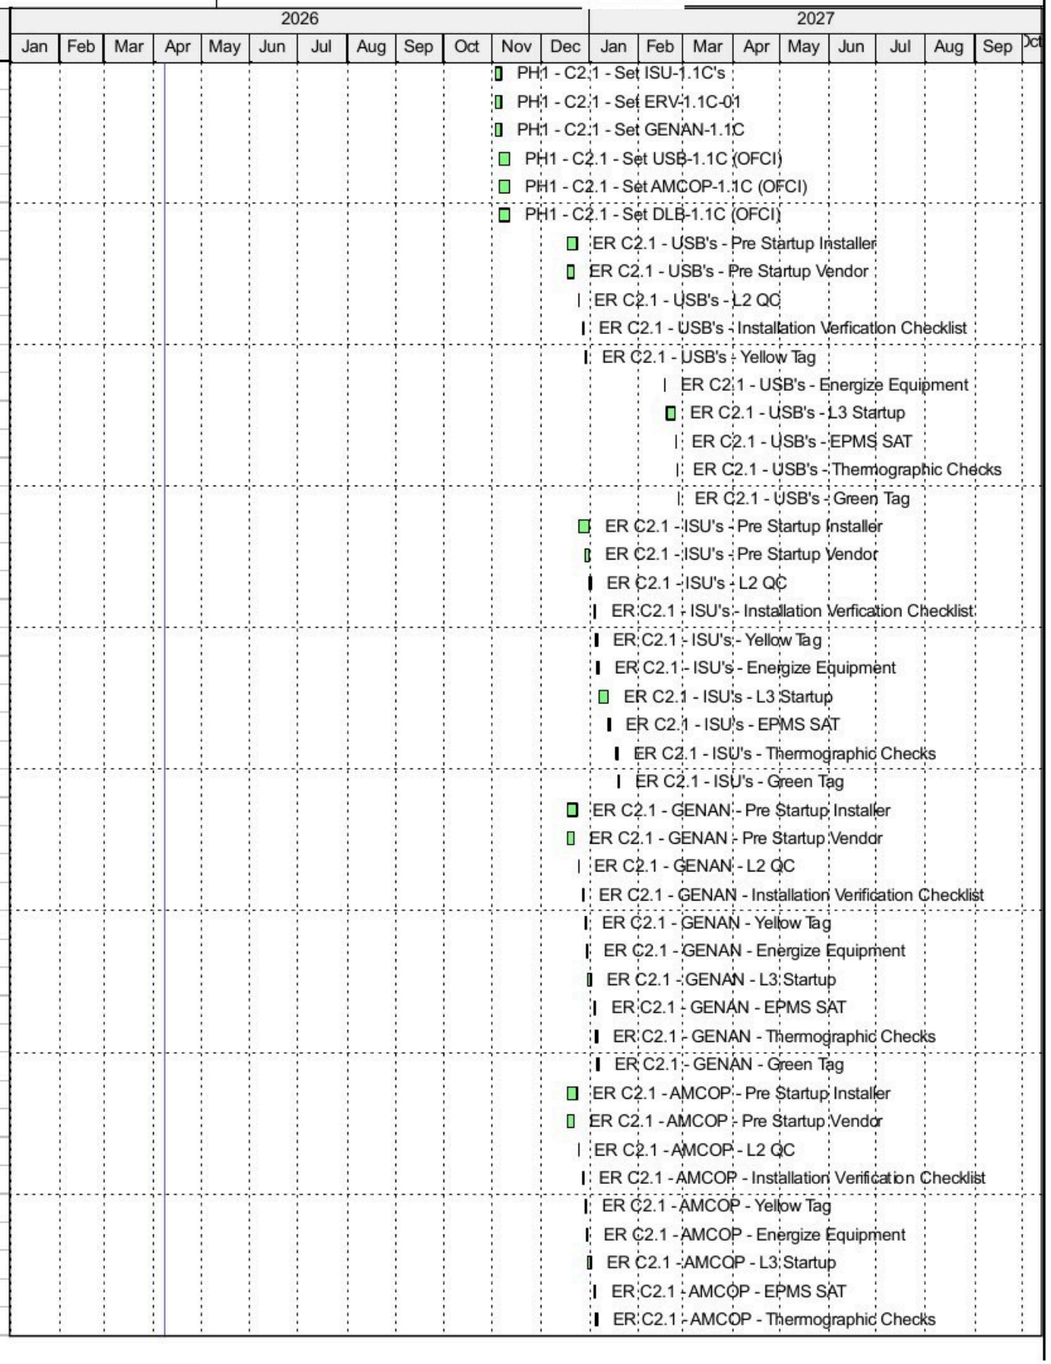


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule


Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH1.Off.ER.C2.1-AMCOP.190	ER C2.1 - AMCOP - Green Tag	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.C2.1-ERV.100	ER C2.1 - ERV - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH1.Off.ER.C2.1-ERV.110	ER C2.1 - ERV - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH1.Off.ER.C2.1-ERV.120	ER C2.1 - ERV - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH1.Off.ER.C2.1-ERV.130	ER C2.1 - ERV - Installation Verification Checklist	1	28-Dec-26	28-Dec-26		
Cx.PH1.Off.ER.C2.1-ERV.140	ER C2.1 - ERV - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.C2.1-ERV.150	ER C2.1 - ERV - Energize Equipment	1	30-Dec-26	30-Dec-26		
Cx.PH1.Off.ER.C2.1-ERV.160	ER C2.1 - ERV - L3 Startup	2	31-Dec-26	01-Jan-27		
Cx.PH1.Off.ER.C2.1-ERV.170	ER C2.1 - ERV - EPMS SAT	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.C2.1-ERV.180	ER C2.1 - ERV - Thermographic Checks	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.C2.1-ERV.190	ER C2.1 - ERV - Green Tag	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.C2.1-DLB.100	ER C2.1 - DLB - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH1.Off.ER.C2.1-DLB.110	ER C2.1 - DLB - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH1.Off.ER.C2.1-DLB.120	ER C2.1 - DLB - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH1.Off.ER.C2.1-DLB.130	ER C2.1 - DLB - Installation Verification Checklist	1	28-Dec-26	28-Dec-26		
Cx.PH1.Off.ER.C2.1-DLB.140	ER C2.1 - DLB - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.C2.1-DLB.150	ER C2.1 - DLB - Energize Equipment	1	30-Dec-26	30-Dec-26		
Cx.PH1.Off.ER.C2.1-DLB.160	ER C2.1 - DLB - L3 Startup	2	31-Dec-26	01-Jan-27		
Cx.PH1.Off.ER.C2.1-DLB.170	ER C2.1 - DLB - EPMS SAT	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.C2.1-DLB.180	ER C2.1 - DLB - Thermographic Checks	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.C2.1-DLB.190	ER C2.1 - DLB - Green Tag	1	06-Jan-27	06-Jan-27		
PH1 - Office - L1 - Electrical Room M2.1		85	02-Nov-26	26-Feb-27		
PH1.Off.ER.M2.1-170	PH1 - M2.1 - Set ISU-1.1M's	5	02-Nov-26	06-Nov-26	Trade	HVAC
PH1.Off.ER.M2.1-210	PH1 - M2.1 - Set ERV-1.1M-01	5	02-Nov-26	06-Nov-26	Trade	HVAC
PH1.Off.ER.M2.1-180	PH1 - M2.1 - Set RCP-01	5	02-Nov-26	06-Nov-26		
PH1.Off.ER.M2.1-200	PH1 - M2.1 - Set GENAN-M1.1	5	02-Nov-26	06-Nov-26		
PH1.Off.ER.M2.1-160	PH1 - M2.1 - Set USB-1.1M (OFCI)	5	05-Nov-26	11-Nov-26		
PH1.Off.ER.M2.1-190	PH1 - M2.1 - Set AMCOP-1.1M (OFCI)	5	05-Nov-26	11-Nov-26		
Cx.PH1.Off.ER.M2.1-USB.100	ER M2.1 - USB - Pre Startup Installer	3	18-Dec-26	22-Dec-26		
Cx.PH1.Off.ER.M2.1-USB.110	ER M2.1 - USB - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH1.Off.ER.M2.1-USB.120	ER M2.1 - USB - L2 QC	1	23-Dec-26	23-Dec-26		
Cx.PH1.Off.ER.M2.1-USB.130	ER M2.1 - USB - Installation Verficiation Checklist	1	24-Dec-26	24-Dec-26		
Cx.PH1.Off.ER.M2.1-USB.140	ER M2.1 - USB - Yellow Tag	1	25-Dec-26	25-Dec-26		
Cx.PH1.Off.ER.M2.1-USB.150	ER M2.1 - USB - Energize Equipment	1	17-Feb-27	17-Feb-27		
Cx.PH1.Off.ER.M2.1-USB.160	ER M2.1 - USB - L3 Startup	4	18-Feb-27	23-Feb-27		
Cx.PH1.Off.ER.M2.1-USB.170	ER M2.1 - USB - EPMS SAT	1	24-Feb-27	24-Feb-27		
Cx.PH1.Off.ER.M2.1-USB.180	ER M2.1 - USB - Thermographic Checks	1	25-Feb-27	25-Feb-27		
Cx.PH1.Off.ER.M2.1-USB.190	ER M2.1 - USB - Green Tag	1	26-Feb-27	26-Feb-27		
Cx.PH1.Off.ER.M2.1-ISU.100	ER M2.1 - ISU - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.M2.1-ISU.110	ER M2.1 - ISU - Pre Startup Vendor	3	29-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.M2.1-ISU.120	ER M2.1 - ISU - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.M2.1-ISU.130	ER M2.1 - ISU - Installation Verification Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.M2.1-ISU.140	ER M2.1 - ISU - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.M2.1-ISU.150	ER M2.1 - ISU - Energize Equipment	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.M2.1-ISU.160	ER M2.1 - ISU - L3 Startup	4	07-Jan-27	12-Jan-27		

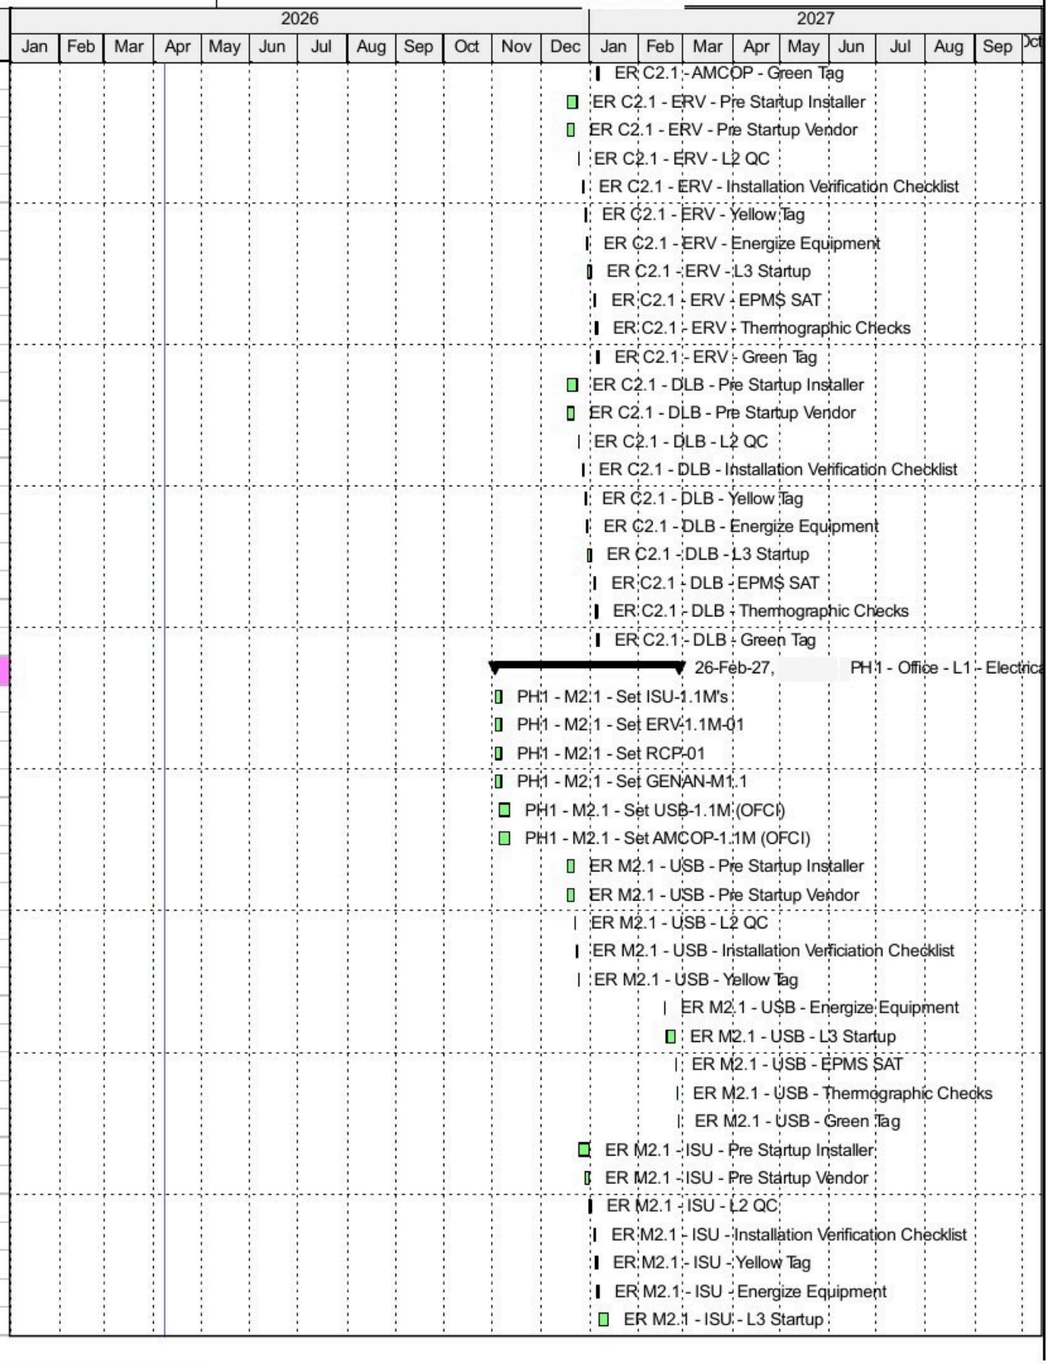


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH1.Off.ER.M2.1-ISU.170	ER M2.1 - ISU - EPMS SAT	1	13-Jan-27	13-Jan-27		
Cx.PH1.Off.ER.M2.1-ISU.180	ER M2.1 - ISU - Thermographic Checks	1	18-Jan-27	18-Jan-27		
Cx.PH1.Off.ER.M2.1-ISU.190	ER M2.1 - ISU - Green Tag	1	19-Jan-27	19-Jan-27		
Cx.PH1.Off.ER.M2.1-ERV.100	ER M2.1 - ERV - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH1.Off.ER.M2.1-ERV.110	ER M2.1 - ERV - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH1.Off.ER.M2.1-ERV.120	ER M2.1 - ERV - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH1.Off.ER.M2.1-ERV.130	ER M2.1 - ERV - Installation Verification Checklist	1	28-Dec-26	28-Dec-26		
Cx.PH1.Off.ER.M2.1-ERV.140	ER M2.1 - ERV - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.M2.1-ERV.150	ER M2.1 - ERV - Energize Equipment	1	30-Dec-26	30-Dec-26		
Cx.PH1.Off.ER.M2.1-ERV.160	ER M2.1 - ERV - L3 Startup	2	31-Dec-26	01-Jan-27		
Cx.PH1.Off.ER.M2.1-ERV.170	ER M2.1 - ERV - EPMS SAT	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.M2.1-ERV.180	ER M2.1 - ERV - Thermographic Checks	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.M2.1-ERV.190	ER M2.1 - ERV - Green Tag	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.M2.1-GENAN.100	ER M2.1 - GENAN - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH1.Off.ER.M2.1-GENAN.110	ER M2.1 - GENAN - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH1.Off.ER.M2.1-GENAN.120	ER M2.1 - GENAN - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH1.Off.ER.M2.1-GENAN.130	ER M2.1 - GENAN - Installation Verification Checklist	1	28-Dec-26	28-Dec-26		
Cx.PH1.Off.ER.M2.1-GENAN.140	ER M2.1 - GENAN - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.M2.1-GENAN.150	ER M2.1 - GENAN - Energize Equipment	1	30-Dec-26	30-Dec-26		
Cx.PH1.Off.ER.M2.1-GENAN.160	ER M2.1 - GENAN - L3 Startup	2	31-Dec-26	01-Jan-27		
Cx.PH1.Off.ER.M2.1-GENAN.170	ER M2.1 - GENAN - EPMS SAT	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.M2.1-GENAN.180	ER M2.1 - GENAN - Thermographic Checks	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.M2.1-GENAN.190	ER M2.1 - GENAN - Green Tag	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.M2.1-AMCOP.100	ER M2.1 - AMCOP - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH1.Off.ER.M2.1-AMCOP.110	ER M2.1 - AMCOP - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH1.Off.ER.M2.1-AMCOP.120	ER M2.1 - AMCOP - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH1.Off.ER.M2.1-AMCOP.130	ER M2.1 - AMCOP - Installation Verification Checkli st	1	28-Dec-26	28-Dec-26		
Cx.PH1.Off.ER.M2.1-AMCOP.140	ER M2.1 - AMCOP - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.M2.1-AMCOP.150	ER M2.1 - AMCOP - Energize Equipment	1	18-Feb-27	18-Feb-27		
Cx.PH1.Off.ER.M2.1-AMCOP.160	ER M2.1 - AMCOP - L3 Startup	2	19-Feb-27	22-Feb-27		
Cx.PH1.Off.ER.M2.1-AMCOP.170	ER M2.1 - AMCOP - EPMS SAT	1	23-Feb-27	23-Feb-27		
Cx.PH1.Off.ER.M2.1-AMCOP.180	ER M2.1 - AMCOP - Thermographic Checks	1	24-Feb-27	24-Feb-27		
Cx.PH1.Off.ER.M2.1-AMCOP.190	ER M2.1 - AMCOP - Green Tag	1	25-Feb-27	25-Feb-27		
PH1 - Office - L1 - Electrical Room H2.1		86	02-Nov-26	01-Mar-27		
PH1.Off.ER.H2.1-190	PH1 - H2.1 - Set ERV-1.1H-01	5	02-Nov-26	06-Nov-26	Trade	HVAC
PH1.Off.ER.H2.1-200	PH1 - H2.1 - Set ISU-1.1H's	5	02-Nov-26	06-Nov-26	Trade	HVAC
PH1.Off.ER.H2.1-210	PH1 - H2.1 - Set MV-CP-01	5	02-Nov-26	06-Nov-26		
PH1.Off.ER.H2.1-160	PH1 - H2.1 - Set TPB-MSDB's (OFCI)	5	05-Nov-26	11-Nov-26		
PH1.Off.ER.H2.1-170	PH1 - H2.1 - Set HSDB & HUPS-MBP (OFCI)	5	05-Nov-26	11-Nov-26		
PH1.Off.ER.H2.1-180	PH1 - H2.1 - Set HUPS-01 (OFCI)	5	05-Nov-26	11-Nov-26		
Cx.PH1.Off.ER.H2.1-MV-CP.100	ER H2.1 - MV-CP - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH1.Off.ER.H2.1-MV-CP.110ER	H2.1 - MV-CP - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH1.Off.ER.H2.1-MV-CP.120	ER H2.1 - MV-CP - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH1.Off.ER.H2.1-MV-CP.130	ER H2.1 - MV-CP - Installation Verification Checklist	1	28-Dec-26	28-Dec-26		
Cx.PH1.Off.ER.H2.1-MV-CP.140	ER H2.1 - MV-CP - Yellow Tag	1	29-Dec-26	29-Dec-26		

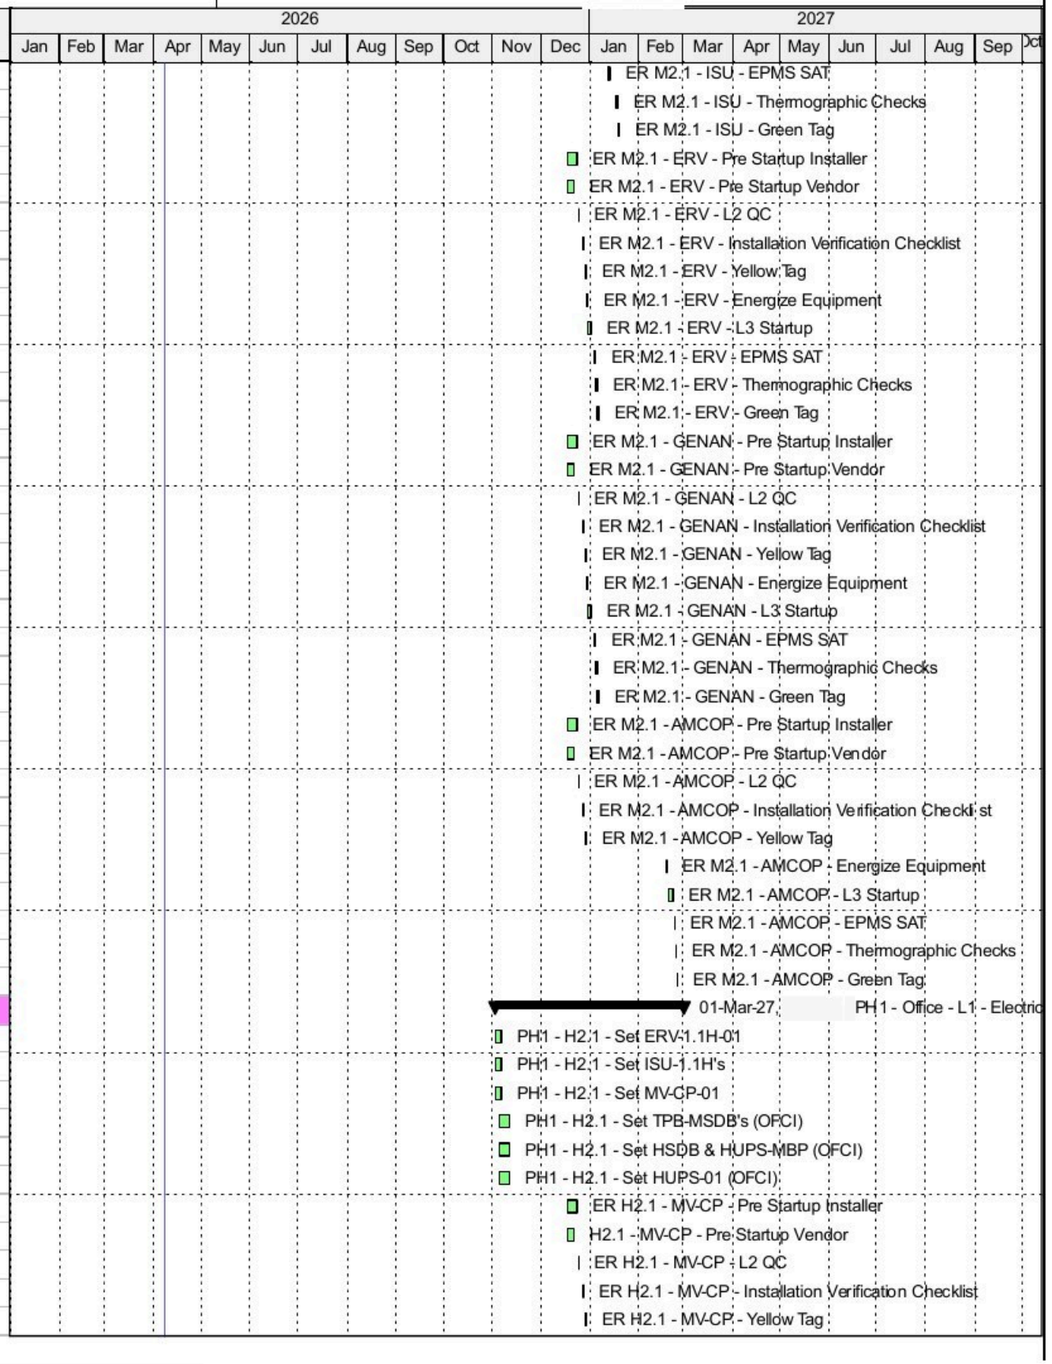


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH1.Off.ER.H2.1-MV-CP.150	ER H2.1 - MV-CP - Energize Equipment	1	30-Dec-26	30-Dec-26		
Cx.PH1.Off.ER.H2.1-MV-CP.160	ER H2.1 - MV-CP - L3 Startup	4	31-Dec-26	05-Jan-27		
Cx.PH1.Off.ER.H2.1-MV-CP.170	ER H2.1 - MV-CP - EPMS SAT	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.H2.1-MV-CP.180	ER H2.1 - MV-CP - Thermographic Checks	1	07-Jan-27	07-Jan-27		
Cx.PH1.Off.ER.H2.1-MV-CP.190	ER H2.1 - MV-CP - Green Tag	1	08-Jan-27	08-Jan-27		
Cx.PH1.Off.ER.H2.1-TPB-MSDB.100	ER H2.1 - TPB-MSDB - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH1.Off.ER.H2.1-TPB-MSDB.110	ER H2.1 - TPB-MSDB - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH1.Off.ER.H2.1-TPB-MSDB.120	ER H2.1 - TPB-MSDB - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH1.Off.ER.H2.1-TPB-MSDB.130	ER H2.1 - TPB-MSDB - Installation Verification Checklist	1	28-Dec-26	28-Dec-26		
Cx.PH1.Off.ER.H2.1-TPB-MSDB.140	ER H2.1 - TPB-MSDB - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.H2.1-TPB-MSDB.150	ER H2.1 - TPB-MSDB - Energize Equipment	1	30-Dec-26	30-Dec-26		
Cx.PH1.Off.ER.H2.1-TPB-MSDB.160	ER H2.1 - TPB-MSDB - L3 Startup	4	31-Dec-26	05-Jan-27		
Cx.PH1.Off.ER.H2.1-TPB-MSDB.170	ER H2.1 - TPB-MSDB - EPMS SAT	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.H2.1-TPB-MSDB.180	ER H2.1 - TPB-MSDB - Thermographic Checks	1	07-Jan-27	07-Jan-27		
Cx.PH1.Off.ER.H2.1-TPB-MSDB.190	ER H2.1 - TPB-MSDB - Green Tag	1	08-Jan-27	08-Jan-27		
Cx.PH1.Off.ER.H2.1-HUPS.100ER	H2.1 - HUP's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH1.Off.ER.H2.1-HUPS.110ER	H2.1 - HUP's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH1.Off.ER.H2.1-HUPS.120ER	H2.1 - HUP's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH1.Off.ER.H2.1-HUPS.130ER	H2.1 - HUP's - Installation Verification Checklist	1	28-Dec-26	28-Dec-26		
Cx.PH1.Off.ER.H2.1-HUPS.140ER	H2.1 - HUP's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.H2.1-HUPS.150ER	H2.1 - HUP's - Energize Equipment	1	18-Feb-27	18-Feb-27		
Cx.PH1.Off.ER.H2.1-HUPS.160ER	H2.1 - HUP's - L3 Startup	4	19-Feb-27	24-Feb-27		
Cx.PH1.Off.ER.H2.1-HUPS.170ER	H2.1 - HUP's - EPMS SAT	1	25-Feb-27	25-Feb-27		
Cx.PH1.Off.ER.H2.1-HUPS.180ER	H2.1 - HUP's - Thermographic Checks	1	26-Feb-27	26-Feb-27		
Cx.PH1.Off.ER.H2.1-HUPS.190ER	H2.1 - HUP's - Green Tag	1	01-Mar-27	01-Mar-27		
Cx.PH1.Off.ER.H2.1-HSDB.100ER	H2.1 - HSDB - Pre Startup Installer	3	18-Dec-26	22-Dec-26		
Cx.PH1.Off.ER.H2.1-HSDB.110ER	H2.1 - HSDB - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH1.Off.ER.H2.1-HSDB.120ER	H2.1 - HSDB - L2 QC	1	23-Dec-26	23-Dec-26		
Cx.PH1.Off.ER.H2.1-HSDB.130ER	H2.1 - HSDB - Installation Verification Checklist	1	24-Dec-26	24-Dec-26		
Cx.PH1.Off.ER.H2.1-HSDB.140ER	H2.1 - HSDB - Yellow Tag	1	25-Dec-26	25-Dec-26		
Cx.PH1.Off.ER.H2.1-HSDB.150ER	H2.1 - HSDB - Energize Equipment	1	17-Feb-27	17-Feb-27		
Cx.PH1.Off.ER.H2.1-HSDB.160ER	H2.1 - HSDB - L3 Startup	4	18-Feb-27	23-Feb-27		
Cx.PH1.Off.ER.H2.1-HSDB.170ER	H2.1 - HSDB - EPMS SAT	1	24-Feb-27	24-Feb-27		
Cx.PH1.Off.ER.H2.1-HSDB.180ER	H2.1 - HSDB - Thermographic Checks	1	25-Feb-27	25-Feb-27		
Cx.PH1.Off.ER.H2.1-HSDB.190ER	H2.1 - HSDB - Green Tag	1	26-Feb-27	26-Feb-27		
Cx.PH1.Off.ER.H2.1-ISU.100	ER H2.1 - ISU's - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.H2.1-ISU.110	ER H2.1 - ISU's - Pre Startup Vendor	3	29-Dec-26	31-Dec-26		
Cx.PH1.Off.ER.H2.1-ISU.120	ER H2.1 - ISU's - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.Off.ER.H2.1-ISU.130	ER H2.1 - ISU's - Installation Verification Checklist	1	04-Jan-27	04-Jan-27		
Cx.PH1.Off.ER.H2.1-ISU.140	ER H2.1 - ISU's - Yellow Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.Off.ER.H2.1-ISU.150	ER H2.1 - ISU's - Energize Equipment	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.H2.1-ISU.160	ER H2.1 - ISU's - L3 Startup	4	07-Jan-27	12-Jan-27		
Cx.PH1.Off.ER.H2.1-ISU.170	ER H2.1 - ISU's - EPMS SAT	1	13-Jan-27	13-Jan-27		
Cx.PH1.Off.ER.H2.1-ISU.180	ER H2.1 - ISU's - Thermographic Checks	1	18-Jan-27	18-Jan-27		
Cx.PH1.Off.ER.H2.1-ISU.190	ER H2.1 - ISU's - Green Tag	1	19-Jan-27	19-Jan-27		

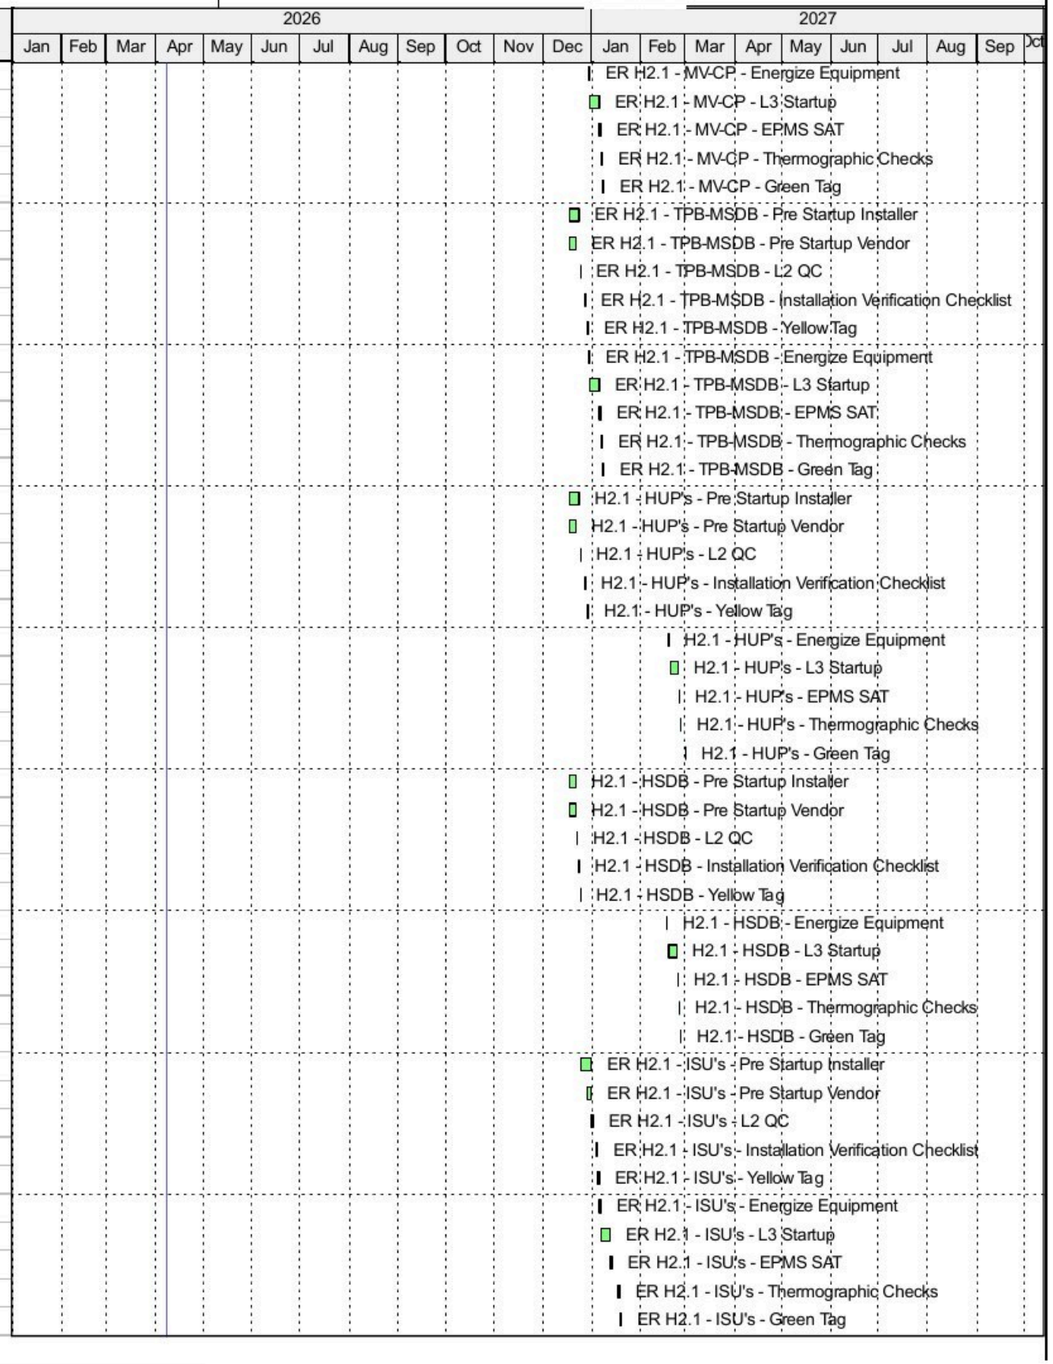


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH1.Off.ER.H2.1-ERV.100	ER H2.1 - ERV - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH1.Off.ER.H2.1-ERV.110	ER H2.1 - ERV - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH1.Off.ER.H2.1-ERV.120	ER H2.1 - ERV - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH1.Off.ER.H2.1-ERV.130	ER H2.1 - ERV - Installation Verification Checklist	1	28-Dec-26	28-Dec-26		
Cx.PH1.Off.ER.H2.1-ERV.140	ER H2.1 - ERV - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.Off.ER.H2.1-ERV.150	ER H2.1 - ERV - Energize Equipment	1	30-Dec-26	30-Dec-26		
Cx.PH1.Off.ER.H2.1-ERV.160	ER H2.1 - ERV - L3 Startup	4	31-Dec-26	05-Jan-27		
Cx.PH1.Off.ER.H2.1-ERV.170	ER H2.1 - ERV - EPMS SAT	1	06-Jan-27	06-Jan-27		
Cx.PH1.Off.ER.H2.1-ERV.180	ER H2.1 - ERV - Thermographic Checks	1	07-Jan-27	07-Jan-27		
Cx.PH1.Off.ER.H2.1-ERV.190	ER H2.1 - ERV - Green Tag	1	08-Jan-27	08-Jan-27		
PH1 - Office - L1 - Flex Rooms		37	18-Dec-26	08-Feb-27		
PH1 - Office - L1 - Flex Room Commissioning OPP-05 Cx		37	18-Dec-26	08-Feb-27		
Cx.Off.EC-OPP.200	Office Flex Room - OPP's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.Off.EC-OPP.210	Office Flex Room - OPP's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.Off.EC-OPP.220	Office Flex Room - OPP's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.Off.EC-OPP.230	Office Flex Room - OPP's - Installation Verification Checklist	1	28-Dec-26	28-Dec-26		
Cx.Off.EC-OPP.240	Office Flex Room - OPP's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.Off.EC-OPP.250	Office Flex Room - OPP's - Energize Equipment	1	28-Jan-27	28-Jan-27		
Cx.Off.EC-OPP.260	Office Flex Room - OPP's - L3 Startup	4	29-Jan-27	03-Feb-27		
Cx.Off.EC-OPP.270	Office Flex Room - OPP's - EPMS SAT	1	04-Feb-27	04-Feb-27		
Cx.Off.EC-OPP.280	Office Flex Room - OPP's - Thermographic Checks	1	05-Feb-27	05-Feb-27		
Cx.Off.EC-OPP.290	Office Flex Room - OPP's - Green Tag	1	08-Feb-27	08-Feb-27		
PH1 - Office - L1 - MMR Room		100	02-Sep-26	19-Jan-27		
Office.L1.MMR.310	Office - MMR - Mechanical OH Rough-ins	5	08-Sep-26	14-Sep-26	Trade	Mechanical
Office.L1.MMR.330	Office - MMR - Mechanical Trim-out	5	01-Dec-26	07-Dec-26	Trade	Mechanical
Office.L1.MMR.170	Office - MMR - Layout & Frame Walls	5	02-Sep-26	08-Sep-26		
Office.L1.MMR.180	Office - MMR - Fire Sprinkler OH Rough-ins	4	02-Sep-26	07-Sep-26		
Office.L1.MMR.190	Office - MMR - One Side Drywall	5	09-Sep-26	15-Sep-26		
Office.L1.MMR.270	Office - MMR - Plumbing In-wall Rough-ins	2	09-Sep-26	10-Sep-26		
Office.L1.MMR.280	Office - MMR - Electrical In-wall Rough-ins	3	09-Sep-26	11-Sep-26		
Office.L1.MMR.350	Office - MMR - Hang Door Frames	5	09-Sep-26	15-Sep-26		
Office.L1.MMR.290	Office - MMR - Mechanical In-wall Rough-ins	2	10-Sep-26	11-Sep-26		
Office.L1.MMR.110	Office - MMR - In-Wall Inspection	1	14-Sep-26	14-Sep-26		
Office.L1.MMR.300	Office - MMR - Electrical OH Rough-ins	5	15-Sep-26	21-Sep-26		
Office.L1.MMR.120	Office - MMR - Hang, Tape, & Finish Drywall	5	16-Sep-26	22-Sep-26		
Office.L1.MMR.140	Office - MMR - Prime Paint	5	18-Sep-26	24-Sep-26		
Office.L1.MMR.130	Office - MMR - OH Inspection	1	22-Sep-26	22-Sep-26		
Office.L1.MMR.150	Office - MMR - Install Ceiling Grid & Tiles	5	10-Nov-26	16-Nov-26		
Office.L1.MMR.160	Office - MMR - Install Cable Tray	5	17-Nov-26	23-Nov-26		
Office.L1.MMR.200	Office - MMR - Pull & Terminate Wires	5	24-Nov-26	30-Nov-26		
Office.L1.MMR.230	Office - MMR - Install Doors & Hardware	5	01-Dec-26	07-Dec-26		
Office.L1.MMR.210	Office - MMR - Install Security Devices (By Others)	5	01-Dec-26	07-Dec-26		
Office.L1.MMR.320	Office - MMR - Electrical Trim-out	5	01-Dec-26	07-Dec-26		
Office.L1.MMR.340	Office - MMR - Fire Alarm Trim-out	5	15-Dec-26	22-Dec-26		
Office.L1.MMR.250	Office - MMR - Punchlist	5	23-Dec-26	29-Dec-26		

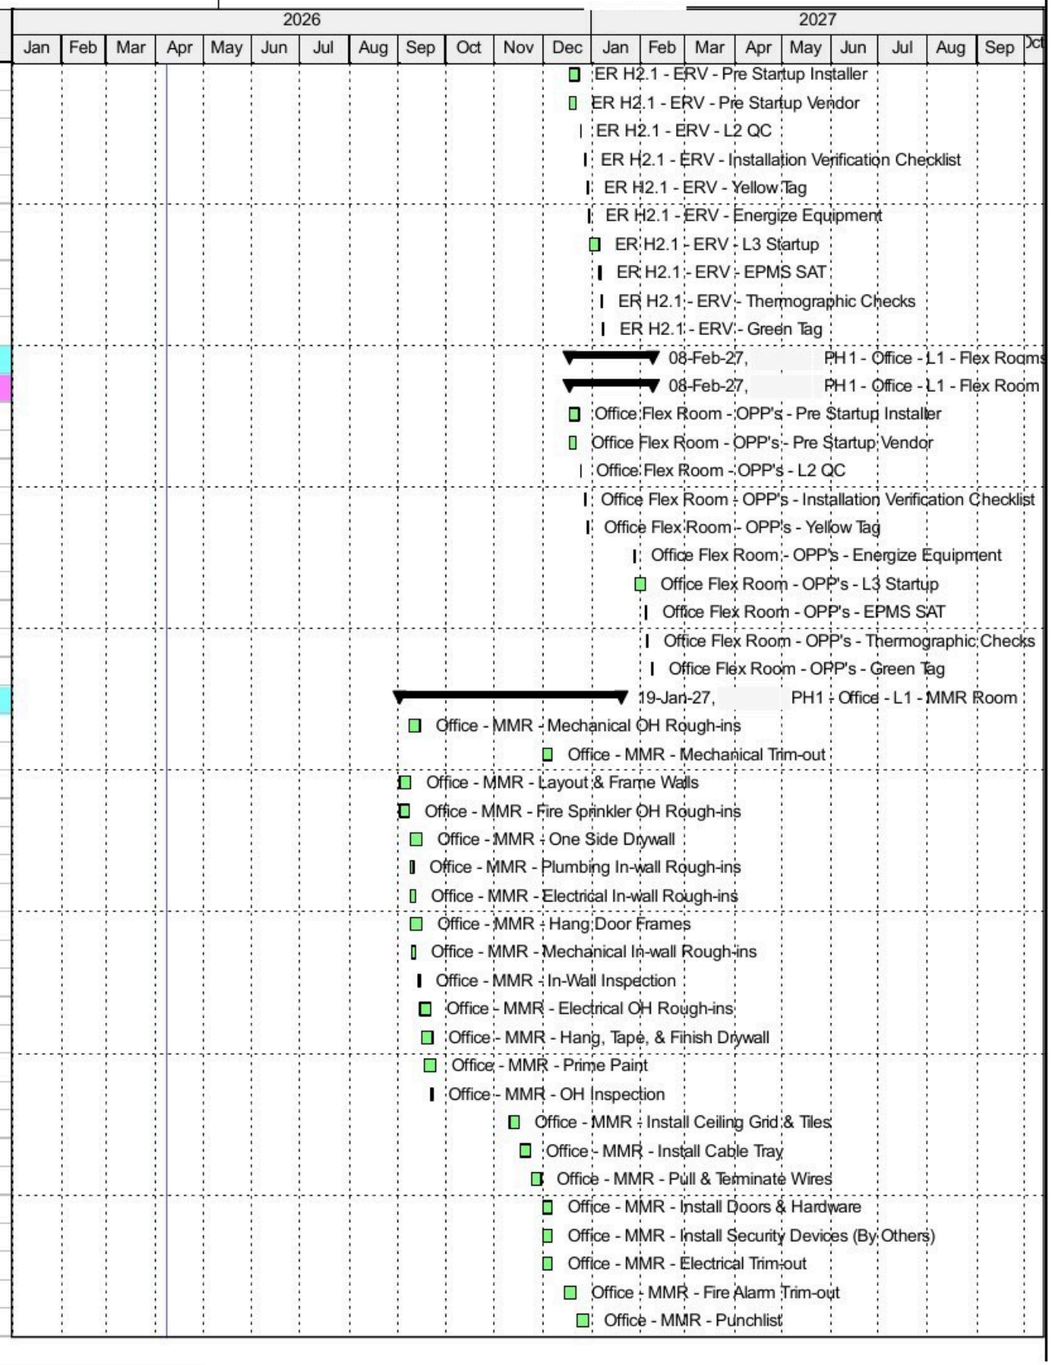

Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Office.L1.MMR.260	Office - MMR - Final Clean	5	30-Dec-26	05-Jan-27		
PH1 - Office - L1 - MMR Room Equipment		5	03-Nov-26	09-Nov-26		
Office.L1.MMR.240	Office - MMR - Set CRAC Units	5	03-Nov-26	09-Nov-26	Trade	HVAC
PH1 - Office - L1 - MMR CRAC-MMR-01 & CRAC-MMR-02 Cx		18	25-Dec-26	19-Jan-27		
Cx.Office.MMR-CRAC.100	MMR - CRAC's - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.Office.MMR-CRAC.110	MMR - CRAC's - Pre Startup Vendor	3	29-Dec-26	31-Dec-26		
Cx.Office.MMR-CRAC.120	MMR - CRAC's - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.Office.MMR-CRAC.130	MMR - CRAC's - Installation Verification Checklist	2	04-Jan-27	05-Jan-27		
Cx.Office.MMR-CRAC.140	MMR - CRAC's - Yellow Tag	1	06-Jan-27	06-Jan-27		
Cx.Office.MMR-CRAC.150	MMR - CRAC's - Energize Equipment	1	07-Jan-27	07-Jan-27		
Cx.Office.MMR-CRAC.160	MMR - CRAC's - L3 Startup	1	08-Jan-27	08-Jan-27		
Cx.Office.MMR-CRAC.180	MMR - CRAC's - BAS SAT	1	11-Jan-27	11-Jan-27		
Cx.Office.MMR-CRAC.170	MMR - CRAC's - TAB	3	12-Jan-27	18-Jan-27		
Cx.Office.MMR-CRAC.190	MMR - CRAC's - Green Tag	1	19-Jan-27	19-Jan-27		
PH1 - Office - L1 - Restrooms		93	02-Sep-26	08-Jan-27		
Office.L1.Rest.330	Office - L1 - RR - Mechanical OH Rough-Ins	10	29-Sep-26	12-Oct-26	Trade	Mechanical
Office.L1.Rest.530	Office - L1 - RR - Mechanical Trim-out	5	10-Nov-26	16-Nov-26	Trade	Mechanical
Office.L1.Rest.300	Office - L1 - RR - Fire Sprinkler OH Rough-Ins	5	02-Sep-26	08-Sep-26		
Office.L1.Rest.100	Office - L1 - RR - Layout Walls	1	02-Sep-26	02-Sep-26		
Office.L1.Rest.110	Office - L1 - RR - Frame Walls	3	03-Sep-26	07-Sep-26		
Office.L1.Rest.120	Office - L1 - RR - One Side Drywall	5	04-Sep-26	10-Sep-26		
Office.L1.Rest.130	Office - L1 - RR - Hang Door Frames	2	08-Sep-26	09-Sep-26		
Office.L1.Rest.220	Office - L1 - RR - Plumbing In-Wall Rough-Ins	8	08-Sep-26	17-Sep-26		
Office.L1.Rest.200	Office - L1 - RR - Electrical/Fire Alarm In-Wall Rough-Ins	5	10-Sep-26	16-Sep-26		
Office.L1.Rest.210	Office - L1 - RR - Sec/Telecom In-Wall Rough-Ins	2	14-Sep-26	15-Sep-26		
Office.L1.Rest.290	Office - L1 - RR - In-Wall Inspections	1	18-Sep-26	18-Sep-26		
Office.L1.Rest.140	Office - L1 - RR - Hang, Tape, & Finish Drywall	10	21-Sep-26	05-Oct-26		
Office.L1.Rest.340	Office - L1 - RR - Plumbing OH Rough-Ins	5	02-Oct-26	08-Oct-26		
Office.L1.Rest.160	Office - L1 - RR - Prime Paint	5	06-Oct-26	12-Oct-26		
Office.L1.Rest.310	Office - L1 - RR - Electrical/Fire Alarm OH Rough-Ins	5	08-Oct-26	14-Oct-26		
Office.L1.Rest.320	Office - L1 - RR - Sec/Telecom OH Rough-Ins	5	13-Oct-26	19-Oct-26		
Office.L1.Rest.390	Office - L1 - RR - OH Inspections	1	20-Oct-26	20-Oct-26		
Office.L1.Rest.350	Office - L1 - RR - Install Cable Tray	5	20-Oct-26	26-Oct-26		
Office.L1.Rest.190	Office - L1 - RR - Install Ceiling	5	21-Oct-26	27-Oct-26		
Office.L1.Rest.410	Office - L1 - RR - Pull & Terminate Wires	10	27-Oct-26	09-Nov-26		
Office.L1.Rest.500	Office - L1 - RR - Fire Sprinkler Trim-out	3	28-Oct-26	30-Oct-26		
Office.L1.Rest.490	Office - L1 - RR - Install Security Devices (By Others)	1	28-Oct-26	28-Oct-26		
Office.L1.Rest.580	Office - L1 - RR - Install Lighting	5	28-Oct-26	03-Nov-26		
Office.L1.Rest.170	Office - L1 - RR - Install Flooring	5	28-Oct-26	03-Nov-26		
Office.L1.Rest.400	Office - L1 - RR - Install Doors & Hardware	2	29-Oct-26	30-Oct-26		
Office.L1.Rest.590	Office - L1 - RR - Security Trim-out (By Others)	1	29-Oct-26	29-Oct-26		
Office.L1.Rest.570	Office - L1 - RR - Install Millwork	5	04-Nov-26	10-Nov-26		
Office.L1.Rest.550	Office - L1 - RR - Install Parititions	5	10-Nov-26	16-Nov-26		
Office.L1.Rest.520	Office - L1 - RR - Fire Alarm Trim-out	5	10-Nov-26	16-Nov-26		
Office.L1.Rest.510	Office - L1 - RR - Electrical Trim-out	5	11-Nov-26	17-Nov-26		

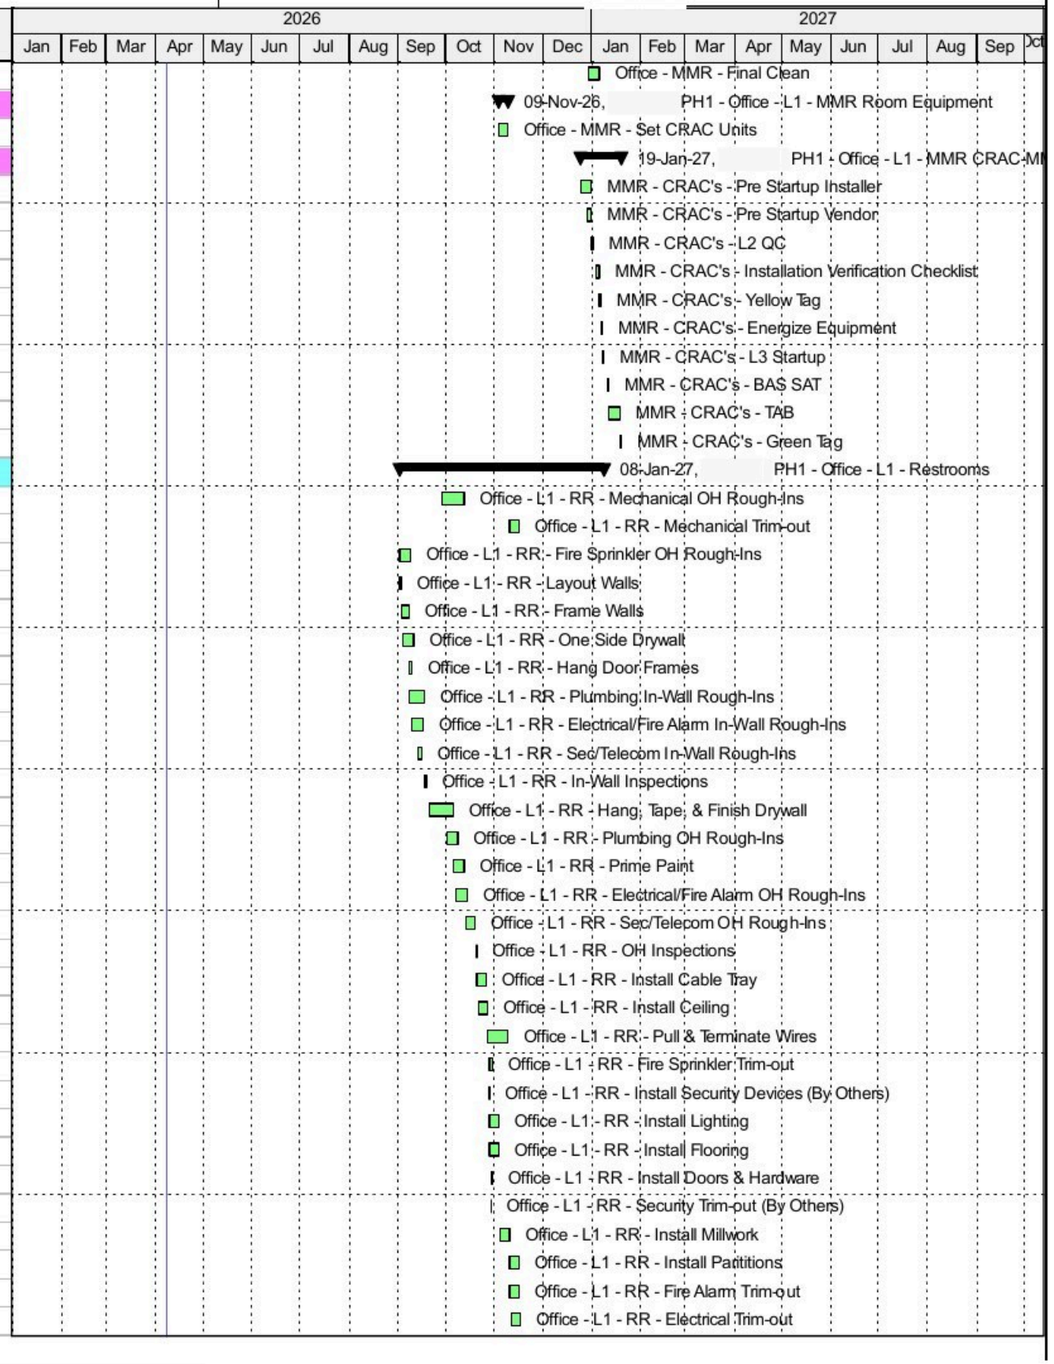


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Office.L1.Rest.575	Office - L1 - RR - Install Plumbing Fixtures	10	11-Nov-26	24-Nov-26		
Office.L1.Rest.620	Office - L1 - RR - Install Restroom Accessories	5	17-Nov-26	23-Nov-26		
Office.L1.Rest.560	Office - L1 - RR - Plumbing Trim-Out	5	25-Nov-26	01-Dec-26		
Office.L1.Rest.600	Office - L1 - RR - Final Paint	5	02-Dec-26	08-Dec-26		
Office.L1.Rest.610	Office - L1 - RR - Install Signage	2	09-Dec-26	10-Dec-26		
Office.L1.Rest.680	Office - L1 - RR - Punchlist	10	11-Dec-26	25-Dec-26		
Office.L1.Rest.690	Office - L1 - RR - Final Clean	10	28-Dec-26	08-Jan-27		
PH1 - Office - L1 - Loading Dock		10	01-Oct-26	14-Oct-26		
Office.L1.Dock.100	Office - Loading Dock - Install Dock Levelers	5	01-Oct-26	07-Oct-26		
Office.L1.Dock.200	Office - Loading Dock - Install Dock Doors	5	08-Oct-26	14-Oct-26		
PH1 - Office - L1 - General Area (Remaining Rooms)		120	02-Sep-26	16-Feb-27		
Office.L1.IB.540	Office - Mechanical OH Rough-ins	10	16-Sep-26	30-Sep-26	Trade	Mechanical
Office.L1.IB.130	Office - Mechanical Trim-out	5	13-Jan-27	21-Jan-27	Trade	Mechanical
Office.L1.IB.520	Office - Fire Sprinkler OH Rough-ins	10	02-Sep-26	15-Sep-26		
Office.L1.IB.110	Office - Layout & Frame Walls	10	09-Sep-26	22-Sep-26		
Office.L1.IB.260	Office - One-Side Drywall	10	23-Sep-26	07-Oct-26		
Office.L1.IB.490	Office - Electrical In- Wall Rough-ins	5	23-Sep-26	30-Sep-26		
Office.L1.IB.500	Office - Mechanical In-Wall Rough-ins	5	23-Sep-26	30-Sep-26		
Office.L1.IB.510	Office - Plumbing In-wall Rough-Ins	5	23-Sep-26	30-Sep-26		
Office.L1.IB.530	Office - Electrical OH Rough-ins	10	23-Sep-26	07-Oct-26		
Office.L1.IB.580	Office - Hang Door Frames	5	23-Sep-26	30-Sep-26		
Office.L1.IB.240	Office - In-Wall Inspection	1	01-Oct-26	01-Oct-26		
Office.L1.IB.140	Office - Hang, Tape, & Finish Drywall	15	08-Oct-26	28-Oct-26		
Office.L1.IB.250	Office - OH Inspection	1	08-Oct-26	08-Oct-26		
Office.L1.IB.150	Office - Prime Paint	5	26-Oct-26	30-Oct-26		
Office.L1.IB.480	Office - Set Exhaust Fans	5	03-Nov-26	09-Nov-26		
Office.L1.IB.200	Office - Install Ceiling System	5	10-Nov-26	16-Nov-26		
Office.L1.IB.170	Office - Install Cable Tray	10	17-Nov-26	30-Nov-26		
Office.L1.IB.220	Office - Pull & Terminate Wires	15	01-Dec-26	22-Dec-26		
Office.L1.IB.160	Office - Install Flooring & Base	5	23-Dec-26	29-Dec-26		
Office.L1.IB.180	Office - Install Millwork	5	30-Dec-26	05-Jan-27		
Office.L1.IB.190	Office - Install Lockers	5	06-Jan-27	12-Jan-27		
Office.L1.IB.270	Office - Install Security Devices (By Others)	5	13-Jan-27	21-Jan-27		
Office.L1.IB.120	Office - Electrical Trim-out	5	13-Jan-27	21-Jan-27		
Office.L1.IB.560	Office - F/A Trim-out	5	13-Jan-27	21-Jan-27		
Office.L1.IB.280	Office - Final Clean / Punch	5	10-Feb-27	16-Feb-27		
PH1 - Office - Level M1 (Mezzanine)		122	02-Sep-26	18-Feb-27		
PH1 - Office - M1 - Elevator and Stair 03 Tower		45	01-Oct-26	02-Dec-26		
Office.M1.ELVST.330	Office - M1 - ELV & ST03 Tower - Mechanical OH Rough-Ins	1	12-Oct-26	12-Oct-26	Trade	Mechanical
Office.M1.ELVST.530	Office - M1 - ELV & ST03 Tower - Mechanical Trim-out	2	03-Nov-26	04-Nov-26	Trade	Mechanical
Office.M1.ELVST.100	Office - M1 - ELV & ST03 Tower - Layout Walls	1	01-Oct-26	01-Oct-26		
Office.M1.ELVST.110	Office - M1 - ELV & ST03 Tower - Frame Walls	2	02-Oct-26	05-Oct-26		
Office.M1.ELVST.200	Office - M1 - ELV & ST03 Tower - Electrical/Fire Alarm In-Wall Rough-	3	06-Oct-26	08-Oct-26		
Office.M1.ELVST.210	Office - M1 - ELV & ST03 Tower - Sec/Telecom In-Wall Rough-Ins	3	06-Oct-26	08-Oct-26		
Office.M1.ELVST.300	Office - M1 - ELV & ST03 Tower - Fire Sprinkler OH Rough-Ins	2	08-Oct-26	09-Oct-26		

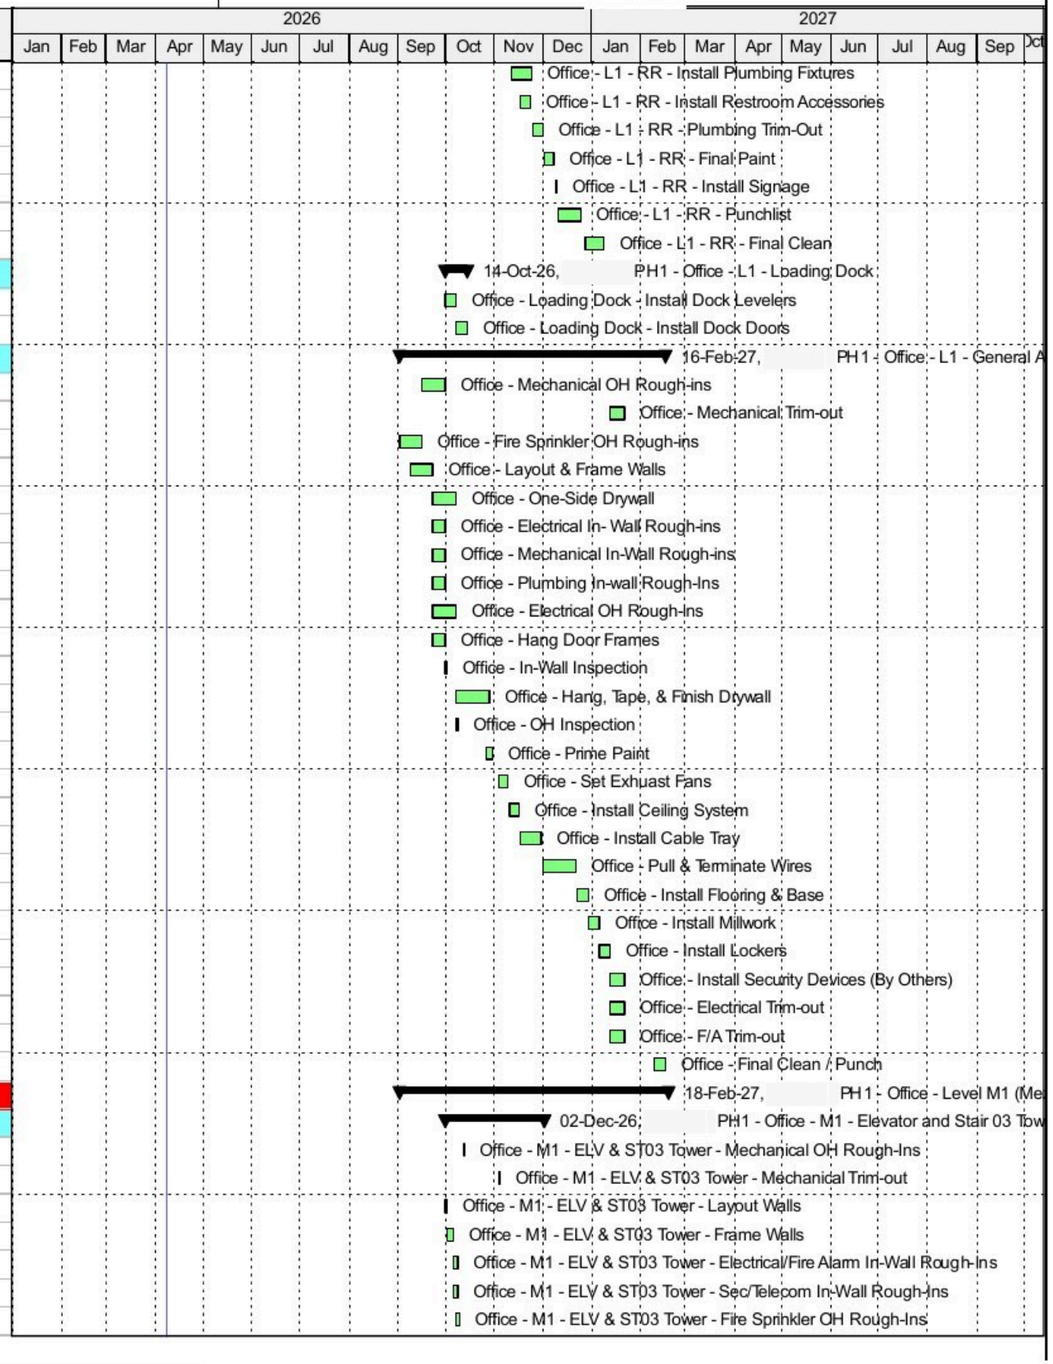


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Office.M1.ELVST.310	Office - M1 - ELV & ST03 Tower - Electrical/Fire Alarm OH Rough-Ins	3	13-Oct-26	15-Oct-26		
Office.M1.ELVST.320	Office - M1 - ELV & ST03 Tower - Sec/Telecom OH Rough-Ins	3	13-Oct-26	15-Oct-26		
Office.M1.ELVST.120	Office - M1 - ELV & ST03 Tower - One Side Drywall	2	14-Oct-26	15-Oct-26		
Office.M1.ELVST.130	Office - M1 - ELV & ST03 Tower - Hang Door Frames	1	16-Oct-26	16-Oct-26		
Office.M1.ELVST.290	Office - M1 - ELV & ST03 Tower - In-Wall Inspections	1	16-Oct-26	16-Oct-26		
Office.M1.ELVST.390	Office - M1 - ELV & ST03 Tower - OH Inspections	1	16-Oct-26	16-Oct-26		
Office.M1.ELVST.140	Office - M1 - ELV & ST03 Tower - Hang, Tape, & Finish Drywall	3	20-Oct-26	22-Oct-26		
Office.M1.ELVST.160	Office - M1 - ELV & ST03 Tower - Prime Paint	2	23-Oct-26	26-Oct-26		
Office.M1.ELVST.500	Office - M1 - ELV & ST03 Tower - Fire Sprinkler Trim-out	2	27-Oct-26	28-Oct-26		
Office.M1.ELVST.490	Office - M1 - ELV & ST03 Tower - Install Security Devices (By Others)	5	27-Oct-26	02-Nov-26		
Office.M1.ELVST.410	Office - M1 - ELV & ST03 Tower - Pull & Terminate Wires	5	27-Oct-26	02-Nov-26		
Office.M1.ELVST.580	Office - M1 - ELV & ST03 Tower - Install Lighting	2	27-Oct-26	28-Oct-26		
Office.M1.ELVST.400	Office - M1 - ELV & ST03 Tower - Install Doors & Hardware	1	30-Oct-26	30-Oct-26		
Office.M1.ELVST.510	Office - M1 - ELV & ST03 Tower - Electrical Trim-out	2	03-Nov-26	04-Nov-26		
Office.M1.ELVST.520	Office - M1 - ELV & ST03 Tower - Fire Alarm Trim-out	2	03-Nov-26	04-Nov-26		
Office.M1.ELVST.590	Office - M1 - ELV & ST03 Tower - Security Trim-out (By Others)	5	03-Nov-26	09-Nov-26		
Office.M1.ELVST.600	Office - M1 - ELV & ST03 Tower - Final Paint	5	10-Nov-26	16-Nov-26		
Office.M1.ELVST.610	Office - M1 - ELV & ST03 Tower - Install Signage	2	17-Nov-26	18-Nov-26		
Office.M1.ELVST.680	Office - M1 - ELV & ST03 Tower - Punchlist	5	19-Nov-26	25-Nov-26		
Office.M1.ELVST.690	Office - M1 - ELV & ST03 Tower - Final Clean	5	26-Nov-26	02-Dec-26		
PH1 - Office - M1 - Stairs 01 & 02		40	01-Oct-26	25-Nov-26		
Office.M1.STR.330	Office - M1 - ST01&02 - Mechanical OH Rough-Ins	1	05-Oct-26	05-Oct-26	Trade	Mechanical
Office.M1.STR.530	Office - M1 - ST01&02 - Mechanical Trim-out	2	26-Oct-26	27-Oct-26	Trade	Mechanical
Office.M1.STR.300	Office - M1 - ST01&02 - Fire Sprinkler OH Rough-Ins	2	01-Oct-26	02-Oct-26		
Office.M1.STR.100	Office - M1 - ST01&02 - Layout Walls	1	01-Oct-26	01-Oct-26		
Office.M1.STR.110	Office - M1 - ST01&02 - Frame Walls	2	02-Oct-26	05-Oct-26		
Office.M1.STR.310	Office - M1 - ST01&02 - Electrical/Fire Alarm OH Rough-Ins	3	05-Oct-26	07-Oct-26		
Office.M1.STR.320	Office - M1 - ST01&02 - Sec/Telecom OH Rough-Ins	3	05-Oct-26	07-Oct-26		
Office.M1.STR.120	Office - M1 - ST01&02 - One Side Drywall	2	06-Oct-26	07-Oct-26		
Office.M1.STR.200	Office - M1 - ST01&02 - Electrical/Fire Alarm In-Wall Rough-Ins	3	06-Oct-26	08-Oct-26		
Office.M1.STR.210	Office - M1 - ST01&02 - Sec/Telecom In-Wall Rough-Ins	3	06-Oct-26	08-Oct-26		
Office.M1.STR.130	Office - M1 - ST01&02 - Hang Door Frames	1	08-Oct-26	08-Oct-26		
Office.M1.STR.390	Office - M1 - ST01&02 - OH Inspections	1	08-Oct-26	08-Oct-26		
Office.M1.STR.290	Office - M1 - ST01&02 - In-Wall Inspections	1	09-Oct-26	09-Oct-26		
Office.M1.STR.140	Office - M1 - ST01&02 - Hang, Tape, & Finish Drywall	3	12-Oct-26	14-Oct-26		
Office.M1.STR.160	Office - M1 - ST01&02 - Prime Paint	2	15-Oct-26	16-Oct-26		
Office.M1.STR.500	Office - M1 - ST01&02 - Fire Sprinkler Trim-out	2	19-Oct-26	20-Oct-26		
Office.M1.STR.490	Office - M1 - ST01&02 - Install Security Devices (By Others)	5	19-Oct-26	23-Oct-26		
Office.M1.STR.410	Office - M1 - ST01&02 - Pull & Terminate Wires	5	19-Oct-26	23-Oct-26		
Office.M1.STR.580	Office - M1 - ST01&02 - Install Lighting	2	19-Oct-26	20-Oct-26		
Office.M1.STR.510	Office - M1 - ST01&02 - Electrical Trim-out	2	26-Oct-26	27-Oct-26		
Office.M1.STR.520	Office - M1 - ST01&02 - Fire Alarm Trim-out	2	26-Oct-26	27-Oct-26		
Office.M1.STR.590	Office - M1 - ST01&02 - Security Trim-out (By Others)	5	26-Oct-26	30-Oct-26		
Office.M1.STR.400	Office - M1 - ST01&02 - Install Doors & Hardware	1	30-Oct-26	30-Oct-26		
Office.M1.STR.600	Office - M1 - ST01&02 - Final Paint	5	02-Nov-26	06-Nov-26		

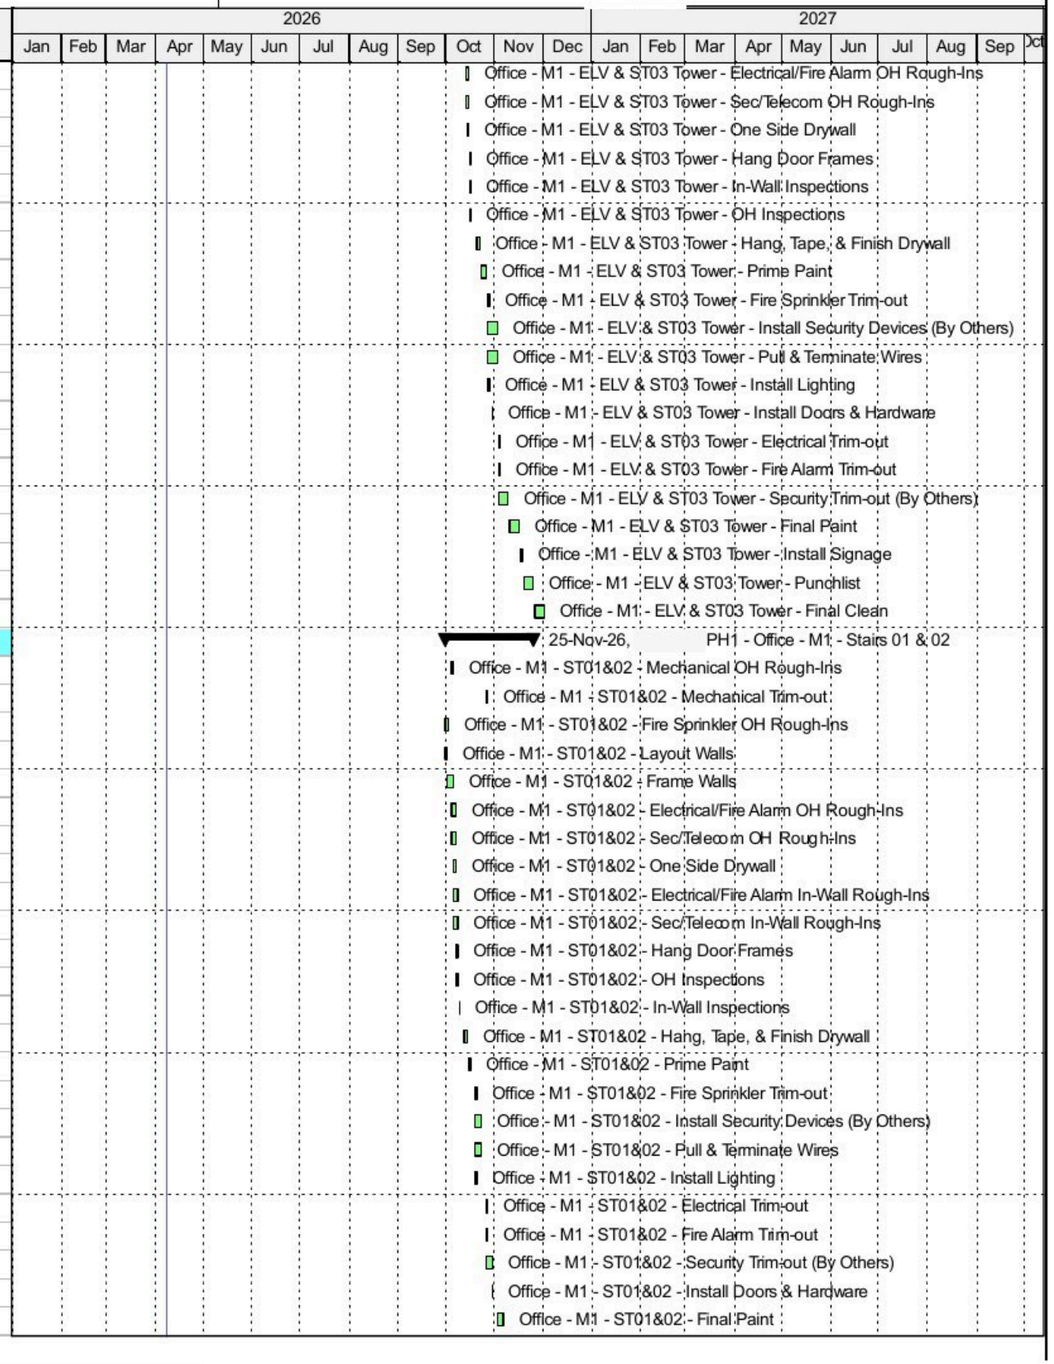


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Office.M1.STR.610	Office - M1 - ST01&02 - Install Signage	2	10-Nov-26	11-Nov-26		
Office.M1.STR.680	Office - M1 - ST01&02 - Punchlist	5	12-Nov-26	18-Nov-26		
Office.M1.STR.690	Office - M1 - ST01&02 - Final Clean	5	19-Nov-26	25-Nov-26		
PH1 - Office - M1 - MDF & Electrical Room		107	02-Sep-26	28-Jan-27		
Office.M1.MDF.ER.330	Office - M1 - MDF & ER - Mechanical OH Rough-Ins	4	04-Sep-26	09-Sep-26	Trade	Mechanical
Office.M1.MDF.ER.530	Office - M1 - MDF & ER - Mechanical Trim-out	2	18-Dec-26	21-Dec-26	Trade	Mechanical
Office.M1.MDF.ER.300	Office - M1 - MDF & ER - Fire Sprinkler OH Rough-Ins	2	02-Sep-26	03-Sep-26		
Office.M1.MDF.ER.100	Office - M1 - MDF & ER - Layout Walls	1	02-Sep-26	02-Sep-26		
Office.M1.MDF.ER.110	Office - M1 - MDF & ER - Frame Walls	2	03-Sep-26	04-Sep-26		
Office.M1.MDF.ER.120	Office - M1 - MDF & ER - One Side Drywall	2	07-Sep-26	08-Sep-26		
Office.M1.MDF.ER.200	Office - M1 - MDF & ER - Electrical/Fire Alarm In-Wall Rough-Ins	5	07-Sep-26	11-Sep-26		
Office.M1.MDF.ER.340	Office - M1 - MDF & ER - Plumbing OH Rough-Ins	3	07-Sep-26	09-Sep-26		
Office.M1.MDF.ER.130	Office - M1 - MDF & ER - Hang Door Frames	1	09-Sep-26	09-Sep-26		
Office.M1.MDF.ER.210	Office - M1 - MDF & ER - Sec/Telecom In-Wall Rough-Ins	5	09-Sep-26	15-Sep-26		
Office.M1.MDF.ER.310	Office - M1 - MDF & ER - Electrical/Fire Alarm OH Rough-Ins	10	10-Sep-26	23-Sep-26		
Office.M1.MDF.ER.320	Office - M1 - MDF & ER - Sec/Telecom OH Rough-Ins	10	14-Sep-26	25-Sep-26		
Office.M1.MDF.ER.290	Office - M1 - MDF & ER - In-Wall Inspections	1	16-Sep-26	16-Sep-26		
Office.M1.MDF.ER.140	Office - M1 - MDF & ER - Hang, Tape, & Finish Drywall	3	17-Sep-26	21-Sep-26		
Office.M1.MDF.ER.160	Office - M1 - MDF & ER - Prime Paint	2	22-Sep-26	23-Sep-26		
Office.M1.MDF.ER.500	Office - M1 - MDF & ER - Fire Sprinkler Trim-out	1	24-Sep-26	24-Sep-26		
Office.M1.MDF.ER.390	Office - M1 - MDF & ER - OH Inspections	1	29-Sep-26	29-Sep-26		
Office.M1.MDF.ER.490	Office - M1 - MDF & ER - Install Security Devices (By Others)	5	29-Sep-26	05-Oct-26		
Office.M1.MDF.ER.580	Office - M1 - MDF & ER - Install Lighting	2	30-Sep-26	01-Oct-26		
Office.M1.MDF.ER.350	Office - M1 - MDF & ER - Install Cable Tray	7	30-Sep-26	08-Oct-26		
Office.M1.MDF.ER.590	Office - M1 - MDF & ER - Security Trim-out (By Others)	5	06-Oct-26	12-Oct-26		
Office.M1.MDF.ER.170	Office - M1 - MDF & ER - Install Flooring	3	09-Oct-26	13-Oct-26		
Office.M1.MDF.ER.400	Office - M1 - MDF & ER - Install Doors & Hardware	1	29-Oct-26	29-Oct-26		
Office.M1.MDF.ER.410	Office - M1 - MDF & ER - Pull & Terminate Wires	15	26-Nov-26	16-Dec-26		
Office.M1.MDF.ER.510	Office - M1 - MDF & ER - Electrical Trim-out	5	18-Dec-26	24-Dec-26		
Office.M1.MDF.ER.520	Office - M1 - MDF & ER - Fire Alarm Trim-out	3	18-Dec-26	22-Dec-26		
Office.M1.MDF.ER.600	Office - M1 - MDF & ER - Final Paint	5	25-Dec-26	31-Dec-26		
Office.M1.MDF.ER.610	Office - M1 - MDF & ER - Install Signage	2	01-Jan-27	04-Jan-27		
Office.M1.MDF.ER.680	Office - M1 - MDF & ER - Punchlist	10	05-Jan-27	20-Jan-27		
Office.M1.MDF.ER.690	Office - M1 - MDF & ER - Final Clean	5	21-Jan-27	28-Jan-27		
PH1 - Office - M1 - MDF & Electrical Room Equipment		5	12-Nov-26	18-Nov-26		
Office.M1.MDF.200	Office - M1 - MDF & ER - Install ICU	5	12-Nov-26	18-Nov-26	Trade	HVAC
Office.M1.MDF.210	Office - M1 - MDF & ER - Install ISU	5	12-Nov-26	18-Nov-26	Trade	HVAC
Office.M1.MDF.220	Office - M1 - MDF & ER - Instal OPP-XFMR (OFCI)	5	12-Nov-26	18-Nov-26		
Office.M1.MDF.230	Office - M1 - MDF & ER - Install OPP (OFCI)	5	12-Nov-26	18-Nov-26		
Office.M1.MDF.240	Office - M1 - MDF & ER - Install OLP (OFCI)	5	12-Nov-26	18-Nov-26		
PH1 - Office - M1 - MDF & ER Comissioning		16	18-Dec-26	08-Jan-27		
MDF ROOM - ICU-07 & ICU - 08		16	18-Dec-26	08-Jan-27		
Cx.Off.MDF-ICU.100	Office MDF Room - ICU's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.Off.MDF-ICU.110	Office MDF Room - ICU's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.Off.MDF-ICU.120	Office MDF Room - ICU's - L2 QC	1	25-Dec-26	25-Dec-26		

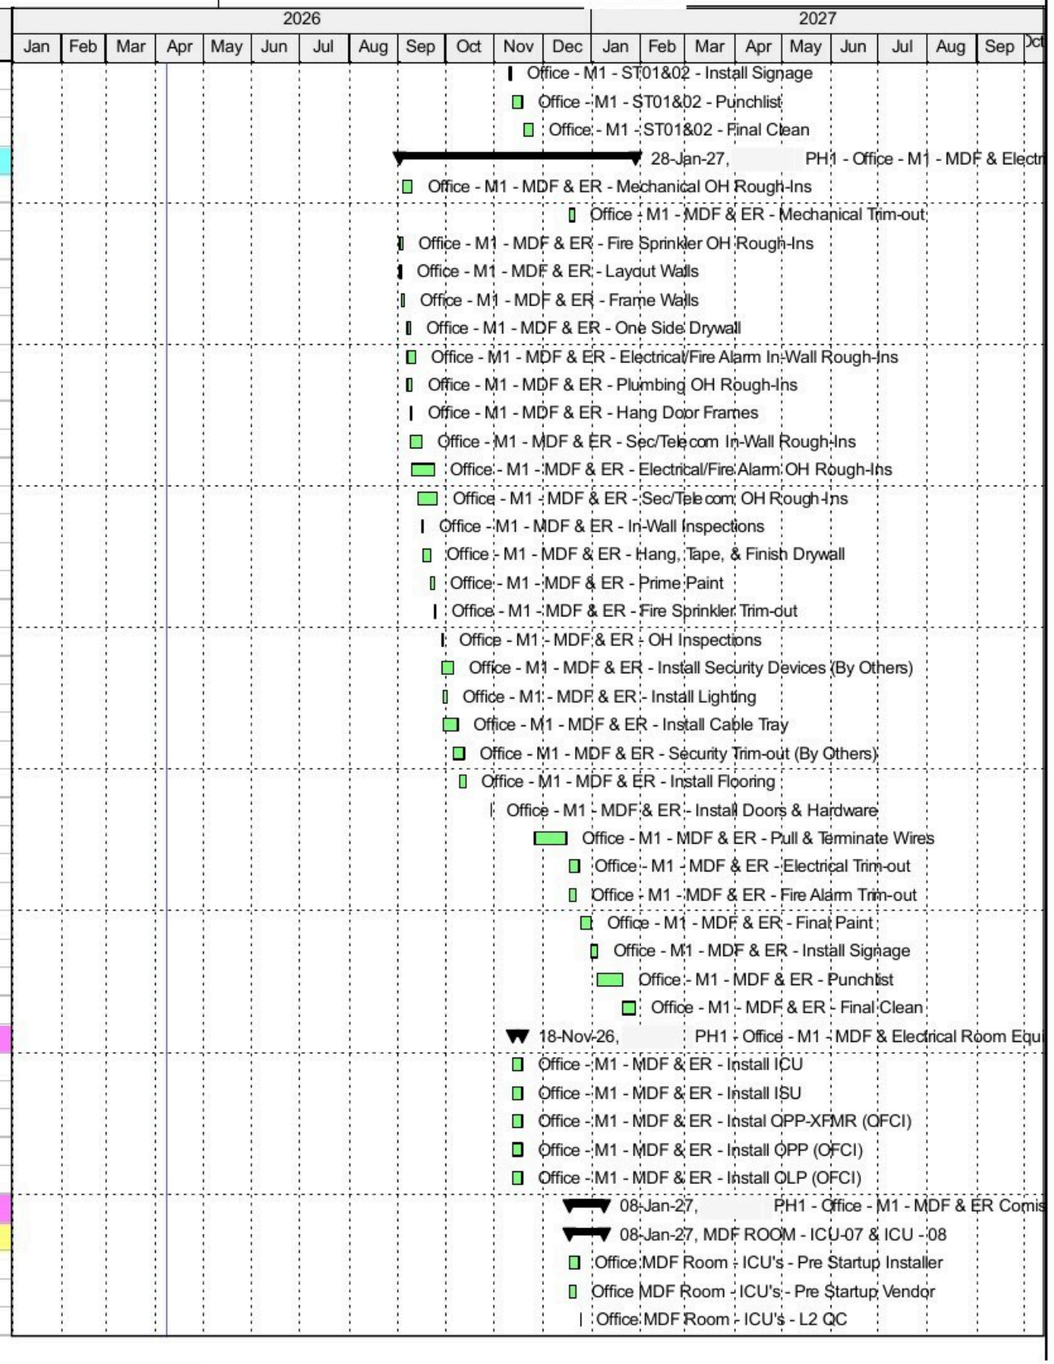


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE | CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.Off.MDF-ICU.130	Office MDF Room - ICU's - Installation Verification Checklist	1	28-Dec-26	28-Dec-26		
Cx.Off.MDF-ICU.140	Office MDF Room - ICU's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.Off.MDF-ICU.150	Office MDF Room - ICU's - Energize Equipment	1	30-Dec-26	30-Dec-26		
Cx.Off.MDF-ICU.160	Office MDF Room - ICU's - L3 Startup	4	31-Dec-26	05-Jan-27		
Cx.Off.MDF-ICU.170	Office MDF Room - ICU's - EPMS SAT	1	06-Jan-27	06-Jan-27		
Cx.Off.MDF-ICU.180	Office MDF Room - ICU's - Thermographic Checks	1	07-Jan-27	07-Jan-27		
Cx.Off.MDF-ICU.190	Office MDF Room - ICU's - Green Tag	1	08-Jan-27	08-Jan-27		
PH1 - Office - M1 - East Rooms (M1.527/ M1.526/M1.523/M1.515 /M1.516/M1.517)		80	01-Oct-26	20-Jan-27		
Office.M1.ESTRM.330	Office - M1 - East Rooms - Mechanical OH Rough-Ins	10	06-Oct-26	19-Oct-26	Trade	Mechanical
Office.M1.ESTRM.530	Office - M1 - East Rooms - Mechanical Trim-out	5	26-Nov-26	02-Dec-26	Trade	Mechanical
Office.M1.ESTRM.300	Office - M1 - East Rooms - Fire Sprinkler OH Rough-Ins	3	01-Oct-26	05-Oct-26		
Office.M1.ESTRM.100	Office - M1 - East Rooms - Layout Walls	2	01-Oct-26	02-Oct-26		
Office.M1.ESTRM.110	Office - M1 - East Rooms - Frame Walls	5	05-Oct-26	09-Oct-26		
Office.M1.ESTRM.120	Office - M1 - East Rooms - One Side Drywall	5	12-Oct-26	16-Oct-26		
Office.M1.ESTRM.200	Office - M1 - East Rooms - Electrical/Fire Alarm In-Wall Rough-Ins	5	12-Oct-26	16-Oct-26		
Office.M1.ESTRM.180	Office - M1 - East Rooms - Install Exterior Windows	5	12-Oct-26	16-Oct-26		
Office.M1.ESTRM.220	Office - M1 - East Rooms - Plumbing In-Wall Rough-In	5	13-Oct-26	19-Oct-26		
Office.M1.ESTRM.210	Office - M1 - East Rooms - Sec/Telecom In-Wall Rough-Ins	5	14-Oct-26	20-Oct-26		
Office.M1.ESTRM.130	Office - M1 - East Rooms - Hang Door Frames	3	19-Oct-26	21-Oct-26		
Office.M1.ESTRM.310	Office - M1 - East Rooms - Electrical/Fire Alarm OH Rough-Ins	10	20-Oct-26	02-Nov-26		
Office.M1.ESTRM.290	Office - M1 - East Rooms - In-Wall Inspections	1	21-Oct-26	21-Oct-26		
Office.M1.ESTRM.140	Office - M1 - East Rooms - Hang, Tape, & Finish Drywall	10	22-Oct-26	04-Nov-26		
Office.M1.ESTRM.320	Office - M1 - East Rooms - Sec/Telecom OH Rough-Ins	10	22-Oct-26	04-Nov-26		
Office.M1.ESTRM.160	Office - M1 - East Rooms - Prime Paint	5	05-Nov-26	11-Nov-26		
Office.M1.ESTRM.390	Office - M1 - East Rooms - OH Inspections	1	05-Nov-26	05-Nov-26		
Office.M1.ESTRM.400	Office - M1 - East Rooms - Install Doors & Hardware	3	06-Nov-26	10-Nov-26		
Office.M1.ESTRM.410	Office - M1 - East Rooms - Pull & Terminate Wires	10	12-Nov-26	25-Nov-26		
Office.M1.ESTRM.190	Office - M1 - East Rooms - Install Ceiling	5	12-Nov-26	18-Nov-26		
Office.M1.ESTRM.500	Office - M1 - East Rooms - Fire Sprinkler Trim-out	3	19-Nov-26	23-Nov-26		
Office.M1.ESTRM.490	Office - M1 - East Rooms - Install Security Devices (By Others)	5	19-Nov-26	25-Nov-26		
Office.M1.ESTRM.580	Office - M1 - East Rooms - Install Lighting	5	19-Nov-26	25-Nov-26		
Office.M1.ESTRM.170	Office - M1 - East Rooms - Install Flooring	5	19-Nov-26	25-Nov-26		
Office.M1.ESTRM.510	Office - M1 - East Rooms - Electrical Trim-out	5	26-Nov-26	02-Dec-26		
Office.M1.ESTRM.520	Office - M1 - East Rooms - Fire Alarm Trim-out	5	26-Nov-26	02-Dec-26		
Office.M1.ESTRM.590	Office - M1 - East Rooms - Security Trim-out (By Others)	5	26-Nov-26	02-Dec-26		
Office.M1.ESTRM.570	Office - M1 - East Rooms - Install Millwork	5	26-Nov-26	02-Dec-26		
Office.M1.ESTRM.630	Office - M1 - East Rooms - Install Furniture	5	03-Dec-26	09-Dec-26		
Office.M1.ESTRM.575	Office - M1 - East Rooms - Install Plumbing Fixtures	2	03-Dec-26	04-Dec-26		
Office.M1.ESTRM.620	Office - M1 - East Rooms - Install Appliances	3	07-Dec-26	09-Dec-26		
Office.M1.ESTRM.550	Office - M1 - East Rooms - Install Window Treatments	2	10-Dec-26	11-Dec-26		
Office.M1.ESTRM.540	Office - M1 - East Rooms - Install FECs	2	15-Dec-26	16-Dec-26		
Office.M1.ESTRM.600	Office - M1 - East Rooms - Final Paint	5	18-Dec-26	24-Dec-26		
Office.M1.ESTRM.610	Office - M1 - East Rooms - Install Signage	2	25-Dec-26	28-Dec-26		
Office.M1.ESTRM.680	Office - M1 - East Rooms - Punchlist	10	29-Dec-26	11-Jan-27		
Office.M1.ESTRM.690	Office - M1 - East Rooms - Final Clean	5	12-Jan-27	20-Jan-27		

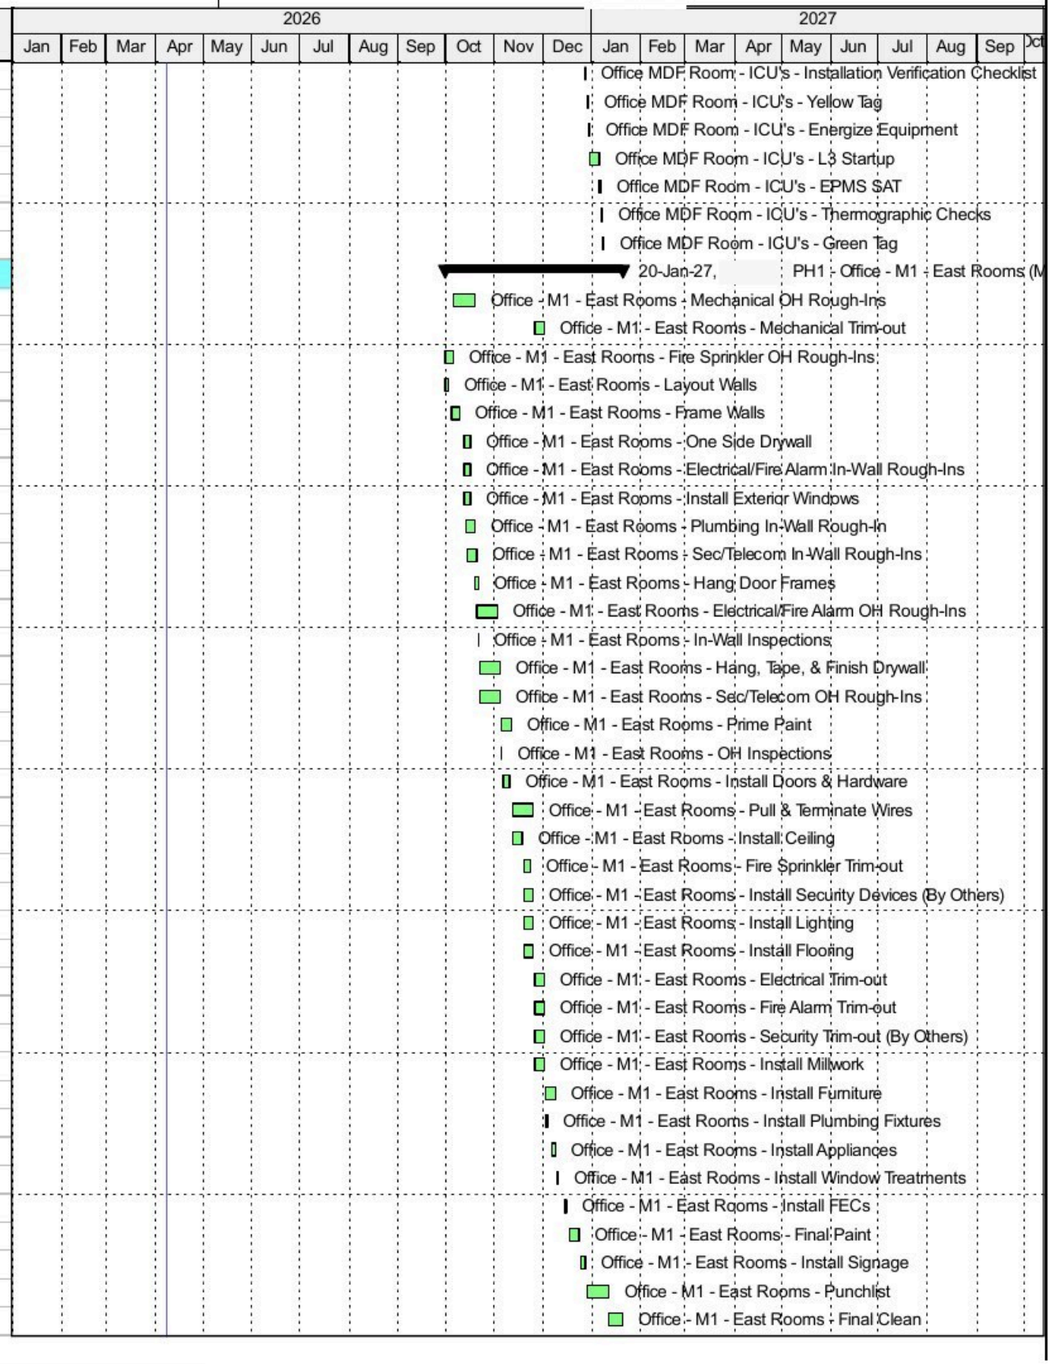


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH1 - Office - M1 - Restrooms		80	01-Oct-26	20-Jan-27		
Office.M1.Rest.330	Office - M1 - RR - Mechanical OH Rough-Ins	10	08-Oct-26	21-Oct-26	Trade	Mechanical
Office.M1.Rest.530	Office - M1 - RR - Mechanical Trim-out	5	25-Nov-26	01-Dec-26	Trade	Mechanical
Office.M1.Rest.300	Office - M1 - RR - Fire Sprinkler OH Rough-Ins	5	01-Oct-26	07-Oct-26		
Office.M1.Rest.100	Office - M1 - RR - Layout Walls	1	01-Oct-26	01-Oct-26		
Office.M1.Rest.110	Office - M1 - RR - Frame Walls	3	02-Oct-26	06-Oct-26		
Office.M1.Rest.120	Office - M1 - RR - One Side Drywall	5	07-Oct-26	13-Oct-26		
Office.M1.Rest.200	Office - M1 - RR - Electrical/Fire Alarm In-Wall Rough-Ins	5	07-Oct-26	13-Oct-26		
Office.M1.Rest.220	Office - M1 - RR - Plumbing In-Wall Rough-Ins	8	08-Oct-26	19-Oct-26		
Office.M1.Rest.210	Office - M1 - RR - Sec/Telecom In-Wall Rough-Ins	3	09-Oct-26	13-Oct-26		
Office.M1.Rest.340	Office - M1 - RR - Plumbing OH Rough-Ins	5	13-Oct-26	19-Oct-26		
Office.M1.Rest.130	Office - M1 - RR - Hang Door Frames	2	14-Oct-26	15-Oct-26		
Office.M1.Rest.290	Office - M1 - RR - In-Wall Inspections	1	20-Oct-26	20-Oct-26		
Office.M1.Rest.140	Office - M1 - RR - Hang, Tape, & Finish Drywall	10	21-Oct-26	03-Nov-26		
Office.M1.Rest.310	Office - M1 - RR - Electrical/Fire Alarm OH Rough-Ins	5	22-Oct-26	28-Oct-26		
Office.M1.Rest.320	Office - M1 - RR - Sec/Telecom OH Rough-Ins	5	26-Oct-26	30-Oct-26		
Office.M1.Rest.390	Office - M1 - RR - OH Inspections	1	02-Nov-26	02-Nov-26		
Office.M1.Rest.160	Office - M1 - RR - Prime Paint	5	04-Nov-26	10-Nov-26		
Office.M1.Rest.400	Office - M1 - RR - Install Doors & Hardware	2	04-Nov-26	05-Nov-26		
Office.M1.Rest.410	Office - M1 - RR - Pull & Terminate Wires	10	11-Nov-26	24-Nov-26		
Office.M1.Rest.190	Office - M1 - RR - Install Ceiling	5	11-Nov-26	17-Nov-26		
Office.M1.Rest.500	Office - M1 - RR - Fire Sprinkler Trim-out	3	18-Nov-26	20-Nov-26		
Office.M1.Rest.490	Office - M1 - RR - Install Security Devices (By Others)	2	18-Nov-26	19-Nov-26		
Office.M1.Rest.580	Office - M1 - RR - Install Lighting	5	18-Nov-26	24-Nov-26		
Office.M1.Rest.170	Office - M1 - RR - Install Flooring	5	18-Nov-26	24-Nov-26		
Office.M1.Rest.590	Office - M1 - RR - Security Trim-out (By Others)	2	20-Nov-26	23-Nov-26		
Office.M1.Rest.550	Office - M1 - RR - Install Paritions	5	25-Nov-26	01-Dec-26		
Office.M1.Rest.520	Office - M1 - RR - Fire Alarm Trim-out	5	25-Nov-26	01-Dec-26		
Office.M1.Rest.570	Office - M1 - RR - Install Millwork	5	25-Nov-26	01-Dec-26		
Office.M1.Rest.620	Office - M1 - RR - Install Restroom Accessories	5	02-Dec-26	08-Dec-26		
Office.M1.Rest.510	Office - M1 - RR - Electrical Trim-out	5	02-Dec-26	08-Dec-26		
Office.M1.Rest.575	Office - M1 - RR - Install Plumbing Fixtures	5	02-Dec-26	08-Dec-26		
Office.M1.Rest.560	Office - M1 - RR - Plumbing Trim-Out	5	09-Dec-26	15-Dec-26		
Office.M1.Rest.540	Office - M1 - RR - Install FECs	2	15-Dec-26	16-Dec-26		
Office.M1.Rest.600	Office - M1 - RR - Final Paint	5	18-Dec-26	24-Dec-26		
Office.M1.Rest.610	Office - M1 - RR - Install Signage	2	25-Dec-26	28-Dec-26		
Office.M1.Rest.680	Office - M1 - RR - Punchlist	10	29-Dec-26	11-Jan-27		
Office.M1.Rest.690	Office - M1 - RR - Final Clean	5	12-Jan-27	20-Jan-27		
PH1 - Office - M1 - General Area (Remaining Rooms)		122	02-Sep-26	18-Feb-27		
Office.M1.IB.330	Office - M1 - General - Mechanical OH Rough-Ins	15	11-Sep-26	02-Oct-26	Trade	Mechanical
Office.M1.IB.530	Office - M1 - General - Mechanical Trim-out	10	02-Dec-26	15-Dec-26	Trade	Mechanical
Office.M1.IB.300	Office - M1 - General - Fire Sprinkler OH Rough-Ins	7	02-Sep-26	10-Sep-26		
Office.M1.IB.100	Office - M1 - General - Layout Walls	4	02-Sep-26	07-Sep-26		
Office.M1.IB.110	Office - M1 - General - Frame Walls	10	04-Sep-26	17-Sep-26		
Office.M1.IB.200	Office - M1 - General - Electrical/Fire Alarm In-Wall Rough-Ins	10	09-Sep-26	22-Sep-26		

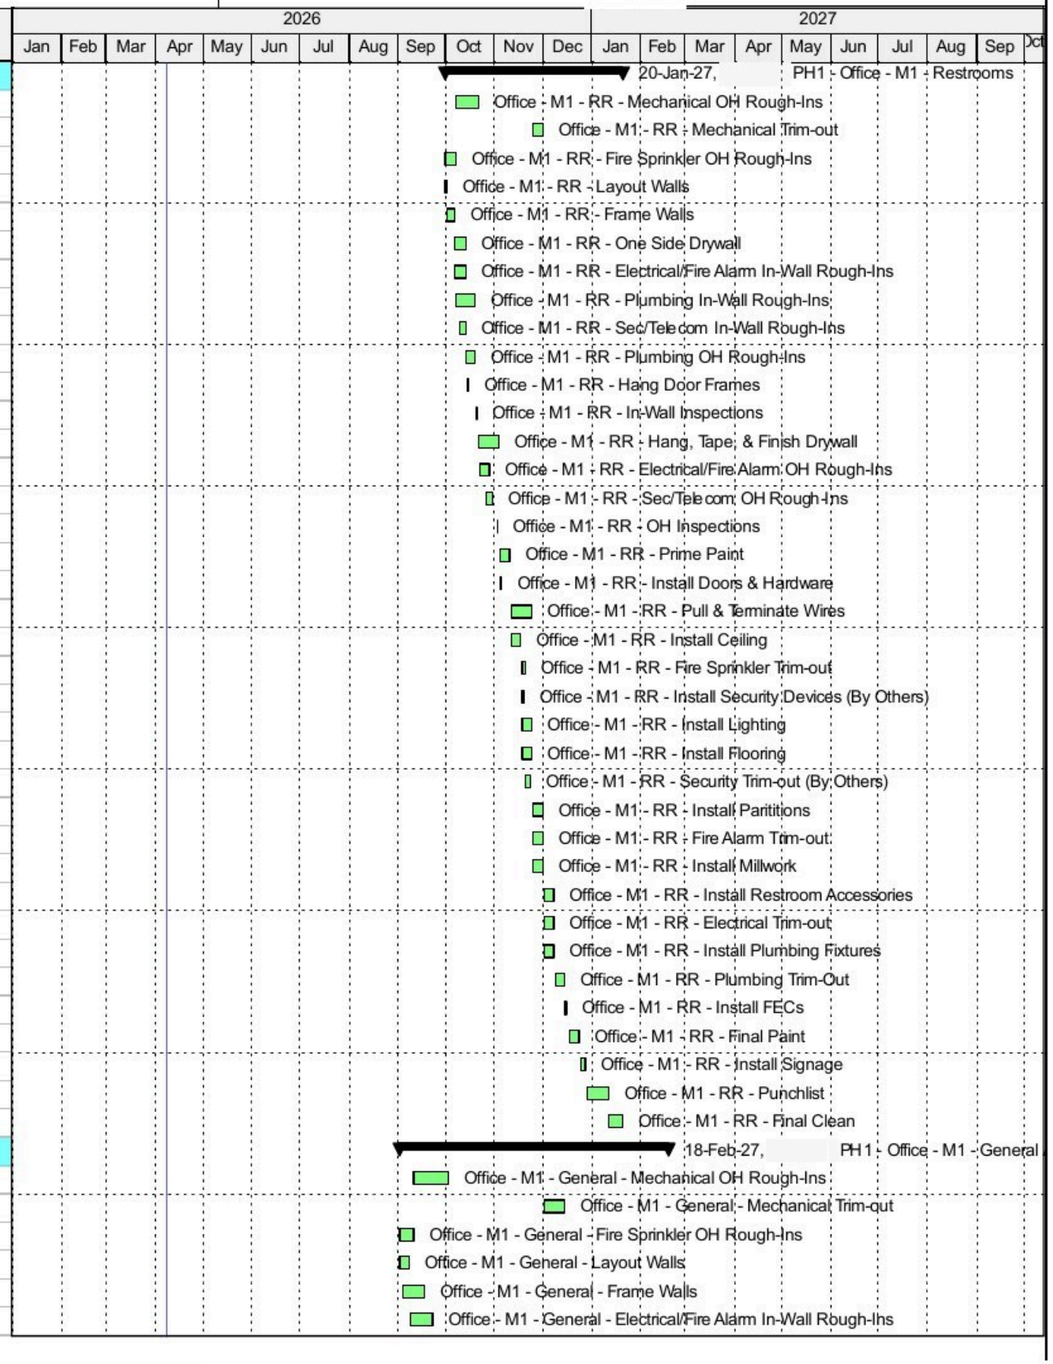


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Office.M1.IB.220	Office - M1 - General - Plumbing In-Wall Rough-In	5	10-Sep-26	16-Sep-26		
Office.M1.IB.120	Office - M1 - General - One Side Drywall	10	11-Sep-26	24-Sep-26		
Office.M1.IB.210	Office - M1 - General - Sec/Telecom In-Wall Rough-Ins	10	14-Sep-26	25-Sep-26		
Office.M1.IB.130	Office - M1 - General - Hang Door Frames	5	18-Sep-26	24-Sep-26		
Office.M1.IB.310	Office - M1 - General - Electrical/Fire Alarm OH Rough-Ins	15	18-Sep-26	09-Oct-26		
Office.M1.IB.320	Office - M1 - General - Sec/Telecom OH Rough-Ins	15	22-Sep-26	13-Oct-26		
Office.M1.IB.290	Office - M1 - General - In-Wall Inspections	1	29-Sep-26	29-Sep-26		
Office.M1.IB.140	Office - M1 - General - Hang, Tape, & Finish Drywall	15	30-Sep-26	20-Oct-26		
Office.M1.IB.160	Office - M1 - General - Prime Paint	10	14-Oct-26	27-Oct-26		
Office.M1.IB.390	Office - M1 - General - OH Inspections	1	14-Oct-26	14-Oct-26		
Office.M1.IB.190	Office - M1 - General - Install Ceiling	10	21-Oct-26	03-Nov-26		
Office.M1.IB.400	Office - M1 - General - Install Doors & Hardware	10	29-Oct-26	11-Nov-26		
Office.M1.IB.500	Office - M1 - General - Fire Sprinkler Trim-out	7	04-Nov-26	12-Nov-26		
Office.M1.IB.490	Office - M1 - General - Install Security Devices (By Others)	10	04-Nov-26	17-Nov-26		
Office.M1.IB.580	Office - M1 - General - Install Lighting	10	04-Nov-26	17-Nov-26		
Office.M1.IB.170	Office - M1 - General - Install Flooring	5	04-Nov-26	10-Nov-26		
Office.M1.IB.340	Office - M1 - General - Install Cable Tray	10	04-Nov-26	17-Nov-26		
Office.M1.IB.590	Office - M1 - General - Security Trim-out (By Others)	10	18-Nov-26	01-Dec-26		
Office.M1.IB.410	Office - M1 - General - Pull & Terminate Wires	15	18-Nov-26	08-Dec-26		
Office.M1.IB.510	Office - M1 - General - Electrical Trim-out	10	02-Dec-26	15-Dec-26		
Office.M1.IB.520	Office - M1 - General - Fire Alarm Trim-out	10	02-Dec-26	15-Dec-26		
Office.M1.IB.570	Office - M1 - General - Install Millwork	3	04-Dec-26	08-Dec-26		
Office.M1.IB.575	Office - M1 - General - Install Plumbing Fixtures	2	09-Dec-26	10-Dec-26		
Office.M1.IB.540	Office - M1 - General - Install FECs	5	15-Dec-26	22-Dec-26		
Office.M1.IB.630	Office - M1 - General - Install Furniture	5	16-Dec-26	23-Dec-26		
Office.M1.IB.600	Office - M1 - General - Final Paint	10	24-Dec-26	06-Jan-27		
Office.M1.IB.610	Office - M1 - General - Install Signage	5	05-Jan-27	11-Jan-27		
Office.M1.IB.680	Office - M1 - General - Punchlist	15	12-Jan-27	04-Feb-27		
Office.M1.IB.690	Office - M1 - General - Final Clean	10	05-Feb-27	18-Feb-27		
PH1 - Office - Penthouse		100	06-Oct-26	22-Feb-27		
Office.Pent.ELVST.330	Office - Pent - ELV & ST03 Tower - Mechanical OH Rough-Ins	1	12-Oct-26	12-Oct-26	Trade	Mechanical
Office.Pent.ELVST.530	Office - Pent - ELV & ST03 Tower - Mechanical Trim-out	2	05-Nov-26	06-Nov-26	Trade	Mechanical
Office.Pent.ELVST.430	Office - Pent - ELV & ST03 Tower - Set ISU	2	27-Oct-26	28-Oct-26	Trade	HVAC
Office.Pent.ELVST.440	Office - Pent - ELV & ST03 Tower - Set OSU	2	27-Oct-26	28-Oct-26	Trade	HVAC
Office.Pent.ELVST.100	Office - Pent - ELV & ST03 Tower - Layout Walls	1	06-Oct-26	06-Oct-26		
Office.Pent.ELVST.110	Office - Pent - ELV & ST03 Tower - Frame Walls	2	07-Oct-26	08-Oct-26		
Office.Pent.ELVST.300	Office - Pent - ELV & ST03 Tower - Fire Sprinkler OH Rough-Ins	2	08-Oct-26	09-Oct-26		
Office.Pent.ELVST.200	Office - Pent - ELV & ST03 Tower - Electrical/Fire Alarm In-Wall Rougl	3	09-Oct-26	13-Oct-26		
Office.Pent.ELVST.210	Office - Pent - ELV & ST03 Tower - Sec/Telecom In-Wall Rough-Ins	3	09-Oct-26	13-Oct-26		
Office.Pent.ELVST.170	Office - Pent - ELV & ST03 Tower - Install Exterior Door & Frames	1	09-Oct-26	09-Oct-26		
Office.Pent.ELVST.220	Office - Pent - ELV & ST03 Tower - Plumbing In-Wall Rough-Ins	3	09-Oct-26	13-Oct-26		
Office.Pent.ELVST.310	Office - Pent - ELV & ST03 Tower - Electrical/Fire Alarm OH Rough-In	3	13-Oct-26	15-Oct-26		
Office.Pent.ELVST.320	Office - Pent - ELV & ST03 Tower - Sec/Telecom OH Rough-Ins	3	13-Oct-26	15-Oct-26		
Office.Pent.ELVST.120	Office - Pent - ELV & ST03 Tower - One Side Drywall	2	14-Oct-26	15-Oct-26		
Office.Pent.ELVST.130	Office - Pent - ELV & ST03 Tower - Hang Interior Door Frame	1	16-Oct-26	16-Oct-26		

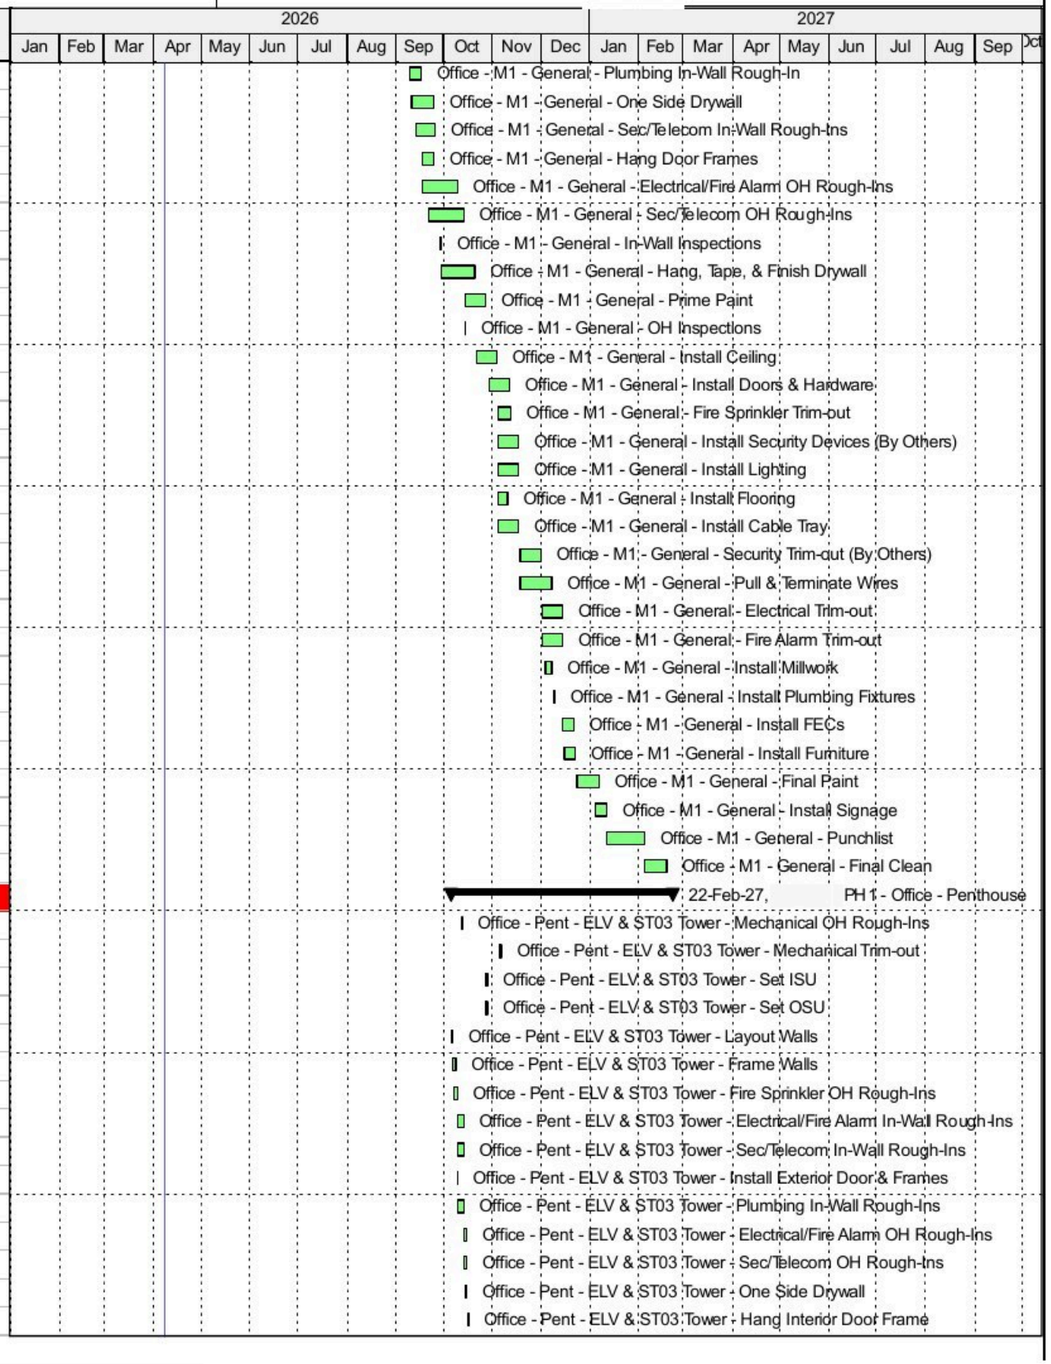


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Office.Pent.ELVST.290	Office - Pent - ELV & ST03 Tower - In-Wall Inspections	1	16-Oct-26	16-Oct-26		
Office.Pent.ELVST.390	Office - Pent - ELV & ST03 Tower - OH Inspections	1	16-Oct-26	16-Oct-26		
Office.Pent.ELVST.140	Office - Pent - ELV & ST03 Tower - Hang, Tape, & Finish Drywall	3	20-Oct-26	22-Oct-26		
Office.Pent.ELVST.160	Office - Pent - ELV & ST03 Tower - Prime Paint	2	23-Oct-26	26-Oct-26		
Office.Pent.ELVST.500	Office - Pent - ELV & ST03 Tower - Fire Sprinkler Trim-out	2	27-Oct-26	28-Oct-26		
Office.Pent.ELVST.490	Office - Pent - ELV & ST03 Tower - Install Security Devices (By Other	5	27-Oct-26	02-Nov-26		
Office.Pent.ELVST.580	Office - Pent - ELV & ST03 Tower - Install Lighting	2	27-Oct-26	28-Oct-26		
Office.Pent.ELVST.410	Office - Pent - ELV & ST03 Tower - Pull & Terminate Wires	5	29-Oct-26	04-Nov-26		
Office.Pent.ELVST.420	Office - Pent - ELV & ST03 Tower - MEPF Equipment Connections	5	29-Oct-26	04-Nov-26		
Office.Pent.ELVST.400	Office - Pent - ELV & ST03 Tower - Install Doors & Hardware	1	30-Oct-26	30-Oct-26		
Office.Pent.ELVST.590	Office - Pent - ELV & ST03 Tower - Security Trim-out (By Others)	5	03-Nov-26	09-Nov-26		
Office.Pent.ELVST.510	Office - Pent - ELV & ST03 Tower - Electrical Trim-out	2	05-Nov-26	06-Nov-26		
Office.Pent.ELVST.520	Office - Pent - ELV & ST03 Tower - Fire Alarm Trim-out	2	05-Nov-26	06-Nov-26		
Office.Pent.ELVST.600	Office - Pent - ELV & ST03 Tower - Final Paint	5	10-Nov-26	16-Nov-26		
Office.Pent.ELVST.610	Office - Pent - ELV & ST03 Tower - Install Signage	2	17-Nov-26	18-Nov-26		
Office.Pent.ELVST.680	Office - Pent - ELV & ST03 Tower - Punchlist	5	19-Nov-26	25-Nov-26		
Office.Pent.ELVST.690	Office - Pent - ELV & ST03 Tower - Final Clean	5	26-Nov-26	02-Dec-26		
PH1 - Office - Penthouse - Commissioning		37	01-Jan-27	22-Feb-27		
Cx.Office.Pent.100	L2 Commissioning - Office Penthouse	10	01-Jan-27	18-Jan-27		
Cx.Office.Pent.110	Energize Equipment - Office Penthouse	5	26-Jan-27	01-Feb-27		
Cx.Office.Pent.120	L3 Commissioning - Office Penthouse	15	02-Feb-27	22-Feb-27		
Phase 1 (ROMP 1 & 2)		124	08-Sep-26	26-Feb-27		
PH1 - ROMP1 & 2 - Electrical Rooms 1.1 & 1.2		100	16-Sep-26	02-Feb-27		
PH1 - ROMP 1 - Electrical Room 1.1		100	16-Sep-26	02-Feb-27		
PH1.R1.ER1.1-IB.690	PH1 - ROMP1 - ER - Mechanical OH Rough-ins	5	23-Sep-26	30-Sep-26	Trade	Mechanical
PH1.R1.ER1.1-IB.720	PH1 - ROMP1 - ER - Mechanical Trim-out	5	24-Dec-26	30-Dec-26	Trade	Mechanical
PH1.R1.ER1.1-320	PH1 - ROMP1 - ER - Set CRAC Units	5	03-Nov-26	09-Nov-26	Trade	HVAC
PH1.R1.ER1.1-IB.300	PH1 - ROMP1 - ER - Layout & Frame Walls	5	16-Sep-26	22-Sep-26		
PH1.R1.ER1.1-IB.310	PH1 - ROMP1 - ER - Fire Sprinkler OH Rough-ins	5	16-Sep-26	22-Sep-26		
PH1.R1.ER1.1-IB.400	PH1 - ROMP1 - ER - One Side Drywall	5	23-Sep-26	30-Sep-26		
PH1.R1.ER1.1-IB.640	PH1 - ROMP1 - ER - Fire Alarm In-Wall Rough-ins	4	23-Sep-26	29-Sep-26		
PH1.R1.ER1.1-IB.650	PH1 - ROMP1 - ER - Electrical In-Wall Rough-ins	4	23-Sep-26	29-Sep-26		
PH1.R1.ER1.1-IB.660	PH1 - ROMP1 - ER - Plumbing In-Wall Rough-ins	2	23-Sep-26	24-Sep-26		
PH1.R1.ER1.1-IB.670	PH1 - ROMP1 - ER - Security/Telecom/LV In-Wall Rough-ins	4	23-Sep-26	29-Sep-26		
PH1.R1.ER1.1-IB.750	PH1 - ROMP1 - ER - Hang Door Frames	5	23-Sep-26	30-Sep-26		
PH1.R1.ER1.1-IB.410	PH1 - ROMP1 - ER - In-Wall Inspection	1	30-Sep-26	30-Sep-26		
PH1.R1.ER1.1-IB.680	PH1 - ROMP1 - ER - Electrical/Fire Alarm OH Rough-ins	15	01-Oct-26	21-Oct-26		
PH1.R1.ER1.1-IB.700	PH1 - ROMP1 - ER - Plumbing OH Rough-ins	4	01-Oct-26	06-Oct-26		
PH1.R1.ER1.1-IB.760	PH1 - ROMP1 - ER - Security/Telecom/LV OH Rough-ins	15	01-Oct-26	21-Oct-26		
PH1.R1.ER1.1-IB.320	PH1 - ROMP1 - ER - Hang, Tape, & Finish Drywall	10	12-Oct-26	23-Oct-26		
PH1.R1.ER1.1-IB.330	PH1 - ROMP1 - ER - Prime Paint	5	21-Oct-26	27-Oct-26		
PH1.R1.ER1.1-IB.430	PH1 - ROMP1 - ER - OH Inspection	1	22-Oct-26	22-Oct-26		
PH1.R1.ER1.1-IB.380	PH1 - ROMP1 - ER - Install Cable Tray	10	11-Nov-26	24-Nov-26		
PH1.R1.ER1.1-IB.370	PH1 - ROMP1 - ER - Pull & Terminate Wires	15	25-Nov-26	15-Dec-26		
PH1.R1.ER1.1-IB.390	PH1 - ROMP1 - ER - Install Doors & Hardware	5	16-Dec-26	23-Dec-26		

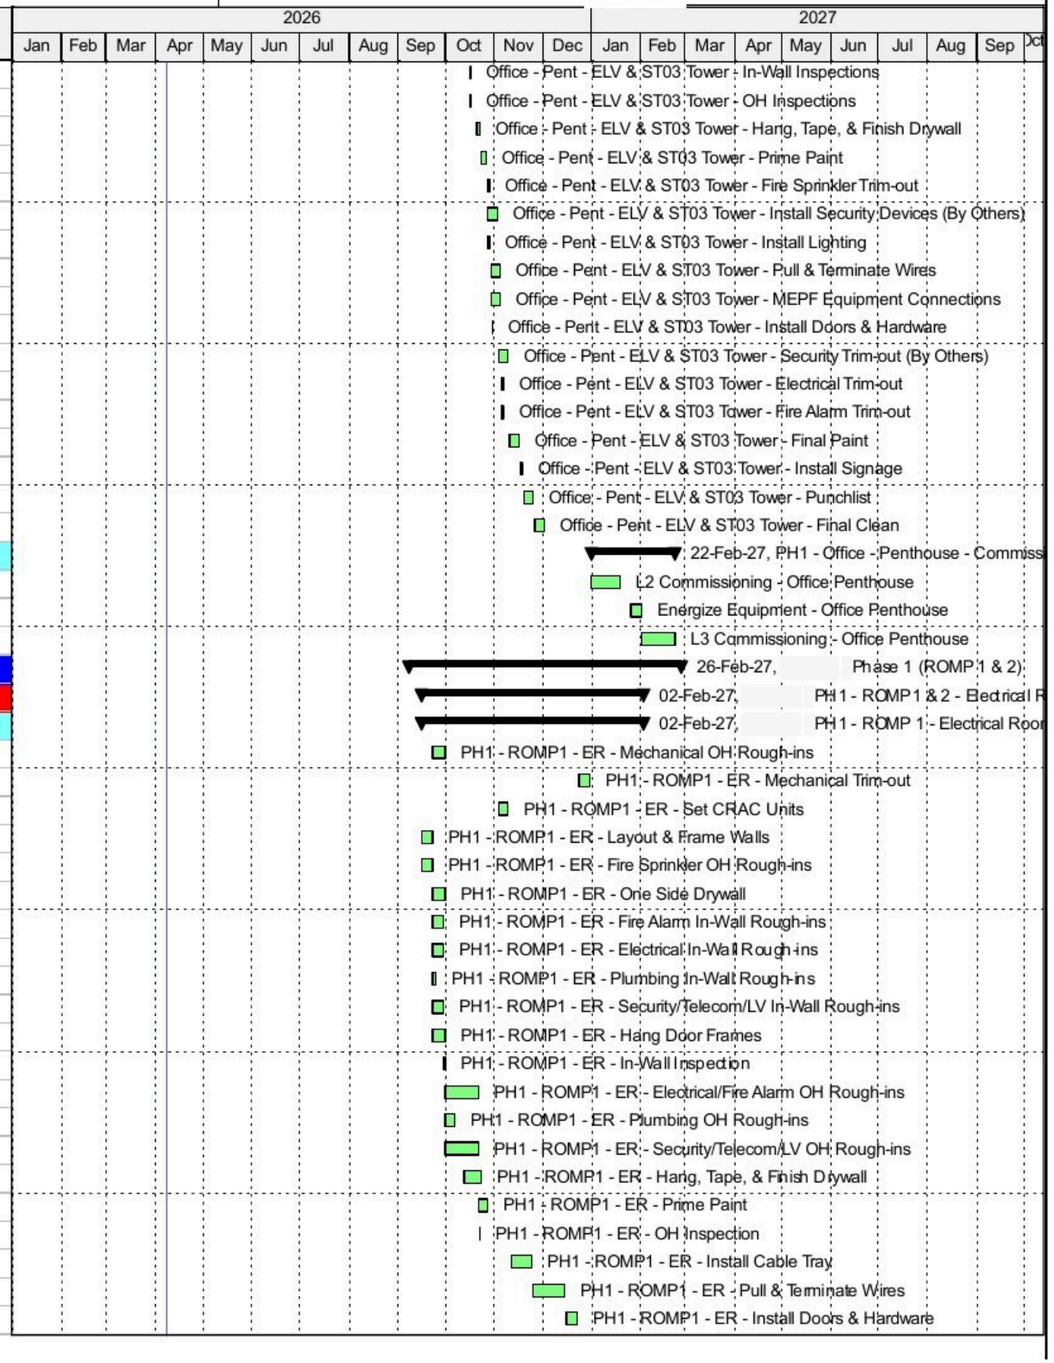


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule


Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH1.R1.ER1.1-IB.440	PH1 - ROMP1 - ER - Security Devices (By Others)	5	16-Dec-26	23-Dec-26		
PH1.R1.ER1.1-IB.710	PH1 - ROMP1 - ER - Electrical Trim-out	5	24-Dec-26	30-Dec-26		
PH1.R1.ER1.1-IB.740	PH1 - ROMP1 - ER - Fire Alarm Trim-out	5	24-Dec-26	30-Dec-26		
PH1.R1.ER1.1-IB.770	PH1 - ROMP1 - ER - Security Trim-out (By Others)	5	24-Dec-26	30-Dec-26		
PH1.R1.ER1.1-IB.600	PH1 - ROMP1 - ER - Punchlist	5	31-Dec-26	06-Jan-27		
PH1.R1.ER1.1-IB.610	PH1 - ROMP1 - ER - Final Clean	5	07-Jan-27	13-Jan-27		
PH1.R1.ER1.1-340	PH1 - ROMP1 - ER - Install VFD's	5	28-Oct-26	03-Nov-26		
PH1.R1.ER1.1-270	PH1 - ROMP1 - ER - Loose Busduct Test & Install (OFCI)	5	28-Oct-26	03-Nov-26		
PH1.R1.ER1.1-350	PH1 - ROMP1 - ER - Busduct Skid Test & Install (OFCI)	10	28-Oct-26	10-Nov-26		
PH1.R1.ER1.1-330	PH1 - ROMP1 - ER - Set Exhuast Fans	5	03-Nov-26	09-Nov-26		
PH1.R1.ER1.1-220	PH1 - ROMP1 - ER - Set USB's & AMCOP's (Skids) (OFCI)	5	05-Nov-26	11-Nov-26		
PH1.R1.ER1.1-230	PH1 - ROMP1 - ER - Set XFMR's (OFCI)	5	05-Nov-26	11-Nov-26		
PH1.R1.ER1.1-240	PH1 - ROMP1 - ER - Set ATS's (OFCI)	5	05-Nov-26	11-Nov-26		
PH1.R1.ER1.1-250	PH1 - ROMP1 - ER - Set HPP's, HLP's, HUPP's (OFCI)	5	05-Nov-26	11-Nov-26		
PH1.R1.ER1.1-260	PH1 - ROMP1 - ER - Set MSDB (OFCI)	5	05-Nov-26	11-Nov-26		
Cx.PH1.R1.ER1.1-XFMR.100	R1 ER 1.1 - XFMR's - Pre Startup Installer	7	16-Dec-26	25-Dec-26		
Cx.PH1.R1.ER1.1-XFMR.110	R1 ER 1.1 - XFMR's - L2 QC	1	28-Dec-26	28-Dec-26		
Cx.PH1.R1.ER1.1-XFMR.120	R1 ER 1.1 - XFMR's - Installation Verification Checklist	2	29-Dec-26	30-Dec-26		
Cx.PH1.R1.ER1.1-XFMR.130	R1 ER 1.1 - XFMR's - Yellow Tag	1	31-Dec-26	31-Dec-26		
Cx.PH1.R1.ER1.1-XFMR.140	R1 ER 1.1 - XFMR's - Energize Equipment	1	26-Jan-27	26-Jan-27		
Cx.PH1.R1.ER1.1-XFMR.150	R1 ER 1.1 - XFMR's - L3 Start-up	1	27-Jan-27	27-Jan-27		
Cx.PH1.R1.ER1.1-XFMR.160	R1 ER 1.1 - XFMR's - Thermographic Checks	1	28-Jan-27	28-Jan-27		
Cx.PH1.R1.ER1.1-XFMR.170	R1 ER 1.1 - XFMR's - Green Tag	1	29-Jan-27	29-Jan-27		
Cx.PH1.R1.ER1.1-USB.100	R1 ER 1.1 - USB's - Pre Startup Installer	5	16-Dec-26	23-Dec-26		
Cx.PH1.R1.ER1.1-USB.110	R1 ER 1.1 - USB's - Pre Startup Vendor	3	16-Dec-26	21-Dec-26		
Cx.PH1.R1.ER1.1-USB.120	R1 ER 1.1 - USB's - L2 QC	1	06-Jan-27	06-Jan-27		
Cx.PH1.R1.ER1.1-USB.130	R1 ER 1.1 - USB's - Installation Verification Checklist	1	07-Jan-27	07-Jan-27		
Cx.PH1.R1.ER1.1-USB.140	R1 ER 1.1 - USB's - Yellow Tag	1	08-Jan-27	08-Jan-27		
Cx.PH1.R1.ER1.1-USB.150	R1 ER 1.1 - USB's - Energize Equipment	1	21-Jan-27	21-Jan-27		
Cx.PH1.R1.ER1.1-USB.160	R1 ER 1.1 - USB's - L3 Startup	4	25-Jan-27	28-Jan-27		
Cx.PH1.R1.ER1.1-USB.170	R1 ER 1.1 - USB's - EPMS SAT	1	29-Jan-27	29-Jan-27		
Cx.PH1.R1.ER1.1-USB.180	R1 ER 1.1 - USB's - Thermographic Checks	1	01-Feb-27	01-Feb-27		
Cx.PH1.R1.ER1.1-USB.190	R1 ER 1.1 - USB's - Green Tag	1	02-Feb-27	02-Feb-27		
Cx.PH1.R1.ER1.1-ATS.100	R1 ER 1.1 - ATS's - Pre Startup Installer	5	30-Dec-26	05-Jan-27		
Cx.PH1.R1.ER1.1-ATS.110	R1 ER 1.1 - ATS's - Pre Startup Vendor	3	30-Dec-26	01-Jan-27		
Cx.PH1.R1.ER1.1-ATS.120	R1 ER 1.1 - ATS's - L2 QC	1	06-Jan-27	06-Jan-27		
Cx.PH1.R1.ER1.1-ATS.130	R1 ER 1.1 - ATS's - Installation Verification Checklist	2	07-Jan-27	08-Jan-27		
Cx.PH1.R1.ER1.1-ATS.140	R1 ER 1.1 - ATS's - Yellow Tag	1	11-Jan-27	11-Jan-27		
Cx.PH1.R1.ER1.1-ATS.150	R1 ER 1.1 - ATS's - Energize Equipment	1	25-Jan-27	25-Jan-27		
Cx.PH1.R1.ER1.1-ATS.160	R1 ER 1.1 - ATS's - L3 Startup	2	26-Jan-27	27-Jan-27		
Cx.PH1.R1.ER1.1-ATS.170	R1 ER 1.1 - ATS's - EPMS SAT	1	28-Jan-27	28-Jan-27		
Cx.PH1.R1.ER1.1-ATS.180	R1 ER 1.1 - ATS's - Thermographic Checks	1	29-Jan-27	29-Jan-27		
Cx.PH1.R1.ER1.1-ATS.190	R1 ER 1.1 - ATS's - Green Tag	1	01-Feb-27	01-Feb-27		
Cx.PH1.R1.ER1.1-MSDB.100	R1 ER 1.1 - MSDB's - Pre Startup Installer	5	16-Dec-26	23-Dec-26		
Cx.PH1.R1.ER1.1-MSDB.110	R1 ER 1.1 - MSDB's - Pre Startup Vendor	3	16-Dec-26	21-Dec-26		

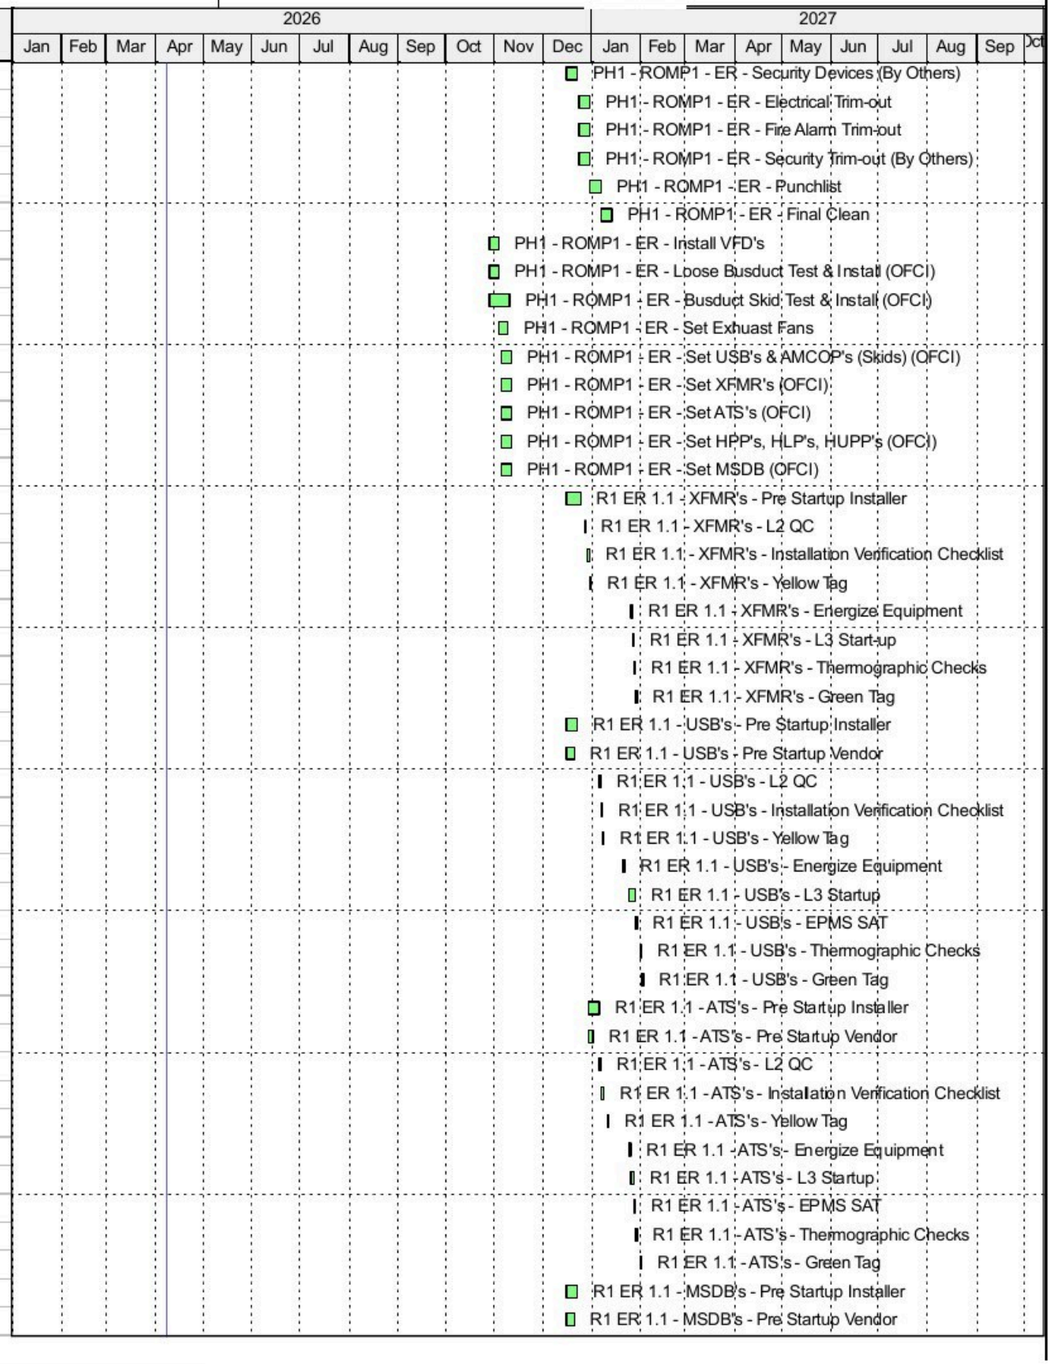


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH1.R1.ER1.1-MSDB.120	R1 ER 1.1 - MSDB's - L2 QC	1	24-Dec-26	24-Dec-26		
Cx.PH1.R1.ER1.1-MSDB.130	R1 ER 1.1 - MSDB's - Installation Verification Checklist	2	25-Dec-26	28-Dec-26		
Cx.PH1.R1.ER1.1-MSDB.140	R1 ER 1.1 - MSDB's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.R1.ER1.1-MSDB.150	R1 ER 1.1 - MSDB's - Energize Equipment	1	25-Jan-27	25-Jan-27		
Cx.PH1.R1.ER1.1-MSDB.160	R1 ER 1.1 - MSDB's - L3 Startup	2	26-Jan-27	27-Jan-27		
Cx.PH1.R1.ER1.1-MSDB.170	R1 ER 1.1 - MSDB's - EPMS SAT	1	28-Jan-27	28-Jan-27		
Cx.PH1.R1.ER1.1-MSDB.180	R1 ER 1.1 - MSDB's - Thermographic Checks	1	29-Jan-27	29-Jan-27		
Cx.PH1.R1.ER1.1-MSDB.190	R1 ER 1.1 - MSDB's - Green Tag	1	01-Feb-27	01-Feb-27		
Cx.PH1.R1.ER1.1-AMCOP.100	R1 ER 1.1 - AMCOP's - Pre Startup Installer	5	16-Dec-26	23-Dec-26		
Cx.PH1.R1.ER1.1-AMCOP.110	R1 ER 1.1 - AMCOP's - Pre Startup Vendor	3	16-Dec-26	21-Dec-26		
Cx.PH1.R1.ER1.1-AMCOP.120	R1 ER 1.1 - AMCOP's - L2 QC	1	22-Dec-26	22-Dec-26		
Cx.PH1.R1.ER1.1-AMCOP.130	R1 ER 1.1 - AMCOP's - Installation Verfication Checklist	2	23-Dec-26	24-Dec-26		
Cx.PH1.R1.ER1.1-AMCOP.140	R1 ER 1.1 - AMCOP's - Yellow Tag	1	25-Dec-26	25-Dec-26		
Cx.PH1.R1.ER1.1-AMCOP.150	R1 ER 1.1 - AMCOP's - Energize Equipment	1	25-Jan-27	25-Jan-27		
Cx.PH1.R1.ER1.1-AMCOP.160	R1 ER 1.1 - AMCOP's - L3 Startup	2	26-Jan-27	27-Jan-27		
Cx.PH1.R1.ER1.1-AMCOP.170	R1 ER 1.1 - AMCOP's - EPMS SAT	1	28-Jan-27	28-Jan-27		
Cx.PH1.R1.ER1.1-AMCOP.180	R1 ER 1.1 - AMCOP's - Thermographic Checks	1	29-Jan-27	29-Jan-27		
Cx.PH1.R1.ER1.1-AMCOP.190	R1 ER 1.1 - AMCOP's - Green Tag	1	01-Feb-27	01-Feb-27		
Cx.PH1.R1.ER1.1-CRAC.100	R1 ER 1.1 - CRAC's - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.R1.ER1.1-CRAC.110	R1 ER 1.1 - CRAC's - Pre Startup Vendor	3	29-Dec-26	31-Dec-26		
Cx.PH1.R1.ER1.1-CRAC.120	R1 ER 1.1 - CRAC's - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.R1.ER1.1-CRAC.130	R1 ER 1.1 - CRAC's - Installation Verification Checklist	2	04-Jan-27	05-Jan-27		
Cx.PH1.R1.ER1.1-CRAC.140	R1 ER 1.1 - CRAC's - Yellow Tag	1	06-Jan-27	06-Jan-27		
Cx.PH1.R1.ER1.1-CRAC.150	R1 ER 1.1 - CRAC's - Energize Equipment	1	07-Jan-27	07-Jan-27		
Cx.PH1.R1.ER1.1-CRAC.160	R1 ER 1.1 - CRAC's - L3 Startup	1	08-Jan-27	08-Jan-27		
Cx.PH1.R1.ER1.1-CRAC.180	R1 ER 1.1 - CRAC's - BAS SAT	1	11-Jan-27	11-Jan-27		
Cx.PH1.R1.ER1.1-CRAC.170	R1 ER 1.1 - CRAC's - TAB	3	12-Jan-27	18-Jan-27		
Cx.PH1.R1.ER1.1-CRAC.190	R1 ER 1.1 - CRAC's - Green Tag	1	19-Jan-27	19-Jan-27		
Cx.PH1.R1.ER1.1-HPP.HLP.100	R1 ER 1.1 - HPP's & HLP's - Pre Startup Installer	5	16-Dec-26	23-Dec-26		
Cx.PH1.R1.ER1.1-HPP.HLP.110	R1 ER 1.1 - HPP's & HLP's - Pre Startup Vendor	3	16-Dec-26	21-Dec-26		
Cx.PH1.R1.ER1.1-HPP.HLP.120	R1 ER 1.1 - HPP's & HLP's - L2 QC	1	24-Dec-26	24-Dec-26		
Cx.PH1.R1.ER1.1-HPP.HLP.130	R1 ER 1.1 - HPP's & HLP's - Installation Verification Checklist	2	25-Dec-26	28-Dec-26		
Cx.PH1.R1.ER1.1-HPP.HLP.140	R1 ER 1.1 - HPP's & HLP's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.R1.ER1.1-HPP.HLP.150	R1 ER 1.1 - HPP's & HLP's - Energize Equipment	1	27-Jan-27	27-Jan-27		
Cx.PH1.R1.ER1.1-HPP.HLP.160	R1 ER 1.1 - HPP's & HLP's - L3 Startup	1	28-Jan-27	28-Jan-27		
Cx.PH1.R1.ER1.1-HPP.HLP.170	R1 ER 1.1 - HPP's & HLP's - EPMS SAT	1	29-Jan-27	29-Jan-27		
Cx.PH1.R1.ER1.1-HPP.HLP.180	R1 ER 1.1 - HPP's & HLP's - Thermographic Checks	1	01-Feb-27	01-Feb-27		
Cx.PH1.R1.ER1.1-HPP.HLP.190	R1 ER 1.1 - HPP's & HLP's - Green Tag	1	02-Feb-27	02-Feb-27		
Cx.PH1.R1.ER1.1-HUPP.100	R1 ER 1.1 - HUPP's - Pre Startup Installer	5	16-Dec-26	23-Dec-26		
Cx.PH1.R1.ER1.1-HUPP.110	R1 ER 1.1 - HUPP's - Pre Startup Vendor	3	16-Dec-26	21-Dec-26		
Cx.PH1.R1.ER1.1-HUPP.120	R1 ER 1.1 - HUPP's - L2 QC	1	22-Dec-26	22-Dec-26		
Cx.PH1.R1.ER1.1-HUPP.130	R1 ER 1.1 - HUPP's - Installation Verification Checklist	2	23-Dec-26	24-Dec-26		
Cx.PH1.R1.ER1.1-HUPP.140	R1 ER 1.1 - HUPP's - Yellow Tag	1	25-Dec-26	25-Dec-26		
Cx.PH1.R1.ER1.1-HUPP.150	R1 ER 1.1 - HUPP's - Energize Equipment	1	27-Jan-27	27-Jan-27		
Cx.PH1.R1.ER1.1-HUPP.160	R1 ER 1.1 - HUPP's - L3 Startup	1	28-Jan-27	28-Jan-27		

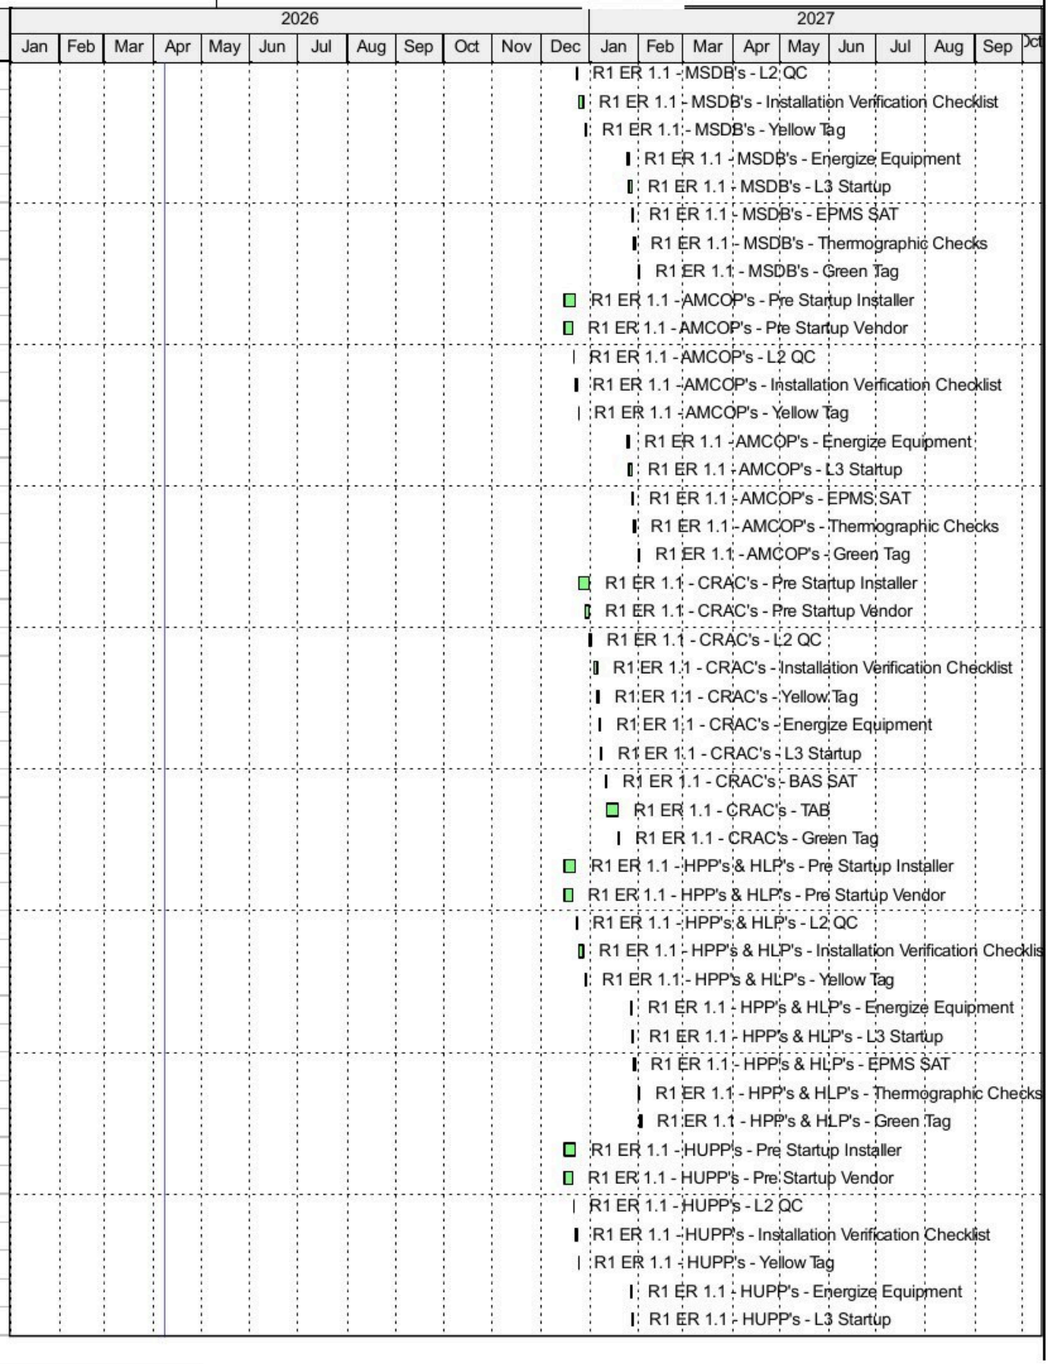

Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH1.R1.ER1.1-HUPP.170	R1 ER 1.1 - HUPP's - EPMS SAT	1	29-Jan-27	29-Jan-27		
Cx.PH1.R1.ER1.1-HUPP.180	R1 ER 1.1 - HUPP's - Thermographic Checks	1	01-Feb-27	01-Feb-27		
Cx.PH1.R1.ER1.1-HUPP.190	R1 ER 1.1 - HUPP's - Green Tag	1	02-Feb-27	02-Feb-27		
Cx.PH1.R1.ER1.1-HUDPP.100	R1 ER 1.1 - HUDPP's - Pre Startup Installer	5	16-Dec-26	23-Dec-26		
Cx.PH1.R1.ER1.1-HUDPP.110	R1 ER 1.1 - HUDPP's - Pre Startup Vendor	3	16-Dec-26	21-Dec-26		
Cx.PH1.R1.ER1.1-HUDPP.120	R1 ER 1.1 - HUDPP's - L2 QC	1	24-Dec-26	24-Dec-26		
Cx.PH1.R1.ER1.1-HUDPP.130	R1 ER 1.1 - HUDPP's - Installation Verification Checklist	2	25-Dec-26	28-Dec-26		
Cx.PH1.R1.ER1.1-HUDPP.140	R1 ER 1.1 - HUDPP's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.R1.ER1.1-HUDPP.150	R1 ER 1.1 - HUDPP's - Energize Equipment	1	26-Jan-27	26-Jan-27		
Cx.PH1.R1.ER1.1-HUDPP.160	R1 ER 1.1 - HUDPP's - L3 Startup	1	27-Jan-27	27-Jan-27		
Cx.PH1.R1.ER1.1-HUDPP.170	R1 ER 1.1 - HUDPP's - EPMS SAT	1	28-Jan-27	28-Jan-27		
Cx.PH1.R1.ER1.1-HUDPP.180	R1 ER 1.1 - HUDPP's - Thermographic Checks	1	29-Jan-27	29-Jan-27		
Cx.PH1.R1.ER1.1-HUDPP.190	R1 ER 1.1 - HUDPP's - Green Tag	1	01-Feb-27	01-Feb-27		
Cx.PH1.R1.ER1.1-GENAN.100	R1 ER 1.1 - GENAN's - Pre Startup Installer	5	16-Dec-26	23-Dec-26		
Cx.PH1.R1.ER1.1-GENAN.110	R1 ER 1.1 - GENAN's - Pre Startup Vendor	3	16-Dec-26	21-Dec-26		
Cx.PH1.R1.ER1.1-GENAN.120	R1 ER 1.1 - GENAN's - L2 QC	1	24-Dec-26	24-Dec-26		
Cx.PH1.R1.ER1.1-GENAN.130	R1 ER 1.1 - GENAN's - Installation Verification Checklist	2	25-Dec-26	28-Dec-26		
Cx.PH1.R1.ER1.1-GENAN.140	R1 ER 1.1 - GENAN's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.R1.ER1.1-GENAN.150	R1 ER 1.1 - GENAN's - Energize Equipment	1	30-Dec-26	30-Dec-26		
Cx.PH1.R1.ER1.1-GENAN.160	R1 ER 1.1 - GENAN's - L3 Startup	1	31-Dec-26	31-Dec-26		
Cx.PH1.R1.ER1.1-GENAN.170	R1 ER 1.1 - GENAN's - EPMS SAT	1	01-Jan-27	01-Jan-27		
Cx.PH1.R1.ER1.1-GENAN.180	R1 ER 1.1 - GENAN's - Thermographics	1	04-Jan-27	04-Jan-27		
Cx.PH1.R1.ER1.1-GENAN.190	R1 ER 1.1 - GENAN's - Green Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.R1.ER1.1-ATS.200	R1 ER 1.1 - ATS's - Pre Startup Installer	5	30-Dec-26	05-Jan-27		
Cx.PH1.R1.ER1.1-ATS.210	R1 ER 1.1 - ATS's - Pre Startup Vendor	3	30-Dec-26	01-Jan-27		
Cx.PH1.R1.ER1.1-ATS.220	R1 ER 1.1 - ATS's - L2 QC	1	04-Jan-27	04-Jan-27		
Cx.PH1.R1.ER1.1-ATS.230	R1 ER 1.1 - ATS's - Installation Verification Checklist	2	05-Jan-27	06-Jan-27		
Cx.PH1.R1.ER1.1-ATS.240	R1 ER 1.1 - ATS's - Yellow Tag	1	07-Jan-27	07-Jan-27		
Cx.PH1.R1.ER1.1-ATS.250	R1 ER 1.1 - ATS's - Energize Equipment	1	25-Jan-27	25-Jan-27		
Cx.PH1.R1.ER1.1-ATS.260	R1 ER 1.1 - ATS's - L3 Startup	2	26-Jan-27	27-Jan-27		
Cx.PH1.R1.ER1.1-ATS.270	R1 ER 1.1 - ATS's - EPMS SAT	1	28-Jan-27	28-Jan-27		
Cx.PH1.R1.ER1.1-ATS.280	R1 ER 1.1 - ATS's - Thermographic Checks	1	29-Jan-27	29-Jan-27		
Cx.PH1.R1.ER1.1-ATS.290	R1 ER 1.1 - ATS's - Green Tag	1	01-Feb-27	01-Feb-27		
Cx.PH1.R1.ER1.1-XFMR.180	R1 ER 1.1 - XFMR's - Pre Startup Installer	7	16-Dec-26	25-Dec-26		
Cx.PH1.R1.ER1.1-XFMR.190	R1 ER 1.1 - XFMR's - L2 QC	1	28-Dec-26	28-Dec-26		
Cx.PH1.R1.ER1.1-XFMR.200	R1 ER 1.1 - XFMR's - Installation Verification Checklist	2	29-Dec-26	30-Dec-26		
Cx.PH1.R1.ER1.1-XFMR.210	R1 ER 1.1 - XFMR's - Yellow Tag	1	31-Dec-26	31-Dec-26		
Cx.PH1.R1.ER1.1-XFMR.220	R1 ER 1.1 - XFMR's - Energize Equipment	1	26-Jan-27	26-Jan-27		
Cx.PH1.R1.ER1.1-XFMR.230	R1 ER 1.1 - XFMR's - L3 Start-up	1	27-Jan-27	27-Jan-27		
Cx.PH1.R1.ER1.1-XFMR.240	R1 ER 1.1 - XFMR's - Thermographic Checks	1	28-Jan-27	28-Jan-27		
Cx.PH1.R1.ER1.1-XFMR.250	R1 ER 1.1 - XFMR's - Green Tag	1	29-Jan-27	29-Jan-27		
PH1 - ROMP 2 - Electrical Room 1.2		100	16-Sep-26	02-Feb-27		
PH1.R2.ER1.2-IB.860	PH1 - ROMP2 - ER - Mechanical OH Rough-ins	5	23-Sep-26	30-Sep-26	Trade	Mechanical
PH1.R2.ER1.2-IB.960	PH1 - ROMP2 - ER - Mechanical Trim-out	5	24-Dec-26	30-Dec-26	Trade	Mechanical
PH1.R2.ER1.2-220	PH1 - ROMP2 - ER - Set CRAC Units	5	03-Nov-26	09-Nov-26	Trade	HVAC

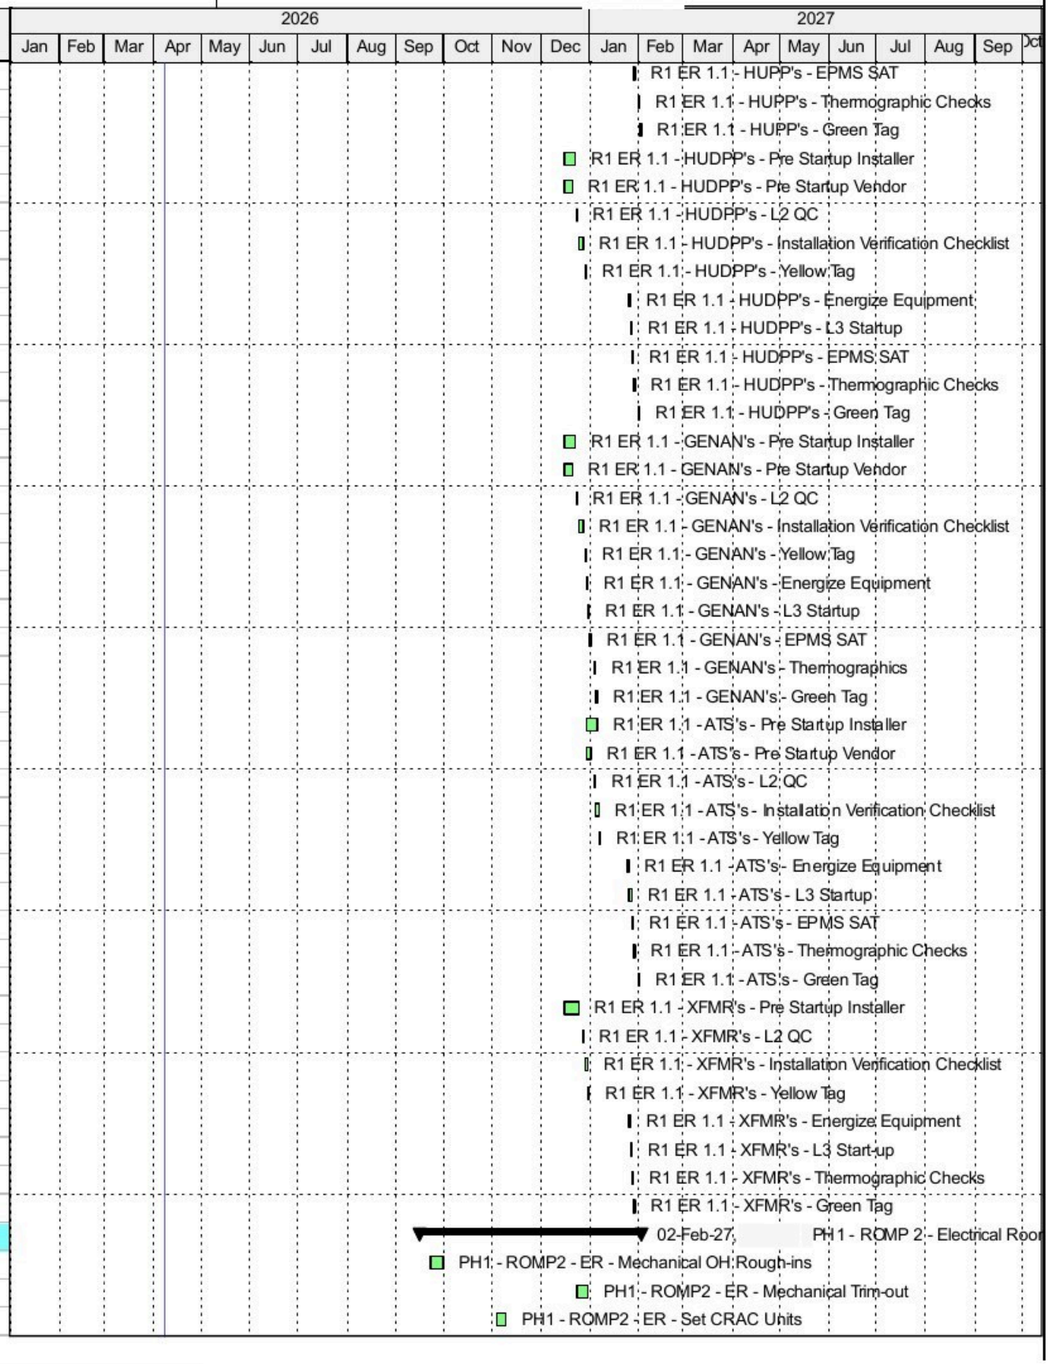


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE | CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule


Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH1.R2.ER1.2-IB.750	PH1 - ROMP2 - ER - Layout & Frame Walls	5	16-Sep-26	22-Sep-26		
PH1.R2.ER1.2-IB.820	PH1 - ROMP2 - ER - Fire Sprinkler OH Rough-ins	5	16-Sep-26	22-Sep-26		
PH1.R2.ER1.2-IB.760	PH1 - ROMP2 - ER - One Side Drywall	5	23-Sep-26	30-Sep-26		
PH1.R2.ER1.2-IB.790	PH1 - ROMP2 - ER - Fire Alarm In-Wall Rough-ins	4	23-Sep-26	29-Sep-26		
PH1.R2.ER1.2-IB.780	PH1 - ROMP2 - ER - Electrical In-Wall Rough-ins	4	23-Sep-26	29-Sep-26		
PH1.R2.ER1.2-IB.770	PH1 - ROMP2 - ER - Plumbing In-Wall Rough-ins	4	23-Sep-26	29-Sep-26		
PH1.R2.ER1.2-IB.810	PH1 - ROMP2 - ER - Security/Telecom/LV In-Wall Rough-ins	2	23-Sep-26	24-Sep-26		
PH1.R2.ER1.2-IB.1005	PH1 - ROMP2 - ER - One Side Drywall	5	23-Sep-26	30-Sep-26		
PH1.R2.ER1.2-IB.800	PH1 - ROMP2 - ER - In-Wall Inspection	1	30-Sep-26	30-Sep-26		
PH1.R2.ER1.2-IB.850	PH1 - ROMP2 - ER - Electrical/Fire Alarm OH Rough-ins	15	01-Oct-26	21-Oct-26		
PH1.R2.ER1.2-IB.840	PH1 - ROMP2 - ER - Plumbing OH Rough-ins	4	01-Oct-26	06-Oct-26		
PH1.R2.ER1.2-IB.1015	PH1 - ROMP2 - ER - Security/Telecom/LV OH Rough-ins	15	01-Oct-26	21-Oct-26		
PH1.R2.ER1.2-IB.830	PH1 - ROMP2 - ER - Hang, Tape, & Finish Drywall	10	12-Oct-26	23-Oct-26		
PH1.R2.ER1.2-IB.870	PH1 - ROMP2 - ER - Prime Paint	5	21-Oct-26	27-Oct-26		
PH1.R2.ER1.2-IB.880	PH1 - ROMP2 - ER - OH Inspection	1	22-Oct-26	22-Oct-26		
PH1.R2.ER1.2-IB.910	PH1 - ROMP2 - ER - Install Cable Tray	15	04-Nov-26	24-Nov-26		
PH1.R2.ER1.2-IB.920	PH1 - ROMP2 - ER - Pull & Terminate Wires	15	25-Nov-26	15-Dec-26		
PH1.R2.ER1.2-IB.930	PH1 - ROMP2 - ER - Install Doors & Hardware	5	16-Dec-26	23-Dec-26		
PH1.R2.ER1.2-IB.940	PH1 - ROMP2 - ER - Security Devices (By Others)	5	16-Dec-26	23-Dec-26		
PH1.R2.ER1.2-IB.950	PH1 - ROMP2 - ER - Electrical Trim-out	5	24-Dec-26	30-Dec-26		
PH1.R2.ER1.2-IB.970	PH1 - ROMP2 - ER - Security Trim-out (By Others)	5	24-Dec-26	30-Dec-26		
PH1.R2.ER1.2-IB.980	PH1 - ROMP2 - ER - Fire Alarm Trim-out	5	24-Dec-26	30-Dec-26		
PH1.R2.ER1.2-IB.990	PH1 - ROMP2 - ER - Punchlist	5	31-Dec-26	06-Jan-27		
PH1.R2.ER1.2-IB.995	PH1 - ROMP2 - ER - Final Clean	5	07-Jan-27	13-Jan-27		
PH1.R2.ER1.2-240	PH1 - ROMP2 - ER - Install VFD's	5	28-Oct-26	03-Nov-26		
PH1.R2.ER1.2-250	PH1 - ROMP2 - ER - Loose Busduct Test & Install (OFCI)	5	28-Oct-26	03-Nov-26		
PH1.R2.ER1.2-260	PH1 - ROMP2 - ER - Busduct Skid Test & Install (OFCI)	10	28-Oct-26	10-Nov-26		
PH1.R2.ER1.2-230	PH1 - ROMP2 - ER - Set Exhuast Fans	5	03-Nov-26	09-Nov-26		
PH1.R2.ER1.2-160	PH1 - ROMP2 - ER - Set USB's & AMCOP's 1.6A & 1.6B - OSA Inst	5	05-Nov-26	11-Nov-26		
PH1.R2.ER1.2-170	PH1 - ROMP2 - ER - Set XFMR's (OFCI)	5	05-Nov-26	11-Nov-26		
PH1.R2.ER1.2-180	PH1 - ROMP2 - ER - Set ATS's (OFCI)	5	05-Nov-26	11-Nov-26		
PH1.R2.ER1.2-190	PH1 - ROMP2 - ER - Set HPP's, HLP's, HUPP's (OFCI)	5	05-Nov-26	11-Nov-26		
PH1.R2.ER1.2-200	PH1 - ROMP2 - ER - Set EVCPP (OFCI)	5	05-Nov-26	11-Nov-26		
PH1.R2.ER1.2-210	PH1 - ROMP2 - ER - Set MSDB (OFCI)	5	05-Nov-26	11-Nov-26		
Cx.PH1.R2.ER1.2-XFMR.100	R2 ER 1.2 - XFMR's - Pre Startup Installer	7	16-Dec-26	25-Dec-26		
Cx.PH1.R2.ER1.2-XFMR.110	R2 ER 1.2 - XFMR's - L2 QC	1	28-Dec-26	28-Dec-26		
Cx.PH1.R2.ER1.2-XFMR.120	R2 ER 1.2 - XFMR's - Installation Verification Checklist	2	29-Dec-26	30-Dec-26		
Cx.PH1.R2.ER1.2-XFMR.130	R2 ER 1.2 - XFMR's - Yellow Tag	1	31-Dec-26	31-Dec-26		
Cx.PH1.R2.ER1.2-XFMR.140	R2 ER 1.2 - XFMR's - Energize Equipment	1	26-Jan-27	26-Jan-27		
Cx.PH1.R2.ER1.2-XFMR.150	R2 ER 1.2 - XFMR's - L3 Start-up	1	27-Jan-27	27-Jan-27		
Cx.PH1.R2.ER1.2-XFMR.160	R2 ER 1.2 - XFMR's - Thermographic Checks	1	28-Jan-27	28-Jan-27		
Cx.PH1.R2.ER1.2-XFMR.170	R2 ER 1.2 - XFMR's - Green Tag	1	29-Jan-27	29-Jan-27		
Cx.PH1.R2.ER1.2-USB.100	R2 ER 1.2 - USB's - Pre Startup Installer	5	16-Dec-26	23-Dec-26		
Cx.PH1.R2.ER1.2-USB.110	R2 ER 1.2 - USB's - Pre Startup Vendor	3	16-Dec-26	21-Dec-26		
Cx.PH1.R2.ER1.2-USB.120	R2 ER 1.2 - USB's - L2 QC	1	24-Dec-26	24-Dec-26		

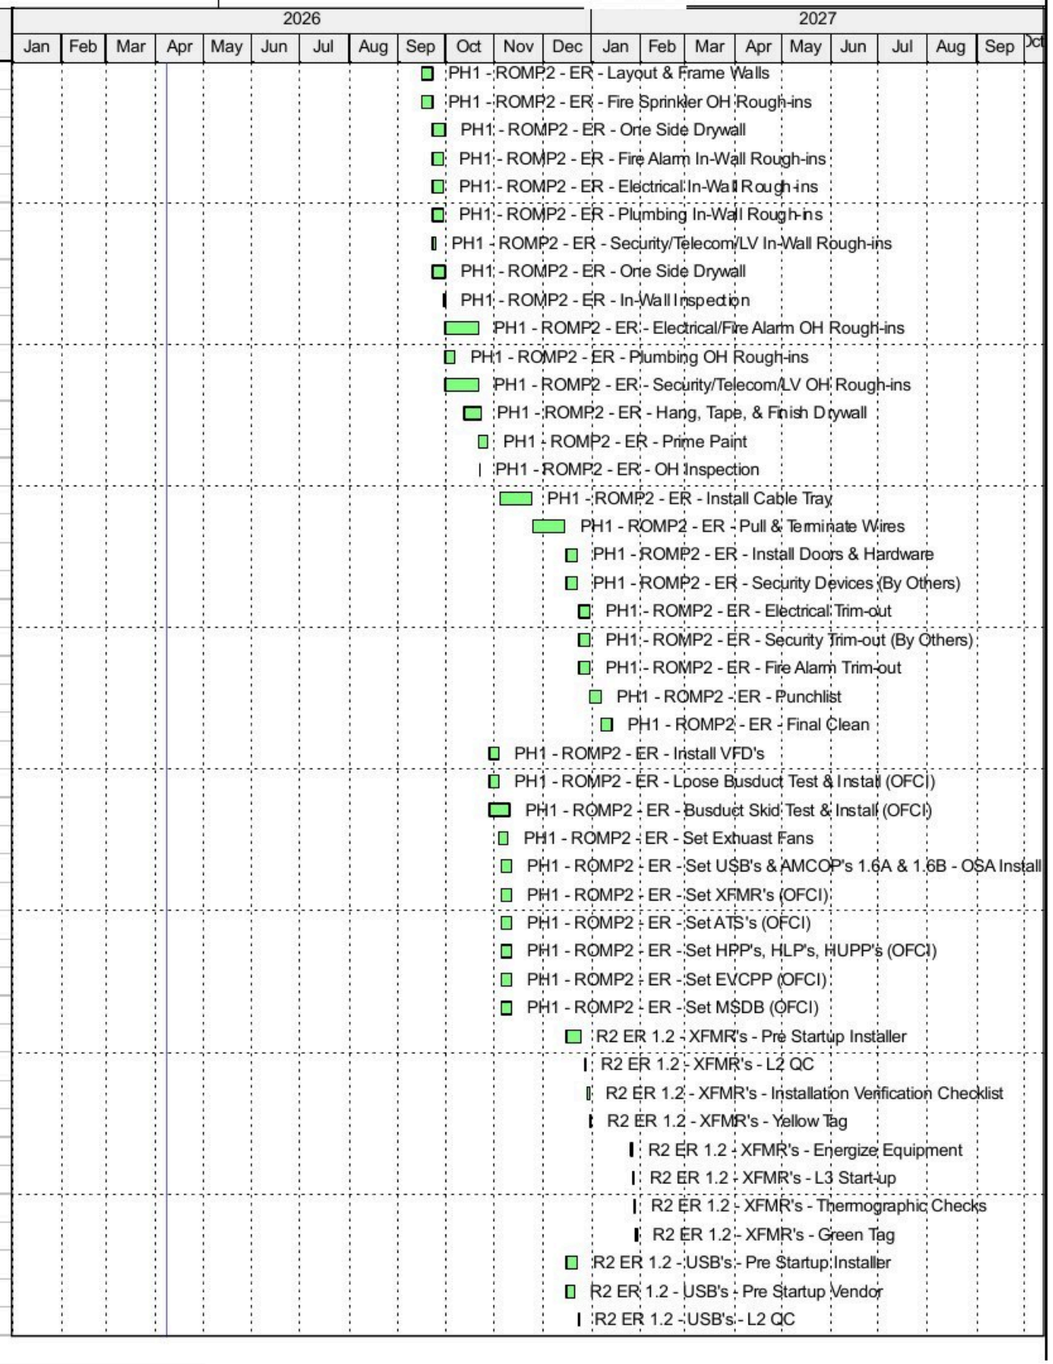


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH1.R2.ER1.2-USB.130	R2 ER 1.2 - USB's - Installation Verification Checklist	1	25-Dec-26	25-Dec-26		
Cx.PH1.R2.ER1.2-USB.140	R2 ER 1.2 - USB's - Yellow Tag	1	28-Dec-26	28-Dec-26		
Cx.PH1.R2.ER1.2-USB.150	R2 ER 1.2 - USB's - Energize Equipment	1	21-Jan-27	21-Jan-27		
Cx.PH1.R2.ER1.2-USB.160	R2 ER 1.2 - USB's - L3 Startup	4	25-Jan-27	28-Jan-27		
Cx.PH1.R2.ER1.2-USB.170	R2 ER 1.2 - USB's - EPMS SAT	1	29-Jan-27	29-Jan-27		
Cx.PH1.R2.ER1.2-USB.180	R2 ER 1.2 - USB's - Thermographic Checks	1	01-Feb-27	01-Feb-27		
Cx.PH1.R2.ER1.2-USB.190	R2 ER 1.2 - USB's - Green Tag	1	02-Feb-27	02-Feb-27		
Cx.PH1.R2.ER1.2-ATS.100	R2 ER 1.2 - ATS's - Pre Startup Installer	5	30-Dec-26	05-Jan-27		
Cx.PH1.R2.ER1.2-ATS.110	R2 ER 1.2 - ATS's - Pre Startup Vendor	3	30-Dec-26	01-Jan-27		
Cx.PH1.R2.ER1.2-ATS.120	R2 ER 1.2 - ATS's - L2 QC	1	06-Jan-27	06-Jan-27		
Cx.PH1.R2.ER1.2-ATS.130	R2 ER 1.2 - ATS's - Installation Verification Checklist	2	07-Jan-27	08-Jan-27		
Cx.PH1.R2.ER1.2-ATS.140	R2 ER 1.2 - ATS's - Yellow Tag	1	11-Jan-27	11-Jan-27		
Cx.PH1.R2.ER1.2-ATS.150	R2 ER 1.2 - ATS's - Energize Equipment	1	25-Jan-27	25-Jan-27		
Cx.PH1.R2.ER1.2-ATS.160	R2 ER 1.2 - ATS's - L3 Startup	2	26-Jan-27	27-Jan-27		
Cx.PH1.R2.ER1.2-ATS.170	R2 ER 1.2 - ATS's - EPMS SAT	1	28-Jan-27	28-Jan-27		
Cx.PH1.R2.ER1.2-ATS.180	R2 ER 1.2 - ATS's - Thermographic Checks	1	29-Jan-27	29-Jan-27		
Cx.PH1.R2.ER1.2-ATS.190	R2 ER 1.2 - ATS's - Green Tag	1	01-Feb-27	01-Feb-27		
Cx.PH1.R2.ER1.2-MSDB.100	R2 ER 1.2 - MSDB's - Pre Startup Installer	5	16-Dec-26	23-Dec-26		
Cx.PH1.R2.ER1.2-MSDB.110	R2 ER 1.2 - MSDB's - Pre Startup Vendor	3	16-Dec-26	21-Dec-26		
Cx.PH1.R2.ER1.2-MSDB.120	R2 ER 1.2 - MSDB's - L2 QC	1	24-Dec-26	24-Dec-26		
Cx.PH1.R2.ER1.2-MSDB.130	R2 ER 1.2 - MSDB's - Installation Verification Checklist	2	25-Dec-26	28-Dec-26		
Cx.PH1.R2.ER1.2-MSDB.140	R2 ER 1.2 - MSDB's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.R2.ER1.2-MSDB.150	R2 ER 1.2 - MSDB's - Energize Equipment	1	25-Jan-27	25-Jan-27		
Cx.PH1.R2.ER1.2-MSDB.160	R2 ER 1.2 - MSDB's - L3 Startup	2	26-Jan-27	27-Jan-27		
Cx.PH1.R2.ER1.2-MSDB.170	ER 1.2- MSDB's - EPMS SAT	1	28-Jan-27	28-Jan-27		
Cx.PH1.R2.ER1.2-MSDB.180	R2 ER 1.2 - MSDB's - Thermographic Checks	1	29-Jan-27	29-Jan-27		
Cx.PH1.R2.ER1.2-MSDB.190	R2 ER 1.2 - MSDB's - Green Tag	1	01-Feb-27	01-Feb-27		
Cx.PH1.R2.ER1.2-AMCOP.100	R2 ER 1.2 - AMCOP's - Pre Startup Installer	5	16-Dec-26	23-Dec-26		
Cx.PH1.R2.ER1.2-AMCOP.110	R2 ER 1.2 - AMCOP's - Pre Startup Vendor	3	16-Dec-26	21-Dec-26		
Cx.PH1.R2.ER1.2-AMCOP.120	R2 ER 1.2 - AMCOP's - L2 QC	1	24-Dec-26	24-Dec-26		
Cx.PH1.R2.ER1.2-AMCOP.130	R2 ER 1.2 - AMCOP's - Installation Verfication Checklist	2	25-Dec-26	28-Dec-26		
Cx.PH1.R2.ER1.2-AMCOP.140	R2 ER 1.2 - AMCOP's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.R2.ER1.2-AMCOP.150	R2 ER 1.2 - AMCOP's - Energize Equipment	1	25-Jan-27	25-Jan-27		
Cx.PH1.R2.ER1.2-AMCOP.160	R2 ER 1.2 - AMCOP's - L3 Startup	2	26-Jan-27	27-Jan-27		
Cx.PH1.R2.ER1.2-AMCOP.170	R2 ER 1.2 - AMCOP's - EPMS SAT	1	28-Jan-27	28-Jan-27		
Cx.PH1.R2.ER1.2-AMCOP.180	R2 ER 1.2 - AMCOP's - Thermographic Checks	1	29-Jan-27	29-Jan-27		
Cx.PH1.R2.ER1.2-AMCOP.190	R2 ER 1.2 - AMCOP's - Green Tag	1	01-Feb-27	01-Feb-27		
Cx.PH1.R2.ER1.2-CRAC.100	R2 ER 1.2 - CRAC's - Pre Startup Installer	5	25-Dec-26	31-Dec-26		
Cx.PH1.R2.ER1.2-CRAC.110	R2 ER 1.2 - CRAC's - Pre Startup Vendor	3	29-Dec-26	31-Dec-26		
Cx.PH1.R2.ER1.2-CRAC.120	R2 ER 1.2 - CRAC's - L2 QC	1	01-Jan-27	01-Jan-27		
Cx.PH1.R2.ER1.2-CRAC.130	R2 ER 1.2 - CRAC's - Installation Verification Checklist	2	04-Jan-27	05-Jan-27		
Cx.PH1.R2.ER1.2-CRAC.140	R2 ER 1.2 - RAC's - Yellow Tag	1	06-Jan-27	06-Jan-27		
Cx.PH1.R2.ER1.2-CRAC.150	R2 ER 1.2 - CRAC's - Energize Equipment	1	07-Jan-27	07-Jan-27		
Cx.PH1.R2.ER1.2-CRAC.160	R2 ER 1.2 - CRAC's - L3 Startup	1	08-Jan-27	08-Jan-27		
Cx.PH1.R2.ER1.2-CRAC.180	R2 ER 1.2 - CRAC's - BAS SAT	1	11-Jan-27	11-Jan-27		

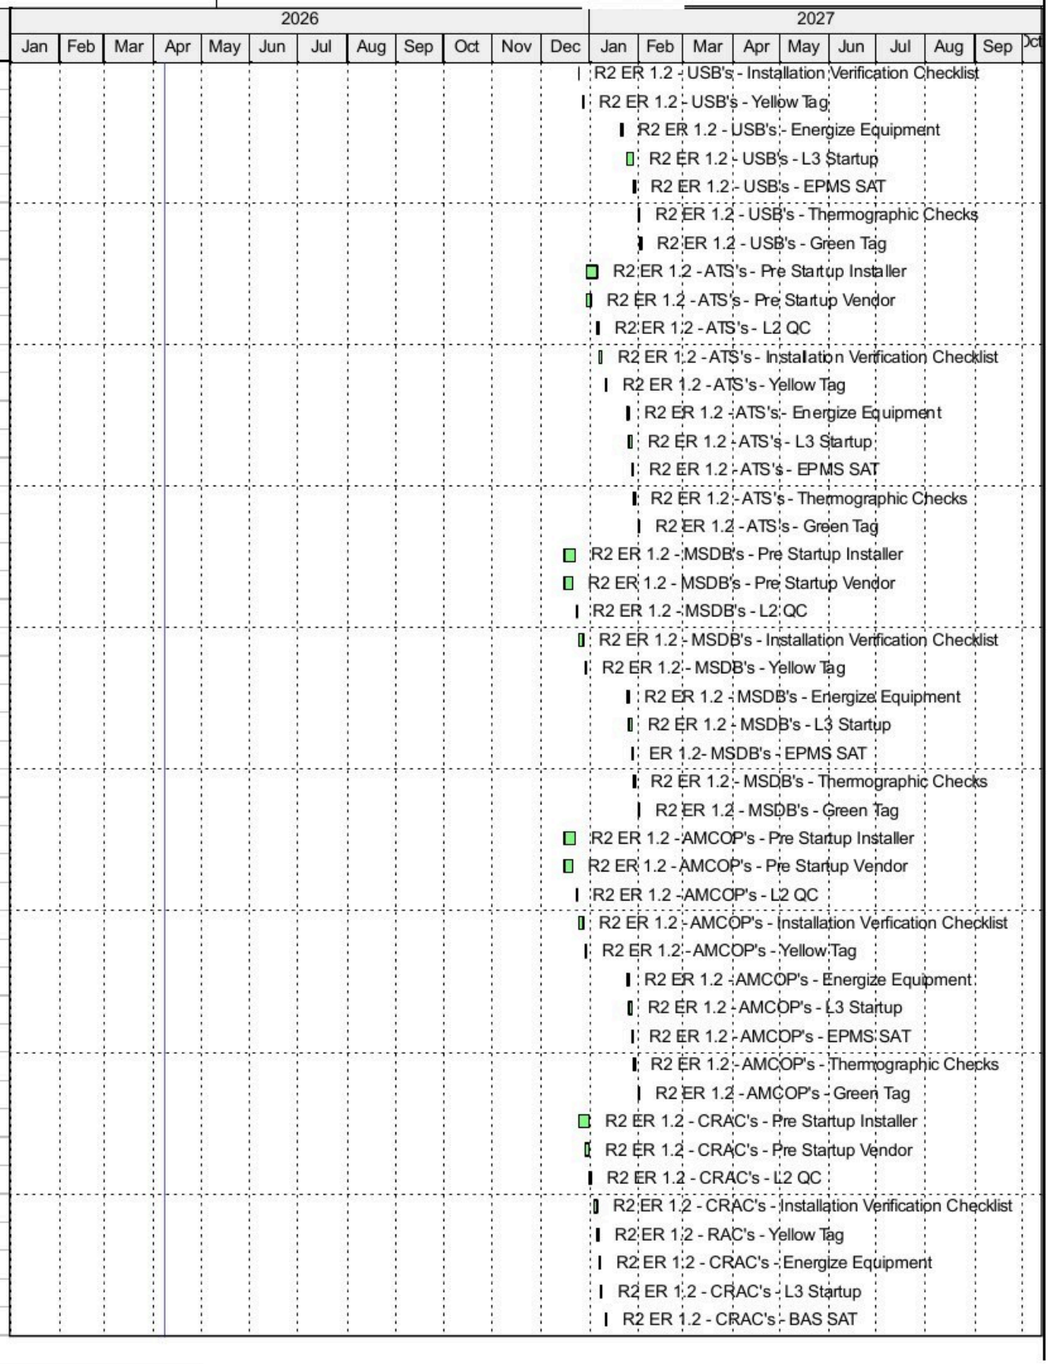

Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH1.R2.ER1.2-CRAC.170	R2 ER 1.2 - CRAC's - TAB	3	12-Jan-27	18-Jan-27		
Cx.PH1.R2.ER1.2-CRAC.190	R2 ER 1.2 - CRAC's - Green Tag	1	19-Jan-27	19-Jan-27		
Cx.PH1.R2.ER1.2-HPP.HLP.100	R2 ER 1.2 - HPP's & HLP's - Pre Startup Installer	5	16-Dec-26	23-Dec-26		
Cx.PH1.R2.ER1.2-HPP.HLP.110	R2 ER 1.2 - HPP's & HLP's - Pre Startup Vendor	3	16-Dec-26	21-Dec-26		
Cx.PH1.R2.ER1.2-HPP.HLP.120	R2 ER 1.2 - HPP's & HLP's - L2 QC	1	24-Dec-26	24-Dec-26		
Cx.PH1.R2.ER1.2-HPP.HLP.130	R2 ER 1.2 - HPP's & HLP's - Installation Verification Checklist	2	25-Dec-26	28-Dec-26		
Cx.PH1.R2.ER1.2-HPP.HLP.140	R2 ER 1.2 - HPP's & HLP's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.R2.ER1.2-HPP.HLP.150	R2 ER 1.2 - HPP's & HLP's - Energize Equipment	1	27-Jan-27	27-Jan-27		
Cx.PH1.R2.ER1.2-HPP.HLP.160	R2 ER 1.2 - HPP's & HLP's - L3 Startup	1	28-Jan-27	28-Jan-27		
Cx.PH1.R2.ER1.2-HPP.HLP.170	R2 ER 1.2 - HPP's & HLP's - EPMS SAT	1	29-Jan-27	29-Jan-27		
Cx.PH1.R2.ER1.2-HPP.HLP.180	R2 ER 1.2 - HPP's & HLP's - Thermographic Checks	1	01-Feb-27	01-Feb-27		
Cx.PH1.R2.ER1.2-HPP.HLP.190	R2 ER 1.2 - HPP's & HLP's - Green Tag	1	02-Feb-27	02-Feb-27		
Cx.PH1.R2.ER1.2-HUPP.100	R2 ER 1.2 - HUPP's - Pre Startup Installer	5	16-Dec-26	23-Dec-26		
Cx.PH1.R2.ER1.2-HUPP.110	R2 ER 1.2 - HUPP's - Pre Startup Vendor	3	16-Dec-26	21-Dec-26		
Cx.PH1.R2.ER1.2-HUPP.120	R2 ER 1.2 - HUPP's - L2 QC	1	24-Dec-26	24-Dec-26		
Cx.PH1.R2.ER1.2-HUPP.130	R2 ER 1.2 - HUPP's - Installation Verification Checklist	2	25-Dec-26	28-Dec-26		
Cx.PH1.R2.ER1.2-HUPP.140	R2 ER 1.2 - HUPP's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.R2.ER1.2-HUPP.150	R2 ER 1.2 - HUPP's - Energize Equipment	1	30-Dec-26	30-Dec-26		
Cx.PH1.R2.ER1.2-HUPP.160	R2 ER 1.2 - HUPP's - L3 Startup	1	31-Dec-26	31-Dec-26		
Cx.PH1.R2.ER1.2-HUPP.170	R2 ER 1.2 - HUPP's - EPMS SAT	1	01-Jan-27	01-Jan-27		
Cx.PH1.R2.ER1.2-HUPP.180	R2 ER 1.2 - HUPP's - Thermographic Checks	1	04-Jan-27	04-Jan-27		
Cx.PH1.R2.ER1.2-HUPP.190	R2 ER 1.2 - HUPP's - Green Tag	1	27-Jan-27	27-Jan-27		
Cx.PH1.R2.ER1.2-GENAN.100	R2 ER 1.2 - GENAN's - Pre Startup Installer	5	16-Dec-26	23-Dec-26		
Cx.PH1.R2.ER1.2-GENAN.110	R2 ER 1.2 - GENAN's - Pre Startup Vendor	3	16-Dec-26	21-Dec-26		
Cx.PH1.R2.ER1.2-GENAN.120	R2 ER 1.2 - GENAN's - L2 QC	1	24-Dec-26	24-Dec-26		
Cx.PH1.R2.ER1.2-GENAN.130	R2 ER 1.2 - GENAN's - Installation Verification Checklist	2	25-Dec-26	28-Dec-26		
Cx.PH1.R2.ER1.2-GENAN.140	R2 ER 1.2 - GENAN's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH1.R2.ER1.2-GENAN.150	R2 ER 1.2 - GENAN's - Energize Equipment	1	30-Dec-26	30-Dec-26		
Cx.PH1.R2.ER1.2-GENAN.160	R2 ER 1.2 - GENAN's - L3 Startup	1	31-Dec-26	31-Dec-26		
Cx.PH1.R2.ER1.2-GENAN.170	R2 ER 1.2 - GENAN's - EPMS SAT	1	01-Jan-27	01-Jan-27		
Cx.PH1.R2.ER1.2-GENAN.180	R2 ER 1.2 - GENAN's - Thermographics	1	04-Jan-27	04-Jan-27		
Cx.PH1.R2.ER1.2-GENAN.190	R2 ER 1.2 - GENAN's - Green Tag	1	05-Jan-27	05-Jan-27		
PH1 - Data Hall - ROMP's 1 & 2		124	08-Sep-26	26-Feb-27		
PH1.TAHU1.1-IB.500	PH1 - R1&2 - TAHU Gallery - Mechanical OH Rough-ins (High)	5	25-Sep-26	02-Oct-26	Trade	Mechanical
PH1.TAHU1.1-IB.530	PH1 - R1&2 - TAHU Gallery - Mechanical Trim-out	5	15-Dec-26	22-Dec-26	Trade	Mechanical
PH1.TAHU1.1-IB.510	PH1 - R1&2 - TAHU Gallery - Gallery Wall Interior IMP Install	5	08-Sep-26	14-Sep-26		
PH1.TAHU1.1-IB.480	PH1 - R1&2 - TAHU Gallery - Fire Sprinkler OH Rough-ins (High)	10	11-Sep-26	24-Sep-26		
PH1.TAHU1.1-IB.570	PH1 - R1&2 - TAHU Gallery - Gallery Wall Duct Install	5	15-Sep-26	21-Sep-26		
PH1.TAHU1.1-IB.600	PH1 - R1&2 - TAHU Gallery - IW OH Rough-ins (High)	10	18-Sep-26	02-Oct-26		
PH1.TAHU1.1-IB.580	PH1 - R1&2 - TAHU Gallery - Gallery Wall Security Mesh Install	5	22-Sep-26	29-Sep-26		
PH1.TAHU1.1-IB.490	PH1 - R1&2 - TAHU Gallery - Electrical/Fire Alarm OH Rough-ins (Hig	10	25-Sep-26	09-Oct-26		
PH1.TAHU1.1-IB.590	PH1 - R1&2 - TAHU Gallery - Security/Controls OH Rough-ins (High)	10	30-Sep-26	13-Oct-26		
PH1.TAHU1.1-IB.220	PH1 - R1&2 - TAHU Gallery - OH Inspections	1	14-Oct-26	14-Oct-26		
PH1.TAHU1.1-IB.160	PH1 - R1&2 - TAHU Gallery - Install Cable Tray	5	27-Oct-26	02-Nov-26		
PH1.TAHU1.1-IB.200	PH1 - R1&2 - TAHU Gallery - MEPF TAHU Connections	10	27-Oct-26	09-Nov-26		

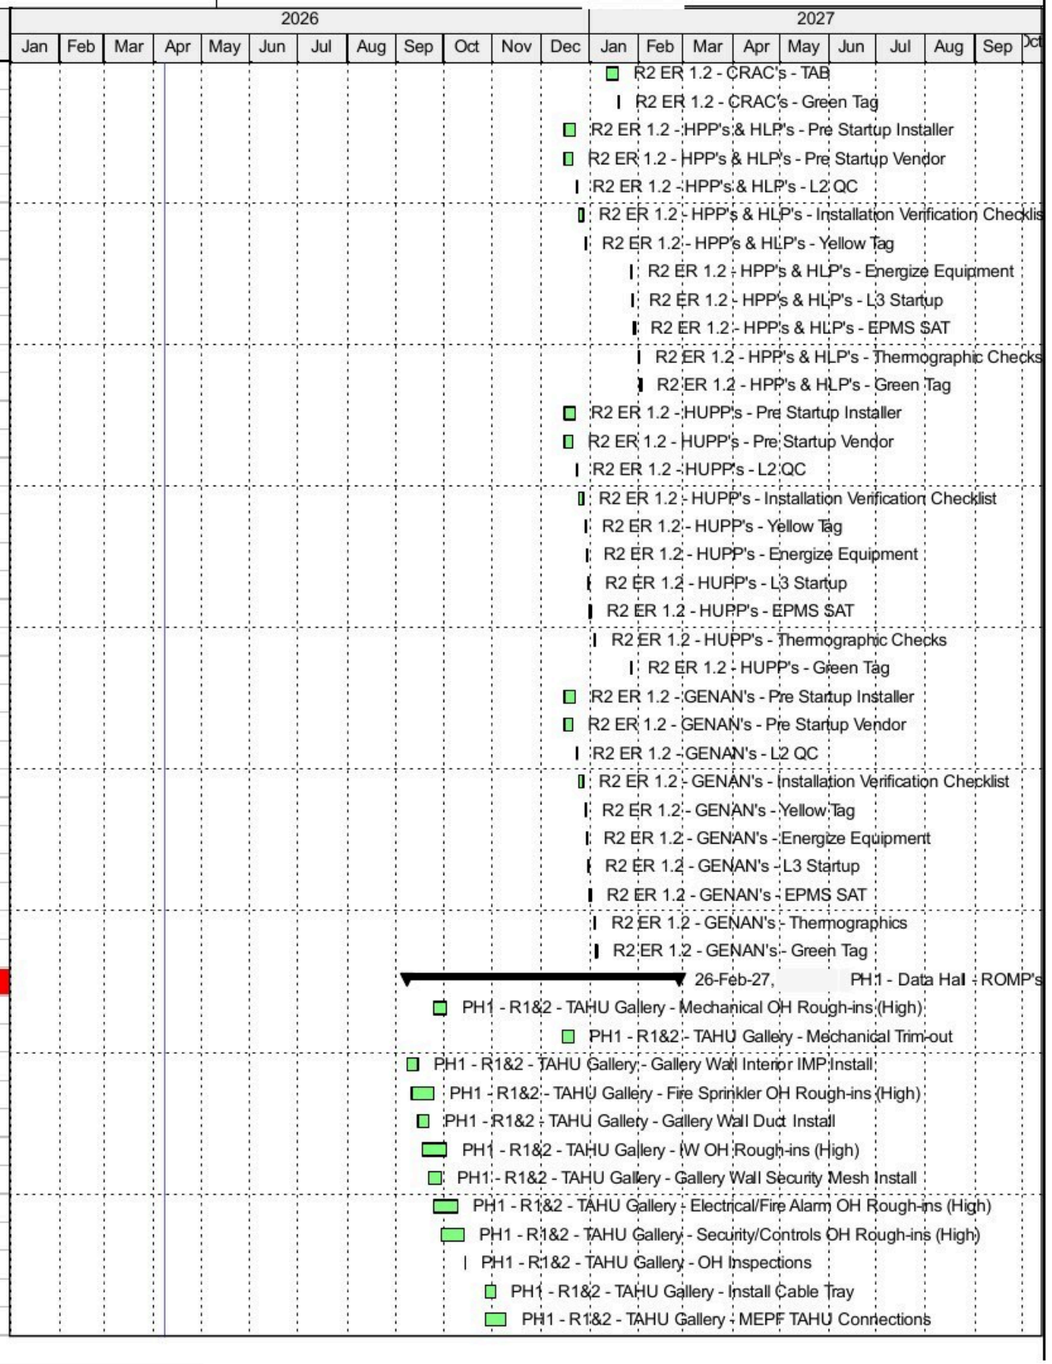


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH1.TAHU1.1-IB.610	PH1 - R1&2 - TAHU Gallery - Electrical/Fire Alarm OH Rough-ins (Lo	10	03-Nov-26	16-Nov-26		
PH1.TAHU1.1-IB.620	PH1 - R1&2 - TAHU Gallery - Security/Controls OH Rough-ins (Low)	10	03-Nov-26	16-Nov-26		
PH1.TAHU1.1-IB.170	PH1 - R1&2 - TAHU Gallery - Pull & Terminate Wires	15	24-Nov-26	14-Dec-26		
PH1.TAHU1.1-IB.520	PH1 - R1&2 - TAHU Gallery - Electrical Trim-out	5	15-Dec-26	22-Dec-26		
PH1.TAHU1.1-IB.540	PH1 - R1&2 - TAHU Gallery - Fire Alarm Trim-out	5	15-Dec-26	22-Dec-26		
PH1.TAHU1.1-IB.400	PH1 - R1&2 - TAHU Gallery - Punchlist	20	23-Dec-26	21-Jan-27		
PH1.TAHU1.1-IB.410	PH1 - R1&2 - TAHU Gallery - Final Clean	15	25-Jan-27	12-Feb-27		
PH1 - ROMP 1 - Data Hall		106	23-Sep-26	17-Feb-27		
PH1.R1.DH1.1-IB.870	PH1 - ROMP1 - DH - Mechanical OH Rough-ins	4	01-Oct-26	06-Oct-26	Trade	Mechanical
PH1.R1.DH1.1-IB.550	PH1 - ROMP1 - DH - CE#0007 - Install Liquid Cooling Systems (CFI	6	04-Jan-27	11-Jan-27	Trade	CFN/SFN Pipir
PH1.R1.DH1.1-IB.950	PH1 - ROMP1 - DH - Install Liquid Cooling Systems (SFN) (OFCI)	4	05-Jan-27	08-Jan-27	Trade	CFN/SFN Pipir
PH1.R1.DH1.1-IB.880	PH1 - ROMP1 - DH - Fire Sprinkler OH Rough-ins	5	23-Sep-26	30-Sep-26		
PH1.R1.DH1.1-IB.940	PH1 - ROMP1 - DH - Layout & Frame Walls	5	23-Sep-26	30-Sep-26		
PH1.R1.DH1.1-IB.580	PH1 - ROMP1 - DH - One-side Drywall	5	01-Oct-26	07-Oct-26		
PH1.R1.DH1.1-IB.820	PH1 - ROMP1 - DH - Electrical In-Wall Rough-ins	4	01-Oct-26	06-Oct-26		
PH1.R1.DH1.1-IB.830	PH1 - ROMP1 - DH - Fire Alarm In- Wall Rough-ins	4	01-Oct-26	06-Oct-26		
PH1.R1.DH1.1-IB.840	PH1 - ROMP1 - DH - Security/Telecom/LV In-Wall Rough-ins	4	01-Oct-26	06-Oct-26		
PH1.R1.DH1.1-IB.850	PH1 - ROMP1 - DH - Plumbing In-Wall Rough-ins	2	01-Oct-26	02-Oct-26		
PH1.R1.DH1.1-IB.970	PH1 - ROMP1 - DH - Hang Door Frames	5	01-Oct-26	07-Oct-26		
PH1.R1.DH1.1-IB.560	PH1 - ROMP1 - DH - In-Wall Inspections	1	07-Oct-26	07-Oct-26		
PH1.R1.DH1.1-IB.860	PH1 - ROMP1 - DH - Electrical/Fire Alarm OH Rough-ins	15	07-Oct-26	27-Oct-26		
PH1.R1.DH1.1-IB.890	PH1 - ROMP1 - DH - Plumbing OH Rough-ins	4	07-Oct-26	12-Oct-26		
PH1.R1.DH1.1-IB.980	PH1 - ROMP1 - DH - Security/Telecom/LV OH Rough-ins	15	07-Oct-26	27-Oct-26		
PH1.R1.DH1.1-IB.420	PH1 - ROMP1 - DH - Hang, Tape, & Finish Drywall	10	08-Oct-26	21-Oct-26		
PH1.R1.DH1.1-IB.430	PH1 - ROMP1 - DH - Prime Paint	5	19-Oct-26	23-Oct-26		
PH1.R1.DH1.1-IB.570	PH1 - ROMP1 - DH - OH Inspections	1	28-Oct-26	28-Oct-26		
PH1.R1.DH1.1-IB.450	PH1 - ROMP1 - DH - Ceiling System	5	29-Oct-26	04-Nov-26		
PH1.R1.DH1.1-IB.480	PH1 - ROMP1 - DH - Install Cable Tray	10	05-Nov-26	18-Nov-26		
PH1.R1.DH1.1-IB.520	PH1 - ROMP1 - DH - Install Rack Whips (OFCI)	5	19-Nov-26	25-Nov-26		
PH1.R1.DH1.1-IB.470	PH1 - ROMP1 - DH - Pull & Terminate Wires	15	24-Nov-26	14-Dec-26		
PH1.R1.DH1.1-IB.490	PH1 - ROMP1 - DH - Install Doors & Hardware	5	15-Dec-26	22-Dec-26		
PH1.R1.DH1.1-IB.590	PH1 - ROMP1 - DH - Install Security Devices (By Others)	5	15-Dec-26	22-Dec-26		
PH1.R1.DH1.1-IB.530	PH1 - ROMP1 - DH - Temporary Barrier Wall	5	22-Dec-26	28-Dec-26		
PH1.R1.DH1.1-IB.900	PH1 - ROMP1 - DH - Mechancial Trim-out	5	23-Dec-26	29-Dec-26		
PH1.R1.DH1.1-IB.910	PH1 - ROMP1 - DH - Electrical Trim-out	5	23-Dec-26	29-Dec-26		
PH1.R1.DH1.1-IB.920	PH1 - ROMP1 - DH - Fire Alarm Trim-out	5	23-Dec-26	29-Dec-26		
PH1.R1.DH1.1-IB.990	PH1 - ROMP1 - DH - Security Trim-out (By Others)	5	23-Dec-26	29-Dec-26		
PH1.R1.DH1.1-IB.540	PH1 - ROMP1 - DH - Punchlist	15	30-Dec-26	21-Jan-27		
PH1.R1.DH1.1-IB.960	PH1 - ROMP1 - DH - CE#0007 - Flush and Fill Liquid	10	12-Jan-27	28-Jan-27		
PH1.R1.DH1.1-IB.790	PH1 - ROMP1 - DH - Final Clean	10	25-Jan-27	05-Feb-27		
PH1 - ROMP 1 - Data Hall Equipment		52	29-Oct-26	08-Jan-27		
PH1.R1.DH1.1-IB.140	PH1 - ROMP1 - DH - Set MTS-IRHX (OFCI)	5	05-Nov-26	11-Nov-26	Trade	HVAC
PH1.R1.DH1.1-IB.130	PH1 - ROMP1 - DH - Set IRHX (OFCI)	5	04-Jan-27	08-Jan-27	Trade	HVAC
PH1.R1.DH1.1-IB.510	PH1 - ROMP1 - DH - Install Racks (OFCI)	10	29-Oct-26	11-Nov-26		
PH1.R1.DH1.1-IB.500	PH1 - ROMP1 - DH - Install HAC's	10	24-Nov-26	07-Dec-26		

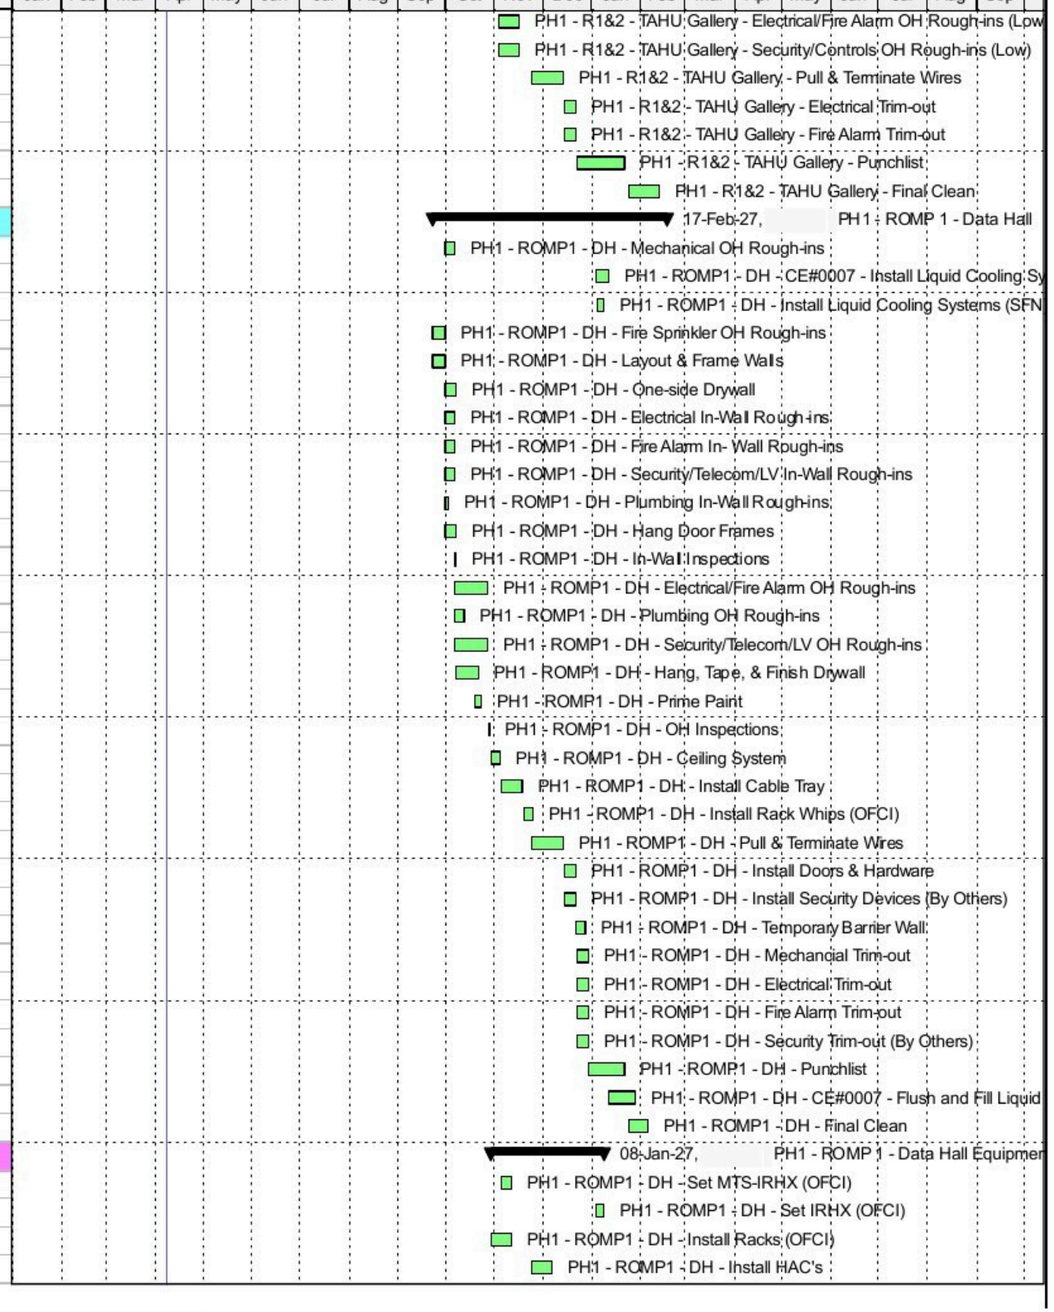


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH1.R1.DH1.1-IB.120	PH1 - ROMP1 - DH - Set PDC's (OFCI)	5	14-Dec-26	21-Dec-26		
PH1 - ROMP 1 Data Hall Commissioning		47	15-Dec-26	17-Feb-27		
Cx.PH1.R1.DH1.1-PDC.100	R1 DH1.1 - PDC's - Pre Startup Installer	3	15-Dec-26	18-Dec-26		
Cx.PH1.R1.DH1.1-PDC.110	R1 DH1.1 - PDC's - Pre Startup Vendor	3	15-Dec-26	18-Dec-26		
Cx.PH1.R1.DH1.1-PDC.120	R1 DH1.1 - PDC's - L2 QC	1	21-Dec-26	21-Dec-26		
Cx.PH1.R1.DH1.1-PDC.130	R1 DH1.1 - PDC's - Installation Verification Checklist	1	22-Dec-26	22-Dec-26		
Cx.PH1.R1.DH1.1-PDC.140	R1 DH1.1 - PDC's - Yellow Tag	1	23-Dec-26	23-Dec-26		
Cx.PH1.R1.DH1.1-PDC.150	R1 DH1.1 - PDC's - Energize Equipment	1	25-Jan-27	25-Jan-27		
Cx.PH1.R1.DH1.1-PDC.160	R1 DH1.1 - PDC's - L3 Startup	2	26-Jan-27	27-Jan-27		
Cx.PH1.R1.DH1.1-PDC.170	R1 DH1.1 - PDC's - EPMS SAT	1	28-Jan-27	28-Jan-27		
Cx.PH1.R1.DH1.1-PDC.180	R1 DH1.1 - PDC's - Thermographic Checks	1	29-Jan-27	29-Jan-27		
Cx.PH1.R1.DH1.1-PDC.190	R1 DH1.1 - PDC's - Green Tag	1	01-Feb-27	01-Feb-27		
Cx.PH1.R1.DH1.1-IRHX.300	R1 DH1.1 - IRHX's - Pre Startup Installer	5	29-Jan-27	04-Feb-27		
Cx.PH1.R1.DH1.1-IRHX.310	R1 DH1.1 - IRHX's - Pre Startup Vendor	3	29-Jan-27	02-Feb-27		
Cx.PH1.R1.DH1.1-IRHX.320	R1 DH1.1 - IRHX's - L2 QC	1	05-Feb-27	05-Feb-27		
Cx.PH1.R1.DH1.1-IRHX.330	R1 DH1.1 - IRHX's - Installation Verification Checklist	1	08-Feb-27	08-Feb-27		
Cx.PH1.R1.DH1.1-IRHX.340	R1 DH1.1 - IRHX's - Yellow Tag	1	09-Feb-27	09-Feb-27		
Cx.PH1.R1.DH1.1-IRHX.350	R1 DH1.1 - IRHX's - Energize Equipment	1	10-Feb-27	10-Feb-27		
Cx.PH1.R1.DH1.1-IRHX.360	R1 DH1.1 - IRHX's - L3 Startup	2	11-Feb-27	12-Feb-27		
Cx.PH1.R1.DH1.1-IRHX.370	R1 DH1.1 - IRHX's - EPMS SAT	1	15-Feb-27	15-Feb-27		
Cx.PH1.R1.DH1.1-IRHX.380	R1 DH1.1 - IRHX's - Thermographic Checks	1	16-Feb-27	16-Feb-27		
Cx.PH1.R1.DH1.1-IRHX.390	R1 DH1.1 - IRHX's - Green Tag	1	17-Feb-27	17-Feb-27		
Cx.PH1.R1.DH1.1-MTS-IRHX.300R1	DH1.1 - MTS-IRHX's - Pre Startup Installer	5	15-Dec-26	22-Dec-26		
Cx.PH1.R1.DH1.1-MTS-IRHX.310R1	DH1.1 - MTS-IRHX's - Pre Startup Vendor	3	15-Dec-26	18-Dec-26		
Cx.PH1.R1.DH1.1-MTS-IRHX.320R1	DH1.1 - MTS-IRHX's - L2 QC	1	23-Dec-26	23-Dec-26		
Cx.PH1.R1.DH1.1-MTS-IRHX.330R1	DH1.1 - MTS-IRHX's - Installation Verification Checklist	1	24-Dec-26	24-Dec-26		
Cx.PH1.R1.DH1.1-MTS-IRHX.340R1	DH1.1 - MTS-IRHX's - Yellow Tag	1	25-Dec-26	25-Dec-26		
Cx.PH1.R1.DH1.1-MTS-IRHX.350R1	DH1.1 - MTS-IRHX's - Energize Equipment	1	26-Jan-27	26-Jan-27		
Cx.PH1.R1.DH1.1-MTS-IRHX.360R1	DH1.1 - MTS-IRHX's - L3 Startup	2	27-Jan-27	28-Jan-27		
Cx.PH1.R1.DH1.1-MTS-IRHX.370R1	DH1.1 - MTS-IRHX's - EPMS SAT	1	29-Jan-27	29-Jan-27		
Cx.PH1.R1.DH1.1-MTS-IRHX.380R1	DH1.1 - MTS-IRHX's - Thermographic Checks	1	01-Feb-27	01-Feb-27		
Cx.PH1.R1.DH1.1-MTS-IRHX.390R1	DH1.1 - MTS-IRHX's - Green Tag	1	02-Feb-27	02-Feb-27		
PH1 - ROMP 2 - Data Hall		113	23-Sep-26	26-Feb-27		
PH1.R2.DH1.2-IB.1170	PH1 - ROMP2 - DH - Mechanical OH Rough-ins	4	01-Oct-26	06-Oct-26	Trade	Mechanical
PH1.R2.DH1.2-IB.1240	PH1 - ROMP2 - DH - Install Liquid Cooling Systems (SFN) (OFCI)	4	11-Jan-27	18-Jan-27	Trade	CFN/SFN Pipir
PH1.R2.DH1.2-IB.1050	PH1 - ROMP2 - DH - CE#0007 - Install Liquid Cooling Systems (CFI	6	12-Jan-27	21-Jan-27	Trade	CFN/SFN Pipir
PH1.R2.DH1.2-IB.1180	PH1 - ROMP2 - DH - Fire Sprinkler OH Rough-ins	5	23-Sep-26	30-Sep-26		
PH1.R2.DH1.2-IB.1230	PH1 - ROMP2 - DH - Layout & Frame Walls	5	23-Sep-26	30-Sep-26		
PH1.R2.DH1.2-IB.1080	PH1 - ROMP2 - DH - One-side Drywall	5	01-Oct-26	07-Oct-26		
PH1.R2.DH1.2-IB.1120	PH1 - ROMP2 - DH - Electrical In-Wall Rough-ins	4	01-Oct-26	06-Oct-26		
PH1.R2.DH1.2-IB.1130	PH1 - ROMP2 - DH - Fire Alarm In- Wall Rough-ins	4	01-Oct-26	06-Oct-26		
PH1.R2.DH1.2-IB.1140	PH1 - ROMP2 - DH - Security/Telecom/LV In-Wall Rough-ins	4	01-Oct-26	06-Oct-26		
PH1.R2.DH1.2-IB.1150	PH1 - ROMP2 - DH - Plumbing In-Wall Rough-ins	2	01-Oct-26	02-Oct-26		
PH1.R2.DH1.2-IB.1260	PH1 - ROMP2 - DH - Hang Door Frames	5	01-Oct-26	07-Oct-26		
PH1.R2.DH1.2-IB.1060	PH1 - ROMP2 - DH - In-Wall Inspections	1	07-Oct-26	07-Oct-26		

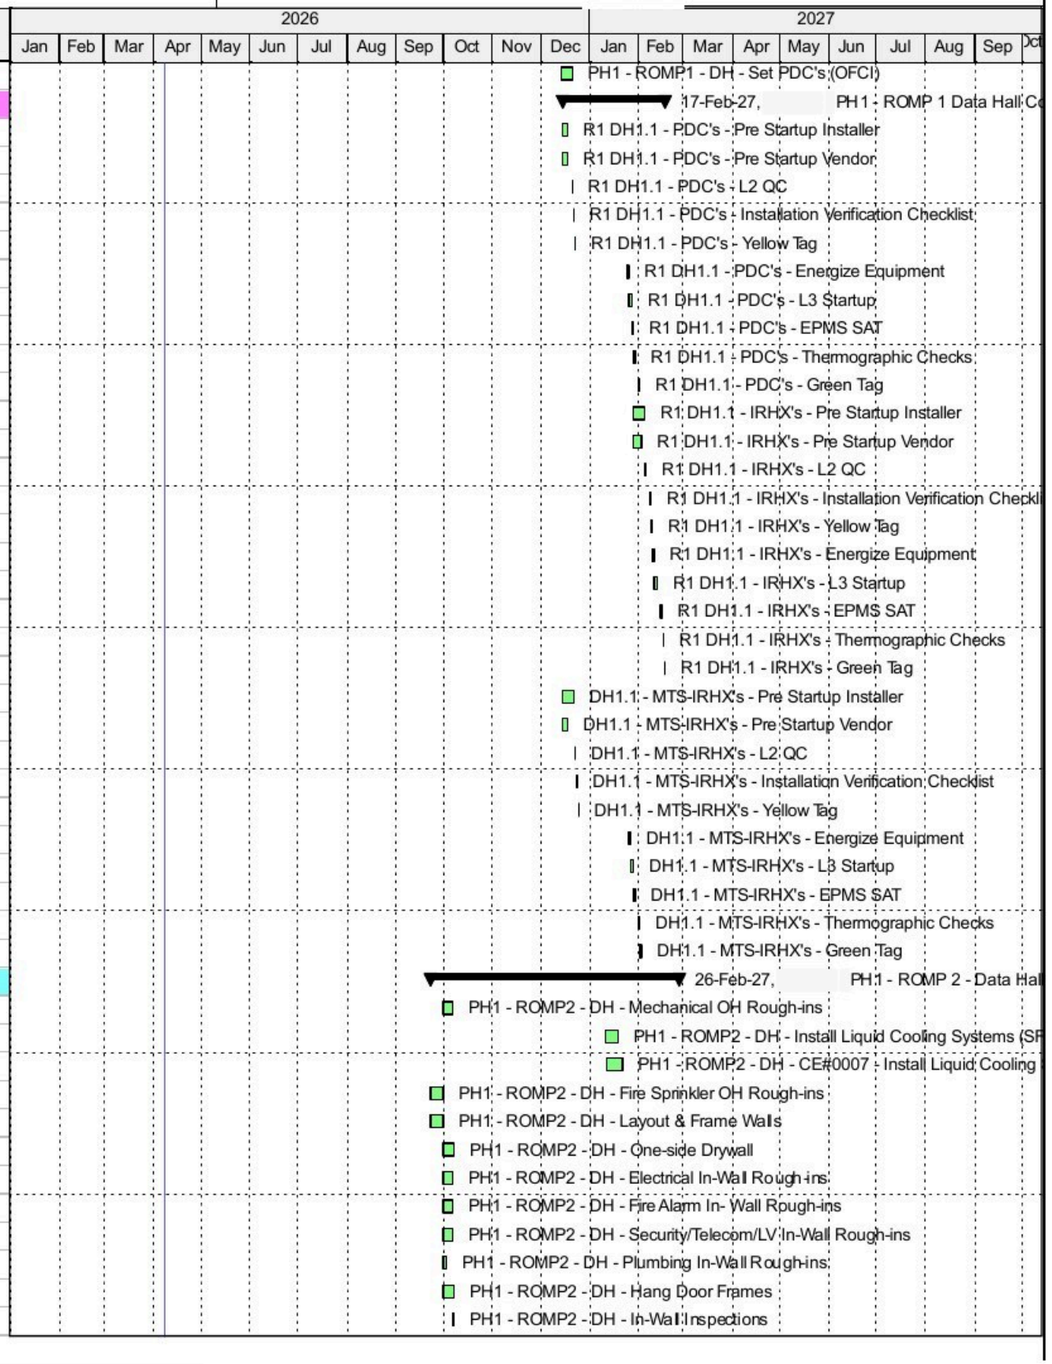


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule


Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH1.R2.DH1.2-IB.1160	PH1 - ROMP2 - DH - Electrical/Fire Alarm OH Rough-ins	15	07-Oct-26	27-Oct-26		
PH1.R2.DH1.2-IB.1190	PH1 - ROMP2 - DH - Plumbing OH Rough-ins	4	07-Oct-26	12-Oct-26		
PH1.R2.DH1.2-IB.1270	PH1 - ROMP2 - DH - Security/Telecom/LV OH Rough-ins	15	07-Oct-26	27-Oct-26		
PH1.R2.DH1.2-IB.950	PH1 - ROMP2 - DH - Hang, Tape, & Finish Drywall	10	08-Oct-26	21-Oct-26		
PH1.R2.DH1.2-IB.960	PH1 - ROMP2 - DH - Prime Paint	5	19-Oct-26	23-Oct-26		
PH1.R2.DH1.2-IB.1070	PH1 - ROMP2 - DH - OH Inspections	1	28-Oct-26	28-Oct-26		
PH1.R2.DH1.2-IB.970	PH1 - ROMP2 - DH - Ceiling System	5	29-Oct-26	04-Nov-26		
PH1.R2.DH1.2-IB.990	PH1 - ROMP2 - DH - Install Cable Tray	10	05-Nov-26	18-Nov-26		
PH1.R2.DH1.2-IB.1030	PH1 - ROMP2 - DH - Install Rack Whips (OFCI)	5	19-Nov-26	25-Nov-26		
PH1.R2.DH1.2-IB.980	PH1 - ROMP2 - DH - Pull & Terminate Wires	15	24-Nov-26	14-Dec-26		
PH1.R2.DH1.2-IB.1000	PH1 - ROMP2 - DH - Install Doors & Hardware	5	15-Dec-26	22-Dec-26		
PH1.R2.DH1.2-IB.1040	PH1 - ROMP2 - DH - Temporary Barrier Wall	5	22-Dec-26	28-Dec-26		
PH1.R2.DH1.2-IB.1200	PH1 - ROMP2 - DH - Mechancial Trim-out	5	23-Dec-26	29-Dec-26		
PH1.R2.DH1.2-IB.1210	PH1 - ROMP2 - DH - Electrical Trim-out	5	23-Dec-26	29-Dec-26		
PH1.R2.DH1.2-IB.1220	PH1 - ROMP2 - DH - Fire Alarm Trim-out	5	23-Dec-26	29-Dec-26		
PH1.R2.DH1.2-IB.1090	PH1 - ROMP2 - DH - Install Security Devices (By Others)	5	29-Dec-26	04-Jan-27		
PH1.R2.DH1.2-IB.1280	PH1 - ROMP2 - Security Trim-out (By Others)	5	05-Jan-27	11-Jan-27		
PH1.R2.DH1.2-IB.1250	PH1 - ROMP2 - DH - CE#0007 - Flush and Fill Liquid	10	25-Jan-27	05-Feb-27		
PH1.R2.DH1.2-IB.1100	PH1 - ROMP2 - DH - Punchlist	5	08-Feb-27	12-Feb-27		
PH1.R2.DH1.2-IB.1110	PH1 - ROMP2 - DH - Final Clean	10	15-Feb-27	26-Feb-27		
PH1 - ROMP 2 - Data Hall Equipment		52	29-Oct-26	08-Jan-27		
PH1.R2.DH1.2-IB.180	PH1 - ROMP2 - DH - Set MTS-IRHX (OFCI)	5	05-Nov-26	11-Nov-26	Trade	HVAC
PH1.R2.DH1.2-IB.170	PH1 - ROMP2 - DH - Set IRHX's (OFCI)	5	04-Jan-27	08-Jan-27	Trade	HVAC
PH1.R2.DH1.2-IB.1020	PH1 - ROMP2 - DH - Install Racks (OFCI)	10	29-Oct-26	11-Nov-26		
PH1.R2.DH1.2-IB.1010	PH1 - ROMP2 - DH - Install HAC's	10	24-Nov-26	07-Dec-26		
PH1.R2.DH1.2-IB.160	PH1 - ROMP2 - DH - Set PDC's (OFCI)	5	14-Dec-26	21-Dec-26		
PH1 - ROMP 2 - Data Hall Commissioning		53	15-Dec-26	25-Feb-27		
Cx.PH1.R2.DH1.2-PDC.200	R2 DH1.1 - PDC's - Pre Startup Installer	3	15-Dec-26	18-Dec-26		
Cx.PH1.R2.DH1.2-PDC.210	R2 DH1.1 - PDC's - Pre Startup Vendor	3	15-Dec-26	18-Dec-26		
Cx.PH1.R2.DH1.2-PDC.220	R2 DH1.1 - PDC's - L2 QC	1	21-Dec-26	21-Dec-26		
Cx.PH1.R2.DH1.2-PDC.230	R2 DH1.1 - PDC's - Installation Verification Checklist	1	22-Dec-26	22-Dec-26		
Cx.PH1.R2.DH1.2-PDC.240	R2 DH1.1 - PDC's - Yellow Tag	1	23-Dec-26	23-Dec-26		
Cx.PH1.R2.DH1.2-PDC.250	R2 DH1.1 - PDC's - Energize Equipment	1	29-Dec-26	29-Dec-26		
Cx.PH1.R2.DH1.2-PDC.260	R2 DH1.1 - PDC's - L3 Startup	2	30-Dec-26	31-Dec-26		
Cx.PH1.R2.DH1.2-PDC.270	R2 DH1.1 - PDC's - EPMS SAT	1	01-Jan-27	01-Jan-27		
Cx.PH1.R2.DH1.2-PDC.280	R2 DH1.1 - PDC's - Thermographic Checks	1	04-Jan-27	04-Jan-27		
Cx.PH1.R2.DH1.2-PDC.290	R2 DH1.1 - PDC's - Green Tag	1	05-Jan-27	05-Jan-27		
Cx.PH1.R2.DH1.2-IRHX.200	R2 DH1.1 - IRHX's - Pre Startup Installer	5	08-Feb-27	12-Feb-27		
Cx.PH1.R2.DH1.2-IRHX.210	R2 DH1.1 - IRHX's - Pre Startup Vendor	3	08-Feb-27	10-Feb-27		
Cx.PH1.R2.DH1.2-IRHX.220	R2 DH1.1 - IRHX's - L2 QC	1	15-Feb-27	15-Feb-27		
Cx.PH1.R2.DH1.2-IRHX.230	R2 DH1.1 - IRHX's - Installation Verification Checklist	1	16-Feb-27	16-Feb-27		
Cx.PH1.R2.DH1.2-IRHX.240	R2 DH1.1 - IRHX's - Yellow Tag	1	17-Feb-27	17-Feb-27		
Cx.PH1.R2.DH1.2-IRHX.250	R2 DH1.1 - IRHX's - Energize Equipment	1	18-Feb-27	18-Feb-27		
Cx.PH1.R2.DH1.2-IRHX.260	R2 DH1.1 - IRHX's - L3 Startup	2	19-Feb-27	22-Feb-27		
Cx.PH1.R2.DH1.2-IRHX.270	R2 DH1.1 - IRHX's - EPMS SAT	1	23-Feb-27	23-Feb-27		

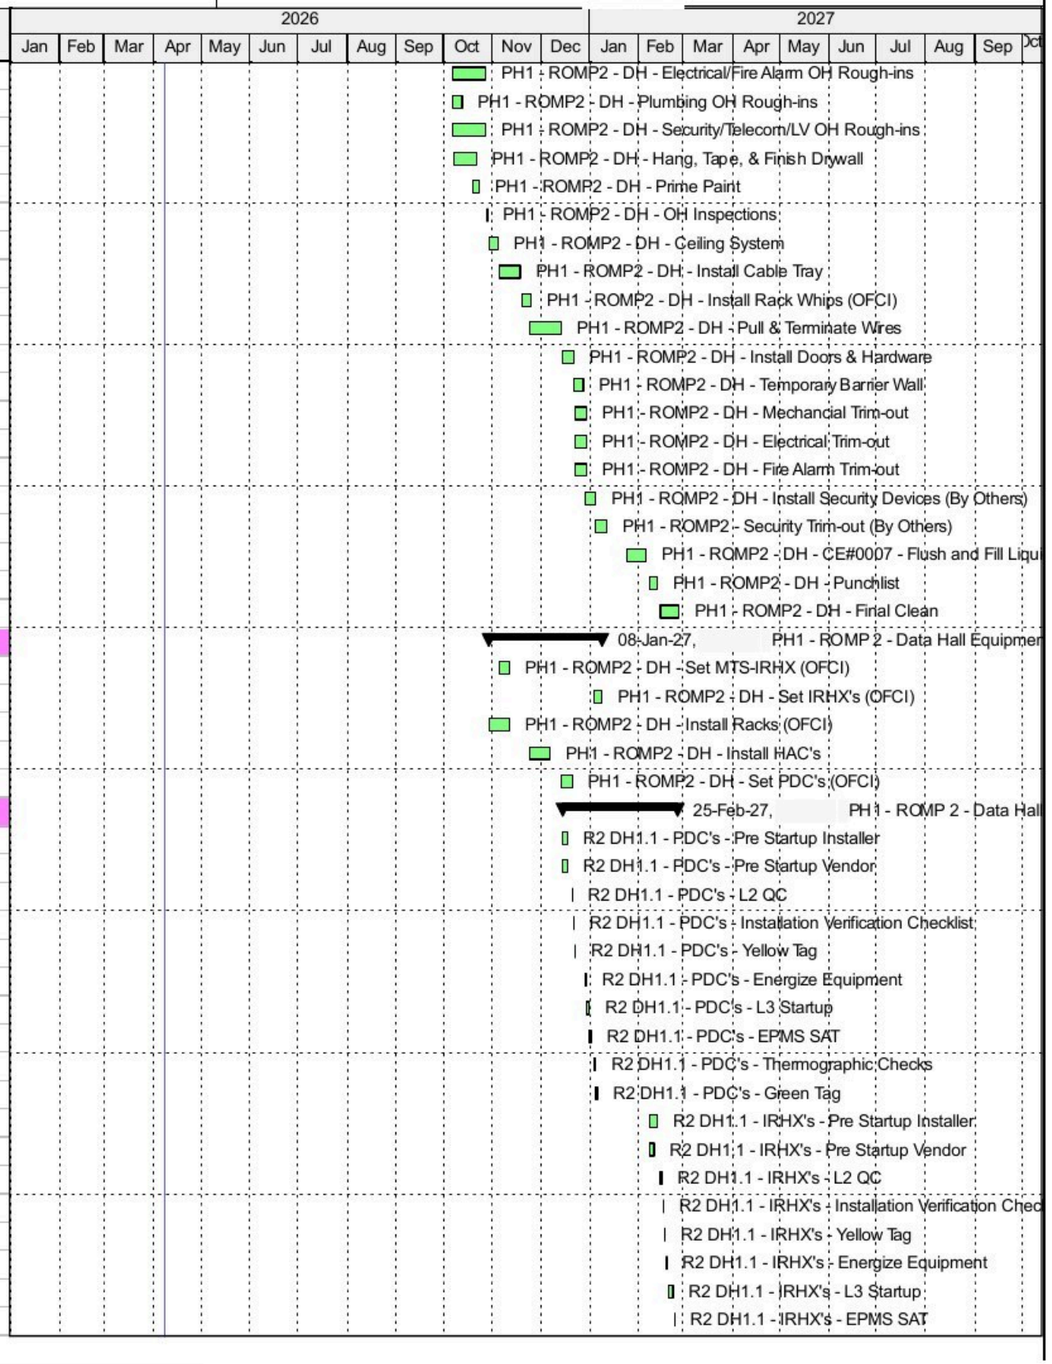

Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH1.R2.DH1.2-IRHX.280	R2 DH1.1 - IRHX's - Thermographic Checks	1	24-Feb-27	24-Feb-27		
Cx.PH1.R2.DH1.2-IRHX.290	R2 DH1.1 - IRHX's - Green Tag	1	25-Feb-27	25-Feb-27		
Cx.PH1.R2.DH1.2-MTS-IRHX.200R2	DH1.1 - MTS-IRHX's - Pre Startup Installer	5	15-Dec-26	22-Dec-26		
Cx.PH1.R2.DH1.2-MTS-IRHX.210R2	DH1.1 - MTS-IRHX's - Pre Startup Vendor	3	15-Dec-26	18-Dec-26		
Cx.PH1.R2.DH1.2-MTS-IRHX.220R2	DH1.1 - MTS-IRHX's - L2 QC	1	23-Dec-26	23-Dec-26		
Cx.PH1.R2.DH1.2-MTS-IRHX.230R2	DH1.1 - MTS-IRHX's - Installation Verification Checklist	1	24-Dec-26	24-Dec-26		
Cx.PH1.R2.DH1.2-MTS-IRHX.240R2	DH1.1 - MTS-IRHX's - Yellow Tag	1	25-Dec-26	25-Dec-26		
Cx.PH1.R2.DH1.2-MTS-IRHX.250R2	DH1.1 - MTS-IRHX's - Energize Equipment	1	30-Dec-26	30-Dec-26		
Cx.PH1.R2.DH1.2-MTS-IRHX.260R2	DH1.1 - MTS-IRHX's - L3 Startup	2	31-Dec-26	01-Jan-27		
Cx.PH1.R2.DH1.2-MTS-IRHX.270R2	DH1.1 - MTS-IRHX's - EPMS SAT	1	04-Jan-27	04-Jan-27		
Cx.PH1.R2.DH1.2-MTS-IRHX.280R2	DH1.1 - MTS-IRHX's - Thermographic Checks	1	05-Jan-27	05-Jan-27		
Cx.PH1.R2.DH1.2-MTS-IRHX.290R2	DH1.1 - MTS-IRHX's - Green Tag	1	06-Jan-27	06-Jan-27		
PH1 - ROMP 1 & 2 - TAHU Gallery 1.1 Corridor		41	27-Oct-26	22-Dec-26		
PH1.TAHU1.1-IB.100	PH1 - R1&2 - TAHU Gallery Corr - Layout & Frame Walls	5	27-Oct-26	02-Nov-26		
PH1.TAHU1.1-IB.440	PH1 - R1&2 - TAHU Gallery Corr - Electrical In-Wall Rough-ins	4	03-Nov-26	06-Nov-26		
PH1.TAHU1.1-IB.450	PH1 - R1&2 - TAHU Gallery Corr - Fire Alarm In-Wall Rough-ins	4	03-Nov-26	06-Nov-26		
PH1.TAHU1.1-IB.460	PH1 - R1&2 - TAHU Gallery Corr - Security/Telecom/LV In-Wall Roug	4	03-Nov-26	06-Nov-26		
PH1.TAHU1.1-IB.470	PH1 - R1&2 - TAHU Gallery Corr - Plumbing In-Wall Rough-ins	2	03-Nov-26	04-Nov-26		
PH1.TAHU1.1-IB.560	PH1 - R1&2 - TAHU Gallery Corr - Hang Door Frames	3	03-Nov-26	05-Nov-26		
PH1.TAHU1.1-IB.210	PH1 - R1&2 - TAHU Gallery Corr - In-wall Inspections	1	09-Nov-26	09-Nov-26		
PH1.TAHU1.1-IB.130	PH1 - R1&2 - TAHU Gallery Corr - Hang, Tape, & Finish Drywall	10	10-Nov-26	23-Nov-26		
PH1.TAHU1.1-IB.140	PH1 - R1&2 - TAHU Gallery Corr - Prime Paint	5	19-Nov-26	25-Nov-26		
PH1.TAHU1.1-IB.150	PH1 - R1&2 - TAHU Gallery Corr - Ceiling System	5	26-Nov-26	02-Dec-26		
PH1.TAHU1.1-IB.240	PH1 - R1&2 - TAHU Gallery Corr - Install Security Devices (By Others	5	26-Nov-26	02-Dec-26		
PH1.TAHU1.1-IB.550	PH1 - R1&2 - TAHU Gallery Corr - Security Trim-out (By Others)	5	03-Dec-26	09-Dec-26		
PH1.TAHU1.1-IB.180	PH1 - R1&2 - TAHU Gallery Corr - Install Doors & Hardware	5	15-Dec-26	22-Dec-26		
PH1 - ROMP 1 & 2 - TAHU Gallery 1.1 Equipment		7	16-Oct-26	26-Oct-26		
PH1.TAHU1.1-120	PH1 - R1&2 - TAHU Gallery - Set TAHU's (OFCI)	7	16-Oct-26	26-Oct-26	Trade	HVAC
PH1 - ROMP 1 & 2 - TAHU Gallery 1.1 Commissioning		46	08-Dec-26	09-Feb-27		
Cx.PH1.TGAL1.1-TAHU.100	TAHU Gallery 1.1 - TAHU's - Pre Startup Installer	5	08-Dec-26	14-Dec-26		
Cx.PH1.TGAL1.1-TAHU.110	TAHU Gallery 1.1 - TAHU's - Pre Startup Vendor	5	08-Dec-26	14-Dec-26		
Cx.PH1.TGAL1.1-TAHU.120	TAHU Gallery 1.1 - TAHU's - L2 QC	1	15-Dec-26	15-Dec-26		
Cx.PH1.TGAL1.1-TAHU.130	TAHU Gallery 1.1 - TAHU's - Installation Verification Checklist	2	16-Dec-26	18-Dec-26		
Cx.PH1.TGAL1.1-TAHU.140	TAHU Gallery 1.1 - TAHU's - Yellow Tag	1	21-Dec-26	21-Dec-26		
Cx.PH1.TGAL1.1-TAHU.150	TAHU Gallery 1.1 - TAHU's - Energize Equipment	1	25-Jan-27	25-Jan-27		
Cx.PH1.TGAL1.1-TAHU.160	TAHU Gallery 1.1 - TAHU's - L3 Startup	4	26-Jan-27	29-Jan-27		
Cx.PH1.TGAL1.1-TAHU.170	TAHU Gallery 1.1 - TAHU's - BAS SAT	1	01-Feb-27	01-Feb-27		
Cx.PH1.TGAL1.1-TAHU.180	TAHU Gallery 1.1 - TAHU's - Water Test / TAB	5	02-Feb-27	08-Feb-27		
Cx.PH1.TGAL1.1-TAHU.190	TAHU Gallery 1.1 - TAHU's - Green Tag	1	09-Feb-27	09-Feb-27		
PH1 - ROMP 1 & 2 - Mezzanine		80	16-Sep-26	05-Jan-27		
PH1.R1&2.Mezz-440	PH1 - R1&2 - Mezz - Mechanical OH Rough-ins	4	23-Sep-26	29-Sep-26	Trade	Mechanical
PH1.R1&2.Mezz-470	PH1 - R1&2 - Mezz - Mechanical Trim-out	5	09-Nov-26	13-Nov-26	Trade	Mechanical
PH1.R1&2.Mezz-420	PH1 - R1&2 - Mezz - Fire Sprinkler OH Rough-ins	5	16-Sep-26	22-Sep-26		
PH1.R1&2.Mezz-450	PH1 - R1&2 - Mezz - Plumbing OH Rough-ins	5	30-Sep-26	06-Oct-26		
PH1.R1&2.Mezz-100	PH1 - R1&2 - Mezz - Layout & Frame Walls	5	01-Oct-26	07-Oct-26		

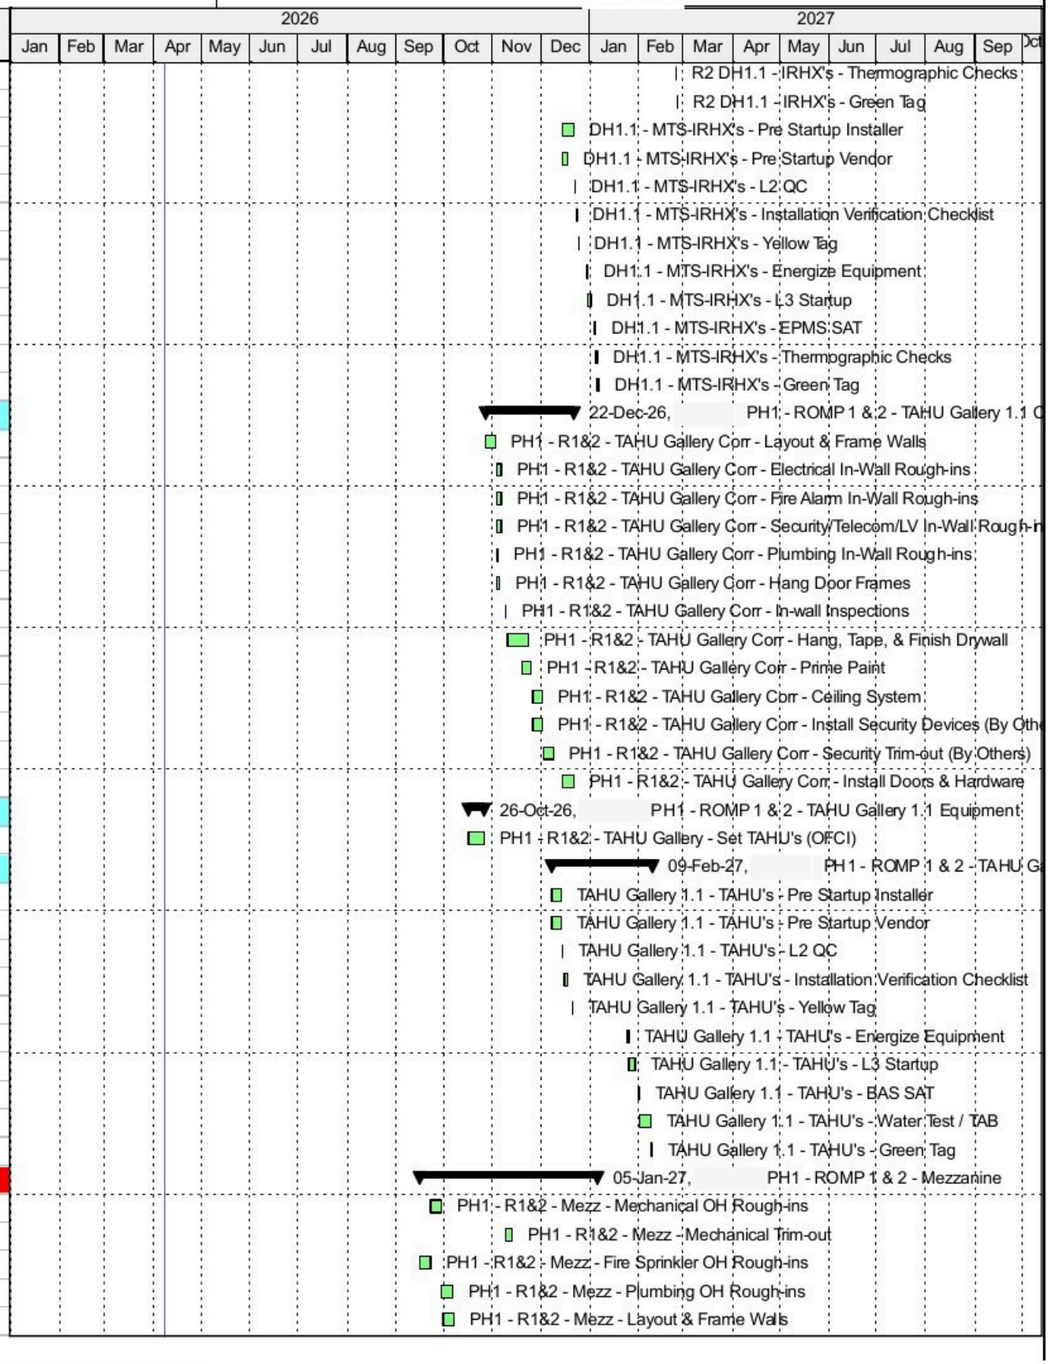


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH1.R1&2.Mezz-430	PH1 - R1&2 - Mezz - Electrical/Fire Alarm OH Rough-ins	10	05-Oct-26	16-Oct-26		
PH1.R1&2.Mezz-510	PH1 - R1&2 - Mezz - Security/Telecom/LV OH Rough-ins	10	05-Oct-26	16-Oct-26		
PH1.R1&2.Mezz-200	PH1 - R1&2 - Mezz - One Side Drywall	5	08-Oct-26	14-Oct-26		
PH1.R1&2.Mezz-380	PH1 - R1&2 - Mezz - Electrical In-Wall Rough-ins	4	08-Oct-26	13-Oct-26		
PH1.R1&2.Mezz-390	PH1 - R1&2 - Mezz - Fire Alarm In-Wall Rough-ins	4	08-Oct-26	13-Oct-26		
PH1.R1&2.Mezz-400	PH1 - R1&2 - Mezz - Security/Telecom/LV In-Wall Rough-ins	4	08-Oct-26	13-Oct-26		
PH1.R1&2.Mezz-410	PH1 - R1&2 - Mezz - Plumbing In-Wall Rough-ins	2	08-Oct-26	09-Oct-26		
PH1.R1&2.Mezz-500	PH1 - R1&2 - Mezz - Hang Door Frames	5	08-Oct-26	14-Oct-26		
PH1.R1&2.Mezz-180	PH1 - R1&2 - Mezz - In-Wall Inspections	1	14-Oct-26	14-Oct-26		
PH1.R1&2.Mezz-130	PH1 - R1&2 - Mezz - Hang, Tape, & Finish Drywall	10	15-Oct-26	28-Oct-26		
PH1.R1&2.Mezz-190	PH1 - R1&2 - Mezz - OH Inspections	1	19-Oct-26	19-Oct-26		
PH1.R1&2.Mezz-520	PH1 - R1&2 - Mezz - Pull & Terminate Wire	10	19-Oct-26	30-Oct-26		
PH1.R1&2.Mezz-140	PH1 - R1&2 - Mezz - Prime Paint	5	26-Oct-26	30-Oct-26		
PH1.R1&2.Mezz-160	PH1 - R1&2 - Mezz - Install Doors & Hardware	5	02-Nov-26	06-Nov-26		
PH1.R1&2.Mezz-460	PH1 - R1&2 - Mezz - Electrical Trim-out	5	09-Nov-26	13-Nov-26		
PH1.R1&2.Mezz-480	PH1 - R1&2 - Mezz - Security Trim-out (By Others)	5	09-Nov-26	13-Nov-26		
PH1.R1&2.Mezz-490	PH1 - R1&2 - Mezz - Fire Alarm Trim-out	5	15-Dec-26	22-Dec-26		
PH1.R1&2.Mezz-340	PH1 - R1&2 - Mezz - Punchlist	5	23-Dec-26	29-Dec-26		
PH1.R1&2.Mezz-350	PH1 - R1&2 - Mezz - Final Clean	5	30-Dec-26	05-Jan-27		
PH1 - ROMP 1 & 2 - Stair 04		46	23-Sep-26	25-Nov-26		
PH1 - ROMP 1 & 2 - L1 - Stair 04		44	23-Sep-26	23-Nov-26		
PH1.R2.L1.STR.330	PH1 - R2 - L1 - ST04 - Mechanical OH Rough-Ins	1	25-Sep-26	25-Sep-26	Trade	Mechanical
PH1.R2.L1.STR.530	PH1 - R2 - L1 - ST04 - Mechanical Trim-out	2	19-Oct-26	20-Oct-26	Trade	Mechanical
PH1.R2.L1.STR.300	PH1 - R2 - L1 - ST04 - Fire Sprinkler OH Rough-Ins	2	23-Sep-26	24-Sep-26		
PH1.R2.L1.STR.100	PH1 - R2 - L1 - ST04 - Layout Walls	1	23-Sep-26	23-Sep-26		
PH1.R2.L1.STR.110	PH1 - R2 - L1 - ST04 - Frame Walls	2	24-Sep-26	25-Sep-26		
PH1.R2.L1.STR.310	PH1 - R2 - L1 - ST04 - Electrical/Fire Alarm OH Rough-Ins	3	25-Sep-26	30-Sep-26		
PH1.R2.L1.STR.320	PH1 - R2 - L1 - ST04 - Sec/Telecom OH Rough-Ins	3	25-Sep-26	30-Sep-26		
PH1.R2.L1.STR.120	PH1 - R2 - L1 - ST04 - One Side Drywall	2	29-Sep-26	30-Sep-26		
PH1.R2.L1.STR.200	PH1 - R2 - L1 - ST04 - Electrical/Fire Alarm In-Wall Rough-Ins	3	29-Sep-26	01-Oct-26		
PH1.R2.L1.STR.210	PH1 - R2 - L1 - ST04 - Sec/Telecom In-Wall Rough-Ins	3	29-Sep-26	01-Oct-26		
PH1.R2.L1.STR.130	PH1 - R2 - L1 - ST04 - Hang Door Frames	1	01-Oct-26	01-Oct-26		
PH1.R2.L1.STR.390	PH1 - R2 - L1 - ST04 - OH Inspections	1	01-Oct-26	01-Oct-26		
PH1.R2.L1.STR.290	PH1 - R2 - L1 - ST04 - In-Wall Inspections	1	02-Oct-26	02-Oct-26		
PH1.R2.L1.STR.140	PH1 - R2 - L1 - ST04 - Hang, Tape, & Finish Drywall	3	05-Oct-26	07-Oct-26		
PH1.R2.L1.STR.160	PH1 - R2 - L1 - ST04 - Prime Paint	2	08-Oct-26	09-Oct-26		
PH1.R2.L1.STR.500	PH1 - R2 - L1 - ST04 - Fire Sprinkler Trim-out	2	12-Oct-26	13-Oct-26		
PH1.R2.L1.STR.490	PH1 - R2 - L1 - ST04 - Install Security Devices (By Others)	5	12-Oct-26	16-Oct-26		
PH1.R2.L1.STR.410	PH1 - R2 - L1 - ST04 - Pull & Terminate Wires	5	12-Oct-26	16-Oct-26		
PH1.R2.L1.STR.580	PH1 - R2 - L1 - ST04 - Install Lighting	2	12-Oct-26	13-Oct-26		
PH1.R2.L1.STR.510	PH1 - R2 - L1 - ST04 - Electrical Trim-out	2	19-Oct-26	20-Oct-26		
PH1.R2.L1.STR.520	PH1 - R2 - L1 - ST04 - Fire Alarm Trim-out	2	19-Oct-26	20-Oct-26		
PH1.R2.L1.STR.590	PH1 - R2 - L1 - ST04 - Security Trim-out (By Others)	5	19-Oct-26	23-Oct-26		
PH1.R2.L1.STR.400	PH1 - R2 - L1 - ST04 - Install Doors & Hardware	1	29-Oct-26	29-Oct-26		
PH1.R2.L1.STR.600	PH1 - R2 - L1 - ST04 - Final Paint	5	30-Oct-26	05-Nov-26		

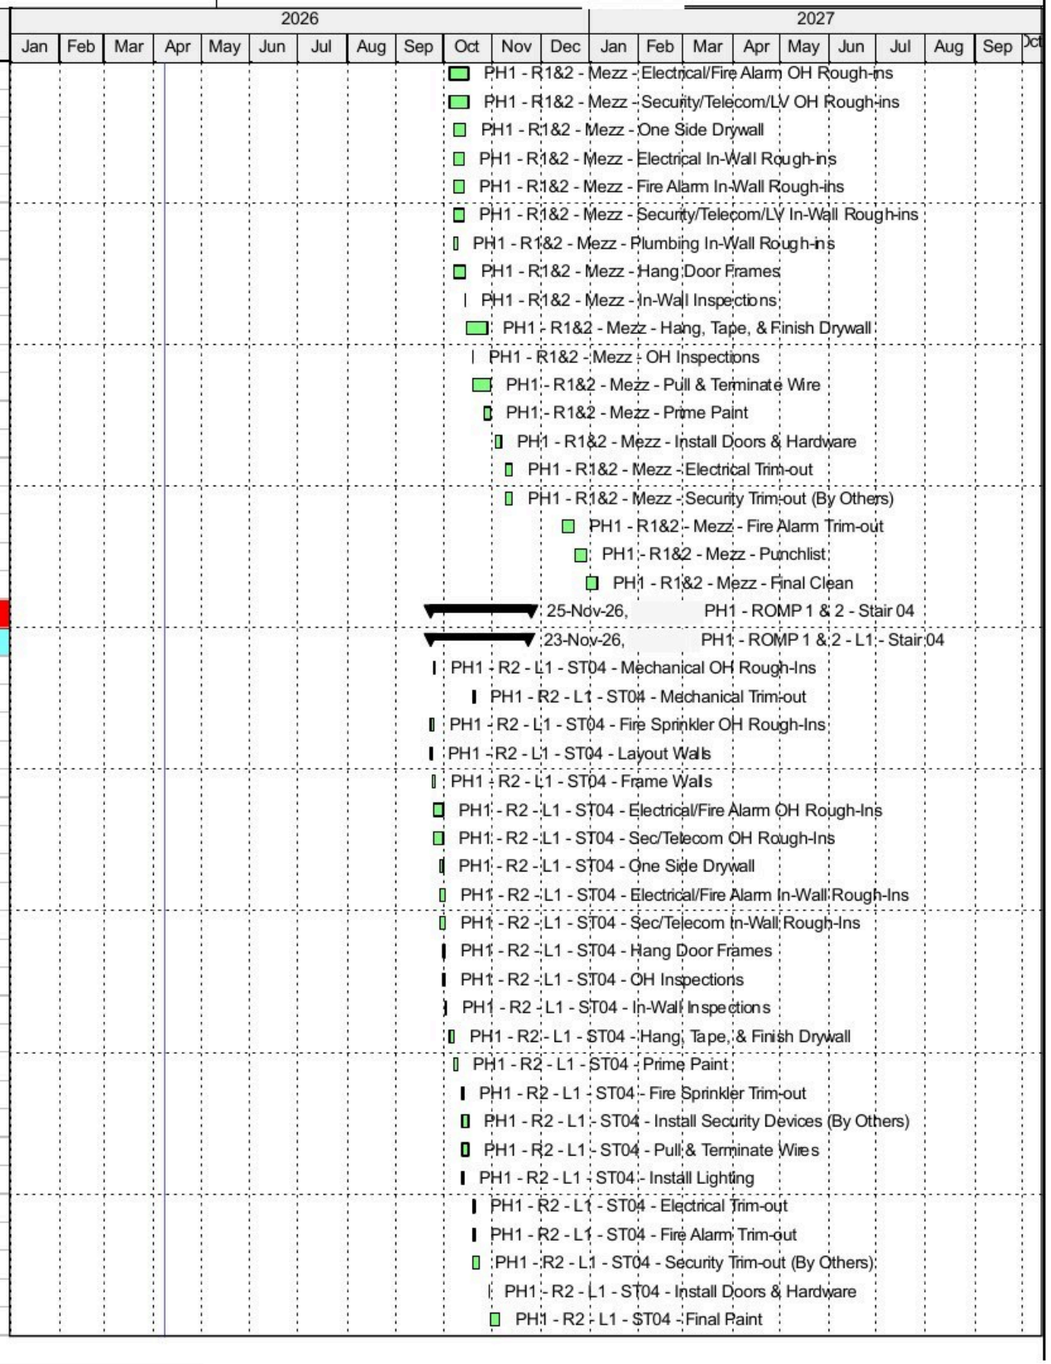


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH1.R2.L1.STR.610	PH1 - R2 - L1 - ST04 - Install Signage	2	06-Nov-26	09-Nov-26		
PH1.R2.L1.STR.680	PH1 - R2 - L1 - ST04 - Punchlist	5	10-Nov-26	16-Nov-26		
PH1.R2.L1.STR.690	PH1 - R2 - L1 - ST04 - Final Clean	5	17-Nov-26	23-Nov-26		
PH1 - ROMP 1 & 2 - M1 - Stair 04		45	24-Sep-26	25-Nov-26		
PH1.R2.M1.STR.330	PH1 - R2 - M1 - ST04 - Mechanical OH Rough-Ins	1	30-Sep-26	30-Sep-26	Trade	Mechanical
PH1.R2.M1.STR.530	PH1 - R2 - M1 - ST04 - Mechanical Trim-out	2	22-Oct-26	23-Oct-26	Trade	Mechanical
PH1.R2.M1.STR.100	PH1 - R2 - M1 - ST04 - Layout Walls	1	24-Sep-26	24-Sep-26		
PH1.R2.M1.STR.300	PH1 - R2 - M1 - ST04 - Fire Sprinkler OH Rough-Ins	2	25-Sep-26	29-Sep-26		
PH1.R2.M1.STR.110	PH1 - R2 - M1 - ST04 - Frame Walls	2	29-Sep-26	30-Sep-26		
PH1.R2.M1.STR.120	PH1 - R2 - M1 - ST04 - One Side Drywall	2	01-Oct-26	02-Oct-26		
PH1.R2.M1.STR.310	PH1 - R2 - M1 - ST04 - Electrical/Fire Alarm OH Rough-Ins	3	01-Oct-26	05-Oct-26		
PH1.R2.M1.STR.320	PH1 - R2 - M1 - ST04 - Sec/Telecom OH Rough-Ins	3	01-Oct-26	05-Oct-26		
PH1.R2.M1.STR.200	PH1 - R2 - M1 - ST04 - Electrical/Fire Alarm In-Wall Rough-Ins	3	02-Oct-26	06-Oct-26		
PH1.R2.M1.STR.210	PH1 - R2 - M1 - ST04 - Sec/Telecom In-Wall Rough-Ins	3	02-Oct-26	06-Oct-26		
PH1.R2.M1.STR.130	PH1 - R2 - M1 - ST04 - Hang Door Frames	1	05-Oct-26	05-Oct-26		
PH1.R2.M1.STR.390	PH1 - R2 - M1 - ST04 - OH Inspections	1	06-Oct-26	06-Oct-26		
PH1.R2.M1.STR.290	PH1 - R2 - M1 - ST04 - In-Wall Inspections	1	07-Oct-26	07-Oct-26		
PH1.R2.M1.STR.140	PH1 - R2 - M1 - ST04 - Hang, Tape, & Finish Drywall	3	08-Oct-26	12-Oct-26		
PH1.R2.M1.STR.160	PH1 - R2 - M1 - ST04 - Prime Paint	2	13-Oct-26	14-Oct-26		
PH1.R2.M1.STR.500	PH1 - R2 - M1 - ST04 - Fire Sprinkler Trim-out	2	15-Oct-26	16-Oct-26		
PH1.R2.M1.STR.490	PH1 - R2 - M1 - ST04 - Install Security Devices (By Others)	5	15-Oct-26	21-Oct-26		
PH1.R2.M1.STR.410	PH1 - R2 - M1 - ST04 - Pull & Terminate Wires	5	15-Oct-26	21-Oct-26		
PH1.R2.M1.STR.580	PH1 - R2 - M1 - ST04 - Install Lighting	2	15-Oct-26	16-Oct-26		
PH1.R2.M1.STR.510	PH1 - R2 - M1 - ST04 - Electrical Trim-out	2	22-Oct-26	23-Oct-26		
PH1.R2.M1.STR.520	PH1 - R2 - M1 - ST04 - Fire Alarm Trim-out	2	22-Oct-26	23-Oct-26		
PH1.R2.M1.STR.590	PH1 - R2 - M1 - ST04 - Security Trim-out (By Others)	5	22-Oct-26	28-Oct-26		
PH1.R2.M1.STR.400	PH1 - R2 - M1 - ST04 - Install Doors & Hardware	1	30-Oct-26	30-Oct-26		
PH1.R2.M1.STR.600	PH1 - R2 - M1 - ST04 - Final Paint	5	02-Nov-26	06-Nov-26		
PH1.R2.M1.STR.610	PH1 - R2 - M1 - ST04 - Install Signage	2	10-Nov-26	11-Nov-26		
PH1.R2.M1.STR.680	PH1 - R2 - M1 - ST04 - Punchlist	5	12-Nov-26	18-Nov-26		
PH1.R2.M1.STR.690	PH1 - R2 - M1 - ST04 - Final Clean	5	19-Nov-26	25-Nov-26		
Phase 2 (ROMP 3 & 4)		138	15-Sep-26	25-Mar-27		
PH2 - ROMP3 & 4 - Electrical Rooms 1.3 & 1.4		114	23-Sep-26	01-Mar-27		
PH2 - ROMP 3 - Electrical Room 1.3		113	23-Sep-26	26-Feb-27		
PH2.R3.ER1.3-IB.850	PH2 - ROMP3 - ER - Mechanical OH Rough-ins	4	01-Oct-26	06-Oct-26	Trade	Mechanical
PH2.R3.ER1.3-IB.880	PH2 - ROMP3 - ER - Mechanical Trim-out	5	25-Dec-26	31-Dec-26	Trade	Mechanical
PH2.R3.ER1.3-330	PH2 - ROMP3 - ER - Set CRAC Units	5	28-Oct-26	03-Nov-26	Trade	HVAC
PH2.R3.ER1.3-IB.450	PH2 - ROMP3 - ER - Layout & Frame Walls	5	23-Sep-26	30-Sep-26		
PH2.R3.ER1.3-IB.860	PH2 - ROMP3 - ER - Fire Sprinkler OH Rough-ins	5	23-Sep-26	30-Sep-26		
PH2.R3.ER1.3-IB.550	PH2 - ROMP3 - ER - One Side Drywall	5	01-Oct-26	07-Oct-26		
PH2.R3.ER1.3-IB.790	PH2 - ROMP3 - ER - Plumbing In-Wall Rough-ins	2	01-Oct-26	02-Oct-26		
PH2.R3.ER1.3-IB.800	PH2 - ROMP3 - ER - Electrical In-Wall Rough-Ins	4	01-Oct-26	06-Oct-26		
PH2.R3.ER1.3-IB.810	PH2 - ROMP3 - ER - Fire Alarm In-Wall Rough-Ins	4	01-Oct-26	06-Oct-26		
PH2.R3.ER1.3-IB.820	PH2 - ROMP3 - ER - Security/Telecom/LV In-Wall Rough-ins	4	01-Oct-26	06-Oct-26		
PH2.R3.ER1.3-IB.1170	PH2 - ROMP3 - ER - Hang Door Frames	5	01-Oct-26	07-Oct-26		

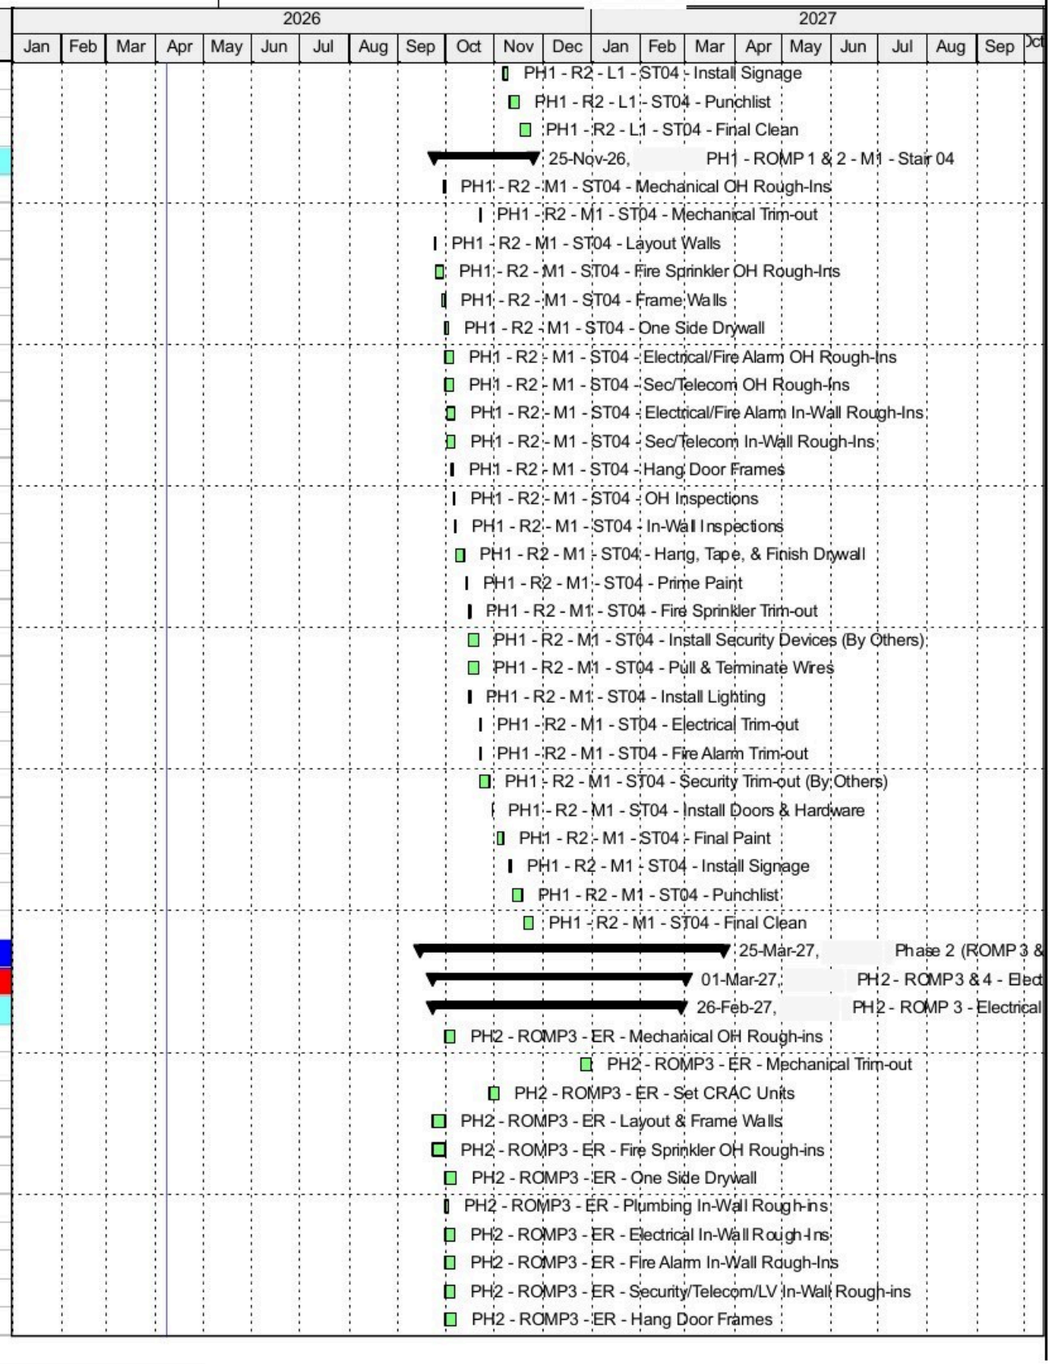


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule


Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH2.R3.ER1.3-IB.560	PH2 - ROMP3 - ER - In-Wall Inspection	1	07-Oct-26	07-Oct-26		
PH2.R3.ER1.3-IB.830	PH2 - ROMP3 - ER - plumbing OH Rough-ins	4	07-Oct-26	12-Oct-26		
PH2.R3.ER1.3-IB.840	PH2 - ROMP3 - ER - Electrical/Fire Alarm OH Rough-ins	15	07-Oct-26	27-Oct-26		
PH2.R3.ER1.3-IB.1180	PH2 - ROMP3 - ER - Security/Telecom/LV OH Rough-ins	15	07-Oct-26	27-Oct-26		
PH2.R3.ER1.3-IB.470	PH2 - ROMP3 - ER - Hang, Tape, & Finish Drywall	10	12-Oct-26	23-Oct-26		
PH2.R3.ER1.3-IB.480	PH2 - ROMP3 - ER - Prime Paint	5	21-Oct-26	27-Oct-26		
PH2.R3.ER1.3-IB.580	PH2 - ROMP3 - ER - OH Inspection	1	28-Oct-26	28-Oct-26		
PH2.R3.ER1.3-IB.530	PH2 - ROMP3 - ER - Install Cable Tray	10	12-Nov-26	25-Nov-26		
PH2.R3.ER1.3-IB.520	PH2 - ROMP3 - ER - Pull & Terminate Wires	15	26-Nov-26	16-Dec-26		
PH2.R3.ER1.3-IB.540	PH2 - ROMP3 - ER - Install Doors & Hardware	5	18-Dec-26	24-Dec-26		
PH2.R3.ER1.3-IB.590	PH2 - ROMP3 - ER - Security Devices (By Others)	5	18-Dec-26	24-Dec-26		
PH2.R3.ER1.3-IB.870	PH2 - ROMP3 - ER - Electrical Trim-out	5	25-Dec-26	31-Dec-26		
PH2.R3.ER1.3-IB.890	PH2 - ROMP3 - ER - Fire Alarm Trim-out	5	25-Dec-26	31-Dec-26		
PH2.R3.ER1.3-IB.900	PH2 - ROMP3 - ER - Security Trim-out (By Others)	5	25-Dec-26	31-Dec-26		
PH2.R3.ER1.3-IB.750	PH2 - ROMP3 - ER - Punchlist	5	01-Jan-27	07-Jan-27		
PH2.R3.ER1.3-IB.760	PH2 - ROMP3 - ER - Final Clean	5	08-Jan-27	18-Jan-27		
PH2.R3.ER1.3-270	PH2 - ROMP3 - ER - Set USB's & AMCOP's 1.5A & 1.5B (OFCI)	5	05-Nov-26	11-Nov-26		
PH2.R3.ER1.3-280	PH2 - ROMP3 - ER - Set XFMR's (OFCI)	5	05-Nov-26	11-Nov-26		
PH2.R3.ER1.3-290	PH2 - ROMP3 - ER - Set ATS's (OFCI)	5	05-Nov-26	11-Nov-26		
PH2.R3.ER1.3-300	PH2 - ROMP3 - ER - Set HUPP's (OFCI)	5	05-Nov-26	11-Nov-26		
PH2.R3.ER1.3-310	PH2 - ROMP3 - ER - Set MSDB (OFCI)	5	05-Nov-26	11-Nov-26		
PH2.R3.ER1.3-320	PH2 - ROMP3 - ER - Loose Busduct Test & Install (OFCI)	5	05-Nov-26	11-Nov-26		
PH2.R3.ER1.3-340	PH2 - ROMP3 - ER - Busduct Skid Test & Install (OFCI)	10	05-Nov-26	18-Nov-26		
Cx.PH2.R3.ER1.3-XFMR.100	R3 ER 1.3 - XFMR's - Pre Startup Installer	7	18-Dec-26	28-Dec-26		
Cx.PH2.R3.ER1.3-XFMR.110	R3 ER 1.3 - XFMR's - L2 QC	1	29-Dec-26	29-Dec-26		
Cx.PH2.R3.ER1.3-XFMR.120	R3 ER 1.3 - XFMR's - Installation Verification Checklist	2	30-Dec-26	31-Dec-26		
Cx.PH2.R3.ER1.3-XFMR.130	R3 ER 1.3 - XFMR's - Yellow Tag	1	01-Jan-27	01-Jan-27		
Cx.PH2.R3.ER1.3-XFMR.140	R3 ER 1.3 - XFMR's - Energize Equipment	1	18-Feb-27	18-Feb-27		
Cx.PH2.R3.ER1.3-XFMR.150	R3 ER 1.3 - XFMR's - L3 Start-up	1	19-Feb-27	19-Feb-27		
Cx.PH2.R3.ER1.3-XFMR.160	R3 ER 1.3 - XFMR's - Thermographic Checks	1	22-Feb-27	22-Feb-27		
Cx.PH2.R3.ER1.3-XFMR.170	R3 ER 1.3 - XFMR's - Green Tag	1	23-Feb-27	23-Feb-27		
Cx.PH2.R3.ER1.3-USB.100	R3 ER 1.3 - USB's - Pre Startup Installer	3	18-Dec-26	22-Dec-26		
Cx.PH2.R3.ER1.3-USB.110	R3 ER 1.3 - USB's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH2.R3.ER1.3-USB.120	R3 ER 1.3 - USB's - L2 QC	1	23-Dec-26	23-Dec-26		
Cx.PH2.R3.ER1.3-USB.130	R3 ER 1.3 - USB's - Installation Verification Checklist	1	24-Dec-26	24-Dec-26		
Cx.PH2.R3.ER1.3-USB.140	R3 ER 1.3 - USB's - Yellow Tag	1	25-Dec-26	25-Dec-26		
Cx.PH2.R3.ER1.3-USB.150	R3 ER 1.3 - USB's - Energize Equipment	1	17-Feb-27	17-Feb-27		
Cx.PH2.R3.ER1.3-USB.160	R3 ER 1.3 - USB's - L3 Startup	4	18-Feb-27	23-Feb-27		
Cx.PH2.R3.ER1.3-USB.170	R3 ER 1.3 - USB's - EPMS SAT	1	24-Feb-27	24-Feb-27		
Cx.PH2.R3.ER1.3-USB.180	R3 ER 1.3 - USB's - Thermographic Checks	1	25-Feb-27	25-Feb-27		
Cx.PH2.R3.ER1.3-USB.190	R3 ER 1.3 - USB's - Green Tag	1	26-Feb-27	26-Feb-27		
Cx.PH2.R3.ER1.3-ATS.100	R3 ER 1.3 - ATS's - Pre Startup Installer	5	04-Feb-27	10-Feb-27		
Cx.PH2.R3.ER1.3-ATS.110	R3 ER 1.3 - ATS's - Pre Startup Vendor	3	04-Feb-27	08-Feb-27		
Cx.PH2.R3.ER1.3-ATS.120	R3 ER 1.3 - ATS's - L2 QC	1	11-Feb-27	11-Feb-27		
Cx.PH2.R3.ER1.3-ATS.130	R3 ER 1.3 - ATS's - Installation Verification Checklist	2	12-Feb-27	15-Feb-27		

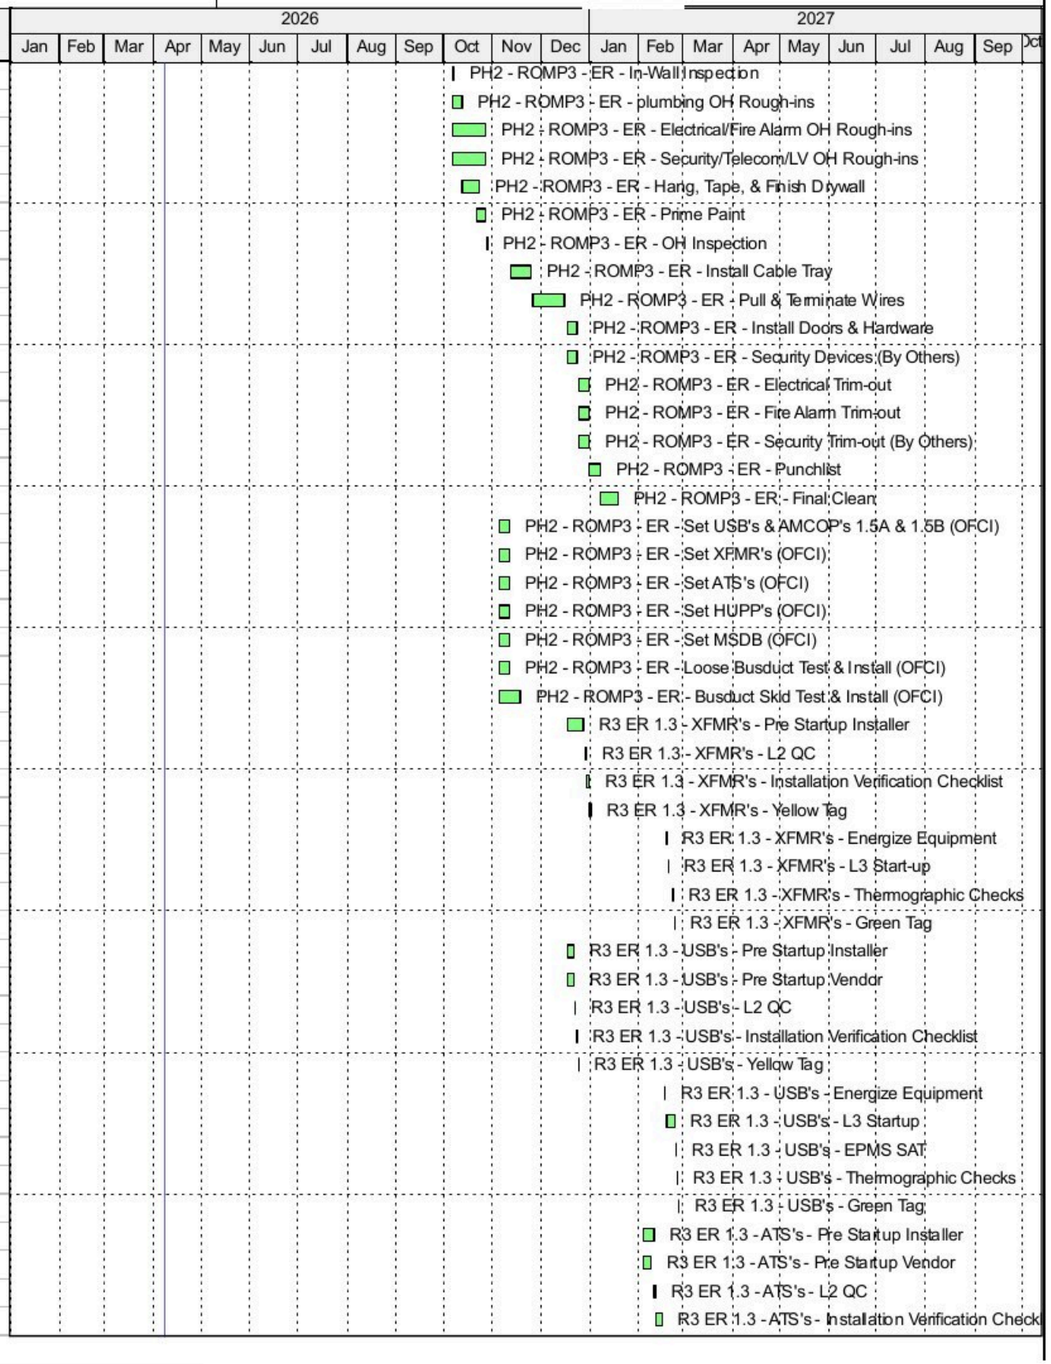


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH2.R3.ER1.3-ATS.140	R3 ER 1.3 - ATS's - Yellow Tag	1	16-Feb-27	16-Feb-27		
Cx.PH2.R3.ER1.3-ATS.150	R3 ER 1.3 - ATS's - Energize Equipment	1	18-Feb-27	18-Feb-27		
Cx.PH2.R3.ER1.3-ATS.160	R3 ER 1.3 - ATS's - L3 Startup	2	19-Feb-27	22-Feb-27		
Cx.PH2.R3.ER1.3-ATS.170	R3 ER 1.3 - ATS's - EPMS SAT	1	23-Feb-27	23-Feb-27		
Cx.PH2.R3.ER1.3-ATS.180	R3 ER 1.3 - ATS's - Thermographic Checks	1	24-Feb-27	24-Feb-27		
Cx.PH2.R3.ER1.3-ATS.190	R3 ER 1.3 - ATS's - Green Tag	1	25-Feb-27	25-Feb-27		
Cx.PH2.R3.ER1.3-MSDB.100	R3 ER 1.3 - MSDB's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH2.R3.ER1.3-MSDB.110	R3 ER 1.3 - MSDB's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH2.R3.ER1.3-MSDB.120	R3 ER 1.3 - MSDB's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH2.R3.ER1.3-MSDB.130	R3 ER 1.3 - MSDB's - Installation Verification Checklist	2	28-Dec-26	29-Dec-26		
Cx.PH2.R3.ER1.3-MSDB.140	R3 ER 1.3 - MSDB's - Yellow Tag	1	30-Dec-26	30-Dec-26		
Cx.PH2.R3.ER1.3-MSDB.150	R3 ER 1.3 - MSDB's - Energize Equipment	1	18-Feb-27	18-Feb-27		
Cx.PH2.R3.ER1.3-MSDB.160	R3 ER 1.3 - MSDB's - L3 Startup	2	19-Feb-27	22-Feb-27		
Cx.PH2.R3.ER1.3-MSDB.170	R3 ER 1.3 - MSDB's - EPMS SAT	1	23-Feb-27	23-Feb-27		
Cx.PH2.R3.ER1.3-MSDB.180	R3 ER 1.3 - MSDB's - Thermographic Checks	1	24-Feb-27	24-Feb-27		
Cx.PH2.R3.ER1.3-MSDB.190	R3 ER 1.3 - MSDB's - Green Tag	1	25-Feb-27	25-Feb-27		
Cx.PH2.R3.ER1.3-AMCOP.100	R3 ER 1.3 - AMCOP's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH2.R3.ER1.3-AMCOP.110	R3 ER 1.3 - AMCOP's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH2.R3.ER1.3-AMCOP.120	R3 ER 1.3 - AMCOP's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH2.R3.ER1.3-AMCOP.130	R3 ER 1.3 - AMCOP's - Installation Verfication Checklist	2	28-Dec-26	29-Dec-26		
Cx.PH2.R3.ER1.3-AMCOP.140	R3 ER 1.3 - AMCOP's - Yellow Tag	1	30-Dec-26	30-Dec-26		
Cx.PH2.R3.ER1.3-AMCOP.150	R3 ER 1.3 - AMCOP's - Energize Equipment	1	18-Feb-27	18-Feb-27		
Cx.PH2.R3.ER1.3-AMCOP.160	R3 ER 1.3 - AMCOP's - L3 Startup	2	19-Feb-27	22-Feb-27		
Cx.PH2.R3.ER1.3-AMCOP.170	R3 ER 1.3 - AMCOP's - EPMS SAT	1	23-Feb-27	23-Feb-27		
Cx.PH2.R3.ER1.3-AMCOP.180	R3 ER 1.3 - AMCOP's - Thermographic Checks	1	24-Feb-27	24-Feb-27		
Cx.PH2.R3.ER1.3-AMCOP.190	R3 ER 1.3 - AMCOP's - Green Tag	1	25-Feb-27	25-Feb-27		
Cx.PH2.R3.ER1.3-CRAC.100	R3 ER 1.3 - CRAC's - Pre Startup Installer	3	13-Jan-27	19-Jan-27		
Cx.PH2.R3.ER1.3-CRAC.110	R3 ER 1.3 - CRAC's - Pre Startup Vendor	3	13-Jan-27	19-Jan-27		
Cx.PH2.R3.ER1.3-CRAC.120	R3 ER 1.3 - CRAC's - L2 QC	1	20-Jan-27	20-Jan-27		
Cx.PH2.R3.ER1.3-CRAC.130	R3 ER 1.3 - CRAC's - Installation Verification Checklist	2	20-Jan-27	21-Jan-27		
Cx.PH2.R3.ER1.3-CRAC.140	R3 ER 1.3 - CRAC's - Yellow Tag	1	25-Jan-27	25-Jan-27		
Cx.PH2.R3.ER1.3-CRAC.150	R3 ER 1.3 - CRAC's - Energize Equipment	1	10-Feb-27	10-Feb-27		
Cx.PH2.R3.ER1.3-CRAC.160	R3 ER 1.3 - CRAC's - L3 Startup	1	11-Feb-27	11-Feb-27		
Cx.PH2.R3.ER1.3-CRAC.180	R3 ER 1.3 - CRAC's - BAS SAT	1	12-Feb-27	12-Feb-27		
Cx.PH2.R3.ER1.3-CRAC.170	R3 ER 1.3 - CRAC's - TAB	3	15-Feb-27	17-Feb-27		
Cx.PH2.R3.ER1.3-CRAC.190	R3 ER 1.3 - CRAC's - Green Tag	1	18-Feb-27	18-Feb-27		
Cx.PH2.R3.ER1.3-HPP.HLP.100	R3 ER 1.3 - HPP's & HLP's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH2.R3.ER1.3-HPP.HLP.110	R3 ER 1.3 - HPP's & HLP's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH2.R3.ER1.3-HPP.HLP.120	R3 ER 1.3 - HPP's & HLP's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH2.R3.ER1.3-HPP.HLP.130	R3 ER 1.3 - HPP's & HLP's - Installation Verification Checklist	2	28-Dec-26	29-Dec-26		
Cx.PH2.R3.ER1.3-HPP.HLP.140	R3 ER 1.3 - HPP's & HLP's - Yellow Tag	1	30-Dec-26	30-Dec-26		
Cx.PH2.R3.ER1.3-HPP.HLP.150	R3 ER 1.3 - HPP's & HLP's - Energize Equipment	1	19-Feb-27	19-Feb-27		
Cx.PH2.R3.ER1.3-HPP.HLP.160	R3 ER 1.3 - HPP's & HLP's - L3 Startup	1	22-Feb-27	22-Feb-27		
Cx.PH2.R3.ER1.3-HPP.HLP.170	R3 ER 1.3 - HPP's & HLP's - EPMS SAT	1	23-Feb-27	23-Feb-27		
Cx.PH2.R3.ER1.3-HPP.HLP.180	R3 ER 1.3 - HPP's & HLP's - Thermographic Checks	1	24-Feb-27	24-Feb-27		

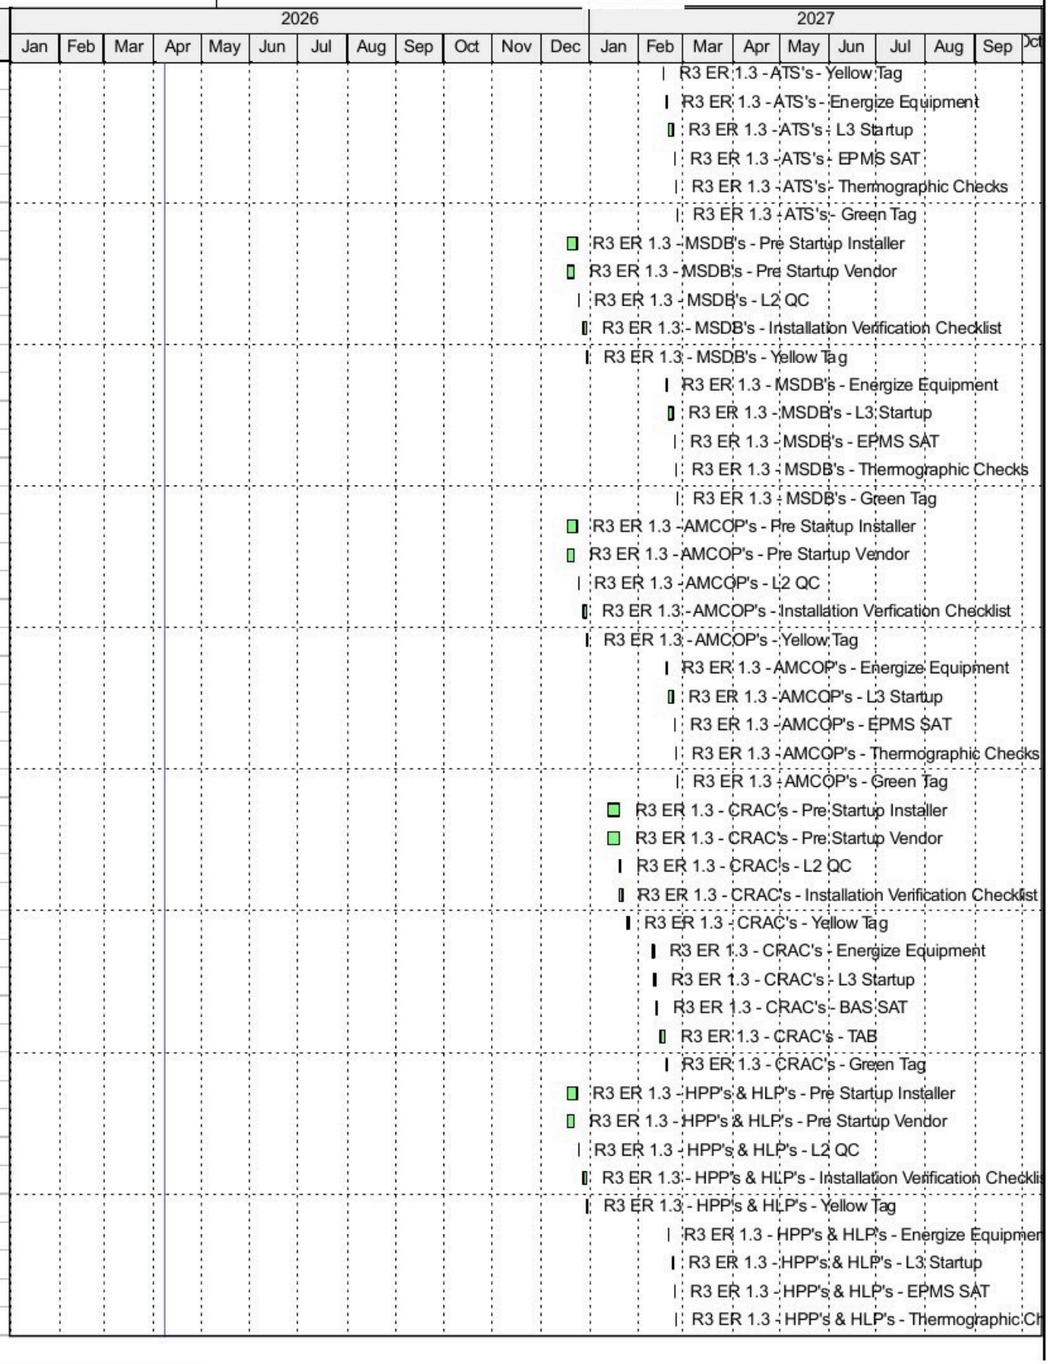

Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH2.R3.ER1.3-HPP.HLP.190	R3 ER 1.3 - HPP's & HLP's - Green Tag	1	25-Feb-27	25-Feb-27		
Cx.PH2.R3.ER1.3-HUPP.100	R3 ER 1.3 - HUPP's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH2.R3.ER1.3-HUPP.110	R3 ER 1.3 - HUPP's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH2.R3.ER1.3-HUPP.120	R3 ER 1.3 - HUPP's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH2.R3.ER1.3-HUPP.130	R3 ER 1.3 - HUPP's - Installation Verification Checklist	2	28-Dec-26	29-Dec-26		
Cx.PH2.R3.ER1.3-HUPP.140	R3 ER 1.3 - HUPP's - Yellow Tag	1	30-Dec-26	30-Dec-26		
Cx.PH2.R3.ER1.3-HUPP.150	R3 ER 1.3 - HUPP's - Energize Equipment	1	22-Feb-27	22-Feb-27		
Cx.PH2.R3.ER1.3-HUPP.160	R3 ER 1.3 - HUPP's - L3 Startup	1	23-Feb-27	23-Feb-27		
Cx.PH2.R3.ER1.3-HUPP.170	R3 ER 1.3 - HUPP's - EPMS SAT	1	24-Feb-27	24-Feb-27		
Cx.PH2.R3.ER1.3-HUPP.180	R3 ER 1.3 - HUPP's - Thermographic Checks	1	25-Feb-27	25-Feb-27		
Cx.PH2.R3.ER1.3-HUPP.190	R3 ER 1.3 - HUPP's - Green Tag	1	26-Feb-27	26-Feb-27		
Cx.PH2.R3.ER1.3-HUDPP.100	R3 ER 1.3 - HUDPP's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH2.R3.ER1.3-HUDPP.110	R3 ER 1.3 - HUDPP's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH2.R3.ER1.3-HUDPP.120	R3 ER 1.3 - HUDPP's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH2.R3.ER1.3-HUDPP.130	R3 ER 1.3 - HUDPP's - Installation Verification Checklist	2	28-Dec-26	29-Dec-26		
Cx.PH2.R3.ER1.3-HUDPP.140	R3 ER 1.3 - HUDPP's - Yellow Tag	1	30-Dec-26	30-Dec-26		
Cx.PH2.R3.ER1.3-HUDPP.150	R3 ER 1.3 - HUDPP's - Energize Equipment	1	19-Feb-27	19-Feb-27		
Cx.PH2.R3.ER1.3-HUDPP.160	R3 ER 1.3 - HUDPP's - L3 Startup	1	22-Feb-27	22-Feb-27		
Cx.PH2.R3.ER1.3-HUDPP.170	R3 ER 1.3 - HUDPP's - EPMS SAT	1	23-Feb-27	23-Feb-27		
Cx.PH2.R3.ER1.3-HUDPP.180	R3 ER 1.3 - HUDPP's - Thermographic Checks	1	24-Feb-27	24-Feb-27		
Cx.PH2.R3.ER1.3-HUDPP.190	R3 ER 1.3 - HUDPP's - Green Tag	1	25-Feb-27	25-Feb-27		
Cx.PH2.R3.ER1.3-GENAN.100	R3 ER 1.3 - GENAN's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH2.R3.ER1.3-GENAN.110	R3 ER 1.3 - GENAN's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH2.R3.ER1.3-GENAN.120	R3 ER 1.3 - GENAN's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH2.R3.ER1.3-GENAN.130	R3 ER 1.3 - GENAN's - Installation Verification Checklist	2	28-Dec-26	29-Dec-26		
Cx.PH2.R3.ER1.3-GENAN.140	R3 ER 1.3 - GENAN's - Yellow Tag	1	30-Dec-26	30-Dec-26		
Cx.PH2.R3.ER1.3-GENAN.150	R3 ER 1.3 - GENAN's - Energize Equipment	1	10-Feb-27	10-Feb-27		
Cx.PH2.R3.ER1.3-GENAN.160	R3 ER 1.3 - GENAN's - L3 Startup	1	11-Feb-27	11-Feb-27		
Cx.PH2.R3.ER1.3-GENAN.170	R3 ER 1.3 - GENAN's - EPMS SAT	1	12-Feb-27	12-Feb-27		
Cx.PH2.R3.ER1.3-GENAN.180	R3 ER 1.3 - GENAN's - Thermographics	1	15-Feb-27	15-Feb-27		
Cx.PH2.R3.ER1.3-GENAN.190	R3 ER 1.3 - GENAN's - Green Tag	1	16-Feb-27	16-Feb-27		
PH2 - ROMP 4 - Electrical Room 1.4		114	23-Sep-26	01-Mar-27		
PH2.R4.ER1.4-IB.1000	PH2 - ROMP4 - ER - Mechanical OH Rough-ins	4	01-Oct-26	06-Oct-26	Trade	Mechanical
PH2.R4.ER1.4-IB.1120	PH2 - ROMP4 - ER - Mechanical Trim-out	5	25-Dec-26	31-Dec-26	Trade	Mechanical
PH2.R4.ER1.4-290	PH2 - ROMP4 - ER - Set CRAC Units	5	28-Oct-26	03-Nov-26	Trade	HVAC
PH2.R4.ER1.4-IB.910	PH2 - ROMP4 - ER - Layout & Frame Walls	5	23-Sep-26	30-Sep-26		
PH2.R4.ER1.4-IB.1010	PH2 - ROMP4 - ER - Fire Sprinkler OH Rough-ins	5	23-Sep-26	30-Sep-26		
PH2.R4.ER1.4-IB.920	PH2 - ROMP4 - ER - One Side Drywall	5	01-Oct-26	07-Oct-26		
PH2.R4.ER1.4-IB.930	PH2 - ROMP4 - ER - plumbing In-Wall Rough-ins	2	01-Oct-26	02-Oct-26		
PH2.R4.ER1.4-IB.940	PH2 - ROMP4 - ER - Electrical In-Wall Rough-Ins	4	01-Oct-26	06-Oct-26		
PH2.R4.ER1.4-IB.950	PH2 - ROMP4 - ER - Fire Alarm In-Wall Rough-Ins	4	01-Oct-26	06-Oct-26		
PH2.R4.ER1.4-IB.960	PH2 - ROMP4 - ER - Security/Telecom/LV In-Wall Rough-ins	4	01-Oct-26	06-Oct-26		
PH2.R4.ER1.4-IB.1180	PH2 - ROMP4 - ER - Hang Door Frames	5	01-Oct-26	07-Oct-26		
PH2.R4.ER1.4-IB.970	PH2 - ROMP4 - ER - In-Wall Inspection	1	07-Oct-26	07-Oct-26		
PH2.R4.ER1.4-IB.980	PH2 - ROMP4 - ER - plumbing OH Rough-ins	4	07-Oct-26	12-Oct-26		

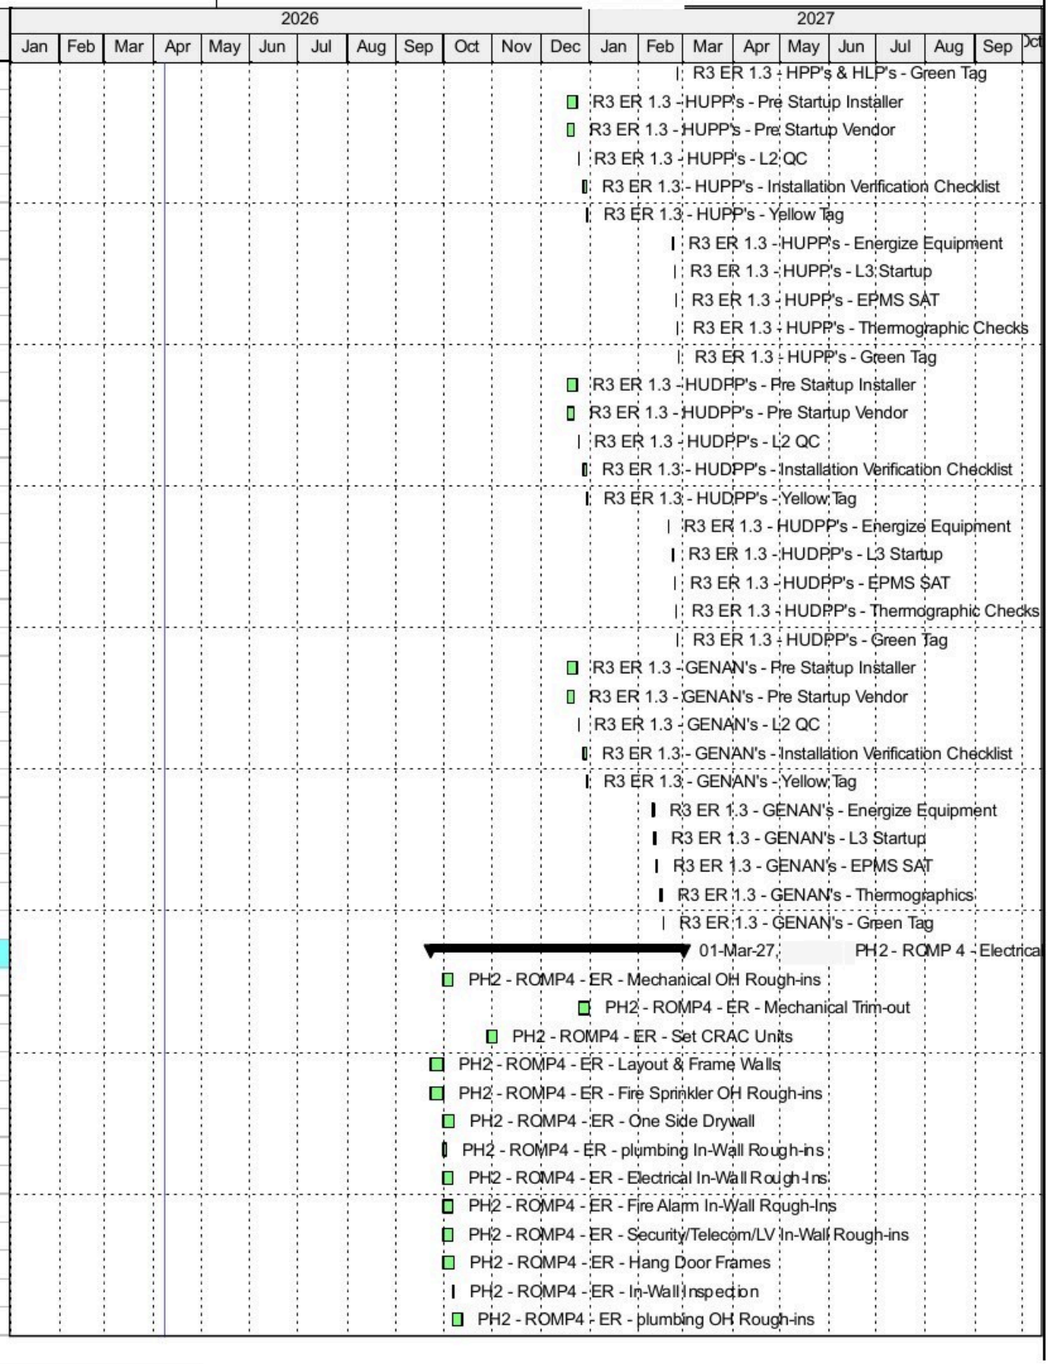


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule


Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH2.R4.ER1.4-IB.990	PH2 - ROMP4 - ER - Electrical/Fire Alarm OH Rough-ins	15	07-Oct-26	27-Oct-26		
PH2.R4.ER1.4-IB.1190	PH2 - ROMP4 - ER - Security/Telecom/LV OH Rough-ins	15	07-Oct-26	27-Oct-26		
PH2.R4.ER1.4-IB.1020	PH2 - ROMP4 - ER - Hang, Tape, & Finish Drywall	10	12-Oct-26	23-Oct-26		
PH2.R4.ER1.4-IB.1040	PH2 - ROMP4 - ER - Prime Paint	5	21-Oct-26	27-Oct-26		
PH2.R4.ER1.4-IB.1030	PH2 - ROMP4 - ER - OH Inspection	1	28-Oct-26	28-Oct-26		
PH2.R4.ER1.4-IB.1070	PH2 - ROMP4 - ER - Install Cable Tray	10	12-Nov-26	25-Nov-26		
PH2.R4.ER1.4-IB.1080	PH2 - ROMP4 - ER - Pull & Terminate Wires	15	26-Nov-26	16-Dec-26		
PH2.R4.ER1.4-IB.1090	PH2 - ROMP4 - ER - Install Doors & Hardware	5	18-Dec-26	24-Dec-26		
PH2.R4.ER1.4-IB.1100	PH2 - ROMP4 - ER - Security Devices (By Others)	5	18-Dec-26	24-Dec-26		
PH2.R4.ER1.4-IB.1110	PH2 - ROMP4 - ER - Electrical Trim-out	5	25-Dec-26	31-Dec-26		
PH2.R4.ER1.4-IB.1130	PH2 - ROMP4 - ER - Fire Alarm Trim-out	5	25-Dec-26	31-Dec-26		
PH2.R4.ER1.4-IB.1140	PH2 - ROMP4 - ER - Security Trim-out (By Others)	5	25-Dec-26	31-Dec-26		
PH2.R4.ER1.4-IB.1150	PH2 - ROMP4 - ER - Punchlist	5	01-Jan-27	07-Jan-27		
PH2.R4.ER1.4-IB.1160	PH2 - ROMP4 - ER - Final Clean	5	08-Jan-27	18-Jan-27		
PH2.R4.ER1.4-220	PH2 - ROMP4 - ER - Set USB's & AMCOP's 1.6A & 1.6B (OFCI)	5	05-Nov-26	11-Nov-26		
PH2.R4.ER1.4-230	PH2 - ROMP4 - ER - Set XFMR's (OFCI)	5	05-Nov-26	11-Nov-26		
PH2.R4.ER1.4-240	PH2 - ROMP4 - ER - Set ATS's (OFCI)	5	05-Nov-26	11-Nov-26		
PH2.R4.ER1.4-250	PH2 - ROMP4 - ER - Set HPP's, HLP's, HUPP's (OFCI)	5	05-Nov-26	11-Nov-26		
PH2.R4.ER1.4-260	PH2 - ROMP4 - ER - Set EVCPP (OFCI)	5	05-Nov-26	11-Nov-26		
PH2.R4.ER1.4-270	PH2 - ROMP4 - ER - Set MSDB (OFCI)	5	05-Nov-26	11-Nov-26		
PH2.R4.ER1.4-280	PH2 - ROMP4 - ER - Loose Busduct Test & Install (OFCI)	5	05-Nov-26	11-Nov-26		
PH2.R4.ER1.4-300	PH2 - ROMP4 - ER - Busduct Skid Test & Install (OFCI)	10	05-Nov-26	18-Nov-26		
Cx.PH2.R4.ER1.4-XFMR.100	R4 ER 1.4 - XFMR's - Pre Startup Installer	7	18-Dec-26	28-Dec-26		
Cx.PH2.R4.ER1.4-XFMR.110	R4 ER 1.4 - XFMR's - L2 QC	1	29-Dec-26	29-Dec-26		
Cx.PH2.R4.ER1.4-XFMR.130	R4 ER 1.4 - XFMR's - Installation Verification Checklist	2	30-Dec-26	31-Dec-26		
Cx.PH2.R4.ER1.4-XFMR.140	R4 ER 1.4 - XFMR's - Yellow Tag	1	01-Jan-27	01-Jan-27		
Cx.PH2.R4.ER1.4-XFMR.150	R4 ER 1.4 - XFMR's - Energize Equipment	1	19-Feb-27	19-Feb-27		
Cx.PH2.R4.ER1.4-XFMR.160	R4 ER 1.4 - XFMR's - L3 Start-up	1	22-Feb-27	22-Feb-27		
Cx.PH2.R4.ER1.4-XFMR.170	R4 ER 1.4 - XFMR's - Thermographic Checks	1	23-Feb-27	23-Feb-27		
Cx.PH2.R4.ER1.4-XFMR.180	R4 ER 1.4 - XFMR's - Green Tag	1	24-Feb-27	24-Feb-27		
Cx.PH2.R4.ER1.4-USB.100	R4 ER 1.4 - USB's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH2.R4.ER1.4-USB.110	R4 ER 1.4 - USB's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH2.R4.ER1.4-USB.120	R4 ER 1.4 - USB's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH2.R4.ER1.4-USB.130	R4 ER 1.4 - USB's - Installation Verification Checklist	1	28-Dec-26	28-Dec-26		
Cx.PH2.R4.ER1.4-USB.140	R4 ER 1.4 - USB's - Yellow Tag	1	29-Dec-26	29-Dec-26		
Cx.PH2.R4.ER1.4-USB.150	R4 ER 1.4 - USB's - Energize Equipment	1	17-Feb-27	17-Feb-27		
Cx.PH2.R4.ER1.4-USB.160	R4 ER 1.4 - USB's - L3 Startup	4	18-Feb-27	23-Feb-27		
Cx.PH2.R4.ER1.4-USB.170	R4 ER 1.4 - USB's - EPMS SAT	1	24-Feb-27	24-Feb-27		
Cx.PH2.R4.ER1.4-USB.180	R4 ER 1.4 - USB's - Thermographic Checks	1	25-Feb-27	25-Feb-27		
Cx.PH2.R4.ER1.4-USB.190	R4 ER 1.4 - USB's - Green Tag	1	26-Feb-27	26-Feb-27		
Cx.PH2.R4.ER1.4-ATS.100	R4 ER 1.4 - ATS's - Pre Startup Installer	5	04-Feb-27	10-Feb-27		
Cx.PH2.R4.ER1.4-ATS.110	R4 ER 1.4 - ATS's - Pre Startup Vendor	3	04-Feb-27	08-Feb-27		
Cx.PH2.R4.ER1.4-ATS.120	R4 ER 1.4 - ATS's - L2 QC	1	11-Feb-27	11-Feb-27		
Cx.PH2.R4.ER1.4-ATS.130	R4 ER 1.4 - ATS's - Installation Verification Checklist	2	12-Feb-27	15-Feb-27		
Cx.PH2.R4.ER1.4-ATS.140	R4 ER 1.4 - ATS's - Yellow Tag	1	16-Feb-27	16-Feb-27		

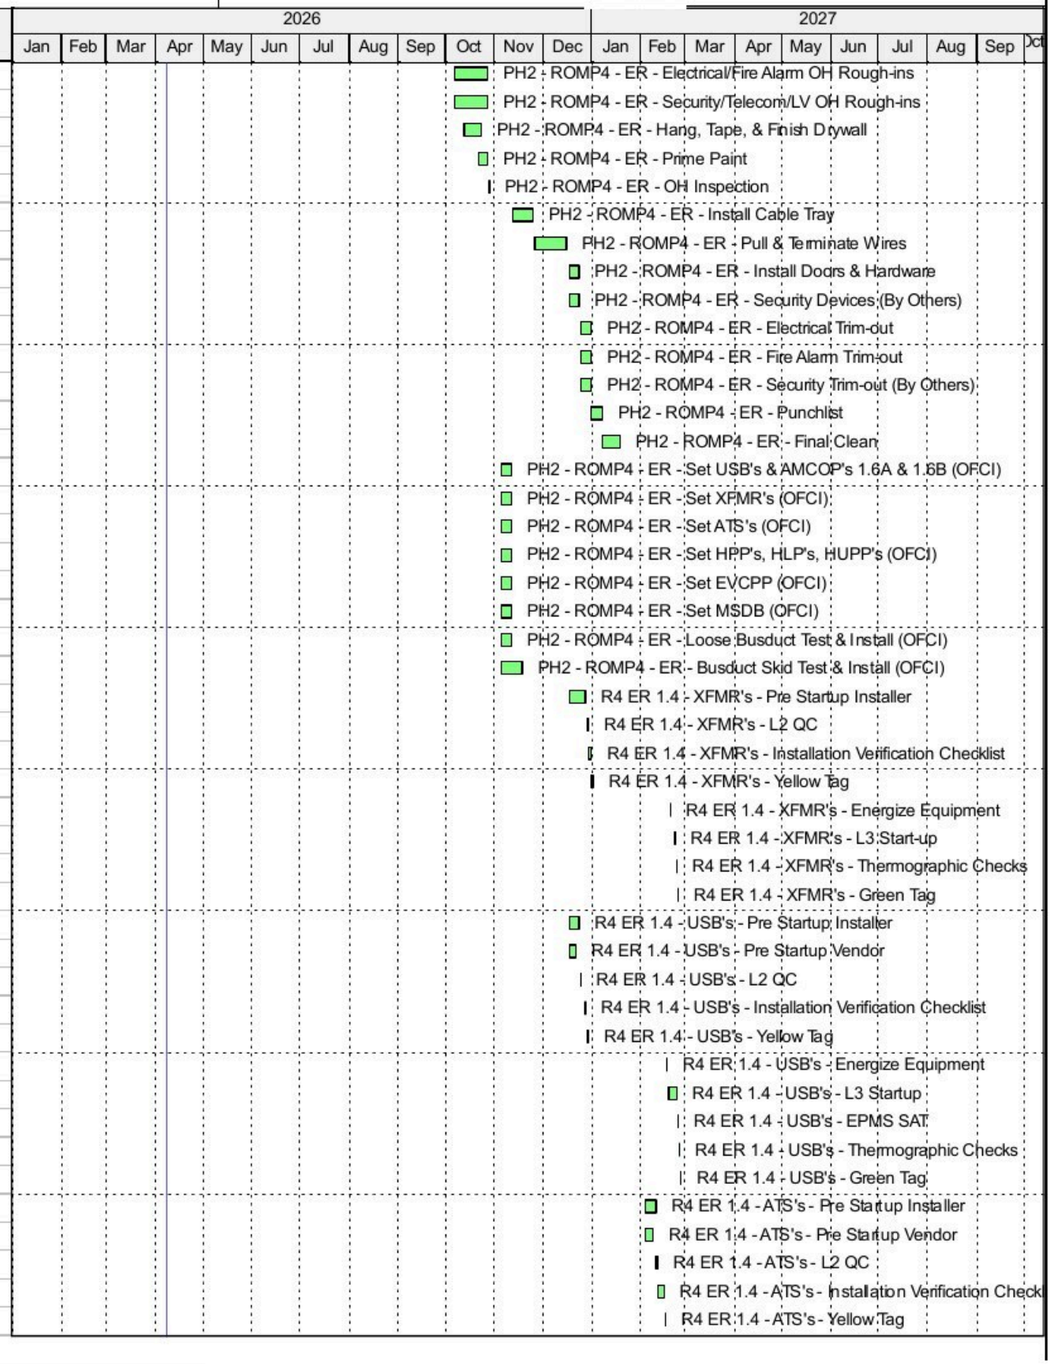

Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH2.R4.ER1.4-ATS.150	R4 ER 1.4 - ATS's - Energize Equipment	1	18-Feb-27	18-Feb-27		
Cx.PH2.R4.ER1.4-ATS.160	R4 ER 1.4 - ATS's - L3 Startup	2	19-Feb-27	22-Feb-27		
Cx.PH2.R4.ER1.4-ATS.170	R4 ER 1.4 - ATS's - EPMS SAT	1	23-Feb-27	23-Feb-27		
Cx.PH2.R4.ER1.4-ATS.180	R4 ER 1.4 - ATS's - Thermographic Checks	1	24-Feb-27	24-Feb-27		
Cx.PH2.R4.ER1.4-ATS.190	R4 ER 1.4 - ATS's - Green Tag	1	25-Feb-27	25-Feb-27		
Cx.PH2.R4.ER1.4-MSDB.100	R4 ER 1.4 - MSDB's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH2.R4.ER1.4-MSDB.110	R4 ER 1.4 - MSDB's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH2.R4.ER1.4-MSDB.120	R4 ER 1.4 - MSDB's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH2.R4.ER1.4-MSDB.130	R4 ER 1.4 - MSDB's - Installation Verification Checklist	2	28-Dec-26	29-Dec-26		
Cx.PH2.R4.ER1.4-MSDB.140	R4 ER 1.4 - MSDB's - Yellow Tag	1	30-Dec-26	30-Dec-26		
Cx.PH2.R4.ER1.4-MSDB.150	R4 ER 1.4 - MSDB's - Energize Equipment	1	22-Feb-27	22-Feb-27		
Cx.PH2.R4.ER1.4-MSDB.160	R4 ER 1.4 - MSDB's - L3 Startup	2	23-Feb-27	24-Feb-27		
Cx.PH2.R4.ER1.4-MSDB.170	R4 ER 1.4 - MSDB's - EPMS SAT	1	25-Feb-27	25-Feb-27		
Cx.PH2.R4.ER1.4-MSDB.180	R4 ER 1.4 - MSDB's - Thermographic Checks	1	26-Feb-27	26-Feb-27		
Cx.PH2.R4.ER1.4-MSDB.190	R4 ER 1.4 - MSDB's - Green Tag	1	01-Mar-27	01-Mar-27		
Cx.PH2.R4.ER1.4-AMCOP.100	R4 ER 1.4 - AMCOP's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH2.R4.ER1.4-AMCOP.110	R4 ER 1.4 - AMCOP's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH2.R4.ER1.4-AMCOP.120	R4 ER 1.4 - AMCOP's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH2.R4.ER1.4-AMCOP.130	R4 ER 1.4 - AMCOP's - Installation Verfication Checklist	2	28-Dec-26	29-Dec-26		
Cx.PH2.R4.ER1.4-AMCOP.140	R4 ER 1.4 - AMCOP's - Yellow Tag	1	30-Dec-26	30-Dec-26		
Cx.PH2.R4.ER1.4-AMCOP.150	R4 ER 1.4 - AMCOP's - Energize Equipment	1	18-Feb-27	18-Feb-27		
Cx.PH2.R4.ER1.4-AMCOP.160	R4 ER 1.4 - AMCOP's - L3 Startup	2	19-Feb-27	22-Feb-27		
Cx.PH2.R4.ER1.4-AMCOP.170	R4 ER 1.4 - AMCOP's - EPMS SAT	1	23-Feb-27	23-Feb-27		
Cx.PH2.R4.ER1.4-AMCOP.180	R4 ER 1.4 - AMCOP's - Thermographic Checks	1	24-Feb-27	24-Feb-27		
Cx.PH2.R4.ER1.4-AMCOP.190	R4 ER 1.4 - AMCOP's - Green Tag	1	25-Feb-27	25-Feb-27		
Cx.PH2.R4.ER1.4-CRAC.100	R4 ER 1.4 - CRAC's - Pre Startup Installer	5	13-Jan-27	21-Jan-27		
Cx.PH2.R4.ER1.4-CRAC.110	R4 ER 1.4 - CRAC's - Pre Startup Vendor	3	13-Jan-27	19-Jan-27		
Cx.PH2.R4.ER1.4-CRAC.120	R4 ER 1.4 - CRAC's - L2 QC	1	25-Jan-27	25-Jan-27		
Cx.PH2.R4.ER1.4-CRAC.130	R4 ER 1.4 - CRAC's - Installation Verification Checklist	2	26-Jan-27	27-Jan-27		
Cx.PH2.R4.ER1.4-CRAC.140	R4 ER 1.4 - CRAC's - Yellow Tag	1	28-Jan-27	28-Jan-27		
Cx.PH2.R4.ER1.4-CRAC.150	R4 ER 1.4 - CRAC's - Energize Equipment	1	10-Feb-27	10-Feb-27		
Cx.PH2.R4.ER1.4-CRAC.160	R4 ER 1.4 - CRAC's - L3 Startup	1	11-Feb-27	11-Feb-27		
Cx.PH2.R4.ER1.4-CRAC.180	R4 ER 1.4 - CRAC's - BAS SAT	1	12-Feb-27	12-Feb-27		
Cx.PH2.R4.ER1.4-CRAC.170	R4 ER 1.4 - CRAC's - TAB	3	15-Feb-27	17-Feb-27		
Cx.PH2.R4.ER1.4-CRAC.190	R4 ER 1.4 - CRAC's - Green Tag	1	18-Feb-27	18-Feb-27		
Cx.PH2.R4.ER1.4-HPP.HLP.100	R4 ER 1.4 - HPP's & HLP's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH2.R4.ER1.4-HPP.HLP.110	R4 ER 1.4 - HPP's & HLP's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH2.R4.ER1.4-HPP.HLP.120	R4 ER 1.4 - HPP's & HLP's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH2.R4.ER1.4-HPP.HLP.130	R4 ER 1.4 - HPP's & HLP's - Installation Verification Checklist	2	28-Dec-26	29-Dec-26		
Cx.PH2.R4.ER1.4-HPP.HLP.140	R4 ER 1.4 - HPP's & HLP's - Yellow Tag	1	30-Dec-26	30-Dec-26		
Cx.PH2.R4.ER1.4-HPP.HLP.150	R4 ER 1.4 - HPP's & HLP's - Energize Equipment	1	22-Feb-27	22-Feb-27		
Cx.PH2.R4.ER1.4-HPP.HLP.160	R4 ER 1.4 - HPP's & HLP's - L3 Startup	1	23-Feb-27	23-Feb-27		
Cx.PH2.R4.ER1.4-HPP.HLP.170	R4 ER 1.4 - HPP's & HLP's - EPMS SAT	1	24-Feb-27	24-Feb-27		
Cx.PH2.R4.ER1.4-HPP.HLP.180	R4 ER 1.4 - HPP's & HLP's - Thermographic Checks	1	25-Feb-27	25-Feb-27		
Cx.PH2.R4.ER1.4-HPP.HLP.190	R4 ER 1.4 - HPP's & HLP's - Green Tag	1	26-Feb-27	26-Feb-27		

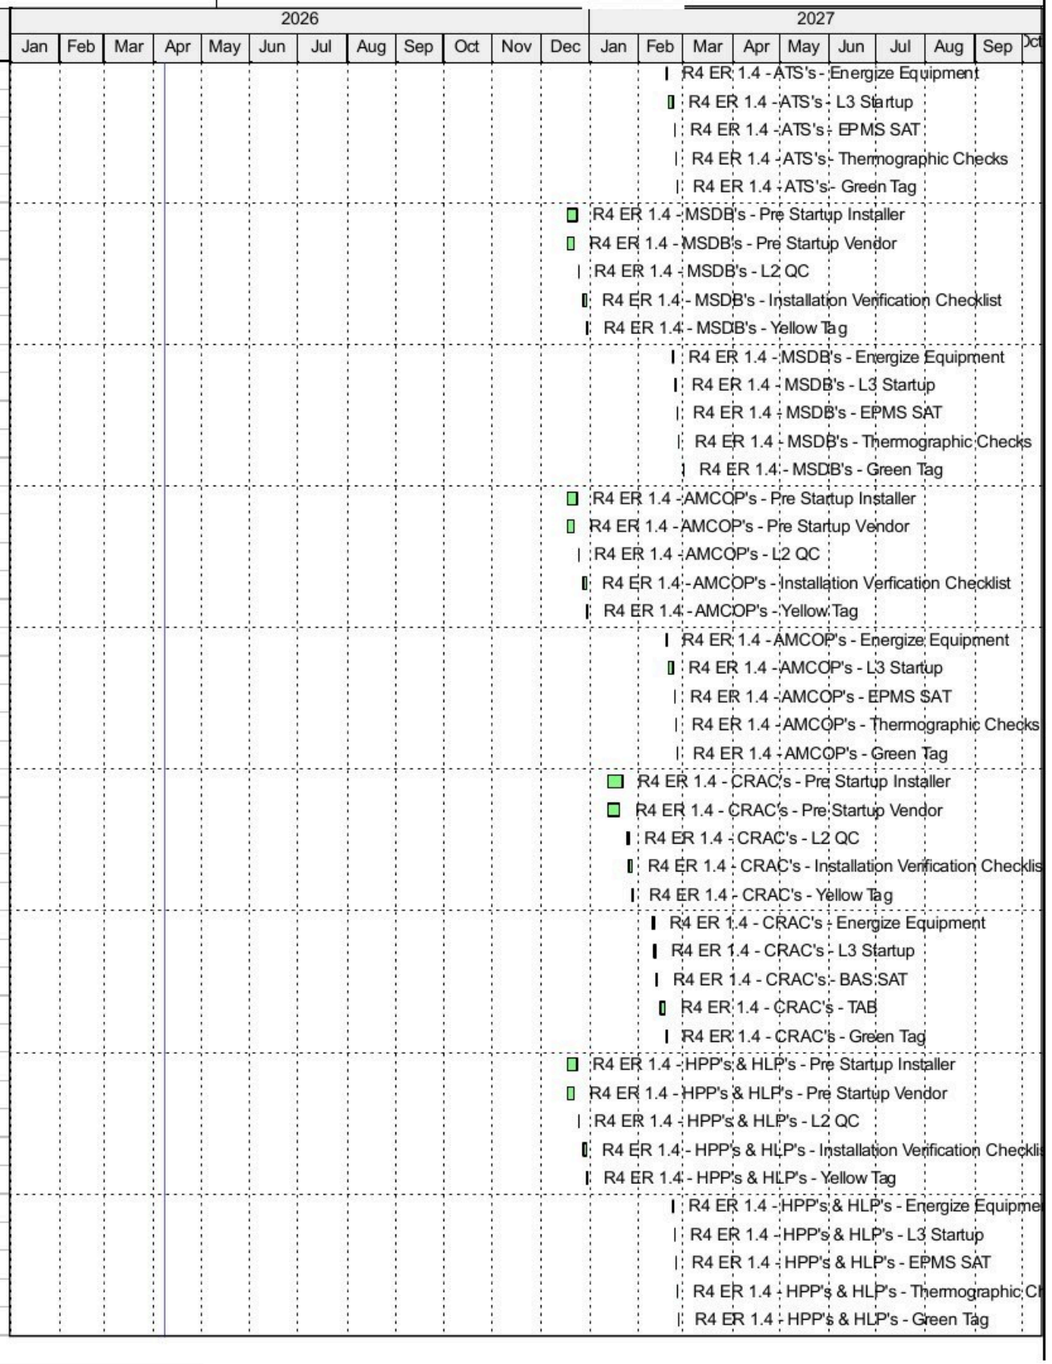


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH2.R4.ER1.4-HUPP.100	R4 ER 1.4 - HUPP's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH2.R4.ER1.4-HUPP.110	R4 ER 1.4 - HUPP's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH2.R4.ER1.4-HUPP.120	R4 ER 1.4 - HUPP's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH2.R4.ER1.4-HUPP.130	R4 ER 1.4 - HUPP's - Installation Verification Checklist	2	28-Dec-26	29-Dec-26		
Cx.PH2.R4.ER1.4-HUPP.140	R4 ER 1.4 - HUPP's - Yellow Tag	1	30-Dec-26	30-Dec-26		
Cx.PH2.R4.ER1.4-HUPP.150	R4 ER 1.4 - HUPP's - Energize Equipment	1	22-Feb-27	22-Feb-27		
Cx.PH2.R4.ER1.4-HUPP.160	R4 ER 1.4 - HUPP's - L3 Startup	1	23-Feb-27	23-Feb-27		
Cx.PH2.R4.ER1.4-HUPP.170	R4 ER 1.4 - HUPP's - EPMS SAT	1	24-Feb-27	24-Feb-27		
Cx.PH2.R4.ER1.4-HUPP.180	R4 ER 1.4 - HUPP's - Thermographic Checks	1	25-Feb-27	25-Feb-27		
Cx.PH2.R4.ER1.4-HUPP.190	R4 ER 1.4 - HUPP's - Green Tag	1	26-Feb-27	26-Feb-27		
Cx.PH2.R4.ER1.4-GENAN.100	R4 ER 1.4 - GENAN's - Pre Startup Installer	5	18-Dec-26	24-Dec-26		
Cx.PH2.R4.ER1.4-GENAN.110	R4 ER 1.4 - GENAN's - Pre Startup Vendor	3	18-Dec-26	22-Dec-26		
Cx.PH2.R4.ER1.4-GENAN.120	R4 ER 1.4 - GENAN's - L2 QC	1	25-Dec-26	25-Dec-26		
Cx.PH2.R4.ER1.4-GENAN.130	R4 ER 1.4 - GENAN's - Installation Verification Checklist	2	28-Dec-26	29-Dec-26		
Cx.PH2.R4.ER1.4-GENAN.140	R4 ER 1.4 - GENAN's - Yellow Tag	1	30-Dec-26	30-Dec-26		
Cx.PH2.R4.ER1.4-GENAN.150	R4 ER 1.4 - GENAN's - Energize Equipment	1	10-Feb-27	10-Feb-27		
Cx.PH2.R4.ER1.4-GENAN.160	R4 ER 1.4 - GENAN's - L3 Startup	1	11-Feb-27	11-Feb-27		
Cx.PH2.R4.ER1.4-GENAN.170	R4 ER 1.4 - GENAN's - EPMS SAT	1	12-Feb-27	12-Feb-27		
Cx.PH2.R4.ER1.4-GENAN.180	R4 ER 1.4 - GENAN's - Thermographics	1	15-Feb-27	15-Feb-27		
Cx.PH2.R4.ER1.4-GENAN.190	R4 ER 1.4 - GENAN's - Green Tag	1	16-Feb-27	16-Feb-27		
PH2 - Data Hall - ROMP's 3 & 4		138	15-Sep-26	25-Mar-27		
PH2.TAHU1.2-IB.650	PH2 - R3&4 - TAHU Gallery - Mechanical OH Rough-ins (High)	5	07-Oct-26	13-Oct-26	Trade	Mechanical
PH2.TAHU1.2-IB.680	PH2 - R3&4 - TAHU Gallery - Mechanical Trim-out	5	25-Jan-27	29-Jan-27	Trade	Mechanical
PH2.TAHU1.2-IB.720	PH2 - R3&4 - TAHU Gallery - Gallery Wall Interior IMP Install	5	15-Sep-26	21-Sep-26		
PH2.TAHU1.2-IB.660	PH2 - R3&4 - TAHU Gallery - Fire Sprinkler OH Rough-ins (High)	10	22-Sep-26	06-Oct-26		
PH2.TAHU1.2-IB.730	PH2 - R3&4 - TAHU Gallery - Gallery Wall Duct Install	5	22-Sep-26	29-Sep-26		
PH2.TAHU1.2-IB.740	PH2 - R3&4 - TAHU Gallery - Gallery Wall Security Mesh Install	5	30-Sep-26	06-Oct-26		
PH2.TAHU1.2-IB.760	PH2 - R3&4 - TAHU Gallery - IW OH Rough-ins (High)	10	30-Sep-26	13-Oct-26		
PH2.TAHU1.2-IB.640	PH2 - R3&4 - TAHU Gallery - Electrical/Fire Alarm OH Rough-ins (Hig	10	07-Oct-26	20-Oct-26		
PH2.TAHU1.2-IB.750	PH2 - R3&4 - TAHU Gallery - Security/Controls OH Rough-ins (High)	10	09-Oct-26	22-Oct-26		
PH2.TAHU1.2-IB.370	PH2 - R3&4 - TAHU Gallery - OH Inspections	1	23-Oct-26	23-Oct-26		
PH2.TAHU1.2-IB.310	PH2 - R3&4 - TAHU Gallery - Install Cable Tray	5	26-Nov-26	02-Dec-26		
PH2.TAHU1.2-IB.350	PH2 - R3&4 - TAHU Gallery - MEPF TAHU Connections	10	26-Nov-26	09-Dec-26		
PH2.TAHU1.2-IB.770	PH2 - R3&4 - TAHU Gallery - Electrical/Fire Alarm OH Rough-ins (Lo	10	03-Dec-26	16-Dec-26		
PH2.TAHU1.2-IB.780	PH2 - R3&4 - TAHU Gallery - Security/Controls OH Rough-ins (Low)	10	03-Dec-26	16-Dec-26		
PH2.TAHU1.2-IB.320	PH2 - R3&4 - TAHU Gallery - Pull & Terminate Wires	15	30-Dec-26	21-Jan-27		
PH2.TAHU1.2-IB.670	PH2 - R3&4 - TAHU Gallery - Electrical Trim-out	5	25-Jan-27	29-Jan-27		
PH2.TAHU1.2-IB.690	PH2 - R3&4 - TAHU Gallery - Fire Alarm Trim-out	5	25-Jan-27	29-Jan-27		
PH2.TAHU1.2-IB.550	PH2 - R3&4 - TAHU Gallery - Punchlist	20	01-Feb-27	26-Feb-27		
PH2.TAHU1.2-IB.560	PH2 - R3&4 - TAHU Gallery - Final Clean	19	01-Mar-27	25-Mar-27		
PH2 - PH2 - ROMP 3 - Data Hall		112	01-Oct-26	05-Mar-27		
PH2.R3.DH1.3-IB.870	PH2 - ROMP3 - DH - Mechanical OH Rough-ins	4	08-Oct-26	13-Oct-26	Trade	Mechanical
PH2.R3.DH1.3-IB.900	PH2 - ROMP3 - DH - Mechanical Trim-out	5	01-Feb-27	05-Feb-27	Trade	Mechanical
PH2.R3.DH1.3-IB.930	PH2 - ROMP3 - DH - Install Liquid Cooling Systems (SFN) (OFCI)	4	19-Jan-27	25-Jan-27	Trade	CFN/SFN Pipir
PH2.R3.DH1.3-IB.740	PH2 - ROMP3 - DH - CE#0007 - Install Liquid Cooling Systems (CFI	6	25-Jan-27	01-Feb-27	Trade	CFN/SFN Pipir

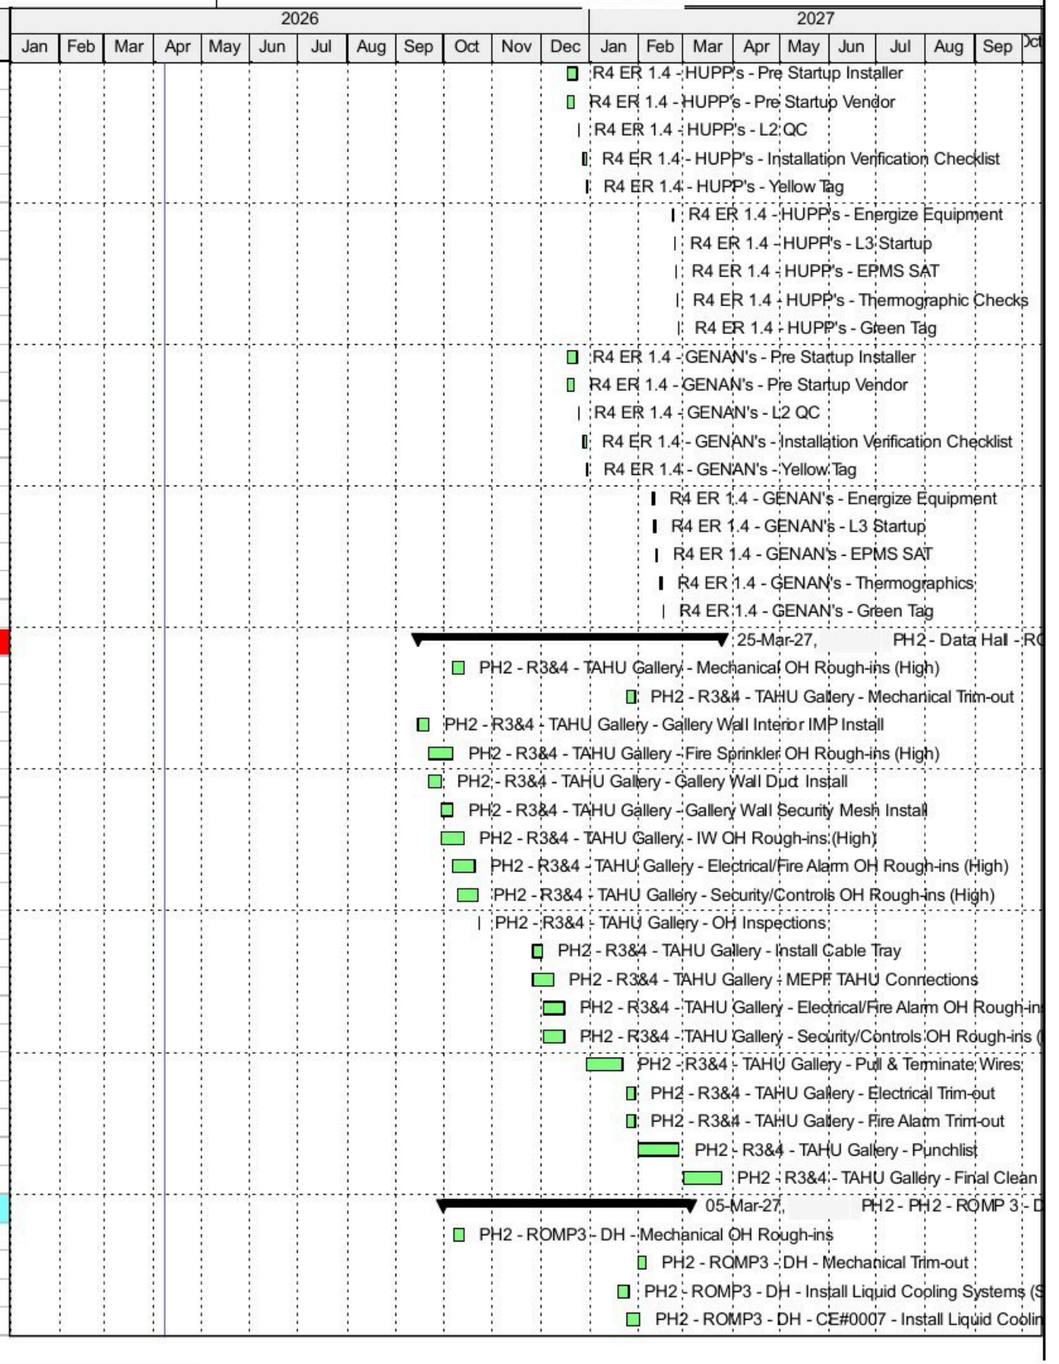


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH2.R3.DH1.3-IB.600	PH2 - ROMP3 - DH - Layout & Frame Walls	5	01-Oct-26	07-Oct-26		
PH2.R3.DH1.3-IB.880	PH2 - ROMP3 - DH - Fire Sprinkler OH Rough-ins	5	01-Oct-26	07-Oct-26		
PH2.R3.DH1.3-IB.770	PH2 - ROMP3 - DH - One-side Drywall	5	08-Oct-26	14-Oct-26		
PH2.R3.DH1.3-IB.810	PH2 - ROMP3 - DH - Plumbing In-Wall Rough-ins	2	08-Oct-26	09-Oct-26		
PH2.R3.DH1.3-IB.820	PH2 - ROMP3 - DH - Electrical In-Wall Rough-Ins	4	08-Oct-26	13-Oct-26		
PH2.R3.DH1.3-IB.830	PH2 - ROMP3 - DH - Fire Alarm In-Wall Rough-Ins	4	08-Oct-26	13-Oct-26		
PH2.R3.DH1.3-IB.840	PH2 - ROMP3 - DH - Security/Telecom/LV In-Wall Rough-ins	4	08-Oct-26	13-Oct-26		
PH2.R3.DH1.3-IB.940	PH2 - ROMP3 - DH - Hang Door Frames	5	08-Oct-26	14-Oct-26		
PH2.R3.DH1.3-IB.750	PH2 - ROMP3 - DH - In-Wall Inspections	1	14-Oct-26	14-Oct-26		
PH2.R3.DH1.3-IB.850	PH2 - ROMP3 - DH - Plumbing OH Rough-ins	4	14-Oct-26	19-Oct-26		
PH2.R3.DH1.3-IB.860	PH2 - ROMP3 - DH - Electrical/Fire Alarm OH Rough-ins	15	14-Oct-26	03-Nov-26		
PH2.R3.DH1.3-IB.950	PH2 - ROMP3 - DH - Security/Telecom/LV OH Rough-ins	15	14-Oct-26	03-Nov-26		
PH2.R3.DH1.3-IB.620	PH2 - ROMP3 - DH - Hang, Tape, & Finish Drywall	10	15-Oct-26	28-Oct-26		
PH2.R3.DH1.3-IB.630	PH2 - ROMP3 - DH - Prime Paint	5	26-Oct-26	30-Oct-26		
PH2.R3.DH1.3-IB.760	PH2 - ROMP3 - DH - OH Inspections	1	04-Nov-26	04-Nov-26		
PH2.R3.DH1.3-IB.650	PH2 - ROMP3 - DH - Ceiling System	5	05-Nov-26	11-Nov-26		
PH2.R3.DH1.3-IB.680	PH2 - ROMP3 - DH - Install Cable Tray	10	15-Dec-26	29-Dec-26		
PH2.R3.DH1.3-IB.735	PH2 - ROMP3 - DH - Temporary Barrier Wall	5	15-Dec-26	22-Dec-26		
PH2.R3.DH1.3-IB.670	PH2 - ROMP3 - DH - Pull & Terminate Wires	15	30-Dec-26	21-Jan-27		
PH2.R3.DH1.3-IB.725	PH2 - ROMP3 - DH - Install Rack Whips (OFCI)	5	30-Dec-26	05-Jan-27		
PH2.R3.DH1.3-IB.690	PH2 - ROMP3 - DH - Install Doors & Hardware	5	25-Jan-27	29-Jan-27		
PH2.R3.DH1.3-IB.890	PH2 - ROMP3 - DH - Electrical Trim-out	5	01-Feb-27	05-Feb-27		
PH2.R3.DH1.3-IB.910	PH2 - ROMP3 - DH - Fire Alarm Trim-out	5	01-Feb-27	05-Feb-27		
PH2.R3.DH1.3-IB.920	PH2 - ROMP3 - DH - Security Trim-out (By Others)	5	01-Feb-27	05-Feb-27		
PH2.R3.DH1.3-IB.780	PH2 - ROMP3 - DH - CE#0007 - Flush and Fill Liquid	10	02-Feb-27	15-Feb-27		
PH2.R3.DH1.3-IB.790	PH2 - ROMP3 - DH - Punchlist	5	08-Feb-27	12-Feb-27		
PH2.R3.DH1.3-IB.800	PH2 - ROMP3 - DH - Final Clean	5	15-Feb-27	19-Feb-27		
PH2 - ROMP 3 - Data Hall Equipment		58	05-Nov-26	25-Jan-27		
PH2.R3.DH1.3-IB.160	PH2 - ROMP3 - DH - Set MTS-IRHX (OFCI)	5	05-Nov-26	11-Nov-26	Trade	HVAC
PH2.R3.DH1.3-IB.150	PH2 - ROMP3 - DH - Set IRHX's (OFCI)	5	18-Jan-27	25-Jan-27	Trade	HVAC
PH2.R3.DH1.3-IB.140	PH2 - ROMP3 - DH - Set PDC's (OFCI)	5	11-Nov-26	17-Nov-26		
PH2.R3.DH1.3-IB.700	PH2 - ROMP3 - DH - Install HAC's	10	24-Nov-26	07-Dec-26		
PH2.R3.DH1.3-IB.710	PH2 - ROMP3 - DH - Install Racks (OFCI)	10	01-Dec-26	14-Dec-26		
PH2 - ROMP 3 - Data Hall Commissioning		30	25-Jan-27	05-Mar-27		
PH2 - ROMP3 - DH - PDC-2.5A-01-05, PDC-2.5B-01-05, PDC-2.6A-01-05, PDC-2.6B-01-05 Cx		30	25-Jan-27	05-Mar-27		
Cx.PH2.R3.DH1.3-PDC.100	R3 DH1.2 - PDC's - Pre Startup Installer	5	25-Jan-27	29-Jan-27		
Cx.PH2.R3.DH1.3-PDC.110	R3 DH1.2 - PDC's - Pre Startup Vendor	5	25-Jan-27	29-Jan-27		
Cx.PH2.R3.DH1.3-PDC.120	R3 DH1.2 - PDC's - L2 QC	1	01-Feb-27	01-Feb-27		
Cx.PH2.R3.DH1.3-PDC.130	R3 DH1.2 - PDC's - Installation Verification Checklist	1	02-Feb-27	02-Feb-27		
Cx.PH2.R3.DH1.3-PDC.140	R3 DH1.2 - PDC's - Yellow Tag	1	03-Feb-27	03-Feb-27		
Cx.PH2.R3.DH1.3-PDC.150	R3 DH1.2 - PDC's - Energize Equipment	1	18-Feb-27	18-Feb-27		
Cx.PH2.R3.DH1.3-PDC.160	R3 DH1.2 - PDC's - L3 Startup	2	19-Feb-27	22-Feb-27		
Cx.PH2.R3.DH1.3-PDC.170	R3 DH1.2 - PDC's - EPMS SAT	1	23-Feb-27	23-Feb-27		
Cx.PH2.R3.DH1.3-PDC.180	R3 DH1.2 - PDC's - Thermographic Checks	1	24-Feb-27	24-Feb-27		
Cx.PH2.R3.DH1.3-PDC.190	R3 DH1.2 - PDC's - Green Tag	1	25-Feb-27	25-Feb-27		

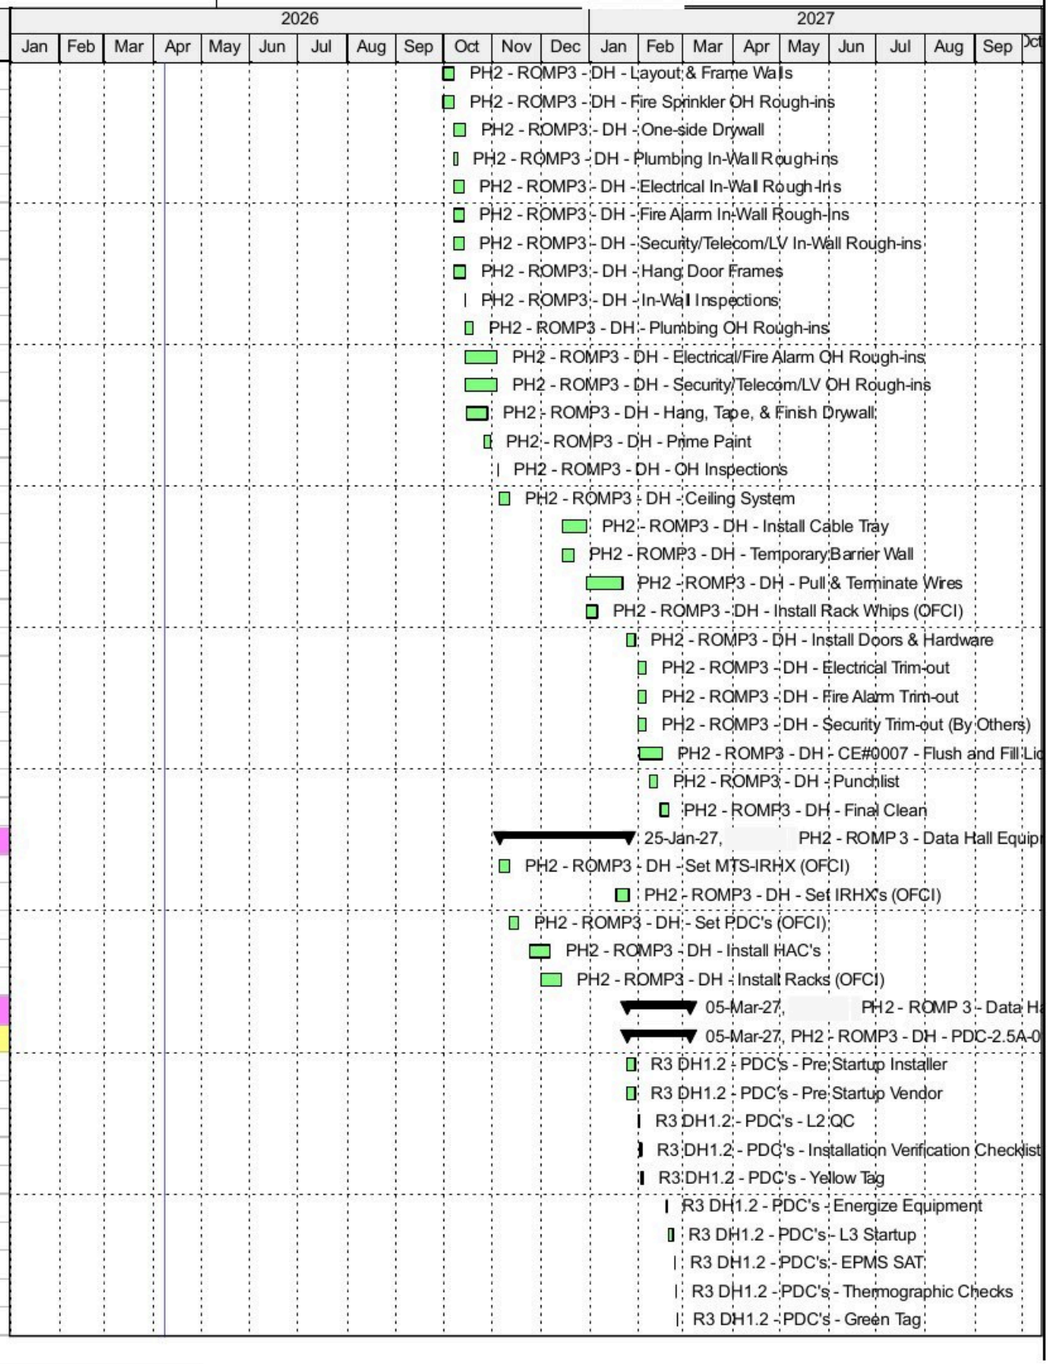


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH2.R3.DH1.3-IRHX.100	R3 DH1.2 - IRHX's - Pre Startup Installer	5	16-Feb-27	22-Feb-27		
Cx.PH2.R3.DH1.3-IRHX.110	R3 DH1.2 - IRHX's - Pre Startup Vendor	3	16-Feb-27	18-Feb-27		
Cx.PH2.R3.DH1.3-IRHX.120	R3 DH1.2 - IRHX's - L2 QC	1	23-Feb-27	23-Feb-27		
Cx.PH2.R3.DH1.3-IRHX.130	R3 DH1.2 - IRHX's - Installation Verification Checklist	1	24-Feb-27	24-Feb-27		
Cx.PH2.R3.DH1.3-IRHX.140	R3 DH1.2 - IRHX's - Yellow Tag	1	25-Feb-27	25-Feb-27		
Cx.PH2.R3.DH1.3-IRHX.150	R3 DH1.2 - IRHX's - Energize Equipment	1	26-Feb-27	26-Feb-27		
Cx.PH2.R3.DH1.3-IRHX.160	R3 DH1.2 - IRHX's - L3 Startup	2	01-Mar-27	02-Mar-27		
Cx.PH2.R3.DH1.3-IRHX.170	R3 DH1.2 - IRHX's - EPMS SAT	1	03-Mar-27	03-Mar-27		
Cx.PH2.R3.DH1.3-IRHX.180	R3 DH1.2 - IRHX's - Thermographic Checks	1	04-Mar-27	04-Mar-27		
Cx.PH2.R3.DH1.3-IRHX.190	R3 DH1.2 - IRHX's - Green Tag	1	05-Mar-27	05-Mar-27		
Cx.PH2.R3.DH1.3-MTS-IRHX.100R3	DH1.2 - MTS-IRHX's - Pre Startup Installer	5	25-Jan-27	29-Jan-27		
Cx.PH2.R3.DH1.3-MTS-IRHX.110R3	DH1.2 - MTS-IRHX's - Pre Startup Vendor	3	25-Jan-27	27-Jan-27		
Cx.PH2.R3.DH1.3-MTS-IRHX.120R3	DH1.2 - MTS-IRHX's - L2 QC	1	01-Feb-27	01-Feb-27		
Cx.PH2.R3.DH1.3-MTS-IRHX.130R3	DH1.2 - MTS-IRHX's - Installation Verification Checklist	1	02-Feb-27	02-Feb-27		
Cx.PH2.R3.DH1.3-MTS-IRHX.140R3	DH1.2 - MTS-IRHX's - Yellow Tag	1	03-Feb-27	03-Feb-27		
Cx.PH2.R3.DH1.3-MTS-IRHX.150R3	DH1.2 - MTS-IRHX's - Energize Equipment	1	19-Feb-27	19-Feb-27		
Cx.PH2.R3.DH1.3-MTS-IRHX.160R3	DH1.2 - MTS-IRHX's - L3 Startup	2	22-Feb-27	23-Feb-27		
Cx.PH2.R3.DH1.3-MTS-IRHX.170R3	DH1.2 - MTS-IRHX's - EPMS SAT	1	24-Feb-27	24-Feb-27		
Cx.PH2.R3.DH1.3-MTS-IRHX.180R3	DH1.2 - MTS-IRHX's - Thermographic Checks	1	25-Feb-27	25-Feb-27		
Cx.PH2.R3.DH1.3-MTS-IRHX.190R3	DH1.2 - MTS-IRHX's - Green Tag	1	26-Feb-27	26-Feb-27		
PH2 - PH2 - ROMP 4 - Data Hall		118	01-Oct-26	15-Mar-27		
PH2.R4.DH1.4-IB.1160	PH2 - ROMP4 - DH - Mechanical OH Rough-ins	4	08-Oct-26	13-Oct-26	Trade	Mechanical
PH2.R4.DH1.4-IB.1190	PH2 - ROMP4 - DH - Mechanical Trim-out	5	01-Feb-27	05-Feb-27	Trade	Mechanical
PH2.R4.DH1.4-IB.1220	PH2 - ROMP4 - DH - Install Liquid Cooling Systems (SFN) (OFCI)	4	26-Jan-27	29-Jan-27	Trade	CFN/SFN Pipir
PH2.R4.DH1.4-IB.1040	PH2 - ROMP4 - DH - CE#0007 - Install Liquid Cooling Systems (CFI	6	02-Feb-27	09-Feb-27	Trade	CFN/SFN Pipir
PH2.R4.DH1.4-IB.930	PH2 - ROMP4 - DH - Layout & Frame Walls	5	01-Oct-26	07-Oct-26		
PH2.R4.DH1.4-IB.1170	PH2 - ROMP4 - DH - Fire Sprinkler OH Rough-ins	5	01-Oct-26	07-Oct-26		
PH2.R4.DH1.4-IB.1070	PH2 - ROMP4 - DH - One-side Drywall	5	08-Oct-26	14-Oct-26		
PH2.R4.DH1.4-IB.1100	PH2 - ROMP4 - DH - plumbing In-Wall Rough-ins	2	08-Oct-26	09-Oct-26		
PH2.R4.DH1.4-IB.1110	PH2 - ROMP4 - DH - Electrical In-Wall Rough-Ins	4	08-Oct-26	13-Oct-26		
PH2.R4.DH1.4-IB.1120	PH2 - ROMP4 - DH - Fire Alarm In-Wall Rough-Ins	4	08-Oct-26	13-Oct-26		
PH2.R4.DH1.4-IB.1130	PH2 - ROMP4 - DH - Security/Telecom/LV In-Wall Rough-ins	4	08-Oct-26	13-Oct-26		
PH2.R4.DH1.4-IB.1240	PH2 - ROMP4 - DH - Hang Door Frames	5	08-Oct-26	14-Oct-26		
PH2.R4.DH1.4-IB.1050	PH2 - ROMP4 - DH - In-Wall Inspections	1	14-Oct-26	14-Oct-26		
PH2.R4.DH1.4-IB.1140	PH2 - ROMP4 - DH - Plumbing OH Rough-ins	4	14-Oct-26	19-Oct-26		
PH2.R4.DH1.4-IB.1150	PH2 - ROMP4 - DH - Electrical/Fire Alarm OH Rough-ins	15	14-Oct-26	03-Nov-26		
PH2.R4.DH1.4-IB.1250	PH2 - ROMP4 - DH - Security/Telecom/LV OH Rough-ins	15	14-Oct-26	03-Nov-26		
PH2.R4.DH1.4-IB.940	PH2 - ROMP4 - DH - Hang, Tape, & Finish Drywall	10	15-Oct-26	28-Oct-26		
PH2.R4.DH1.4-IB.950	PH2 - ROMP4 - DH - Prime Paint	5	26-Oct-26	30-Oct-26		
PH2.R4.DH1.4-IB.1060	PH2 - ROMP4 - DH - OH Inspections	1	04-Nov-26	04-Nov-26		
PH2.R4.DH1.4-IB.960	PH2 - ROMP4 - DH - Ceiling System	5	05-Nov-26	11-Nov-26		
PH2.R4.DH1.4-IB.980	PH2 - ROMP4 - DH - Install Cable Tray	10	15-Dec-26	29-Dec-26		
PH2.R4.DH1.4-IB.1030	PH2 - ROMP4 - DH - Temporary Barrier Wall	5	15-Dec-26	22-Dec-26		
PH2.R4.DH1.4-IB.970	PH2 - ROMP4 - DH - Pull & Terminate Wires	15	30-Dec-26	21-Jan-27		
PH2.R4.DH1.4-IB.1020	PH2 - ROMP4 - DH - Install Rack Whips (OFCI)	5	30-Dec-26	05-Jan-27		

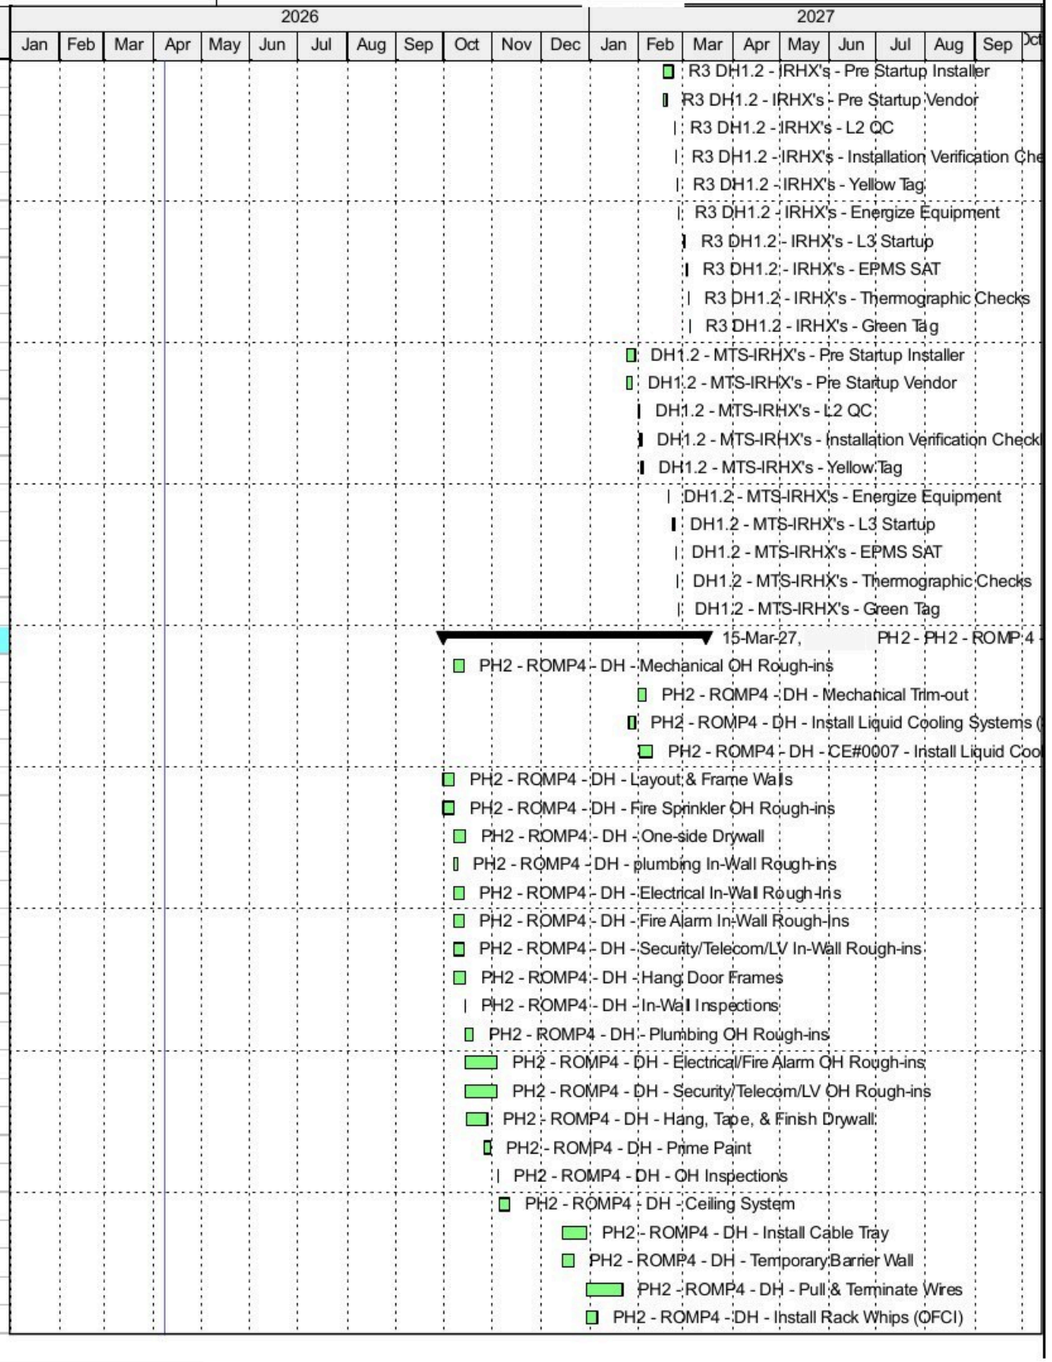


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH2.R4.DH1.4-IB.990	PH2 - ROMP4 - DH - Install Doors & Hardware	5	25-Jan-27	29-Jan-27		
PH2.R4.DH1.4-IB.1180	PH2 - ROMP4 - DH - Electrical Trim-out	5	01-Feb-27	05-Feb-27		
PH2.R4.DH1.4-IB.1200	PH2 - ROMP4 - DH - Fire Alarm Trim-out	5	01-Feb-27	05-Feb-27		
PH2.R4.DH1.4-IB.1210	PH2 - ROMP4 - DH - Security Trim-out (By Others)	5	01-Feb-27	05-Feb-27		
PH2.R4.DH1.4-IB.1080	PH2 - ROMP4 - DH - Punchlist	5	08-Feb-27	12-Feb-27		
PH2.R4.DH1.4-IB.1230	PH2 - ROMP4 - DH - CE#0007 - Flush and Fill Liquid	10	10-Feb-27	23-Feb-27		
PH2.R4.DH1.4-IB.1090	PH2 - ROMP4 - DH - Final Clean	5	15-Feb-27	19-Feb-27		
PH2 - ROMP 4 - Data Hall Equipment		58	05-Nov-26	25-Jan-27		
PH2.R4.DH1.4-IB.200	PH2 - ROMP4 - DH - Set MTS-IRHX (OFCI)	5	05-Nov-26	11-Nov-26	Trade	HVAC
PH2.R4.DH1.4-IB.190	PH2 - ROMP4 - DH - Set IRHX's (OFCI)	5	18-Jan-27	25-Jan-27	Trade	HVAC
PH2.R4.DH1.4-IB.180	PH2 - ROMP4 - DH - Set PDC's (OFCI)	5	11-Nov-26	17-Nov-26		
PH2.R4.DH1.4-IB.1000	PH2 - ROMP4 - DH - Install HAC's	10	24-Nov-26	07-Dec-26		
PH2.R4.DH1.4-IB.1010	PH2 - ROMP4 - DH - Install Racks (OFCI)	10	01-Dec-26	14-Dec-26		
PH2 - ROMP 4 - Data Hall Commissioning		36	25-Jan-27	15-Mar-27		
PH2 - ROMP4 - DH - PDC-1.4A-01-05, PDC-1.4B-01-05, PDC-1.3A-01-05, PDC-1.3B-01-05 Cx		36	25-Jan-27	15-Mar-27		
Cx.PH2.R4.DH1.4-PDC.200	R4 DH1.2 - PDC's - Pre Startup Installer	5	25-Jan-27	29-Jan-27		
Cx.PH2.R4.DH1.4-PDC.210	R4 DH1.2 - PDC's - Pre Startup Vendor	5	25-Jan-27	29-Jan-27		
Cx.PH2.R4.DH1.4-PDC.220	R4 DH1.2 - PDC's - L2 QC	1	01-Feb-27	01-Feb-27		
Cx.PH2.R4.DH1.4-PDC.230	R4 DH1.2 - PDC's - Installation Verification Checklist	1	02-Feb-27	02-Feb-27		
Cx.PH2.R4.DH1.4-PDC.240	R4 DH1.2 - PDC's - Yellow Tag	1	03-Feb-27	03-Feb-27		
Cx.PH2.R4.DH1.4-PDC.250	R4 DH1.2 - PDC's - Energize Equipment	1	10-Feb-27	10-Feb-27		
Cx.PH2.R4.DH1.4-PDC.260	R4 DH1.2 - PDC's - L3 Startup	2	11-Feb-27	12-Feb-27		
Cx.PH2.R4.DH1.4-PDC.270	R4 DH1.2 - PDC's - EPMS SAT	1	15-Feb-27	15-Feb-27		
Cx.PH2.R4.DH1.4-PDC.280	R4 DH1.2 - PDC's - Thermographic Checks	1	16-Feb-27	16-Feb-27		
Cx.PH2.R4.DH1.4-PDC.290	R4 DH1.2 - PDC's - Green Tag	1	17-Feb-27	17-Feb-27		
Cx.PH2.R4.DH1.4-IRHX.200	R4 DH1.2 - IRHX's - Pre Startup Installer	5	24-Feb-27	02-Mar-27		
Cx.PH2.R4.DH1.4-IRHX.210	R4 DH1.2 - IRHX's - Pre Startup Vendor	3	24-Feb-27	26-Feb-27		
Cx.PH2.R4.DH1.4-IRHX.220	R4 DH1.2 - IRHX's - L2 QC	1	03-Mar-27	03-Mar-27		
Cx.PH2.R4.DH1.4-IRHX.230	R4 DH1.2 - IRHX's - Installation Verification Checklist	1	04-Mar-27	04-Mar-27		
Cx.PH2.R4.DH1.4-IRHX.240	R4 DH1.2 - IRHX's - Yellow Tag	1	05-Mar-27	05-Mar-27		
Cx.PH2.R4.DH1.4-IRHX.250	R4 DH1.2 - IRHX's - Energize Equipment	1	08-Mar-27	08-Mar-27		
Cx.PH2.R4.DH1.4-IRHX.260	R4 DH1.2 - IRHX's - L3 Startup	2	09-Mar-27	10-Mar-27		
Cx.PH2.R4.DH1.4-IRHX.270	R4 DH1.2 - IRHX's - EPMS SAT	1	11-Mar-27	11-Mar-27		
Cx.PH2.R4.DH1.4-IRHX.280	R4 DH1.2 - IRHX's - Thermographic Checks	1	12-Mar-27	12-Mar-27		
Cx.PH2.R4.DH1.4-IRHX.290	R4 DH1.2 - IRHX's - Green Tag	1	15-Mar-27	15-Mar-27		
Cx.PH2.R4.DH1.4-MTS-IRHX.200R4	DH1.2 - MTS-IRHX's - Pre Startup Installer	5	25-Jan-27	29-Jan-27		
Cx.PH2.R4.DH1.4-MTS-IRHX.210R4	DH1.2 - MTS-IRHX's - Pre Startup Vendor	3	25-Jan-27	27-Jan-27		
Cx.PH2.R4.DH1.4-MTS-IRHX.220R4	DH1.2 - MTS-IRHX's - L2 QC	1	01-Feb-27	01-Feb-27		
Cx.PH2.R4.DH1.4-MTS-IRHX.230R4	DH1.2 - MTS-IRHX's - Installation Verification Checklist	1	02-Feb-27	02-Feb-27		
Cx.PH2.R4.DH1.4-MTS-IRHX.240R4	DH1.2 - MTS-IRHX's - Yellow Tag	1	03-Feb-27	03-Feb-27		
Cx.PH2.R4.DH1.4-MTS-IRHX.250R4	DH1.2 - MTS-IRHX's - Energize Equipment	1	11-Feb-27	11-Feb-27		
Cx.PH2.R4.DH1.4-MTS-IRHX.260R4	DH1.2 - MTS-IRHX's - L3 Startup	2	12-Feb-27	15-Feb-27		
Cx.PH2.R4.DH1.4-MTS-IRHX.270R4	DH1.2 - MTS-IRHX's - EPMS SAT	1	16-Feb-27	16-Feb-27		
Cx.PH2.R4.DH1.4-MTS-IRHX.280R4	DH1.2 - MTS-IRHX's - Thermographic Checks	1	17-Feb-27	17-Feb-27		
Cx.PH2.R4.DH1.4-MTS-IRHX.290R4	DH1.2 - MTS-IRHX's - Green Tag	1	18-Feb-27	18-Feb-27		

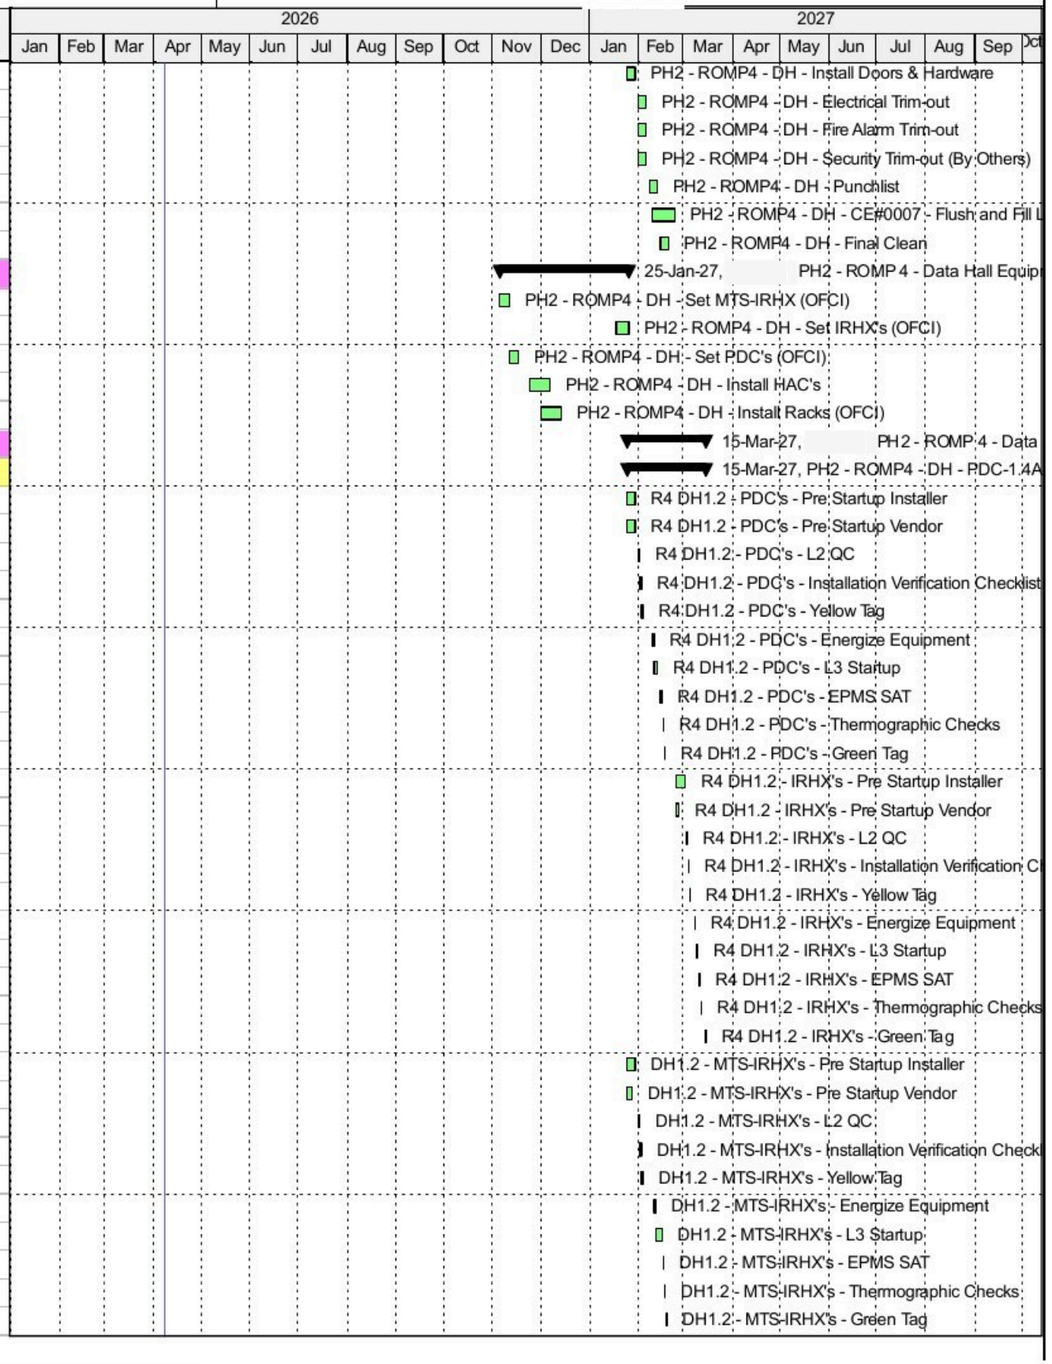


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH2 - ROMP 3 & 4 - TAHU Gallery 1.2 Corridor & Restroom		47	26-Nov-26	29-Jan-27		
PH2.TAHU1.2-IB.250	PH2 - R3&4 - TAHU Gallery Corr - Layout & Frame Walls	5	26-Nov-26	02-Dec-26		
PH2.TAHU1.2-IB.630	PH2 - R3&4 - TAHU Gallery Corr - Plumbing OH Rough-ins	2	26-Nov-26	27-Nov-26		
PH2.TAHU1.2-IB.380	PH2 - R3&4 - TAHU Gallery Corr - One Side Drywall	5	03-Dec-26	09-Dec-26		
PH2.TAHU1.2-IB.590	PH2 - R3&4 - TAHU Gallery Corr - Plumbing In-Wall Rough-ins	4	03-Dec-26	08-Dec-26		
PH2.TAHU1.2-IB.600	PH2 - R3&4 - TAHU Gallery Corr - Electrical In-Wall Rough-Ins	4	03-Dec-26	08-Dec-26		
PH2.TAHU1.2-IB.610	PH2 - R3&4 - TAHU Gallery Corr - Fire Alarm In-Wall Rough-Ins	4	03-Dec-26	08-Dec-26		
PH2.TAHU1.2-IB.620	PH2 - R3&4 - TAHU Gallery Corr - Security/Telecom/LV In-Wall Roug	4	03-Dec-26	08-Dec-26		
PH2.TAHU1.2-IB.710	PH2 - R3&4 - TAHU Gallery Corr - Hang Door Frames	3	03-Dec-26	07-Dec-26		
PH2.TAHU1.2-IB.360	PH2 - R3&4 - TAHU Gallery Corr - In-wall Inspections	1	09-Dec-26	09-Dec-26		
PH2.TAHU1.2-IB.280	PH2 - R3&4 - TAHU Gallery Corr - Hang, Tape, & Finish Drywall	10	10-Dec-26	24-Dec-26		
PH2.TAHU1.2-IB.290	PH2 - R3&4 - TAHU Gallery Corr - Prime Paint	5	22-Dec-26	28-Dec-26		
PH2.TAHU1.2-IB.300	PH2 - R3&4 - TAHU Gallery Corr - Ceiling System	5	29-Dec-26	04-Jan-27		
PH2.TAHU1.2-IB.390	PH2 - R3&4 - TAHU Gallery Corr - Install Security Devices (By Others	5	29-Dec-26	04-Jan-27		
PH3.TAHU1.3-IB.490	PH2 - R3&4 - TAHU Gallery Corr - Install Plumbing Fixtures	2	29-Dec-26	30-Dec-26		
PH3.TAHU1.3-IB.740	PH2 - R3&4 - TAHU Gallery Corr - Flooring	2	31-Dec-26	01-Jan-27		
PH2.TAHU1.2-IB.700	PH2 - R3&4 - TAHU Gallery Corr - Security Trim-out (By Others)	2	05-Jan-27	06-Jan-27		
PH3.TAHU1.3-IB.410	PH2 - R3&4 - TAHU Gallery Corr - Install Toilet Accessories	2	05-Jan-27	06-Jan-27		
PH2.TAHU1.2-IB.330	PH2 - R3&4 - TAHU Gallery Corr - Install Doors & Hardware	5	25-Jan-27	29-Jan-27		
PH2 - ROMP 3 & 4 - TAHU Gallery 1.2 Equipment		5	19-Nov-26	25-Nov-26		
PH2.TAHU1.2-130	PH2 - R3&4 - TAHU Gallery - Set TAHU's (OFCI)	5	19-Nov-26	25-Nov-26	Trade	HVAC
PH2 - ROMP 3 & 4 - TAHU Gallery 1.2 Commissioning		41	13-Jan-27	10-Mar-27		
Cx.PH2.TGAL1.2-TAHU.100	TAHU Gallery 1.2 - TAHU's - Pre Startup Installer	5	13-Jan-27	21-Jan-27		
Cx.PH2.TGAL1.2-TAHU.110	TAHU Gallery 1.2 - TAHU's - Pre Startup Vendor	5	13-Jan-27	21-Jan-27		
Cx.PH2.TGAL1.2-TAHU.120	TAHU Gallery 1.2 - TAHU's - L2 QC	1	25-Jan-27	25-Jan-27		
Cx.PH2.TGAL1.2-TAHU.130	TAHU Gallery 1.2 - TAHU's - Installation Verification Checklist	2	26-Jan-27	27-Jan-27		
Cx.PH2.TGAL1.2-TAHU.140	TAHU Gallery 1.2 - TAHU's - Yellow Tag	1	28-Jan-27	28-Jan-27		
Cx.PH2.TGAL1.2-TAHU.150	TAHU Gallery 1.2 - TAHU's - Energize Equipment	1	19-Feb-27	19-Feb-27		
Cx.PH2.TGAL1.2-TAHU.160	TAHU Gallery 1.2 - TAHU's - L3 Startup	4	22-Feb-27	25-Feb-27		
Cx.PH2.TGAL1.2-TAHU.170	TAHU Gallery 1.2 - TAHU's - BAS SAT	4	26-Feb-27	03-Mar-27		
Cx.PH2.TGAL1.2-TAHU.180	TAHU Gallery 1.2 - TAHU's - Water Test / TAB	4	04-Mar-27	09-Mar-27		
Cx.PH2.TGAL1.2-TAHU.190	TAHU Gallery 1.2 - TAHU's - Green Tag	1	10-Mar-27	10-Mar-27		
PH2 - ROMP 3 & 4 - Mezzanine		65	07-Oct-26	05-Jan-27		
PH2.R3&4.Mezz-650	PH2 - R3&4 - Mezz - Mechanical OH Rough-ins	4	14-Oct-26	19-Oct-26	Trade	Mechanical
PH2.R3&4.Mezz-620	PH2 - R3&4 - Mezz - Mechanical Trim-out	5	18-Nov-26	24-Nov-26	Trade	Mechanical
PH2.R3&4.Mezz-630	PH2 - R3&4 - Mezz - Fire Sprinkler OH Rough-ins	5	07-Oct-26	13-Oct-26		
PH2.R3&4.Mezz-220	PH2 - R3&4 - Mezz - Layout & Frame Walls	5	08-Oct-26	14-Oct-26		
PH2.R3&4.Mezz-320	PH2 - R3&4 - Mezz - One Side Drywall	5	15-Oct-26	21-Oct-26		
PH2.R3&4.Mezz-580	PH2 - R3&4 - Mezz - Plumbing In-Wall Rough-ins	2	15-Oct-26	16-Oct-26		
PH2.R3&4.Mezz-590	PH2 - R3&4 - Mezz - Electrical In-Wall Rough-ins	4	15-Oct-26	20-Oct-26		
PH2.R3&4.Mezz-600	PH2 - R3&4 - Mezz - Fire Alarm In-Wall Rough-ins	4	15-Oct-26	20-Oct-26		
PH2.R3&4.Mezz-610	PH2 - R3&4 - Mezz - Security/Telecom/LV In-Wall Rough-ins	4	15-Oct-26	20-Oct-26		
PH2.R3&4.Mezz-700	PH2 - R3&4 - Mezz - Hang Door Frames	5	15-Oct-26	21-Oct-26		
PH2.R3&4.Mezz-640	PH2 - R3&4 - Mezz - Electrical/Fire Alarm OH Rough-ins	10	20-Oct-26	02-Nov-26		
PH2.R3&4.Mezz-690	PH2 - R3&4 - Mezz - Plumbing OH Rough-ins	5	20-Oct-26	26-Oct-26		

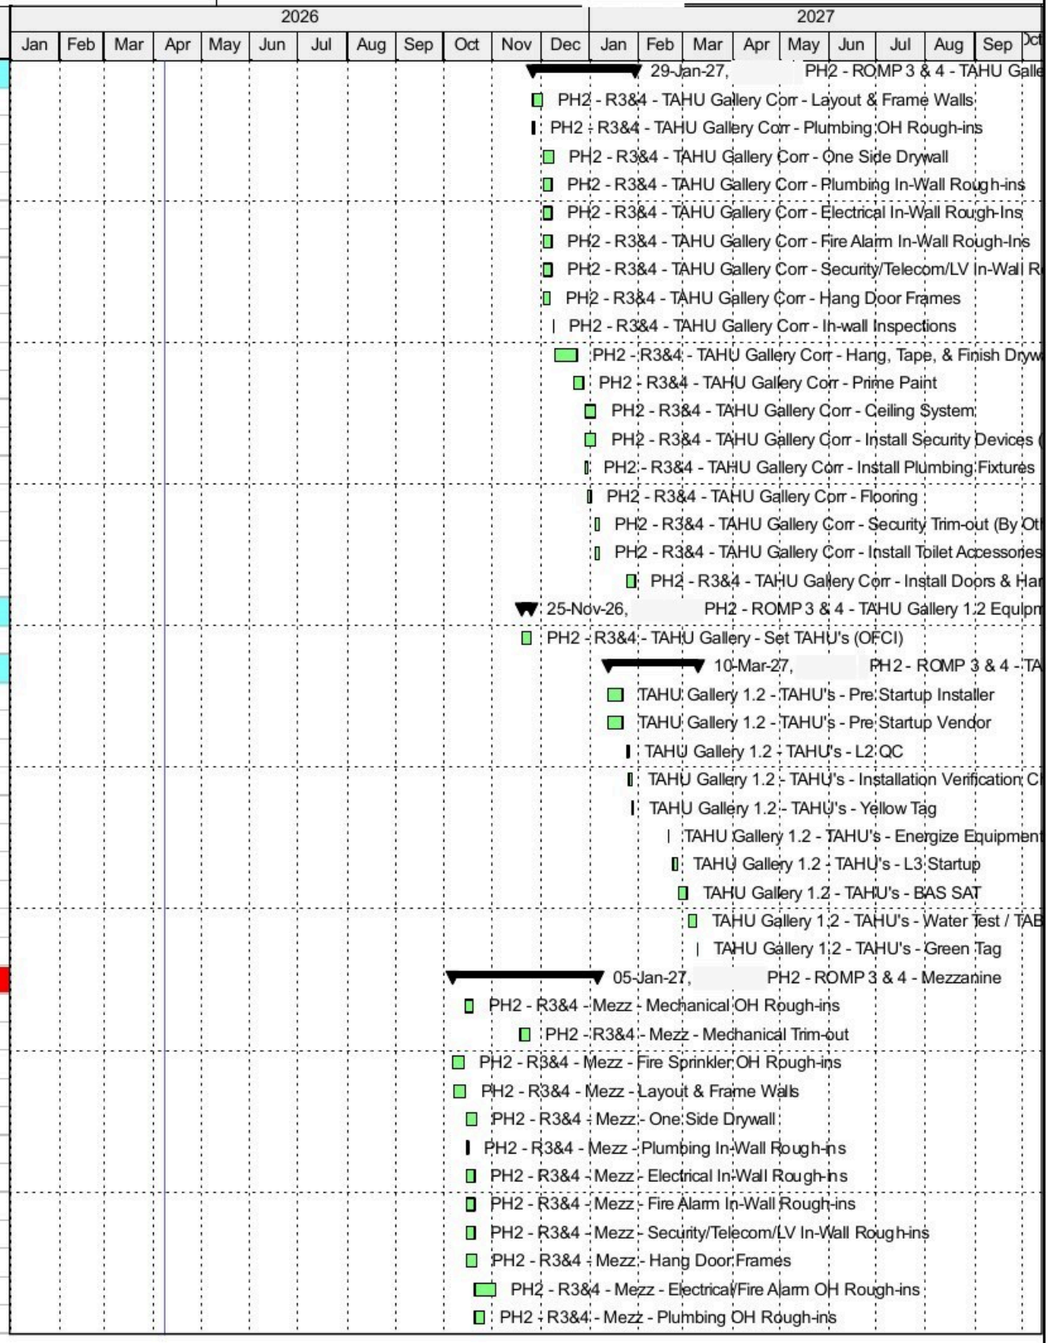


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH2.R3&4.Mezz-645	PH2 - R3&4 - Mezz - Security/Telecom/LV OH Rough-ins	10	20-Oct-26	02-Nov-26		
PH2.R3&4.Mezz-300	PH2 - R3&4 - Mezz - In-Wall Inspections	1	21-Oct-26	21-Oct-26		
PH2.R3&4.Mezz-250	PH2 - R3&4 - Mezz - Hang, Tape, & Finish Drywall	10	22-Oct-26	04-Nov-26		
PH2.R3&4.Mezz-260	PH2 - R3&4 - Mezz - Prime Paint	5	02-Nov-26	06-Nov-26		
PH2.R3&4.Mezz-310	PH2 - R3&4 - Mezz - OH Inspections	1	03-Nov-26	03-Nov-26		
PH2.R3&4.Mezz-680	PH2 - R3&4 - Mezz - Security Trim-out (By Others)	5	04-Nov-26	10-Nov-26		
PH2.R3&4.Mezz-710	PH2 - R3&4 - Mezz - Pull & Terminate Wire	10	04-Nov-26	17-Nov-26		
PH2.R3&4.Mezz-280	PH2 - R3&4 - Mezz - Install Doors & Hardware	5	09-Nov-26	13-Nov-26		
PH2.R3&4.Mezz-570	PH2 - R3&4 - Mezz - Electrical Trim-out	5	18-Nov-26	24-Nov-26		
PH2.R3&4.Mezz-670	PH2 - R3&4 - Mezz - Fire Alarm Trim-out	5	15-Dec-26	22-Dec-26		
PH2.R3&4.Mezz-460	PH2 - R3&4 - Mezz - Punchlist	5	23-Dec-26	29-Dec-26		
PH2.R3&4.Mezz-470	PH2 - R3&4 - Mezz - Final Clean	5	30-Dec-26	05-Jan-27		
PH2 - ROMP 3 & 4 - Stair 05		42	01-Oct-26	27-Nov-26		
PH2 - ROMP 3 & 4 - L1 - Stair 05		39	01-Oct-26	24-Nov-26		
PH2.R4.L1.STR.330	PH2 - R4 - L1 - ST05 - Mechanical OH Rough-Ins	1	05-Oct-26	05-Oct-26	Trade	Mechanical
PH2.R4.L1.STR.530	PH2 - R4 - L1 - ST05 - Mechanical Trim-out	2	26-Oct-26	27-Oct-26	Trade	Mechanical
PH2.R4.L1.STR.300	PH2 - R4 - L1 - ST05 - Fire Sprinkler OH Rough-Ins	2	01-Oct-26	02-Oct-26		
PH2.R4.L1.STR.100	PH2 - R4 - L1 - ST05 - Layout Walls	1	01-Oct-26	01-Oct-26		
PH2.R4.L1.STR.110	PH2 - R4 - L1 - ST05 - Frame Walls	2	02-Oct-26	05-Oct-26		
PH2.R4.L1.STR.310	PH2 - R4 - L1 - ST05 - Electrical/Fire Alarm OH Rough-Ins	3	05-Oct-26	07-Oct-26		
PH2.R4.L1.STR.320	PH2 - R4 - L1 - ST05 - Sec/Telecom OH Rough-Ins	3	05-Oct-26	07-Oct-26		
PH2.R4.L1.STR.120	PH2 - R4 - L1 - ST05 - One Side Drywall	2	06-Oct-26	07-Oct-26		
PH2.R4.L1.STR.200	PH2 - R4 - L1 - ST05 - Electrical/Fire Alarm In-Wall Rough-Ins	3	06-Oct-26	08-Oct-26		
PH2.R4.L1.STR.210	PH2 - R4 - L1 - ST05 - Sec/Telecom In-Wall Rough-Ins	3	06-Oct-26	08-Oct-26		
PH2.R4.L1.STR.130	PH2 - R4 - L1 - ST05 - Hang Door Frames	1	08-Oct-26	08-Oct-26		
PH2.R4.L1.STR.390	PH2 - R4 - L1 - ST05 - OH Inspections	1	08-Oct-26	08-Oct-26		
PH2.R4.L1.STR.290	PH2 - R4 - L1 - ST05 - In-Wall Inspections	1	09-Oct-26	09-Oct-26		
PH2.R4.L1.STR.140	PH2 - R4 - L1 - ST05 - Hang, Tape, & Finish Drywall	3	12-Oct-26	14-Oct-26		
PH2.R4.L1.STR.160	PH2 - R4 - L1 - ST05 - Prime Paint	2	15-Oct-26	16-Oct-26		
PH2.R4.L1.STR.500	PH2 - R4 - L1 - ST05 - Fire Sprinkler Trim-out	2	19-Oct-26	20-Oct-26		
PH2.R4.L1.STR.490	PH2 - R4 - L1 - ST05 - Install Security Devices (By Others)	5	19-Oct-26	23-Oct-26		
PH2.R4.L1.STR.410	PH2 - R4 - L1 - ST05 - Pull & Terminate Wires	5	19-Oct-26	23-Oct-26		
PH2.R4.L1.STR.580	PH2 - R4 - L1 - ST05 - Install Lighting	2	19-Oct-26	20-Oct-26		
PH2.R4.L1.STR.510	PH2 - R4 - L1 - ST05 - Electrical Trim-out	2	26-Oct-26	27-Oct-26		
PH2.R4.L1.STR.520	PH2 - R4 - L1 - ST05 - Fire Alarm Trim-out	2	26-Oct-26	27-Oct-26		
PH2.R4.L1.STR.590	PH2 - R4 - L1 - ST05 - Security Trim-out (By Others)	5	26-Oct-26	30-Oct-26		
PH2.R4.L1.STR.400	PH2 - R4 - L1 - ST05 - Install Doors & Hardware	1	29-Oct-26	29-Oct-26		
PH2.R4.L1.STR.600	PH2 - R4 - L1 - ST05 - Final Paint	5	02-Nov-26	06-Nov-26		
PH2.R4.L1.STR.610	PH2 - R4 - L1 - ST05 - Install Signage	2	09-Nov-26	10-Nov-26		
PH2.R4.L1.STR.680	PH2 - R4 - L1 - ST05 - Punchlist	5	11-Nov-26	17-Nov-26		
PH2.R4.L1.STR.690	PH2 - R4 - L1 - ST05 - Final Clean	5	18-Nov-26	24-Nov-26		
PH2 - ROMP 3 & 4 - M1 - Stair 05		41	02-Oct-26	27-Nov-26		
PH2.R4.M1.STR.330	PH2 - R4 - M1 - ST05 - Mechanical OH Rough-Ins	1	07-Oct-26	07-Oct-26	Trade	Mechanical
PH2.R4.M1.STR.530	PH2 - R4 - M1 - ST05 - Mechanical Trim-out	2	29-Oct-26	30-Oct-26	Trade	Mechanical
PH2.R4.M1.STR.100	PH2 - R4 - M1 - ST05 - Layout Walls	1	02-Oct-26	02-Oct-26		

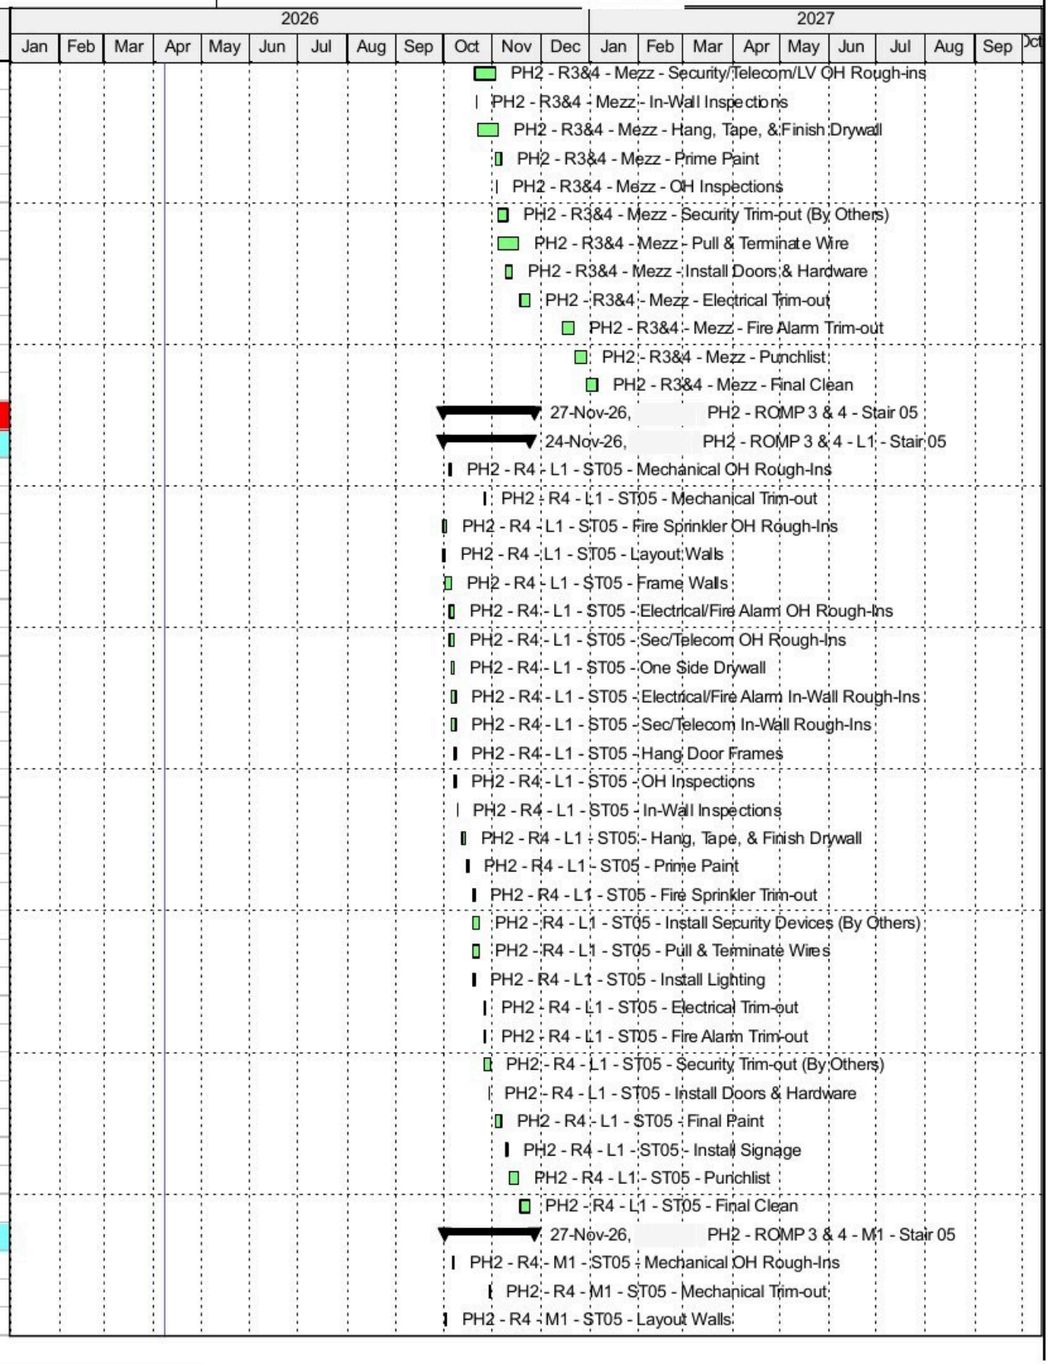


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH2.R4.M1.STR.300	PH2 - R4 - M1 - ST05 - Fire Sprinkler OH Rough-Ins	2	05-Oct-26	06-Oct-26		
PH2.R4.M1.STR.110	PH2 - R4 - M1 - ST05 - Frame Walls	2	06-Oct-26	07-Oct-26		
PH2.R4.M1.STR.120	PH2 - R4 - M1 - ST05 - One Side Drywall	2	08-Oct-26	09-Oct-26		
PH2.R4.M1.STR.310	PH2 - R4 - M1 - ST05 - Electrical/Fire Alarm OH Rough-Ins	3	08-Oct-26	12-Oct-26		
PH2.R4.M1.STR.320	PH2 - R4 - M1 - ST05 - Sec/Telecom OH Rough-Ins	3	08-Oct-26	12-Oct-26		
PH2.R4.M1.STR.200	PH2 - R4 - M1 - ST05 - Electrical/Fire Alarm In-Wall Rough-Ins	3	09-Oct-26	13-Oct-26		
PH2.R4.M1.STR.210	PH2 - R4 - M1 - ST05 - Sec/Telecom In-Wall Rough-Ins	3	09-Oct-26	13-Oct-26		
PH2.R4.M1.STR.130	PH2 - R4 - M1 - ST05 - Hang Door Frames	1	12-Oct-26	12-Oct-26		
PH2.R4.M1.STR.390	PH2 - R4 - M1 - ST05 - OH Inspections	1	13-Oct-26	13-Oct-26		
PH2.R4.M1.STR.290	PH2 - R4 - M1 - ST05 - In-Wall Inspections	1	14-Oct-26	14-Oct-26		
PH2.R4.M1.STR.140	PH2 - R4 - M1 - ST05 - Hang, Tape, & Finish Drywall	3	15-Oct-26	19-Oct-26		
PH2.R4.M1.STR.160	PH2 - R4 - M1 - ST05 - Prime Paint	2	20-Oct-26	21-Oct-26		
PH2.R4.M1.STR.500	PH2 - R4 - M1 - ST05 - Fire Sprinkler Trim-out	2	22-Oct-26	23-Oct-26		
PH2.R4.M1.STR.490	PH2 - R4 - M1 - ST05 - Install Security Devices (By Others)	5	22-Oct-26	28-Oct-26		
PH2.R4.M1.STR.410	PH2 - R4 - M1 - ST05 - Pull & Terminate Wires	5	22-Oct-26	28-Oct-26		
PH2.R4.M1.STR.580	PH2 - R4 - M1 - ST05 - Install Lighting	2	22-Oct-26	23-Oct-26		
PH2.R4.M1.STR.510	PH2 - R4 - M1 - ST05 - Electrical Trim-out	2	29-Oct-26	30-Oct-26		
PH2.R4.M1.STR.520	PH2 - R4 - M1 - ST05 - Fire Alarm Trim-out	2	29-Oct-26	30-Oct-26		
PH2.R4.M1.STR.590	PH2 - R4 - M1 - ST05 - Security Trim-out (By Others)	5	29-Oct-26	04-Nov-26		
PH2.R4.M1.STR.400	PH2 - R4 - M1 - ST05 - Install Doors & Hardware	1	30-Oct-26	30-Oct-26		
PH2.R4.M1.STR.600	PH2 - R4 - M1 - ST05 - Final Paint	5	05-Nov-26	11-Nov-26		
PH2.R4.M1.STR.610	PH2 - R4 - M1 - ST05 - Install Signage	2	12-Nov-26	13-Nov-26		
PH2.R4.M1.STR.680	PH2 - R4 - M1 - ST05 - Punchlist	5	16-Nov-26	20-Nov-26		
PH2.R4.M1.STR.690	PH2 - R4 - M1 - ST05 - Final Clean	5	23-Nov-26	27-Nov-26		
Phase 3 (ROMP 5 & 6)		174	22-Sep-26	21-May-27		
PH3 - ROMP5 & 6 - Electrical Rooms 1.5 & 1.6		133	01-Oct-26	05-Apr-27		
PH3 - ROMP5 - Electrical Room 1.5		125	01-Oct-26	24-Mar-27		
PH3.R5.ER1.5-IB.1000	PH3 - ROMP5 - ER - Mechanical OH Rough-ins	4	08-Oct-26	13-Oct-26	Trade	Mechanical
PH3.R5.ER1.5-IB.1030	PH3 - ROMP5 - ER - Mechanical Trim-out	5	02-Feb-27	08-Feb-27	Trade	Mechanical
PH3.R5.ER1.5-380	PH3 - ROMP5 - ER - Set CRAC Units	5	02-Nov-26	06-Nov-26	Trade	HVAC
PH3.R5.ER1.5-IB.600	PH3 - ROMP5 - ER - Layout & Frame Walls	5	01-Oct-26	07-Oct-26		
PH3.R5.ER1.5-IB.1010	PH3 - ROMP5 - ER - Fire Sprinkler OH Rough-ins	5	01-Oct-26	07-Oct-26		
PH3.R5.ER1.5-IB.700	PH3 - ROMP5 - ER - One Side Drywall	5	08-Oct-26	14-Oct-26		
PH3.R5.ER1.5-IB.940	PH3 - ROMP5 - ER - Plumbing In-Wall Rough-ins	2	08-Oct-26	09-Oct-26		
PH3.R5.ER1.5-IB.950	PH3 - ROMP5 - ER - Electrical In-Wall Rough-ins	4	08-Oct-26	13-Oct-26		
PH3.R5.ER1.5-IB.960	PH3 - ROMP5 - ER - Fire Alarm In-Wall Rough-ins	4	08-Oct-26	13-Oct-26		
PH3.R5.ER1.5-IB.970	PH3 - ROMP5 - ER - Security/Telecom/LV In-Wall Rough-ins	4	08-Oct-26	13-Oct-26		
PH3.R5.ER1.5-IB.1060	PH3 - ROMP5 - ER - Hang Door Frames	5	08-Oct-26	14-Oct-26		
PH3.R5.ER1.5-IB.710	PH3 - ROMP5 - ER - In-Wall Inspection	1	14-Oct-26	14-Oct-26		
PH3.R5.ER1.5-IB.980	PH3 - ROMP5 - ER - Plumbing OH Rough-ins	4	14-Oct-26	19-Oct-26		
PH3.R5.ER1.5-IB.990	PH3 - ROMP5 - ER - Electrical/Fire Alarm OH Rough-ins	15	14-Oct-26	03-Nov-26		
PH3.R5.ER1.5-IB.995	PH3 - ROMP5 - ER - Security/Telecom/LV OH Rough-ins	15	14-Oct-26	03-Nov-26		
PH3.R5.ER1.5-IB.620	PH3 - ROMP5 - ER - Hang, Tape, & Finish Drywall	10	15-Oct-26	28-Oct-26		
PH3.R5.ER1.5-IB.630	PH3 - ROMP5 - ER - Prime Paint	5	26-Oct-26	30-Oct-26		
PH3.R5.ER1.5-IB.730	PH3 - ROMP5 - ER - OH Inspection	1	04-Nov-26	04-Nov-26		

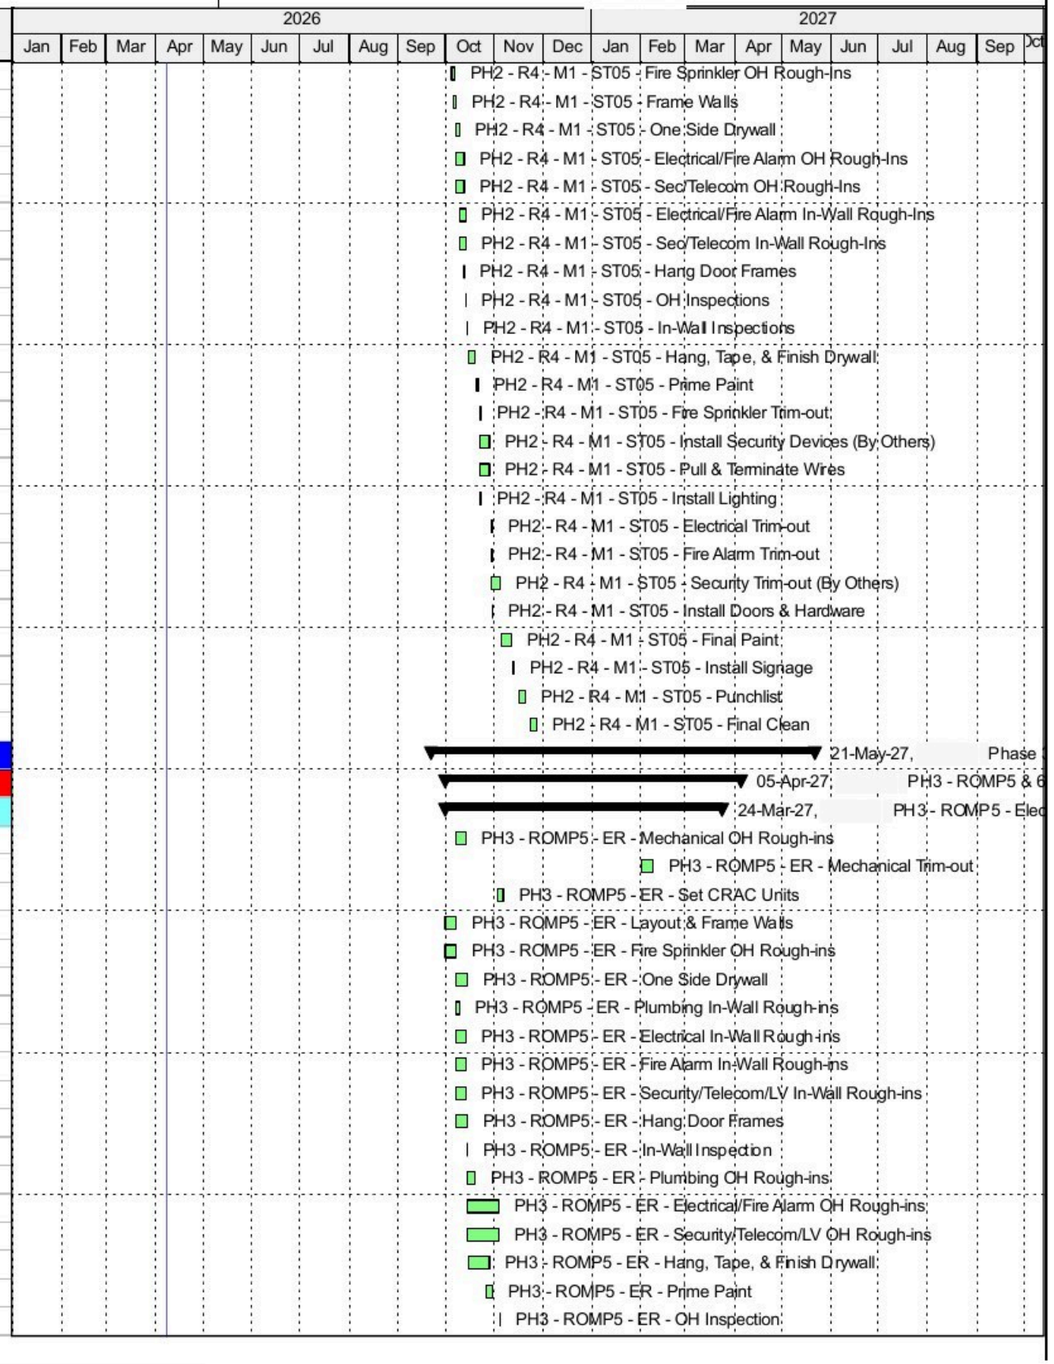


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH3.R5.ER1.5-IB.680	PH3 - ROMP5 - ER - Install Cable Tray	10	16-Dec-26	30-Dec-26		
PH3.R5.ER1.5-IB.670	PH3 - ROMP5 - ER - Pull & Terminate Wires	15	31-Dec-26	25-Jan-27		
PH3.R5.ER1.5-IB.690	PH3 - ROMP5 - ER - Install Doors & Hardware	5	26-Jan-27	01-Feb-27		
PH3.R5.ER1.5-IB.740	PH3 - ROMP5 - ER - Security Devices (By Others)	5	26-Jan-27	01-Feb-27		
PH3.R5.ER1.5-IB.660	PH3 - ROMP5 - ER - MEPF Trim-out	10	02-Feb-27	15-Feb-27		
PH3.R5.ER1.5-IB.1020	PH3 - ROMP5 - ER - Electrical Trim-out	5	02-Feb-27	08-Feb-27		
PH3.R5.ER1.5-IB.1040	PH3 - ROMP5 - ER - Fire Alarm Trim-out	5	02-Feb-27	08-Feb-27		
PH3.R5.ER1.5-IB.1050	PH3 - ROMP5 - ER - Security Trim-out (By Others)	5	02-Feb-27	08-Feb-27		
PH3.R5.ER1.5-IB.900	PH3 - ROMP5 - ER - Punchlist	5	16-Feb-27	22-Feb-27		
PH3.R5.ER1.5-IB.910	PH3 - ROMP5 - ER - Final Clean	5	23-Feb-27	01-Mar-27		
PH3.R5.ER1.5-320	PH3 - ROMP5 - ER - Set USB's & AMCOP's 1.5A & 1.5B (OFCI)	5	09-Dec-26	15-Dec-26		
PH3.R5.ER1.5-330	PH3 - ROMP5 - ER - Set XFMR's (OFCI)	5	09-Dec-26	15-Dec-26		
PH3.R5.ER1.5-340	PH3 - ROMP5 - ER - Set ATS's (OFCI)	5	09-Dec-26	15-Dec-26		
PH3.R5.ER1.5-350	PH3 - ROMP5 - ER - Set HUPP's (OFCI)	5	09-Dec-26	15-Dec-26		
PH3.R5.ER1.5-360	PH3 - ROMP5 - ER - Set MSDB (OFCI)	5	09-Dec-26	15-Dec-26		
PH3.R5.ER1.5-370	PH3 - ROMP5 - ER - Loose Busduct Test & Install (OFCI)	5	09-Dec-26	15-Dec-26		
PH3.R5.ER1.5-390	PH3 - ROMP5 - ER - Busduct Skid Test & Install (OFCI)	10	09-Dec-26	23-Dec-26		
Cx.PH3.R5.ER1.5-XFMR.180	R5 ER 1.5 - XFMR's - Pre Startup Installer	7	02-Mar-27	10-Mar-27		
Cx.PH3.R5.ER1.5-XFMR.190	R5 ER 1.5 - XFMR's - L2 QC	1	11-Mar-27	11-Mar-27		
Cx.PH3.R5.ER1.5-XFMR.100	R5 ER 1.5 - XFMR's - Installation Verification Checklist	2	12-Mar-27	15-Mar-27		
Cx.PH3.R5.ER1.5-XFMR.110	R5 ER 1.5 - XFMR's - Yellow Tag	1	16-Mar-27	16-Mar-27		
Cx.PH3.R5.ER1.5-XFMR.120	R5 ER 1.5 - XFMR's - Energize Equipment	1	17-Mar-27	17-Mar-27		
Cx.PH3.R5.ER1.5-XFMR.130	R5 ER 1.5 - XFMR's - L3 Start-up	1	18-Mar-27	18-Mar-27		
Cx.PH3.R5.ER1.5-XFMR.140	R5 ER 1.5 - XFMR's - Thermographic Checks	1	19-Mar-27	19-Mar-27		
Cx.PH3.R5.ER1.5-XFMR.150	R5 ER 1.5 - XFMR's - Green Tag	1	22-Mar-27	22-Mar-27		
Cx.PH3.R5.ER1.5-USB.100	R5 ER 1.5 - USB's - Pre Startup Installer	5	02-Mar-27	08-Mar-27		
Cx.PH3.R5.ER1.5-USB.110	R5 ER 1.5 - USB's - Pre Startup Vendor	3	02-Mar-27	04-Mar-27		
Cx.PH3.R5.ER1.5-USB.120	R5 ER 1.5 - USB's - L2 QC	1	09-Mar-27	09-Mar-27		
Cx.PH3.R5.ER1.5-USB.130	R5 ER 1.5 - USB's - Installation Verification Checklist	1	10-Mar-27	10-Mar-27		
Cx.PH3.R5.ER1.5-USB.140	R5 ER 1.5 - USB's - Yellow Tag	1	11-Mar-27	11-Mar-27		
Cx.PH3.R5.ER1.5-USB.150	R5 ER 1.5 - USB's - Energize Equipment	1	12-Mar-27	12-Mar-27		
Cx.PH3.R5.ER1.5-USB.160	R5 ER 1.5 - USB's - L3 Startup	4	15-Mar-27	18-Mar-27		
Cx.PH3.R5.ER1.5-USB.170	R5 ER 1.5 - USB's - EPMS SAT	1	19-Mar-27	19-Mar-27		
Cx.PH3.R5.ER1.5-USB.180	R5 ER 1.5 - USB's - Thermographic Checks	1	22-Mar-27	22-Mar-27		
Cx.PH3.R5.ER1.5-USB.190	R5 ER 1.5 - USB's - Green Tag	1	23-Mar-27	23-Mar-27		
Cx.PH3.R5.ER1.5-ATS.110	R5 ER 1.5 - ATS's - Pre Startup Vendor	3	16-Feb-27	18-Feb-27		
Cx.PH3.R5.ER1.5-ATS.100	R5 ER 1.5 - ATS's - Pre Startup Installer	5	02-Mar-27	08-Mar-27		
Cx.PH3.R5.ER1.5-ATS.120	R5 ER 1.5 - ATS's - L2 QC	1	09-Mar-27	09-Mar-27		
Cx.PH3.R5.ER1.5-ATS.130	R5 ER 1.5 - ATS's - Installation Verification Checklist	2	10-Mar-27	11-Mar-27		
Cx.PH3.R5.ER1.5-ATS.140	R5 ER 1.5 - ATS's - Yellow Tag	1	12-Mar-27	12-Mar-27		
Cx.PH3.R5.ER1.5-ATS.150	R5 ER 1.5 - ATS's - Energize Equipment	1	15-Mar-27	15-Mar-27		
Cx.PH3.R5.ER1.5-ATS.160	R5 ER 1.5 - ATS's - L3 Startup	2	16-Mar-27	17-Mar-27		
Cx.PH3.R5.ER1.5-ATS.170	R5 ER 1.5 - ATS's - EPMS SAT	1	18-Mar-27	18-Mar-27		
Cx.PH3.R5.ER1.5-ATS.180	R5 ER 1.5 - ATS's - Thermographic Checks	1	19-Mar-27	19-Mar-27		
Cx.PH3.R5.ER1.5-ATS.190	R5 ER 1.5 - ATS's - Green Tag	1	22-Mar-27	22-Mar-27		

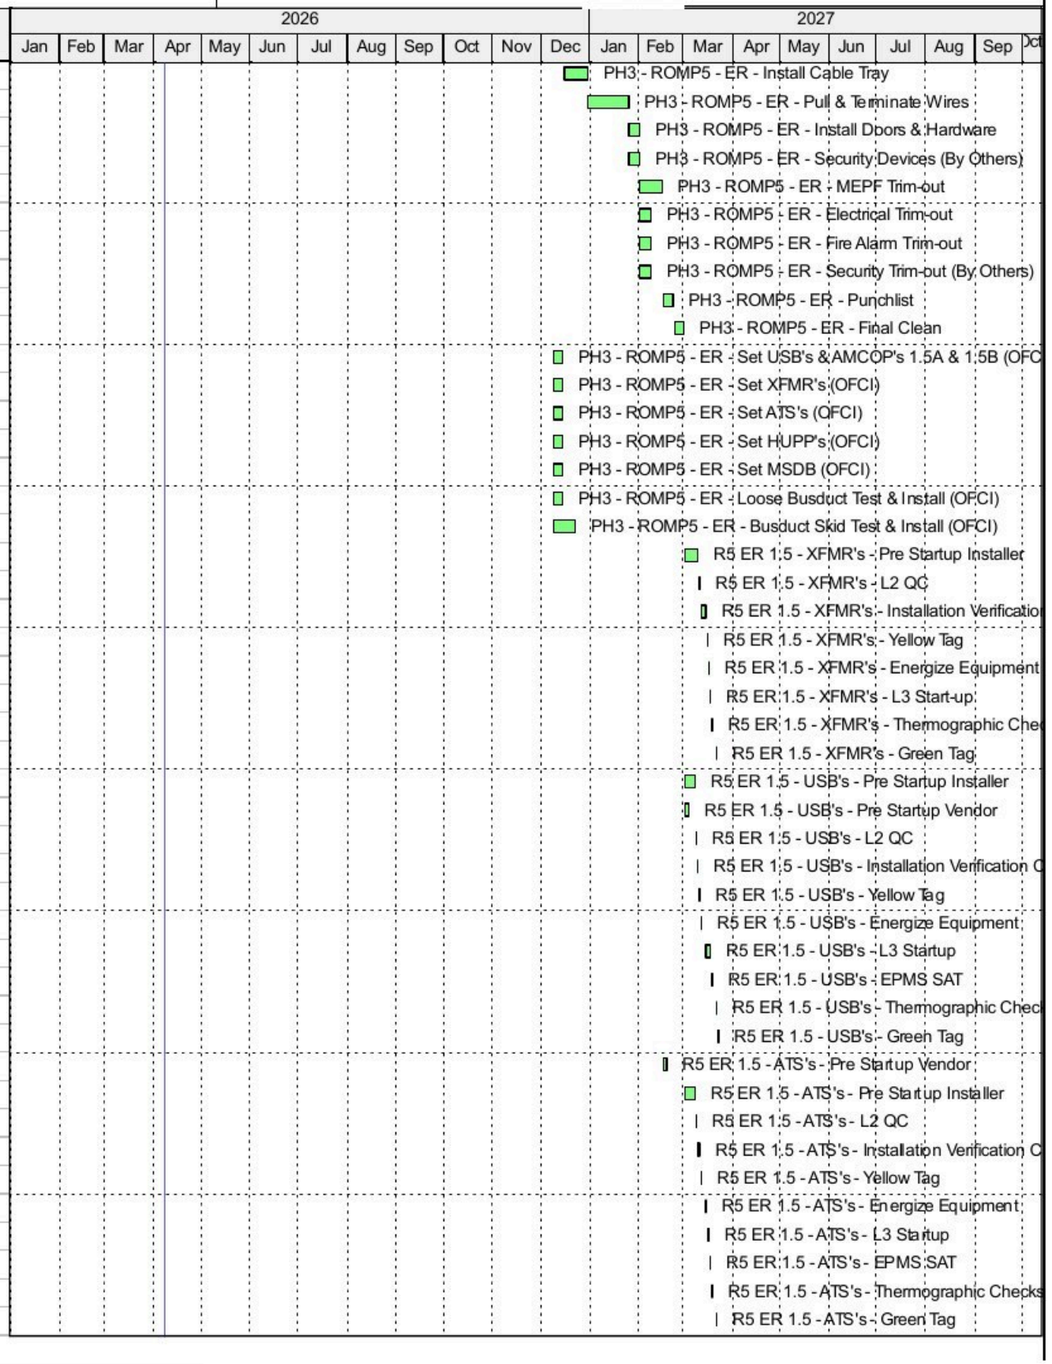


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH3.R5.ER1.5-MSDB.110	R5 ER 1.5 - MSDB's - Pre Startup Vendor	3	26-Jan-27	28-Jan-27		
Cx.PH3.R5.ER1.5-MSDB.100	R5 ER 1.5 - MSDB's - Pre Startup Installer	5	02-Mar-27	08-Mar-27		
Cx.PH3.R5.ER1.5-MSDB.120	R5 ER 1.5 - MSDB's - L2 QC	1	09-Mar-27	09-Mar-27		
Cx.PH3.R5.ER1.5-MSDB.130	R5 ER 1.5 - MSDB's - Installation Verification Checklist	2	10-Mar-27	11-Mar-27		
Cx.PH3.R5.ER1.5-MSDB.140	R5 ER 1.5 - MSDB's - Yellow Tag	1	12-Mar-27	12-Mar-27		
Cx.PH3.R5.ER1.5-MSDB.150	R5 ER 1.5 - MSDB's - Energize Equipment	1	15-Mar-27	15-Mar-27		
Cx.PH3.R5.ER1.5-MSDB.160	R5 ER 1.5 - MSDB's - L3 Startup	2	16-Mar-27	17-Mar-27		
Cx.PH3.R5.ER1.5-MSDB.170	R5 ER 1.5 - MSDB's - EPMS SAT	1	18-Mar-27	18-Mar-27		
Cx.PH3.R5.ER1.5-MSDB.180	R5 ER 1.5 - MSDB's - Thermographic Checks	1	19-Mar-27	19-Mar-27		
Cx.PH3.R5.ER1.5-MSDB.190	R5 ER 1.5 - MSDB's - Green Tag	1	22-Mar-27	22-Mar-27		
Cx.PH3.R5.ER1.5-AMCOP.100	R5 ER 1.5 - AMCOP's - Pre Startup Installer	5	02-Mar-27	08-Mar-27		
Cx.PH3.R5.ER1.5-AMCOP.110	R5 ER 1.5 - AMCOP's - Pre Startup Vendor	3	02-Mar-27	04-Mar-27		
Cx.PH3.R5.ER1.5-AMCOP.120	R5 ER 1.5 - AMCOP's - L2 QC	1	09-Mar-27	09-Mar-27		
Cx.PH3.R5.ER1.5-AMCOP.130	R5 ER 1.5 - AMCOP's - Installation Verfication Checklist	2	10-Mar-27	11-Mar-27		
Cx.PH3.R5.ER1.5-AMCOP.140	R5 ER 1.5 - AMCOP's - Yellow Tag	1	12-Mar-27	12-Mar-27		
Cx.PH3.R5.ER1.5-AMCOP.150	R5 ER 1.5 - AMCOP's - Energize Equipment	1	15-Mar-27	15-Mar-27		
Cx.PH3.R5.ER1.5-AMCOP.160	R5 ER 1.5 - AMCOP's - L3 Startup	2	16-Mar-27	17-Mar-27		
Cx.PH3.R5.ER1.5-AMCOP.170	R5 ER 1.5 - AMCOP's - EPMS SAT	1	18-Mar-27	18-Mar-27		
Cx.PH3.R5.ER1.5-AMCOP.180	R5 ER 1.5 - AMCOP's - Thermographic Checks	1	19-Mar-27	19-Mar-27		
Cx.PH3.R5.ER1.5-AMCOP.190	R5 ER 1.5 - AMCOP's - Green Tag	1	22-Mar-27	22-Mar-27		
Cx.PH3.R5.ER1.5-CRAC.110	R5 ER 1.5 - CRAC's - Pre Startup Vendor	3	08-Feb-27	10-Feb-27		
Cx.PH3.R5.ER1.5-CRAC.100	R5 ER 1.5 - CRAC's - Pre Startup Installer	5	02-Mar-27	08-Mar-27		
Cx.PH3.R5.ER1.5-CRAC.120	R5 ER 1.5 - CRAC's - L2 QC	1	09-Mar-27	09-Mar-27		
Cx.PH3.R5.ER1.5-CRAC.130	R5 ER 1.5 - CRAC's - Installation Verification Checklist	2	10-Mar-27	11-Mar-27		
Cx.PH3.R5.ER1.5-CRAC.140	R5 ER 1.5 - CRAC's - Yellow Tag	1	12-Mar-27	12-Mar-27		
Cx.PH3.R5.ER1.5-CRAC.150	R5 ER 1.5 - CRAC's - Energize Equipment	1	15-Mar-27	15-Mar-27		
Cx.PH3.R5.ER1.5-CRAC.160	R5 ER 1.5 - CRAC's - L3 Startup	1	16-Mar-27	16-Mar-27		
Cx.PH3.R5.ER1.5-CRAC.180	R5 ER 1.5 - CRAC's - BAS SAT	1	17-Mar-27	17-Mar-27		
Cx.PH3.R5.ER1.5-CRAC.170	R5 ER 1.5 - CRAC's - TAB	3	18-Mar-27	22-Mar-27		
Cx.PH3.R5.ER1.5-CRAC.190	R5 ER 1.5 - CRAC's - Green Tag	1	23-Mar-27	23-Mar-27		
Cx.PH3.R5.ER1.5-HPP.HLP.110	R5 ER 1.5 - HPP's & HLP's - Pre Startup Vendor	3	26-Jan-27	28-Jan-27		
Cx.PH3.R5.ER1.5-HPP.HLP.100	R5 ER 1.5 - HPP's & HLP's - Pre Startup Installer	5	02-Mar-27	08-Mar-27		
Cx.PH3.R5.ER1.5-HPP.HLP.120	R5 ER 1.5 - HPP's & HLP's - L2 QC	1	09-Mar-27	09-Mar-27		
Cx.PH3.R5.ER1.5-HPP.HLP.130	R5 ER 1.5 - HPP's & HLP's - Installation Verification Checklist	2	10-Mar-27	11-Mar-27		
Cx.PH3.R5.ER1.5-HPP.HLP.140	R5 ER 1.5 - HPP's & HLP's - Yellow Tag	1	12-Mar-27	12-Mar-27		
Cx.PH3.R5.ER1.5-HPP.HLP.150	R5 ER 1.5 - HPP's & HLP's - Energize Equipment	1	18-Mar-27	18-Mar-27		
Cx.PH3.R5.ER1.5-HPP.HLP.160	R5 ER 1.5 - HPP's & HLP's - L3 Startup	1	19-Mar-27	19-Mar-27		
Cx.PH3.R5.ER1.5-HPP.HLP.170	R5 ER 1.5 - HPP's & HLP's - EPMS SAT	1	22-Mar-27	22-Mar-27		
Cx.PH3.R5.ER1.5-HPP.HLP.180	R5 ER 1.5 - HPP's & HLP's - Thermographic Checks	1	23-Mar-27	23-Mar-27		
Cx.PH3.R5.ER1.5-HPP.HLP.190	R5 ER 1.5 - HPP's & HLP's - Green Tag	1	24-Mar-27	24-Mar-27		
Cx.PH3.R5.ER1.5-HUPP.110	R5 ER 1.5 - HUPP's - Pre Startup Vendor	3	26-Jan-27	28-Jan-27		
Cx.PH3.R5.ER1.5-HUPP.100	R5 ER 1.5 - HUPP's - Pre Startup Installer	5	02-Mar-27	08-Mar-27		
Cx.PH3.R5.ER1.5-HUPP.120	R5 ER 1.5 - HUPP's - L2 QC	1	09-Mar-27	09-Mar-27		
Cx.PH3.R5.ER1.5-HUPP.130	R5 ER 1.5 - HUPP's - Installation Verification Checklist	2	10-Mar-27	11-Mar-27		
Cx.PH3.R5.ER1.5-HUPP.140	R5 ER 1.5 - HUPP's - Yellow Tag	1	12-Mar-27	12-Mar-27		

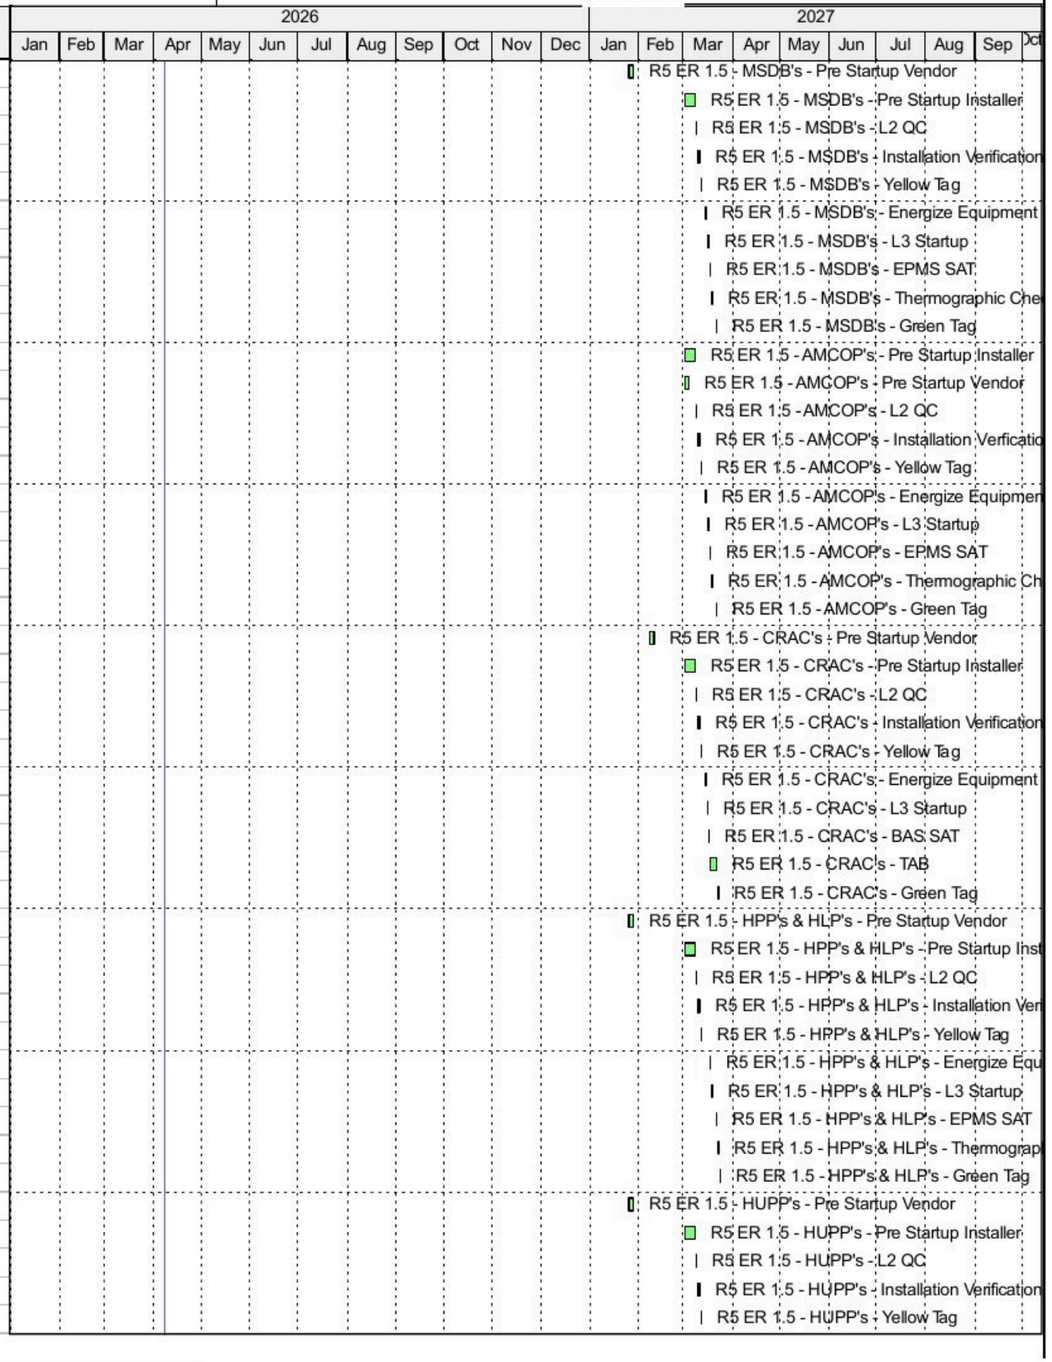


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH3.R5.ER1.5-HUPP.150	R5 ER 1.5 - HUPP's - Energize Equipment	1	15-Mar-27	15-Mar-27		
Cx.PH3.R5.ER1.5-HUPP.160	R5 ER 1.5 - HUPP's - L3 Startup	1	16-Mar-27	16-Mar-27		
Cx.PH3.R5.ER1.5-HUPP.170	R5 ER 1.5 - HUPP's - EPMS SAT	1	17-Mar-27	17-Mar-27		
Cx.PH3.R5.ER1.5-HUPP.180	R5 ER 1.5 - HUPP's - Thermographic Checks	1	18-Mar-27	18-Mar-27		
Cx.PH3.R5.ER1.5-HUPP.190	R5 ER 1.5 - HUPP's - Green Tag	1	19-Mar-27	19-Mar-27		
Cx.PH3.R5.ER1.5-GENAN.110	R5 ER 1.5 - GENAN's - Pre Startup Vendor	3	26-Jan-27	28-Jan-27		
Cx.PH3.R5.ER1.5-GENAN.100	R5 ER 1.5 - GENAN's - Pre Startup Installer	5	02-Mar-27	08-Mar-27		
Cx.PH3.R5.ER1.5-GENAN.120	R5 ER 1.5 - GENAN's - L2 QC	1	09-Mar-27	09-Mar-27		
Cx.PH3.R5.ER1.5-GENAN.130	R5 ER 1.5 - GENAN's - Installation Verification Checklist	2	10-Mar-27	11-Mar-27		
Cx.PH3.R5.ER1.5-GENAN.140	R5 ER 1.5 - GENAN's - Yellow Tag	1	12-Mar-27	12-Mar-27		
Cx.PH3.R5.ER1.5-GENAN.150	R5 ER 1.5 - GENAN's - Energize Equipment	1	15-Mar-27	15-Mar-27		
Cx.PH3.R5.ER1.5-GENAN.160	R5 ER 1.5 - GENAN's - L3 Startup	1	16-Mar-27	16-Mar-27		
Cx.PH3.R5.ER1.5-GENAN.170	R5 ER 1.5 - GENAN's - EPMS SAT	1	17-Mar-27	17-Mar-27		
Cx.PH3.R5.ER1.5-GENAN.180	R5 ER 1.5 - GENAN's - Thermographics	1	18-Mar-27	18-Mar-27		
Cx.PH3.R5.ER1.5-GENAN.190	R5 ER 1.5 - GENAN's - Green Tag	1	19-Mar-27	19-Mar-27		
PH3 - ROMP6 - Electrical Room 1.6		133	01-Oct-26	05-Apr-27		
PH3.R6.ER1.6-IB.1150	PH3 - ROMP6 - ER - Mechanical OH Rough-ins	4	08-Oct-26	13-Oct-26	Trade	Mechanical
PH3.R6.ER1.6-IB.1280	PH3 - ROMP6 - ER - Mechanical Trim-out	5	02-Feb-27	08-Feb-27	Trade	Mechanical
PH3.R6.ER1.6-350	PH3 - ROMP6 - ER - Set CRAC Units	5	02-Nov-26	06-Nov-26	Trade	HVAC
PH3.R6.ER1.6-IB.1060	PH3 - ROMP6 - ER - Layout & Frame Walls	5	01-Oct-26	07-Oct-26		
PH3.R6.ER1.6-IB.1160	PH3 - ROMP6 - ER - Fire Sprinkler OH Rough-ins	5	01-Oct-26	07-Oct-26		
PH3.R6.ER1.6-IB.1070	PH3 - ROMP6 - ER - One Side Drywall	5	08-Oct-26	14-Oct-26		
PH3.R6.ER1.6-IB.1080	PH3 - ROMP6 - ER - Plumbing In-Wall Rough-ins	2	08-Oct-26	09-Oct-26		
PH3.R6.ER1.6-IB.1090	PH3 - ROMP6 - ER - Electrical In-Wall Rough-ins	4	08-Oct-26	13-Oct-26		
PH3.R6.ER1.6-IB.1100	PH3 - ROMP6 - ER - Fire Alarm In-Wall Rough-ins	4	08-Oct-26	13-Oct-26		
PH3.R6.ER1.6-IB.1110	PH3 - ROMP6 - ER - Security/Telecom/LV In-Wall Rough-ins	4	08-Oct-26	13-Oct-26		
PH3.R6.ER1.6-IB.1330	PH3 - ROMP6 - ER - Hang Door Frames	5	08-Oct-26	14-Oct-26		
PH3.R6.ER1.6-IB.1120	PH3 - ROMP6 - ER - In-Wall Inspection	1	14-Oct-26	14-Oct-26		
PH3.R6.ER1.6-IB.1130	PH3 - ROMP6 - ER - Plumbing OH Rough-ins	4	14-Oct-26	19-Oct-26		
PH3.R6.ER1.6-IB.1140	PH3 - ROMP6 - ER - Electrical/Fire Alarm OH Rough-ins	15	14-Oct-26	03-Nov-26		
PH3.R6.ER1.6-IB.1145	PH3 - ROMP6 - ER - Security/Telecom/LV OH Rough-ins	15	14-Oct-26	03-Nov-26		
PH3.R6.ER1.6-IB.1170	PH3 - ROMP6 - ER - Hang, Tape, & Finish Drywall	10	15-Oct-26	28-Oct-26		
PH3.R6.ER1.6-IB.1190	PH3 - ROMP6 - ER - Prime Paint	5	26-Oct-26	30-Oct-26		
PH3.R6.ER1.6-IB.1180	PH3 - ROMP6 - ER - OH Inspection	1	04-Nov-26	04-Nov-26		
PH3.R6.ER1.6-IB.1220	PH3 - ROMP6 - ER - Install Cable Tray	10	16-Dec-26	30-Dec-26		
PH3.R6.ER1.6-IB.1230	PH3 - ROMP6 - ER - Pull & Terminate Wires	15	31-Dec-26	25-Jan-27		
PH3.R6.ER1.6-IB.1240	PH3 - ROMP6 - ER - Install Doors & Hardware	5	26-Jan-27	01-Feb-27		
PH3.R6.ER1.6-IB.1250	PH3 - ROMP6 - ER - Security Devices (By Others)	5	26-Jan-27	01-Feb-27		
PH3.R6.ER1.6-IB.1260	PH3 - ROMP6 - ER - MEPF Trim-out	10	02-Feb-27	15-Feb-27		
PH3.R6.ER1.6-IB.1270	PH3 - ROMP6 - ER - Electrical Trim-out	5	02-Feb-27	08-Feb-27		
PH3.R6.ER1.6-IB.1290	PH3 - ROMP6 - ER - Fire Alarm Trim-out	5	02-Feb-27	08-Feb-27		
PH3.R6.ER1.6-IB.1300	PH3 - ROMP6 - ER - Security Trim-out (By Others)	5	02-Feb-27	08-Feb-27		
PH3.R6.ER1.6-IB.1310	PH3 - ROMP6 - ER - Punchlist	5	16-Feb-27	22-Feb-27		
PH3.R6.ER1.6-IB.1320	PH3 - ROMP6 - ER - Final Clean	5	23-Feb-27	01-Mar-27		
PH3.R6.ER1.6-280	PH3 - ROMP6 - ER - Set USB's & AMCOP's 1.6A & 1.6B (OFCI)	5	09-Dec-26	15-Dec-26		

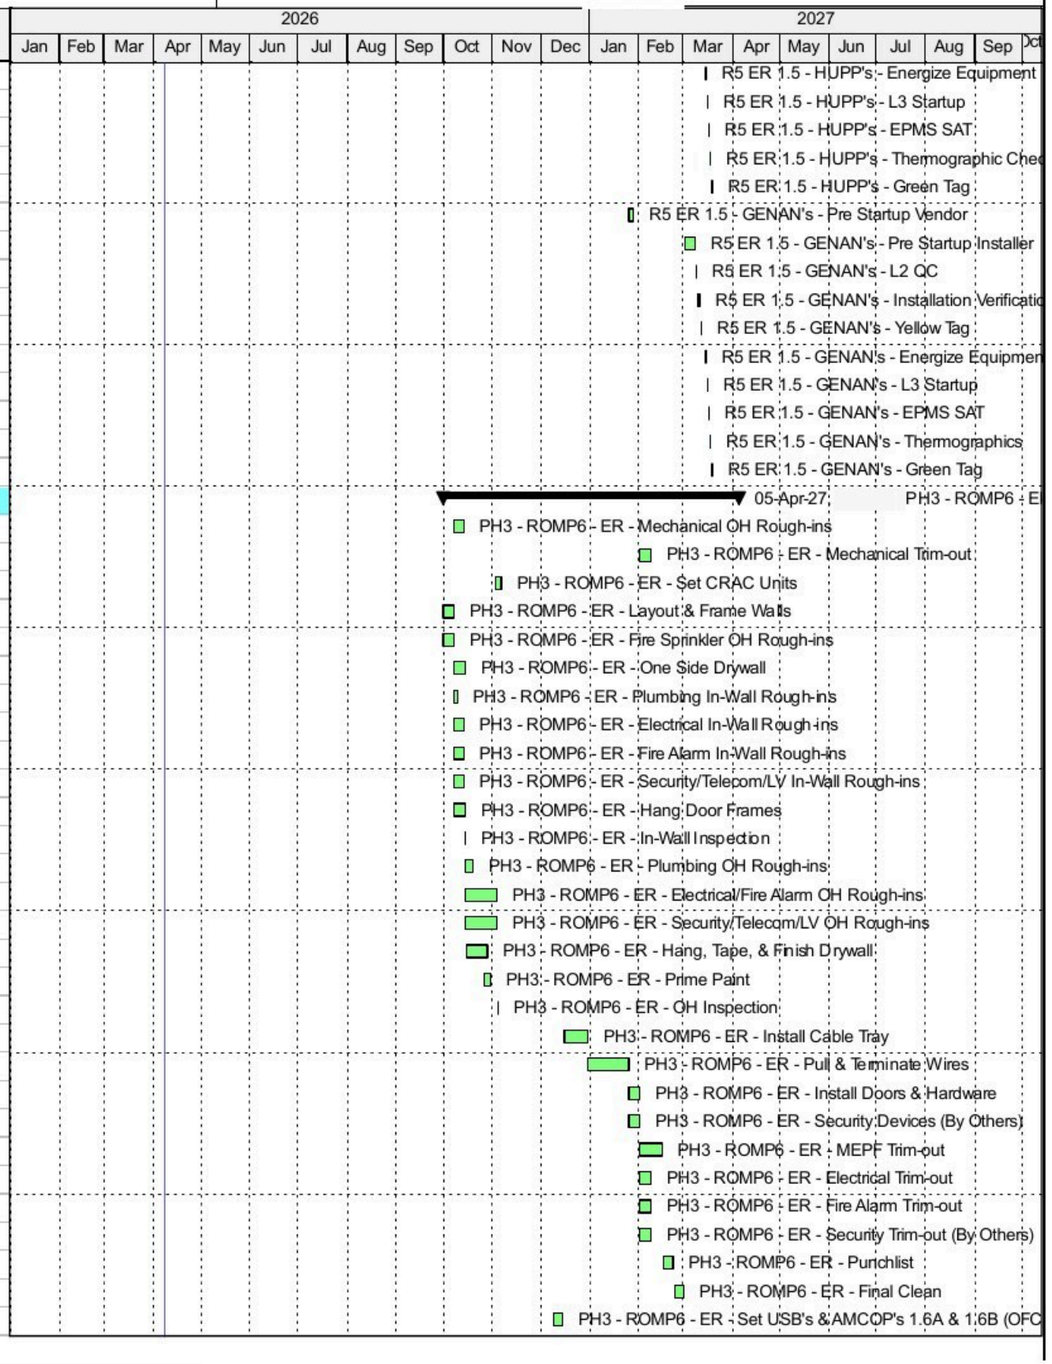


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule


Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH3.R6.ER1.6-290	PH3 - ROMP6 - ER - Set XFMR's (OFCI)	5	09-Dec-26	15-Dec-26		
PH3.R6.ER1.6-300	PH3 - ROMP6 - ER - Set ATS's (OFCI)	5	09-Dec-26	15-Dec-26		
PH3.R6.ER1.6-310	PH3 - ROMP6 - ER - Set HPP's, HLP's, HUPP's (OFCI)	5	09-Dec-26	15-Dec-26		
PH3.R6.ER1.6-320	PH3 - ROMP6 - ER - Set EVCPP (OFCI)	5	09-Dec-26	15-Dec-26		
PH3.R6.ER1.6-330	PH3 - ROMP6 - ER - Set MSDB (OFCI)	5	09-Dec-26	15-Dec-26		
PH3.R6.ER1.6-340	PH3 - ROMP6 - ER - Loose Busduct Test & Install (OFCI)	5	09-Dec-26	15-Dec-26		
PH3.R6.ER1.6-360	PH3 - ROMP6 - ER - Busduct Skid Test & Install (OFCI)	10	09-Dec-26	23-Dec-26		
Cx.PH3.R6.ER1.6-XFMR.190	R6 ER 1.6 - XFMR's - Pre Startup Installer	7	02-Mar-27	10-Mar-27		
Cx.PH3.R6.ER1.6-XFMR.100	R6 ER 1.6 - XFMR's - L2 QC	1	11-Mar-27	11-Mar-27		
Cx.PH3.R6.ER1.6-XFMR.110	R6 ER 1.6 - XFMR's - Installation Verification Checklist	2	12-Mar-27	15-Mar-27		
Cx.PH3.R6.ER1.6-XFMR.120	R6 ER 1.6 - XFMR's - Yellow Tag	1	16-Mar-27	16-Mar-27		
Cx.PH3.R6.ER1.6-XFMR.130	R6 ER 1.6 - XFMR's - Energize Equipment	1	17-Mar-27	17-Mar-27		
Cx.PH3.R6.ER1.6-XFMR.140	R6 ER 1.6 - XFMR's - L3 Start-up	1	18-Mar-27	18-Mar-27		
Cx.PH3.R6.ER1.6-XFMR.150	R6 ER 1.6 - XFMR's - Thermographic Checks	1	19-Mar-27	19-Mar-27		
Cx.PH3.R6.ER1.6-XFMR.160	R6 ER 1.6 - XFMR's - Green Tag	1	22-Mar-27	22-Mar-27		
Cx.PH3.R6.ER1.6-USB.110	R6 ER 1.6 - USB's - Pre Startup Vendor	3	26-Jan-27	28-Jan-27		
Cx.PH3.R6.ER1.6-USB.100	R6 ER 1.6 - USB's - Pre Startup Installer	5	02-Mar-27	08-Mar-27		
Cx.PH3.R6.ER1.6-USB.120	R6 ER 1.6 - USB's - L2 QC	1	09-Mar-27	09-Mar-27		
Cx.PH3.R6.ER1.6-USB.130	R6 ER 1.6 - USB's - Installation Verification Checklist	1	10-Mar-27	10-Mar-27		
Cx.PH3.R6.ER1.6-USB.140	R6 ER 1.6 - USB's - Yellow Tag	1	11-Mar-27	11-Mar-27		
Cx.PH3.R6.ER1.6-USB.150	R6 ER 1.6 - USB's - Energize Equipment	1	12-Mar-27	12-Mar-27		
Cx.PH3.R6.ER1.6-USB.160	R6 ER 1.6 - USB's - L3 Startup	4	15-Mar-27	18-Mar-27		
Cx.PH3.R6.ER1.6-USB.170	R6 ER 1.6 - USB's - EPMS SAT	1	19-Mar-27	19-Mar-27		
Cx.PH3.R6.ER1.6-USB.180	R6 ER 1.6 - USB's - Thermographic Checks	1	22-Mar-27	22-Mar-27		
Cx.PH3.R6.ER1.6-USB.190	R6 ER 1.6 - USB's - Green Tag	1	23-Mar-27	23-Mar-27		
Cx.PH3.R6.ER1.6-ATS.110	R6 ER 1.6 - ATS's - Pre Startup Vendor	3	16-Feb-27	18-Feb-27		
Cx.PH3.R6.ER1.6-ATS.100	R6 ER 1.6 - ATS's - Pre Startup Installer	5	02-Mar-27	08-Mar-27		
Cx.PH3.R6.ER1.6-ATS.120	R6 ER 1.6 - ATS's - L2 QC	1	09-Mar-27	09-Mar-27		
Cx.PH3.R6.ER1.6-ATS.130	R6 ER 1.6 - ATS's - Installation Verification Checklist	2	10-Mar-27	11-Mar-27		
Cx.PH3.R6.ER1.6-ATS.140	R6 ER 1.6 - ATS's - Yellow Tag	1	12-Mar-27	12-Mar-27		
Cx.PH3.R6.ER1.6-ATS.150	R6 ER 1.6 - ATS's - Energize Equipment	1	15-Mar-27	15-Mar-27		
Cx.PH3.R6.ER1.6-ATS.160	R6 ER 1.6 - ATS's - L3 Startup	2	16-Mar-27	17-Mar-27		
Cx.PH3.R6.ER1.6-ATS.170	R6 ER 1.6 - ATS's - EPMS SAT	1	18-Mar-27	18-Mar-27		
Cx.PH3.R6.ER1.6-ATS.180	R6 ER 1.6 - ATS's - Thermographic Checks	1	19-Mar-27	19-Mar-27		
Cx.PH3.R6.ER1.6-ATS.190	R6 ER 1.6 - ATS's - Green Tag	1	22-Mar-27	22-Mar-27		
Cx.PH3.R6.ER1.6-MSDB.110	R6 ER 1.6 - MSDB's - Pre Startup Vendor	3	26-Jan-27	28-Jan-27		
Cx.PH3.R6.ER1.6-MSDB.100	R6 ER 1.6 - MSDB's - Pre Startup Installer	5	02-Mar-27	08-Mar-27		
Cx.PH3.R6.ER1.6-MSDB.120	R6 ER 1.6 - MSDB's - L2 QC	1	09-Mar-27	09-Mar-27		
Cx.PH3.R6.ER1.6-MSDB.130	R6 ER 1.6 - MSDB's - Installation Verification Checklist	2	10-Mar-27	11-Mar-27		
Cx.PH3.R6.ER1.6-MSDB.140	R6 ER 1.6 - MSDB's - Yellow Tag	1	12-Mar-27	12-Mar-27		
Cx.PH3.R6.ER1.6-MSDB.150	R6 ER 1.6 - MSDB's - Energize Equipment	1	29-Mar-27	29-Mar-27		
Cx.PH3.R6.ER1.6-MSDB.160	R6 ER 1.6 - MSDB's - L3 Startup	2	30-Mar-27	31-Mar-27		
Cx.PH3.R6.ER1.6-MSDB.170	R6 ER 1.6 - MSDB's - EPMS SAT	1	01-Apr-27	01-Apr-27		
Cx.PH3.R6.ER1.6-MSDB.180	R6 ER 1.6 - MSDB's - Thermographic Checks	1	02-Apr-27	02-Apr-27		
Cx.PH3.R6.ER1.6-MSDB.190	R6 ER 1.6 - MSDB's - Green Tag	1	05-Apr-27	05-Apr-27		

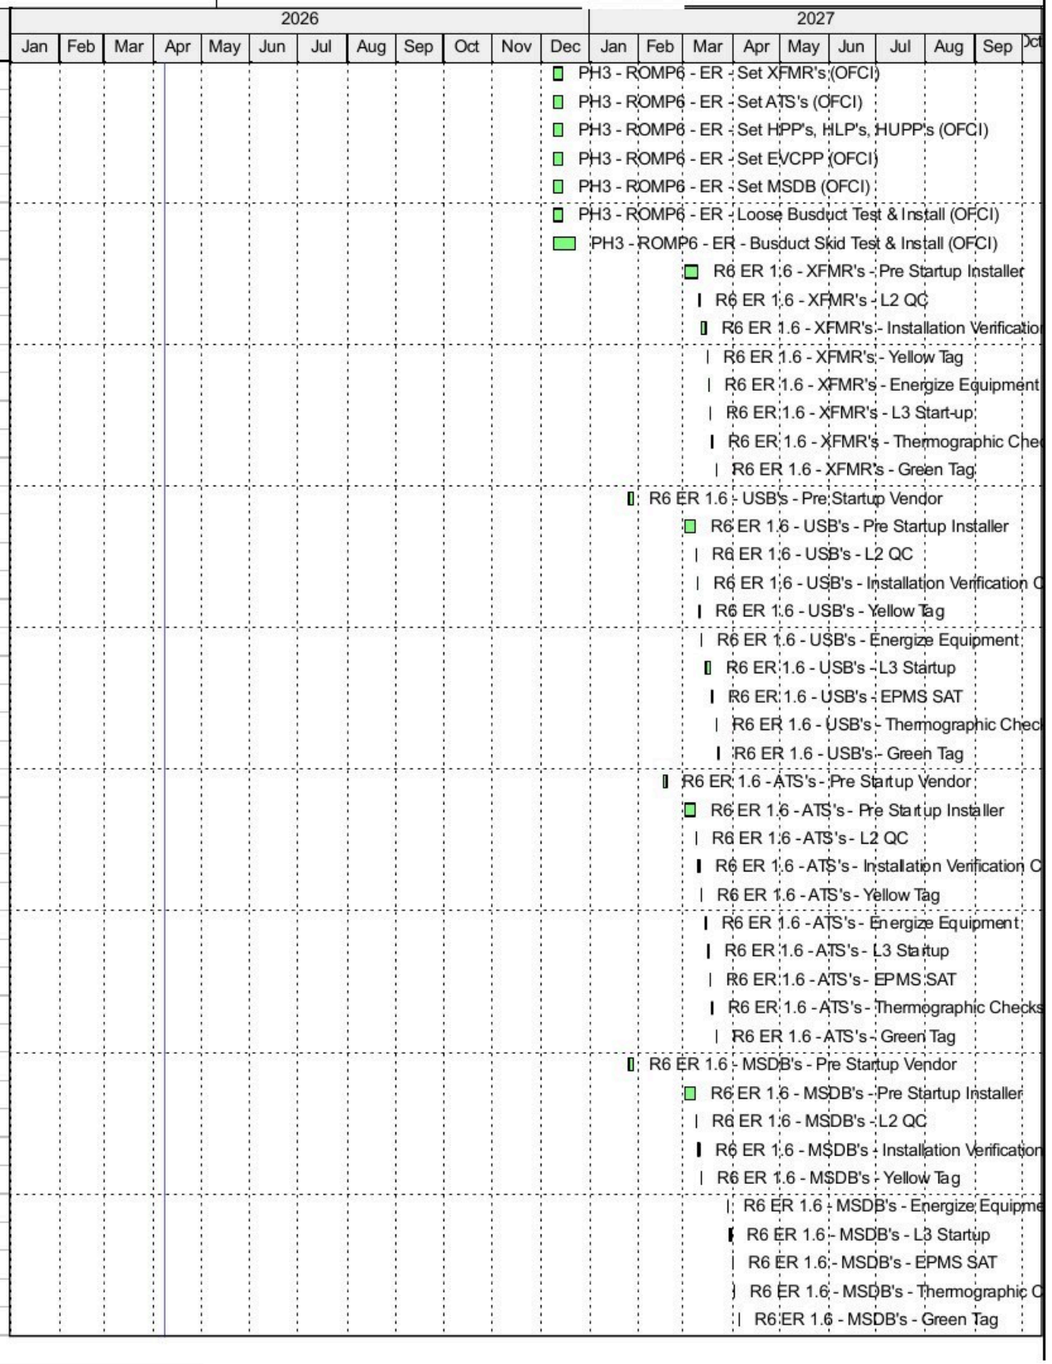

Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH3.R6.ER1.6-AMCOP.110	R6 ER 1.6 - AMCOP's - Pre Startup Vendor	3	26-Jan-27	28-Jan-27		
Cx.PH3.R6.ER1.6-AMCOP.100	R6 ER 1.6 - AMCOP's - Pre Startup Installer	5	02-Mar-27	08-Mar-27		
Cx.PH3.R6.ER1.6-AMCOP.120	R6 ER 1.6 - AMCOP's - L2 QC	1	09-Mar-27	09-Mar-27		
Cx.PH3.R6.ER1.6-AMCOP.130	R6 ER 1.6 - AMCOP's - Installation Verfication Checklist	2	10-Mar-27	11-Mar-27		
Cx.PH3.R6.ER1.6-AMCOP.140	R6 ER 1.6 - AMCOP's - Yellow Tag	1	12-Mar-27	12-Mar-27		
Cx.PH3.R6.ER1.6-AMCOP.150	R6 ER 1.6 - AMCOP's - Energize Equipment	1	15-Mar-27	15-Mar-27		
Cx.PH3.R6.ER1.6-AMCOP.160	R6 ER 1.6 - AMCOP's - L3 Startup	2	16-Mar-27	17-Mar-27		
Cx.PH3.R6.ER1.6-AMCOP.170	R6 ER 1.6 - AMCOP's - EPMS SAT	1	18-Mar-27	18-Mar-27		
Cx.PH3.R6.ER1.6-AMCOP.180	R6 ER 1.6 - AMCOP's - Thermographic Checks	1	19-Mar-27	19-Mar-27		
Cx.PH3.R6.ER1.6-AMCOP.190	R6 ER 1.6 - AMCOP's - Green Tag	1	22-Mar-27	22-Mar-27		
Cx.PH3.R6.ER1.6-CRAC.110	R6 ER 1.6 - CRAC's - Pre Startup Vendor	3	08-Feb-27	10-Feb-27		
Cx.PH3.R6.ER1.6-CRAC.100	R6 ER 1.6 - CRAC's - Pre Startup Installer	5	02-Mar-27	08-Mar-27		
Cx.PH3.R6.ER1.6-CRAC.120	R6 ER 1.6 - CRAC's - L2 QC	1	09-Mar-27	09-Mar-27		
Cx.PH3.R6.ER1.6-CRAC.130	R6 ER 1.6 - CRAC's - Installation Verification Checklist	2	10-Mar-27	11-Mar-27		
Cx.PH3.R6.ER1.6-CRAC.140	R6 ER 1.6 - CRAC's - Yellow Tag	1	12-Mar-27	12-Mar-27		
Cx.PH3.R6.ER1.6-CRAC.150	R6 ER 1.6 - CRAC's - Energize Equipment	1	15-Mar-27	15-Mar-27		
Cx.PH3.R6.ER1.6-CRAC.160	R6 ER 1.6 - CRAC's - L3 Startup	1	16-Mar-27	16-Mar-27		
Cx.PH3.R6.ER1.6-CRAC.180	R6 ER 1.6 - CRAC's - BAS SAT	1	17-Mar-27	17-Mar-27		
Cx.PH3.R6.ER1.6-CRAC.170	R6 ER 1.6 - CRAC's - TAB	3	18-Mar-27	22-Mar-27		
Cx.PH3.R6.ER1.6-CRAC.190	R6 ER 1.6 - CRAC's - Green Tag	1	23-Mar-27	23-Mar-27		
Cx.PH3.R6.ER1.6-HPP.HLP.110	R6 ER 1.6 - HPP's & HLP's - Pre Startup Vendor	3	26-Jan-27	28-Jan-27		
Cx.PH3.R6.ER1.6-HPP.HLP.100	R6 ER 1.6 - HPP's & HLP's - Pre Startup Installer	5	02-Mar-27	08-Mar-27		
Cx.PH3.R6.ER1.6-HPP.HLP.120	R6 ER 1.6 - HPP's & HLP's - L2 QC	1	09-Mar-27	09-Mar-27		
Cx.PH3.R6.ER1.6-HPP.HLP.130	R6 ER 1.6 - HPP's & HLP's - Installation Verification Checklist	2	10-Mar-27	11-Mar-27		
Cx.PH3.R6.ER1.6-HPP.HLP.140	R6 ER 1.6 - HPP's & HLP's - Yellow Tag	1	12-Mar-27	12-Mar-27		
Cx.PH3.R6.ER1.6-HPP.HLP.150	R6 ER 1.6 - HPP's & HLP's - Energize Equipment	1	18-Mar-27	18-Mar-27		
Cx.PH3.R6.ER1.6-HPP.HLP.160	R6 ER 1.6 - HPP's & HLP's - L3 Startup	1	19-Mar-27	19-Mar-27		
Cx.PH3.R6.ER1.6-HPP.HLP.170	R6 ER 1.6 - HPP's & HLP's - EPMS SAT	1	22-Mar-27	22-Mar-27		
Cx.PH3.R6.ER1.6-HPP.HLP.180	R6 ER 1.6 - HPP's & HLP's - Thermographic Checks	1	23-Mar-27	23-Mar-27		
Cx.PH3.R6.ER1.6-HPP.HLP.190	R6 ER 1.6 - HPP's & HLP's - Green Tag	1	24-Mar-27	24-Mar-27		
Cx.PH3.R6.ER1.6-HUPP.110	R6 ER 1.6 - HUPP's - Pre Startup Vendor	3	26-Jan-27	28-Jan-27		
Cx.PH3.R6.ER1.6-HUPP.100	R6 ER 1.6 - HUPP's - Pre Startup Installer	5	02-Mar-27	08-Mar-27		
Cx.PH3.R6.ER1.6-HUPP.120	R6 ER 1.6 - HUPP's - L2 QC	1	09-Mar-27	09-Mar-27		
Cx.PH3.R6.ER1.6-HUPP.130	R6 ER 1.6 - HUPP's - Installation Verification Checklist	2	10-Mar-27	11-Mar-27		
Cx.PH3.R6.ER1.6-HUPP.140	R6 ER 1.6 - HUPP's - Yellow Tag	1	12-Mar-27	12-Mar-27		
Cx.PH3.R6.ER1.6-HUPP.150	R6 ER 1.6 - HUPP's - Energize Equipment	1	15-Mar-27	15-Mar-27		
Cx.PH3.R6.ER1.6-HUPP.160	R6 ER 1.6 - HUPP's - L3 Startup	1	16-Mar-27	16-Mar-27		
Cx.PH3.R6.ER1.6-HUPP.170	R6 ER 1.6 - HUPP's - EPMS SAT	1	17-Mar-27	17-Mar-27		
Cx.PH3.R6.ER1.6-HUPP.180	R6 ER 1.6 - HUPP's - Thermographic Checks	1	18-Mar-27	18-Mar-27		
Cx.PH3.R6.ER1.6-HUPP.190	R6 ER 1.6 - HUPP's - Green Tag	1	19-Mar-27	19-Mar-27		
Cx.PH3.R6.ER1.6-GENAN.110	R6 ER 1.6 - GENAN's - Pre Startup Vendor	3	26-Jan-27	28-Jan-27		
Cx.PH3.R6.ER1.6-GENAN.100	R6 ER 1.6 - GENAN's - Pre Startup Installer	5	02-Mar-27	08-Mar-27		
Cx.PH3.R6.ER1.6-GENAN.120	R6 ER 1.6 - GENAN's - L2 QC	1	09-Mar-27	09-Mar-27		
Cx.PH3.R6.ER1.6-GENAN.130	R6 ER 1.6 - GENAN's - Installation Verification Checklist	2	10-Mar-27	11-Mar-27		
Cx.PH3.R6.ER1.6-GENAN.140	R6 ER 1.6 - GENAN's - Yellow Tag	1	12-Mar-27	12-Mar-27		

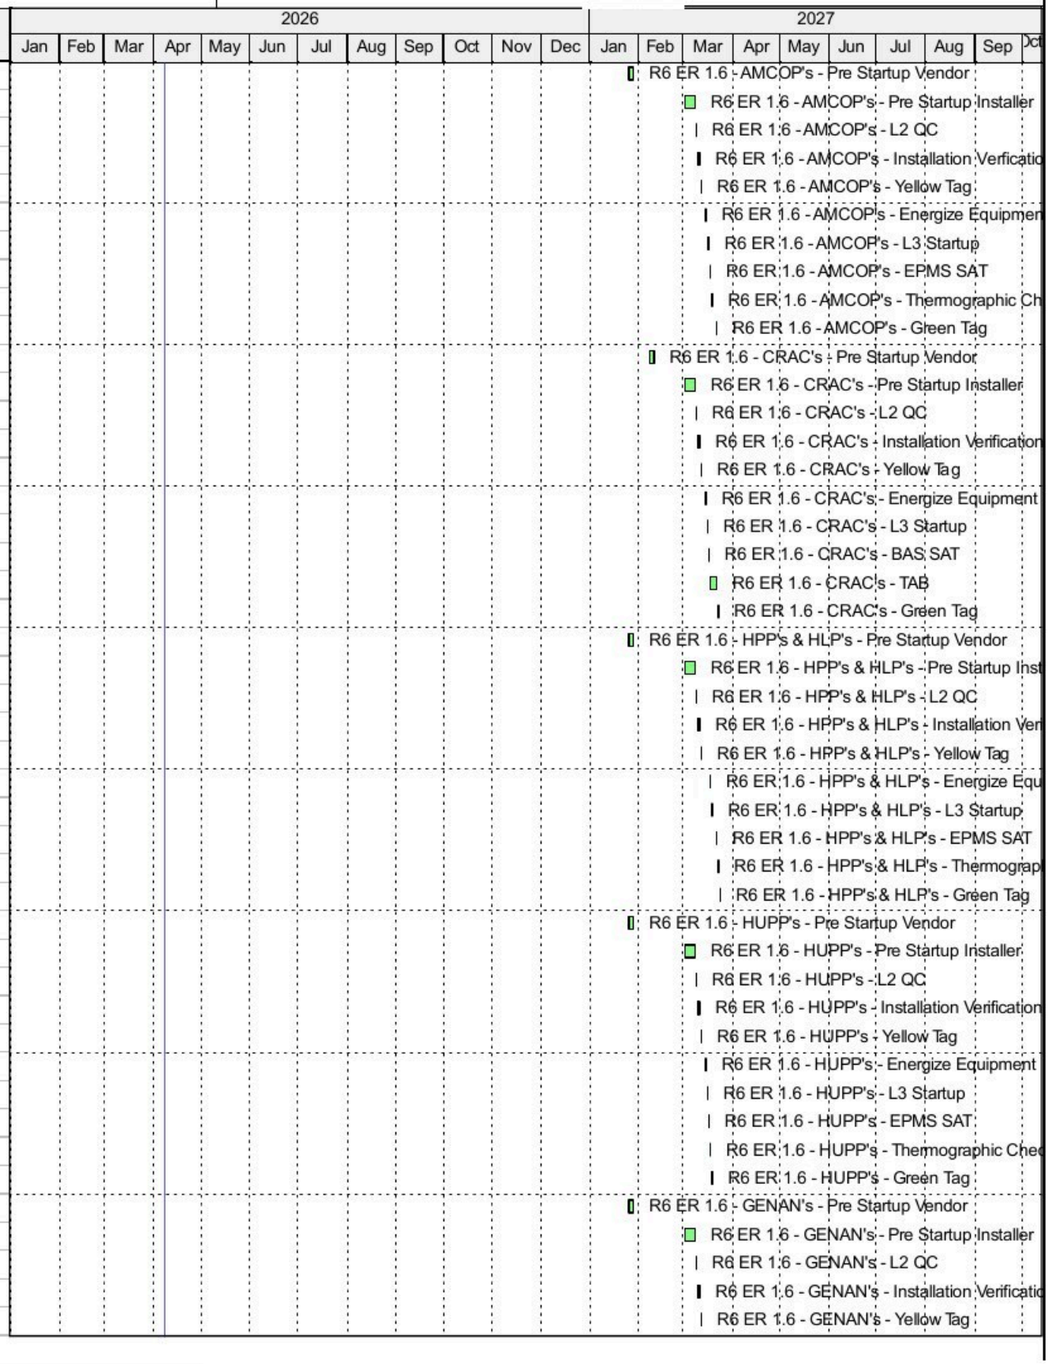


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH3.R6.ER1.6-GENAN.150	R6 ER 1.6 - GENAN's - Energize Equipment	1	15-Mar-27	15-Mar-27		
Cx.PH3.R6.ER1.6-GENAN.160	R6 ER 1.6 - GENAN's - L3 Startup	1	16-Mar-27	16-Mar-27		
Cx.PH3.R6.ER1.6-GENAN.170	R6 ER 1.6 - GENAN's - EPMS SAT	1	17-Mar-27	17-Mar-27		
Cx.PH3.R6.ER1.6-GENAN.180	R6 ER 1.6 - GENAN's - Thermographics	1	18-Mar-27	18-Mar-27		
Cx.PH3.R6.ER1.6-GENAN.190	R6 ER 1.6 - GENAN's - Green Tag	1	19-Mar-27	19-Mar-27		
PH3 - Data Hall - ROMP's 5 & 6		174	22-Sep-26	21-May-27		
PH3.TAHU1.3-IB.630	PH3 - R5&6 - TAHU Gallery - Mechanical OH Rough-ins (High)	5	21-Oct-26	27-Oct-26	Trade	Mechanical
PH3.TAHU1.3-IB.660	PH3 - R5&6 - TAHU Gallery - Mechanical Trim-out	5	15-Mar-27	19-Mar-27	Trade	Mechanical
PH3.TAHU1.3-IB.700	PH3 - R5&6 - TAHU Gallery - Gallery Wall Interior IMP Install	5	22-Sep-26	29-Sep-26		
PH3.TAHU1.3-IB.710	PH3 - R5&6 - TAHU Gallery - Gallery Wall Duct Install	5	01-Oct-26	07-Oct-26		
PH3.TAHU1.3-IB.640	PH3 - R5&6 - TAHU Gallery - Fire Sprinkler OH Rough-ins (High)	10	07-Oct-26	20-Oct-26		
PH3.TAHU1.3-IB.720	PH3 - R5&6 - TAHU Gallery - Gallery Wall Security Mesh Install	5	08-Oct-26	14-Oct-26		
PH3.TAHU1.3-IB.770	PH3 - R5&6 - TAHU Gallery - IW OH Rough-ins (High)	10	14-Oct-26	27-Oct-26		
PH3.TAHU1.3-IB.620	PH3 - R5&6 - TAHU Gallery - Electrical/Fire Alarm OH Rough-ins (Hig	10	21-Oct-26	03-Nov-26		
PH3.TAHU1.3-IB.730	PH3 - R5&6 - TAHU Gallery - Security/Controls OH Rough-ins (High)	10	23-Oct-26	05-Nov-26		
PH3.TAHU1.3-IB.460	PH3 - R5&6 - TAHU Gallery - Install Cable Tray	5	04-Jan-27	08-Jan-27		
PH3.TAHU1.3-IB.500	PH3 - R5&6 - TAHU Gallery - MEPF TAHU Connections	10	04-Jan-27	19-Jan-27		
PH3.TAHU1.3-IB.520	PH3 - R5&6 - TAHU Gallery - OH Inspections	1	21-Jan-27	21-Jan-27		
PH3.TAHU1.3-IB.750	PH3 - R5&6 - TAHU Gallery - Electrical/Fire Alarm OH Rough-ins (Lo	10	25-Jan-27	05-Feb-27		
PH3.TAHU1.3-IB.760	PH3 - R5&6 - TAHU Gallery - Security/Controls OH Rough-ins (Low)	10	25-Jan-27	05-Feb-27		
PH3.TAHU1.3-IB.470	PH3 - R5&6 - TAHU Gallery - Pull & Terminate Wires	15	22-Feb-27	12-Mar-27		
PH3.TAHU1.3-IB.650	PH3 - R5&6 - TAHU Gallery - Electrical Trim-out	5	15-Mar-27	19-Mar-27		
PH3.TAHU1.3-IB.670	PH3 - R5&6 - TAHU Gallery - Fire Alarm Trim-out	5	15-Mar-27	19-Mar-27		
PH3.TAHU1.3-IB.550	PH3 - R5&6 - TAHU Gallery - Punchlist	15	19-Apr-27	07-May-27		
PH3.TAHU1.3-IB.560	PH3 - R5&6 - TAHU Gallery - Final Clean	10	10-May-27	21-May-27		
PH3 - ROMP 5 - Data Hall		147	08-Oct-26	30-Apr-27		
PH3.R5.DH1.3-IB.1270	PH3 - ROMP5 - DH - Mechanical OH Rough-ins	4	15-Oct-26	20-Oct-26	Trade	Mechanical
PH3.R5.DH1.3-IB.1300	PH3 - ROMP5 - DH - Mechanical Trim-out	5	29-Mar-27	02-Apr-27	Trade	Mechanical
PH3.R5.DH1.3-IB.930	PH3 - ROMP5 - DH - CE#0007 - Install Liquid Cooling Systems (CFI	6	08-Mar-27	15-Mar-27	Trade	CFN/SFN Pipir
PH3.R5.DH1.3-IB.1330	PH3 - ROMP5 - DH - Install Liquid Cooling Systems (SFN) (OFCI)	4	08-Mar-27	11-Mar-27	Trade	CFN/SFN Pipir
PH3.R5.DH1.3-IB.790	PH3 - ROMP5 - DH - Layout & Frame Walls	5	08-Oct-26	14-Oct-26		
PH3.R5.DH1.3-IB.1280	PH3 - ROMP5 - DH - Fire Sprinkler OH Rough-ins	5	08-Oct-26	14-Oct-26		
PH3.R5.DH1.3-IB.960	PH3 - ROMP5 - DH - One-side Drywall	5	15-Oct-26	21-Oct-26		
PH3.R5.DH1.3-IB.1210	PH3 - ROMP5 - DH - Plumbing In-Wall Rough-ins	2	15-Oct-26	16-Oct-26		
PH3.R5.DH1.3-IB.1220	PH3 - ROMP5 - DH - Electrical In-Wall Rough-ins	4	15-Oct-26	20-Oct-26		
PH3.R5.DH1.3-IB.1230	PH3 - ROMP5 - DH - Fire Alarm In-Wall Rough-ins	4	15-Oct-26	20-Oct-26		
PH3.R5.DH1.3-IB.1240	PH3 - ROMP5 - DH - Security/Telecom/LV In-Wall Rough-ins	4	15-Oct-26	20-Oct-26		
PH3.R5.DH1.3-IB.1340	PH3 - ROMP5 - DH - Hang Door Frames	5	15-Oct-26	21-Oct-26		
PH3.R5.DH1.3-IB.940	PH3 - ROMP5 - DH - In-Wall Inspections	1	21-Oct-26	21-Oct-26		
PH3.R5.DH1.3-IB.1250	PH3 - ROMP5 - DH - Plumbing OH Rough-ins	4	21-Oct-26	26-Oct-26		
PH3.R5.DH1.3-IB.1260	PH3 - ROMP5 - DH - Electrical/Fire Alarm OH Rough-ins	15	21-Oct-26	10-Nov-26		
PH3.R5.DH1.3-IB.1265	PH3 - ROMP5 - DH - Security/Telecom/LV OH Rough-ins	15	21-Oct-26	10-Nov-26		
PH3.R5.DH1.3-IB.810	PH3 - ROMP5 - DH - Hang, Tape, & Finish Drywall	10	22-Oct-26	04-Nov-26		
PH3.R5.DH1.3-IB.820	PH3 - ROMP5 - DH - Prime Paint	5	02-Nov-26	06-Nov-26		
PH3.R5.DH1.3-IB.950	PH3 - ROMP5 - DH - OH Inspections	1	11-Nov-26	11-Nov-26		

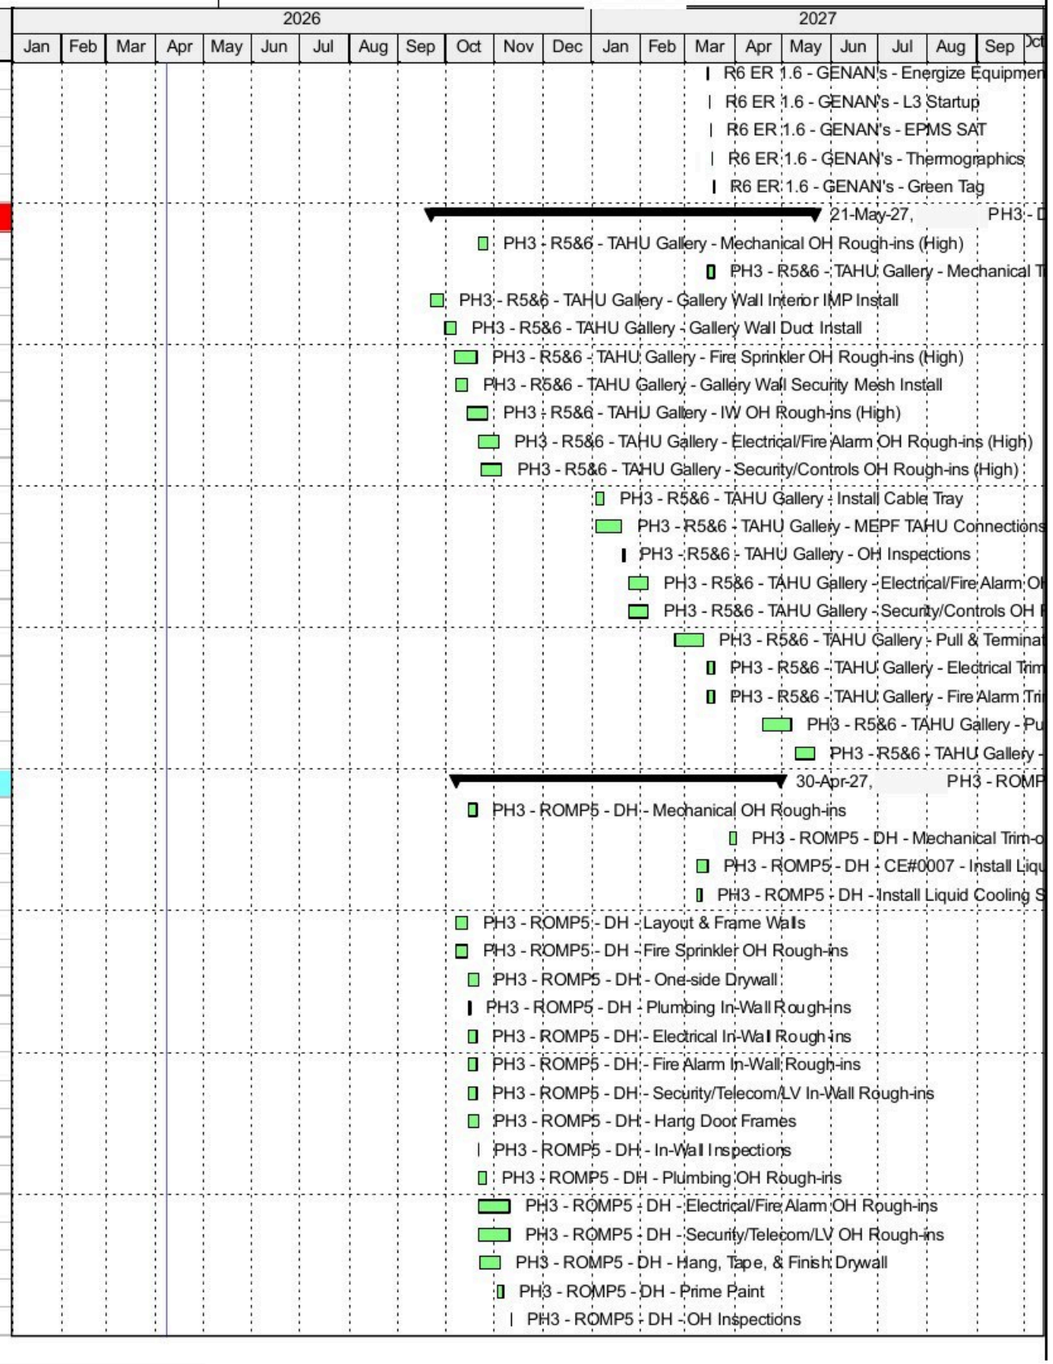


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE | CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH3.R5.DH1.3-IB.840	PH3 - ROMP5 - DH - Ceiling System	5	12-Nov-26	18-Nov-26		
PH3.R5.DH1.3-IB.870	PH3 - ROMP5 - DH - Install Cable Tray	10	08-Feb-27	19-Feb-27		
PH3.R5.DH1.3-IB.860	PH3 - ROMP5 - DH - Pull & Terminate Wires	15	22-Feb-27	12-Mar-27		
PH3.R5.DH1.3-IB.910	PH3 - ROMP5 - DH - Install Rack Whips (OFCI)	5	22-Feb-27	26-Feb-27		
PH3.R5.DH1.3-IB.920	PH3 - ROMP5 - DH - Temporary Barrier Wall	5	22-Feb-27	26-Feb-27		
PH3.R5.DH1.3-IB.880	PH3 - ROMP5 - DH - Install Doors & Hardware	5	15-Mar-27	19-Mar-27		
PH3.R5.DH1.3-IB.970	PH3 - ROMP5 - DH - Install Security Devices (By Others)	5	15-Mar-27	19-Mar-27		
PH3.R5.DH1.3-IB.980	PH3 - ROMP5 - DH - CE#0007 - Flush and Fill Liquid	10	16-Mar-27	29-Mar-27		
PH3.R5.DH1.3-IB.850	PH3 - ROMP5 - DH - MEPF Trim-out	5	22-Mar-27	26-Mar-27		
PH3.R5.DH1.3-IB.1290	PH3 - ROMP5 - DH - Electrical Trim-out	5	22-Mar-27	26-Mar-27		
PH3.R5.DH1.3-IB.1310	PH3 - ROMP5 - DH - Fire Alarm Trim-out	5	05-Apr-27	09-Apr-27		
PH3.R5.DH1.3-IB.1320	PH3 - ROMP5 - DH - Security Trim-out (By Others)	5	12-Apr-27	16-Apr-27		
PH3.R5.DH1.3-IB.1170	PH3 - ROMP5 - DH - Punchlist	5	19-Apr-27	23-Apr-27		
PH3.R5.DH1.3-IB.1180	PH3 - ROMP5 - DH - Final Clean	5	26-Apr-27	30-Apr-27		
PH3 - ROMP 5 - Data Hall Equipment		79	24-Nov-26	12-Mar-27		
PH3.R5.DH1.3-IB.180	PH3 - ROMP5 - DH - Set MTS-IRHX (OFCI)	5	09-Dec-26	15-Dec-26	Trade	HVAC
PH3.R5.DH1.3-IB.170	PH3 - ROMP5 - DH - Set IRHX's (OFCI)	5	08-Mar-27	12-Mar-27	Trade	HVAC
PH3.R5.DH1.3-IB.890	PH3 - ROMP5 - DH - Install HAC's	10	24-Nov-26	07-Dec-26		
PH3.R5.DH1.3-IB.900	PH3 - ROMP5 - DH - Install Racks (OFCI)	10	08-Feb-27	19-Feb-27		
PH3.R5.DH1.3-IB.160	PH3 - ROMP5 - DH - Set PDC's (OFCI)	5	10-Feb-27	16-Feb-27		
PH3 - ROMP 5 - Data Hall Commissioning		25	15-Mar-27	16-Apr-27		
PH3 - ROMP5 - DH - PDC-1.5A-01-05, PDC-1.5B-01-05, PDC-1.6A-01-05, PDC-1.6B-01-05 Cx		25	15-Mar-27	16-Apr-27		
Cx.PH3.R5.DH1.3-PDC.100	R5 DH1.3 - PDC's - Pre Startup Installer	5	15-Mar-27	19-Mar-27		
Cx.PH3.R5.DH1.3-PDC.110	R5 DH1.3 - PDC's - Pre Startup Vendor	5	15-Mar-27	19-Mar-27		
Cx.PH3.R5.DH1.3-PDC.120	R5 DH1.3 - PDC's - L2 QC	1	22-Mar-27	22-Mar-27		
Cx.PH3.R5.DH1.3-PDC.130	R5 DH1.3 - PDC's - Installation Verification Checklist	1	23-Mar-27	23-Mar-27		
Cx.PH3.R5.DH1.3-PDC.140	R5 DH1.3 - PDC's - Yellow Tag	1	24-Mar-27	24-Mar-27		
Cx.PH3.R5.DH1.3-PDC.150	R5 DH1.3 - PDC's - Energize Equipment	1	25-Mar-27	25-Mar-27		
Cx.PH3.R5.DH1.3-PDC.160	R5 DH1.3 - PDC's - L3 Startup	2	26-Mar-27	29-Mar-27		
Cx.PH3.R5.DH1.3-PDC.170	R5 DH1.3 - PDC's - EPMS SAT	1	30-Mar-27	30-Mar-27		
Cx.PH3.R5.DH1.3-PDC.180	R5 DH1.3 - PDC's - Thermographic Checks	1	31-Mar-27	31-Mar-27		
Cx.PH3.R5.DH1.3-PDC.190	R5 DH1.3 - PDC's - Green Tag	1	01-Apr-27	01-Apr-27		
Cx.PH3.R5.DH1.3-IRHX.100	R5 DH1.3 - IRHX's - Pre Startup Installer	5	30-Mar-27	05-Apr-27		
Cx.PH3.R5.DH1.3-IRHX.110	R5 DH1.3 - IRHX's - Pre Startup Vendor	3	30-Mar-27	01-Apr-27		
Cx.PH3.R5.DH1.3-IRHX.120	R5 DH1.3 - IRHX's - L2 QC	1	06-Apr-27	06-Apr-27		
Cx.PH3.R5.DH1.3-IRHX.130	R5 DH1.3 - IRHX's - Installation Verification Checklist	1	07-Apr-27	07-Apr-27		
Cx.PH3.R5.DH1.3-IRHX.140	R5 DH1.3 - IRHX's - Yellow Tag	1	08-Apr-27	08-Apr-27		
Cx.PH3.R5.DH1.3-IRHX.150	R5 DH1.3 - IRHX's - Energize Equipment	1	09-Apr-27	09-Apr-27		
Cx.PH3.R5.DH1.3-IRHX.160	R5 DH1.3 - IRHX's - L3 Startup	2	12-Apr-27	13-Apr-27		
Cx.PH3.R5.DH1.3-IRHX.170	R5 DH1.3 - IRHX's - EPMS SAT	1	14-Apr-27	14-Apr-27		
Cx.PH3.R5.DH1.3-IRHX.180	R5 DH1.3 - IRHX's - Thermographic Checks	1	15-Apr-27	15-Apr-27		
Cx.PH3.R5.DH1.3-IRHX.190	R5 DH1.3 - IRHX's - Green Tag	1	16-Apr-27	16-Apr-27		
Cx.PH3.R5.DH1.3-MTS-IRHX.100R5	DH1.3 - MTS-IRHX's - Pre Startup Installer	5	15-Mar-27	19-Mar-27		
Cx.PH3.R5.DH1.3-MTS-IRHX.110R5	DH1.3 - MTS-IRHX's - Pre Startup Vendor	3	15-Mar-27	17-Mar-27		
Cx.PH3.R5.DH1.3-MTS-IRHX.120R5	DH1.3 - MTS-IRHX's - L2 QC	1	22-Mar-27	22-Mar-27		

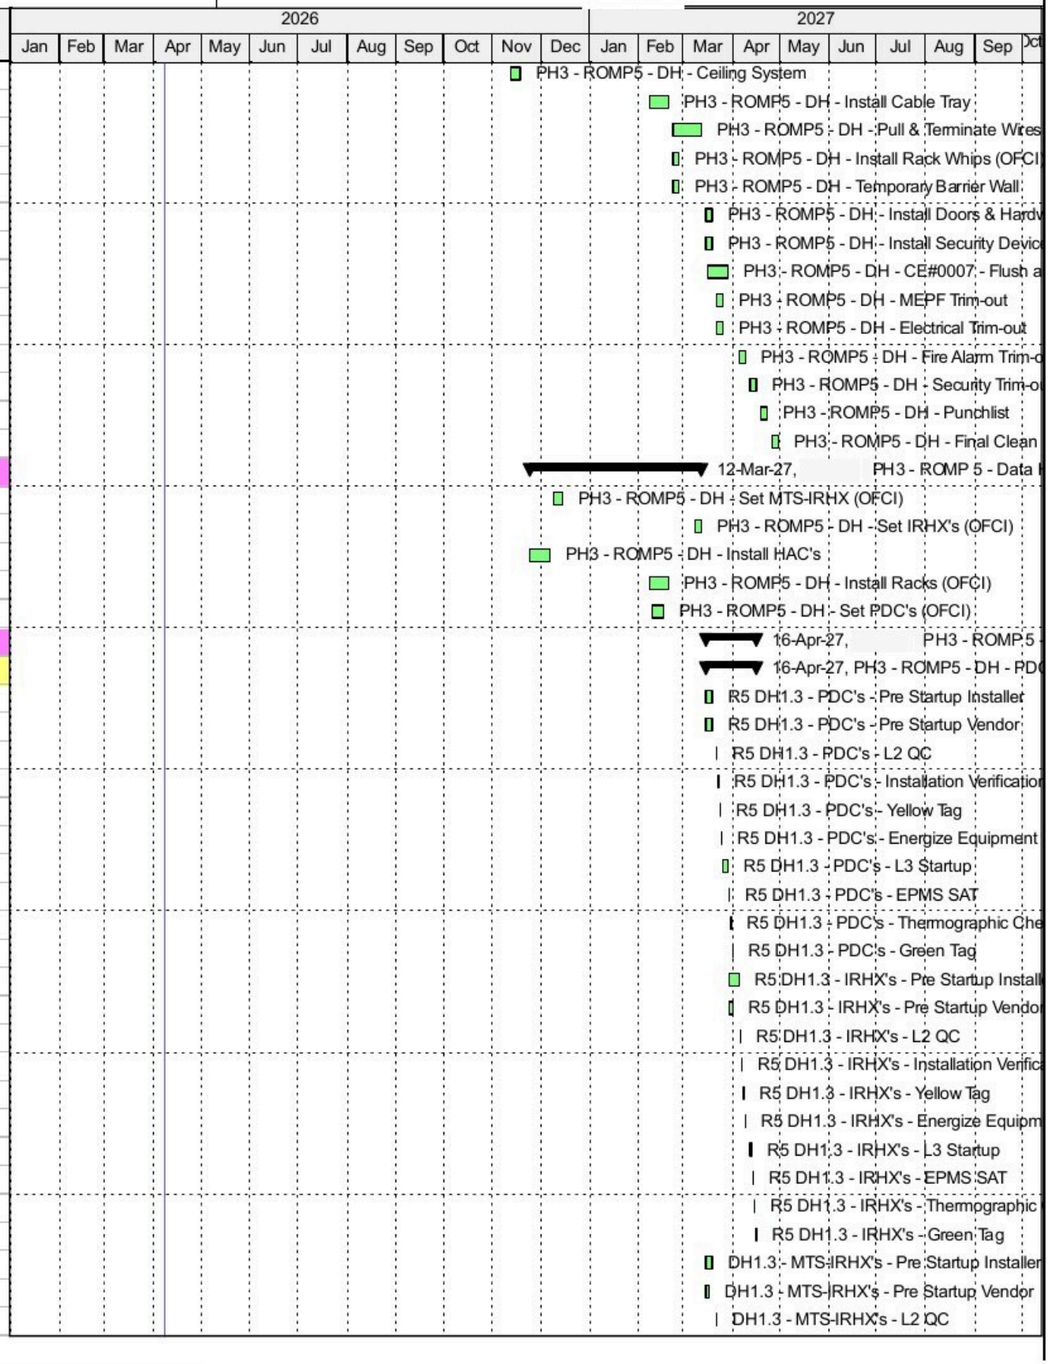


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
Cx.PH3.R5.DH1.3-MTS-IRHX.130R5	DH1.3 - MTS-IRHX's - Installation Verification Checklist	1	23-Mar-27	23-Mar-27		
Cx.PH3.R5.DH1.3-MTS-IRHX.140R5	DH1.3 - MTS-IRHX's - Yellow Tag	1	24-Mar-27	24-Mar-27		
Cx.PH3.R5.DH1.3-MTS-IRHX.150R5	DH1.3 - MTS-IRHX's - Energize Equipment	1	26-Mar-27	26-Mar-27		
Cx.PH3.R5.DH1.3-MTS-IRHX.160R5	DH1.3 - MTS-IRHX's - L3 Startup	2	29-Mar-27	30-Mar-27		
Cx.PH3.R5.DH1.3-MTS-IRHX.170R5	DH1.3 - MTS-IRHX's - EPMS SAT	1	31-Mar-27	31-Mar-27		
Cx.PH3.R5.DH1.3-MTS-IRHX.180R5	DH1.3 - MTS-IRHX's - Thermographic Checks	1	01-Apr-27	01-Apr-27		
Cx.PH3.R5.DH1.3-MTS-IRHX.190R5	DH1.3 - MTS-IRHX's - Green Tag	1	02-Apr-27	02-Apr-27		
PH3 - ROMP 6 - Data Hall		139	08-Oct-26	20-Apr-27		
PH3.R6.DH1.3-IB.1580	PH3 - ROMP6 - DH - Mechanical OH Rough-ins	4	15-Oct-26	20-Oct-26	Trade	Mechanical
PH3.R6.DH1.3-IB.1610	PH3 - ROMP6 - DH - Mechanical Trim-out	5	15-Mar-27	19-Mar-27	Trade	Mechanical
PH3.R6.DH1.3-IB.1450	PH3 - ROMP6 - DH - CE#0007 - Install Liquid Cooling Systems (CFI	6	08-Mar-27	15-Mar-27	Trade	CFN/SFN Pipir
PH3.R6.DH1.3-IB.1640	PH3 - ROMP6 - DH - Install Liquid Cooling Systems (SFN) (OFCI)	4	12-Mar-27	17-Mar-27	Trade	CFN/SFN Pipir
PH3.R6.DH1.3-IB.1330	PH3 - ROMP6 - DH - Layout & Frame Walls	5	08-Oct-26	14-Oct-26		
PH3.R6.DH1.3-IB.1590	PH3 - ROMP6 - DH - Fire Sprinkler OH Rough-ins	5	08-Oct-26	14-Oct-26		
PH3.R6.DH1.3-IB.1480	PH3 - ROMP6 - DH - One-side Drywall	5	15-Oct-26	21-Oct-26		
PH3.R6.DH1.3-IB.1520	PH3 - ROMP6 - DH - Plumbing In-Wall Rough-ins	2	15-Oct-26	16-Oct-26		
PH3.R6.DH1.3-IB.1530	PH3 - ROMP6 - DH - Electrical In-Wall Rough-ins	4	15-Oct-26	20-Oct-26		
PH3.R6.DH1.3-IB.1540	PH3 - ROMP6 - DH - Fire Alarm In-Wall Rough-ins	4	15-Oct-26	20-Oct-26		
PH3.R6.DH1.3-IB.1550	PH3 - ROMP6 - DH - Security/Telecom/LV In-Wall Rough-ins	4	15-Oct-26	20-Oct-26		
PH3.R6.DH1.3-IB.1660	PH3 - ROMP6 - DH - Hang Door Frames	5	15-Oct-26	21-Oct-26		
PH3.R6.DH1.3-IB.1460	PH3 - ROMP6 - DH - In-Wall Inspections	1	21-Oct-26	21-Oct-26		
PH3.R6.DH1.3-IB.1560	PH3 - ROMP6 - DH - Plumbing OH Rough-ins	4	21-Oct-26	26-Oct-26		
PH3.R6.DH1.3-IB.1570	PH3 - ROMP6 - DH - Electrical/Fire Alarm OH Rough-ins	15	21-Oct-26	10-Nov-26		
PH3.R6.DH1.3-IB.1575	PH3 - ROMP6 - DH - Security/Telecom/LV OH Rough-ins	15	21-Oct-26	10-Nov-26		
PH3.R6.DH1.3-IB.1340	PH3 - ROMP6 - DH - Hang, Tape, & Finish Drywall	10	22-Oct-26	04-Nov-26		
PH3.R6.DH1.3-IB.1350	PH3 - ROMP6 - DH - Prime Paint	5	02-Nov-26	06-Nov-26		
PH3.R6.DH1.3-IB.1470	PH3 - ROMP6 - DH - OH Inspections	1	11-Nov-26	11-Nov-26		
PH3.R6.DH1.3-IB.1360	PH3 - ROMP6 - DH - Ceiling System	5	12-Nov-26	18-Nov-26		
PH3.R6.DH1.3-IB.1390	PH3 - ROMP6 - DH - Install Cable Tray	10	08-Feb-27	19-Feb-27		
PH3.R6.DH1.3-IB.1380	PH3 - ROMP6 - DH - Pull & Terminate Wires	15	22-Feb-27	12-Mar-27		
PH3.R6.DH1.3-IB.1430	PH3 - ROMP6 - DH - Install Rack Whips (OFCI)	5	22-Feb-27	26-Feb-27		
PH3.R6.DH1.3-IB.1440	PH3 - ROMP6 - DH - Temporary Barrier Wall	5	22-Feb-27	26-Feb-27		
PH3.R6.DH1.3-IB.1400	PH3 - ROMP6 - DH - Install Doors & Hardware	5	15-Mar-27	19-Mar-27		
PH3.R6.DH1.3-IB.1490	PH3 - ROMP6 - DH - Install Security Devices (By Others)	5	15-Mar-27	19-Mar-27		
PH3.R6.DH1.3-IB.1620	PH3 - ROMP6 - DH - Fire Alarm Trim-out	5	15-Mar-27	19-Mar-27		
PH3.R6.DH1.3-IB.1630	PH3 - ROMP6 - DH - Security Trim-out (By Others)	5	15-Mar-27	19-Mar-27		
PH3.R6.DH1.3-IB.1650	PH3 - ROMP6 - DH - CE#0007 - Flush and Fill Liquid	10	18-Mar-27	31-Mar-27		
PH3.R6.DH1.3-IB.1370	PH3 - ROMP6 - DH - MEPF Trim-out	5	22-Mar-27	26-Mar-27		
PH3.R6.DH1.3-IB.1600	PH3 - ROMP6 - DH - Electrical Trim-out	5	22-Mar-27	26-Mar-27		
PH3.R6.DH1.3-IB.1500	PH3 - ROMP6 - DH - Punchlist	5	29-Mar-27	02-Apr-27		
PH3.R6.DH1.3-IB.1510	PH3 - ROMP6 - DH - Final Clean	5	05-Apr-27	09-Apr-27		
PH3 - ROMP 6 - Data Hall Equipment		79	24-Nov-26	12-Mar-27		
PH3.R6.DH1.3-IB.220	PH3 - ROMP6 - DH - Set MTS-IRHX (OFCI)	5	09-Dec-26	15-Dec-26	Trade	HVAC
PH3.R6.DH1.3-IB.210	PH3 - ROMP6 - DH - Set IRHX's (OFCI)	5	08-Mar-27	12-Mar-27	Trade	HVAC
PH3.R6.DH1.3-IB.1410	PH3 - ROMP6 - DH - Install HAC's	10	24-Nov-26	07-Dec-26		

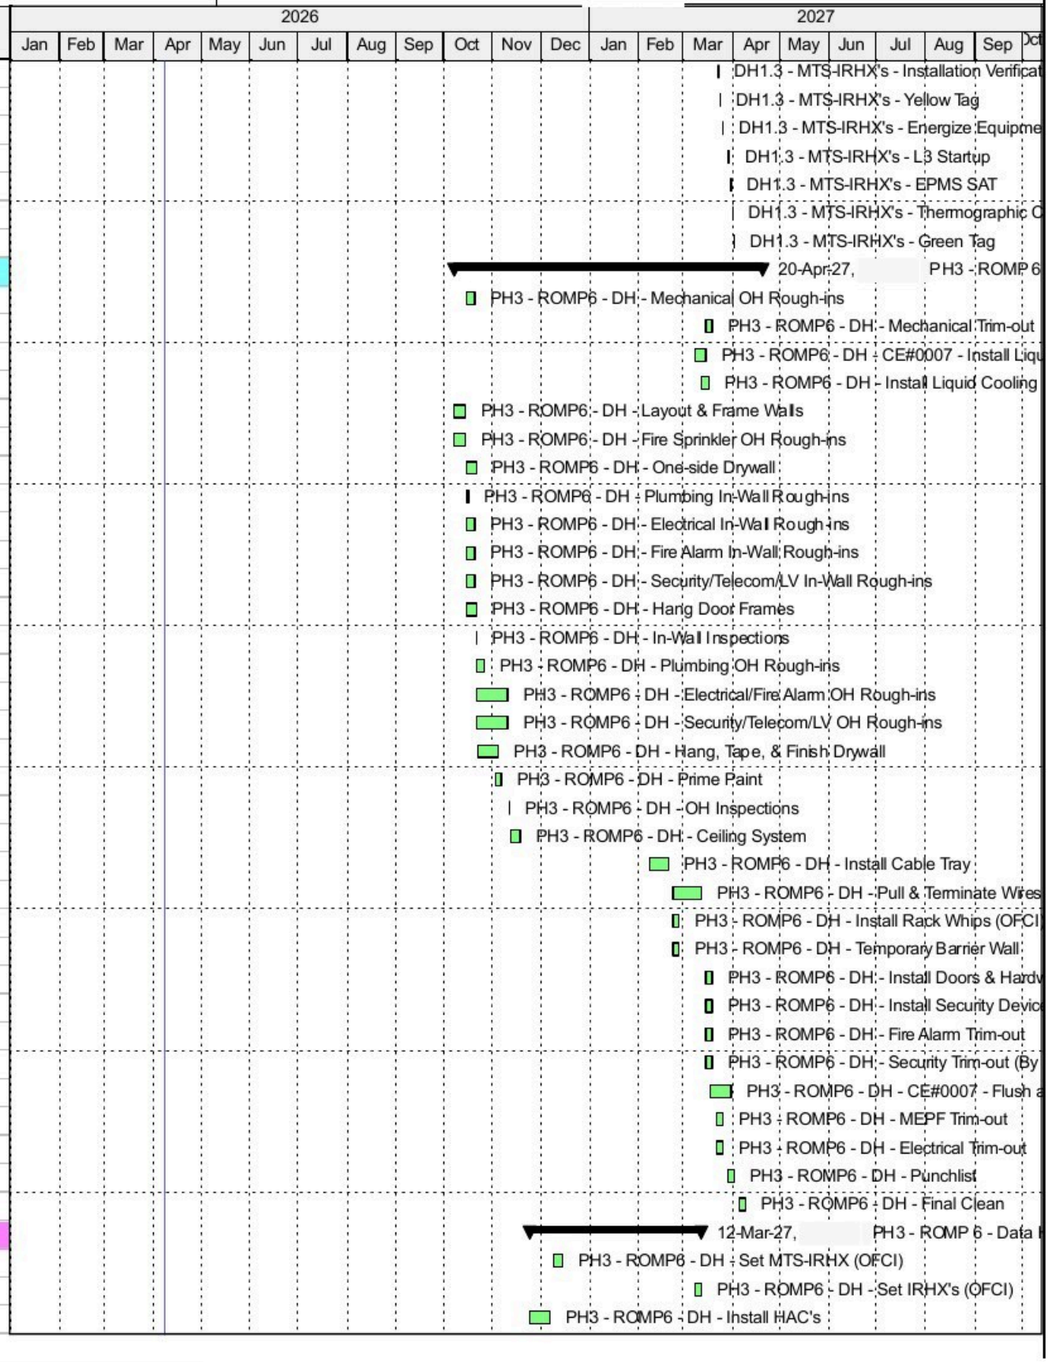


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH3.R6.DH1.3-IB.1420	PH3 - ROMP6 - DH - Install Racks (OFCI)	10	08-Feb-27	19-Feb-27		
PH3.R6.DH1.3-IB.200	PH3 - ROMP6 - DH - Set PDC's (OFCI)	5	10-Feb-27	16-Feb-27		
PH3 - ROMP 6 - Data Hall Commissioning		27	15-Mar-27	20-Apr-27		
PH3 - ROMP6 - DH - PDC-1.5A-01-05, PDC-1.5B-01-05, PDC-1.6A-01-05, PDC-1.6B-01-05 Cx		27	15-Mar-27	20-Apr-27		
Cx.PH3.R6.DH1.3-PDC.200	R6 DH1.3 - PDC's - Pre Startup Installer	5	15-Mar-27	19-Mar-27		
Cx.PH3.R6.DH1.3-PDC.210	R6 DH1.3 - PDC's - Pre Startup Vendor	5	15-Mar-27	19-Mar-27		
Cx.PH3.R6.DH1.3-PDC.220	R6 DH1.3 - PDC's - L2 QC	1	22-Mar-27	22-Mar-27		
Cx.PH3.R6.DH1.3-PDC.230	R6 DH1.3 - PDC's - Installation Verification Checklist	1	23-Mar-27	23-Mar-27		
Cx.PH3.R6.DH1.3-PDC.240	R6 DH1.3 - PDC's - Yellow Tag	1	24-Mar-27	24-Mar-27		
Cx.PH3.R6.DH1.3-PDC.250	R6 DH1.3 - PDC's - Energize Equipment	1	25-Mar-27	25-Mar-27		
Cx.PH3.R6.DH1.3-PDC.260	R6 DH1.3 - PDC's - L3 Startup	2	26-Mar-27	29-Mar-27		
Cx.PH3.R6.DH1.3-PDC.270	R6 DH1.3 - PDC's - EPMS SAT	1	30-Mar-27	30-Mar-27		
Cx.PH3.R6.DH1.3-PDC.280	R6 DH1.3 - PDC's - Thermographic Checks	1	31-Mar-27	31-Mar-27		
Cx.PH3.R6.DH1.3-PDC.290	R6 DH1.3 - PDC's - Green Tag	1	01-Apr-27	01-Apr-27		
Cx.PH3.R6.DH1.3-IRHX.200	R6 DH1.3 - IRHX's - Pre Startup Installer	5	01-Apr-27	07-Apr-27		
Cx.PH3.R6.DH1.3-IRHX.210	R6 DH1.3 - IRHX's - Pre Startup Vendor	3	01-Apr-27	05-Apr-27		
Cx.PH3.R6.DH1.3-IRHX.220	R6 DH1.3 - IRHX's - L2 QC	1	08-Apr-27	08-Apr-27		
Cx.PH3.R6.DH1.3-IRHX.230	R6 DH1.3 - IRHX's - Installation Verification Checklist	1	09-Apr-27	09-Apr-27		
Cx.PH3.R6.DH1.3-IRHX.240	R6 DH1.3 - IRHX's - Yellow Tag	1	12-Apr-27	12-Apr-27		
Cx.PH3.R6.DH1.3-IRHX.250	R6 DH1.3 - IRHX's - Energize Equipment	1	13-Apr-27	13-Apr-27		
Cx.PH3.R6.DH1.3-IRHX.260	R6 DH1.3 - IRHX's - L3 Startup	2	14-Apr-27	15-Apr-27		
Cx.PH3.R6.DH1.3-IRHX.270	R6 DH1.3 - IRHX's - EPMS SAT	1	16-Apr-27	16-Apr-27		
Cx.PH3.R6.DH1.3-IRHX.280	R6 DH1.3 - IRHX's - Thermographic Checks	1	19-Apr-27	19-Apr-27		
Cx.PH3.R6.DH1.3-IRHX.290	R6 DH1.3 - IRHX's - Green Tag	1	20-Apr-27	20-Apr-27		
Cx.PH3.R6.DH1.3-MTS-IRHX.200R6	DH1.3 - MTS-IRHX's - Pre Startup Installer	5	15-Mar-27	19-Mar-27		
Cx.PH3.R6.DH1.3-MTS-IRHX.210R6	DH1.3 - MTS-IRHX's - Pre Startup Vendor	3	15-Mar-27	17-Mar-27		
Cx.PH3.R6.DH1.3-MTS-IRHX.220R6	DH1.3 - MTS-IRHX's - L2 QC	1	22-Mar-27	22-Mar-27		
Cx.PH3.R6.DH1.3-MTS-IRHX.230R6	DH1.3 - MTS-IRHX's - Installation Verification Checklist	1	23-Mar-27	23-Mar-27		
Cx.PH3.R6.DH1.3-MTS-IRHX.240R6	DH1.3 - MTS-IRHX's - Yellow Tag	1	24-Mar-27	24-Mar-27		
Cx.PH3.R6.DH1.3-MTS-IRHX.250R6	DH1.3 - MTS-IRHX's - Energize Equipment	1	26-Mar-27	26-Mar-27		
Cx.PH3.R6.DH1.3-MTS-IRHX.260R6	DH1.3 - MTS-IRHX's - L3 Startup	2	29-Mar-27	30-Mar-27		
Cx.PH3.R6.DH1.3-MTS-IRHX.270R6	DH1.3 - MTS-IRHX's - EPMS SAT	1	31-Mar-27	31-Mar-27		
Cx.PH3.R6.DH1.3-MTS-IRHX.280R6	DH1.3 - MTS-IRHX's - Thermographic Checks	1	01-Apr-27	01-Apr-27		
Cx.PH3.R6.DH1.3-MTS-IRHX.290R6	DH1.3 - MTS-IRHX's - Green Tag	1	02-Apr-27	02-Apr-27		
PH3 - ROMP 5 & 6 - TAHU Gallery 1.3 Corridor 01.966		55	04-Jan-27	19-Mar-27		
PH3.TAHU1.3-IB.400	PH3 - R5&6 - TAHU Gallery Corr - Layout & Frame Walls	5	04-Jan-27	08-Jan-27		
PH3.TAHU1.3-IB.530	PH3 - R5&6 - TAHU Gallery Corr - One Side Drywall	5	11-Jan-27	19-Jan-27		
PH3.TAHU1.3-IB.570	PH3 - R5&6 - TAHU Gallery Corr - Plumbing In-Wall Rough-ins	2	11-Jan-27	12-Jan-27		
PH3.TAHU1.3-IB.580	PH3 - R5&6 - TAHU Gallery Corr - Electrical In-Wall Rough-ins	4	11-Jan-27	18-Jan-27		
PH3.TAHU1.3-IB.590	PH3 - R5&6 - TAHU Gallery Corr - Fire Alarm In-Wall Rough-ins	4	11-Jan-27	18-Jan-27		
PH3.TAHU1.3-IB.600	PH3 - R5&6 - TAHU Gallery Corr - Security/Telecom/LV In-Wall Roug	4	11-Jan-27	18-Jan-27		
PH3.TAHU1.3-IB.690	PH3 - R5&6 - TAHU Gallery Corr - Hang Door Frames	5	11-Jan-27	19-Jan-27		
PH3.TAHU1.3-IB.510	PH3 - R5&6 - TAHU Gallery Corr - In-wall Inspections	1	19-Jan-27	19-Jan-27		
PH3.TAHU1.3-IB.610	PH3 - R5&6 - TAHU Gallery - Plumbing OH Rough-ins	2	19-Jan-27	20-Jan-27		
PH3.TAHU1.3-IB.430	PH3 - R5&6 - TAHU Gallery Corr - Hang, Tape, & Finish Drywall	10	20-Jan-27	03-Feb-27		

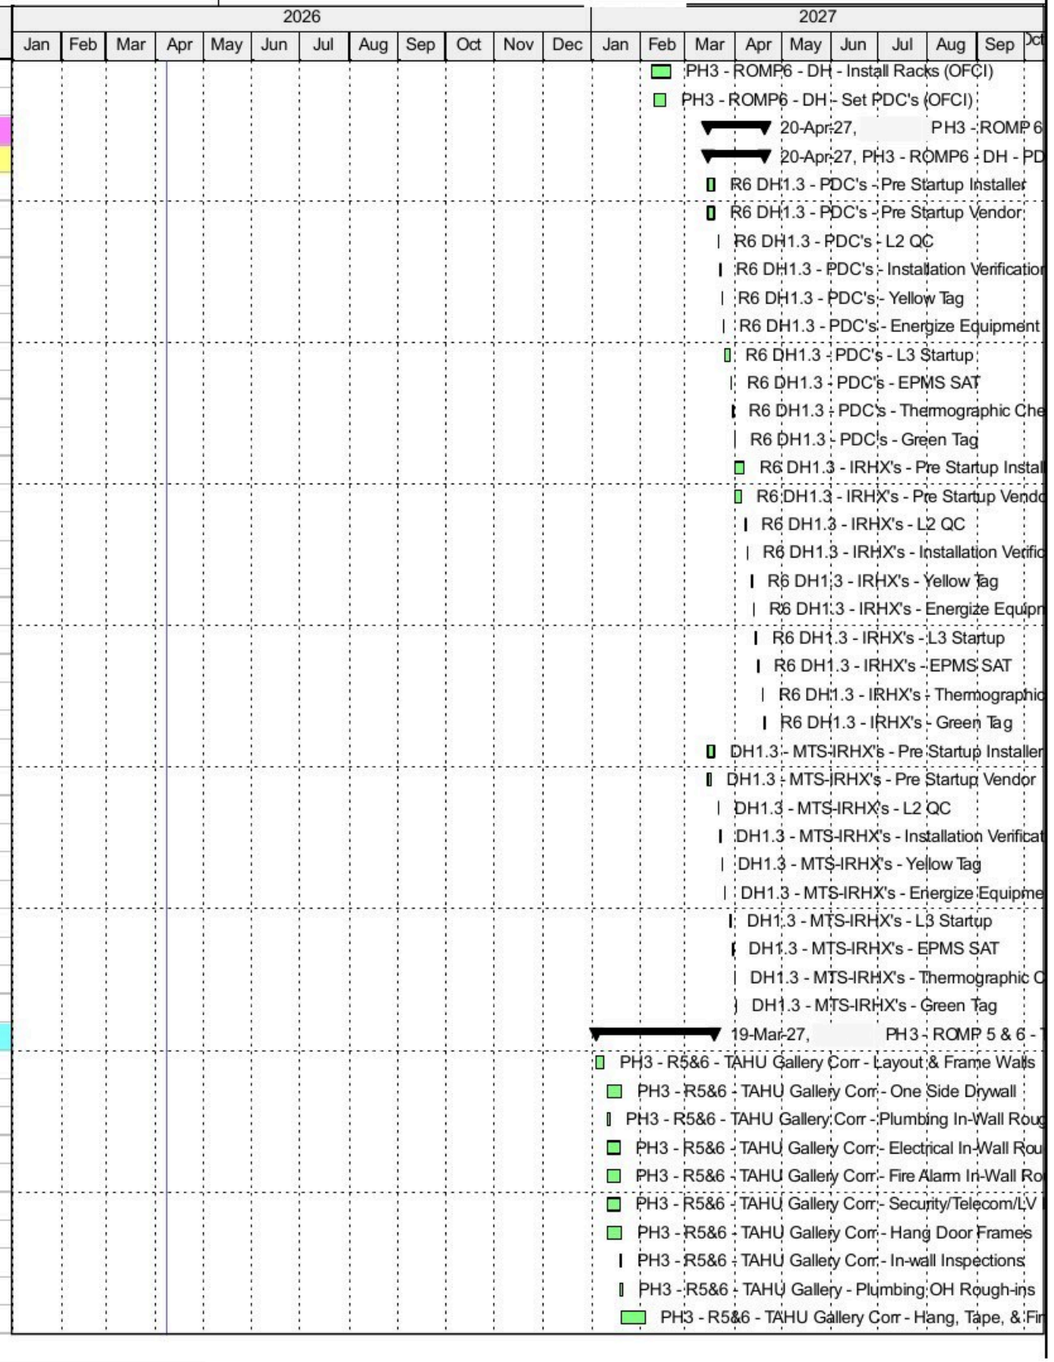


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH3.TAHU1.3-IB.440	PH3 - R5&6 - TAHU Gallery Corr - Prime Paint	5	01-Feb-27	05-Feb-27		
PH3.TAHU1.3-IB.680	PH3 - R5&6 - TAHU Gallery Corr - Security Trim-out (By Others)	2	08-Feb-27	09-Feb-27		
PH3.TAHU1.3-IB.480	PH3 - R5&6 - TAHU Gallery Corr - Install Doors & Hardware	5	15-Mar-27	19-Mar-27		
PH3.TAHU1.3-IB.540	PH3 - R5&6 - TAHU Gallery Corr - Install Security Devices (By Others	5	15-Mar-27	19-Mar-27		
PH3 - ROMP 5 & 6 - TAHU Gallery 1.3 Equipment		5	28-Dec-26	01-Jan-27		
PH3.TAHU1.3-140	PH3 - R5&6 - TAHU Gallery - Set TAHU's (OFCI)	5	28-Dec-26	01-Jan-27	Trade	HVAC
PH3 - ROMP 5 & 6 - TAHU Gallery 1.3 Commissioning		30	08-Mar-27	16-Apr-27		
Cx.PH3.TGAL1.3-TAHU.100	TAHU Gallery 1.2 - TAHU's - Pre Startup Installer	5	08-Mar-27	12-Mar-27		
Cx.PH3.TGAL1.3-TAHU.110	TAHU Gallery 1.2 - TAHU's - Pre Startup Vendor	5	08-Mar-27	12-Mar-27		
Cx.PH3.TGAL1.3-TAHU.120	TAHU Gallery 1.2 - TAHU's - L2 QC	1	15-Mar-27	15-Mar-27		
Cx.PH3.TGAL1.3-TAHU.130	TAHU Gallery 1.2 - TAHU's - Installation Verification Checklist	2	16-Mar-27	17-Mar-27		
Cx.PH3.TGAL1.3-TAHU.140	TAHU Gallery 1.2 - TAHU's - Yellow Tag	1	18-Mar-27	18-Mar-27		
Cx.PH3.TGAL1.3-TAHU.150	TAHU Gallery 1.2 - TAHU's - Energize Equipment	2	26-Mar-27	29-Mar-27		
Cx.PH3.TGAL1.3-TAHU.160	TAHU Gallery 1.2 - TAHU's - L3 Startup	4	30-Mar-27	02-Apr-27		
Cx.PH3.TGAL1.3-TAHU.170	TAHU Gallery 1.2 - TAHU's - BAS SAT	4	05-Apr-27	08-Apr-27		
Cx.PH3.TGAL1.3-TAHU.180	TAHU Gallery 1.2 - TAHU's - Water Test / TAB	4	09-Apr-27	14-Apr-27		
Cx.PH3.TGAL1.3-TAHU.190	TAHU Gallery 1.2 - TAHU's - Green Tag	2	15-Apr-27	16-Apr-27		
PH3 - ROMP 5 & 6 - Mezzanine		60	14-Oct-26	05-Jan-27		
PH3.R5&6.Mezz-680	PH3 - R5&6 - Mezz - Mechanical OH Rough-ins	4	21-Oct-26	26-Oct-26	Trade	Mechanical
PH3.R5&6.Mezz-710	PH3 - R5&6 - Mezz - Mechanical Trim-out	5	23-Nov-26	27-Nov-26	Trade	Mechanical
PH3.R5&6.Mezz-690	PH3 - R5&6 - Mezz - Fire Sprinkler OH Rough-ins	5	14-Oct-26	20-Oct-26		
PH3.R5&6.Mezz-340	PH3 - R5&6 - Mezz - Layout & Frame Walls	5	15-Oct-26	21-Oct-26		
PH3.R5&6.Mezz-440	PH3 - R5&6 - Mezz - One Side Drywall	5	22-Oct-26	28-Oct-26		
PH3.R5&6.Mezz-620	PH3 - R5&6 - Mezz - Plumbing In-Wall Rough-ins	2	22-Oct-26	23-Oct-26		
PH3.R5&6.Mezz-630	PH3 - R5&6 - Mezz - Electrical In-Wall Rough-ins	4	22-Oct-26	27-Oct-26		
PH3.R5&6.Mezz-640	PH3 - R5&6 - Mezz - Fire Alarm In-Wall Rough-ins	4	22-Oct-26	27-Oct-26		
PH3.R5&6.Mezz-650	PH3 - R5&6 - Mezz - Security/Telecom/LV In-Wall Rough-ins	4	22-Oct-26	27-Oct-26		
PH3.R5&6.Mezz-740	PH3 - R5&6 - Mezz - Hang Door Frames	5	22-Oct-26	28-Oct-26		
PH3.R5&6.Mezz-660	PH3 - R5&6 - Mezz - Plumbing OH Rough-ins	5	27-Oct-26	02-Nov-26		
PH3.R5&6.Mezz-670	PH3 - R5&6 - Mezz - Electrical/Fire Alarm OH Rough-ins	10	27-Oct-26	09-Nov-26		
PH3.R5&6.Mezz-675	PH3 - R5&6 - Mezz - Security/Telecom/LV OH Rough-ins	10	27-Oct-26	09-Nov-26		
PH3.R5&6.Mezz-750	PH3 - R5&6 - Mezz - Pull & Terminate Wire	10	27-Oct-26	09-Nov-26		
PH3.R5&6.Mezz-420	PH3 - R5&6 - Mezz - In-Wall Inspections	1	28-Oct-26	28-Oct-26		
PH3.R5&6.Mezz-370	PH3 - R5&6 - Mezz - Hang, Tape, & Finish Drywall	10	29-Oct-26	11-Nov-26		
PH3.R5&6.Mezz-380	PH3 - R5&6 - Mezz - Prime Paint	5	09-Nov-26	13-Nov-26		
PH3.R5&6.Mezz-430	PH3 - R5&6 - Mezz - OH Inspections	1	10-Nov-26	10-Nov-26		
PH3.R5&6.Mezz-730	PH3 - R5&6 - Mezz - Security Trim-out (By Others)	5	11-Nov-26	17-Nov-26		
PH3.R5&6.Mezz-400	PH3 - R5&6 - Mezz - Install Doors & Hardware	5	16-Nov-26	20-Nov-26		
PH3.R5&6.Mezz-700	PH3 - R5&6 - Mezz - Electrical Trim-out	5	23-Nov-26	27-Nov-26		
PH3.R5&6.Mezz-720	PH3 - R5&6 - Mezz - Fire Alarm Trim-out	5	15-Dec-26	22-Dec-26		
PH3.R5&6.Mezz-580	PH3 - R5&6 - Mezz - Punchlist	5	23-Dec-26	29-Dec-26		
PH3.R5&6.Mezz-590	PH3 - R5&6 - Mezz - Final Clean	5	30-Dec-26	05-Jan-27		
PH3 - ROMP 5 & 6 - Stair 06		42	08-Oct-26	04-Dec-26		
PH3 - ROMP 5 & 6 - L1 - Stair 06		39	08-Oct-26	01-Dec-26		
PH3.R6.L1.STR.330	PH3 - R6 - L1 - ST06 - Mechanical OH Rough-Ins	1	12-Oct-26	12-Oct-26	Trade	Mechanical

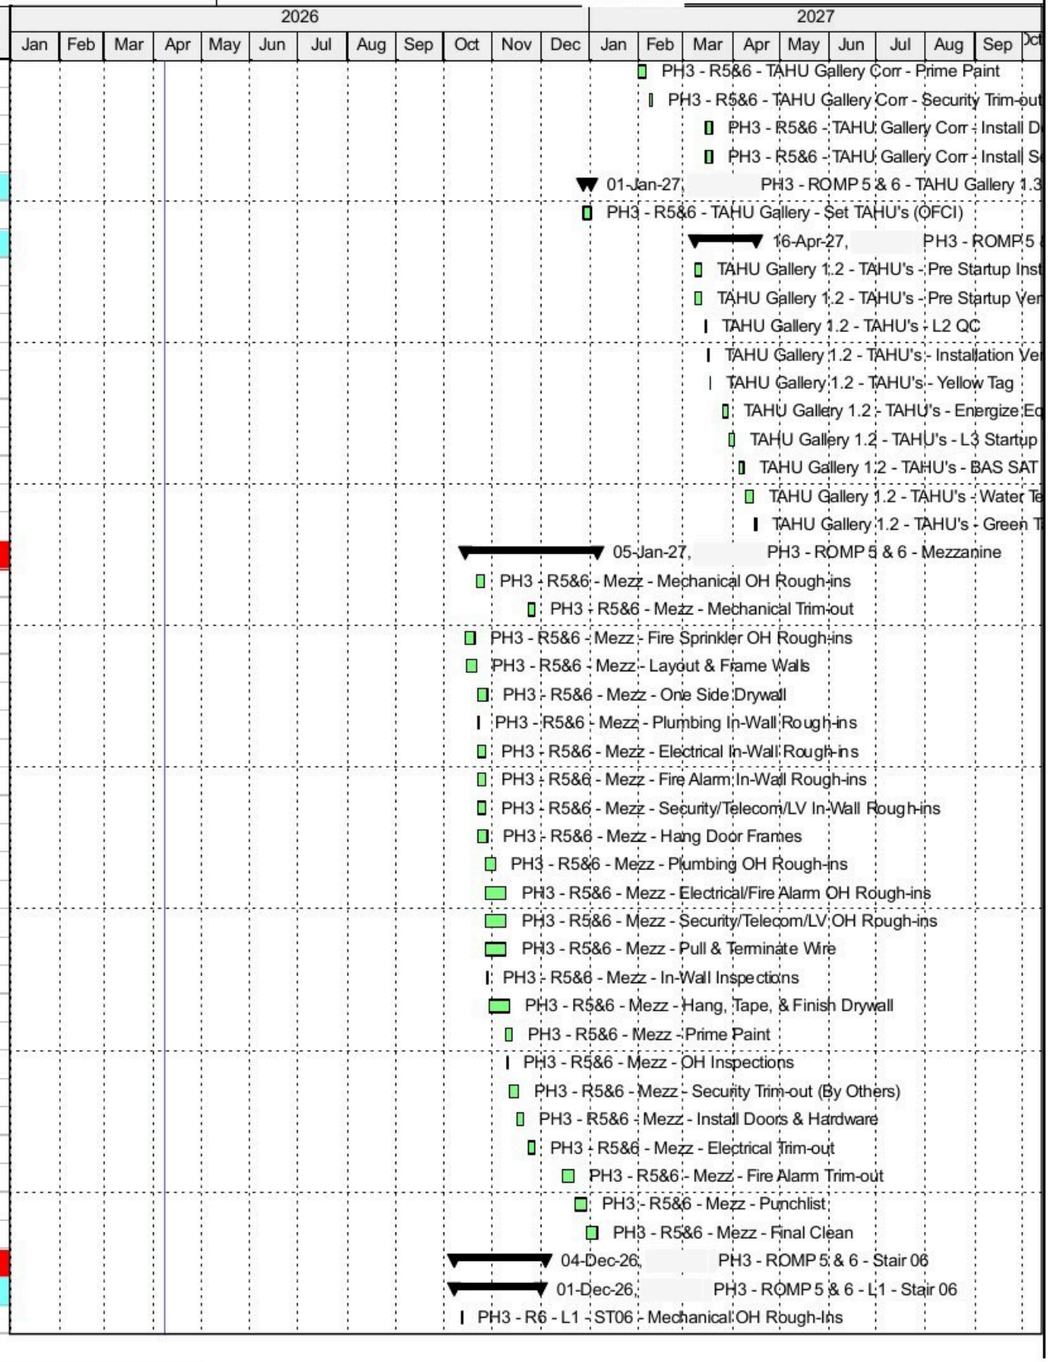


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH3.R6.L1.STR.530	PH3 - R6 - L1 - ST06 - Mechanical Trim-out	2	02-Nov-26	03-Nov-26	Trade	Mechanical
PH3.R6.L1.STR.300	PH3 - R6 - L1 - ST06 - Fire Sprinkler OH Rough-Ins	2	08-Oct-26	09-Oct-26		
PH3.R6.L1.STR.100	PH3 - R6 - L1 - ST06 - Layout Walls	1	08-Oct-26	08-Oct-26		
PH3.R6.L1.STR.110	PH3 - R6 - L1 - ST06 - Frame Walls	2	09-Oct-26	12-Oct-26		
PH3.R6.L1.STR.310	PH3 - R6 - L1 - ST06 - Electrical/Fire Alarm OH Rough-Ins	3	12-Oct-26	14-Oct-26		
PH3.R6.L1.STR.320	PH3 - R6 - L1 - ST06 - Sec/Telecom OH Rough-Ins	3	12-Oct-26	14-Oct-26		
PH3.R6.L1.STR.120	PH3 - R6 - L1 - ST06 - One Side Drywall	2	13-Oct-26	14-Oct-26		
PH3.R6.L1.STR.200	PH3 - R6 - L1 - ST06 - Electrical/Fire Alarm In-Wall Rough-Ins	3	13-Oct-26	15-Oct-26		
PH3.R6.L1.STR.210	PH3 - R6 - L1 - ST06 - Sec/Telecom In-Wall Rough-Ins	3	13-Oct-26	15-Oct-26		
PH3.R6.L1.STR.130	PH3 - R6 - L1 - ST06 - Hang Door Frames	1	15-Oct-26	15-Oct-26		
PH3.R6.L1.STR.390	PH3 - R6 - L1 - ST06 - OH Inspections	1	15-Oct-26	15-Oct-26		
PH3.R6.L1.STR.290	PH3 - R6 - L1 - ST06 - In-Wall Inspections	1	16-Oct-26	16-Oct-26		
PH3.R6.L1.STR.140	PH3 - R6 - L1 - ST06 - Hang, Tape, & Finish Drywall	3	19-Oct-26	21-Oct-26		
PH3.R6.L1.STR.160	PH3 - R6 - L1 - ST06 - Prime Paint	2	22-Oct-26	23-Oct-26		
PH3.R6.L1.STR.500	PH3 - R6 - L1 - ST06 - Fire Sprinkler Trim-out	2	26-Oct-26	27-Oct-26		
PH3.R6.L1.STR.490	PH3 - R6 - L1 - ST06 - Install Security Devices (By Others)	5	26-Oct-26	30-Oct-26		
PH3.R6.L1.STR.410	PH3 - R6 - L1 - ST06 - Pull & Terminate Wires	5	26-Oct-26	30-Oct-26		
PH3.R6.L1.STR.580	PH3 - R6 - L1 - ST06 - Install Lighting	2	26-Oct-26	27-Oct-26		
PH3.R6.L1.STR.400	PH3 - R6 - L1 - ST06 - Install Doors & Hardware	1	29-Oct-26	29-Oct-26		
PH3.R6.L1.STR.510	PH3 - R6 - L1 - ST06 - Electrical Trim-out	2	02-Nov-26	03-Nov-26		
PH3.R6.L1.STR.520	PH3 - R6 - L1 - ST06 - Fire Alarm Trim-out	2	02-Nov-26	03-Nov-26		
PH3.R6.L1.STR.590	PH3 - R6 - L1 - ST06 - Security Trim-out (By Others)	5	02-Nov-26	06-Nov-26		
PH3.R6.L1.STR.600	PH3 - R6 - L1 - ST06 - Final Paint	5	09-Nov-26	13-Nov-26		
PH3.R6.L1.STR.610	PH3 - R6 - L1 - ST06 - Install Signage	2	16-Nov-26	17-Nov-26		
PH3.R6.L1.STR.680	PH3 - R6 - L1 - ST06 - Punchlist	5	18-Nov-26	24-Nov-26		
PH3.R6.L1.STR.690	PH3 - R6 - L1 - ST06 - Final Clean	5	25-Nov-26	01-Dec-26		
PH3 - ROMP 5 & 6 - M1 - Stair 06		41	09-Oct-26	04-Dec-26		
PH3.R6.M1.STR.330	PH3 - R6 - M1 - ST06 - Mechanical OH Rough-Ins	1	14-Oct-26	14-Oct-26	Trade	Mechanical
PH3.R6.M1.STR.530	PH3 - R6 - M1 - ST06 - Mechanical Trim-out	2	05-Nov-26	06-Nov-26	Trade	Mechanical
PH3.R6.M1.STR.100	PH3 - R6 - M1 - ST06 - Layout Walls	1	09-Oct-26	09-Oct-26		
PH3.R6.M1.STR.300	PH3 - R6 - M1 - ST06 - Fire Sprinkler OH Rough-Ins	2	12-Oct-26	13-Oct-26		
PH3.R6.M1.STR.110	PH3 - R6 - M1 - ST06 - Frame Walls	2	13-Oct-26	14-Oct-26		
PH3.R6.M1.STR.120	PH3 - R6 - M1 - ST06 - One Side Drywall	2	15-Oct-26	16-Oct-26		
PH3.R6.M1.STR.310	PH3 - R6 - M1 - ST06 - Electrical/Fire Alarm OH Rough-Ins	3	15-Oct-26	19-Oct-26		
PH3.R6.M1.STR.320	PH3 - R6 - M1 - ST06 - Sec/Telecom OH Rough-Ins	3	15-Oct-26	19-Oct-26		
PH3.R6.M1.STR.200	PH3 - R6 - M1 - ST06 - Electrical/Fire Alarm In-Wall Rough-Ins	3	16-Oct-26	20-Oct-26		
PH3.R6.M1.STR.210	PH3 - R6 - M1 - ST06 - Sec/Telecom In-Wall Rough-Ins	3	16-Oct-26	20-Oct-26		
PH3.R6.M1.STR.130	PH3 - R6 - M1 - ST06 - Hang Door Frames	1	19-Oct-26	19-Oct-26		
PH3.R6.M1.STR.390	PH3 - R6 - M1 - ST06 - OH Inspections	1	20-Oct-26	20-Oct-26		
PH3.R6.M1.STR.290	PH3 - R6 - M1 - ST06 - In-Wall Inspections	1	21-Oct-26	21-Oct-26		
PH3.R6.M1.STR.140	PH3 - R6 - M1 - ST06 - Hang, Tape, & Finish Drywall	3	22-Oct-26	26-Oct-26		
PH3.R6.M1.STR.160	PH3 - R6 - M1 - ST06 - Prime Paint	2	27-Oct-26	28-Oct-26		
PH3.R6.M1.STR.500	PH3 - R6 - M1 - ST06 - Fire Sprinkler Trim-out	2	29-Oct-26	30-Oct-26		
PH3.R6.M1.STR.490	PH3 - R6 - M1 - ST06 - Install Security Devices (By Others)	5	29-Oct-26	04-Nov-26		
PH3.R6.M1.STR.410	PH3 - R6 - M1 - ST06 - Pull & Terminate Wires	5	29-Oct-26	04-Nov-26		

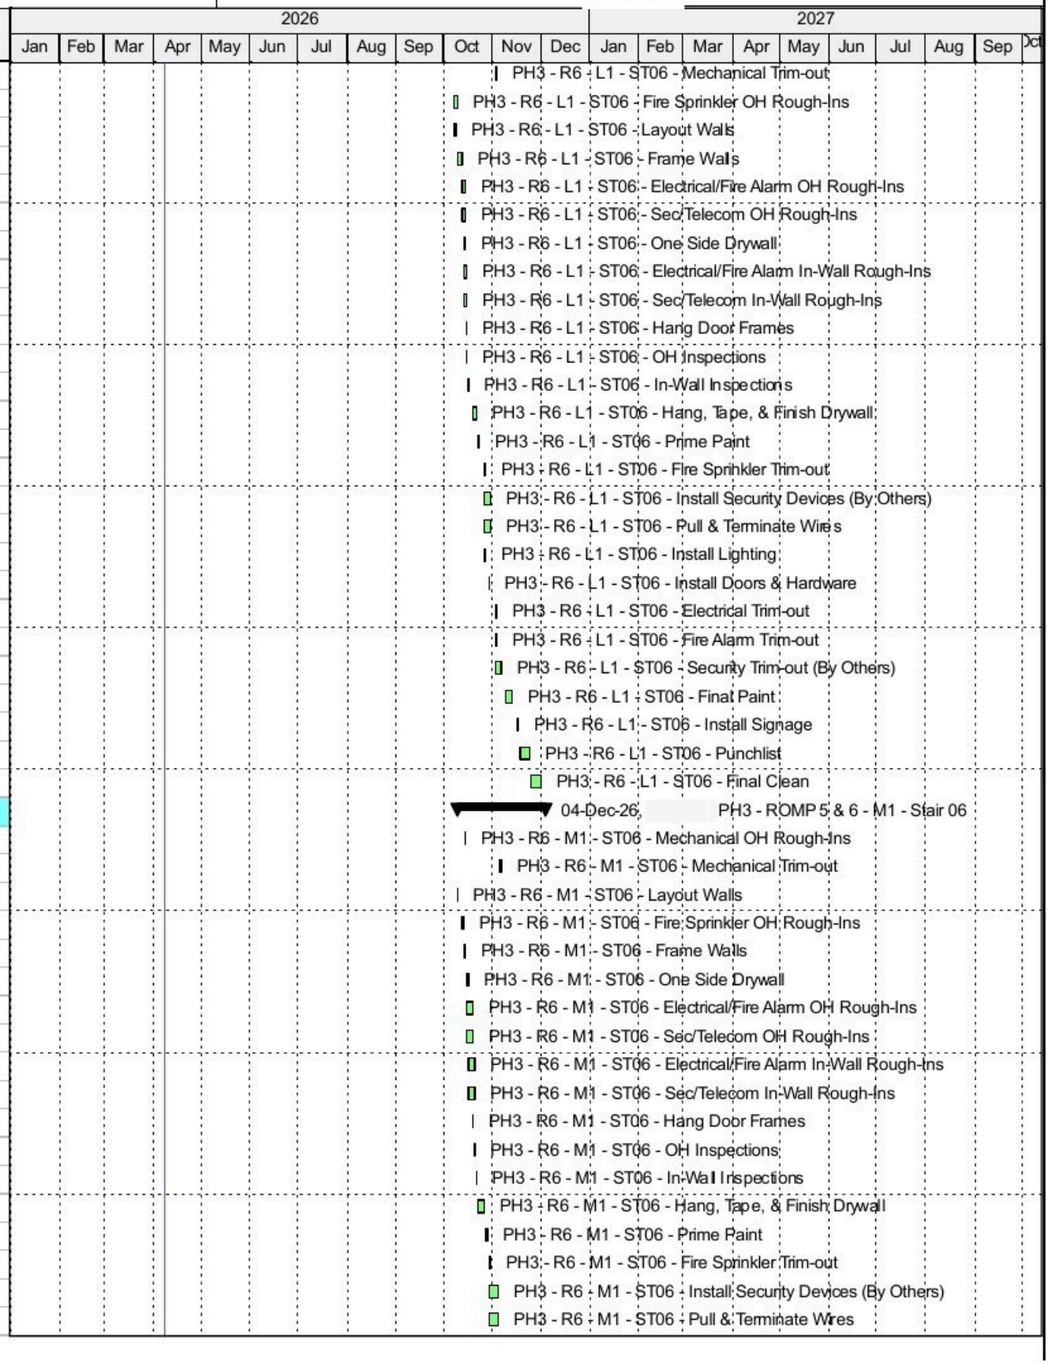


Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary

HSE | CPM SCHEDULING CONSULTANTS

Sample Data Center Baseline Schedule

Remaining Activites

Activity ID	Activity Name	Original Duration	Start	Finish	Responsibility	Discipline
PH3.R6.M1.STR.580	PH3 - R6 - M1 - ST06 - Install Lighting	2	29-Oct-26	30-Oct-26		
PH3.R6.M1.STR.400	PH3 - R6 - M1 - ST06 - Install Doors & Hardware	1	30-Oct-26	30-Oct-26		
PH3.R6.M1.STR.510	PH3 - R6 - M1 - ST06 - Electrical Trim-out	2	05-Nov-26	06-Nov-26		
PH3.R6.M1.STR.520	PH3 - R6 - M1 - ST06 - Fire Alarm Trim-out	2	05-Nov-26	06-Nov-26		
PH3.R6.M1.STR.590	PH3 - R6 - M1 - ST06 - Security Trim-out (By Others)	5	05-Nov-26	11-Nov-26		
PH3.R6.M1.STR.600	PH3 - R6 - M1 - ST06 - Final Paint	5	12-Nov-26	18-Nov-26		
PH3.R6.M1.STR.610	PH3 - R6 - M1 - ST06 - Install Signage	2	19-Nov-26	20-Nov-26		
PH3.R6.M1.STR.680	PH3 - R6 - M1 - ST06 - Punchlist	5	23-Nov-26	27-Nov-26		
PH3.R6.M1.STR.690	PH3 - R6 - M1 - ST06 - Final Clean	5	30-Nov-26	04-Dec-26		
Commissioning		181	22-Dec-26	31-Aug-27		
Phase 1 Commissioning (ROMP 1 & 2 + Office & Catcher)		120	22-Dec-26	07-Jun-27		
OWN.Cx.P1.100	PH1 Cx - L2/L3 Early Commissioning (New)	50	22-Dec-26	05-Mar-27		
OWN.Cx.P1.110	PH1 Cx - L3 Remaining Commissiong	26	05-Mar-27	09-Apr-27		
OWN.Cx.P1.120	PH1 Cx - IST	41	12-Apr-27	07-Jun-27		
Phase 2 Commissioning (ROMP 3 & 4)		107	22-Feb-27	20-Jul-27		
OWN.Cx.P2.100	PH2 Cx - L2/L3 Early Commissioning (New)	50	22-Feb-27	03-May-27		
OWN.Cx.P2.110	PH2 Cx - L3 Remaining Commissiong	26	04-May-27	08-Jun-27		
OWN.Cx.P2.120	PH2 Cx - IST	29	09-Jun-27	20-Jul-27		
Phase 3 Commissioning (ROMP 5 & 6)		107	05-Apr-27	31-Aug-27		
OWN.Cx.P3.100	PH3 Cx - L2/L3 Early Commissioning (New)	50	05-Apr-27	14-Jun-27		
OWN.Cx.P3.110	PH3 Cx - L3 Remaining Commissiong	24	15-Jun-27	17-Jul-27		
OWN.Cx.P3.120	PH3 Cx - IST	31	19-Jul-27	31-Aug-27		

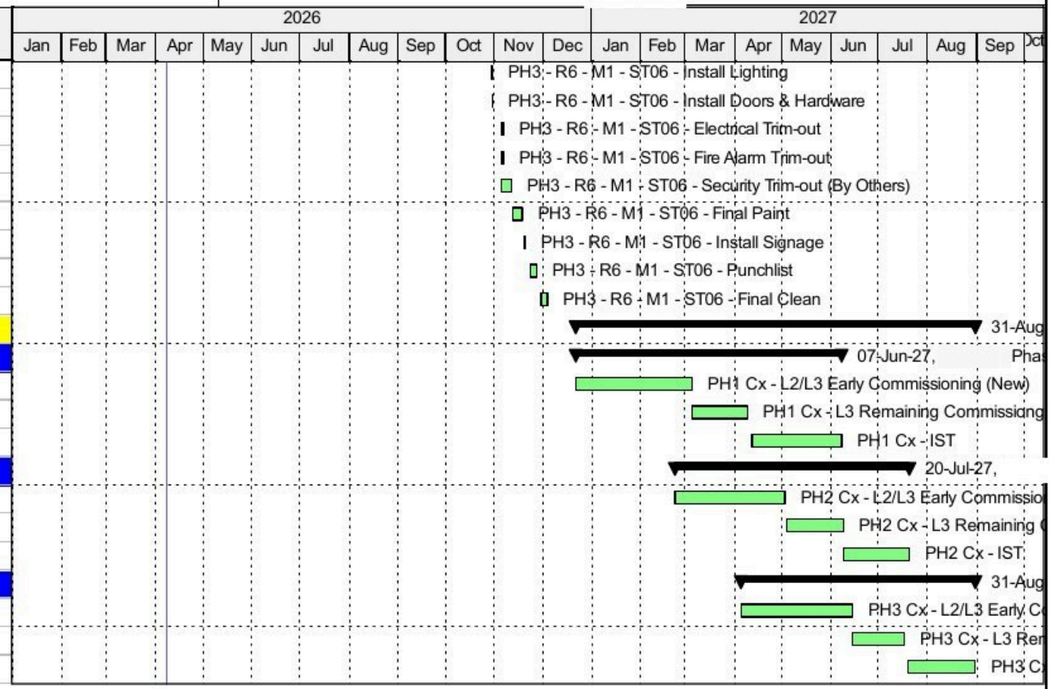

Remaining Level of Effort
Remaining Work
Critical Remaining Work
Milestone
Summary
