

	Abbreviations		
		Abbreviations	
TRAD	<u>Trade</u>	AREA	Project Area
ACFLR	Access Floor System Subcontractor	SUMM	Milestones and Summaries
ACOUS	Acoustic Ceiling Subcontractor	O/S	Off-Site or Admin Activity
ARCH	Architect and Consulting Engineers	ALL	All Areas / General
AUTOD	Automatic Door Vendor/ Installer	NSITE	Site -North of Clinic
BLIND	Window Treatments Subcontractor	SSITE	Site -South of Clinic
BOLLD	Hydraulic/Fixed Bollards Vendor/Installer	BLDG	Overall Building Footprint
CASEW	Wood and Metal Casework Subcontractor	WEST	West Bldg Area
CIVIL	Civil Utilities Subcontractor	CEPLT	Central Energy Plant
CLEAN	Construction Cleaning Service	EAST	East Bldg Area
KRAFTC	Cast-In-Place Concrete Subcontractor	VISIT	Visitor Entry Canopy
CPMC	CPM Scheduling Consultant (Catalyst Contractors)	URGNT	Urgent Care Entry Canopy
CURTW	Ceramic Tile Subcontractor	CTYRD	Cooling Tower Yard
DIRT	Curtainwall System Subcontractor Excavation and Grading Subcontractor	SERVI	Service Yard
DOCK	Loading Dock Specialties Subcontractor	ELEV	Floor/Elevation
DRYWL	Gypsum Drywall Systems Subcontractor	GRADE	At or Below Grade Construction
ELECT	Electrical Subcontractor (Quinco)	1STFL	First Floor
ELEV	Elevator Subcontractor	ECNPY	Entry Canopy Roofs
FIRE	Fire Protection Subcontractor (Coastal)	2NDFL	2nd Floor
FLRG	Reslient Flooring/Carpet Subcontractor	2NDRF	Roofs at 2nd Floor Level
FOLD	Folding Fire Door Vendor/Installer	3RDFL	3rd Floor
FPRFG	Firesafing/ Sprayed Fireproofing Subcontractor	3RDRF	Roofs at 3rd Floor Level
KRAFTH	Hardware Subcontractor	D&TPH	Diagnostic &Treatment Wing Mech Penthouse
KRAFTD	Hollow Metal Frames/Doors Subcontractor	D&TRF	Diagnostic & Treatment Wing Mech Penthouse Roof
INSPT	Inspecting Authorities Having Jurisdiction	4THFL	4th Floor
INSUL	Insulation Subcontractor	5THFL	5th Floor Level (Service Elevator Lobby)
IRRIG	Irrigation System Subcontractor	5THRF	Roofs at 5th Floor Level
KCCSP KRAFT	Kraft Construction Company Self Performed Scope GC (Kraft Construction Company)	PEMRM PEMRR	Passenger Elevator Machine Room Level Passenger Elevator Machine Rm Roof Level
LCAHJ	Lee County Authorities Having Jurisdiction	SEMRM	Service Elevator Machine Room Level
LCEC	Lee County Flectric Cooperative	SEMRR	Service Elevator Machine Room Roof Level
LDSCP	Landscaping Subcontractor	CLNPH	Clinic Wing Mech Penthouse
LOCKR	Locker Vendor/Installer	CLPHR	Clinic Wing Mech Penthouse Roof
LOUVR	Building Louver Subcontractor	ALLFL	All Floor Levels or Elevations
KRAFTM	Masonry Subcontractor		
MDGAS	Medical Gases/Vacumn Systems Subcontractor	<u>PPHS</u>	Project Phase
MECH	Mechanical Systems Subcontractor (B&I)	SUMM	Project Overview
MEDSP	Medical Specialty Subcontractor	VAFFE	VA Supplied FFE "Need" Dates
MEPFP	All Mech/Elec/Plbg/Fire Protection Trades	PRECN	Preconstruction Activities
MTLPN OWNER	Composite Metal Panel Subcontractor	MOBIL SITE	Mobilization and Site Organization
PAINT	Owner (Veterans Administration) Painting Subcontractor	FNDNS	Site Clearing/Earthwork/Civil Infrastructure Foundations Construction
PAVER	Paving Subconfactor	STRUC	Elevated Structure Construction
PLUMB	Plumbing Subcontractor (B&I)	SOG	U/G MEP and Slab on Grade Construction
PNEUM	Pneumatic Tube System Vendor/Installer	EXTER	Exterior Envelope Bldg Systems
PRCST	Precast Concrete Subcontractor (Stabil Concrete)	EQPMT	Major MEPFP Equipment
KRAFTRC	Rough Carpentry Subcontractor	R/IWK	Framing and MEPFP Rough Ins
REFRG	Refrigeration Equipment Vendor/Installer	WALLS	Insulation and Completion of Interior Partitions
ROLLD	Rolling Door Subcontractor	ELEV	Elevator Installation
ROOF	Roofing Systems Subcontractor	FINWK	Finishes and Fixtures Installation
SEAL	Sealants Subcontractor	FFFE	Fixed FFE Installation and Specialty Items
SECUR	Electronic Safety and Security Subcontractor	HS/LS	Site Hardscape and Landscape Completion
SIGN	Signage and Graphics Subcontractor	COMM	Systems Commissioning
SITE	Site Specialties Subcontractor	COMPL	Project Completion Activities
SKYLT SPEC	Skylight Subcontractor Specialties Subcontractor		
STEEL	Speciaties Subcontractor Structural and Misc Metal Subcontractor	+ +	
STONE	Stonework Subcontactor	 	
STUCC	Stucco Finishes Subcontractor	- 	
SURVG	Surveying and Layout Subcontractor	- 	
T&B	HVAC Test and Balance Subcontractor	- 	
TCARP	Trim Carpentry/Finish Carpentry Subcontractor	 	
TRZZO	Terrazzo Flooring Subcontractor		
VAULT	Vault Door/Day Gate Vendor/Installer		
VIBRO	Vibratory Compaction Subcontractor		
WPRFG	Waterproofing/Dampproofing Subcontractor		
WWASH	Window-Washing Egpmnt Vendor/Installer		

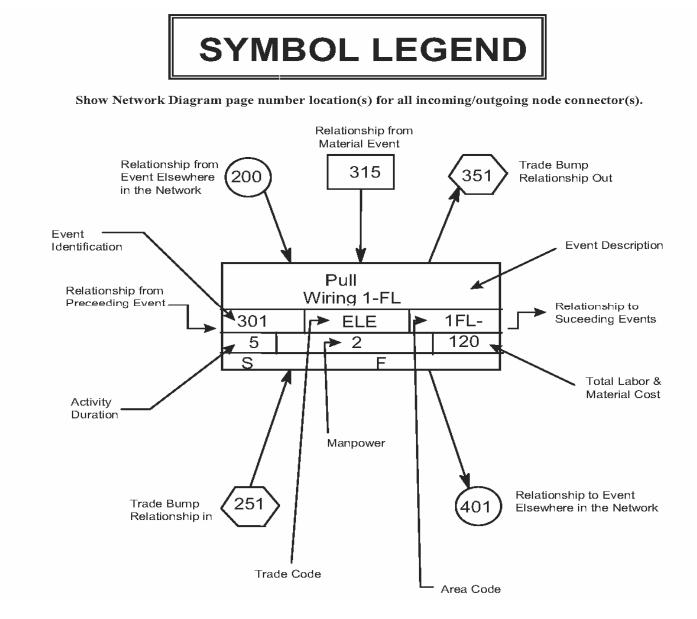

Department of Veterans Affairs Lee County Outpatient Clinic

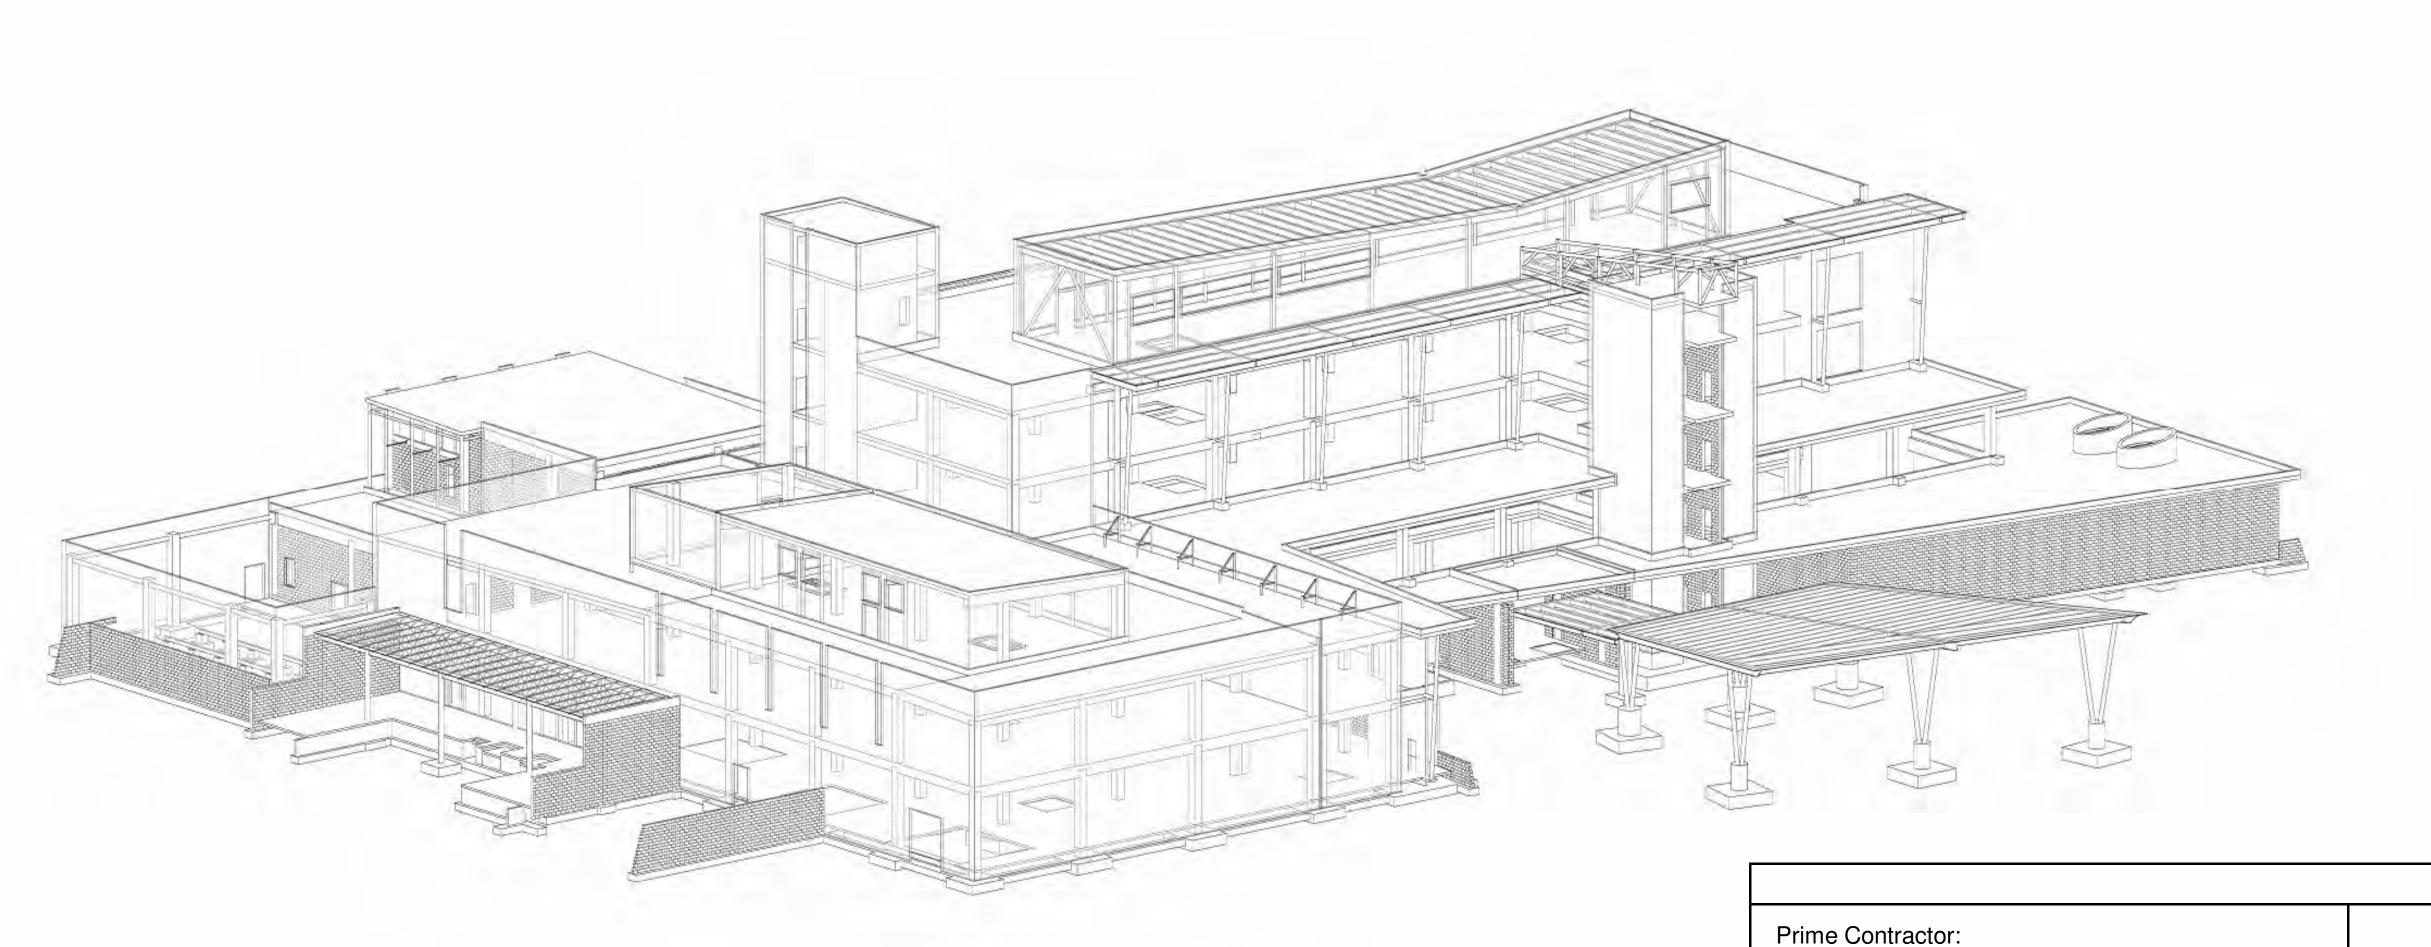

5000 500135 500140 East Bldg. Area - First Floor (Elevated Strctrs., U/G MEP) East Bldg. Area - First Floor (Exterior Envelope, Framing, & Insulation) East Bldg. Area -First Floor (Finishes & Fixtures)

East Bldg. Area - First Floor (Finishes & Fixtures Installation, & Fixed FFE Inst.)

East Bldg. Area - Entry Canopy Roofs East Bldg. Area - Second Floor (Elevated Strctrs., & Exterior Envelope, & Insulation) East Bldg. Area - Second Floor (Framing) East Bldg. Area - Second Floor (Fixed FFE Inst.)
East Bldg. Area - Roofs at Second Floor East Bldg. Area - Third Floor (Elevated Strctrs., & Exterior Envelope) East Bldg. Area - Third Floor (Framing, & Insulation) East Bldg. Area - Third Floor (Finishes & Fixtures Inst., & Fixed FFE Inst.) East Bldg. Area - Roofs at Third Floor East Bldg. Area - Fourth Floor (Elevated Strctrs., Exterior Envelope, Framing) East Bldg. Area - (Insulation, & Finishes & Fixtures Inst.) East Bldg. Area - Fourth Floor (Finishes & Fixtures, & Fixed FFE Installation) East Bldg. Area - Roofs at Fifth Floor East Bldg. Area - Roofs Passenger Elev. Machine Room Lvl.
East Bldg. Area - Roofs at Service Elev. Machine Room Lvl.
East Bldg. Area - Roofs at Clinic Wing Mech. Penhouse
East Bldg. Area - All Floor Levels or Elevations East Bldg. Area - Passenger Elev. Machine Room Lvl. East Bldg. Area - Service Elev. Machine Room Lvl. East Bldg. Area - Clinic Wing Mech. Penhouse Visitor Entry Canopy Urgent Care Entry Canopy Cooling Tower Yard Service Yard

Overall Building Footprint

West Bldg. Area - First Floor (Insulation, & Finishes)

West Bldg. Area - Second Floor (Insulation, & Finishes)

Central Energy Plant - All Floor Levels or Elevations

West Bldg. Area - Roofs at 3rd Floor

Central Energy Plant - Second Floor
Central Energy Plant - Third Floor
Central Energy Plant - Roofs at 3rd Floor

West Bldg. Area - At or Below Grade Const.
West Bldg. Area - First Floor (Elevated Strctrs., U/G MEP, Exterior Envelope, & Framing)

West Bldg. Area - First Floor (Finishes & Fixtures, & Fixed FFE Installation)

West Bldg. Area - Second Floor (Elevated Strctrs., Exterior Envelope, & Framing)

West Bldg. Area - Second Floor (Finishes & Fixtures, & Fixed FFE Installation)

West Bldg. Area - Diagnostic & Treatment Wing Mech. Penthouse & Penthouse Roof

400135 400140

400160 400165

400255

Cover Sheet

Kraft Construction Company, Inc.
11125 Gulfshore Drive North, Naples, Florida 34108

CPM Scheduling Consultant:

Catalyst Contractors Inc.

11905 Hatcher Circle, Orlando, FL 32824

VA New Ambulatory Surgery/Outpatient
Diagnostic Support Center
Lee County, FL
Project #516 CA 2400
Contract # VA-101-09-RP-0181

Department of Veteran's Affairs

Project Administration By:
Office of Construction & Facilities Management

Architect/Engineers: Hellumuth, Obata & Kassabaum, Inc.

